

OxyChem®

Wichita Plant

January 30, 2014

RECEIVED

FEB 06 2014

AWMD/WRAP-KNRP



Responsible Care®
Good Chemistry at Work

CERTIFIED MAIL 7010 3090 0003 3945 3447
Return Receipt Requested

U.S. Environmental Protection Agency Region 7
Attn: Chief, RCRA Corrective Action and Permits Branch
Air, RCRA and Toxics Division
11201 Renner Boulevard
Lenexa, Kansas 66219

REC'D

FEB 03 2014

APCO

**RE: 4th QUARTER 2013 QUARTERLY PROGRESS REPORT; OCCIDENTAL
CHEMICALS CORPORATION, WICHITA PLANT; USEPA ID# KSD007482029**

Dear Sir:

Enclosed please find the Quarterly Progress Report, as required by Occidental Chemical Corporation's RCRA hazardous waste permit number KSD007482029. This report summarizes the activities conducted for Part II of the Facility's RCRA Permit during the fourth quarter of 2013. In addition, please find enclosed the most recent version of the RFI Schedule, which is dated January 20, 2014, along with the most recent Vapor Intrusion ICM Monitoring Report for the fourth quarter of 2014, for your review and use. If you have any questions, please call Lisa R. Thurman at 316/529-7204.

Sincerely,

Steve Hieger
Plant Manager

Enclosure

c.c.: Mostafa Kamal; KDHE
Brad Roberts, USEPA Region VII
Juan Somoano; GSHI
Lisa Thurman; OCC
Bruce Clegg; CRA

CERTIFIED MAIL: 7010 3090 0003 3945 3454
CERTIFIED MAIL: 7010 3090 0003 3945 3461

RCRA



528693



Occidental Chemical Corporation



**Occidental Chemical Corporation, Quarterly Progress Report
October 1, 2013 through December 31, 2013**

Pursuant to Occidental Chemical Corporation's (OCC) hazardous waste permit KSD007482029, Part II, Section C.13, OCC is submitting this quarterly progress report. This report updates the progress of RCRA Corrective Action activities conducted during the fourth quarter of 2013.

- Completed the second 2013 semiannual groundwater monitoring event.
- A quarterly building monitoring and inspection event was completed. The completed reporting form was submitted to EPA and attached hereto.
- Completed the Phase II On-Site Groundwater RFI field investigation and commenced drafting the summary report.
- Completed subsurface DNAPL delineation and source area evaluation.
- Commenced drafting the summary of results for the Inorganics Area Phase III field investigation work.
- Continued construction of a wastewater treatment plant (third carbon absorption system) for interceptor wells (IW40, IW44, IW45 and IW46).
- Continued operation of the interceptor well network for groundwater control around Occidental's Wichita plant.
- Continued with the implementation of modifications to the groundwater extraction and treatment system.
- Received a new NPDES permit from KDHE regulating the discharge of extracted and treated groundwater to listed outfalls.
- There have been no releases of hazardous materials to report.



Work scheduled for the first quarter of 2014 includes:

- Submit the second 2013 Semiannual Groundwater Monitoring report.
- Submit the Phase II On-Site Groundwater RFI Summary Report. The report will include the results of Phase III Inorganics Area field investigation work and Chloromethanes I, II, Perc and Hazwaste Areas Phase II results.
- Continue operation of the interceptor well network for groundwater control around Occidental's Wichita plant.
- Continue with the implementation of modifications to the groundwater extraction and treatment system, including modifications to the piping conveyance system and construction of an additional treatment system.
- Conduct and report a quarterly building inspection and pressure monitoring event.

Notifications:

- None

CORRECTIVE ACTION CHRONOLOGY	
DATE	EVENT
07/07/2008	Draft Work Plan for Indoor Soil Gas Sampling
07/07/2008	Comments to QAPP Addendum 04/18/08
07/07/2008	Spring 2008 Neighbor Results
07/11/2008	Request for Interim Measures for Railroad Tracked Areas
07/25/2008	Revised Asbestos Surface Impoundment SWMU Interim Corrective Measure Implementation Report
07/28/2008	2008 2nd Quarter Progress Report
08/05/2008	Comments to Draft Work Plan for Collection & Analysis of Groundwater Samples (Appendix 9)
08/08/2008	Notice of Plug & Abandonment of DW #4
08/08/2008	Request for Extension of QAPP Comment Response
08/15/2008	Response to Railroad Tracked Areas Interim Measures Letter
08/18/2008	Interim Corrective Measures Implementation Report for Asbestos Surface Impoundment SWMU
09/03/2008	Draft Work Plan for Collection & Analysis of Groundwater Samples (Appendix 9)
09/19/2008	Revised Draft Work Plan for Indoor Soil Gas Sampling
09/22/2008	Comments to Draft Work Plan for Indoor Soils Gas Sampling
09/30/2008	Approval Letter for Work Plan for Indoor Soils Gas Sampling
10/03/2008	Comments to Draft Work Plan for Collection & Analysis of Groundwater Samples (Appendix 9)
10/30/2008	Appendix IX Semi-Annual Groundwater Monitoring Report
11/03/2008	Draft Work Plan for Collection & Analysis of Groundwater Samples
11/21/2008	Off-Site Soils Gas Sampling Data Evaluation Report
11/21/2008	Off-Site Geoprobe Groundwater Investigation Report
01/05/2009	Draft QAPP
01/19/2009	Indoor Soils Gas Sampling Report
01/23/2009	Sub-Slab Soils Gas Sampling
01/28/2009	Semi-Annual Neighbor Well Data
01/28/2009	4 th Quarter Corrective Action Report
02/10/2009	Direct Push Investigation Comments to EPA
02/12/2009	Off-Site Geoprobe Groundwater Investigation Report
02/20/2009	Soil Gas Sampling Data Evaluation Comments to EPA
03/19/2009	Soils Gas Sampling Data Evaluation
03/26/2009	2009 Ongoing Activities Cost Estimate

DATE	CORRECTIVE ACTION CHRONOLOGY EVENT
04/20/2009	Off-Site Geoprobe Report
04/21/2009	Email responding to QAPP Comments
04/30/2009	Semi-Annual Groundwater Report
04/30/2009	Monitor Well Inspection Summary Report
05/08/2009	Response to Comments for Sub-Slab Soils Gas Sampling Report
06/08/2009	Final QAPP and SAP Reports
06/30/2009	RFI Investigation Work Plan for Landfill, Hex Pits, and Brine Ponds
06/30/2009	ICM Effectiveness Evaluation Report
08/26/2009	Revised RFI Work Plan for Alpha Cake Landfill, Hex Waste Pits and Brine Ponds
09/14/2009	Response to EPA's Comments letter dated July 9, 2009 regarding on-Site vapor intrusion
09/14/2009	On-Site Vapor Intrusion Investigation, Assessment and Interim Corrective Measures Implementation Report
11/30/2009	Draft Penta Area and Shipping RFI Work Plan
12/14/2009	Response to EPA Comments & Submission of Revised Interceptor Well ICM Effectiveness Evaluation Report
12/22/2009	Supplemental Off-Site Soil Gas Sample Collection and Analysis, 1 st Quarterly, letter submission
12/30/2009	Preliminary Draft Phase I Summary/Phase II Recommendations letter report
01/15/2010	Response to EPA Comments – On-Site VI, Assessment & Interim ICM Implementation Report
02/12/2010	Final Revision to Interceptor Well ICM Effectiveness Report
02/12/2010	Second 2009 Semiannual Groundwater Monitoring Report
02/16/2010	Received comments from EPA for Penta Area and Shipping RFI Work Plan
02/19/2010	Phase I Summary/Phase II Recommendations Letter Report (final), Alpha Cake Landfill, Hex Waste Pits and Brine Ponds RFI Work Plan
04/30/2010	Response to EPA Comments – Penta Area and Shipping RFI Work Plan
04/30/2010	Revised Penta Area and Shipping RFI Work Plan
05/17/2010	Resampling of MW137S1 Letter to EPA
05/28/2010	Inorganics Area RFI Work Plan
07/09/2010	Received comments from EPA for Inorganics Area RFI Work Plan
08/11/2010	Response to EPA Comments – Inorganics Area RFI Work Plan
08/11/2010	Revised Inorganics Area RFI Work Plan
08/24/2010	First Semiannual Groundwater Monitoring Report
09/23/2010	Groundwater Screening (near MW-140) Investigation Summary Letter


CORRECTIVE ACTION CHRONOLOGY	
DATE	EVENT
10/4/2010	Operation and Maintenance Plan for On-Site Vapor Intrusion ICM for on-Site buildings
10/15/2010	RFI Summary Report for the Alpha Cake Landfill, Hex Waste Pits and Brine Ponds
10/29/2010	Supplemental Quarterly Off-Site Soil Gas Monitoring Summary Report
12/20/2010	Response to EPA Comments on the Operation and Maintenance Plan for On-Site Vapor Intrusion ICM for on-Site buildings
12/16/2010	Received comments from EPA for Supplemental Quarterly Off-Site Soil Gas Monitoring Summary Report
12/16/2010	Received comments from EPA for RFI Summary Report, Alpha Cake Landfill, Hex Waste Pits and Brine Ponds
12/30/2010	Comprehensive Well Survey letter submittal to EPA
1/4/2011	Penta Area and Shipping RFI Summary Report
1/17/2011	Response to EPA comments and revised Supplemental Quarterly Off-Site Soil Gas Monitoring Summary Report
1/18/2011	Response to EPA comments and revised RFI Summary Report – Landfill Areas
2/16/2011	Inorganic Area RFI Summary Report
2/23/2011	Second 2010 Semiannual Groundwater Monitoring Report
3/2/2011	Draft Conceptual Design Summary for Groundwater ICM Modifications
4/18/2011	Chloromethanes I, II, Perc and Hazwaste Areas RFI Work Plan
4/18/2011	Arkema Area Investigative Work Plan
4/29/2011	Response to EPA comments and revised RFI Summary Report – Penta Area and Shipping
4/29/2011	Response to EPA comments and revised RFI Summary Report – Inorganics Area
5/2/2011	On-Site Vapor Intrusion Mitigation ICM Construction Completion Report
6/17/2011	Response to EPA comments and revised Preliminary Conceptual Design Groundwater ICM Modifications Rpt
6/30/2011	On-Site Groundwater RFI Work Plan
6/30/2011	Vapor Intrusion ICM Inspection and Pressure Monitoring Record Report Form
7/20/2011	Response to EPA comments and revised Arkema Area Investigative Work Plan
8/1/2011	Response to EPA comments and revised On-Site Vapor Intrusion Mitigation ICM Construction Completion Rpt
8/18/2011	First 2011 Semiannual Groundwater Monitoring Report
8/22/2011	Response to EPA comments and revised Penta Area and Shipping RFI Summary Report
8/22/2011	Response to EPA comments and revised Chloromethanes I, II, Perc and Hazwaste Areas RFI Work Plan
8/26/2011	Response to EPA comments and revised Conceptual Design Groundwater ICM Modifications Report
9/12/2011	Response to EPA comments and revised Groundwater Monitoring Program Summary Table
9/30/2011	Response to EPA comments and revised Arkema Investigative Work Plan

CORRECTIVE ACTION CHRONOLOGY	
DATE	EVENT
10/31/2011	Vapor Intrusion ICM Inspection and Pressure Monitoring Record Report Form
11/14/2011	Received EPA comments on On-Site Groundwater RFI Work Plan
11/14/2011	Received EPA approval letter for Arkema Area Investigative Work Plan
11/30/2011	Sampling and Analysis Plan
12/14/2011	Response to Comments and Revised On-Site Groundwater RFI Work Plan
1/5/2012	EPA Comments on Draft Sampling and Analysis Plan
1/27/2012	EPA Comments on On-Site Groundwater RFI Work Plan
2/8/2012	Response to Comments and Revised Sampling and Analysis Plan
2/20/2012	Second 2011 Semiannual Groundwater Monitoring Report
3/9/2012	Revised Sampling and Analysis Plan (SAP)
3/13/2012	Revised Standard Operating Procedures 4 for SAP
3/19/2012	Response to Comments and Revised On-Site Groundwater RFI Work Plan
3/21/2012	EPA Approval letter – On-Site Groundwater RFI Work Plan
4/17/2012	Stormwater Ponds Area RFI Work Plan
4/17/2012	Fuel Depot Area RFI Work Plan
8/6/2012	Penta Area and Shipping Phase II RFI Summary Report
8/6/2012	Chloromethanes I, II, Perc and Hazwaste Areas RFI and Arkema Area Investigation Summary Report
8/13/2012	Response to Comments and Revised Stormwater Ponds RFI Work Plan and Revised Fuel Depot RFI Work Plan
8/14/2012	Inorganics Area Supplemental Report
8/17/2012	Formal Notification of Additional SWMUs
8/24/2012	First 2012 Semiannual Groundwater Monitoring Report
11/14/2012	Class I Modification Letter for Additional SWMUs
11/15/2012	Phase I On-Site Groundwater Investigation RFI Summary Report
2/22/2013	Second 2012 Semiannual Groundwater Monitoring Report
3/7/2013	Response to EPA Comments and Revised Penta Area and Shipping Phase II RFI Summary Report
3/15/2013	Response to EPA Comments and Revised Phase I On-Site Groundwater RFI Summary Report
3/22/2013	Fuel Depot and Stormwater Ponds Area RFI Summary Report
4/19/2013	EPA approval letter – Revised Phase I On-Site Groundwater Summary Report and Revised Phase II Penta Area and Shipping RFI Summary Report
4/24/2013	Monitoring Well Abandonment and Replacement letter

CORRECTIVE ACTION CHRONOLOGY	
DATE	EVENT
4/25/13	EPA approval letter – Fuel Depot and Stormwater Pond Area RFI Summary Report
8/22/13	Second 2013 Semiannual Groundwater Monitoring Report

Occidental Chemical Corporation


Wichita Facility
DRAFT RFI Schedule
January 20, 2014

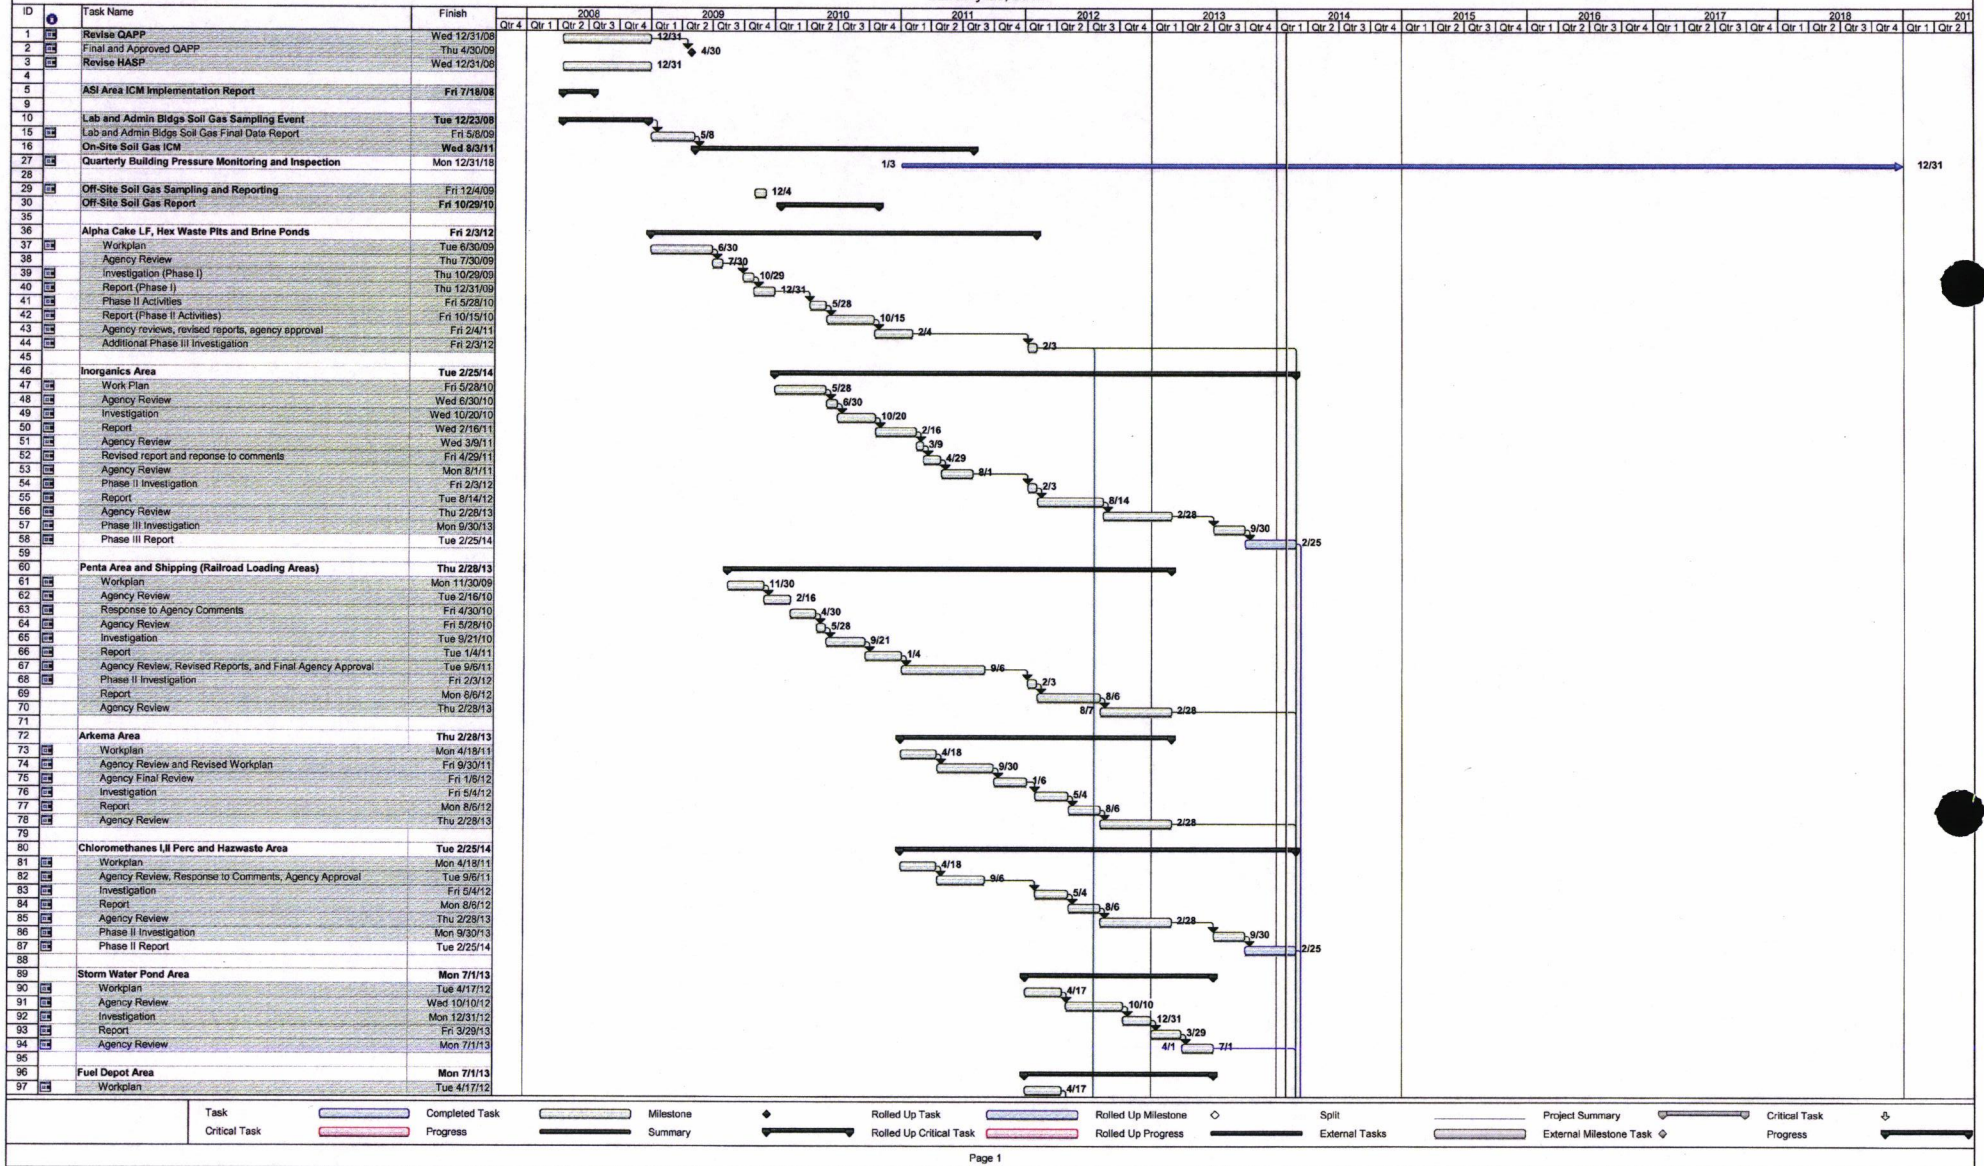

Occidental Chemical Corporation

Wichita Facility
DRAFT RFI Schedule
January 20, 2014

Task Name ID 88 89 90 91 92 93 94 95 96 97 98 99 100 101 102 103 104 105 106 107 108 109 110 111 112 113 114 115 116 117 118 119 120 121 122 123 124 125 126 127 128 129 130 131 132 133 134 135 136 137 138 139 140 141 142 143 144 145 146 147 148 149 150 151 152 153 154 155 156 157 158 159 160 161 162 163 164 165 166 167 168 169 170 171

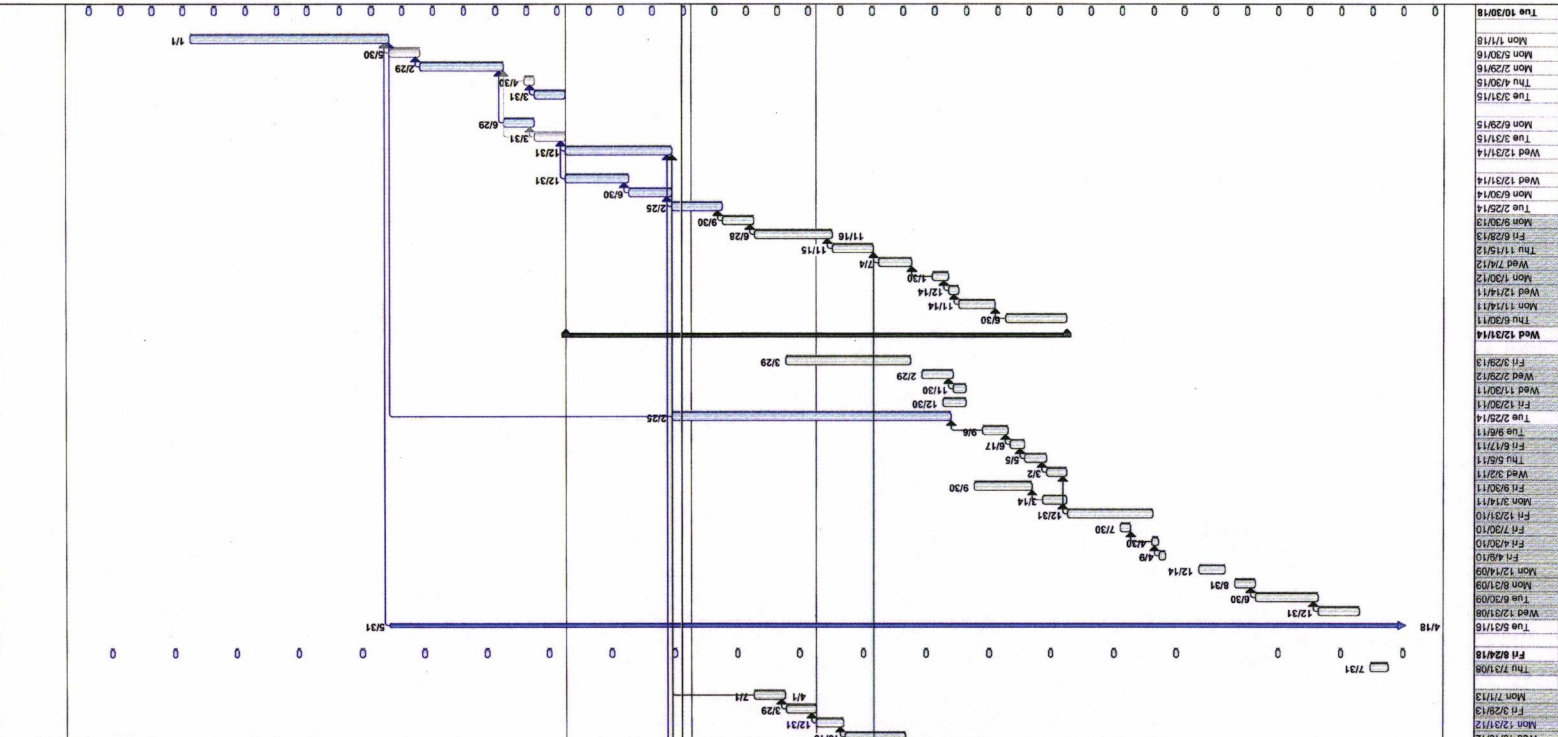

Task	Completed Task	Progress	Summary	Rollup Up Task	Rollup Up Critical Task	Rollup Up Milestone	Rollup Up Progress	Split	External Task	Project Summary	External Milestone Task	Progress	Critical Task
------	----------------	----------	---------	----------------	-------------------------	---------------------	--------------------	-------	---------------	-----------------	-------------------------	----------	---------------

Pressure Measurement Record

Administration Building, Technical Center, Control Laboratory

Technician Name: Jeremy Raye

Date: 12/27/2013

Equipment and Calibration

Pressure Meter Make, Model, and Identifier
Omniguard 4

Unusual weather conditions ☐ yes ☒ no

Units
☒ in WC
☐ _____

Zero Calibration

☒ Pass ☐ Fail

Pressure meter reads 0.000 when both ports are open to ambient air.

Pressure measurement requires a differential pressure meter (aka micromanometer) with a resolution of 0.01 inches of water (in WC) or less (0.001 preferred). The recorded pressure measurement will be the average of readings collected over a half-hour time span (to avoid ephemeral pressure changes such as wind gusts).

Administration Building

	Time	Half-Hour Average Differential Pressure (in WC)	Minimum Effective +0.001 in WC	Notes
Second Floor	11:25	0.031	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	
Cafeteria	10:50	0.007	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	
Basement	10:10	0.002	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	

Note: Inlet 1 should be open to indoor air. Inlet 2 (Reference) should be connected to the outdoor air tubing.

Technical Center (R&D Lab)

	Time	Half-Hour Average Differential Pressure (in WC)	Minimum Effective +0.001 in WC	Notes
North Basement	12:40	0.028	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	
South Basement	12:00	0.007	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	

Note: Inlet 1 should be open to indoor air. Inlet 2 (Reference) should be connected to the outdoor air tubing.

Control Laboratory

	Time	Half-Hour Average Differential Pressure (in WC)	Minimum Effective +0.001 in WC	Notes
Lab Area	13:20	0.027	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	

Note: This monitoring location is outside the building (unlike the Administration Building and Technical Center) and the tubing should be connected as follows: Inlet 1 should be connected to the indoor air tubing. Inlet 2 (Reference) should be open to outdoor air.

Notes:

All measuring points passed.

Upon completion, this form should be sent to the OXY Wichita Environmental Department (Lisa Blair) or Conestoga-Rovers & Associates (Doug Soutter: dsoutter@croworld.com).



Building Inspection Record

Administration Building, Technical Center, Control Laboratory

Technician Name: Jeremy Raye

Date 12/27/2013

Administration Building

Building Inspection Notes
(Building Envelope and Floors)

Second Floor	Good
Cafeteria	Good
Basement	Good

Additional details and corrective action

Technical Center (R&D Lab)

Building Inspection Notes
(Building Envelope and Floors)

North Basement	Good
South Basement	Good

Additional details and corrective action

Control Laboratory

Building Inspection Notes
(Building Envelope and Floors)

Lab Area	Good
----------	------

Additional details and corrective action

Upon completion, this form should be sent to the OXY Wichita Environmental Department (Lisa Blair) or Conestoga-Rovers & Associates (Doug Soutter: dsoutter@craworld.com).

