



Site 12 Field Work Progress Former Naval Station Treasure Island

August 2014 RAB Meeting
Chris Yantos, Project Manager
Contracted Support for Navy BRAC

8/20/2014

Current Field Work at Site 12



1. Radiological Housing Surveys
2. Solid Waste Disposal Area (SWDA) Building Demolition (Phase III)
3. Bigelow Court Radiological and Chemical Cleanup

Radiological Housing Surveys



Surveys 100% complete as of August 19

- 50 full days of surveying
- 794 residential units and garages completed
- 3 areas of elevated activity above background

All 3 elevated areas were determined to have no immediate health concern

- In-house readings result in a radiation dose of less than 10 mrem a year

Residents were notified of survey results and human health risk assessment by letter from TIDA

Other observations during field work

- *Some toilets, tile floors/walls, clay bricks, contained elevated natural radioactivity separate from objects of concern*
- *Naturally occurring; no letter from TIDA*

3

BRAC Program Management Office

Elevated Survey Results June 30, 2014



| <u>Date</u> | <u>Location</u> |
|-------------|----------------------|
| 06-30-2014 | Hallway near kitchen |

- **Dose calculation: 5.5 mrem/yr**
- Reading at 12" inches: 8.8 uR/hr
- Reading on contact: 20 uR/hr
- Background: 3.6 uR/hr



4

BRAC Program Management Office

4

Elevated Survey Results July 29, 2014



| <u>Date</u> | <u>Location</u> |
|-------------|-------------------------------|
| 07-29-2014 | Living room - 3 feet off wall |

- **Dose calculation: 2.9 mrem/yr**
- Reading at 12" inches: 6 uR/hr
- Reading on contact: 16.0 uR/hr
- Background: 3.2 uR/hr



5

BRAC Program Management Office


5

Elevated Survey Results July 30, 2014



| <u>Date</u> | <u>Location</u> |
|-------------|-----------------------|
| 07-30-2014 | Exterior storage shed |

- **Dose calculation: 1.7 mrem/yr**
- Reading at 12" inches: 4.8 uR/hr
- Reading on contact: 12 uR/hr
- Background: 3.2 uR/hr

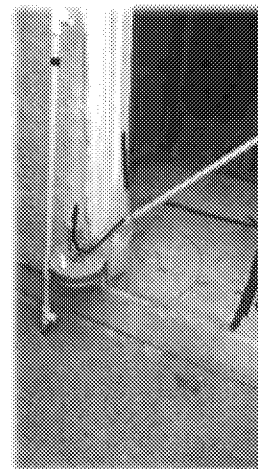

6

BRAC Program Management Office

6

SWDA Building Demolition



Buildings are being removed to allow for the investigation and excavation of contaminated soils beneath the structures

Buildings located in SWDA Westside, SWDA Bayside, SWDA North Point
1119, 1125, 1319, 1207, 1209, 1211, 1213, 1231, & 1233

- Prior to demo, all buildings will undergo asbestos removal
 - Began on August 11 in building 1125, and will continue at buildings 1119 and 1319
- Building demolition is scheduled for September 2 - October 24
 - Start at SWDA Westside; complete in SWDA North Point
- In January 2015, the Navy will be excavating and removing any contamination that may be present under these buildings

7

BRAC Program Management Office



SWDA Bigelow Field Work Status




- On July 21 and 30, two radiologically elevated areas were found on RSY pads.
 - Two objects removed
- Planned excavation extent has been met (map on separate slide)
 - Performed step-outs in Area L (lead) and Area G (PCBs)
- Four radiological screening pads are currently filled with 1,700 cubic yards of excavated soil
- Radiological scanning and sampling completed on three screening pads
 - Fourth pad used for soil from step-outs and soil/gravel sorting.
 - Awaiting gamma spec analytical data
- All chemical and radiological confirmation samples collected,
 - ~90% of chemical analytical results received
 - radiological analyses are pending.

8

BRAC Program Management Office

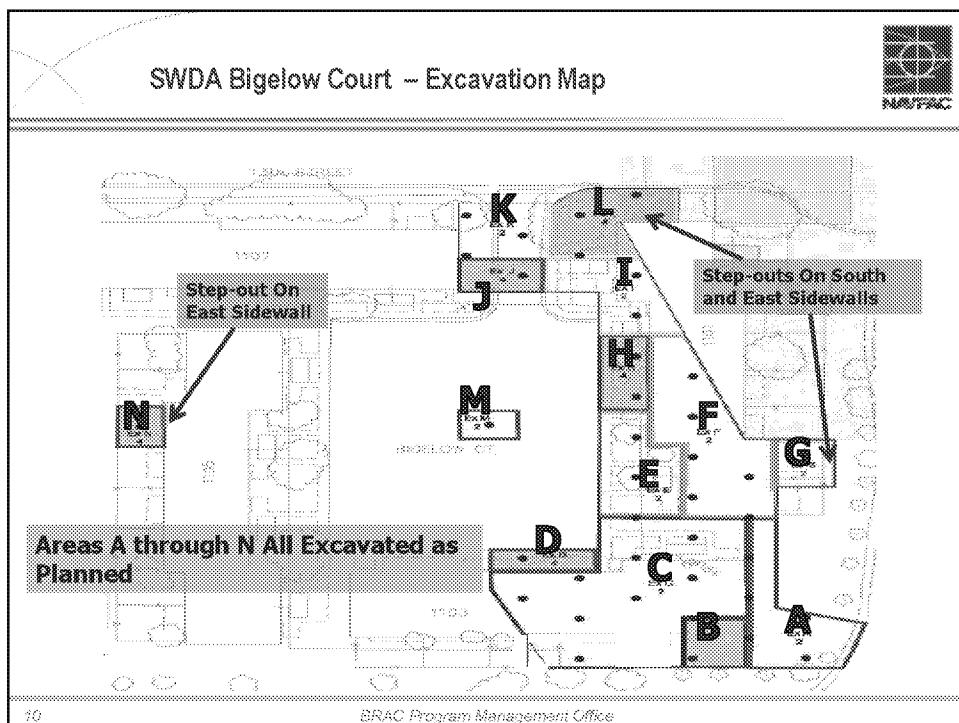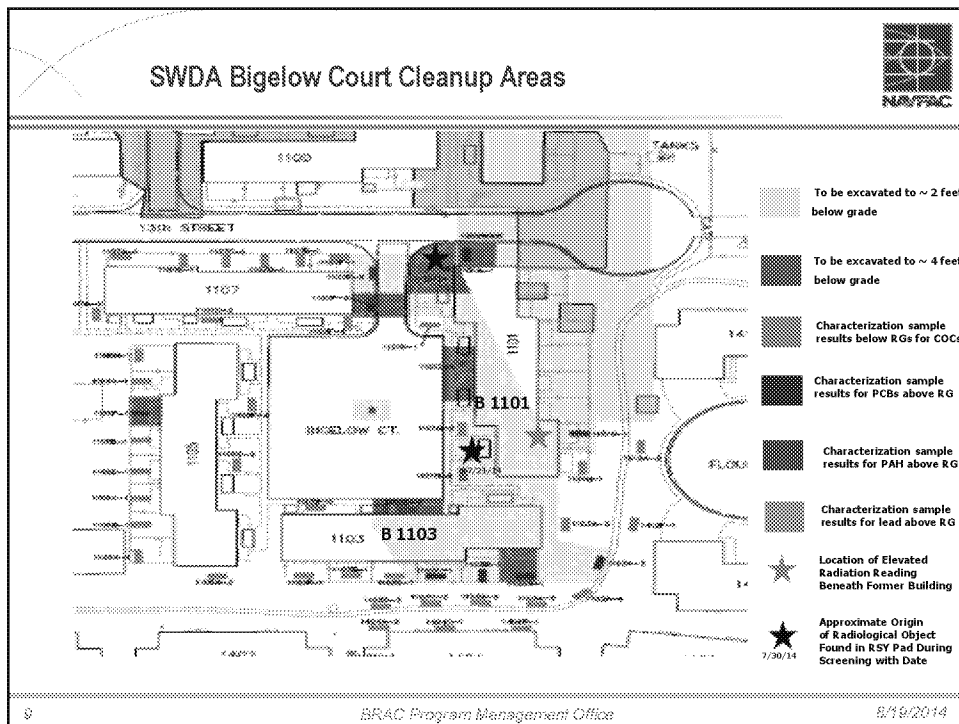


SWDA Bigelow Court – Chemical Confirmation Sample Map

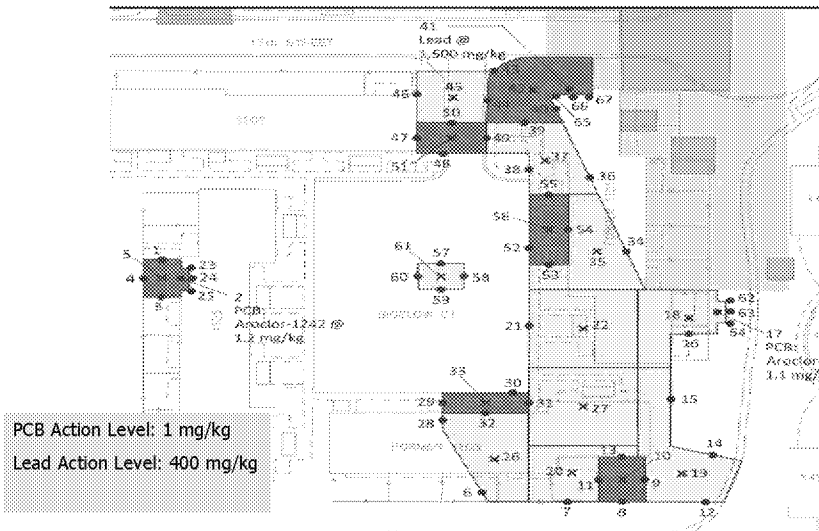


11

BRAC Program Management Office

SWDA Bigelow Court Object Removal

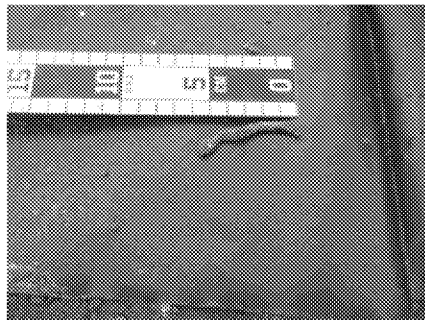

July 21 (copper pipe segment) – origin Excavation Area E.
Dose reading with NaI detector was 26 uR/hr at 12 inches

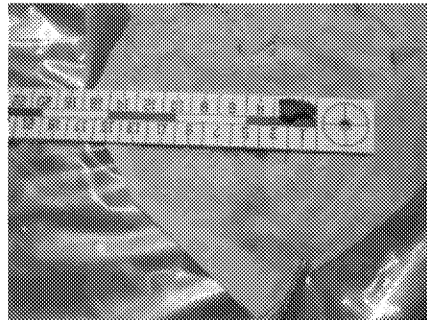

July 30 (metal fragment) –origin Excavation Area L2.
Dose reading with NaI detector was 10 uR/hr at 12 inches

12

BRAC Program Management Office

SWDA Bigelow Court Excavation



Screening rock from soil in the excavation areas



Gamma survey in Excavation Area D

13

BRAC Program Management Office

SWDA Bigelow Court Excavation



Excavation in area L



Sidewall sampling location

14

BRAC Program Management Office

SWDA Bigelow Court Cleanup Schedule



- **In Progress** (May 15 – Early September): Cleanup Field work
- **October 2014:** Draft Characterization Report/Final Status Survey Work Plan
- **March 2015:** Draft Post Construction Summary Report/Radiological Survey Report

15

BRAC Program Management Office



QUESTIONS?

16

BRAC Program Management Office
