

**Monthly Progress Report #1
July 17, 2009**

**U.S. EPA Region 5 / VIM Recycling, Inc.
Administrative Consent Order # EPA-5-09-113(a)-IN-05**

Introduction

On June 29, 2009, VIM Recycling, Inc. entered into an Administrative Consent Order (ACO) #EPA-5-09-113(a)-IN-05 with the United States Environmental Protection Agency, Region 5. The ACO contains a 'Compliance Program' that VIM Recycling, Inc. must follow in order to stay in compliance with the agreement. The VIM Recycling, Inc. facility referenced in the ACO is located at 29861 Old US Highway 33 in Elkhart, Indiana.

A detailed 'Compliance Program' is set forth in paragraphs 26 – 58 of the ACO. In general, the program stipulates the following:

- Monitoring for and control of fire, smoke, dust and odors from stockpiled debris,
- Monitoring and surveillance of the stockpiled debris to detect fires,
- Recordkeeping, documentation and reporting of progress to EPA and IDEM,
- Sorting, screening and removal the larger fraction (greater than 4 inches) of construction and demolition debris found in stockpiles C-1 and O-1 (delineated in Attachment 1),
- Placement of the smaller fraction (less than 4 inches) of the debris sorted and screened into engineered windrows on site.

The C-1 pile contains construction and demolition debris mixed with soil and must be sorted and screened prior to removal from the site for disposal. The O-1 pile contains larger fraction material (4" or greater) which was previously screened out and will not require sorting or screening prior to removal from the site. A topographic map of the C-1 pile dated May 20, 2009 is found in Attachment 2. The ACO stipulates that additional construction and demolition debris cannot be placed within the limits of either the C-1 or O-1 pile, and that no grinding of materials can take place.

Finally, the ACO requires development of a contingency plan for possible emergencies which may occur during the project and a provision to establish a website to keep the public apprised of progress on the removal project.

The following report reviews the progress made to implement the ACO between June 29, 2009 and July 5, 2009, which is the month end for general accounting purposes for VIM Recycling, Inc.

Progress Report

This report is divided into two sections, the administrative aspect of the ACO and the field activities aspect of the ACO. A summary of these respective activities during this reporting period is found below.

Administrative Management Activities Update

- The ACO was signed by Mr. Kenneth Will on June 25, 2009 and submitted to U.S. EPA Region 5 the same day.
- On June 29, 2009, the ACO was executed by Ms. Cheryl Newton, Director of the U.S. EPA Region 5 Air & Radiation Division.
- An executed original of the ACO was received by express mail at VIM Recycling, Inc. on July 2, 2009.
- VIM Recycling, Inc. contacted the U.S. EPA Region 5 field personnel and immediately began work to implement the ACO.
- A weekly progress report format was developed and proposed to U.S. EPA for consideration on July 1, 2009. This form was accepted and is found in Attachment 3.
- A three-ring binder was established to log required documentation pursuant to the ACO on site in the main trailer. Agency personnel are provided access to the binder upon request.
- Meetings were held with Mr. Kim Davis at the Elkhart County Landfill and Mr. Tom Wilson at the Earthmovers Landfill to assess and discuss disposal options and procedures for the C-1 and O-1 pile materials which will require disposal on July 2, 2009.
- A general staff meeting was held between all employees of VIM Recycling, Inc. and U.S. EPA Region 5 field personnel on July 2, 2009 to clarify expectations on both operations and safety procedures to be adhered to during the project.
- The VIM Recycling, Inc. main website (<http://www.vimrecycling.com>) will be updated to include monthly progress reports (which contain all weekly reports), photographs to show current conditions of the C-1 and O-1 piles, and equipment being utilized during the project. Contact was made with Holt Communications to update the project website.

Field Activities Update

- Grading and placement of stone was conducted to establish an access, equipment staging and vehicle turn-around area in the southwest corner of the C-1 pile (see Photo Log photo #1).
- Grading of areas adjacent to the C-1 and O-1 piles was initiated to establish adequate area for placement of the smaller fraction (less than 4 inches) of the debris to be screened in engineered windrows. This activity involved establishing positive drainage for the areas where the material will be windrowed.

- The height of the O-1 pile was reduced to facilitate safe excavation and removal of debris contained within the pile into large trucks or containers for transport off site.
- Heavy equipment to be used in the project for excavation, screening and transport was brought to the site and maintenance and cleaning was performed in preparation for start-up of sorting and screening operations. See Photo Log photos #2, 3 and 4 for details on the equipment anticipated to be used during the project.

Paragraph 43 of the ACO requires Weekly Progress Reports to be submitted to U.S. EPA each Monday. The following Weekly Progress Reports corresponding to the reporting period for this Monthly Progress Report are identified in the table below.

Weekly Report #	Reporting Period
1	6/29 – 7/5

Copies of the Weekly Progress Reports are found in Attachment 4.

Anticipated Activities Next Month

- Certification reports will be obtained for the scales at the VIM Recycling, Inc. facility and the destination facility selected for material disposal to comply with Paragraph 41 of the ACO.
- During the month of July, it is anticipated that sorting, screening and removal activities on the C-1 and O-1 piles will commence. It is fully expected that the weekly target stipulated in Paragraph 33 of 1000 cubic yards per week will be met or exceeded.
- Meetings will be scheduled with local and state officials to advise them of the ACO, provide an overview of planned activities to remove, transport and dispose of the materials, and answer any questions.
- A field survey will be conducted and an updated topographic map of the C-1 stockpile will be finalized and submitted to comply with Paragraph 44 of the ACO.

- A draft Site Emergency Plan will be developed to comply with Paragraph 52 of the ACO and submitted by the deadline of July 21, 2009. A meeting will be held on site with the Baugo Fire Department, Elkhart County Emergency Management Agency, the Indiana Department of Environmental Management Emergency Response Branch, and the U.S. EPA Region 5 to provide a general site orientation and overview of the plan. Comments, input and suggestions will be solicited and incorporated into a draft which will be submitted to U.S. EPA as required. Copies of the finalized document will be provided to all parties referenced above.
- The VIM Recycling, Inc. website will be updated to comply with Paragraph 56 of the ACO to provide the public with updates on progress made to remove stockpiled materials in the C-1 and O-1 piles.

Contact Information

Copies of all reporting and documentation required by the ACO are available on site for review at any time by Agency personnel. Any questions regarding this Monthly Report should be directed to:

Mr. Kenneth Will
VIM Recycling, Inc.
29861 Old US Highway 33
Elkhart, Indiana 46516
Phone: 574/642-3677
Email: kwill05@comcast.net

Report Submittal

As required by Paragraph 57 of the ACO, copies of this report were submitted to the following entities:

Attention: Compliance Tracker (AE-17J)
Air Enforcement and Compliance Assurance Branch
U.S. EPA Region 5
77 West Jackson Boulevard
Chicago, Illinois 60604

Attention: Mr. Bruce Palin
State of Indiana Department of Environmental Management
Office of Land Quality (MC 66-30)
100 North Senate Avenue
Indianapolis, Indiana 46204-2251

Signature:


Kenneth Will, VIM Recycling, Inc.

Site	Monthly Report	PAGE 1
VIM Recycling, Inc., Elkhart, Indiana	1	

Photo Log



Photo 1. VIM Recycling, Inc., Elkhart, Indiana.

Description: Gravel pad established at SW corner of "C Pile" for access, staging, vehicle turn-around

Date Taken: 7/2/09



Photo 2. VIM Recycling, Elkhart Indiana.

Description: Excavator, screener and bulldozer used for excavation and screening of "C Pile" materials

Date Taken: 7/13/09

3. Site Contact	Date
K. Will	07/17/09

Site Visit Photo Log



Photo 3. VIM Recycling, Elkhart, Indiana.

Description: Equipment dedicated to "O-1" stockpile excavation and removal

Date Taken: 7/13/09

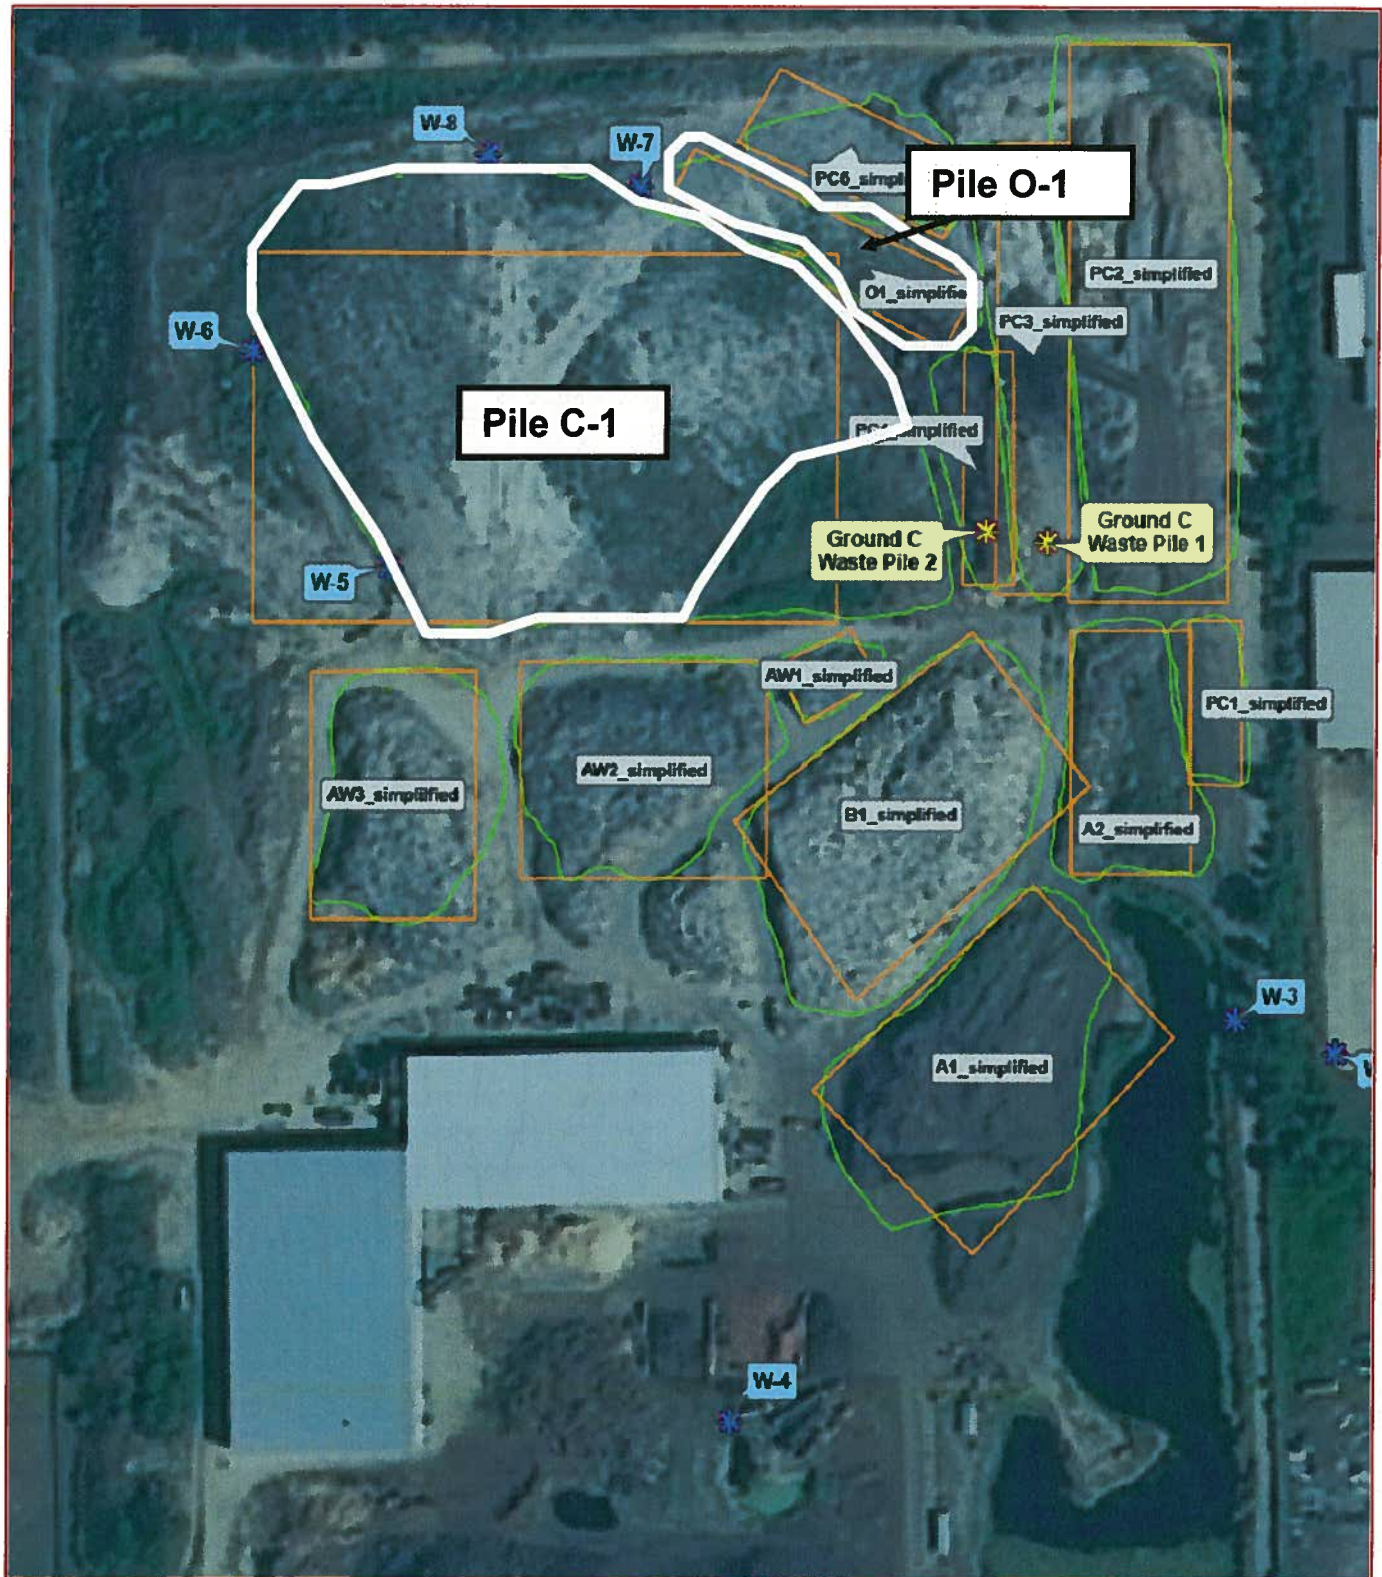


Photo 4. VIM Recycling, Elkhart, Indiana.

Description: Water truck utilized for dust control on roadways and fire suppression if necessary


Date Taken: 7/2/09

Attachment 1. Boundaries of “C Pile” material stockpiles to be addressed pursuant to paragraph 31 of Compliance Program*



***The precise limits of “C Pile” material stockpiles C-1 and O-1 may be adjusted by EPA in the field as the removal progresses.**

EXISTING GROUND TO C-PILE CUT = 0.35 CU. YD. FILL = 95540.78 CU. YD.

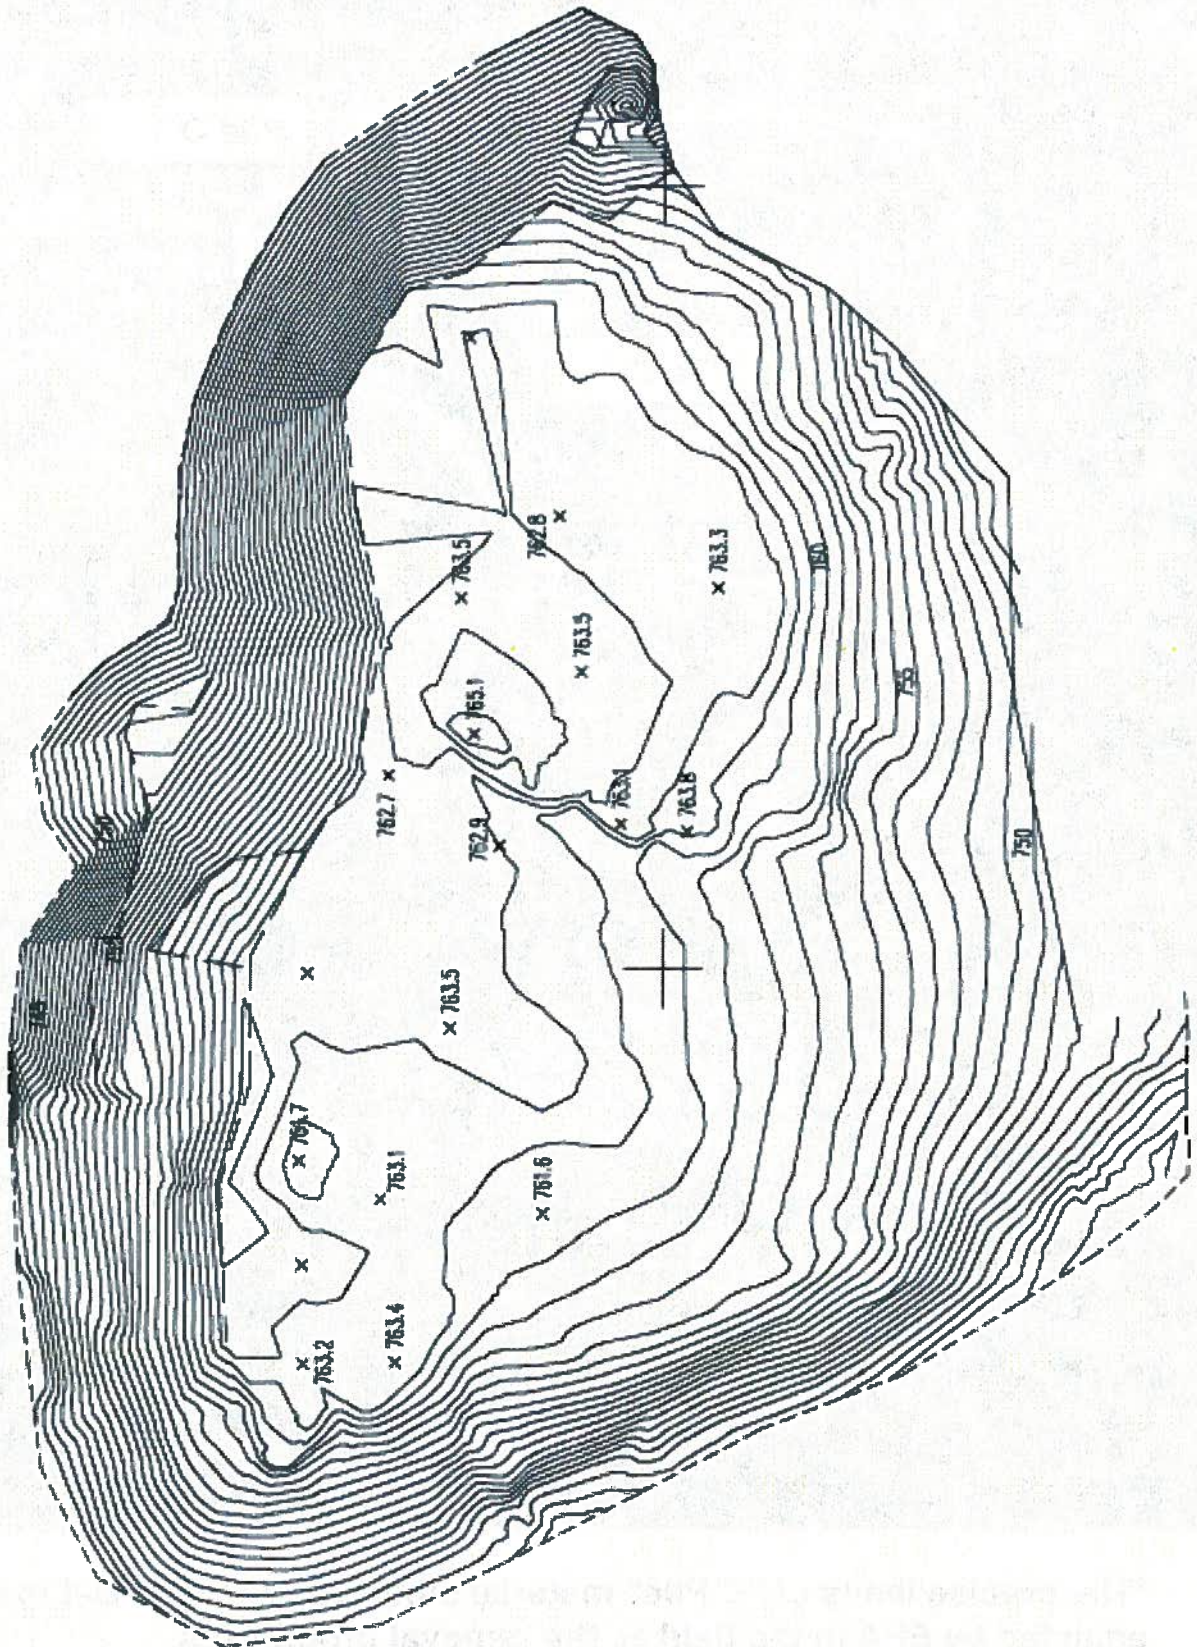

Attachment 3. Weekly Progress Report Format

VIM Recycling, Inc.

Administrative Consent Order # EPA-5-09-113(a)-IN-05

Weekly Progress Summary

Report No.	<i>insert weekly report #</i>
Month	<i>insert month</i>
Date	<i>insert date report submitted</i>
Period	<i>insert dates covered by report</i>

PARAGRAPH	REQUIREMENT	DETAILS
28a, 28b, 43a	Soil and water placement	<i>Provide details (dates, locations, estimated amounts) of soil and/or water placed on smoldering, smoking or burning areas of the C pile(s) covered by the Order</i>
43b	Material removed from site	<i>Provide amount of C pile overs removed from the site during the reporting period in tons and yd³</i>
43d	Cumulative total removed	<i>Estimate the TOTAL amount of C pile overs removed from the site in yd³ to date</i>
43c	Volume left on site	<i>Estimate the amount of screened C pile material left on site during the reporting period in yd³</i>
43e	Cumulative total left on site	<i>Estimate the TOTAL amount of screened C pile materials left on site in yd³ to date</i>
40, 43f	Load tickets	<i>Insert the number of C pile load tickets retained in records on site during reporting period</i>
43g	Dedicated equipment on site	<i>List out the equipment (dozers, backhoes, loaders, screeners) dedicated to C pile removal during the reporting period</i>
43h	Dedicated personnel on site	<i>List the personnel dedicated to C pile removal during the reporting period</i>
43i	Anticipated resources next week	<i>List the equipment, personnel and anticipated work activities on C piles for the next reporting period</i>
44	Update topographic map	<i>Yes or No if C pile topographic map updated during reporting period and/or date of last update</i>
48, 49	Surveillance activities, reports	<i>Confirm surveillance activities here and note any observations or occurrences outside the normal (i.e., smoke, fires, etc.)</i>
55	Site emergency plan	<i>Yes or No if plan in effect and provide information on any notifications or if plan put into effect during reporting period</i>
56	Informational website	<i>Yes or No if website operational / accessible during reporting period and date of most recent update</i>
	Agency personnel on site	<i>List the names & dates of IDEM or EPA personnel visiting site and date(s)</i>

Notes: *Special notes or clarifications (i.e., topo attached, incidents reported, accidents, etc)*

Prepared by: *Name of person preparing report and date*

ATTACHMENT #4

COPIES OF WEEKLY REPORTS

SUBMITTED DURING

REPORTING PERIOD

Weekly Report #	Reporting Period
1	6/29 – 7/5

VIM Recycling, Inc.
Administrative Consent Order # EPA-5-09-113(a)-IN-05
Weekly Progress Summary

Report No.	1
Month	<i>Jun-09</i>
Date	<i>7/6/2009</i>
Period	<i>6/29/09 TO 7/5/09</i>

PARAGRAPH	REQUIREMENT	DETAILS
28a, 28b, 43a	Soil and water placement	<i>PRIOR TO 6-29-09 TOPSOIL WAS PLACED ON NORTH SIDE OF "C" PILE UNDER EPA SUPERVISION</i>
43b	Material removed from site	<i>NONE</i>
43d	Cumulative total removed	<i>NONE</i>
43c	Volume left on site	<i>NONE</i>
43e	Cumulative total left on site	<i>NONE</i>
40, 43f	Load tickets	<i>NONE</i>
43g	Dedicated equipment on site	<i>1400 WARRIOR, 330BL CAT EXCAVATOR, JD750 DOZER</i>
43h	Dedicated personnel on site	<i>AARON LEHMAN & JOSE MOLINA</i>
43i	Anticipated resources next week	<i>1400 WARRIOR, 330BL CAT EXCAVATOR, JD750 DOZER, AARON LEHMAN & JOSE HERNANDEZ & JOSE MOLINA</i>
44	Update topographic map	<i>NO, CURRENT TOPOGRAPH DATED JUNE 2009</i>
48, 49	Surveillance activities, reports	<i>JESSE PALOMINO (7-4-09), AARON (7-5-09)</i>
55	Site emergency plan	<i>UNDER DEVELOPMENT</i>
56	Informational website	<i>UNDER DEVELOPMENT</i>
	Agency personnel on site	<i>R. ROUDEBUSH, J PALIN (7-1-09), P RUESCH (7-2-09)</i>

Notes: *ACTIVITIES INCLUDED PAD PREP FOR "C" PILE MANAGEMENT*

Prepared by: *KEN WILL 7/6/09*

