



## Parcels UC-1 and UC-2 RA




# Remedial Action in Parcels UC-1 and UC-2, Hunters Point Naval Shipyard



Hunters Point Naval Shipyard BCT Meeting



# Parcel Map

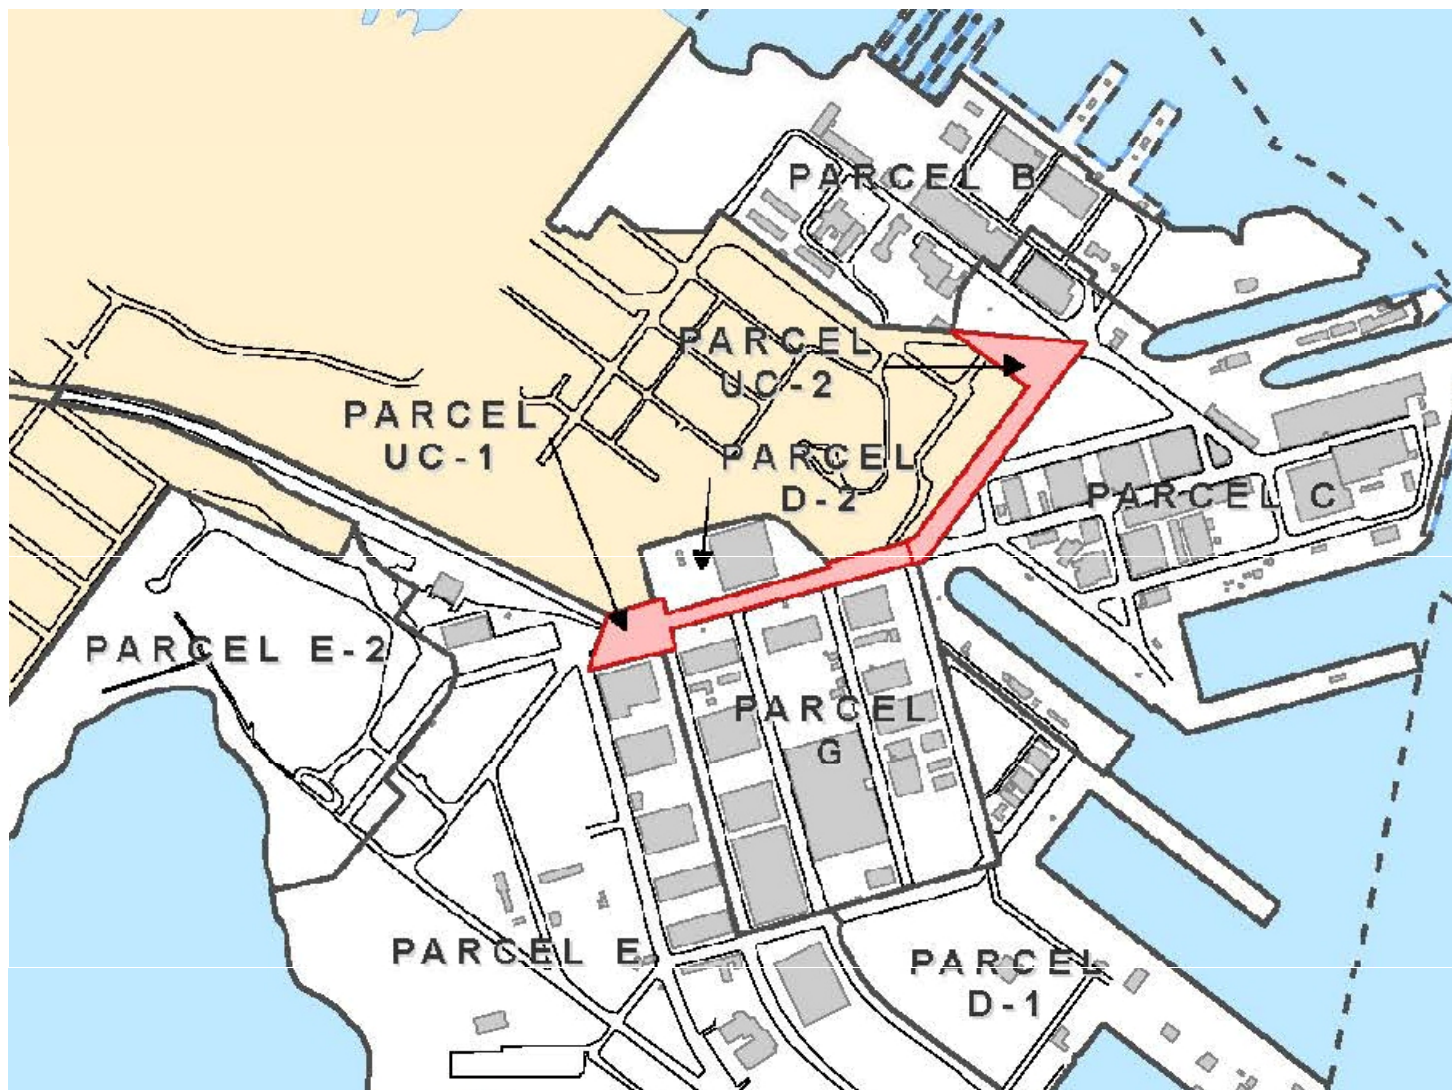


Hunters Point Naval Shipyard BCT Meeting



# Presentation Overview



- **RA Implementation Update**
- **RA Schedule Update**
- **RA Photos**



# RA Implementation Update



- Soil cover installation completed on slopes; including installation of 2 feet of clean soil, erosion control fabric, and live plants (strawberry, poppy, and lupine).
- Subgrade restoration completed in damaged areas of Fischer Ave., Spear Ave., and Robinson St.
  - Excavated to competent material
  - Installed and compacted new subgrade material (Class II AB)
- Asphalt grinding performed to remove pavement surface in areas to receive asphalt overlay
- Fence posts installed along parcel boundaries; fence fabric to be installed prior to demobilization
- Paving in progress






## RA Schedule Update



- Mobilization (completed): May 14
- Clearing and Grubbing (completed): May 16 – Jun 11
- Soil Excavation (completed): Jun 4 – Jul 6
- Soil Cover Installation (completed): Jun 25 – Jul 19
- Cover Stabilization & Vegetation (ongoing): Jul 19 – Aug 24
- AC Restoration and Replacement (ongoing): Jul 24 – Aug 27
- Site Cleanup, Final Survey, and Demobilization: Aug 27 – Aug 29
- Excavated Soil and Waste T&D: Aug 29 – Sep 11
  
- One year of O&M following RA completion Aug 2012 – Aug 2013
  - Vegetation establishment
  - Site inspections
  - Periodic pavement repair/maintenance



# Stabilized Slopes and Live Plants



Hunters Point Naval Shipyard BCT Meeting





# Road Subgrade Excavation



Hunters Point Naval Shipyard BCT Meeting



# Subgrade Excavation Completed



Hunters Point Naval Shipyard BCT Meeting





# Subgrade Restoration



Hunters Point Naval Shipyard BCT Meeting
