

**BAYONNE BARREL & DRUM****REPORT #** 35**O.S.C.** JOE COSENTINO  
**R.M.** M.R.ELLIS**DATE:** 11/11/94

**DESCRIPTION OF DELIVERY ORDER:** Mobilize necessary personnel and equipment to facilitate removal action. Overpack, sample, haz-cat drummed waste on site, to include storage tanks above & below ground, pits, gutters, courtyard and ash/soil piles. Proceed with T & D of drummed waste, rubber, ash/soils and drums related to shredding operations. Further provide any additional support needed to assist with the site removal per the O.S.C.

**LOCATION OF WORK:** 150 RAYMOND BLVD. NEWARK, NJ 07105

**WEATHER:** Sunny**TEMPERATURE:** 55**WORK PERFORMED TODAY BY OHM:**

- \* Continued the drum shredding operation, due to colder than normal temperatures, additional time is given for the power pack to warm up prior to starting the shredding.
- \* At 1300 hrs. crew shuts down for lunch. Between 1330 and 1430, general cleanup of the area is performed, crew demobilizes for week end having shredded 327 drums today.

**SUBCONTRACTOR SERVICES PERFORMED:**

- \* Schiavone - Bonomo pick up 20 yard can and deliver 2 empty cans today.
- \* Duffy Fuel - delivery today.
- \* Hertz - notified of problems with the bobcat, will be on site Monday morning to repair.

**EXCEPTIONS / UNUSUAL CONDITIONS:**


- \* Follow up call to City Fire & Extinguisher Services, Paul Mundy who informs me that Monday he should be receiving the necessary components to complete the suppression system.

**CHANGE IN METHOD OR SCOPE, SPECIFIC DIRECTION RECEIVED FROM OSC:****DOCUMENTS SUBMITTED:****MEETINGS HELD, SUBJECT MATTER, DIRECTION AND OR DECISIONS:****COMMENTS:**

- \* Crew shuts down field operations today @ 1345 hrs. Perform general cleanup of the work area.
- \* Demobilize operator / mechanic Todd Hicks, flown back to corporate office.



Drum Progress	Drums Shredded	Poly Liners Removed	Steel Removed
M 10/31		38	
T 11/01			
W 11/02		105	
T 11/03			
F 11/04		93	
M 11/07		57	
T 11/08	10	119	
W 11/09	366		
T 11/10	525		8.08
F 11/11	327		?
TOTAL	1228	412	

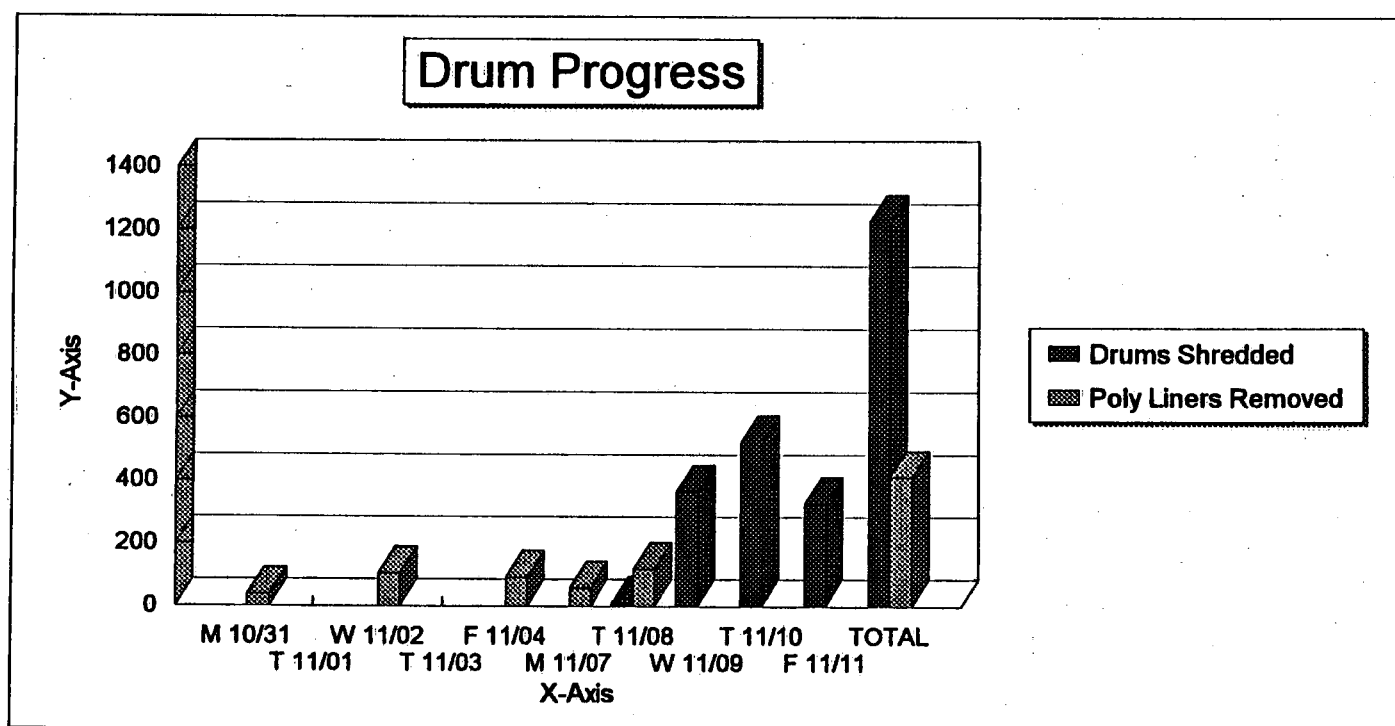

Drum Progress	Drums Shredded	Poly Liners Removed	Steel Removed
M 10/31		38	
T 11/01			
W 11/02		105	
T 11/03			
F 11/04		93	
M 11/07		57	
T 11/08	10	119	
W 11/09	366		8.08 ton
T 11/10	525		
TOTAL	901	412	

