

1900694 - R8 SDMS

From:

Thomas J. Krasovec <TJKrasovec@Geosyntec.com>

Sent:

Thursday, March 8, 2018 11:57 AM

To:

Ackerman, Joyce

Subject:

Confirmation Sampling of Phase 3

Attachments:

FIG3 DRFAT.pdf

Joyce,

We are hoping to complete confirmation sampling of Phase 3 excavation either tomorrow or Saturday. Our intention is to dig 1 to 2' into the floor where possible as well as the side walls. Based on currently available survey data, draft attached we will need approximately 5 side wall samples and at least 2 floor samples to meet the DRWP criteria. The samples will be submitted for total VOCs, SVOCs and RCRA metals at a minimum . Please let me know if this is acceptable and I will advise you this afternoon if it will be tomorrow. If there is a problem in conducting the work in the next two days please advise me at your earliest convenience. Also if you would like additional sampling or analyses please let me know. If you have any questions I can be reached on my Cell number below.

Thanks TJK

Thomas J Krasovec
Senior Professional
Geosyntec Consultants


Ph: 720-509-8911 Cell: 517-719-4984

Geosyntec Consultants, Inc.

5670 Greenwood Plaza Blvd, Suite 540

Greenwood Village, CO 80111

This message and any attachments may contain confidential information protected by attorney-client or other privilege. If you believe this message has been sent to you in error, please reply to the sender that you received it in error and delete the message. Thank you

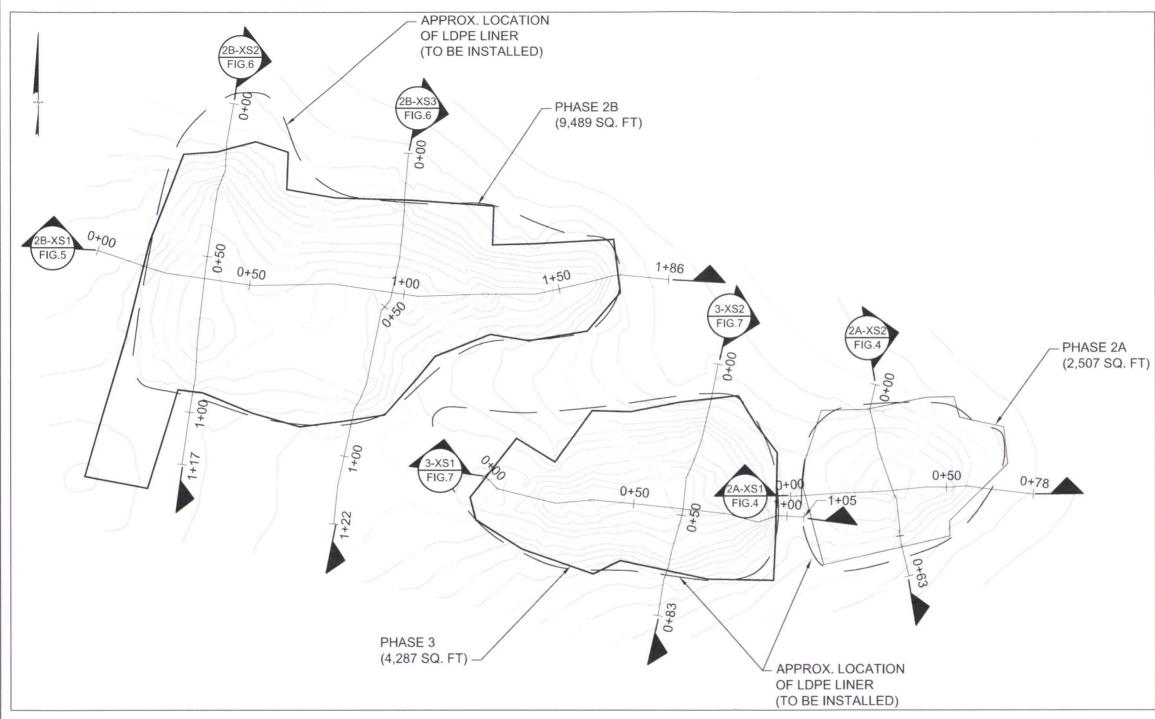



NOTES:

1. INFORMATION IS BASED ON SURVEY COMPLETED BY CWC ON 2-17-2018.

2. LINER TO BE ANCHORED INTO 1' DEEP TRENCH AROUND PERIMETER AND PLACED TO ALLOW FOR A SUMP AREA FOR PUMPING OF SURFACE WATER INTO THE FRAC TANK AS NEEDED.

DRAFT

NEUHAUSER LANDFILL SITE

PROPOSED INTERIM SHUT DOWN PHASES 2A, 2B AND 3 - PLAN VIEW

Geosyntec[▶]

consultants

FIGURE

PROJECT NO: DE0302

MARCH 2018

3

