

# FRIDAY - AXTELL


SEQUENCE	TASK	EXPLANATION	WHO	STATUS
A	Axtell Creek			
	Set turbidity monitors		EQ	
	Drop gabion basket at discharge		EQ	
	Set up street signs on Crosstown		EQ	
	Mobe in Long Reach Excavator w/ dredge bucket	need to stage for GPS mount set up	CMC	
	Weld up mounts on Long Reach	during holiday week	EQ	
	Install silt fence	20' wings off sheet piles, fix S bank	EQ	
	Set GPS post	by marked stump N of Lil' Belle	EQ	
	Install temp fence John St. sump area	6 panels along sidewalk from John St	EQ	
	Install ground rod fuel cell	hanging on fence post	EQ	
	Weld up 20yd Boxes	Use Plate	CMC	
B	SA5D SET-UP / BYPASS / GW DE-WATERING SYSTEM			
	Order & set croc for bypass sump	5' diameter?, hooks for lift, 4 - 2" bottom w/ holes for drain	EQ	
	Install bypass system	AFTER JULY 4, past Vine St bridge	sub	
	Install GW dewatering system	AFTER JULY 4, up to footbridge	sub	
	Curb cuts	AFTER JULY 4	sub	
	Fence off right-of-way in Upjohn Park	AFTER JULY 4, up to footbridge	sub	
	Fabric & mat righ-of-way in Upjohn	AFTER JULY 4, up to footbridge	EQ	
	Clear/Grub W bank	Start 7/13	Total	
	PR Stabilize Springfield Belle	pool chemicals, run during break?	OSC	

Thursday

US EPA RECORDS CENTER REGION 5



474174

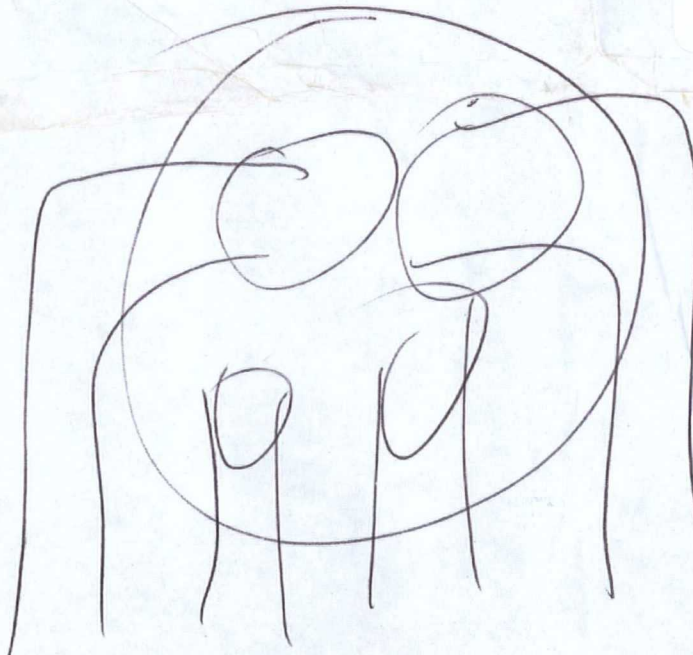

FRIDAY - AXTEL



# FRI DAY - SA 6

Portage Creek Area Site  
SA6 Demobe Checklist - update 6/28

SEQUENCE	TASK	EXPLANATION	WHO	STATUS
A	CREEK			
B	BYPASS / DEWATERING SYSTEM			
	Remove 30" discharge line		R4R	
✓	Remove fuel cells		R4R	FRI
✓	Remove spill mats		R4R	FRI
✓	Remove 24" pumps	stage 6" de-watering pumps & hardware at John St?	R4R	FRI
C	SUPPORT AREA			
✓	Remove heavy equipment attachments		EQ	FRI
	Remove Stockbridge street signs	move to Crosstown	EQ	FRI
	Sweep School barn & SA6 pavement	power wash barn lot <i>Adv Rain for this</i>	EQ	FRI
D	RESTORATION			
✓	Re-configure temp fence at Stockbridge	leave 4 panels across fence line, bring rest to John St	EQ	FRI
	Smooth out rail spur ballast	concurrent w/ removal of 30" pipe	EQ	
✓	Scrape W bank	move rock to Lake St. bypass pump staging area	EQ	WED/THUR
	Fix Ron's yard	level yard, seed, rear fence sections, after 30" gone	EQ, sub	
✓	Fix bank around croc	remove grate/posts, fill in sump w/ riprap, shape bank	EQ	FRI

Thursday 7/5

- Bake change at pumps / fix discharge / re-site containment
- MI laser calibrate GPS
- Ran bell 45 min.
- Fixed fence @ John St.

2A2 - 1A9 157
