

PAU

Portage Creek Area Site
Demobilization Plan - UPDATE 10/22

AREA	TASK	EXPLANATION	WHO	TARGET	
A	Axtell Creek				
	Touch up Lake St sump area	cover rock on banks, coir logs	EQ	10/24	
	Temp fence S bank	lot side of guard rail start at parking lot moving E	EQ	10/26	
	Top off bentonite w/ sand	N banks	EQ	ASAP	
	Restoration		KV		
B	SAS-C				
	Thurs Install exit logs SW corner	where pipes come up on bank	EQ	10/23	
	Thurs Remove bypass pipelines	lines 2 on base of 1A to SAS	EQ	10/23	
	Thurs Fill in de-watering well holes	W bank under discharge pipes	EQ	10/26	
	Thurs Touch up Vine St bridge	cover rock, bank run in hole, coir logs W bank off wing	EQ	10/26	
	Thurs Grade & top dress impacted areas	impact area on 1A	EQ	ASAP	
MON	Remove apron/curb cut	see Debbie sheet	Quality		
	Restoration	start on E bank	KV	10/29 → start, then SD next	
C	SAS-D				
	Demolish 12' pumps	ES&E trucks on Lake St	EQ	10/23	
	Touch up Lake St sump	fill jersey barriers, float, fill sump, cover rock, coir log	EQ	10/23	
	Remove rock from Lake St sump area	put on log pile	EQ	10/23	
	Save porta potties to staging area	demolish garbage can	EQ	10/25	
	Install footbridge approaches	garbage	EQ	10/25	
	MON	Remove temp fence	Upjohn, Youth Center side of sump	Farm & Garden	10/25 → 10/29
Sign	Grade & top dress impacted areas	high banks and Lake St sump pad	EQ	10/25	
	Remove apron/curb cuts/sidewalk repairs	see Debbie worksheet	Quality	ASAP	
	Restoration		KV	ASAP	
X	Post construction surveying		PAU	10/25 → need to process samples	
D	SASA				
	Remove access bank	cut bank	EQ	10/25	
	Thurs Stage discharge pipe on E bank	sections of 12' cut down w/ T posts & wire	EQ	10/25	
	Kook Ct Access Agreement	meet w/ property owners 0930	Paul	10/25 → 10/29 return to staging pad	
E	SA3A				
	Remove trash	from staging area and along banks	EQ	10/23	
	Cut down weeds	access road & staging area	EQ	10/23	
	Build access road/staging pad	clear bank area, dirt on pad (fillion loader)	EQ	10/23	
	Thurs	Clear & grub banks	NVI property only 20% done	Total	10/24 → start
	Thurs	Clean up rock pad	pull fabric, honeycomb	EQ	10/25
	Load out debris pile	at entrance Fulton load(s) to C&C	EQ	10/25	
WED	Dr. Sarah video - road cut / not in 3A	file/map from Kevin		10/	
	Pre-sampling in 3A				
F	STAGING PAD				
	Remove tires	Mark called last week	Tire Reclaimers	10/25	
	Extend temp fence to creek	put up panels w/ sand bags to creek edge	EQ	10/25	
	Scrap steel	return yellow bin	Shupan	10/26	
	Remove orange fence from staging pad	post 'Keep Out' signs on 1 T-post on each side	EQ	10/26	
	Decon & demobe AIS heavy equipment	300, broom, H2O trk, 329, 800's, 250, 380, atts (wipes)		ASAP	
	Demobe porta potties and sink	3 left / 1 sink	Plummers	10/30	
	Load Conex box	bentonite chip pallets, xtra coir logs		10/30	
	Call off garbage dumpster		Plummers	10/30	
	Empty fuel cell	keep tank for winter, re-do secondary containment		10/30	
Remove water meter from hydrant	keep in crew trailer	EQ	10/30		
G	SA7				
	Thurs Topsoil & seed on parkway	1 bucket to Reed St. Entrance, seed & straw down	EQ	ASAP	
F	ADMINISTRATIVE				
	Post inspection	2 w/ Remo 10/2	PAU		
	Post-construction survey	SASD / Axtell	FIELDS	ASAP	
	Post-removal structural assessment		(P&V)	ASAP →	
	camp wireless	Comcast Charter	PAU		

~~idea on pad?~~

Pumps at sump

~~AX~~

NOT DONE

E bank river rock

need to process samples

return to staging pad

10/15 → [good time]

SASC


3000 decon/wipe 10/25

FRIDAY

Portage Creek Area Site

Demobilization Plan - UPDATED ~~10/22~~ **10/25**

AREA	TASK	EXPLANATION	WHO	TARGET
A	Axtell Creek			
X	Temp fence S bank	lot side of guard rail start at parking lot moving E ✓	EQ	10/26
	Restoration		KV	ASAP
B	SAS-C			
	Remove apron/curb cut	see Debbie sheet	Quality	10/26 10/29
	Restoration	E + W banks	KV	10/29
C	SAS-D			
X	Extend south perimeter fence	install 4 panels out toward creek ✓	EQ	10/26
	Remove temp fence	Upjohn, Youth Center	Farm & Garden	10/29
	Remove apron/curb cuts/sidewalk repairs	see Debbie worksheet	Quality	10/29
	Replace short fence at Lake St	W bank 4' fence	Farm & Garden	10/30
	Restoration		KV	ASAP
	Lake St. Touch-Up	Pull out wood @ south corner X Coir logs Youth Center ✓		
D	SASA			
X	Lash down 18" pipe	4 sets of T-posts w/ wire across top ✓	EQ	10/26
E	SA3A			
X	Bring junk to front pile	stage on pile of ties, asphalt at Michigan St entrance ○	EQ	10/26
X	Clear channel	for chipping ✓	EQ	10/26
	Chip up trees + brush	load out logs ✓	Total	10/26
	Load out debris pile	at entrance Fulton load(s) to C&C	EQ	10/29
	Pick up trash	another sweep w. trees down	EQ	10/29
	Put big rocks across entrance	to prevent access, get from behind Little Belle	EQ	10/29
F	STAGING PAD			
X	Extend temp fence to creek	put up panels w/ sand bags to creek edge ✓	EQ	10/26
X	Decon & demobe AIS heavy equipment	250 loader + attachments, Komatsu ✓	EQ	10/26
X	Load EQ trailer	tools, equipment to warehouse ✓	EQ	10/26
X	Put coir logs in ConEx box	after install ✓	EQ	10/26
	Scrap steel	return yellow bin	Shupan	10/29
	Fix up orange fence on staging pad	post 'Keep Out' signs on 1 T-post on each side	EQ	10/29
X	Pump out staging pad sump	10,000 gal	EQ	10/29
	Decon & demobe AIS heavy equipment	street sweep, water truck, 380 loader	EQ	10/29
	Demobe porta potties and sink		Plummers	10/30
	Put garbage dumpster	stage next to trailers	Plummers	10/30
	Empty fuel cell	keep tank for winter, re-do secondary containment	Kalamazoo Oil	10/30
	Remove water meter from hydrant	keep in crew trailer	EQ	10/30
	Remove tires	Mark called last week ✓	Tire Reclaimers	ASAP
	Demobe Little Belle	to EQ warehouse	EQ	ASAP 10/26
	Fix rip in liner		EQ	ASAP
	wash lot down		EQ	10/30
F	ADMINISTRATIVE			
	Post-removal structural assessment		F&V	ASAP
	Read electric meter	block off outlet	PAUL	10/31

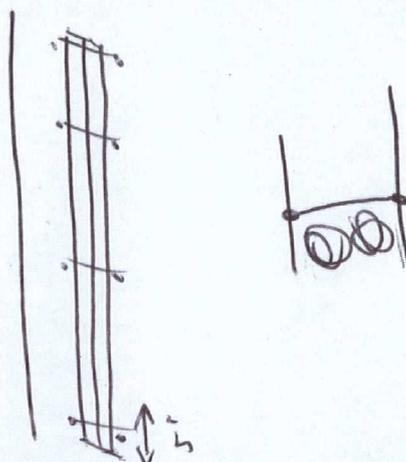

MONDAY

Portage Creek Area Site
Demobilization Plan - UPDATE 10/25

AREA	TASK	EXPLANATION	WHO	TARGET
A	Axtell Creek			
	Restoration		KV	ASAP
B	SA5-C			
	Restoration ✓ X	E + W banks	KV	10/29
	Recon entire area	Coir logs, stone, holes, debris, backfill curbs	EQ	10/30
C	SA5-D			
	Remove temp fence ✓ X	Upjohn, Youth Center	Farm & Garden	10/29
	Remove wood & stairs behind YC ✓ X	put on pallets	EQ	10/29
	Replace short fence at Lake St	W bank 4' fence	Farm & Garden	10/30
	Recon entire area	Coir logs, stone, holes, debris, backfill curbs	EQ	10/30
	Restoration		KV	ASAP
E	SA3A			
	Chip up trees + brush	load out logs	Total	10/29
	Load out debris pile SA first ✓ X	at entrance Fullon load(s) to C&C <i>Corder lead OSW</i>	EQ	10/29
	Pick up trash ✓ X	another sweep w/ trees down	EQ	10/29
	Put big rocks across entrance	to prevent access when Total is out	EQ	ASAP
F	STAGING PAD			
	Cut up and move bad mats ✓ X	stack next to dumpster for load out next year	EQ	10/29
	Scrap steel ✓ X	return yellow bin	Shupan	10/29
	Fix up orange fence on staging pad ✓ X	post 'Keep Out' signs on 1 T-post on each side	EQ	10/29
	Wash down parking lot O		EQ	10/29
	Decon & demobe AIS heavy equipment ✓	street sweep, water truck, 380 loader	EQ	10/29
	Demobe porta potties and sink		Plummers	10/30
	Load out dumpster		Plummers	10/30
	Empty fuel cell	keep tank for winter, re-do secondary containment	Kalamazoo Oil	10/30
	Rebuild secondary containment on fuel cell	pull out and dispose of plastic, sand bags	EQ	10/30
	Remove water meter from hydrant	keep in crew trailer	EQ	10/30
	Clean out all trailers	sweep, mop, empty fridges, take water away	EQ	10/30
	Fix rip in liner		sub	ASAP
	O			
F	ADMINISTRATIVE			
	Post-removal structural assessment		F&V	ASAP
	Read electric meter	shut off breakers and padlock control box	EQ	10/31

+ Salt 1-3's on load-out pad ✓ X

+ topsoil around aprons

+ Pump out sump 2 more loads? ✓

2 bucket/pavers?, Read St & John St.

TUES

Portage Creek Area Site
Demobilization Plan - UPDATE 10/29

AREA	TASK	EXPLANATION	WHO	TARGET
A	Axtell Creek			
	Restoration		KV	ASAP
B	SA5-C			
	Restoration X	E + W banks	KV	ongoing
	Fill in topsoil behind new curb / sidewalk		EQ	10/30 ASAP
C	SA5-D			
	Replace short fence at Lake St	W bank 4' fence	Farm & Garden	ASAP
	Restoration		KV	ASAP
	Fill in behind new curb / sidewalk		EQ	10/30 ASAP
D	STAGING PAD			
	Demobe porta potties and sink		Plummers	10/30
	Treat fuel in cell	treat fuel left in cell	Dave	11/1
	Wash down lot ✓ X		EQ	10/30
	Remove all orange fence from staging pad ✓ X		EQ	10/30
	Rebuild secondary containment on fuel cell ✓ X	pull out and dispose of plastic, sand bags	EQ	10/30
	Clean out all trailers ✓ X	sweep, mop, empty fridges, take water away	EQ	10/30
	Fix rip in liner X		sub	ASAP
	Berm off entrance/exit to staging pad ✓ X		EQ	10/30
Take skid out X				
E	ADMINISTRATIVE			
	Post-removal structural assessment		F&V	ASAP
	Read electric meter	padlock control box	EQ	10/30

X Gas cans out of yellow thing (No)
 Hay bales out (to KV)

