

STATE OF OREGON
MONITORING WELL REPORT
(as required by ORS 537.765 & OAR 690-240-095)

MULT
3805

Start Card #

60130

(1) OWNER/PROJECT:

WELL NO. MW#3

Name Port of Portland
Address 700 NE Multnomah
City Portland State OR Zip 97232

(2) TYPE OF WORK:


<input checked="" type="checkbox"/> New construction	<input type="checkbox"/> Repair	<input type="checkbox"/> Recondition
<input type="checkbox"/> Conversion	<input type="checkbox"/> Deepening	<input type="checkbox"/> Abandonment

(3) DRILLING METHOD

☐ Rotary Air ☐ Rotary Mud ☐ Cable
☒ Hollow Stem Auger ☐ Other _____

(4) BORE HOLE CONSTRUCTION

Special Standards ☐ Yes ☒ No Depth of completed well 20' ft.

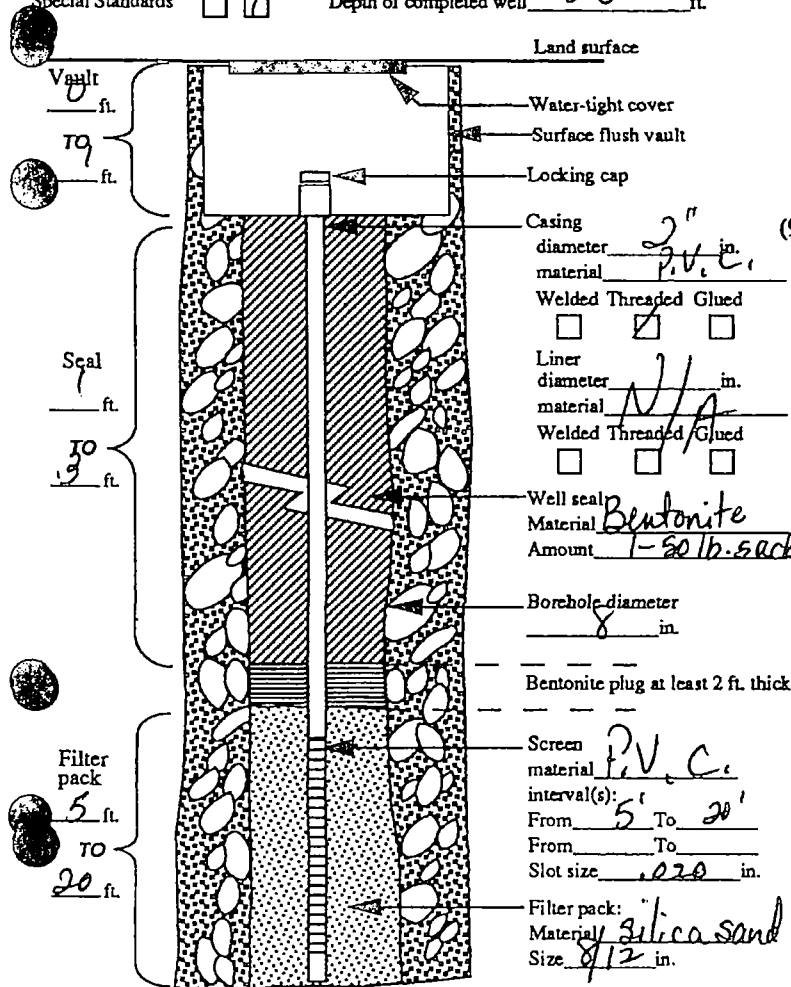

(6) LOCATION OF WELL By legal description

Well Location: County Multnomah
Township 2 (N or S) Range 1 (E or W) Section 23
1. NE 1/4 of SE 1/4 of above section.
2. Street address of well location 14400 - 15500 N. Lombard
Portland, OR
3. Tax lot number of well location N/A
4. ATTACH MAP WITH LOCATION IDENTIFIED.

(7) STATIC WATER LEVEL:

7.5 Ft. below land surface. Date 10-20-93
Artesian Pressure _____ lb/sq. in. Date _____

(8) WATER BEARING ZONES:

Depth at which water was first found 1.5

From	To	Est. Flow Rate	SWL
7.5'	20'	?	7.5'

(9) WELL LOG:

Ground elevation

[illegible]

Date started 10-20-93 Completed 10-20-93

(5) WELL TEST:

☐ Pump ☒ Bailer ☐ Air ☐ Flowing Artesian

Permeability _____ Yield _____ GPM _____

Conductivity _____ PH _____
Temperature of water 14°C °F/C Depth artesian flow found _____ ft

Was water analysis done? ☒ Yes ☒ No

By whom? Century West
Depth of strata to be analyzed. From 7.5' ft. to 20' ft.

Remarks:

(unbonded) Monitor Well Constructor Certification:

I certify that the work I performed on the construction, alteration, or abandonment of this well is in compliance with Oregon well construction standards. Materials used and information reported above are true to the best knowledge and belief.

MWC Number

Signed _____ Date _____

(bonded) Monitor Well Constructor Certification:

I accept responsibility for the construction, alteration, or abandonment work performed on this well during the construction dates reported above. All work performed during this time is in compliance with Oregon well construction standards. This report is true to the best of my knowledge and belief.

MWC Number 10013

Signed Kandy V. Crisman Date 11-20-93

USEPA SF



1286491

Geologist/Engineer Inqam Sahel


FIRST COPY-WATER RESOURCES DEPARTMENT

SECOND COPY-CONSTRUCTOR THIRD COPY-CUSTOMER

Port of Portland
Terminal 5
Blue Lagoon

MULT 3805

10/19/93

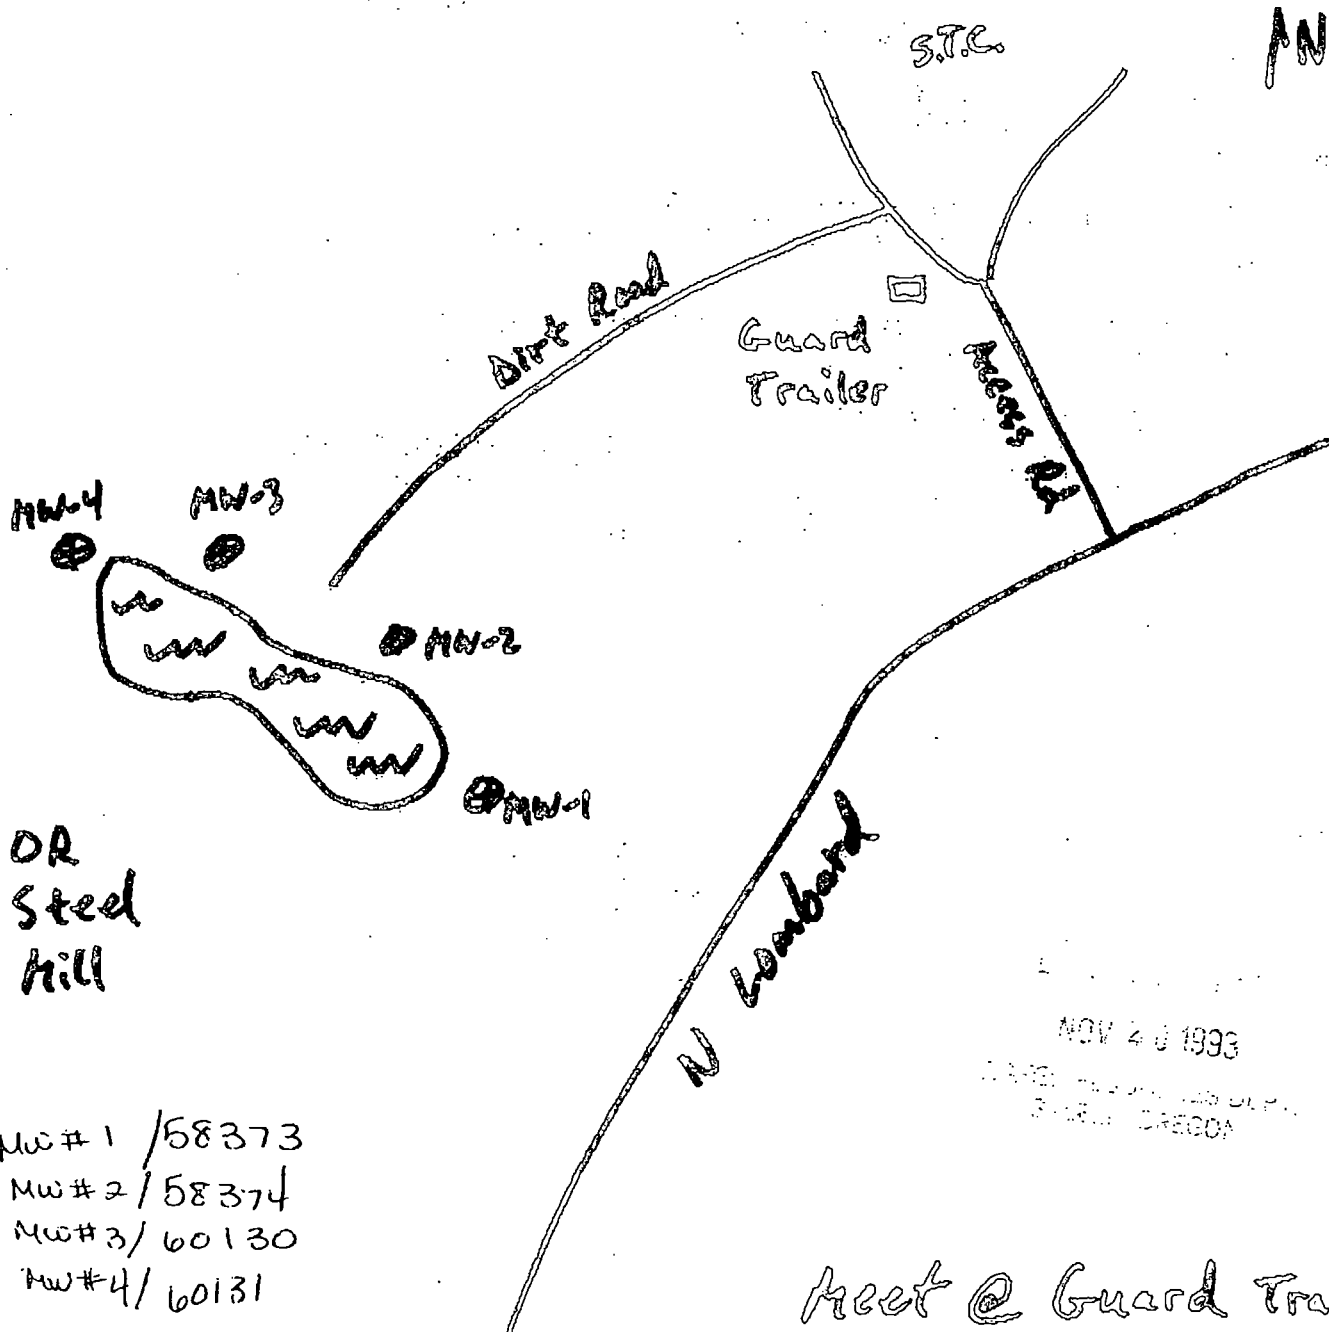

MW #1 / 58373
MW #2 / 58374
MW #3 / 60130
MW #4 / 60131

Post-It brand fax transmittal memo 7671		# of pages > 1
To: RANDY ER	From: ERIC COLLINS	
Co: CRISMAN	Co: CNE	
Dept:	Phone: 231-6078	
Fax: 620-1248	Fax:	

Meet @ Guard Trailer
8:00 10/20
