



SECOR
INTERNATIONAL
INCORPORATED
400 Bruns Lane
Springfield, IL 62702
217.698.7247 phone
217.698.8538 fax

www.secor.com

June 20, 2006

EPA Region 5 Records Ctr.



302549

Mr. Doyle W. Wilson
Remedial Project Manager
Illinois Environmental Protection Agency
1021 North Grand Avenue East
P.O. Box 19276
Springfield, Illinois 62792-9276

Re: Schedule and Design Drawings
Interstate Pollution Control/Roto-Rooter Superfund Site
Winnebago County, Illinois
SECOR Project No.: 61UN.05046.00.0004

Dear Mr. Wilson:

SECOR International Incorporated (SECOR) hereby submits a revised schedule and revised design drawings for the above-referenced project on behalf of Interstate Pollution Control/Roto-Rooter Superfund Site Remedial Design/Remedial Action Steering Committee (Group).

Please note on the drawings that we have made the following revisions:

- The slopes at the north edge of the site have been flattened to provide a more stable area. This was done at the suggestion of the paving contractor.
- The 12" layer of CA-16 was replace with 6" of CA-6 over 6" of CA-16 with the geotextile in between. The purpose of this change is to allow better compaction while meeting the requirements of the FML manufacturer.


If you have any questions, please call me.



Sincerely,
SECOR International Incorporated

Kenneth G. Smith, P.E.
Project Manager

xc: S. Moyer
T. Lupo
C. Simonsen
J. Hooker
M. Hirt


**Figure 3
IPC Site - RD/RA Project
Schedule**

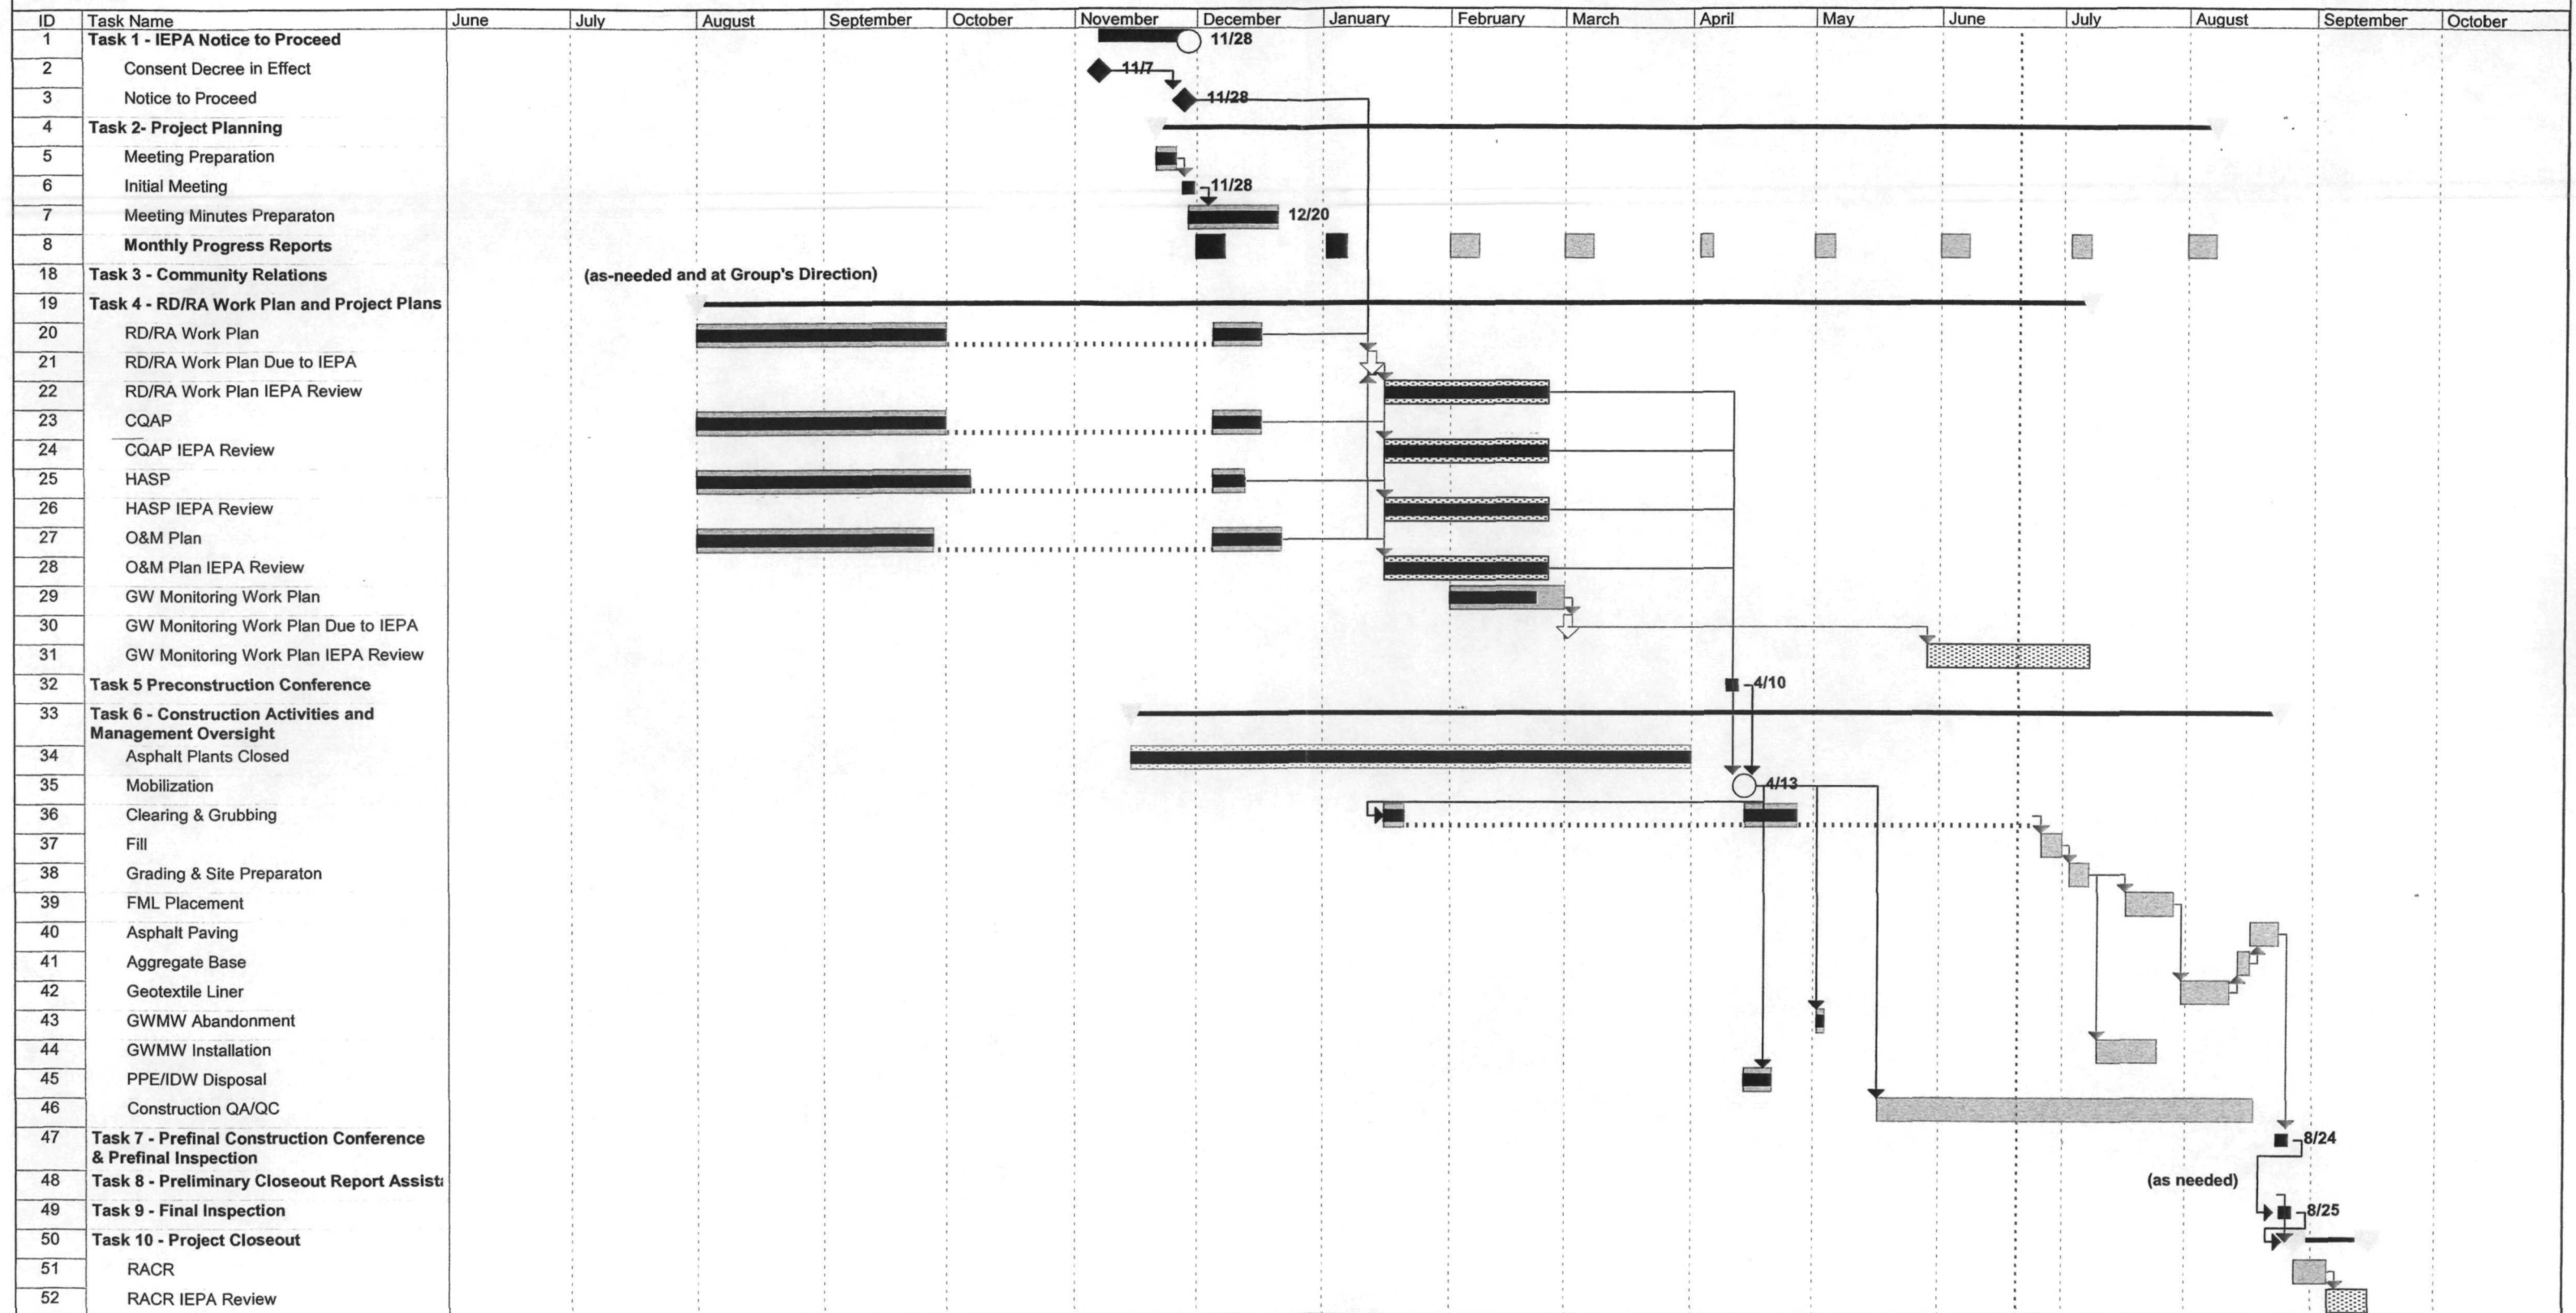

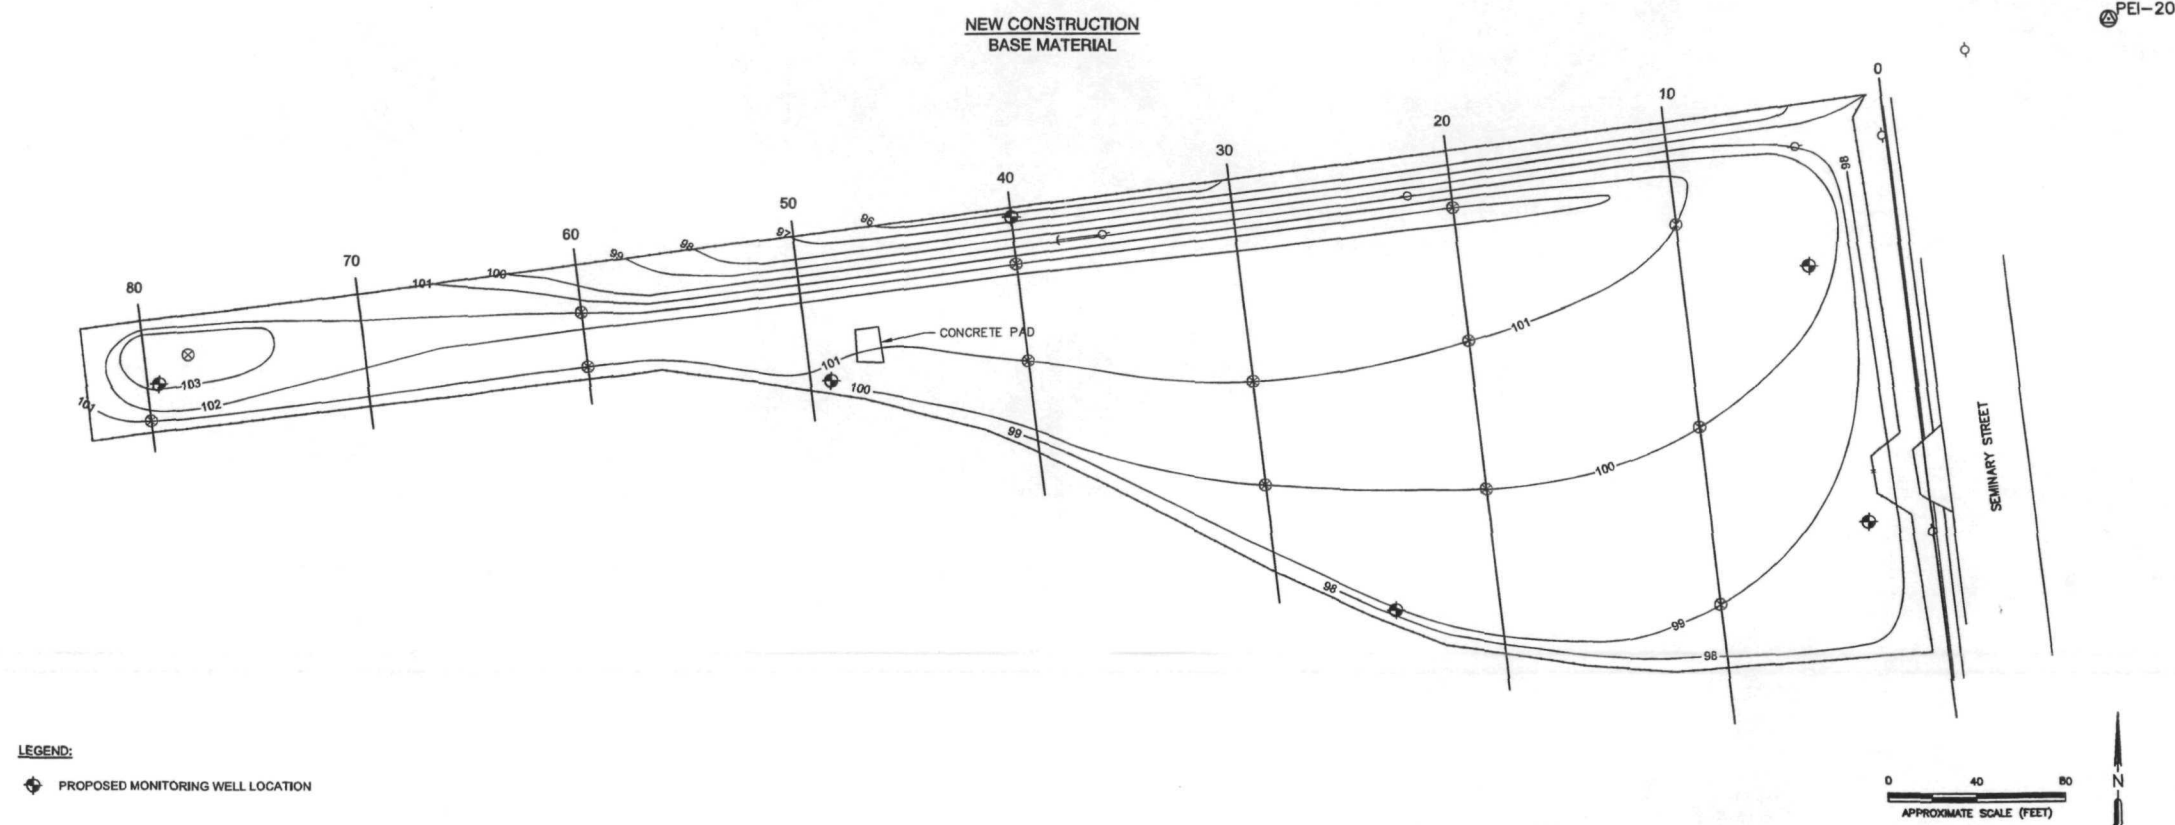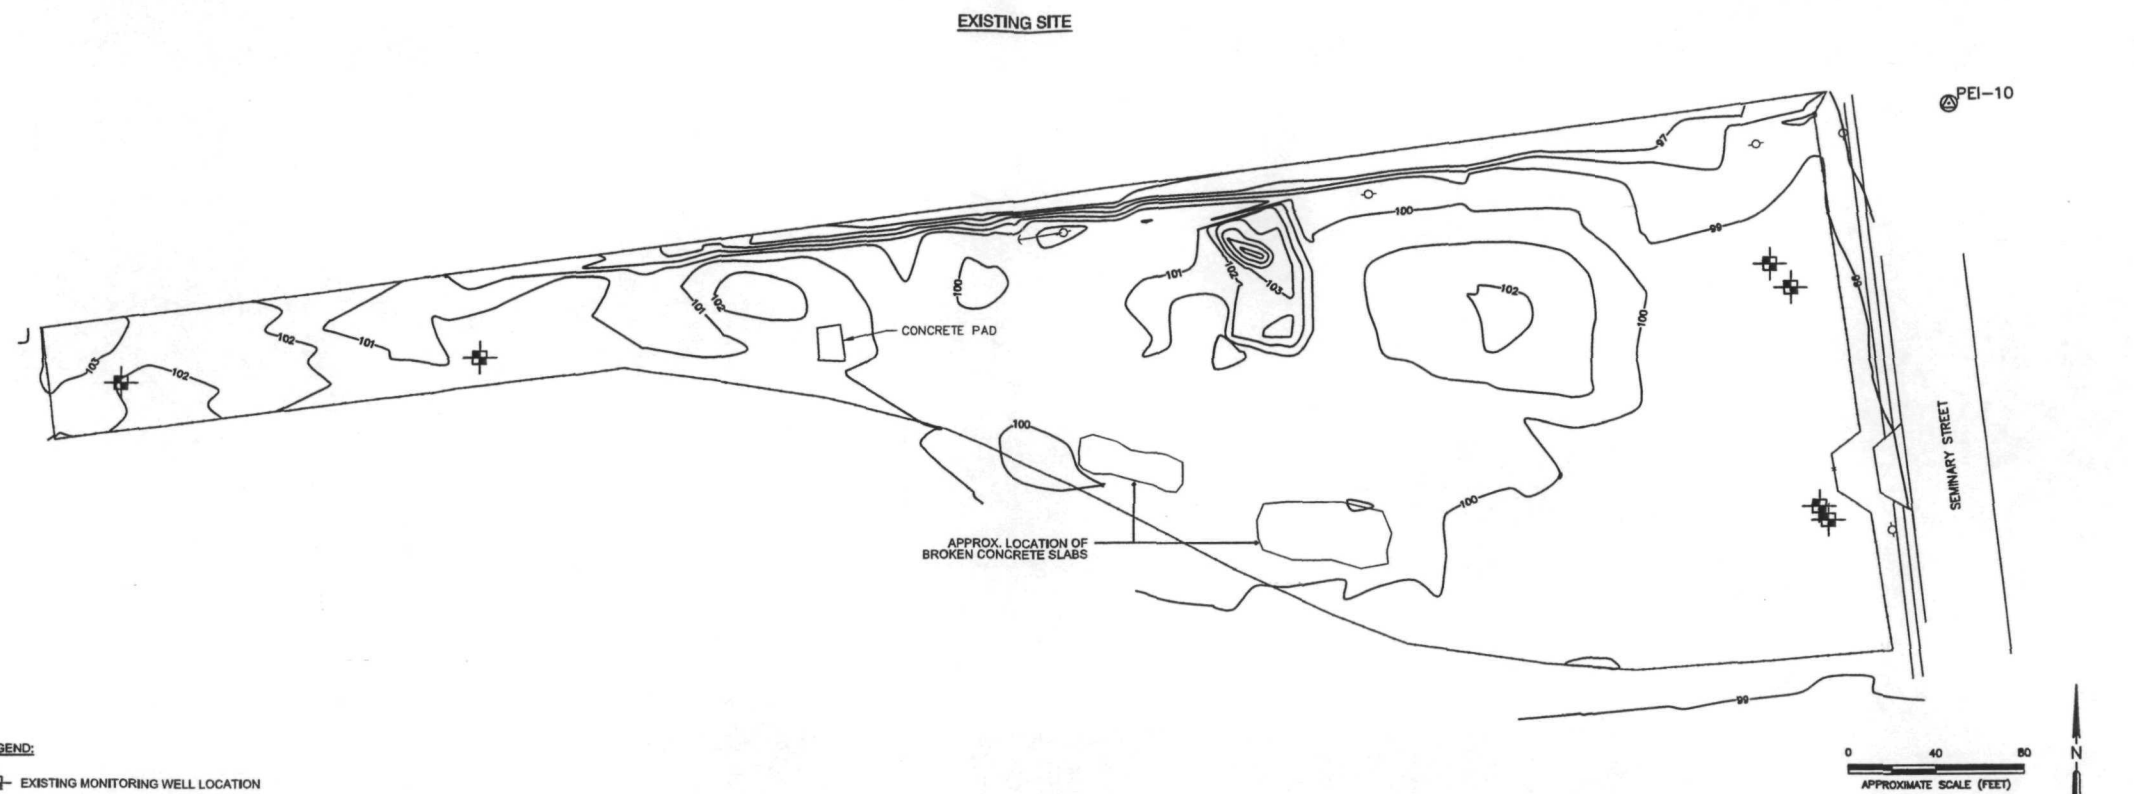

DATE: 05/31/06 06/19/06	REVISION FOR EPA REVIEW FOR CONSTRUCTION	FOR: SEMINARY STREET SITE ROCKFORD, ILLINOIS	SITE PLAN BASE MATERIAL	FIGURE 1
SECOR 400 BRUNS LANE SPRINGFIELD, ILLINOIS 62762 PHONE: (217) 696-7247 FAX: (217) 696-8538		JOB NUMBER: 61UNJ06046.00	DRAWN BY: GH	CHECKED BY: KS
		APPROVED BY: KS	DATE: 5-9-06	

FINISHED CONSTRUCTION
ASPHALT CAP

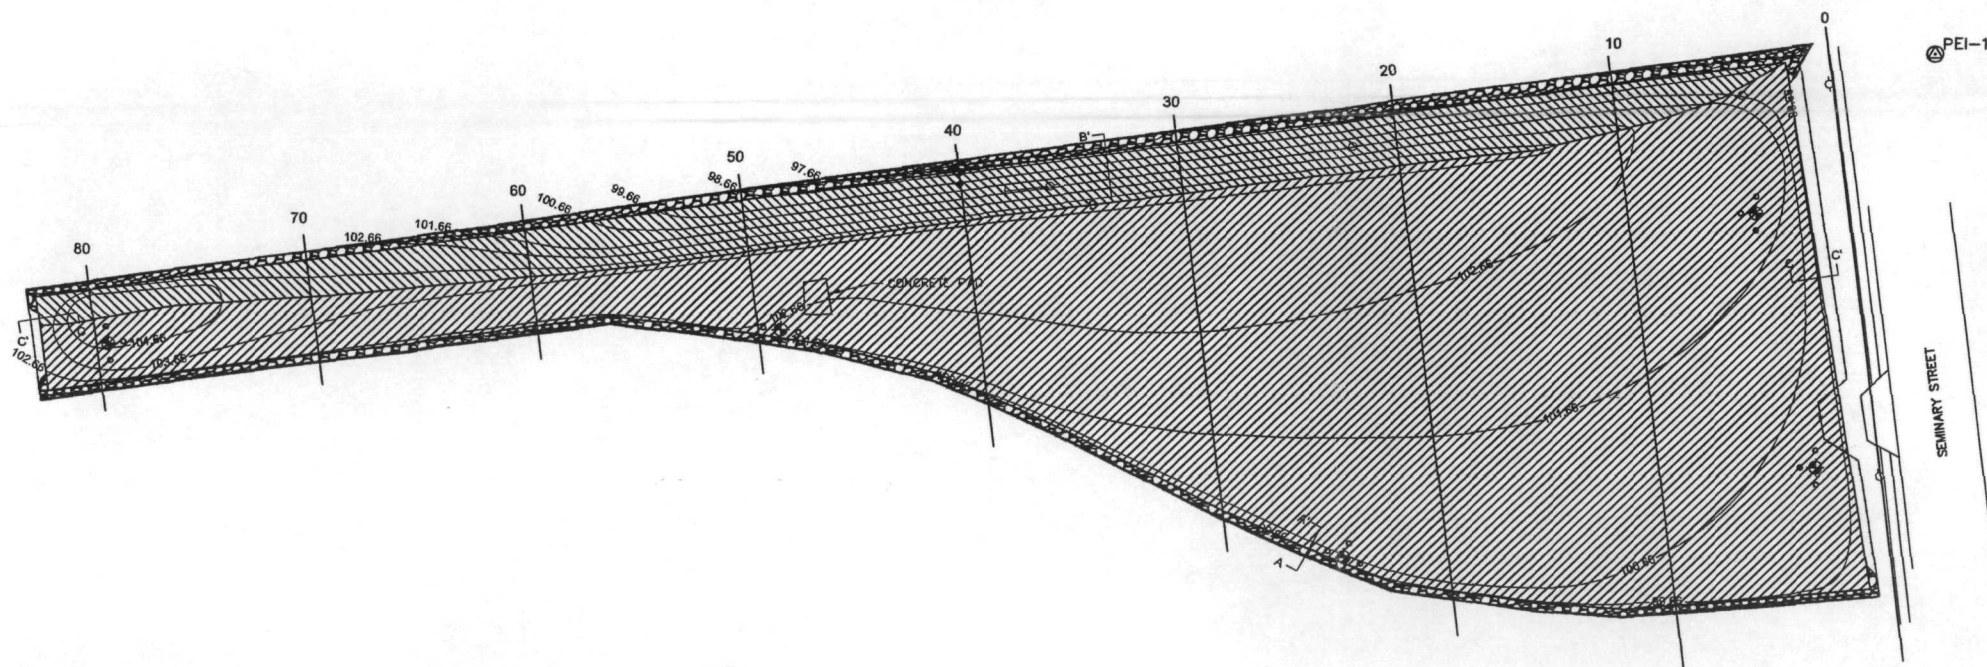


LEGEND:
 ASPHALT CAP
 ROCK (CA-1)

NOTES


1. BASE FILL MATERIAL (BELOW GEOTEXTILE) SHALL BE CLEAN MATERIAL, FREE OF ROOTS, ROCKS OVER 3 INCHES IN DIAMETER AND DEBRIS.
2. BASE SHALL BE ROLLED WITH STEEL ROLLER.
3. PROPOSED MONITORING WELLS, TO BE INSTALLED BY OTHERS.
4. COVER FILL PLACED ABOVE FML SHALL BE 6" OF CA-6 UNDER 6" OF CA-6 OR AS APPROVED BY ENGINEER.
5. EXISTING CONCRETE PAD MAY REMAIN IN PLACE IF IT DOES NOT INTERFERE WITH GRADING. ANY PORTION OF THE PAD WHICH MUST BE REMOVED SHALL BE DISPOSED OF BY BURYING ON SITE.
6. BROKEN CONCRETE SHOWN ON FIGURE 1 SHALL BE SPREAD OUT IN A SINGLE LAYER IN FILL AREAS. SUFFICIENT SPACE BETWEEN PIECES OF CONCRETE SHALL BE MAINTAINED TO PREVENT VOIDS IN BACKFILL MATERIAL.

BENCHMARKS

PEI-10 EL. 97.56
 PEI-20 EL. 98.53




TYPICAL BOLLARD
NOT TO SCALE

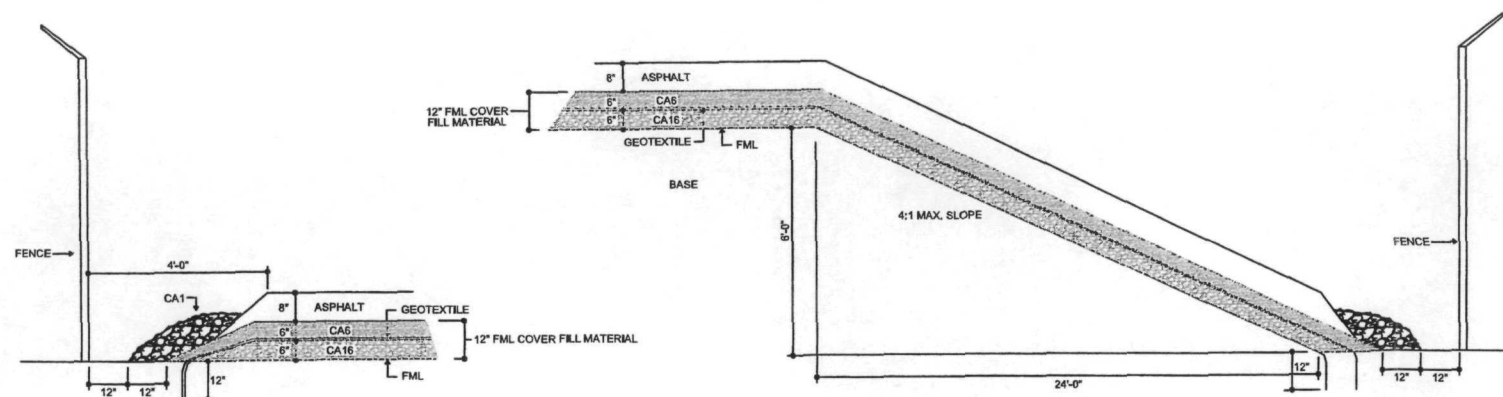


A-A'
NOT TO SCALE

B-B'
NOT TO SCALE

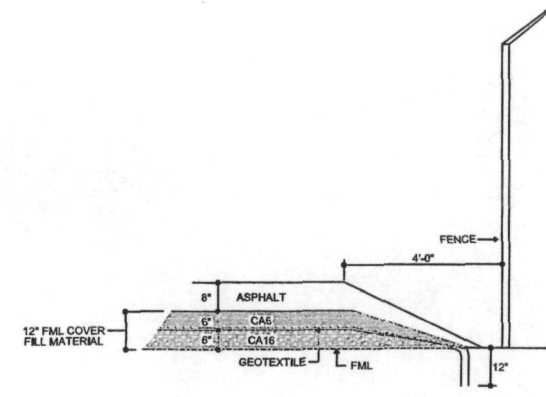

C-C'
NOT TO SCALE



MONITORING WELL DETAIL
NOT TO SCALE

DATE: 05/31/06 06/19/06	REVISION: FOR EPA REVIEW FOR CONSTRUCTION	FOR: SEMINARY STREET SITE ROCKFORD, ILLINOIS	SITE PLAN FINISHED CONSTRUCTION	FIGURE 2
JOB NUMBER: 61UNJ5046.00	DRAWN BY: GH	CHECKED BY: KS	APPROVED BY: KS	DATE: 5-9-06

SECOR
 400 BRUNS LANE
 SPRINGFIELD, ILLINOIS 62762
 PHONE: (217) 598-7247 FAX: (217) 598-8538
