

Chow, Kevin

From: Dan Caplice <dan@kplus.com>
Sent: Friday, February 27, 2015 3:48 PM
To: Beslow, Mike
Cc: 'Dimond, Thomas'; 'Kent Keutzer'; Boseman, Anita; Chow, Kevin; 'cordell.renner@tetrattech.com'; 'mark.retzlaff@illinois.gov'; 'chuck.curtis@illinois.gov'; 'mark.gurnik@illinois.gov'; 'Mike.Roubitchek@Illinois.gov'; 'Grant, Christopher J. (CGrant@atg.state.il.us)'; 'Susan Morakalis (susan.morakalis@mwr.org)'; 'mark.leibrock@mwr.org'
Subject: RE: Olympic Oil Update
Attachments: 24163-VSO-02b Recovery Well Locations.pdf; IMAG0496.jpg; IMAG0529.jpg

Drillers have just finished on site for the day. We were able to install 3 of the 4 planned recover wells. Unfortunately, while the area may seem large on paper, it is actually a relatively small space in which to maneuver a standard sized drill rig. For this reason, we were unable to install the well in the NWC as planned. The drillers will return to the site on Monday morning with a smaller ATV that will be able to maneuver and install the last of the 4 planned wells. Attached is a revised version of the drawing that was sent yesterday which shows the approximate locations of the finished wells. Also attached are a couple of pictures showing the work and the wells.



K-PLUS ENGINEERING

Daniel M. Caplice, P.E.

312.207.5700 | 312.207.1600 (Main)

www.kplus.com

Chicago Office | 329 West 18th Street, Suite 614 | Chicago, IL 60616

Hinsdale Office | 15 Spinning Wheel Road, Suite 320 | Hinsdale, IL 60521

From: Dan Caplice
Sent: Thursday, February 26, 2015 6:38 PM
To: Beslow, Mike
Cc: 'Dimond, Thomas'; Kent Keutzer; 'boseman.anita@epa.gov'; 'chow.kevin@epa.gov'; 'cordell.renner@tetrattech.com'; 'mark.retzlaff@illinois.gov'; 'chuck.curtis@illinois.gov'; 'mark.gurnik@illinois.gov'; 'Mike.Roubitchek@Illinois.gov'; 'Grant, Christopher J. (CGrant@atg.state.il.us)'; 'Susan Morakalis (susan.morakalis@mwr.org)'; 'mark.leibrock@mwr.org'
Subject: Olympic Oil Update

We have made the necessary arrangements for drillers to be on site tomorrow morning at 7:30 AM to begin installation of 4 recovery wells inside the containment area. Each well will be a 6 in diameter well with a 10' screen that will fully intersect the silty clay layer where the sand seam has been identified during yesterday's drilling and prior drilling along the canal. Attached is an aerial photo of the area showing the tentative locations. As noted each location is tentative and will be adjusted in the field to obtain optimal recovery and avoid any existing structures in the area. Once the wells are installed, we will install a submersible pump in each and pump all possible liquid to a holding tank on site for disposal.

If you have any questions or concerns, please contact me or see me on site first thing in the morning.



K-PLUS ENGINEERING


Daniel M. Caplice, P.E.

312.207.5700 | 312.207.1600 (Main)

www.kplus.com

Chicago Office | 329 West 18th Street, Suite 614 | Chicago, IL 60616

Hinsdale Office | 15 Spinning Wheel Road, Suite 320 | Hinsdale, IL 60521

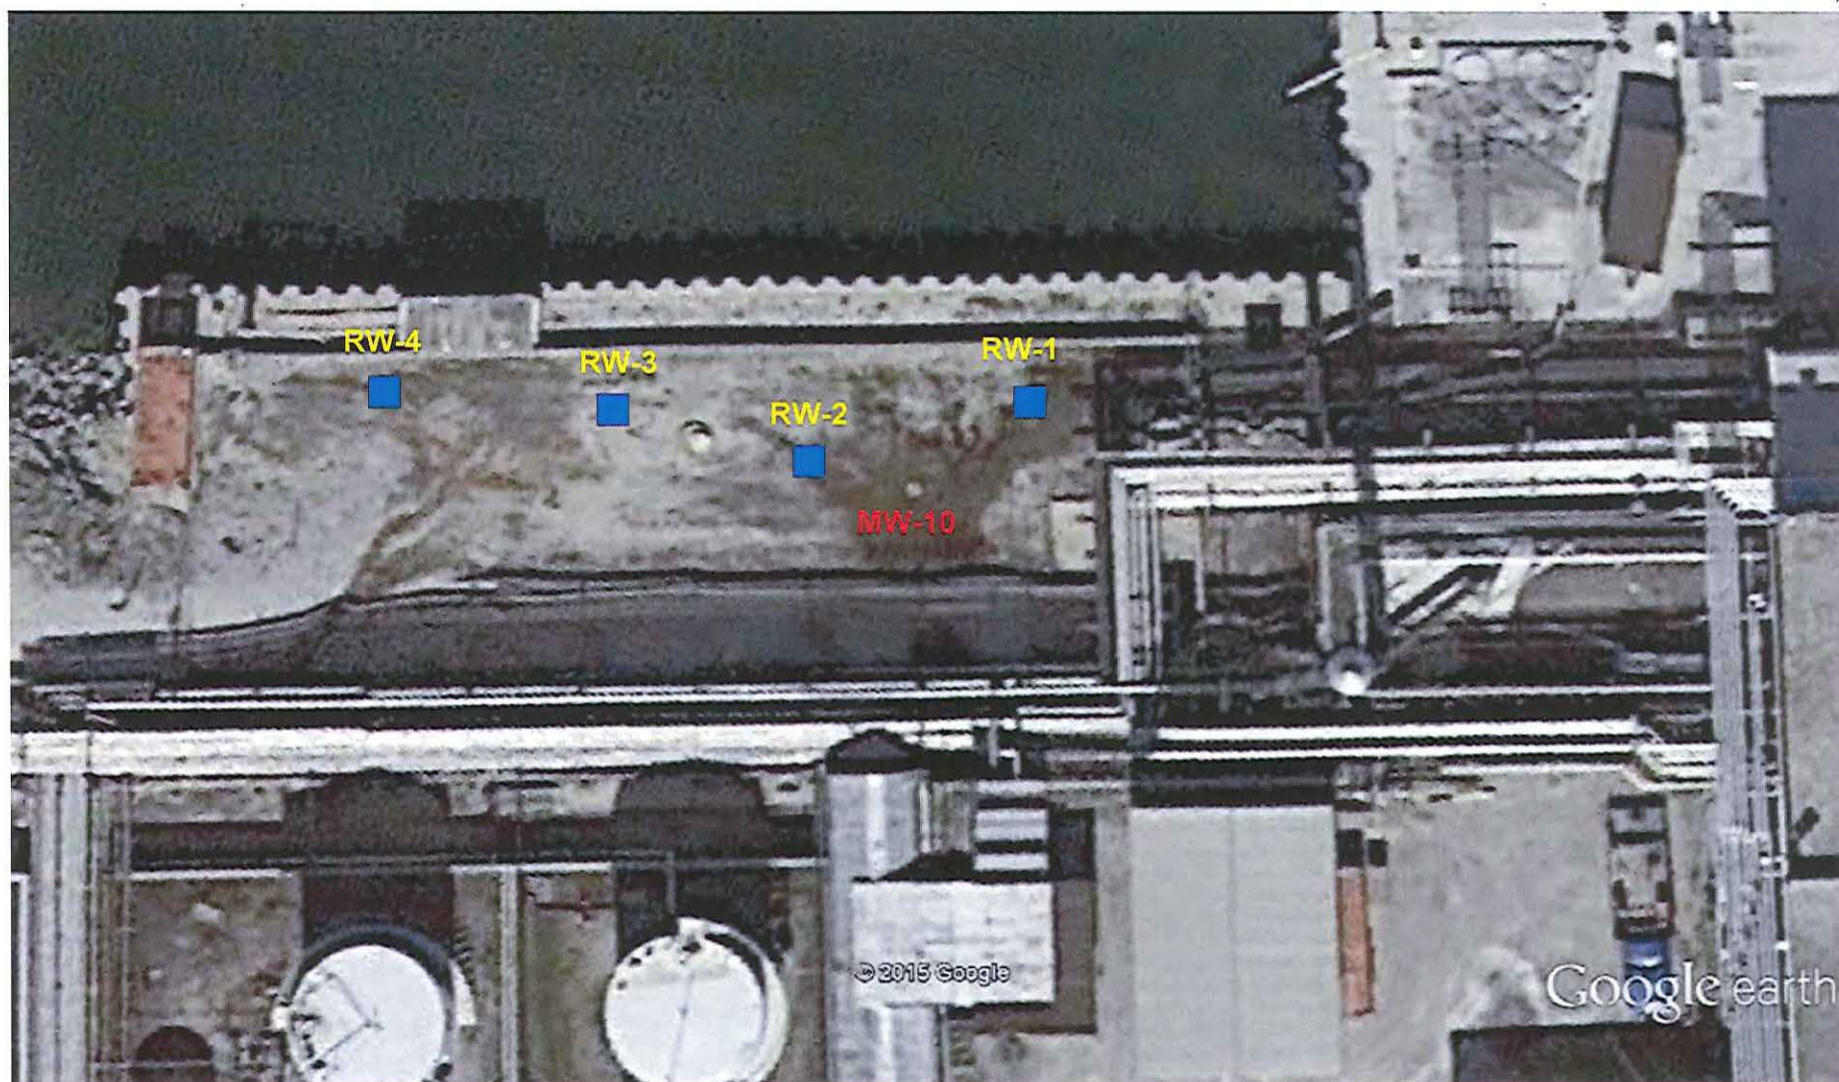

K-PLUS ENGINEERING, LLC
15 Spinning Wheel Rd. SUITE 320, Hinsdale, IL 60521
P 312.207.1600, F 312.831.2191, WWW.KPLUS.COM

Recovery Well Location Map

Olympic Oil
Cicero, Illinois

Date: February 27, 2015

Scale: approximate

Document No. 24163-VSO-02b

