

**RMT, Inc.**

2025 E. Beltline Ave SE  
Suite 402  
Grand Rapids, MI 49546

Phone: 616-975-5415  
Fax: 616-975-1098

**TRANSMITTAL****No. 00068****PROJECT: LEC Remediation Services****DATE: 3/21/2005**

**TO:** NJDEP  
Bureau of Federal Case Management  
Div. of Responsible Site Party Remed  
CN028  
Trenton, NJ 08625

**REF: PPU No. 8****ATTN: Anthony Cinque**

WE ARE SENDING:	SUBMITTED FOR:	ACTION TAKEN:
<input type="checkbox"/> Shop Drawings	<input type="checkbox"/> Approval	<input type="checkbox"/> Approved as Submitted
<input type="checkbox"/> Letter	<input checked="" type="checkbox"/> Your Use	<input type="checkbox"/> Approved as Noted
<input type="checkbox"/> Prints	<input type="checkbox"/> As Requested	<input type="checkbox"/> Returned After Loan
<input type="checkbox"/> Change Order	<input type="checkbox"/> Review and Comment	<input type="checkbox"/> Resubmit
<input type="checkbox"/> Plans		<input type="checkbox"/> Submit
<input type="checkbox"/> Samples	<b>SENT VIA:</b>	<input type="checkbox"/> Returned
<input type="checkbox"/> Specifications	<input type="checkbox"/> Attached	<input type="checkbox"/> Returned for Corrections
<input checked="" type="checkbox"/> Other: Project Progress Update No. 8	<input checked="" type="checkbox"/> Separate Cover Via: Email 3/21/05	<input type="checkbox"/> Due Date:

ITEM NO.	COPIES	DATE	ITEM NUMBER	REV. NO.	DESCRIPTION	STATUS
01	1	3/18/2005			Project Progress Update No. 8	APP
02	1	3/18/2005			Project Progress Update No. 8 Photos	NEW

CC: S. Cipot, R. Alvey, F. Zizilia, J. Prendergast, G. Blyskun, J. Lewis  
C. Anderson, E. Schaub, C. Clavadetscher, J. Rheinhardt, RMT Project Team

Signed: *Christie Whitford for*  
Nick Clevett *Nick Clevett*





Christy Whitford  
<Christy.Whitford@rmt  
inc.com>

03/21/2005 10:13 AM

To: gblyskun@dep.state.nj.us, jprendergast@dep.state.nj.us, Robert  
Alvey/R2/USEPA/US@EPA, Stephen Cipot/R2/USEPA/US@EPA,  
morrissol@optonline.net, cristopher.anderson@polyone.com,  
Ernie.Schaub@polyone.com, james.lewis@polyone.com, Dan Oman  
<Dan.Oman@rmtinc.com>, Jeff Macri <Jeff.Macri@rmtinc.com>, Jim  
Dexter <Jim.Dexter@rmtinc.com>, Nakia Addison  
<Nakia.Addison@rmtinc.com>, Nicholas Clevett  
<Nicholas.Clevett@rmtinc.com>, Wally Kurzeja  
<Wally.Kurzeja@rmtinc.com>, jrheinhardt@whartonnj.com

cc:

Subject: LEC Source Reduction Progress Update No.@ 8

Please see attached Transmittal No. 00068.  
This is transmitting Progress Update No. 8 and the associated  
photo documentation.

Christy Whitford  
Construction Management Project Assistant  
RMT, Inc., Grand Rapids, MI  
Ph. 616.975.5415 Ext. 1424  
Fax 616.975.1098

Outgoing messages, along with any attachments, are scanned for  
viruses prior to sending.

NOTICE-- This email may contain confidential and privileged  
information for the sole use of the intended recipient. Any  
review or distribution by others is strictly prohibited. If you  
are not the intended recipient, please contact the sender



immediately and delete all copies. Trans 00068.pdf

**L.E. CARPENTER & COMPANY ~ NJD002168748**  
**BOROUGH OF WHARTON, MORRIS COUNTY, NEW JERSEY**  
**SOURCE REDUCTION REMEDIAL PROJECT PROGRESS UPDATE NO. 8**

---

**Date:** March 18, 2005

**To:** Stephen Cipot, USEPA  
Anthony Cinque, NJDEP

**From:** Nicholas J. Clevett, RMT

**cc:** Robert Alvey, USEPA  
Frances Zizila, USEPA  
John Prendergast, NJDEP  
George Blyskun, NJDEP  
Jim Lewis, LEC  
Cris Anderson, LEC  
Ernie Schaub, LEC  
Colin Clavadetscher, Morris County

Jon Rheinhardt, Borough of Wharton  
Dan Oman, RMT  
Jim Dexter, RMT  
Walter Kurzeja, RMT  
Jeff Macri, RMT  
Dave Pratt, RMT  
Nakia Addison, RMT

**Project No.:** 00-06527.09

**Subject:** **SOURCE REDUCTION REMEDIAL ACTION**  
**Project Progress Update No. 8**

**I. SOURCE REDUCTION REMEDIAL ACTIONS - THROUGH MARCH 11<sup>TH</sup> THROUGH MARCH 17<sup>TH</sup> 2005**

1. Continued morning safety briefings (e.g., discussion of daily work scope and associated health and safety procedures)
2. Maintained air monitoring equipment (e.g., Weather Station, Miniram, PID, data loggers etc.) and air monitoring program (e.g., data log download, grab sampling)
3. Maintained all on-site heavy equipment (e.g., excavators, skid steer, off-road truck, screen, etc.)
4. Performed and documented daily inspections on the silt fence as outlined in the certified SESCP
5. Cleaned all paved areas with a skid steer broom attachment
6. Continued to load, transport and dispose of process wastes from the B-1 and B-2 areas. To date a total of 378 tons of process wastes have been removed from the site
7. Continued PCB impacted soil excavation and stockpiling of in those areas inside and outside [west] of the delineated wetland areas. To date, a total of 2,572 tons of PCB impacted soils have been excavated, loaded and transported off-site for disposal as non TSCA PCB wastes. When needed, cement kiln dust (CKD) was added to dry the excavated PCB soils prior to transportation and off-site disposal
8. Collected and submitted for analysis confirmatory samples (base and sidewall samples) for total PCBs in the PCB area as outlined in the RAWP documents (e.g., RAWP and regulatory response letters)
9. Initiated PCB area (wetland and non wetland area) backfilling activities
10. Completed setup of the batch plant and ancillary equipment to prepare slurry to facilitate the smear zone excavation within the saturated zone. The water pump was replaced due to mechanical failure and the Venturi maintenance performed due to clogging
11. Completed preparation of test slurry mix to ensure the correct mix and consistency prior to smear zone excavation activities

**L.E. CARPENTER & COMPANY ~ NJD002168748**  
**BOROUGH OF WHARTON, MORRIS COUNTY, NEW JERSEY**  
**SOURCE REDUCTION REMEDIAL PROJECT PROGRESS UPDATE NO. 8**

---



12. Initiated smear zone excavation utilizing the slurry mix. Once excavated, CKD was added to these materials to facilitate screening.
13. To date a total of 745 tons of CKD (32 loads) have been delivered to the site.

**II. PROPOSED SOURCE REDUCTION REMEDIAL ACTIONS - MARCH 18<sup>TH</sup> THROUGH MARCH 24<sup>TH</sup> 2005**

1. Continue to stockpile, load, transport and dispose of PCB impacted soils within permitted wetlands areas existing within the Wharton Enterprise property east of the LEC site, and conduct confirmatory sampling as required in the RAWP
2. Continue loading, transporting and disposing of process waste materials
3. Continue smear zone excavation activities

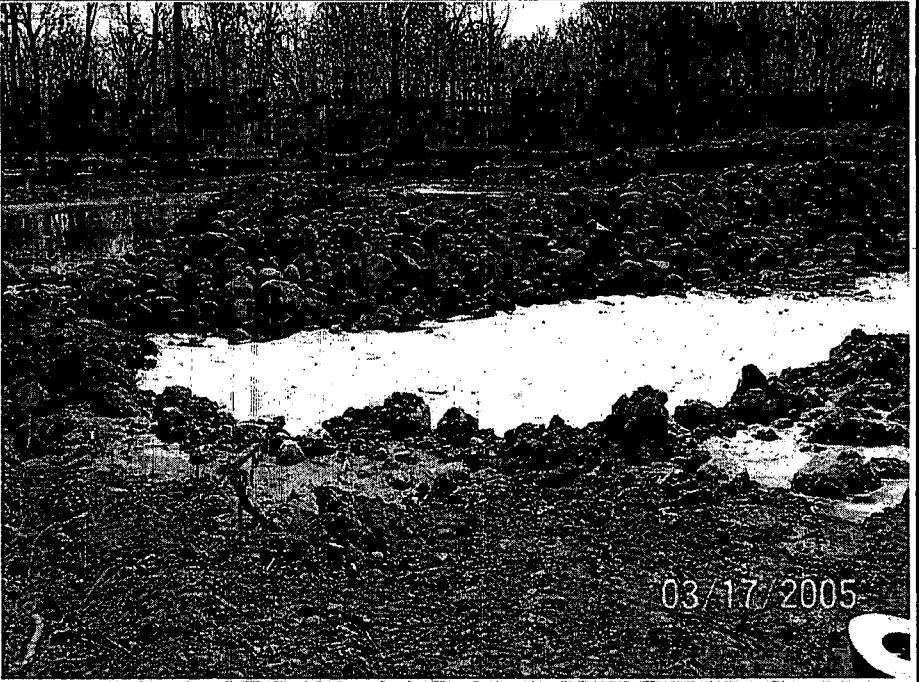



## Photographic Log Progress Update No. 8

<b>Client Name:</b> L.E. CARPENTER & COMPANY		<b>Site Location:</b> Wharton, Morris County, NJ	<b>Project No.:</b> 00-06527.09
<b>Photo No.</b> 1	<b>Date</b> 3/17/05		
<b>Description</b> Cement Kiln Dust (CKD)			
<b>Photo No.</b> 2	<b>Date</b> 3/11/05		
<b>Description</b> Pumping mixed slurry into the excavation			

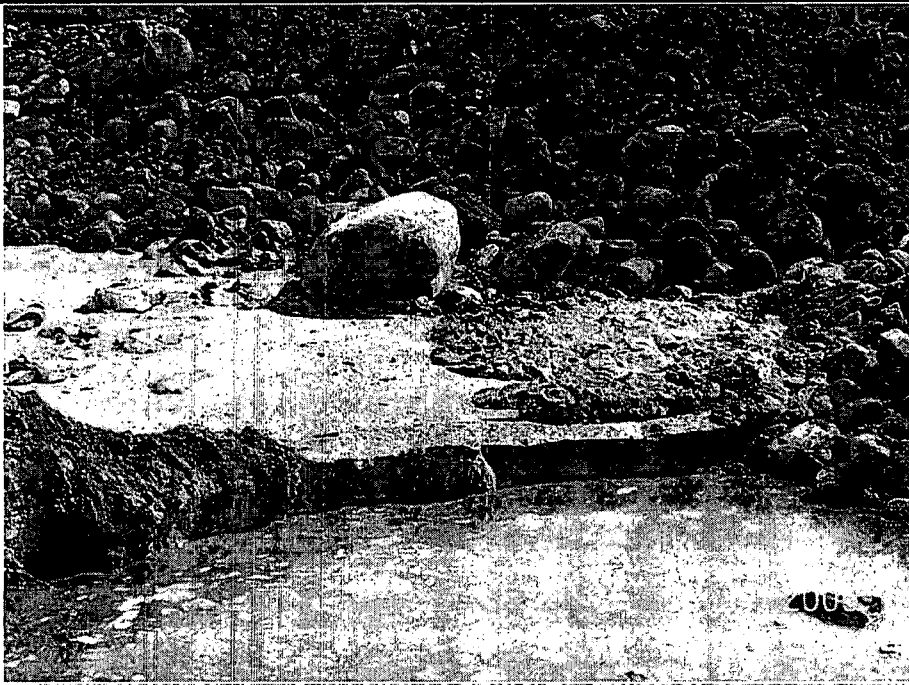



## Photographic Log Progress Update No. 8

<b>Client Name:</b> L.E. CARPENTER & COMPANY		<b>Site Location:</b> Wharton, Morris County, NJ	<b>Project No.:</b> 00-06527.09
<b>Photo No.</b> 3	<b>Date</b> 3/17/05		
<b>Description</b> Slurry mix curing in the excavation			
<b>Photo No.</b> 4	<b>Date</b> 3/17/05		
<b>Description</b> Curing slurry  View looking east			



## Photographic Log Progress Update No. 8

<b>Client Name:</b> L.E. CARPENTER & COMPANY		<b>Site Location:</b> Wharton, Morris County, NJ	<b>Project No.:</b> 00-06527.09
<b>Photo No.</b> 5	<b>Date</b> 3/17/05		
<b>Description</b> Hardened slurry			
<b>Photo No.</b> 6	<b>Date</b> 3/17/05		
<b>Description</b> Smear zone material ex-situ blending area (CKD, screening etc)			
