



Nicholas Clevett
<Nicholas.Clevett@rmt
inc.com>

02/28/2005 05:01 PM

To: ACINQUE@dep.state.nj.us, Stephen Cipot/R2/USEPA/US@EPA
cc: George.Blyskun@dep.state.nj.us, John.Prendergast@dep.state.nj.us,
Robert Alvey/R2/USEPA/US@EPA, Frances
Zizila/R2/USEPA/US@EPA, morrissoil@optonline.net,
cristopher.anderson@Polyone.com, Ernie.Schaub@Polyone.com,
James.Lewis@Polyone.com, Dan Oman <Dan.Oman@rmtinc.com>,
David Pratt <David.Pratt@rmtinc.com>, Jeff Macri
<Jeff.Macri@rmtinc.com>, Jim Dexter <Jim.Dexter@rmtinc.com>,
Nakia Addison <Nakia.Addison@rmtinc.com>, Wally Kurzeja
<Wally.Kurzeja@rmtinc.com>, jrheinhardt@whartonnj.com
Subject: LEC Source Reduction Progress Update No.@ 5

See Attached Progress Update No. 5
Contact me with any questions and/or comments
Regards,

Nicholas J. Clevett
Senior Project Manager
RMT, Inc., Michigan
2025 E. Beltline Ave. SE
Suite 402
Grand Rapids, MI 49546
(616) 975-5415 (Office)
(616) 975-1098 (Fax)
(616) 780-2398 (Mobile)
Nicholas.Clevett@rmtinc.com

Outgoing messages, along with any attachments, are scanned for
viruses prior to sending.

NOTICE-- This email may contain confidential and privileged
information for the sole use of the intended recipient. Any
review or distribution by others is strictly prohibited. If you
are not the intended recipient, please contact the sender
immediately and delete all copies.



Trans 00061 Progress Update No. 5 Feb 18 to Feb 25 20

346423



RMT, Inc.

2025 E. Beltline Ave SE
Suite 402
Grand Rapids, MI 49546

Phone: 616-975-5415
Fax: 616-975-1098

TRANSMITTAL**No. 00061****PROJECT: LEC Remediation Services****DATE: 2/28/2005**

TO: NJDEP
Bureau of Federal Case Management
Div. of Responsible Site Party Remed
CN028
Trenton, NJ 08625

REF: PPU No. 5**ATTN: Anthony Cinque**

WE ARE SENDING:	SUBMITTED FOR:	ACTION TAKEN:
<input type="checkbox"/> Shop Drawings	<input type="checkbox"/> Approval	<input type="checkbox"/> Approved as Submitted
<input type="checkbox"/> Letter	<input checked="" type="checkbox"/> Your Use	<input type="checkbox"/> Approved as Noted
<input type="checkbox"/> Prints	<input type="checkbox"/> As Requested	<input type="checkbox"/> Returned After Loan
<input type="checkbox"/> Change Order	<input type="checkbox"/> Review and Comment	<input type="checkbox"/> Resubmit
<input type="checkbox"/> Plans		<input type="checkbox"/> Submit
<input type="checkbox"/> Samples	SENT VIA:	<input type="checkbox"/> Returned
<input type="checkbox"/> Specifications	<input type="checkbox"/> Attached	<input type="checkbox"/> Returned for Corrections
<input checked="" type="checkbox"/> Other: Project Progress Update No. 5	<input checked="" type="checkbox"/> Separate Cover Via: Email 2/28/05	<input type="checkbox"/> Due Date:

ITEM NO.	COPIES	DATE	ITEM NUMBER	REV. NO.	DESCRIPTION	STATUS
01	1	2/28/2005			Project Progress Update No. 5	APP
02	1	2/18/2005			Project Progress Update No. 5 Photos	NEW

CC: S. Cipot, R. Alvey, F. Zizilia, J. Prendergast, G. Blyskun, J. Lewis
C. Anderson, E. Schaub, C. Clavadetscher, J. Rheinhardt, RMT Project Team

Signed:


Nick Clavett

L.E. CARPENTER & COMPANY ~ NJD002168748
BOROUGH OF WHARTON, MORRIS COUNTY, NEW JERSEY
SOURCE REDUCTION REMEDIAL PROJECT PROGRESS UPDATE NO. 5

Date: February 28, 2005

To: Stephen Cipot, USEPA
Anthony Cinque, NJDEP

From: Nicholas J. Clevett, RMT

cc: Robert Alvey, USEPA
Frances Zizila, USEPA
John Prendergast, NJDEP
George Blyskun, NJDEP
Jim Lewis, LEC
Cris Anderson, LEC
Ernie Schaub, LEC
Colin Clavadetscher, Morris County

Jon Rheinhardt, Borough of Wharton
Dan Oman, RMT
Jim Dexter, RMT
Walter Kurzeja, RMT
Jeff Macri, RMT
Dave Pratt, RMT
Nakia Addison, RMT

Project No.: 00-06527.09

Subject: SOURCE REDUCTION REMEDIAL ACTION
Project Progress Update No. 5

I. SOURCE REDUCTION REMEDIAL ACTIONS - FEBRUARY 18TH THROUGH FEBRUARY 25TH 2005

1. Continued morning safety briefings (e.g., discussion of daily work scope and associated health and safety procedures)
2. Maintained air monitoring equipment (e.g., Weather Station, Miniram, PID, data loggers etc.) and air monitoring program (e.g., data log download, grab sampling)
3. Maintained all on-site heavy equipment (e.g., excavators, skid steer, off-road truck, screen, etc.)
4. Performed and documented daily inspections on the silt fence as outlined in the certified SESCP
5. Completed the excavation, screening, stockpiling, loading and transportation of all lead impacted soil area (A-1, A-2 and A-3). From Jan 31st to Feb 18th 2005, a total of 403 trucks have hauled 9,292 tons of lead impacted soils off-site for disposal [averaging 620 tons/day of lead soils removed from the site].
6. Continued to collect and submit for analysis confirmatory lead soil samples (base and sidewall samples) as outlined in the RAWP documents (e.g., RAWP and regulatory response letters)
7. Performed additional lead soil excavation and re-confirmatory sampling (if required) as outlined in the RAWP in those area which exhibited a lead soil concentration > 400 mg/kg
8. Continued excavation of process waste area B-1. All materials have been placed on and covered with poly sheeting. A total of 96 tons from the B-1 process wastes area have been excavated, screened and transported off-site as hazardous waste for disposal.
9. Continued excavation and screening of clean soils (C-1). Confirmatory samples (as outlined in the RAWP documents) of stockpiled clean soils were collected for every 300 cubic yards of material stockpiled.
10. Secured the Stream Encroachment Permit from the NJDEP Land Use Regulation Program. The Freshwater Wetland General Permit No. 4 (GP4) is anticipated for approval during the week of February 28, 2005. Based on the receipt of permits, excavation, screening, loading, transportation and disposal of PCB impacted soils existing within delineated wetland areas are tentatively scheduled to begin on March 1, 2005.



L.E. CARPENTER & COMPANY ~ NJD002168748
BOROUGH OF WHARTON, MORRIS COUNTY, NEW JERSEY
SOURCE REDUCTION REMEDIAL PROJECT PROGRESS UPDATE NO. 5

II. PROPOSED SOURCE REDUCTION REMEDIAL ACTIONS - FEBRUARY 28TH THROUGH MARCH 4TH 2005

1. Continue with excavation, screening, loading, off-site transportation of the process waste area B-1
2. Continue with the excavation, screening, stockpiling, and confirmatory sampling the clean soils area C-1
3. Initiate excavation, screening, stockpiling, loading, transportation and disposal of PCB impacted soils west of and within permitted wetlands areas existing within the Wharton Enterprise property east of the LEC site.



Photographic Log Progress Update No. 5

Client Name: L.E. CARPENTER & COMPANY		Site Location: Wharton, Morris County, NJ	Project No.: 00-06527.09
Photo No. 1	Date 2/19/05		
Description Excavating clean soils (C-1) View looking northwest			
Photo No. 2	Date 2/23/05		
Description Excavating B-2 process waste area. View looking south southeast towards the Rockaway River			



Photographic Log Progress Update No. 5


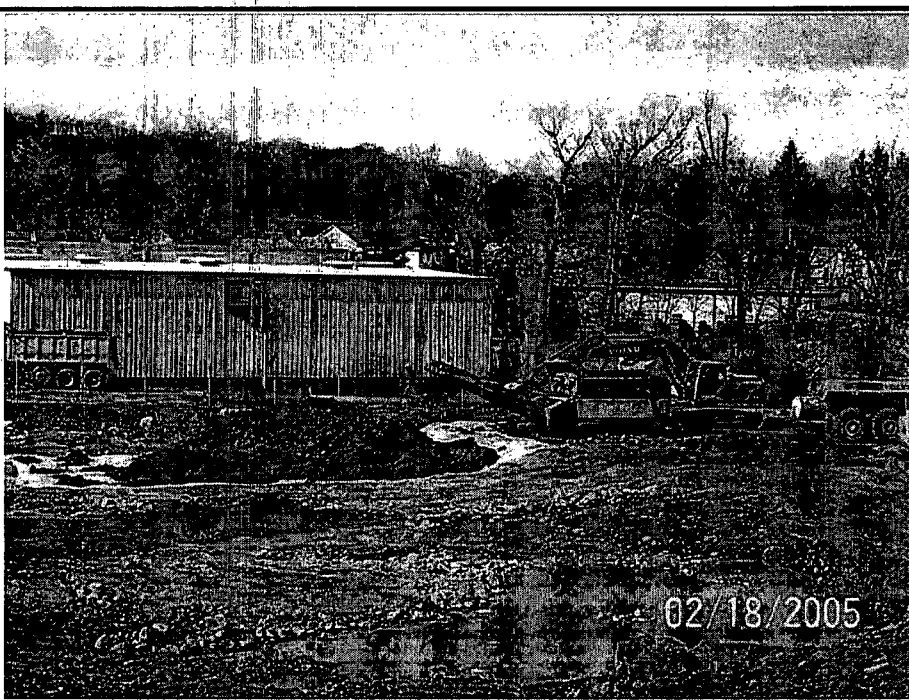
Client Name: L.E. CARPENTER & COMPANY		Site Location: Wharton, Morris County, NJ	Project No.: 00-06527.09
Photo No. 3	Date 2/19/05		
Description Stockpiling B-2 process waste area materials View looking west			

Photo No. 4	Date 2/18/05	
Description Screening B-1 process waste area materials View looking west		
