



October 12, 2007

Mr. Joseph Canzano  
EPA-New England, Region 1  
1 Congress St.  
Suite 1100 (SEW)  
Boston, MA 02114-2023


Dear Joseph,


Per your request here is an update of the improvements we have made based on your site visit.

1. We have sealed both drains in the Zodiac Garage with cement – see photos enclosed.
2. We have purchased and placed a flammable storage cabinet in the Zodiac Garage – see photo
3. Waste gasoline drums have been vented, grounded and stenciled – see photos
4. Ring around fuel fill covers painted to match covers to prevent accidental switching – see photo
5. Have asked Gloucester DPW to replace manhole cover by dumpster, it's on their list to do
6. Had Waste Management install drain plug in dumpster – see photo
7. Debris on edge of water by ramp has been cleaned up – see photos
8. Parts washer has been replaced with Aqueous model – see photo
9. Purchased and installed flammable storage cabinet in ob shop – see photos
10. All 3 floor drains in ob shop & marine store plugged w/cement – see photos
11. Gas & oil containers in ob shop replaced with safety cans – see photo
12. Flammable storage cabinet purchased and installed in west shed – see photo
13. Ordered replacement for frayed fuel hose, waiting for correct swivel connectors
14. Stenciled "gas" & "diesel" on ramp pipes – see photo
15. Gas tank storage locker labeled as flammable & all tanks empty – see photo
16. Guard rails around propane tanks painted yellow, stand pipe painted red – see photo
17. Kerosene and waste oil tanks all stenciled and valves plugged – see photos. We also plan to replace all our 275 gallon tanks with double walled tanks later this Fall.
18. Empty fuel and oil containers disposed of and junk batteries covered – see photo
19. Urinal discharge to harbor has been removed – see photo
20. Have purchased waste water treatment system from Next Generation and are in process of installing. See copy of installation layout attached. Will also connect test tank and sink drains in ob shop to this system.
21. Have contacted for professional assistance with **spill prevention plan** and **storm water drain permitting**.

Thank you for your help and patience while we work on these projects.

Sincerely yours,

  
Joan Chabot  
Office Manager

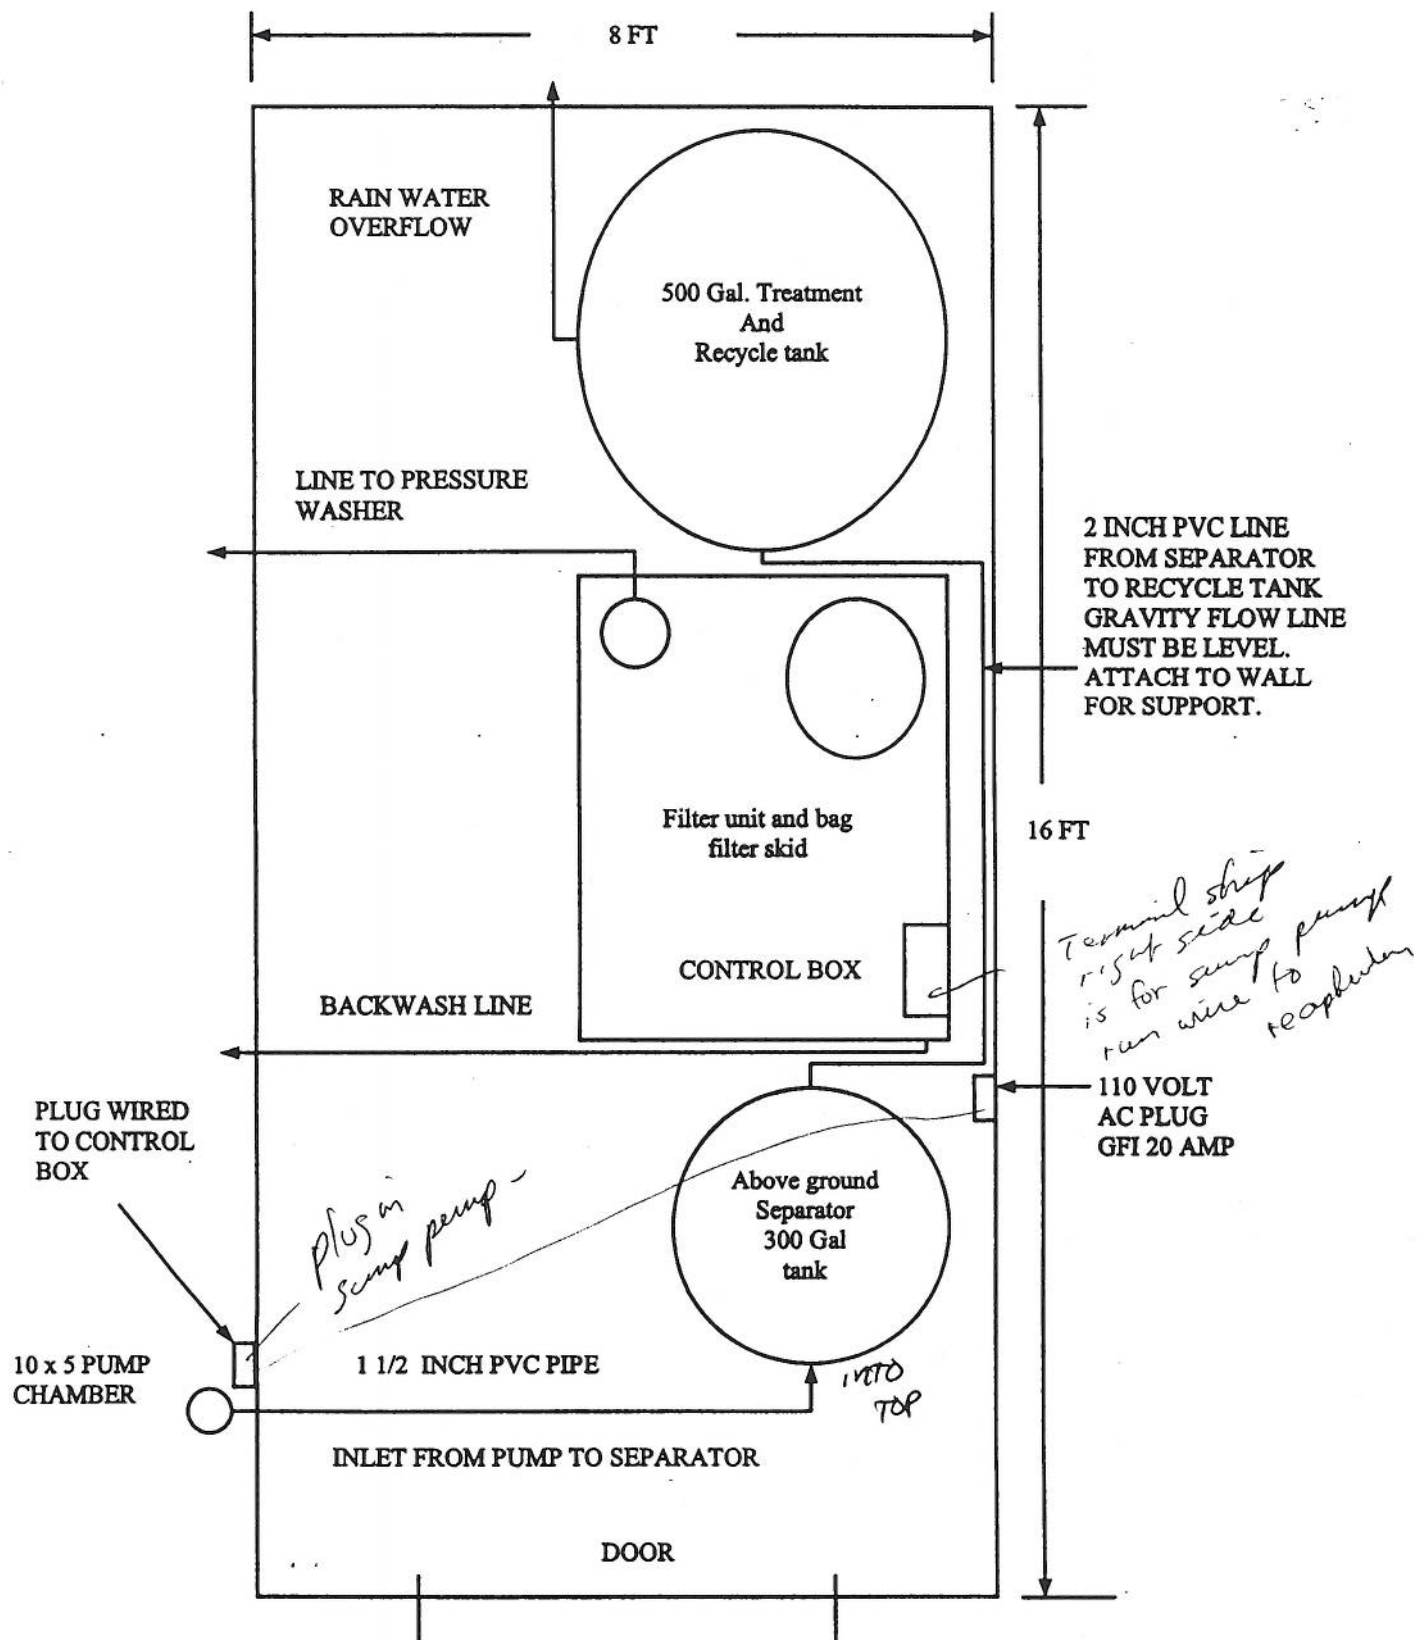

BUILDING LAYOUT AND INSTALLATION FOR RECYCLE SYSTEM  
BROWNS YACHT YARD

SCALE 1/2 INCH = 1 FT.
