

City of Baltimore Wet Weather Consent Decree Smoke and Dyed Water Testing Form

Page 1 of 1

Sewershed: Gwynns Falls

Company: Savin

Date: 7/8/2009

Test to be performed:

Smoke ☐ Dyed Water ☒

Ground Condition:

Dry ☒ Damp ☐ Wet ☐

Supervisor: JAW


Manhole_ID: S03YY_009MH

Test ID: D1032-026027

Notification Made: NA

(Residents, Fire, 311)

Field Sketch: Show all manholes with Numbers, Blower Placement Locations, Sandbag or Isolation Locations, Street Names, Building Addresses and Locations, Defect Locations and Photo Numbers.

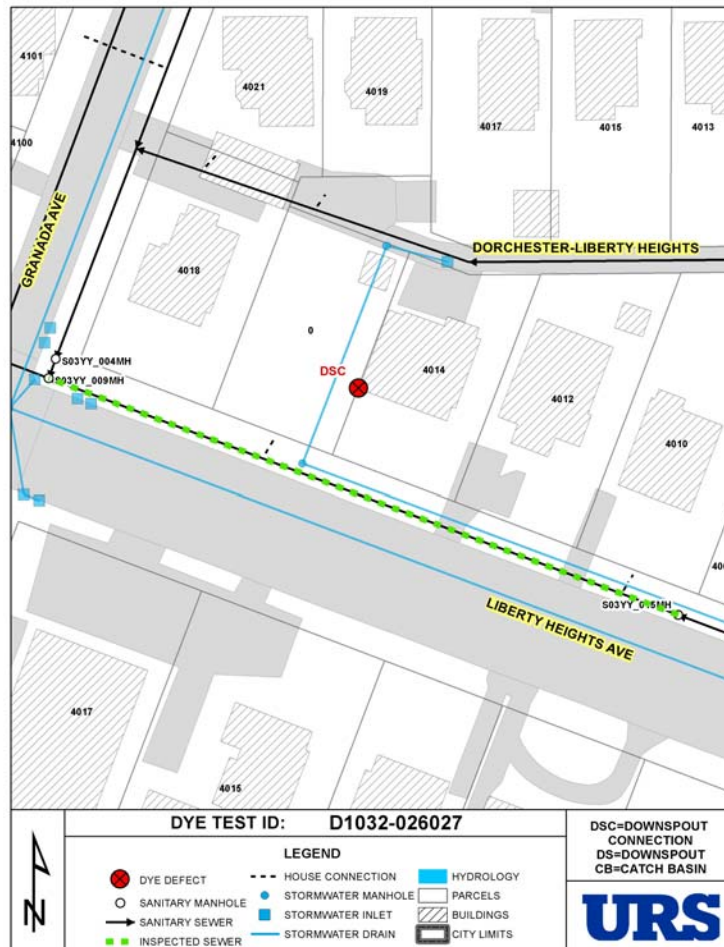

Defect Loc	Obs_ClockFrom	Obs_ClockTo	Observation	Obs_Remarks
0			Start of Survey	
0			Manhole	S03YY_015MH
0			Water Level	
188.5	02		Tap Factory Active	From 4014 Liberty Heights
188.6000061			Dye Test Visible	@ TFA - toilet
188.6000061			Dye Test Visible	@ TFA - downspout
200			End of Survey	DYE TEST COMPLETED
200			Manhole	S03YY_009MH
