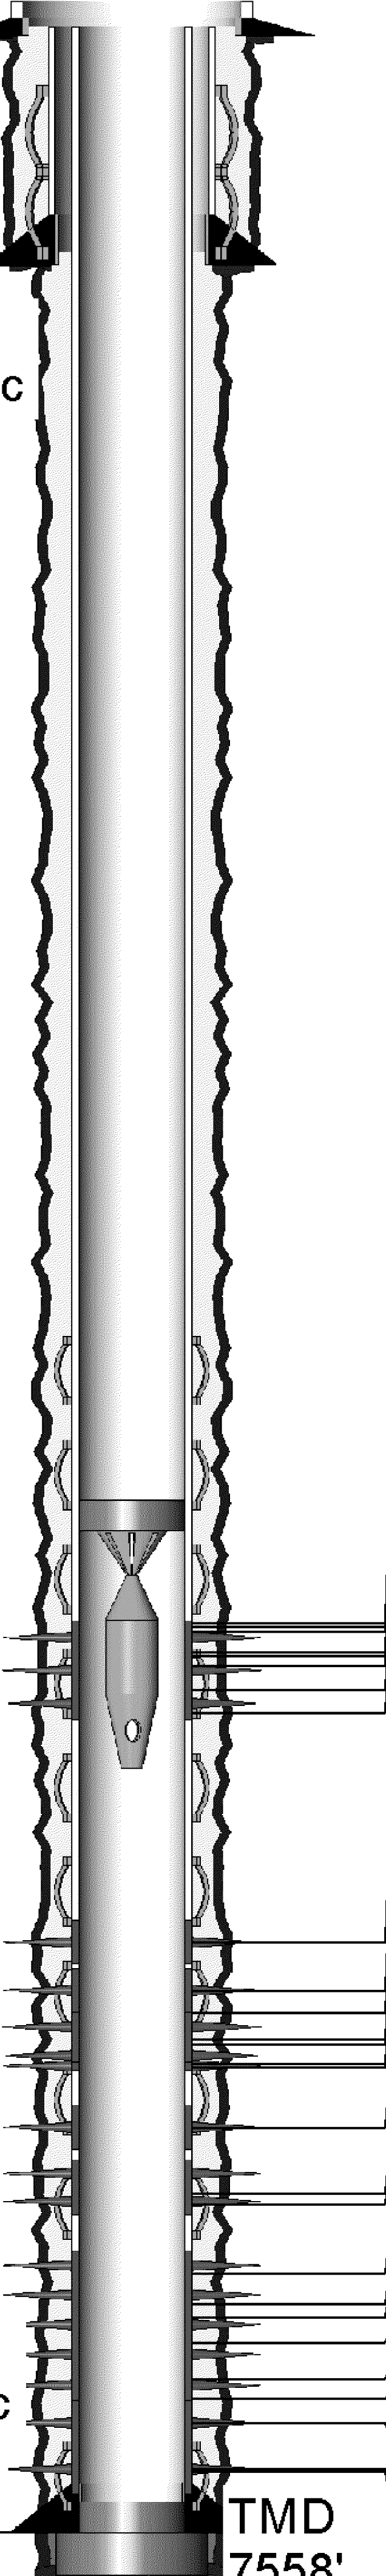


Event: Pre Well for Side track Event End: 10/28/2008 00:00 Sec. Reason: PREPARE FOR REDRILLING End Status: FINISHED - SUCCESS Well Classification: DEVELOPMENT			OCCIDENTAL OF ELK HILLS INC 318A-35S			Wellbore: ORIGINAL HOLE PBMD: 6,400.0ft Btm TMD: 7,558.0ft Spud Date: 6/27/2002 00:00 BH Coord X: 6,150,817.18uss ft BH Coord Y: 2,287,308.76uss ft					
Ground Level: 925.4ft Datum: ORIGINAL KB @ 946.40ft (default) API No.: 0403020777											
Casing Shoes (ft)	Schematic (10/28/2008)	Openings Top/Btm/Type/Status	PLUG BACK Report Date: 10/24/2008 00:00			CONDUCTOR CASING Report Date: 6/24/2002 00:00					
61.0		<i>Tulare Zone Deemed An Exempt Aquifer By EPA</i>	Component	Top MD (ft)	Btm MD (ft)	Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
			CEMENT	6,400.0	6,642.0	CASING JOINT(S)	14.000			21.0	61.0
1,049.5			PLUG BACK Report Date: 4/4/2008 00:00			SURFACE CASING Report Date: 6/28/2002 00:00					
			Component	Top MD (ft)	Btm MD (ft)	Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
			FISH	6,642.0	6,991.2	CASING JOINT(S)	9.625	K-55	36.00	21.0	1,003.6
			PLUG BACK Report Date: 7/21/2002 00:00			CASING JOINT(S)	9.625	K-55	36.00	1,003.6	1,003.6
			Component	Top MD (ft)	Btm MD (ft)	CASING JOINT(S)	9.625	K-55	36.00	1,003.6	1,048.4
			CEMENT	7,453.0	7,550.0	GUIDE SHOE	9.625		36.00	1,048.4	1,049.5
			PLUG BACK Report Date: 7/21/2002 00:00			PRODUCTION CASING Report Date: 7/12/2002 00:00					
			Component	Top MD (ft)	Btm MD (ft)	Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
			CEMENT	7,550.0	7,558.0	CASING JOINT(S)	7.000	N-80	29.00	21.0	6,869.3
			PLUG BACK Report Date: 7/21/2002 00:00			FLAG JOINT	7.000	N-80	29.00	6,869.3	6,894.4
			Component	Top MD (ft)	Btm MD (ft)	CASING JOINT(S)	7.000	N-80	29.00	6,894.4	7,453.0
			CEMENT	7,550.0	7,558.0	FLOAT COLLAR	7.000	N-80	29.00	7,453.0	7,454.4
						CASING JOINT(S)	7.000	N-80	29.00	7,454.4	7,548.5
						FLOAT SHOE	7.000	N-80	29.00	7,548.5	7,550.0
