# **Progress Report**

April 13, 2016 Steam Enhanced Extraction at the Former Williams AFB, ST012 Site

Mesa, AZ



## 1. Summary

This report covers the period of operations from Tuesday, April 5, 2016 through Monday, April 11, 2016. The following table provides a summary of the project operational status.

**Table 1. Project Summary** 

Table 1: Troject Sammary		
	Value	Unit
Target Treatment Zone (TTZ) Soil Volume	410,000	cubic yards (cy)
Area	199,000	square feet (ft²)
Upper Depth of Treatment	145	feet (ft) below ground surface (bgs)
Lower Depth of Treatment	245	ft bgs
Vapor Liquid Treatment Started	09/29/14	
Thermal Operations Started	09/29/14	
Last Process Data Update	04/11/16	
Last Temperature Data Update	04/11/16	
Estimated Total Days of Operation	422	days
Days of Operation	560	days
Days of Operation vs. Estimate	133	percent (%)
Estimated Total Energy Usage	11,343,000	kilowatt hours (kWh)
Total Energy Used	5,827,793	kWh
Used Electrical Energy vs. Estimate	51	%
Total Steam Injected	302.4	million pounds (lbs)
Projected Total Steam Injection	320	million lbs
Steam Injected Vs Projected	94	%
Total Mass Removed in Vapor Based on		
Photoionization Detector (PID) Readings	1,166,662	lbs
Total Mass Removed as NAPL	1,386,808	lbs
Average Daily NAPL Mass Removal Last Week	0	lbs/day
Total Vapor and Liquid Mass Removal (based on	2 552 470	lbs
PID readings)	2,553,470	
Average Power Usage Rate Last Week	477	kilowatts (kW)
Average Wellfield Vapor Extraction Rate Last	366	standard cubic feet per minute (scfm)
Average Condensate Production Rate Last Week	0.2	gallons per minute (gpm)
Average Water Extraction Rate Last Week	141	gpm
Total Water Extracted	92,146,959	gallons
Total Recovered Light Non-Aqueous Phase Liquid	211,082	gallons
Average Water Discharge Rate Last Week	171	gpm
Total Treated Water Discharge	121,739,000	gallons

Note: The NAPL removal rate in the table is the average weekly removal based on full NAPL batch transfers. The actual NAPL recovery may be more, but is not accounted for until a full batch (~1,500 gallons) of NAPL is processed in the NAPL conditioning system. Based on daily readings of the NAPL level in the holding tank, the current NAPL production is estimated to approximately 0-100 lbs/day.

Operational highlights from the past week include:

- The site wide depressurization that was initiated on Friday, March 4, 2016 continues.
- Eductor skids were operated with six skids online throughout this period. The average liquid extraction rate from the formation was approximately 141 gpm.
- Collected process, wellfield and laboratory samples per the sampling schedule.
- Conducted regular maintenance on the treatment system.
- The following MPE wells will require maintenance:
  - o CZ11\*
  - o CZ09
  - o CZ18
  - o CZ16
  - o LSZ31

<sup>\*</sup>Temperatures at this MPE well are at boiling – well maintenance will be postponed until the temperature is below boiling due to health and safety concerns. TerraTherm is currently working on a method to actively cool the well.

## 2. Vapor Extraction

Figure 1 below shows the vapor extraction rate from the site. Note that the estimated steam extraction rate is a calculated value based on the water generated at the moisture separators after cooling the vapors from the wellfield. Based on energy balance analysis, additional steam is likely being pulled into and condensing in the liquid extraction system. This steam extraction is not measureable and not accounted for in Figure 1. Additionally the wellfield flow is calculated as the difference between the air stripper flows and thermal accelerator influent, and is therefore only an estimate.

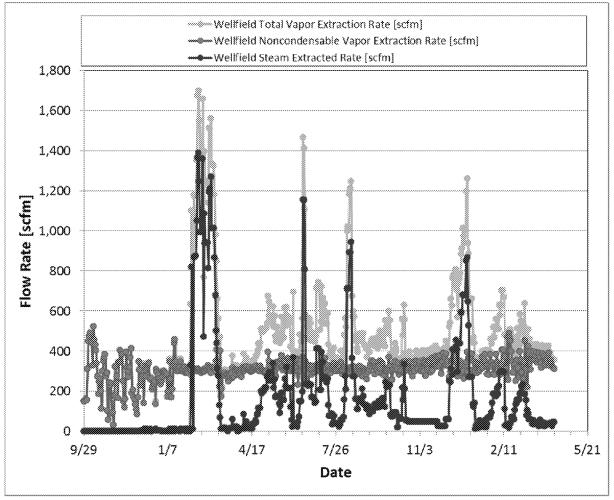


Figure 1. Vapor Extraction Rate

Note: Well SVE01M was tied into the SEE extraction system on June 5, 2015. Wells SVE10M and SVE14M were tied into the SEE extraction system on September 23, 2015.

#### 3. PID Measurements

The following figure depicts the PID concentrations from the wellfield effluent to the effluent of the thermal accelerators collected since the start of operations. Note that PID readings of 0.0 parts per million by volume (ppmV) are shown in the figures as 0.01 ppmV due to the logarithmic scale that does not allow display of 0-values. Accelerator influent readings are interpolated for days where no data is collected, since the value is used in the mass removal calculation.

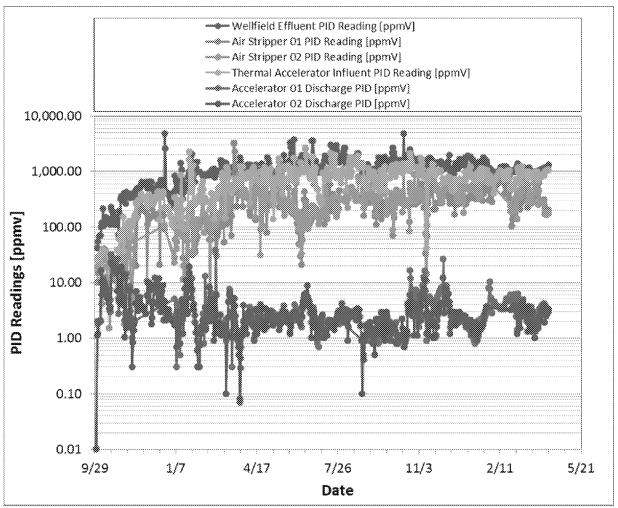


Figure 2. PID Readings

#### 4. Mass Removal

The mass removal is calculated based on the PID and laboratory data collected at the thermal accelerator influent and the LNAPL recovered. The figure also depicts the mass removed based on PID and laboratory data.

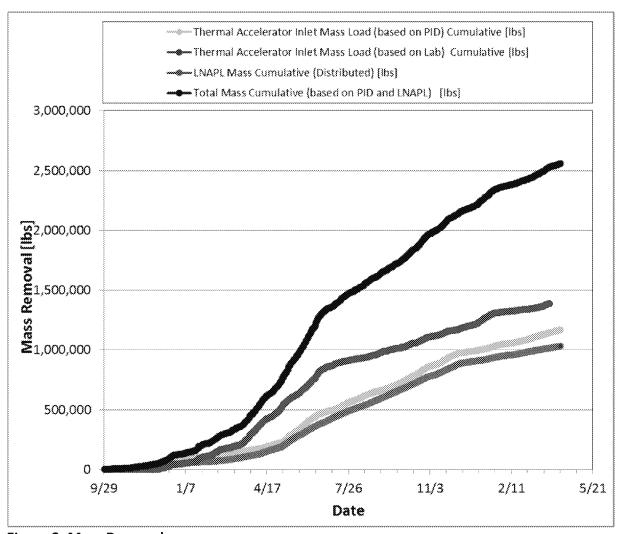


Figure 3. Mass Removal

Note: A NAPL density of 6.57 lbs/gallon is used to convert the NAPL volume to pounds. A molecular weight of 106.168 g/mol (corresponding to xylene) is used to convert PID readings to concentrations.

## 5. Daily Mass Removed

Figure 4 outlines the daily mass removed as vapor and LNAPL. The total daily mass removed is the combination of vapor and LNAPL. The liquid mass removal is captured in the vapor phase due to the volatilization of liquid contaminants in the air strippers.

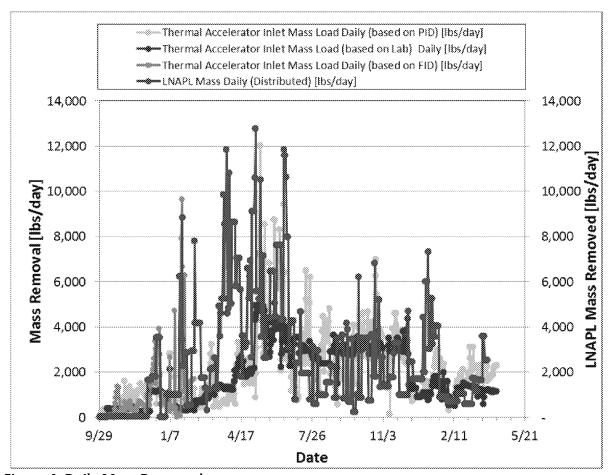


Figure 4. Daily Mass Removed

Note: Laboratory data are not collected daily. The "Thermal Accelerator Inlet Mass Load (based on lab)" is an average daily rate of actual laboratory data results received. The report has been updated based on laboratory data results received for samples collected through February 24, 2016 (please note that the February 11, 2016 correction factor looks to be biased low and is not thought to be a representative sample; it has not been used in the mass removal calculations).

Note that accumulated LNAPL is pumped through the NAPL conditioning system in a batch style process. The LNAPL daily mass removal rate has been calculated by calculating an average daily rate based on the total gallons processed for each batch over the number of days between batches. Last transfer included in the report was on March 29, 2016.

## 6. Power Usage

The cumulative power usage is shown below. All electricity used at the site is utilized to run the process system and steam generators.

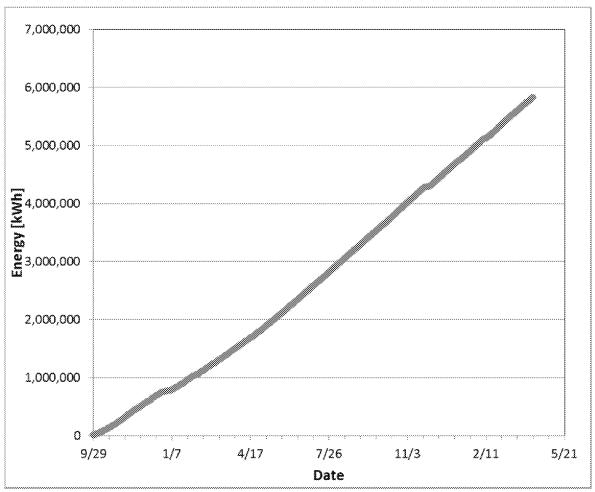


Figure 5. Cumulative Power Usage

## 7. Average Temperature

A detailed review of thermocouple sensor depths and temperatures over time was performed week ending November 13, 2015. Results of the review and updates are detailed below in Table 2 and Figure 6.

**Table 2. Temperature Monitoring Sensor History** 

Temperature Monitoring Point	Temperature Monitoring Sensor History
TMP01	Well compromised 6/9/2015, select sensors back online 7/15/2015. Well not extended down in the Lower Permeable Zone (LPZ) and LSZ.
TMP03	Well compromised 12/18/15. All sensors offline as of 12/18/15.
TMP04	Well compromised 6/21/2015. Not included in LPZ and LSZ since 6/21/2015.
TMP05	Well compromised 5/6/2015, select sensors back online 7/15/2015. Sensors deeper than 160 ft have not been online since 5/6/2015 and therefore are not included in UWBZ, LPZ and LSZ.
TMP06	Well compromised 3/27/2015, select sensors back online 7/14/2015.
TMP07	Well compromised 3/27/2015, select sensors back online 7/14/2015.
TMP08	Well partly compromised 9/11/2015 from 210 ft and down. The 215 and 235 ft sensors are still operating.
TMP09	Well compromised 2/9/2015 before CZ was turned on and UWBZ was up to temperature. The CZ and UWBZ temperatures have been excluded. LSZ temperatures have not been updated since 2/9/2015 (taken out of LSZ average).
TMP12	Sensors from 150 to 170 ft bgs only at ~50C. Brings down the average in CZ and UWBZ.
TMP13	Well compromised 3/27/2015, select sensors back online 4/30/2015. Since 7/1/2015 no sensor deeper than 225 ft has been operational.
TMP15	Well compromised 8/15/2015. 8/15/2015 temperatures assumed from this day.
TMP17	Well compromised 3/27/2015, select sensors back online 6/12/2015 but not reporting properly, total failure 7/16/2015. Depths lower than 235 ft not included in average since well was not at temperature when sensors failed. 7/16/2015 temperatures applied to average since well failed.

The average soil temperatures as degrees Celsius (°C) and degrees Fahrenheit (°F) are shown in the figure below by treatment zone (i.e., LSZ, UWBZ and CZ).

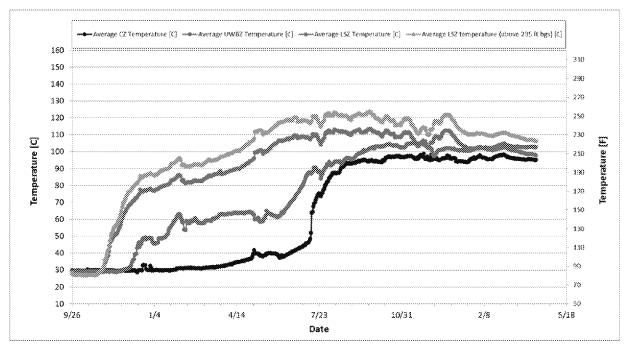


Figure 6. Average Soil Temperatures

Table 3 below provides a breakdown of the maximum average temperatures achieved at individual temperature monitoring points throughout SEE operations. The table below breaks down the average temperatures achieved across the CZ, UWBZ, Lower Permeability Zone (LPZ) and the LSZ to date. The LSZ is further broken down into the average for all LSZ sensors and those LSZ sensors above 235 ft bgs.

**Table 3. Temperature Monitoring Point Maximum Depth-Averaged Temperature** 

•	Temperature Monitoring Point Maximum Depth-Averaged										
	Temperature <sup>1</sup> (°C) During SEE Operations by Zone										
Temperature Monitoring Point	CZ	UWBZ	LPZ	LSZ	LSZ (depths above						
	114.0	120 F	NI/A	NI/A	235 ft bgs)						
TMP01	114.9	130.5	N/A	N/A	N/A						
TMP03	N/A	N/A	137.5	114.2	120.7						
TMP04	N/A	N/A	103.8	118.8	127.1						
TMP05	110.3	N/A	N/A	N/A	N/A						
TMP06	N/A	N/A	137.4	135.0	135.9						
TMP07	N/A	N/A	134.6	137.2	140.2						
TMP08	N/A	N/A	136.6	131.3	135.4						
TMP09	N/A	N/A	132.5	134.1	139.3						
TMP11	N/A	N/A	110.6	119.1	131.7						
TMP12	78.7	95.3	121.8	121.4	131.3						
TMP13	102.1	119.8	130.6	138.4	140.0						
TMP14	N/A	N/A	133.6	124.3	136.3						
TMP15	113.1	123.3	128.7	126.5	135.6						
TMP16	N/A	N/A	126.7	120.5	131.0						
TMP17	N/A	N/A	135.2	136.9	136.9						
Maximum depth-	103.8	117.2	128.4	127.5	134.0						
averaged by zone <sup>2</sup>	102.0	11/.2	120.4	127.5	134.0						

If N/A, Temperature Monitoring Point has no sensors in that zone

Temperature of the thermocouples across each depth zone are averaged for each TMP and each available time interval and then the maximum value of those averages throughout operations is listed in the table.

<sup>&</sup>lt;sup>2</sup> Average of maximum depth-averages listed above for all TMPs in each zone.

## 8. Vertical and Horizontal Temperature Profiles

The following Figures 7 and 8 show the temperature in °C versus depth profiles for each of the 17 individual temperature monitoring points. Please see Table 2 for an updated temperature monitoring sensor status.

Temperature highlights for the past week include:

- Minor temperature drops were observed across the arrays at perimeter wells TMP 02 and TMP 10.
- Slight temperature decreases were observed in the UWBZ and LSZ at TMP 08. The current maximum temperature for this array is 46°C at 185 and 190 ft bgs.
- Minor temperature decreases were observed in all three zones at TMPs 11, 14 and 16.
- The majority of the TMPs either remained stable or saw very minor temperature reductions.

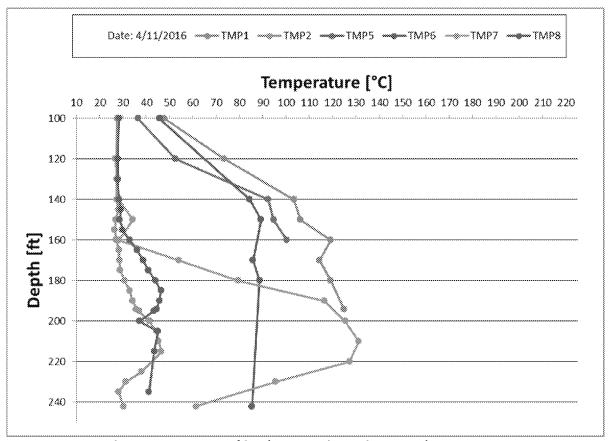


Figure 7. Vertical Temperature Profiles (TMP01 through TMP08)

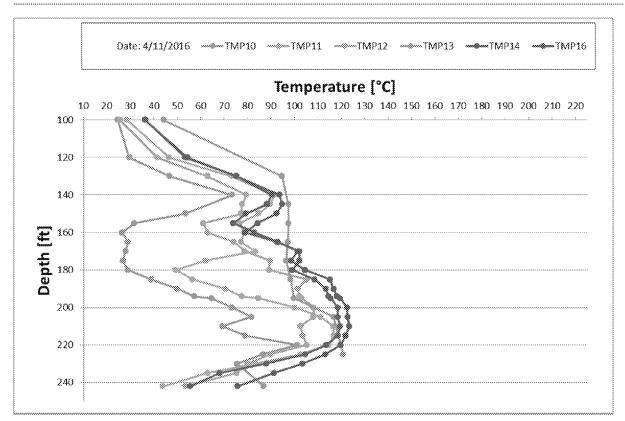


Figure 8. Vertical Temperature Profiles (TMP09 through TMP17)

Figures 9-12 show the horizontal temperature distribution across the site in four depth intervals.

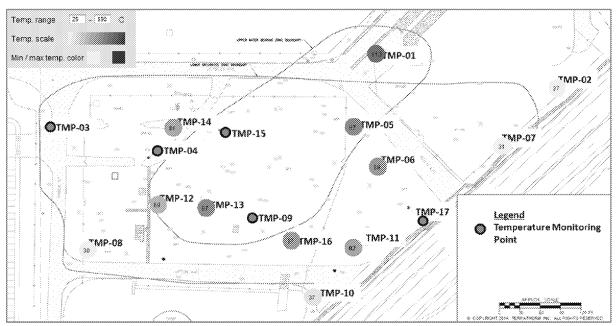


Figure 9. Horizontal Temperature Distribution across the CZ (145-160 ft bgs) (temperatures shown in °C)

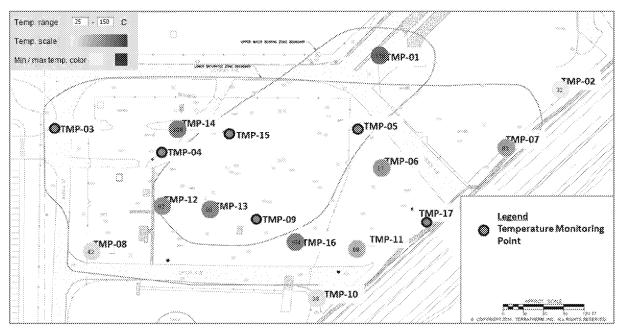


Figure 10. Horizontal Temperature Distribution across the UWBZ (161-195 ft bgs) (temperatures shown in °C)

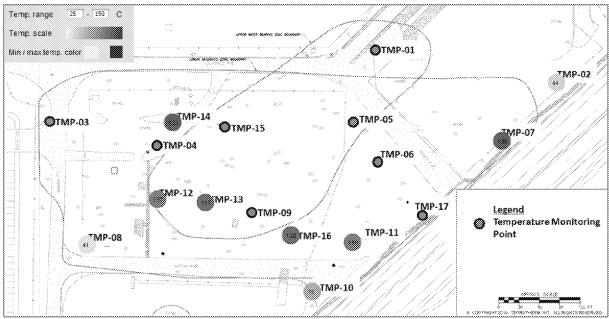


Figure 11. Horizontal Temperature Distribution across the Lower Permeable Zone (196-210 ft bgs) (temperatures shown in °C)

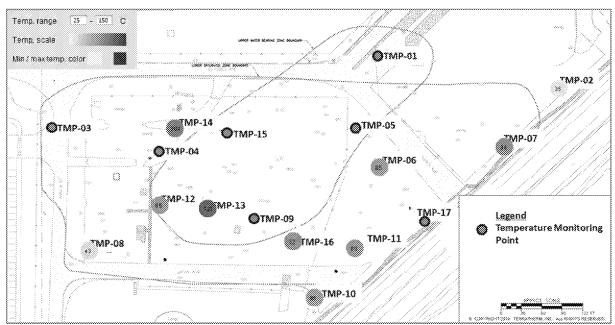


Figure 12. Horizontal Temperature Distribution across the LSZ (211-245 ft bgs) (temperatures shown in °C)



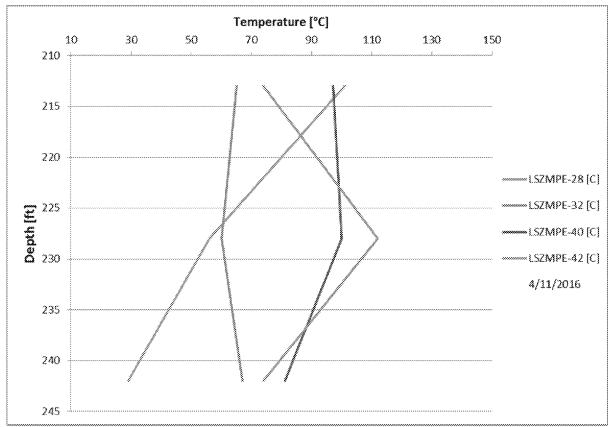


Figure 13. Temperatures by Depth at Selected LSZ Extraction Wells (211-245 ft bgs) (temperatures shown in °C)

## 9. Cumulative Steam Injection

Steam injection was initiated Thursday, October 16, 2014. Figure 14 below shows the cumulative steam injection for each of the three injection zones.

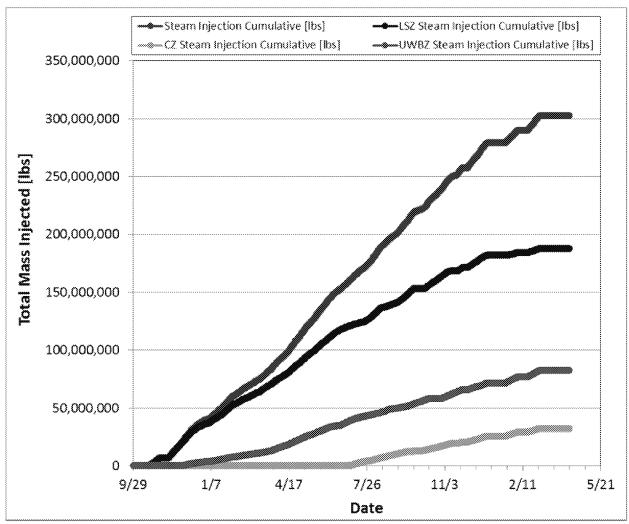


Figure 14. Cumulative Steam Injection for Each of the Three Injection Zones

## 10. Steam Injection Rates

The figure below shows the steam injection rates for each of the three injection zones.

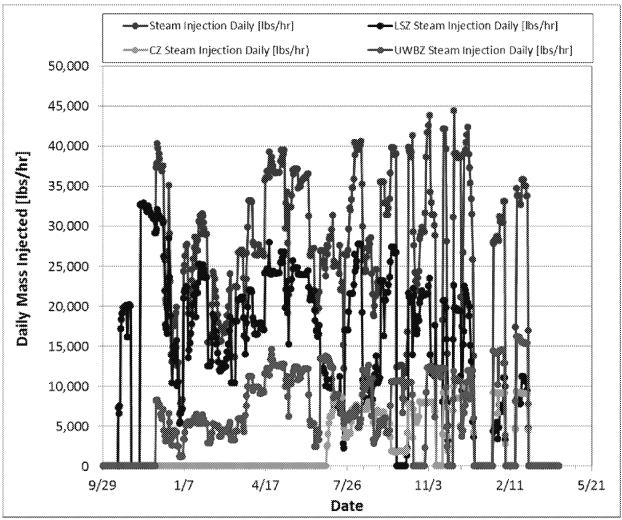


Figure 15. Steam Injection Rate for Each of the Three Injection Zones

## 11. Cumulative Water Extraction by Zone

The cumulative water extraction for each of the three treatment zones is shown below. The cumulative water extraction is calculated based on flow meters installed at each of the 57 extraction wells (accuracy should be considered +/- 20%). The figure below shows the net liquid extracted from the subsurface at the site and does not include the fraction of water that is recirculated to the eductor wells and used as motive water.

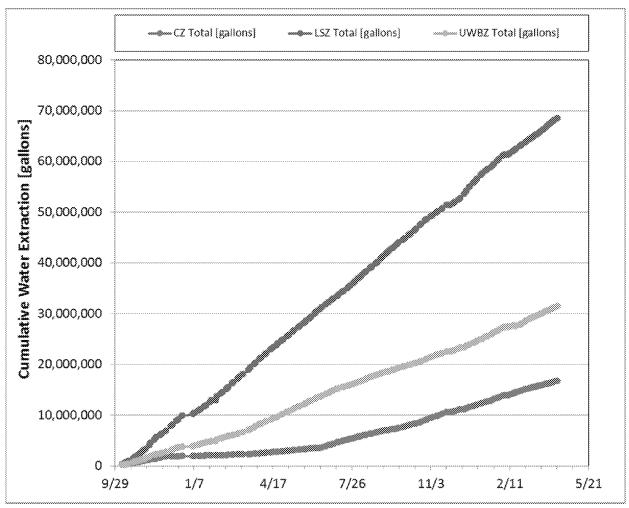


Figure 16. Cumulative Water Extraction for Each of the Three Treatment Zones

## 12. Water Extraction Rates by Zone

The figure below shows the water extraction rates for each of the three treatment zones.

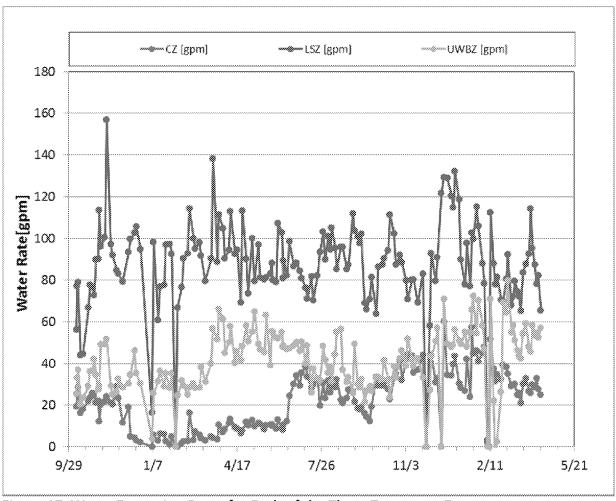


Figure 17. Water Extraction Rates for Each of the Three Treatment Zones

#### 13. Cumulative Water Balance

The cumulative water balance for the site is shown below. The chart shows the net liquid extracted from the subsurface at the site and does not include the fraction of water that is recirculated to the eductor wells and used as motive water.

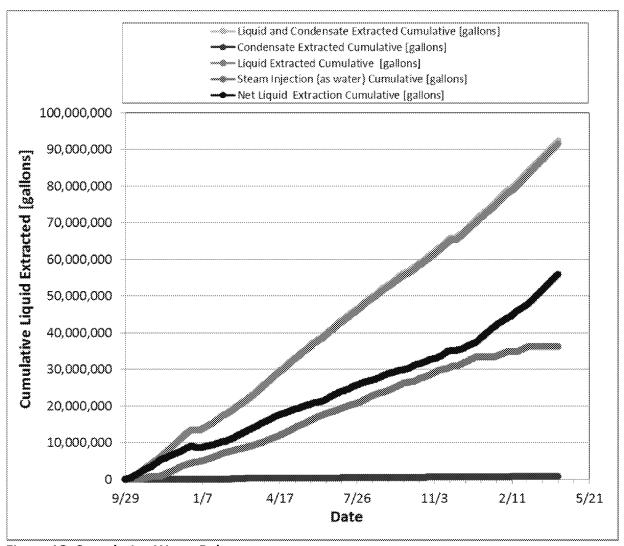


Figure 18. Cumulative Water Balance

### 14. Water Balance Rate

The total system water extraction rates are shown in the figure below.

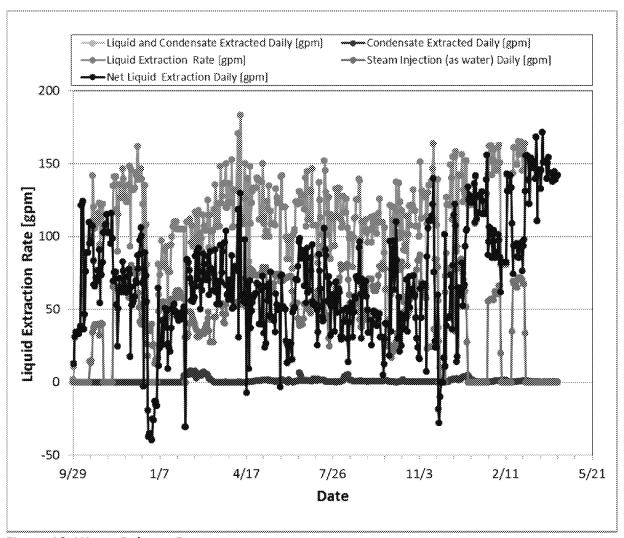


Figure 19. Water Balance Rates

#### 15. Perimeter Water Level Data

Table 4 below presents the change in perimeter groundwater elevations since SEE system startup. The readings collected on September 24, 2014 (not shown) represent baseline conditions. A negative number shows that the groundwater elevation is lower than the baseline elevation, thus indicating an inward hydraulic gradient into the treatment zone. Liquid extraction began on September 29, 2014. Perimeter water level data are collected on a weekly basis. The regional groundwater table at the Site is increasing at a rate of approximately 1.5 ft/year; thus, each measured value shown in Table 4 has been corrected to take the regional changes into account.

**Table 4. Perimeter Groundwater Elevation Changes** 

	3/18/	2016	3/25/	2016	4/1/:	2016	4/8/2016				
	Change from										
Monitoring Well	Baseline	Previous	Baseline	Previous	Baseline	Previous	Baseline	Previous			
CZ/UWBZ Wells											
ST012-C01	-1.90	-0.25	-1.99	-0.06	-2.32	-0.30	-2.38	-0.03			
ST012-C02	-2.03	-0.40	-2.25	-0.19	-2.55	-0.27	-2.72	-0.14			
UWBZ Wells											
ST012-RB-3A	-4.32	-0.96	-4.54	-0.19	-4.85	-0.28	-6.60	-1.72			
ST012-U02	-3.24	-0.97	-3.73	-0.46	-4.22	-0.46	-4.44	-0.19			
ST012-U11	-5.00	-0.48	-5.17	-0.14	-5.48	-0.28	-4.93	0.58			
ST012-U12	-6.61	-1.22	-7.02	-0.38	-7.24	-0.19	-6.83	0.44			
ST012-U37	-5.79	-1.17	-6.05	-0.23	-6.37	-0.29	-6.01	0.39			
ST012-U38	-2.83	-0.89	-3.19	-0.33	-3.60	-0.38	-3.64	-0.01			
LSZ Wells											
ST012-W11	-7.13	-0.50	-6.99	0.17	-7.09	-0.07	-6.67	0.44			
ST012-W12	-6.61	-0.64	-6.57	0.07	-6.68	-0.08	-6.25	0.46			
ST012-W24	-6.09	-1.08	-5.61	0.51	-5.77	-0.13	-5.50	0.30			
ST012-W30	-6.64	-0.67	-6.50	0.17	-6.58	-0.05	-6.15	0.46			
ST012-W34	-5.32	-0.72	-5.24	0.11	-5.41	-0.14	-5.19	0.25			
ST012-W36	-5.46	-0.76	-5.42	0.07	-5.53	-0.08	-5.29	0.27			
ST012-W37	-7.57	-2.20	-7.37	0.23	-7.71	-0.31	-7.30	0.44			
ST012-W38	-4.68	-0.61	-4.76	-0.05	-4.94	-0.15	-4.77	0.20			

Figure 20 shows the manually collected groundwater elevation trends since system startup. Additionally Figure 21 shows the groundwater elevations continuously logged in selected perimeter wells equipped with transducers. The regional groundwater table correction has also been applied to Figure 20 below.

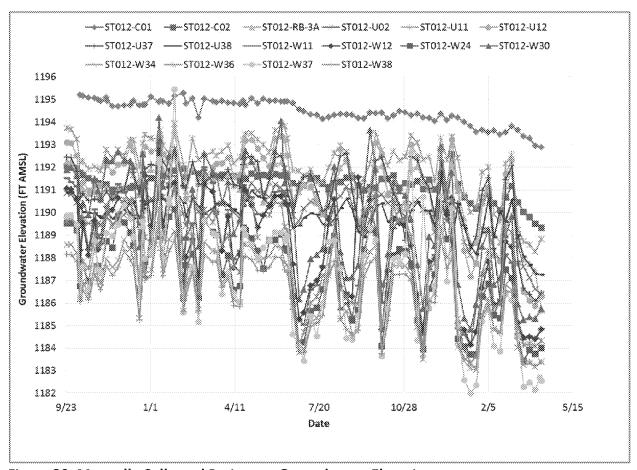


Figure 20. Manually Collected Perimeter Groundwater Elevations

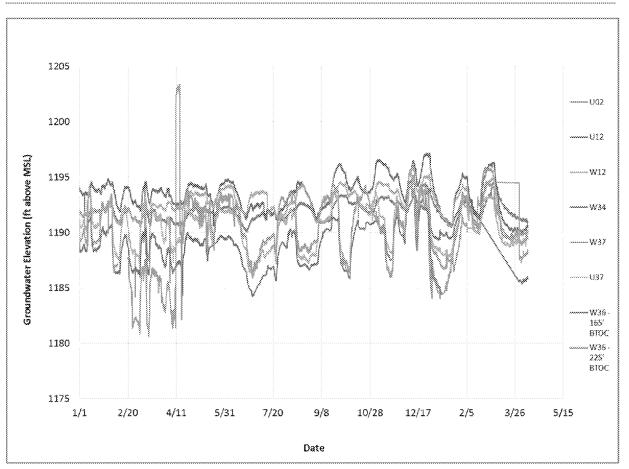


Figure 21. Automatically Collected Perimeter Groundwater Elevations

Table 5 below presents the measured LNAPL thicknesses of the perimeter wells at the site. Perimeter LNAPL thickness data are collected on a weekly basis.

**Table 5. Perimeter LNAPL Thicknesses (ft)** 

Monitoring Well		3/18/2016			3/25/2016			4/1/2016		4/8/2016					
	Before	After	Weekly	Before	After	Weekly	Before	After	Weekly	Before	After	Weekly			
	bailing/	Bailing/	Gallons	bailing/	Bailing/	Gallons	bailing/	Bailing/	Gallons	bailing/	Bailing/	Gallons			
CZ/UWBZ Wells	pumping	pumping	Removed	pumping	pumping	Removed	pumping	pumping	Removed	pumping	pumping	Removed			
ST012-C01	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			
ST012-C02	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			
UWBZ Wells															
ST012-U02	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			
ST012-U11	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			
ST012-U12	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			
ST012-U37	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			
ST012-U38	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			
ST012-RB-3A	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			
LSZ Wells															
ST012-W11	5.57	5.57	0.00	5.49	5.49	0.00	5.49	5.49	0.00	5.52	5.52	0.00			
ST012-W12	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			
ST012-W24	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			
ST012-W30	0.01	0.01	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			
ST012-W34	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			
ST012-W36	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			
ST012-W37	13.39	13.39	0.00	13.60	13.60	0.00	20.97	11.85	5.95	14.74	9.85	3.19			
ST012-W38	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00			

#### Notes:

<sup>&</sup>lt;sup>1</sup>Estimated gallons removed based on 4-inch casing and difference in product level in well before and after removal. Does not account for volume of hose or other equipment

in the column of product. Includess all dates bailed/pumped in the week.

 $<sup>^2</sup>$ In addition to the weekly measurements, ST012-W37 LNAPL levels were measured and LNAPL was pumped on 2/10/16 and 2/15/16

April 13, 2016

On December 1, 2014, temperatures at selected perimeter wells were added to the monitoring program. Figure 22 below shows the manually collected temperatures recorded at the wells included in the monitoring program. Additionally, Figure 23 shows the temperatures continuously logged in selected perimeter wells equipped with transducers.

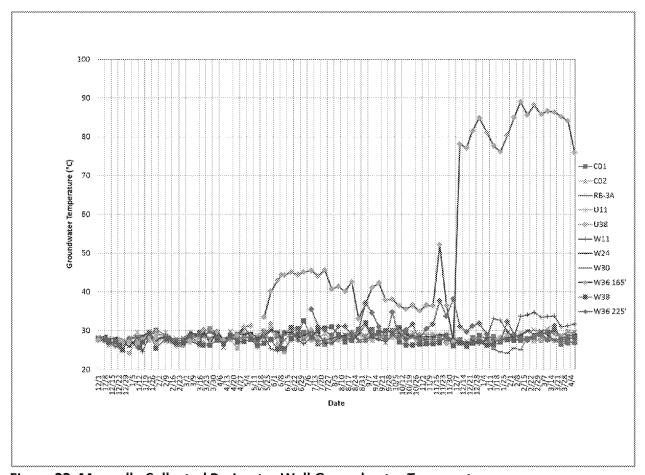


Figure 22. Manually Collected Perimeter Well Groundwater Temperatures

Note: Thermocouples are measured at approximate depths as follows (in feet below top of casing): C01=162; C02=168; RB-3A=161; U11=180; U38=164; W11=228; W24=230; W30=231; W36=225; and W38=228.

As a response to the increased temperatures observed at W36 on December 12, 2015 steam at nearby UWBZ9 and UWBZ25 were decreased.

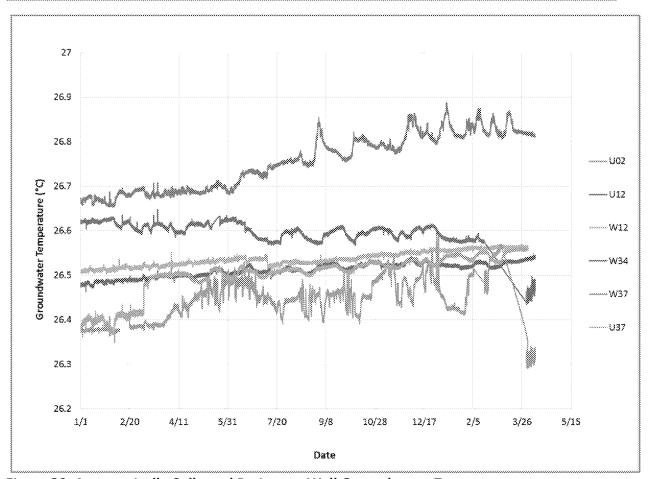


Figure 23. Automatically Collected Perimeter Well Groundwater Temperatures

#### Notes:

On March 7, 2015 operational personnel replaced the U37 logger unit. The increase in temperature on March 7, 2015 at U37 is a result of this replacement. Transducers in W34 and W37 were reinstalled on March 30, 2016.

Transducers are measured at depths as follows (in feet below top of casing): U02= 175; U12= 175; U37= 182; W12= 228; W34= 225; and W37= 226.

## 16. Natural Gas Usage

The following figure shows the natural gas usage rate in cubic feet per hour (cf/hr) and cumulative natural gas use in cubic feet (cf) to date at the site.

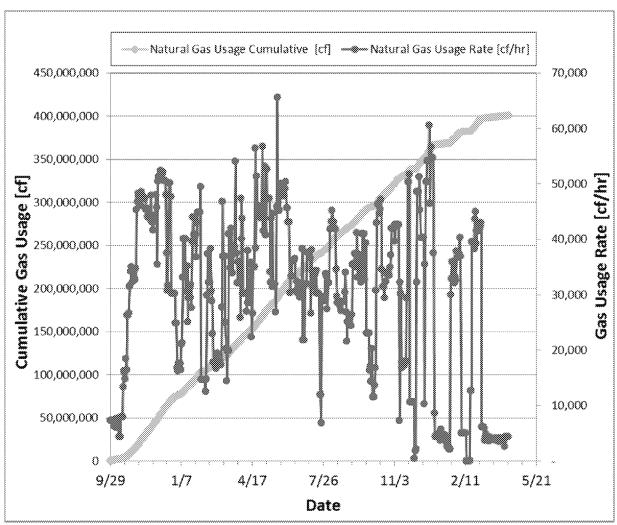


Figure 24. Natural Gas Usage

## 17. Waste Generation

On January 19, 2015 a total of 8,033 gallons of material from tank cleanout activities was removed from the site by Mesa Oil for recycling. The mass of JP-4 in the material was estimated to be 2,857 gallons or 18,800 lbs.

On February 18 and 19, 2015 a total of 24,430 gallons of material from tank cleanout activities was removed from the site by Mesa Oil for recycling. The mass of JP-4 in the material was estimated to be 3,645 gallons or 23,984 lbs.

On March 12, 2015 a total of 11,359 gallons of predominantly water from tank cleanout activities was removed from the site by Mesa Oil for recycling. The JP-4 mass in the water was limited.

On March 20, 2015 the first shipment of bag filters (four cubic yard boxes) from the SEE process treatment system was shipped offsite for non-hazardous disposal.

On March 30 and 31, 2015 a total of 32,000 lbs of spent liquid carbon was removed from the site by Evoqua Water Technologies for regeneration at their Red Bluff, CA facility.

On April 24, 2015 a shipment of bag filters (three cubic yard boxes) from the SEE process treatment system was shipped offsite for non-hazardous disposal.

On May 29, 2015 a shipment of bag filters (four cubic yard boxes) from the SEE process treatment system was shipped offsite for non-hazardous disposal.

On June 11, 2015 three 55-gallon drums of soil dug from around the Hypro NAPL filter were shipped offsite for non-hazardous disposal.

On June 10, 2015 a total of 5,727 gallons of oily bio-impacted water from tank cleanout activities was removed from the site by Mesa Oil for recycling.

On June 25, 2015 a shipment of bag filters (four cubic yard boxes) from the SEE process treatment system was shipped offsite for non-hazardous disposal.

On August 19, 2015 a total of 16,000 lbs of spent liquid carbon was removed from the site by Evoqua Water Technologies for regeneration at their Red Bluff, CA facility.

On August 27, 2015 a total of five totes with approximately 250 gallons each of water/solids from disinfection of the liquid carbon vessel were removed from the site by MP Environmental for disposal.

On October 22, 2015 a shipment of bag filters (four cubic yard boxes) from the SEE process treatment system was shipped offsite for non-hazardous disposal.

On November 23, 2015 a shipment of bag filters (four cubic yard boxes) from the SEE process treatment system was shipped offsite for non-hazardous disposal.

On December 31, 2015 a shipment of bag filters (four cubic yard boxes) from the SEE process treatment system was shipped offsite for non-hazardous disposal.

On February 1, 2016 a shipment of bag filters (four cubic yard boxes) from the SEE process treatment system was shipped offsite for non-hazardous disposal.

On March 10, 2016 a shipment of bag filters (four cubic yard boxes) from the SEE process treatment system was shipped offsite for non-hazardous disposal.

#### 18. NAPL Reuse

On April 7, 2015 a total of 12,647 gallons of stored NAPL was sent to Mesa Oil for reuse. The analysis showed that 703 gallons of the total fluid was water. The water has been subtracted from the NAPL recovery estimate.

On April 21-22, 2015 a total of 13,076 gallons of stored NAPL was sent to Mesa Oil for reuse. Analysis showed a water content between <1% to 3% or a total of 227 gallons of water. The water removed has been subtracted from the NAPL recovery estimate.

On May 7, 2015 a total of 5,722 gallons of stored NAPL was sent to Mesa Oil for reuse.

On May 21, 2015 a total of 1,400 gallons of stored NAPL was sent to Mesa Oil for reuse.

On June 24, 2015 a total of 6,771 gallons of stored NAPL was sent to Mesa Oil for reuse.

#### 19. Estimated Formation Water Temperature

The estimated formation water temperatures are indicated in Table 6 below. The formation water temperatures have been estimated for each MPE well by measuring the eductor liquid feed and return flow rate together with the eductor liquid feed and return temperatures. The enthalpy increase in the liquid return temperature as compared to the liquid feed stream temperature is used to provide the MPE well specific formation temperature. Estimated formation water temperatures above the boiling point likely indicate that steam is being pulled into the liquid extraction system. These estimated data for each MPE well location are used in conjunction with the extracted vapor data collected at the MPE wells to make determinations on steam breakthrough around the site. All of these data are reviewed holistically (with other site data such as the TMP data) to determine when and where steam cycling events should commence.

The location of each MPE well is also indicated in the table. Since perimeter extraction wells are expected to extract colder water from outside of the treatment zone, the formation temperature at these locations is not expected to reach steam temperatures. Thus, full or partial steam breakthrough can still be occurring at the perimeter locations without the estimated formation water temperature being at boiling. Please note that if the estimated formation water temperature is higher than 220°C for a given well, ">220" is indicated in the table.

Please note that no vapor temperature data were collected from the MPE wellheads November 5-13, 2015 due to issues with the temperature equipment.

**Table 6. Estimated Well Formation Temperatures** 

	MPE Formation Temperatures  MPE Formation Temperatures																												
Well -	Well	Required to Reach	Reached Steam	Vapor Extraction	2/2/16	2/4/16	2/11/16	2/15/16	2/17/16	2/19/16	2/24/16	2/26/16	3/1/16	3/3/16	3/7/16	3/9/16	3/11/16	3/14/16	3/16/16	3/18/16	3/21/16	3/24/16	3/28/16	3/30/16	4/1/16	4/4/16	4/6/16	4/8/16	4/11/16
	Location	Steam Temperature	Temperature (Calculated)	Max Temperature [°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]
CZ07	Perimeter	No	Yes	158	>220	>220	212	104	105	100	>220	- 8	>220	>220	>220	>220	218	>220	>220	220	208	×220	225	2.10	194	209	211	198	181
CZ08	Perimeter	No	Yes	192					8		>220											192	199	165	181	153	187	192	176
CZ09	Perimeter	No	Yes	156	123	139	76	126	×220	86	123	97	186	149	134	125	153	2.39	2.77	194	182	142	88						
CZ10	Perimeter	No	Yes	206	201	>220	170	50	Ç()	55	186	71	*2.20	198	1.86	178	169	:87	59	165	161	150	168	144	166	158	156	123	- 6
CZ11	Interior	Yes	Yes	217														ļ											
CZ12	Perimeter	No	Yes	220	>220	>220	205	186	218	35	191	212	>220	>220	>220							>220	-220	>220	>220	×220	73	>220	+220
CZ13	Perimeter	No	Yes	160	>220	>220	83		45	80	>220	172	+220	>220	>220	×220	213	206	194	189	204	167	192	193	193	196	188	190	182
CZ14	Perimeter	No	Yes	112	216	>220	186	96	96		9220		>220	>220	216	>220	206	181	2.0	200	>220	>220	165	200	174	210	171	199	140
CZ15	Interior	Yes	Yes	170	>220	>220	130	100	101	116	>220	134	>220	>220	>220	>220	201	137	198	90	196	180	188	1.77	169	192	183	186	177
CZ16	Perimeter	No	Yes	212	>220	9220	216	82	84	73	>220	>220	×220	>220	>220	>220	203	>220	>220	>220	185	>220	162	72	107	82	102	98	
CZ17	Perimeter	No	Yes	200	>220	>220				2.1.2	20%	110	191	>220	2:9	205	180	197	1,79	188	1.70	185	175	184	187	182	2.73	180	176
CZ18	Perimeter	No	Yes	208	>220	200	88	158	182	79	167	93	152	165	142	143	170	120	140	89	132	157	141	38	214	>220			
CZ19	Perimeter	No	Yes	110	182	>220	184	107	106	95	198	191	207	219	1.88	>230	213	207	183	191	178	178	183	111	175	166	166	186	170
CZ20	Outside CZ	No	No	111	102	95	91		71	67		88	101	87	86	82	113	86	95	93	94	101	84	83	71	112	88	80	38
LSZ01	Interior	Yes	Yes	126	206	>220	122	157	136	80	195	198	191	197	137	170	195	167	195	213		1,77	175	190	159	162	179	180	214
LSZ02	Interior	Yes	Ves	130	181	192	7.4	×220	>220	116	195	66	181	193	188	130	193	168	174	58		177	186	197	>220	167	208	197	>220
LZS04	Interior	Yes	Yes	206																									
LSZ05	Interior	Yes	Yes	220	>220	>220	207	149	149	130	>220	77	>220	>220	>220	>220	215	203		>220	170	206	203	195	139	212	213	205	215
LSZ06	Interior	Yes	Yes	218	>220	>220	>220	124	124	177	207	188	177	>220	189	>220	+220	>220	92.20	>220	220	190	203	195	>220	+220	202	214	193
LSZ08	Perimeter	No	Yes	120	155	160	1.98	152	143	82	130	63	122	130	124	1.00	143	232	108	108	121	126	108	123	111	126	124	120	133
LSZ11	Perimeter	No	Yes	119	92	96		44			94			97								104	102	99	99	98	106	103	95
LSZ12	Perimeter	No	Yes	126	187	181	153	126	128	97	164	164	126	176	154	180	157	123	157	153	153	156	156	157	1.44	136	157	147	149
LSZ13	Interior	Yes	Yes	125	150	167	>/20	210	209	33	178	139	×220	198	133	215	218	202	165	1.86	219	189	123	173	148	180	×220	187	200
LSZ14	Perimeter	No	Yes	177	197	196	171	125	123	68	207	169	196	185	168	158	143	165	158		138	166	186		163	157	168	156	153
LSZ15	Interior	Yes	Yes	208	+220	>220		120	108	135	710	193	205	202	209	196	202	205	207	303	191	195	162	202	207	191	195	195	201
LSZ16	Interior	Yes	Yes	205	200		188	92	89	28		48	205	199	178	170	1.75	137	155	9220	158	176	162	1.65	159	165	166	155	159
LSZ17	Perimeter	No	Yes	220	123	120	96	79	79	66 ***	101	68	109	105	98	97	99	98	97 255	122	94	99	95	91	96	95	97	96	95
LSZ28	Perimeter	No	Yes	129	172	189	175	68	68	76	175	4	176	168	1.72	148	151	1.72	4	164	166	144	133	195	159	165	154	151	134
LSZ29	Perimeter	No	Yes	116		208	115	177	163	>220	>220	-220	149	194	186	211	215	211	27	217	190	+220	9220	100	>220	200	>220	+220	>220
LSZ30 LSZ31	Interior Interior	Yes Yes	995 Van	133 147	>220 _33	9220 9220	1220	9 <b>220</b> 108	219		>220	95	9220 9220	9220 9220	238	9 <b>220</b>	210 182	164 181	7220 7220	9220 173	197 117	152	9220 200	>220	9220 134	7220 125	74	9220 46	22
			Yes		<b></b>	•									4			<del> </del>								<b></b>			
LSZ32	Interior	Yes	Yes	120 130	72.0 72.20	9220 9220		76 9220	96 9220	35	230	186 197	216 +220	9220	195 189	9220 198	197	234	398	9 <b>220</b> 202	220	204 193	220	190	202 133	138	220	220	120
LSZ33 LSZ34	Perimeter	No Voc	Yes	168	7220	7223	-	7220	7223	33 47	177		193	>220	174	158	170	123	275 383	192	220	193	181	190	173	166	184	170	175
LSZ34 LSZ35	Interior	Yes	766	121	113	1.1.5	111	115	115	47 118	110	166	183	177		103	109	106	103	192	176			101	103		104	101	102
LSZ35 LSZ36	Perimeter	No No	Yes	121	147	1.33	125	110 85	85	59	150	108 145	143	112	102	129	139	101	135	140	101 142	109	103	138	136	103 138	137	135	138
	Perimeter	No No	Yes	208	158	155	117	60 87	90		151	152	174	170	129	152	109					123	116	108	103		107	103	153
LSZ37 LSZ38	Perimeter	No No	Yes		<b></b>		99	60 60	90 98	76	157	131	154	148	143	1.92	109	170	102	123	137	<del> </del>	143	138	153	101	144	143	
LSZ38 LSZ39	Perimeter	No No	Yes No	116 118	240		379	185		72 18	122	131	120	116	148	131	124	121	125	143	126 137	153 126	124	1.20	133	141 145	145	121	128
LSZ39 LSZ40	Perimeter	No Vos	No Yes	135	9220		>220	180		1.5	2.22	213	220	×2.00	240	195	194	188	388	2220	137	120	196	182	202	191	199	196	180
	Interior	Yes			<del> </del>				102										159				190				155	166	119
LSZ42	Perimeter	No	Yes	130	>220	L	178	103	202	72	179	167	180	177	172	177	128	158	1 233	172	121	175	1 23/2	172	158	162	100	200	1 1133 /

	MPE Formation Temperatures																												
147. II	Well	Required to Reach	Reached Steam	Vapor Extraction	2/2/16	2/4/16	2/11/16	2/15/16	2/17/16	2/19/16	2/24/16	2/26/16	3/1/16	3/3/16	3/7/16	3/9/16	3/11/16	3/14/16	3/16/16	3/18/16	3/21/16	3/24/16	3/28/16	3/30/16	4/1/16	4/4/16	4/6/16	4/8/16	4/11/16
Well -	Location	Steam Temperature	Temperature (Calculated)	Max Temperature [°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]	[°F]
UWBZ01	Interior	Yes	Yes	206					56	43	193	176	211	188	208	170	174	142	159	151	100	166	201	160	149	152	103	129	114
UWBZ02	Interior	Yes	Yes	210	22.0	>220		94	99	138	>220	73	-220				2220	2220	9220	×220	39	>220	220	9220	+220	159	>220	>220	9220
UWBZ04	Interior	Yes	Yes	201	>220	>220	>220	108		101	>220	146	9770	×2.00	>200	>220	>220	>220	>220	>220	920	168	187	192	204	179	197	182	188
UWBZ05	Interior	Yes	Yes	220	9220	+220		196		46	+220			>220	230	216	187	166	142	186	1.%	140	136	127	131	143	1,29	128	127
UWBZ06	Interior	Yes	Yes	165	364	175	169	120	119	103	165	92	172	178	1.64	161	165	>//0	168	129	106	132	124	1.12	116	124	116	113	108
UWBZ10	Perimeter	No	166	179	>220	>220	1.86	189	161	59	>220	89	>220	>220	200	198	1.72	206	216	196	194	180	1.72	1.66	1.70	163	166	161	148
UWBZ17	Perimeter	No	165	220	>220	+220	198	59	46	25	+220	63	+220	-220	>220	+220	>220	>220	×220	151	207	216	126	177	181	173	172	189	185
UWBZ18	Interior	Yes	100	200	>220	>220	>220			122	>220	95	>220	>220	>220	>220	>220	>220	143	91	>220	>220	>220	206	188	211	188	183	182
UWBZ19	Perimeter	No	7.0	162	>220	>220	154	121	120	69	201	98	>220	>220	×220	×220	>220	>220	9220	>220	200	183	170	205	154	156	158	166	119
UWBZ20	Dual Phase - Perimeter	No	No	112							96																		
UWBZ21	Outside UWBZ	No	Yes	118	9220	>220	161	170	201	92	5220	>220	+220	>220	>220	>220	>220	185	214	>220	>270	>220	220	>220	194	187	205	206	208
UWBZ22	Perimeter	No	Yes	127	9220	205	>220	23	43	>220	192	190	218	>220	>220	190	169	127	96		91	145	147		127	150	106		104
UWBZ23	Outside UWBZ	No	Yes	206					125	38	5220	5220	>220	+220	>220	>270	>220	>220	5220	9220	×220	209	220	>220	201	194	5220	194	203
UWBZ24	Dual Phase - Perimeter	No	18	200	-220	>220	-220	218	218	91	218	>220	+220	>220	>220	>220	-220	-220	-220	107	×220	>220	+220	208	220	212	9220	>220	190
UWBZ26	Outside UWBZ	No	Yes	105	352	165		132	131		150			167	138	110	133	160	133	137		138	122	122	133	111	137	116	135
UWBZ27	Outside UWBZ	No	Yes	115	200	1.44			52	100	166			133	113	1.14	131	109	114	118	121	113	118	96	136	1.05	113	96	137

RED	: at or above steam temperature (≥210 °F)
GREEN	: below steam temperature (<210 °F)

### 20. NAPL Screening Results and Calculated Benzene Concentrations

Figures 25-27 below present the screening level results for NAPL detected in samples collected from MPE wells across the site. Screening samples are typically collected on a weekly basis. The figures below also include calculated benzene concentrations of groundwater samples collected from MPE wells across the site.

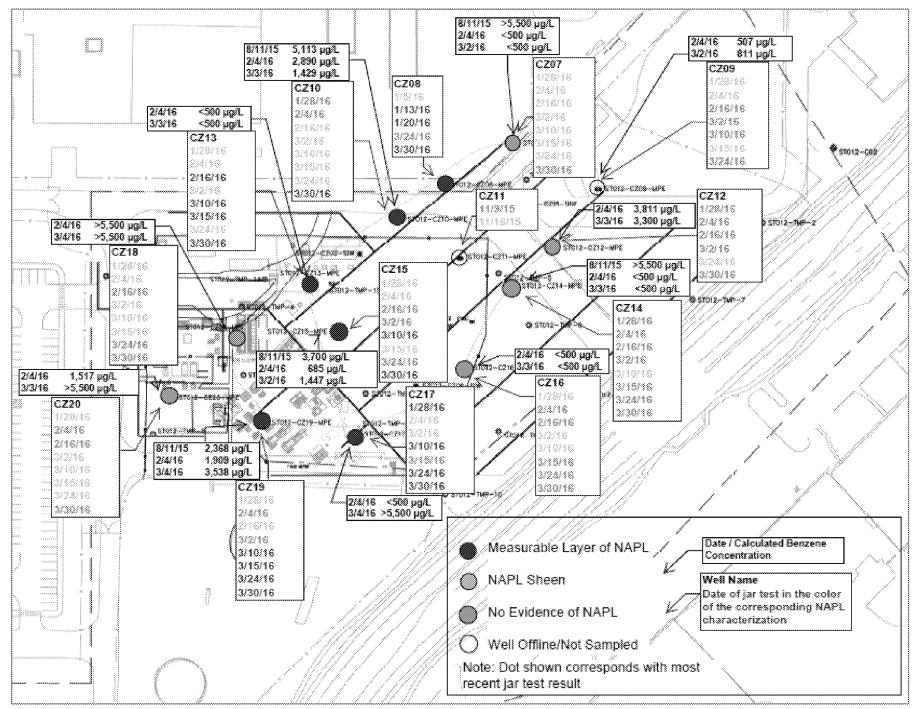


Figure 25. NAPL Screening Results and Calculated Benzene Concentrations - Cobble Zone

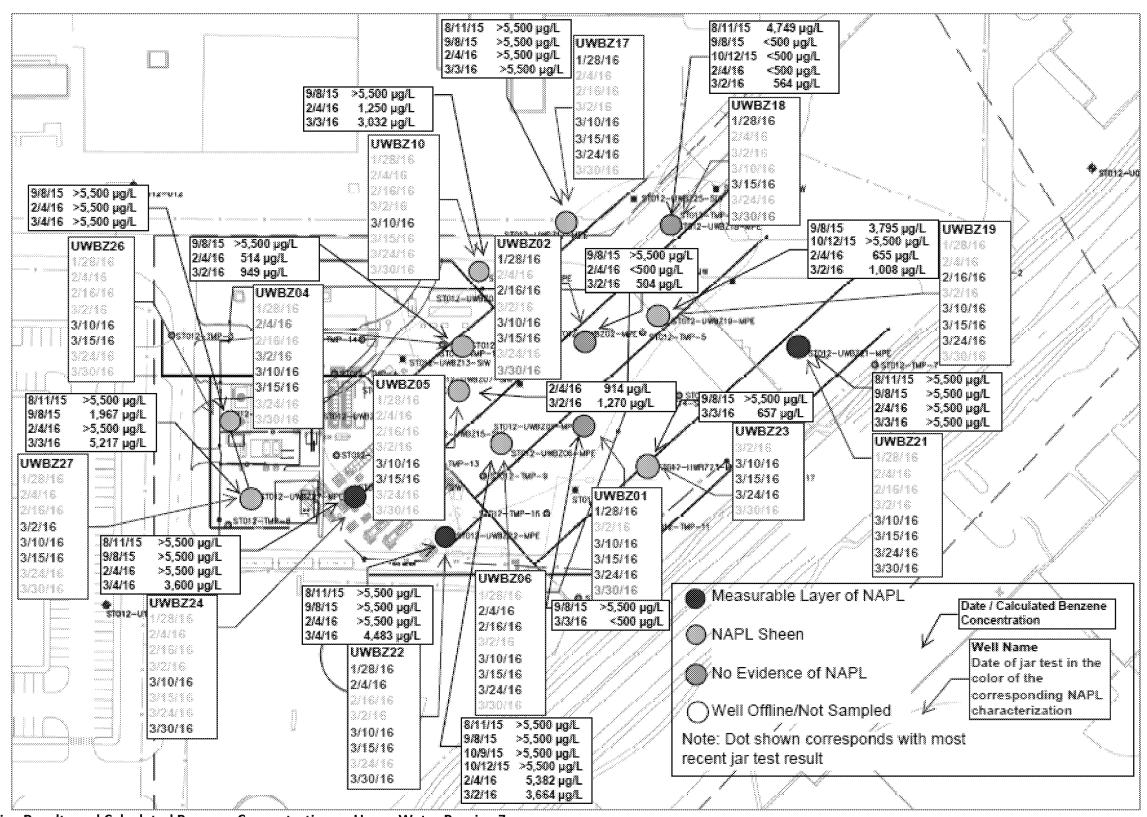


Figure 26. NAPL Screening Results and Calculated Benzene Concentrations – Upper Water Bearing Zone

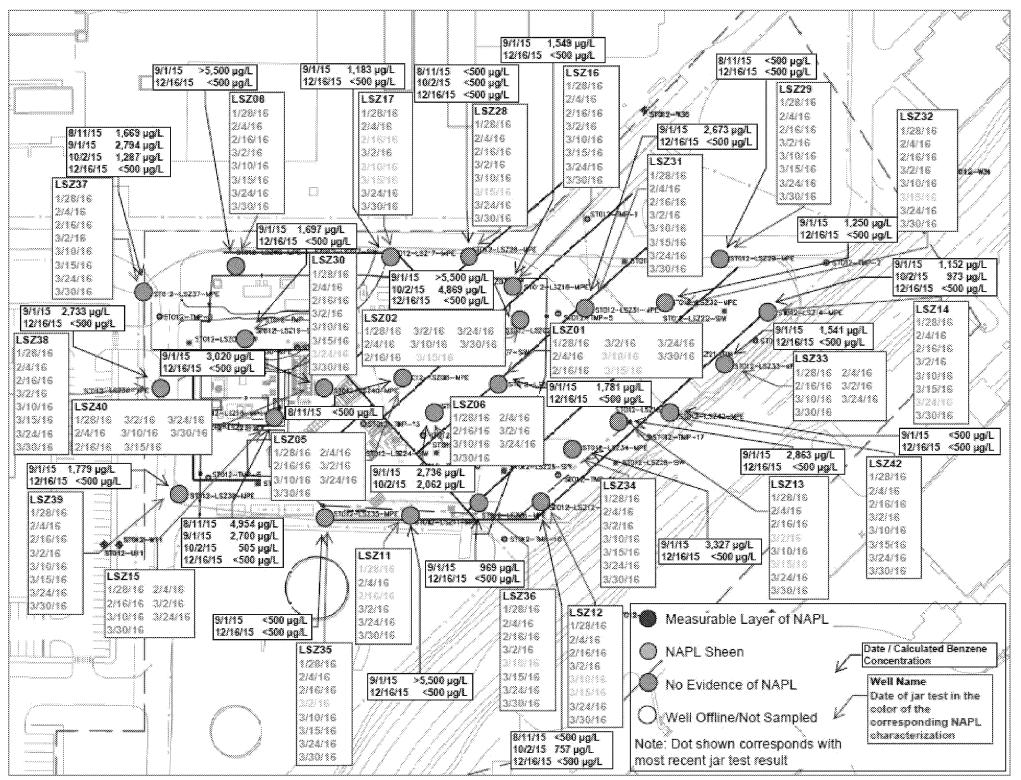


Figure 27. NAPL Screening Results and Calculated Benzene Concentrations – Lower Saturated Zone
