


KJMM Range Site Plan – 130726

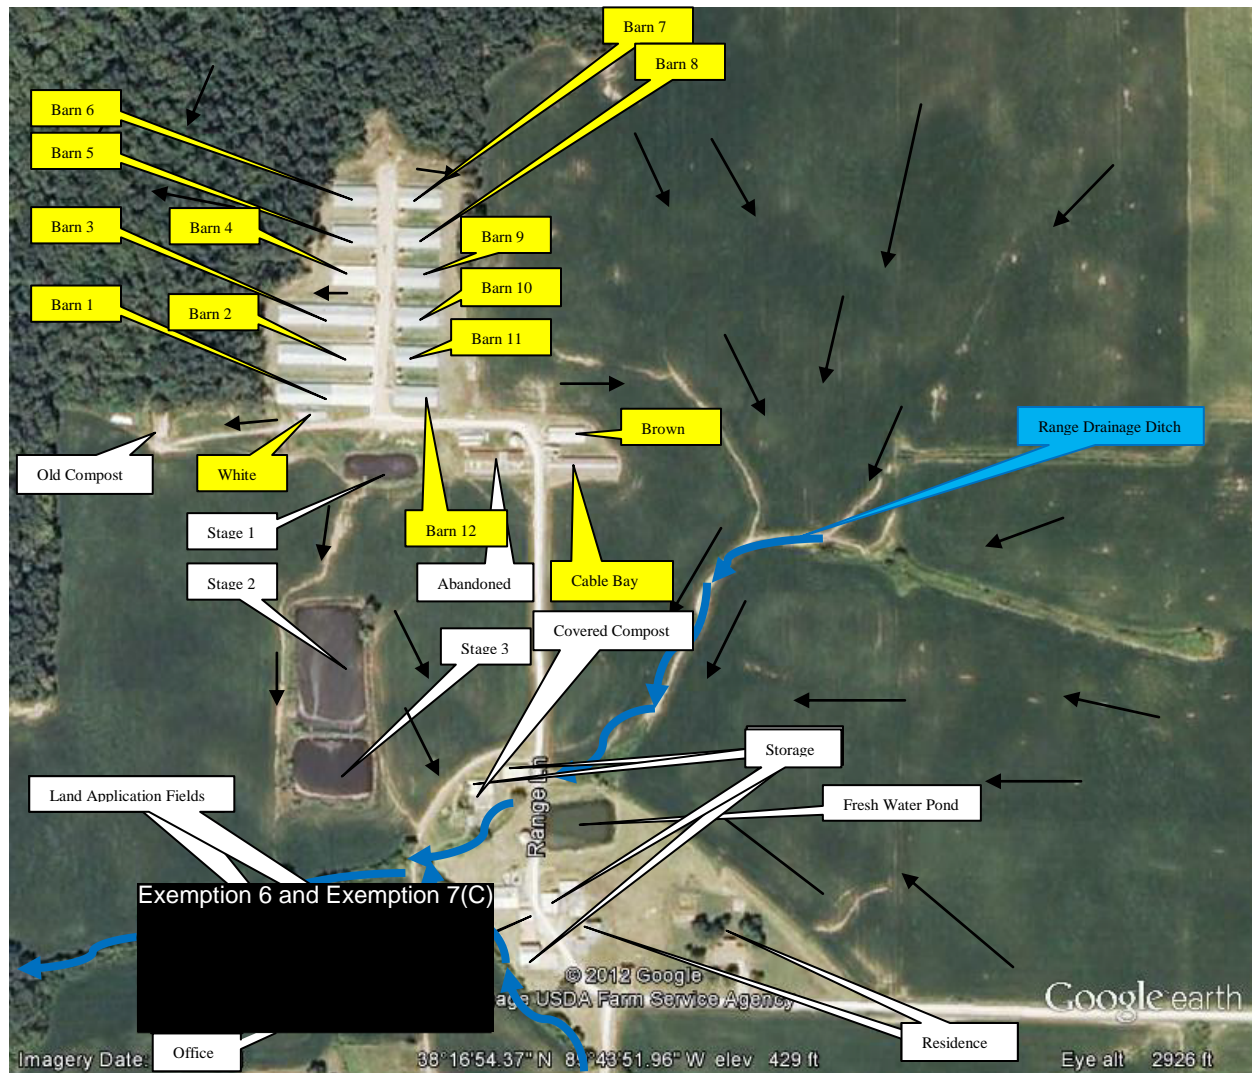

Black arrows show the direction of storm water drainage. Swine production barns are labeled as shown using yellow identifiers. All production barns have under floor deep pits ranging from 4 to 10 feet deep. The White, Brown, House, and Cable Bay production barns are pumped to stage 1 of the 3 stage lagoon system that gravity overflows from stage 1 to stage 2 then to stage 3. The old compost facility was discontinued and cleaned out after the final compost was finished out then land applied. Compost now occurs in the new covered composting operation identified above. Land application was ongoing from Barn 2 on the fields located west of the office, tilled, and appeared to be well incorporated. No discharge was occurring at the time of inspection.
