

**Plymouth-Whitemarsh High School
COLONIAL SCHOOL DISTRICT
SIX MONTH SURVEILLANCE
June 14, 2007**

The homogeneous areas listed below have been inspected in accordance with 40 CFR Part 763.92(b) and confirmed to be in the same condition as the previous surveillance date of May 21, 2005. Also listed below are any changes in homogeneous areas such as condition changes in ACM's and abatement. Any actions taken will have the supporting documentation attached.

Executive Summary

No major changes in ACM locations were observed in this school. Listed below are the abatement, repair and sampling completed in the school.

- 1) October 18, 2006 Visiting team locker room abatement.
- 2) March 26, 2007 Transite panel and miscellaneous debris abatement (CITV).

Additional bulk sampling: No additional bulk sampling was done.

All previously assumed materials including floor tiles and mastic under carpet, fire doors and vibration cloth remains as assumed material. These materials will be tested to confirm or dismiss asbestos content prior to handling or disturbing these materials.

Methods

In accordance with 40 CFR Part 763.92 (b) the "Periodic Surveillance" was conducted to include friable and non friable, known or assumed "previously identified ACM in Plymouth Whitemarsh High School.

The following actions were performed:

- 1) Visually re-inspect and re-assess the condition of all previously identified friable known or assumed ACM.
- 2) Identify any homogeneous areas with materials that have become friable since the last inspection.
- 3) Assess the condition of newly friable materials.
- 4) Record findings.
- 5) Make appropriate repairs and or removal.
- 6) Supply copies and review the finding to the Custodial Supervisors.

Restrictions

The scope of the inspection is limited to the visual inspection and assessment of previously identified ACM's in the original AHERA study, the inspections performed after the study and available construction blueprints. No destructive means was used to identify concealed assumed or suspect materials.

**Colonial School District
Plymouth-Whitemarsh High School
Six Month Periodic Surveillance**

Functional Space	Material Type/ Description	Sample	Estimated Quantity LF/SF/EA	Previously Assessed Condition	Current Assessed Condition	Priority/ Response Action
Facility lounge 1st floor, entrance near gym 20 and						
Weight room	9"x9" green marble floor tiles	PC	160 S/F	Good	Good	3/O&M
Slop sink closet near auditorium, music area, 1st floor copy rm						
	9"x9" blue marble floor tile	PC	520 S/F	Good	Good	3/O&M
Entire office end of East wing						
2nd floor, choral rm, Citv area	9"x9" beige marble floor tile	PC	320 S/F	Good	Good	3/O&M
Crawl space under original school Confined space in boiler room under auditorium pool area and pool locker room, office room area below plaster ceilings, laundry room, above ceilings on 1st, 2nd, 3rd floors East wing, Maintenance shop, end of hallway near room 50						
	Pipe Insulation	PC	12,000/15,000	Poor	Poor	1/O&M
Rooms 103,105,107, teacher rm,						
Lounge room	9"x9" beige spot floor tile/mastic	PC	3,900 S/F	Good	Good	3/O&M

Material Type = Misc. - Miscellaneous, Surf. - Surfacing, TSI - Thermal System Insulation

Sample = A - Assumed, C - Confirmed, PC - Previous Confirmed

Priority = 1 - Restrict Access, 2 - Abate ASAP, 3 - O&M

Response Action = R - Remove, E/R - Encapsulate/Repair, Encl. - Enclosure, O&M - Operations & Maintenance

**Colonial School District
Plymouth-Whitemarsh High School
Six Month Periodic Surveillance**

Functional Space	Material Type/ Description	Sample	Estimated Quantity LF/SF/EA	Previously Assessed Condition	Current Assessed Condition	Priority/ Response Action
Small storage room near side hallway exit of the Auditorium, Restroom below Auditorium	9"x9" red floor tile.	PC	310 S/F	Fair	Fair	3/O&M
Employees break room Café 7 or East. Entrance near gym 20 and weight room.	9"x9" dark green marble floor tiles	PC	275 S/F	Good	Good	3/O&M
Rooms 202, 206 through 210, Guidance office	9"x9" black floor tiles	PC	460 S/F	Fair	Fair	3/O&M
Room 44 and 50, boiler room office slop sink area near library	9"x9" black floor tiles	PC	200 S/F	Fair	Fair	3/O&M
Citv area, telephone room near auditorium, copy room 1st floor.	12"x12" white/black floor tile	PC	195 S/F	Good	Good	3/O&M
Rooms 202, 204, through 212, 214,215,301,302,304,306, 307 308 and 311A	9"x9" mint colored floor tile	PC	3200 S/F	Good	Good	3/O&M
Rooms 312,305,305c,38, library storage room closet room Closet in Room 45	9"x9" gray marble floor	PC	1800 S/F	Good	Good	3/O&M

Material Type = Misc. - Miscellaneous, Surf. - Surfacing, TSI - Thermal System Insulation

Sample = A - Assumed, C - Confirmed, PC - Previous Confirmed

Priority = 1 - Restrict Access, 2 - Abate ASAP, 3 - O&M

Response Action = R - Remove, E/R - Encapsulate/Repair, Encl. - Enclosure, O&M - Operations & Maintenance

**Colonial School District
Plymouth-Whitemarsh High School
Six Month Periodic Surveillance**

Functional Space	Material Type/ Description	Sample	Estimated Quantity LF/SF/EA	Previously Assessed Condition	Current Assessed Condition	Priority/ Response Action
Room in book storage closet near Cafeteria	Vertical tank insulation	A	150 S/F	Good	Good	3/O&M
Room in book storage closet near Cafeteria	Transite insulation	A	10 L/F	Good	Good	3/O&M
Rooms 300,301,301A,302,304 through 311,311A,313,314,316, 102 through 108,202,204 through 217, 2nd floor office area, entrance to Citv room, pool offices	Transite sheeting above Classroom and offices	A	500 S/F	Good	Good	3/O&M
Classrooms and office areas throughout the school	Assumed vinyl asbestos floor tile & mastic under carpet	A	69,300 S/F	Good	Good	3/O&M

Material Type = Misc. - Miscellaneous, Surf. - Surfacing, TSI - Thermal System Insulation

Sample = A - Assumed, C - Confirmed, PC - Previous Confirmed

Priority = 1 - Restrict Access, 2 - Abate ASAP, 3 - O&M

Response Action = R - Remove, E/R - Encapsulate/Repair, Encl. - Enclosure, O&M - Operations & Maintenance


Date of surveillance: 6/14/07

Inspector ID# 041681

Inspector: George J Donofry Jr

Signature: _____

George J Donofry Jr

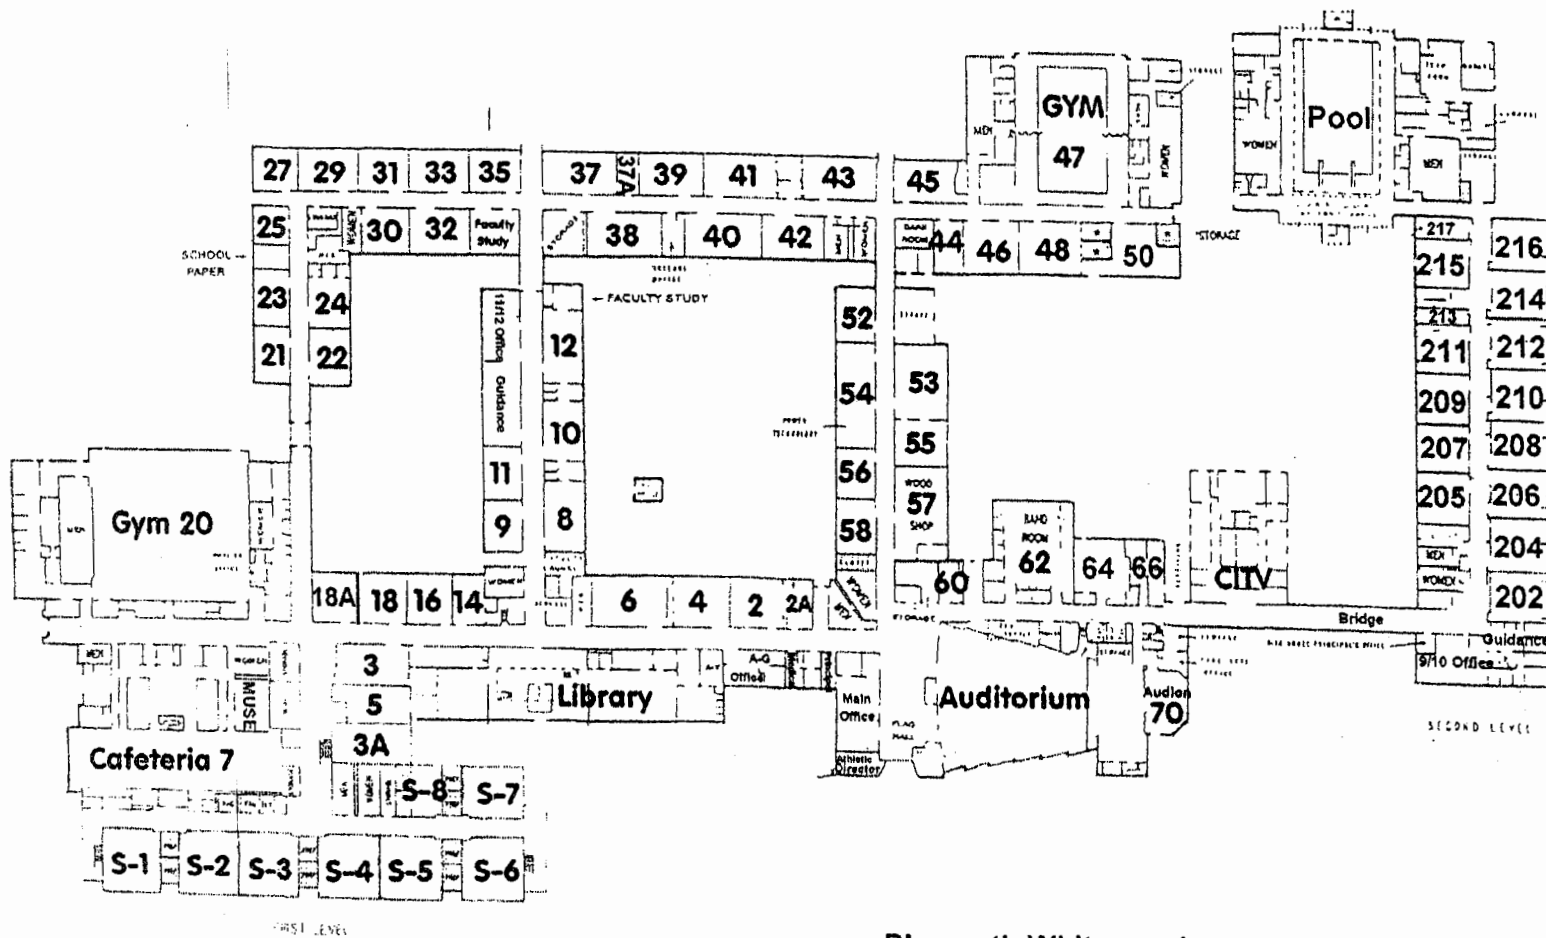

Plymouth Whitmarsh
High School

