

BAYONNE BARREL & DRUM**REPORT #** 33**O.S.C.** JOE COSENTINO
R.M. M.R.ELLIS**DATE:** 11/09/94

DESCRIPTION OF DELIVERY ORDER: Mobilize necessary personnel and equipment to facilitate removal action. Overpack, sample, haz-cat drummed waste on site, to include storage tanks above & below ground, pits, gutters, courtyard and ash/soil piles. Proceed with T & D of drummed waste, rubber, ash/soils and drums related to shredding operations. Further provide any additional support needed to assist with the site removal per the O.S.C.

LOCATION OF WORK: 150 RAYMOND BLVD. NEWARK, NJ 07105

WEATHER: Sunny, Partly Cloudy

TEMPERATURE: 65

WORK PERFORMED TODAY BY OHM:

- * Drum shredding operations today yield 366 drums plus the 10 from day previous= 376 total.
- * Constructed top for the bulking chamber, (holding tank).

SUBCONTRACTOR SERVICES PERFORMED:

- * Schiavone-Bonomo Corp. delivers a 20 yard roll off container for the shredded drums, Mike Cerreta (owner) visits job site to review the metal being placed inside the can. Discussions with him ensure that a roll off container to stand by for use may be possible.

EXCEPTIONS / UNUSUAL CONDITIONS:

- * Evaluation of the time spent to remove drums that clogged hopper, lunch, breaks and to move roll off forward equals approximately 123 min. or 2.05 hrs. (down). Starting time was 0845 hrs. completing the day at 1700 hrs. = 7hrs. & 45min. of operational time, subtract the 2.05 hrs. from this time as "down time", which now equait to 5 hrs. & 40 min. actual running time of the shredder in conclusion the average drums per hour run equals 68 drums/ hr.

CHANGE IN METHOD OR SCOPE, SPECIFIC DIRECTION RECEIVED FROM OSC:**DOCUMENTS SUBMITTED:****MEETINGS HELD, SUBJECT MATTER, DIRECTION AND OR DECISIONS:**


- * Conversations with WADCO's Representative Harold Saconik, regarding the de-heading operation of the acid pack drums. WADCO wishes to place his personnel on site to de-head the drums then remove. NOTE: Meeting is established for Monday 11/14/94 @ 0930 hrs. on site.

COMMENTS:

- * O.S.C. authorizes new start time of 0700 hrs. Crew further authorized to work until 1700 hrs. today incurring 9.5 hrs. total.



Drum Progress	Drums Shredded	Poly Liners Removed	Steel Removed
M 10/31		38	
T 11/01			
W 11/02		105	
T 11/03			
F 11/04		93	
M 11/07		57	
T 11/08	10	119	
W 11/09	366		8.08 ton
Total	376	412	8.08 ton

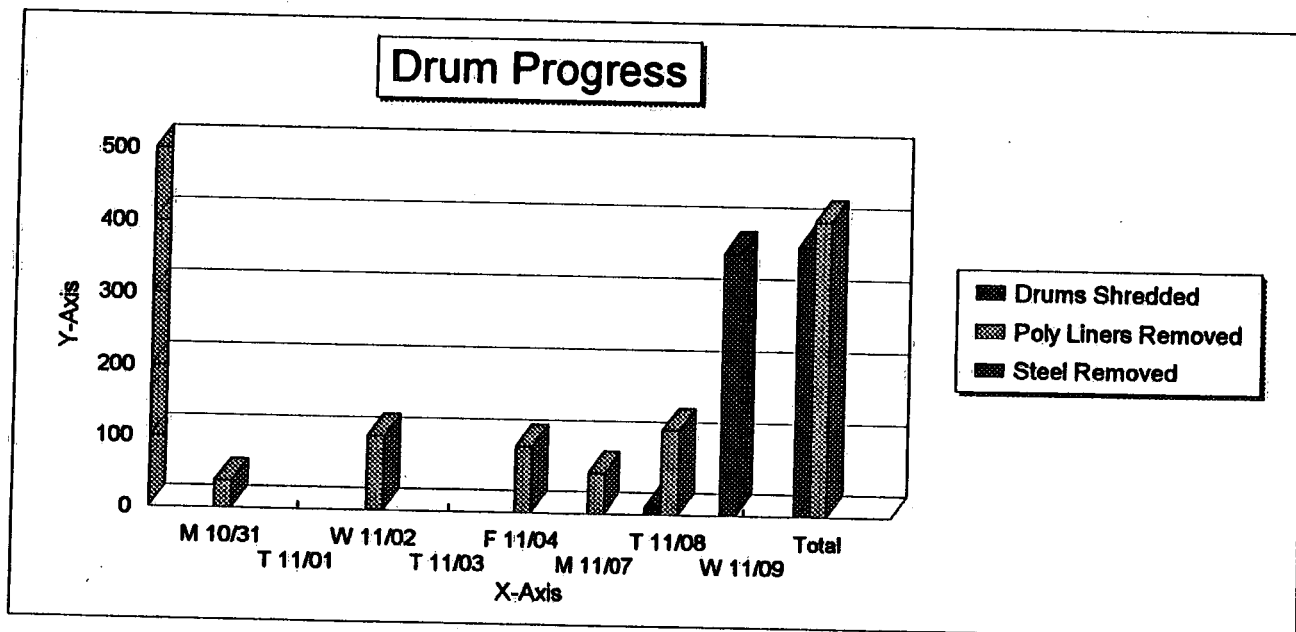

NOTE: The first roll off container weighed in at 18,100 lbs. Using 2,240 as a long ton calculation.
