

June 11, 2010

1300 CST

Water Quality Protection Division



Mississippi Canyon 252 Oil Spill, Gulf of Mexico Region 6 Update

Subject: **Water Quality Division Update # 30**
 Mississippi Canyon 252 Oil Spill, Gulf of Mexico

Date: June 11, 2010

Reporting Period: June 10, 2010 1300 – June 11, 2010 1300

Forecast

- The nearshore oil forecast created by NOAA on 6/10/10 at 2100 CDT for 6/11/10 at 1200 CDT (Figure 1) indicates that the main part of the oil slick will be east-southeast of Louisiana with portions stretching west of Southwest Pass. Persistent onshore winds out of the south/southeast are forecast to remain throughout the weekend which will continue to push the oil slick northward Mississippi, Alabama and the Florida Panhandle. The persistent southeasterly winds are also pushing the oil slick towards the Chandeleur Islands, Breton Sound and the Delta. Shoreline impacts may occur in these areas.
- The offshore oil forecast created by NOAA on 6/10/10 at 1900 CDT for 6/11/10 at 1200 CDT (Figure 2). An oily sheen still remains in an eddy on the northern edge of the Loop Current but some is moving southerly along the eastern edge of this eddy and some may become entrained in an eddy northeast of the Loop Current. NOAA overflights observed patchy sheens 45 nm south-southeast of the source.

Monitoring and Assessment

- Continuing to coordinate with the REOC Environmental Unit on the review of incoming water and sediment quality monitoring data, including results from water samples analyzed for dispersants and sediment toxicity testing results.
- Attending regular meetings and calls with Region 4, HQ, & REOC.

Drinking Water

- Drinking water intakes, public drinking water wells, and domestic wells have not been impacted by the oil sheen and are not projected to be impacted.
- EPA Region 6 is providing the Louisiana Department of Health and Hospitals (LDHH) daily situation report as well as data summaries as they become available.
- EPA Region 6 continues to coordinate closely with the LDHH on all drinking water issues.

Data Management – Mapping Efforts

- Updated the Shoreline Coastal Assessment Team (SCAT) and spill trajectory data.

NPDES

- No changes since 6/10/2010.
- NPDES Permits and TMDL Branch continues to be available to provide technical assistance as needed.

Coastal Programs

Louisiana Large-Scale Coastal Barrier Plan:

- Ongoing coordination on the monitoring plan for the six approved sections authorized by the New Orleans Corps District (NOD-20) MVN 2010-1066-ETT. The basic plan includes requirements relating to berm performance; surveys of borrow sites, stockpiles, and berms; daily production rates; sediment contaminant testing; and surveys of nesting birds. Initial comments were delivered to the Corps on June 9, 2010.
- Coastal staff coordinated with OW and provided guidance to the berm contractor (Shaw Group, Inc.) regarding the application of CWA Section 404 to the dredged material stockpile areas for the berm construction. The area in question relates to dredged material that will be transported either by scow or hopper dredge from the Passe a Loutre borrow site to the re-handling area and then piped to the berm sites near Pelican Island. A CWA Section 404 emergency permit for the project has been obtained by the State of Louisiana and the contractor was advised to contact the Corps to determine whether this activity is covered under that authorization.

Corps Emergency Authorizations for Coastal Protection Features:

- Coordination is ongoing with the Corps, OW, and Region 4 on a continuing series of emergency authorization requests for incremental work to install booms, sand bags, tiger dams, concrete blocks, and similar structures in the Chandeleur Sound, Barataria Bay, Terrebonne Bay, and adjoining waterways.

OW Ecological Impact Analyses:

- Follow up discussions are underway regarding the marsh protection and marsh remediation alternatives and techniques.
- Ongoing coordination, through OW, with the Association of National Estuary Programs and NEP Directors regarding baseline characterization data, habitat and restoration priorities, and a request to OWOW to provide a bridge between the NRDA process and the NEPs.

Corps Navigation Maintenance Dredging:

- Continued coordination between OW, Region 4, and Region 6 regarding dredged material and ocean dumping sites potentially impacted by the oil spill.
- Shoaling and flocculation are being reported in SW Pass and three hopper dredges are working in the pass. The Corps is considering redirecting two of these dredges to work on the sand berm project.

- The Corps is employing oil detection kits on the dredges, a technique coordinated with EPA and Corps research facilities during the 2008 Mississippi River oil spill. In addition, new ship decontamination sites have been established in the lower Mississippi River and Southwest Pass which may be within the area of influence of the EPA-designated ocean disposal site.
- Discussions are underway regarding marsh remediation efforts and initial agency coordination is occurring regarding monitoring the long-term landscape-scale coastal habitat impacts.

Coastal Wetlands Planning, Protection and Restoration Act (CWPPRA)

- Based upon the shoreline impact assessment map (Figure 3) and the EPA OSC shoreline cleanup efforts (Table 1), there have been no changes to the list of CWPPRA projects in the vicinity of oil impacted areas since 6/10/10.

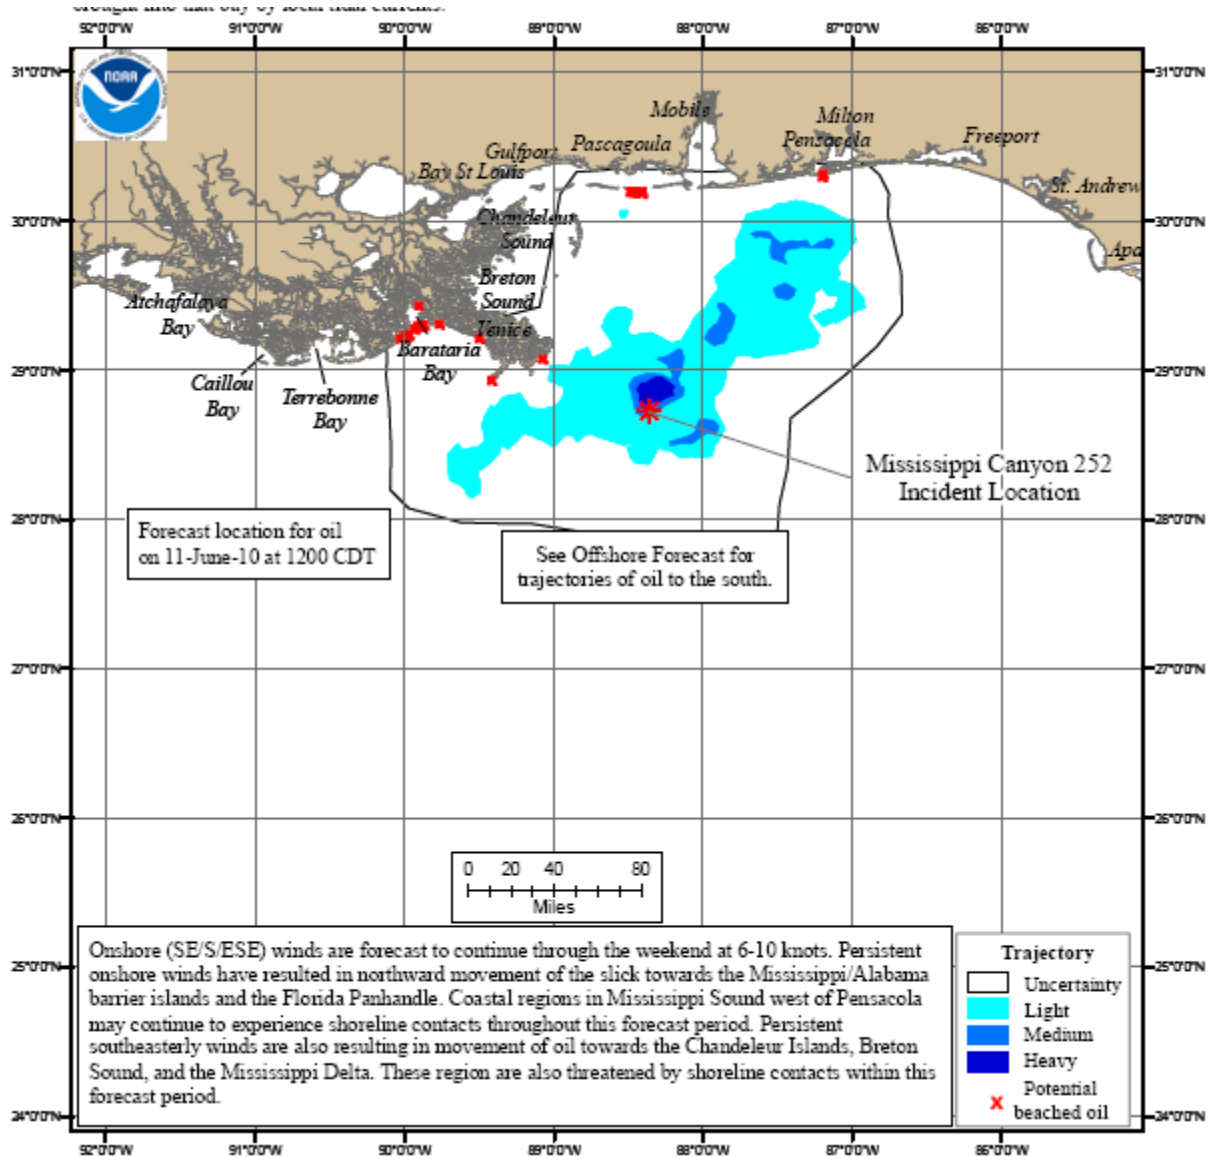


Figure 1 NOAA nearshore oil slick trajectory forecast for 6/11/10.

<http://www.deepwaterhorizonresponse.com/go/doctype/2931/53979/>

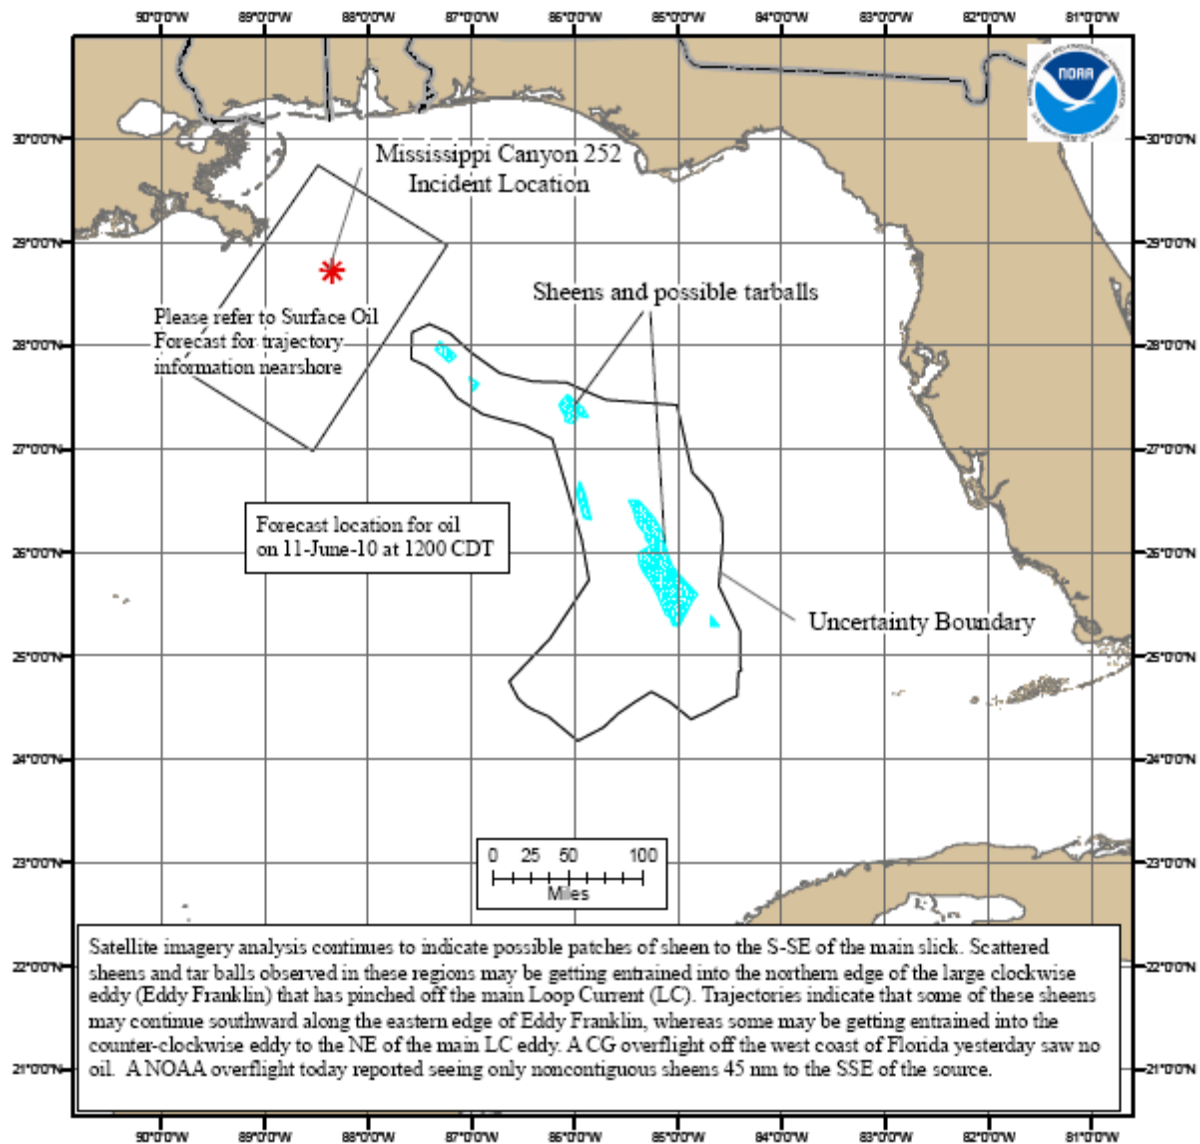


Figure 2 NOAA offshore oil slick trajectory forecast for 6/11/10.
<http://www.deepwaterhorizonresponse.com/go/doctype/2931/53979/>

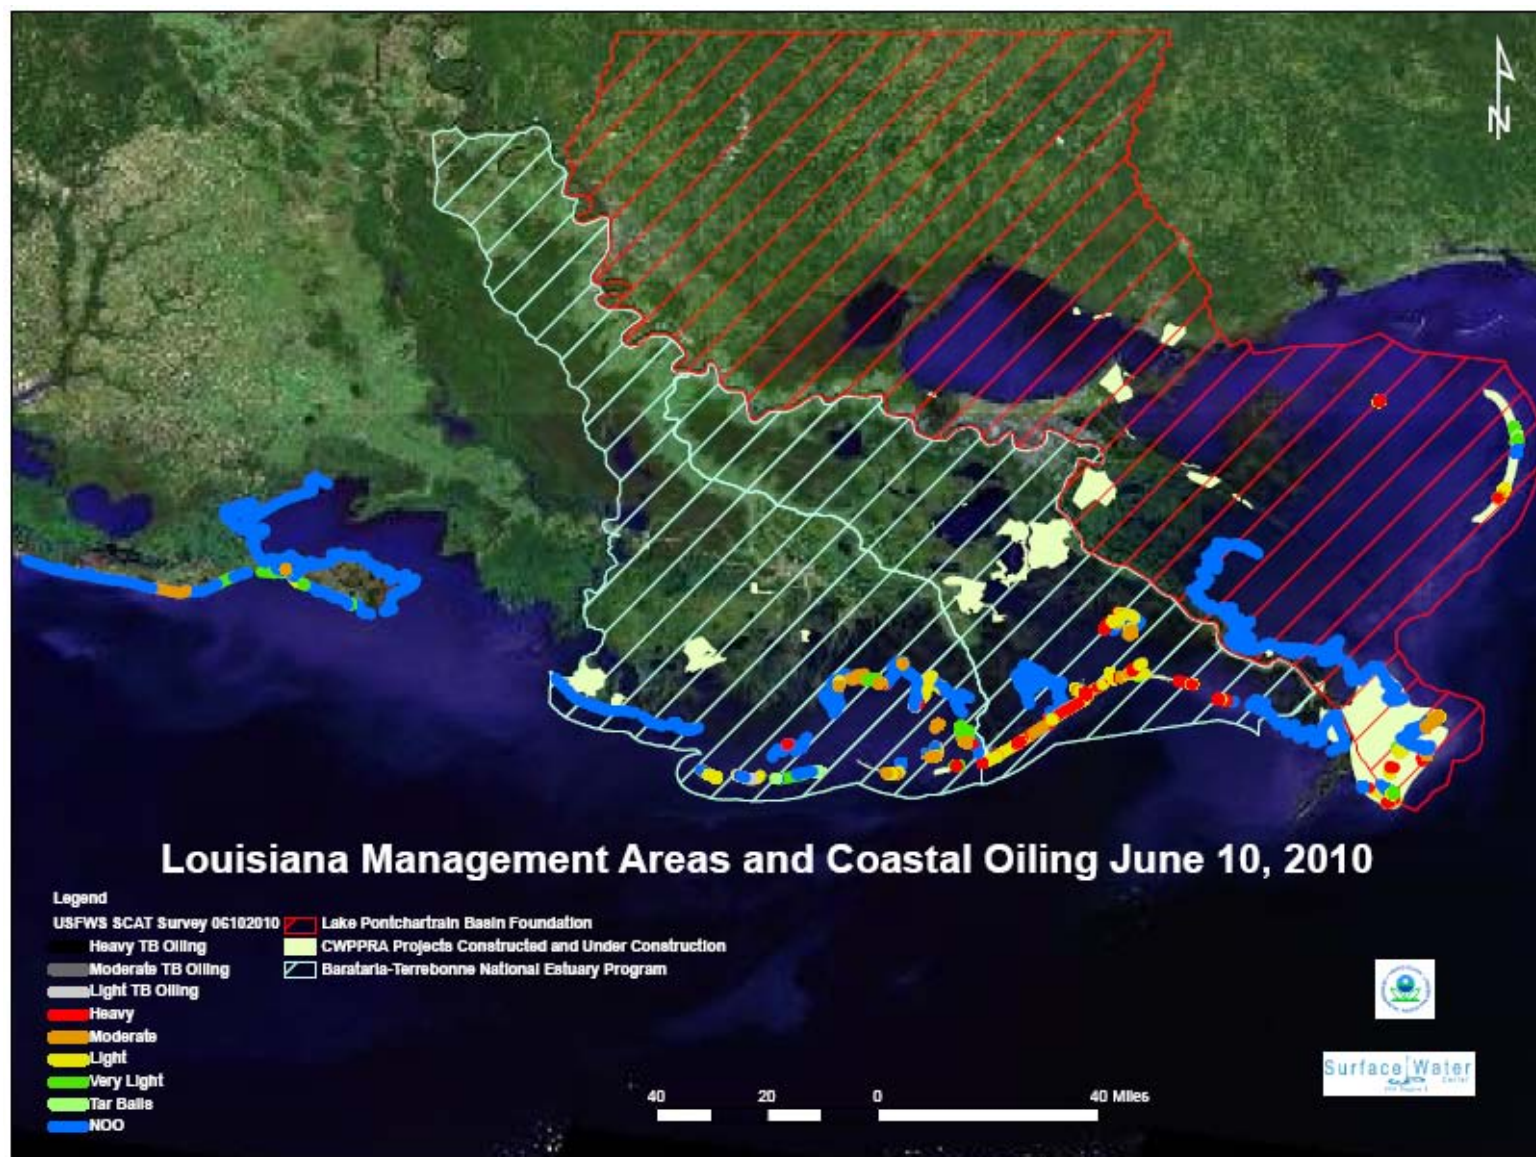


Figure 3 Oil impact assessment map including Barataria Terrebonne National Estuary Program, Lake Pontchartrain Basin Foundation boundaries, constructed CWPPRA projects and reported oiled shorelines.

June 11, 2010

Shoreline Impact Areas	Stage	Parish	Miles Impacted	Progress
Southpass Inner Sandbar	Venice	Plaquemines	2.78	80% complete
Pilot Bayou/Johnson Pass	Venice	Plaquemines	1.5	using containment boom
Pass a L'outre/Red Fish Bay	Venice	Plaquemines	4	70% complete
Inner Area Southpass	Venice	Plaquemines	1.49	TBD
Chandeleur Island	Hopedale	St. Bernard	7.2	100% complete
Grand Isle/Elmer's Island	Grand Isle	Jefferson	7.6	Re-Oiling; ongoing
Isle Grande Terre	Grand Isle	Plaquemines	1.77	TBD
Brush Island	Hopedale	St. Bernard	1.33	100% complete
Lake Raccourci	Fourchon	LaFourche	0.8	TBD
Chenier Au Tigre	St. Mary	Vermillion	0.7	100% complete
Trinity Island	Cocodrie	Terrebonne	0.48	100 % complete
Fourchon Beach	Fourchon	LaFourche	3.75	90% complete
Timbalier Bay	Fourchon	LaFourche	0.43	TBD
Lake Felicity	Cocodrie	Terrebonne	1	Ongoing
Marsh Island	St. Mary	Iberia	0.4	100% complete
Marsh Island	St. Mary	Iberia	0.2	100% complete
Cheniere Ronquille	Grand Isle	Plaquemines	0.2485	TBD
Spartina Marsh	Grand Isle	Jefferson	0.2	TBD

Table 1 Deepwater Horizon shoreline impacts and status of cleanup. Information provided by EPA OSC web page. Created on 6/10/10 at 1300 CST
