


# Smoke and Dye Testing Summary

## High Level Sewershed

### Run Summary

Test ID	Test Type	Date Inspected	Company / Super.	Blower MH	Ground Condition	Notification Made?	Total Length
S1028-131	Smoke	10/21/2008	ADS/TM	S13II_047MH	Dry	Yes	724.92

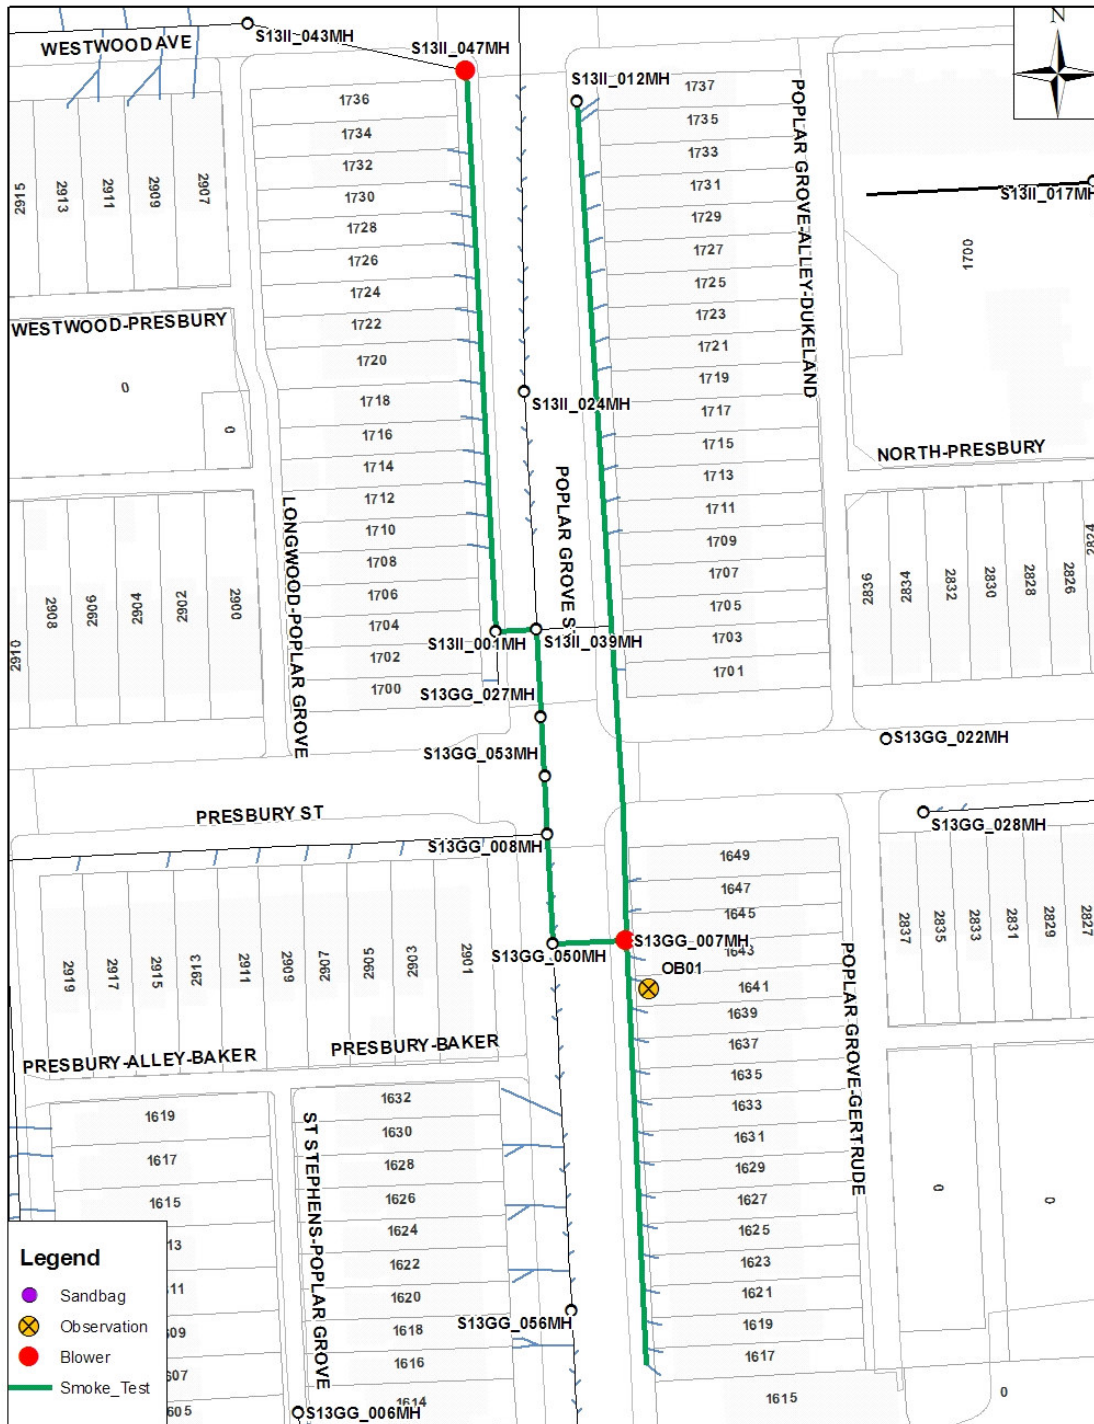

---

# Smoke and Dye Testing Summary

---

## High Level Sewershed

### Run Summary

Test ID	Test Type	Date Inspected	Company / Super.	Blower MH	Ground Condition	Notification Made?	Total Length
S1028-131	Smoke	10/21/2008	ADS/TM	S13II_047MH	Dry	Yes	724.92

### Isolated Pipes

Pipe ID	Upstream MH	Downstream MH	Length (ft)	Diameter (In)
S13II_008G1	S13II_008MH	S13II_024MH	174.6954	12
S13II_012G1	S13II_012MH	S13GG_031MH	312.7562	8
S13GG_007G1	S13GG_007MH	S13GG_050MH	32.22124	8
S13GG_064G1	S13GG_064DE	S13GG_007MH	187.2724	8
S13II_001G1	S13II_001MH	S13II_039MH	17.9745	8

### Observations & Photos

**Obs\_ID** S1028-131-OB01

**Address** 1641 Poplar Grove St

**Status** Private

**Source** Service Lateral

**Location** Paved concrete

**Nearest MH** S13GG\_007MH

**Comments** Smoke from service lateral underneath concrete stairs. 1641 Poplar Grove St.



**Picture** \S1028-131-OB01-P01.jpg

**Comments** Front of house, 1641 Poplar Grove St.
