


Smoke and Dye Testing Summary

High Level Sewershed

Run Summary

Test ID	Test Type	Date Inspected	Company / Super.	Blower MH	Ground Condition	Notification Made?	Total Length
S1028-226	Smoke	8/11/2009	ADS/TM	S19MM_011MH	Dry	Yes	762.36

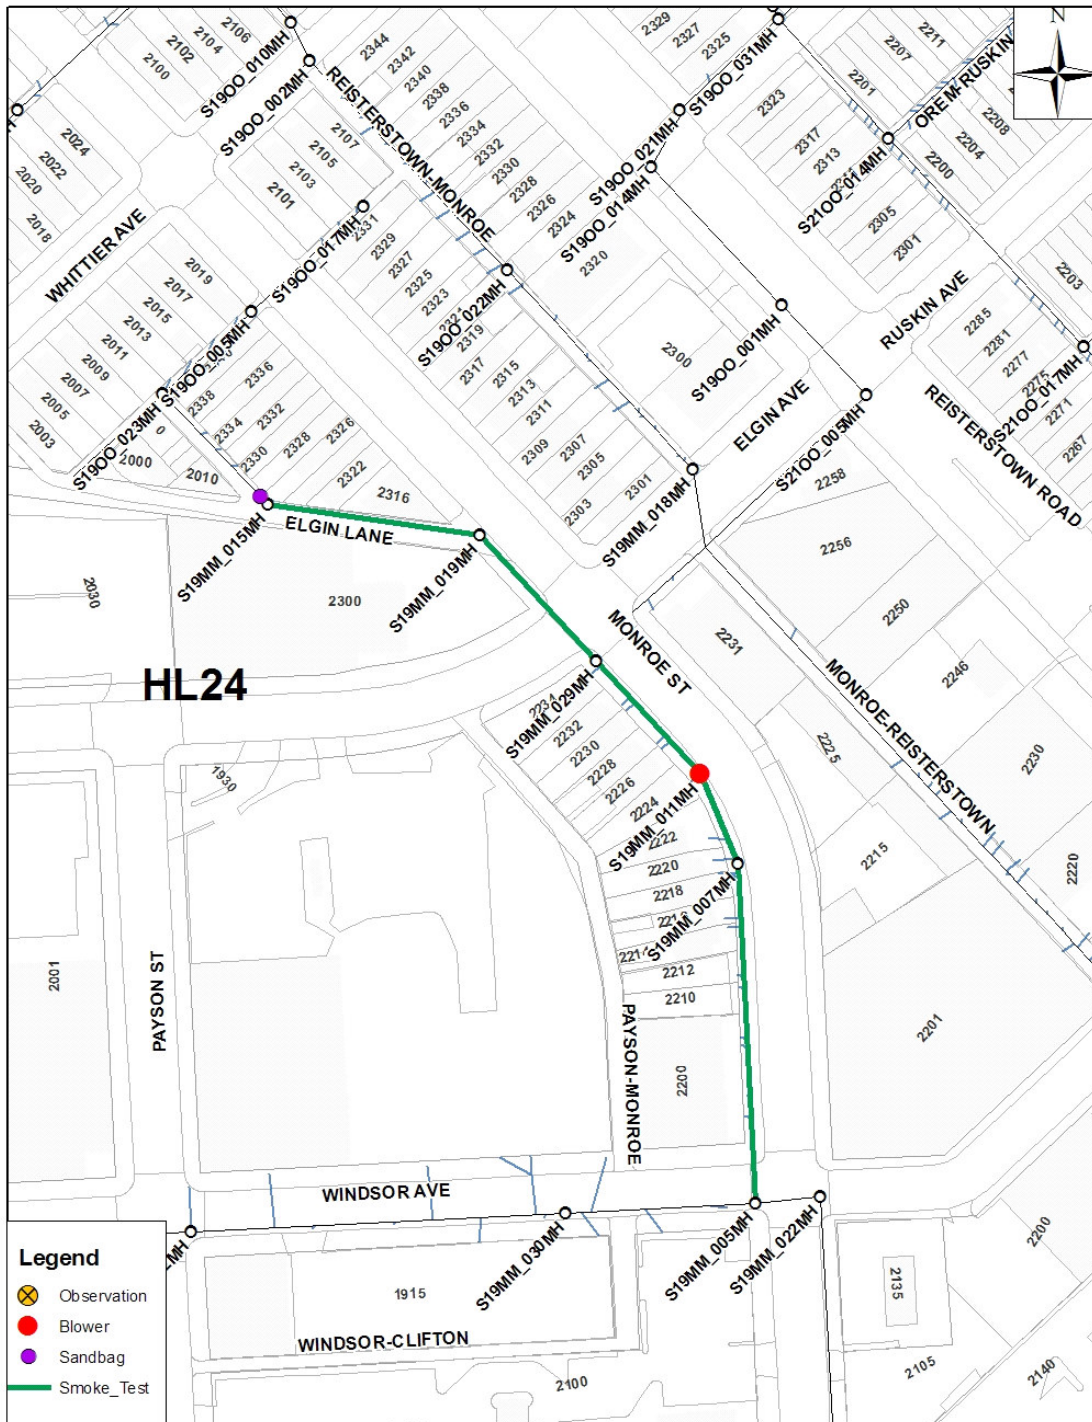

Smoke and Dye Testing Summary

High Level Sewershed

Run Summary

Test ID	Test Type	Date Inspected	Company / Super.	Blower MH	Ground Condition	Notification Made?	Total Length
S1028-226	Smoke	8/11/2009	ADS/TM	S19MM_011MH	Dry	Yes	762.36

Isolated Pipes

Pipe ID	Upstream MH	Downstream MH	Length (ft)	Diameter (In)
S19MM_015G1	S19MM_015MH	S19MM_019MH	166.738	8
S19MM_019G1	S19MM_019MH	S19MM_029MH	133.599	8
S19MM_011G1	S19MM_011MH	S19MM_007MH	75.6021	8
S19MM_007G1	S19MM_007MH	S19MM_005MH	265.998	8
S19MM_029G1	S19MM_029MH	S19MM_011MH	120.424	8

Observations & Photos

