

# Manhole Inspection Summary

Manhole # S19KK\_045MH

Printed On: 6/30/2009

Page 1 of 4

**Inspection** ☐ Is Incomplete Rating: **3) Fair**

Record Plat: **19KK** Node: **045** Status: **Found**

Insp Date: **6/5/07 7:46 AM**

Incomplete Comments

Crew: **ADS4**  
Inspector: **ADS4**  
Firm: **HQ**

**Location** Address: **2014 CLIFTON AVE**

Cross Street: **PAYSON ST**

**Manhole** Type: **Junction**

Location: **Sidewalk**

Ground Conditions: **Dry**

☐ Prev. Rehab

Weather: **Dry**

Subject To Ponding: **None**

Comments

**Cover**

Shape: **Circular**

Diameter: **24** (in.) Length: (in.) Dist A/B Grade: **0** (in.)

Type: **Sanitary**

Condition: **Sound**

Cover Material: **Cast Iron**

Properties: ☐ Bolted ☐ Vented ☐ Water Tight ☐ Water Tight Insert

**Frame**

Offset: **1** (in.)

Condition: ☒ Sound ☐ Cracked ☐ Leaks

**Chimney / Frame Adjustment**

☒ Exists Material: **Brick**

☐ Parged Height: **3** (in.)

Condition: ☐ Sound ☐ Cracked ☐ Root Intrusion ☐ Loose Brick ☒ **Deteriorated**

Infiltration: ☒ None ☐ Joint ☐ Cracks ☐ Mortar ☐ Roots ☐ Wall

**Corbel**

Material: **Brick**

☐ Parged

Type: **Concentric/Eccentric**

Condition: ☒ Sound ☐ Cracked ☐ Root Intrusion ☐ Loose Brick ☐ Deteriorated

Infiltration: ☒ None ☐ Joint ☐ Cracks ☐ Mortar ☐ Roots ☐ Wall

**Barrel**

Material: **Brick**

☐ Parged

Shape: **Circular**

Diameter: **46** (in.) Length: (in.)

Condition: ☒ Sound ☐ Cracked ☐ Root Intrusion ☐ Loose Brick ☐ Deteriorated

Infiltration: ☒ None ☐ Joint ☐ Cracks ☐ Mortar ☐ Roots ☐ Wall

**Bench**

☒ Exists Material: **Brick**

☐ Parged

Condition: ☒ Sound ☐ Cracked ☐ Root Intrusion ☐ Deteriorated ☐ Leaks ☐ Debris

**Channel**

Material: **Brick**

☐ Parged

Channel Exposure: **Fully Open** Junc Dist: **0** nearest .5 ft. Azimuth:

Condition: ☒ Sound ☐ Cracked ☐ Root Intrusion ☐ Deteriorated ☐ Leaks ☐ Debris

**Steps**

Count: **2** Missing: **3** ☒ **Corroded**

**Surcharge**

☐ Evidence Of Surcharge Depth: (ft.) ☐ Active Surcharge Present

# Manhole Inspection Summary

Manhole # S19KK\_045MH


Printed On: 6/30/2009

Page 2 of 4

Location View



Top View

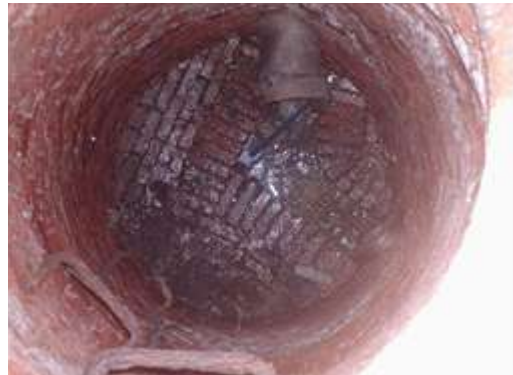

Defect 3



DETERIORATION OF CHIMNEY

Defect 2



CORRODED STEPS AND MISSING

Defect 1



FRAME OFFSET

## Manhole Inspection Summary

Manhole # S19KK\_045MH

Printed On: 6/30/2009

Page 3 of 4

8 in. Circular Gravity Sewer  
Pipe Out @ 12 O'Clock

12 O'Clock Outflow



Pipe Height: **7.2** (in.) Rod and Bar (Angled)  
Pipe Material: **Clay** ☐ Pipe Lined  
Invert Depth: **8.61** (ft.) Flow Characteristics: **Slow**  
Deposits: ☐ None ☐ Mud ☐ Sludge ☒ **Debris** ☐ Grease  
Silt Depth: **3** (in.) Deposits Extent: **Medium**  
Infiltration: **None** Pipe Seal Cond: **Sound**

Drop: **None**

Connects To: **Manhole**

☐ Possible Illicit Connection

8 in. Circular Gravity Sewer  
Pipe In @ 12 O'Clock

12 O'Clock Inflow



Pipe Height: **8.4** (in.) Rod and Bar (Angled)  
Pipe Material: **DIP/CI** ☐ Pipe Lined  
Invert Depth: **6.92** (ft.) Flow Characteristics: **None**  
Deposits: ☐ None ☐ Mud ☐ Sludge ☒ **Debris** ☐ Grease  
Silt Depth: **1** (in.) Deposits Extent: **Light**  
Infiltration: **None** Pipe Seal Cond: **Broken**

Drop: **None**

Connects To: **Connecting Node Not Available**

☐ Possible Illicit Connection

# Manhole Inspection Summary

Manhole # S19KK\_045MH

Printed On: 6/30/2009

Page 4 of 4

8 in. Circular Gravity Sewer

4 O'Clock Inflow

Pipe In @ 4 O'Clock

Drop In @ 4 O'Clock



Pipe Height: **7.2** (in.) Rod and Bar (Angled)

Pipe Material: **Clay** ☐ Pipe Lined

Invert Depth: **6.74** (ft.) Flow Characteristics: **Slow**

Deposits: ☒ None ☐ Mud ☐ Sludge ☐ Debris ☐ Grease

Silt Depth: (in.) Deposits Extent:

Infiltration: **None** Pipe Seal Cond: **Sound**

Drop: **Outside** Rod and Bar

Angled: **Yes** Reading: **7.52** (ft.)

Inv Depth: **8.52** (ft.)

Drop Condition: **Partly Clogged**

Connects To: **Manhole**

☐ Possible Illicit Connection
