


Process Flow, Weston PCB Collection

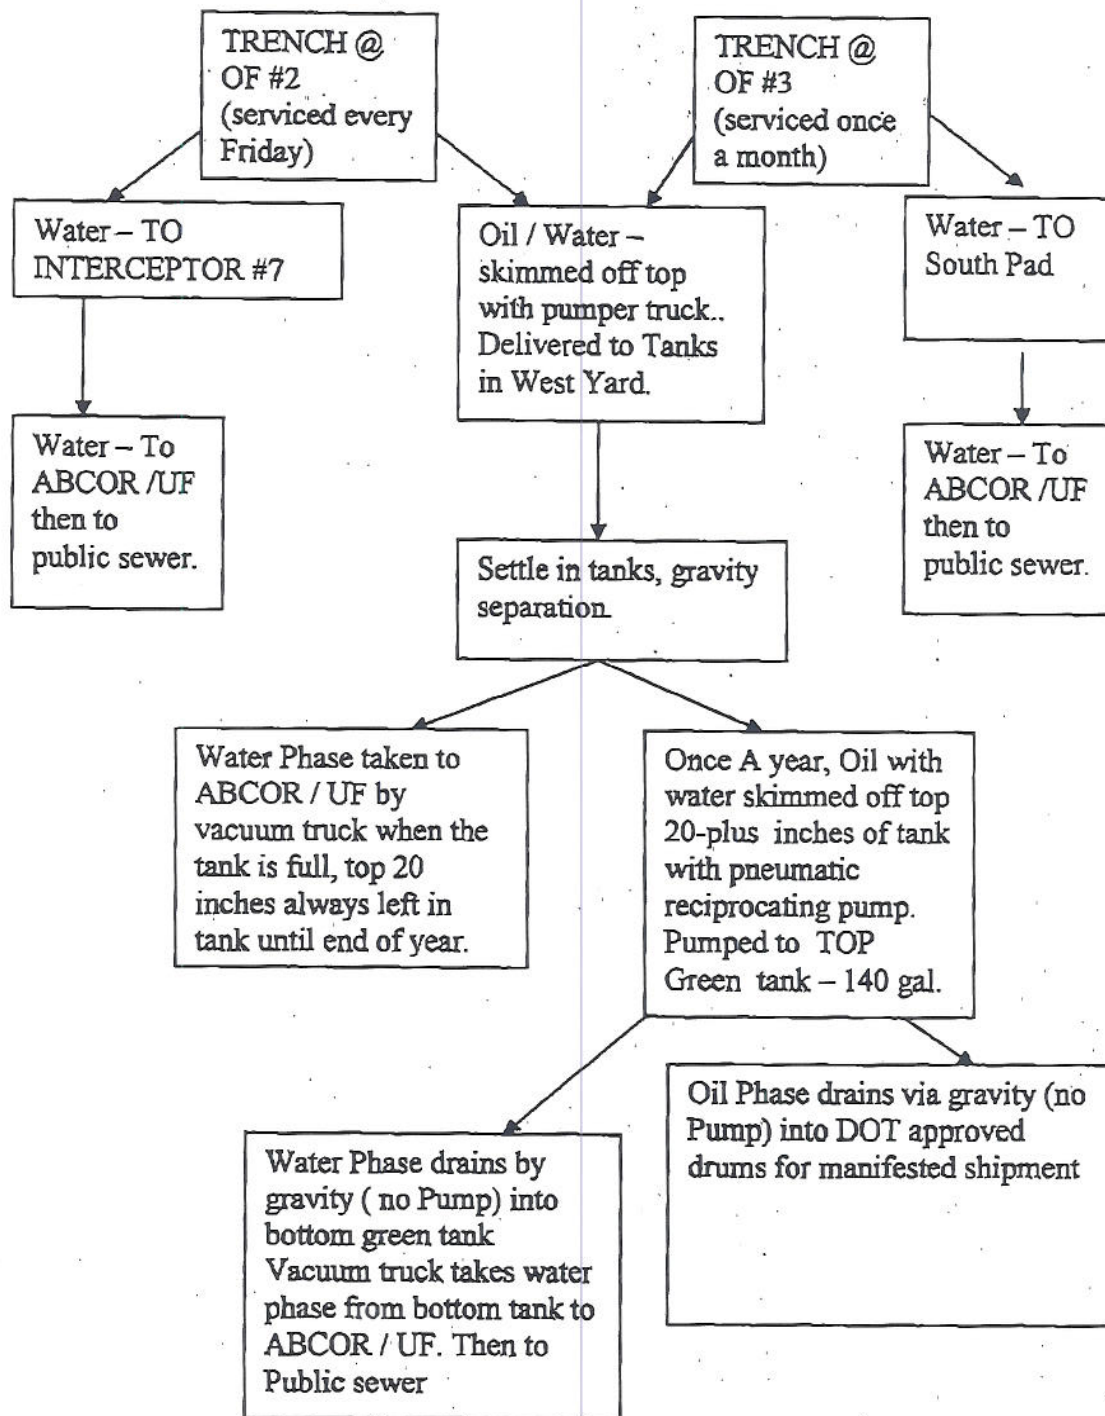

First Four Shipments

Avg. PCB 347*

Avg. Gallons Per Month 22.5**

Last Four Shipments

267.7 Drop of 79.3

12.5 Drop of 10

Avg. Months Per Shipment 6.3**

11.5 Increase of 5.2

*Second month missing; average of three months

**First month missing; average of three months

X1854

PCB Disposal System, Weston Sumps
1991 - 2001


September 28, 2001

<u>Start Date</u>	<u>PCB PPM</u>	<u>Ship Date</u>	<u># Of Barrels</u>	<u>Months of Shipping Cycle</u>	<u>Gallons Per Month</u>
Jul-91	430	Apr-92	3		
Apr-92		Oct-92	3	6	25.0
Sep-92	205	Jun-93	2	8	12.5
May-93	406	Nov-93	3	5	30.0
Oct-93	170	Jul-94	2	8	12.5
Jun-94	253	Jan-95	2	7	14.3
Dec-94	295	Nov-95	2	10	10.0
Oct-95	252	Jul-96	3	8	18.8
Jun-96	210	Nov-96	3	4	37.5
Oct-96	145	Aug-97	3	10	15.0
Jul-97	285	Dec-97	2	4	25.0
Nov-97	208	Aug-98	3	8	18.8
Aug-98	280	Aug-99	3	12	12.5
Jun-99	353	Oct-00	3	14	10.7
Sep-00	230	Sep-01	2	12	8.3
Aug-01					

Last off site shipment 9/21/01

To: Marianne
milette
4 pages

Photo below shows the reciprocating pneumatic pump on top of the highest tank.

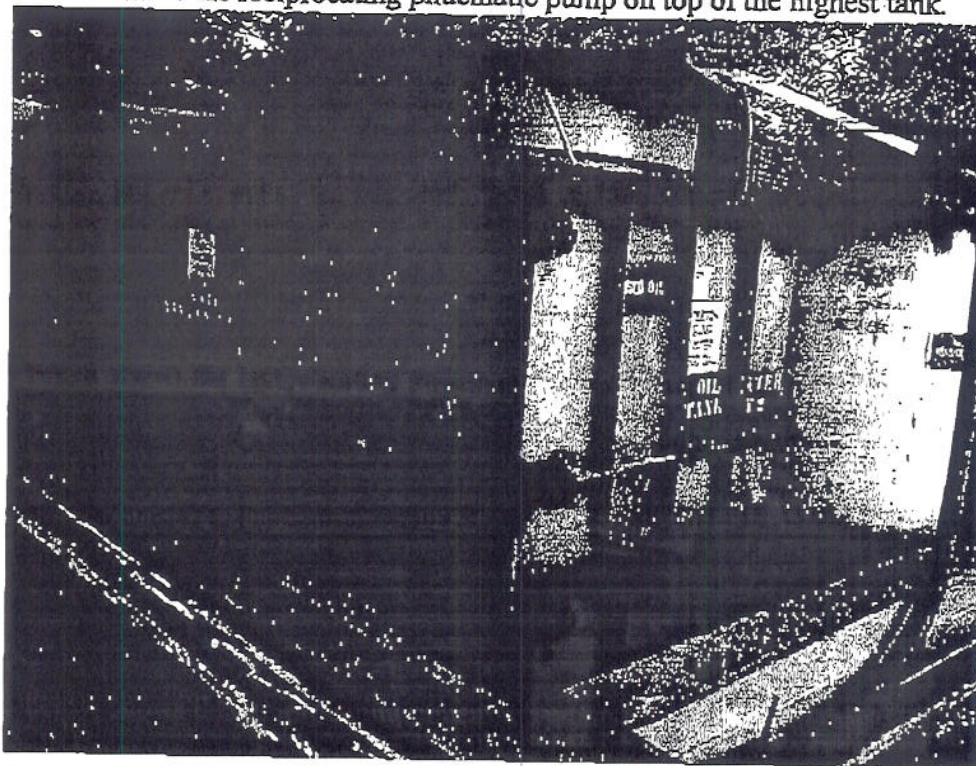

The Photo below is another view showing the pneumatic reciprocating pump at the top of the tallest tank. To operate the pump, the operator runs an air hose from the building out to the pump.

