


1241215 - R8 SDMS



Third West Air Monitor Result
Shepherd, Michael

to:

Joyce Ackerman, 'Craig Barnitz (cbarnitz@utah.gov)'

06/15/2012 10:38 AM

Hide Details

From: "Shepherd, Michael" <Michael.Shepherd@rockymountainpower.net>

To: Joyce Ackerman/R8/USEPA/US@EPA, "'Craig Barnitz (cbarnitz@utah.gov)'"
<cbarnitz@utah.gov>

1 Attachment



237906-1.pdf

Joyce & Craig,

We had two positive hits on Tuesday, June 12, 2012. Both were chrysotile, see the attached. Please let me know if you have any questions or concerns.

Thanks,

Mike Shepherd
Project Manager
Rocky Mountain Power - Major Projects
801.220.4584 Office
801.631.1310 Cell
801.220.2797 Fax
michael.shepherd@pacificorp.com



June 14, 2012

Laboratory Code: RES
Subcontract Number: NA
Laboratory Report: RES 237906-1
Project # / P.O. #: None Given
Project Description: 3rd West Sub - RMP

Eldon Romney
R & R Environmental
47 West 9000 South #2
Sandy UT 84070

Dear Customer,

Reservoirs Environmental, Inc. is an analytical laboratory accredited for the analysis of Industrial Hygiene and Environmental matrices by the National Voluntary Laboratory Accreditation Program (NVLAP), Lab Code 101896-0 for Transmission Electron Microscopy (TEM) and Polarized Light Microscopy (PLM) analysis and the American Industrial Hygiene Association (AIHA), Lab ID 101533 - Accreditation Certificate #480 for Phase Contrast Microscopy (PCM) analysis. This laboratory is currently proficient in both Proficiency Testing and PAT programs respectively.

Reservoirs Environmental, Inc. has analyzed the following samples for asbestos content as per your request. The analysis has been completed in general accordance with the appropriate methodology as stated in the attached analysis table. The results have been submitted to your office.

RES 237906-1 is the job number assigned to this study. This report is considered highly confidential and the sole property of the customer. Reservoirs Environmental, Inc. will not discuss any part of this study with personnel other than those of the client. The results described in this report only apply to the samples analyzed. This report must not be used to claim endorsement of products or analytical results by NVLAP or any agency of the U.S. Government. This report shall not be reproduced except in full, without written approval from Reservoirs Environmental, Inc. Samples will be disposed of after sixty days unless longer storage is requested. If you have any questions about this report, please feel free to call 303-964-1986.

Sincerely,

A handwritten signature in cursive script, appearing to read "Jeanne Spencer", is written over a horizontal line.

Jeanne Spencer
President

RESERVOIRS ENVIRONMENTAL, INC.

NVLAP Lab Code 101896-0; TDH: #30-0016

TABLE I. TEM AIR FILTER SAMPLE DATA AND ANALYTICAL RESULTS

RES Job Number: RES 237906-1
Client: R & R Environmental
Client Project Number / P.O.: None Given
Client Project Description: 3rd West Sub - RMP
Date Samples Received: June 13, 2012
Analysis Type: TEM, AHERA
Turnaround: 24 Hour
Date Samples Analyzed: June 13, 2012

Client ID Number	Lab ID Number	Area Analyzed	Air Volume Sampled	Number of Asbestos Structures Detected	Analytical Sensitivity	Asbestos Concentration	Filter Loading
		(mm ²)	(L)		(s/cc)	(s/cc)	(s/mm ²)
3W-061212 W	EM 886246	0.0800	969	ND	0.0050	BAS	BAS
3W-061212 N	EM 886247	0.0900	959	2	0.0045	0.0089	22.2
3W-061212 E	EM 886248	0.0900	955	ND	0.0045	BAS	BAS
3W-061212 S	EM 886249	0.0900	949	ND	0.0045	BAS	BAS

NA = Not Analyzed
ND = None Detected
BAS = Below Analytical Sensitivity
Average Grid Opening in mm² = 0.010

Filter Material = Mixed Cellulose Ester
Filter Diameter = 25 mm
Effective Filter Area = 385 sq mm

ll
Digitally signed by
Linda L. Lippert
DN: cn=Linda
Lippert, c=US
o=Reservoirs
Environmental, Inc.
Date: 2012.06.13
14:29:12 -0500

DATA QA

RESERVOIRS ENVIRONMENTAL, INC.
NVLAP Lab Code 101896-0; TDH: #30-0015

TABLE II. SUMMARY OF ANALYTICAL DATA

RES Job Number: RES 237906-1
Client: R & R Environmental
Client Project Number / P.O.: None Given
Client Project Description: 3rd West Sub - RMP
Date Samples Received: June 13, 2012
Analysis Type: TEM, AHERA
Turnaround: 24 Hour
Date Samples Analyzed: June 13, 2012

Client ID Number	Lab ID Number	Asbestos Mineral	Asbestos Structure Types*				Structures >5 Microns in Length	**Excluded Structures	Asbestos Structures for Concentration
			Fibers	Bundles	Clusters	Matrices			
3W-061212 W	EM 886246	ND	0	0	0	0	0	0	0
3W-061212 N	EM 886247	Chrysotile	2	0	0	0	0	0	2
3W-061212 E	EM 886248	ND	0	0	0	0	0	0	0
3W-061212 S	EM 886249	ND	0	0	0	0	0	0	0

*See Analytical Procedure for definitions

**C = Excluded from total due to lack of confirmation

**L = Excluded from total for length less than 0.5 micron (AHERA only)

**A = Excluded from total due to incorrect aspect ratio

ND = None Detected

Due Date: 6/14/12
 Due Time: AM

REILAB Reservoirs Environmental, Inc.
 9801 Logan St. Denver, CO 80216 • Ph: 303-964-1936 • Fax 303-477-4275 • Toll Free :866-RESI-ENV
 Pager : 303-508-2098

Job # _____
 Page 1 of _____

INVOICE TO: (IF DIFFERENT)

CONTACT INFORMATION:

Company: <u>R&R Environmental</u>	Company:	Contact: <u>Dave Roskelley</u>	Contact:
Address: <u>47 W 9000 S #2</u>	Address:	Phone:	Phone:
<u>Sandy W. 84070</u>		Fax:	Fax:
Project Number and/or P.O. #:		Cell/pager: <u>801 541-1035</u>	Cell/pager:
Project Description/Location: <u>3rd West Sub RMP</u>		Final Data Deliverable Email Address: <u>dave@rrenviro.com</u>	

ASBESTOS LABORATORY HOURS: Weekdays: 7am - 7pm		REQUESTED ANALYSIS												VALID MATRIX CODES		LAB NOTES:				
PLM / PCM / TEM <u>TEM</u> RUSH (Same Day) <input checked="" type="checkbox"/> PRIORITY (Next Day) <input type="checkbox"/> STANDARD (Rush PCM = 2hr, TEM = 6hr.)		PLM - Short report, Long report, Point Count	TEM - AHERA, Level II, 7402, ISO, +/-, Quant, Semi-quant, Micro-vac, ISO-Indirect Preps	PCM - 7400A, 7400B, OSHA	DUST - Total, Respirable	METALS - Analyte(s)	ROPA 8, TCLP, Welding Fume, Metals Scan	ORGANICS - METH	Salmonella +/-	E.coli O157:H7 +/-	Listeria +/-	Aerobic Plate Count +/- or Quantification	E.coli +/- or Quantification	Coliforms +/- or Quantification	Staphylococcus +/- or Quantification	Y & M +/- or Quantification	Mold +/- Identification, Quantification	Air = A	Bulk = B	
CHEMISTRY LABORATORY HOURS: Weekdays: 8am - 5pm																		Dust = D	Paint = P	
Metal(s) / Dust RUSH 24 hr. 3-5 Day																		Soil = S	Wipe = W	
RCRA 8 / Metals & Welding Fume Scan / TCLP RUSH 5 day 10 day **Prior notification is required for RUSH turnarounds.**																		Swab = SW	F = Food	
Organics 24 hr. 3 day 5 Day																		Drinking Water = DW	Waste Water = WW	
MICROBIOLOGY LABORATORY HOURS: Weekdays: 9am - 5pm														O = Other						
E.coli O157:H7, Coliforms, S.aureus 24 hr. 2 Day 3-5 Day														**ASTM E1792 approved wipe media only**						
Salmonella, Listeria, E.coli, APC, Y & M 48 Hr. 3-5 Day														Sample Volume (L) / Area	Matrix Code	# Containers	Data Collected mm/dd/yy	Time Collected hh/mm a/p	EM Number (Laboratory Use Only)	
Mold RUSH 24 Hr 48 Hr 3 Day 5 Day																				
Turnaround times establish a laboratory priority, subject to laboratory volume and are not guaranteed. Additional fees apply for afterhours, weekends and holidays.																				
Special Instructions:																				
Client sample ID number (Sample ID's must be unique)																				
1	3W-061212 W	X															968	A	6/12/12	8586246
2	3W-061212 N																959			47
3	3W-061212 E																955			48
4	3W-061212 S																949			49
5																				
6																				
7																				
8																				
9																				
10																				

Number of samples received: _____ (Additional samples shall be listed on attached long form.)

NOTE: REI will analyze incoming samples based upon information received and will not be responsible for errors or omissions in calculations resulting from the inaccuracy of original data. By signing client/company representative agrees that submission of the following samples for requested analysis as indicated on this Chain of Custody shall constitute an analytical services agreement with payment terms of NET 30 days, failure to comply with payment terms may result in a 1.5% monthly interest surcharge.

Relinquished By: <u>Justin Kyri</u>	Fed Ex	Date/Time: <u>6/12/12</u>	Sample Condition: On Ice <input checked="" type="checkbox"/> Sealed <input checked="" type="checkbox"/> Intact <input checked="" type="checkbox"/>
Laboratory Use Only			Temp. (F°) _____ Yes <input checked="" type="checkbox"/> No <input checked="" type="checkbox"/> Yes <input checked="" type="checkbox"/> No <input checked="" type="checkbox"/>
Received By: <u>[Signature]</u>	Date/Time: <u>6/13/12 9:10</u>	Carrier: <u>Arden</u>	
Results:	Contact: <u>Dave</u> Phone: _____ Email: _____ Fax: _____	Date: <u>6/14</u> Time: <u>0A</u> Initials: <u>AK</u>	Contact: _____ Phone: _____ Email: _____ Fax: _____
	Contact: _____ Phone: _____ Email: _____ Fax: _____	Date: _____ Time: _____ Initials: _____	Contact: _____ Phone: _____ Email: _____ Fax: _____

Attachment I

Key to Count Sheets Count Sheets Analytical Procedures

Structures identifications consist of an Asbestos Type followed by a Structure Type

Asbestos Type

A = Amosite
An = Anthophyllite
C = Chrysotile
Cr = Crocidolite
T = Tremolite

Structure Types

F = Fiber
B = Bundle
C = Cluster
M = Matrix

ND = no structures detected
M = other structure associated with a matrix
NAM = Non Asbestos Mineral
XGB = partly obscured by a grid bar

Sizing Conversion


1 length unit = 5 mm on screen = 0.278 micron
1.80 length units = 0.5 micron
18.0 length units = 5 microns

1 width unit = 1 mm on screen = 0.0556 micron

TEM Analysts

Jeanne S. Orr
Nathan DelHiero
Angela Heitger
Jonathan Bernard

Paul D. LoScalzo
Mark Steiner
Norberto Zimbleman
Robert Workman

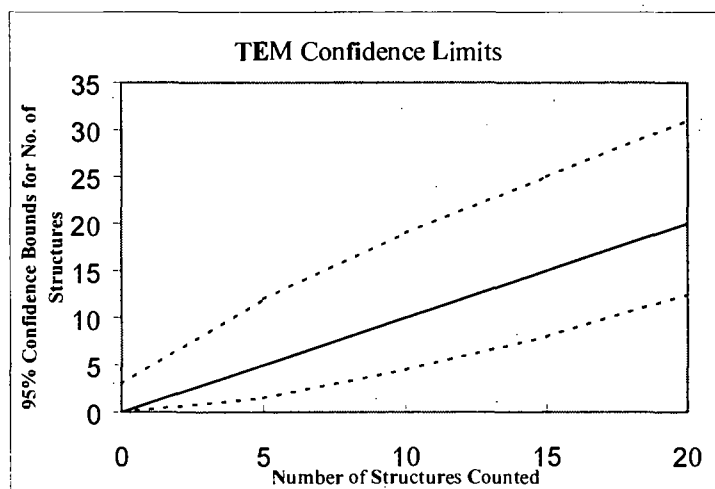

Upper and lower 95% confidence bounds for the number of structures counted assuming a Poisson distribution.

Reservoirs Environmental, Inc.
TEM Asbestos Structure Count

Laboratory name:	REI
Instrument	JEOL 100 CX N (S)
Voltage (KV)	100 KV
Magnification	20KX 10KX
Grid opening area (mm ²)	0.01
Scale: 1L =	0.28 um
Scale: 1D =	0.056 um
Primary filter area (mm ²)	385
Secondary Filter Area (mm ²)	
QA Type	

Client:	R+R
Sample Typo (A=Air, D=Dust):	A
Air volume (L) or dust area (cm ²)	968
Date received by lab	6/13/12
Lab Job Number:	237906
Lab Sample Number:	886246

Analyzed by	JK
Analysis date	6/13/12
Method (D=Direct, I=Indirect, IA=Indirect, ashed)	D
Counting rules (ISO, AHERA, ASTM)	AH
Grid storage location	Month Analyzed
Scope Alignment	Date Analyzed

F-Factor Calculation (Indirect Preps Only):

Fraction of primary filter used	
Total Resuspension Volume (ml)	
Volume Applied to secondary filter (ml)	

Grid	Grid Opening	Structure Type	No. of Structures		Dimensions		Identification	Mineral Class			Sketch/Comments	1 = yes, blank = no		
			Primary	Total	Length	Width		Amphibole	C	NAM		Sketch	Photo	EDS
A	F3-3	NO												
	E3-3	NO					Prep A	80% intact	5-10%	debris				
	C3-3	NO												
	B3-3	NO												
B	45-3	NO					Prep B	60% intact	5-10%	debris				
	F5-3	NO												
	E5-3	NO												
	G5-3	NO												

LA = Libby-type amphibole

OA = Other (non-Libby type) amphibole

C = Chrysotile

NAM = Non-asbestos material

Reservoirs Environmental, Inc.
TEM Asbestos Structure Count

Laboratory name:	REI
Instrument	JEOL 100 CX N <u>S</u>
Voltage (KV)	100 KV
Magnification	<u>20KX</u> 10KX
Grid opening area (mm ²)	0.01
Scale: 1L =	0.2S um
Scale: 1D =	0.056 um
Primary filter area (mm ²)	385
Secondary Filter Area (mm ²)	
QA Type	

Client:	R+R
Sample Type (A=Air, D=Dust):	A
Air volume (L) or dust area (cm ²)	259
Date received by lab	6/13/12
Lab Job Number:	237906
Lab Sample Number:	886247

Analyzed by	JK
Analysis date	6/13/12
Method (D=Direct, I=Indirect, IA=Indirect, ashed)	D
Counting rules (ISO, AHERA, ASTM)	A4
Grid storage location	Month Analyzed
Scope Alignment	Date Analyzed

F-Factor Calculation (Indirect Preps Only):

Fraction of primary filter used	
Total Resuspension Volume (ml)	
Volume Applied to secondary filter (ml)	

Grid	Grid Opening	Structure Type	No. of Structures		Dimensions		Identification	Mineral Class			Sketch/Comments	1 = yes, blank = no		
			Primary	Total	Length	Width		Amphibole	C	NAM		Sketch	Photo	EDS
A	FS-1	ND												
	ES-1	ND												
	CS-1	ND					Prep A	70% intact	5-10% debris					
	BS-1	ND					Prep B = A							
B	H3-4	ND												
	G3-4	ND												
	F3-4	ND												
	E3-4	F		1	2	1	CD		-		/			
	D3-4	F		2	2	1	CD		-		-			

LA = Libby-type amphibole

OA = Other (non-Libby type) amphibole

C = Chrysotile

NAM = Non-asbestos material

Reservoirs Environmental, Inc.
TEM Asbestos Structure Count

Laboratory name:	REI
Instrument	JEOL 100 CX N (S)
Voltage (KV)	100 KV
Magnification	20KX 10KX
Grid opening area (mm ²)	0.01
Scale: 1L =	0.28 um
Scale: 1D =	0.056 um
Primary filter area (mm ²)	385
Secondary Filter Area (mm ²)	
QA Type	

Client:	R+R
Sample Type (A=Air, D=Dust):	A
Air volume (L) or dust area (cm ²)	955
Date received by lab	6/13/12
Lab Job Number:	237906
Lab Sample Number:	886248

F-Factor Calculation (Indirect Preps Only):

Fraction of primary filter used	
Total Resuspension Volume (ml)	
Volume Applied to secondary filter (ml)	

Analyzed by	JK
Analysis date	6/13/12
Method (D=Direct, I=Indirect, IA=Indirect, ashed)	D
Counting rules (ISO, AHERA, ASTM)	AH
Grid storage location	Month Analyzed
Scope Alignment	Date Analyzed

Grid	Grid Opening	Structure Type	No. of Structures		Dimensions		Identification	Mineral Class			Sketch/Comments	1 = yes, blank = no		
			Primary	Total	Length	Width		Amphibole	C	NAM		Sketch	Photo	EDS
A	G4-3	MD												
	F4-3	MD					Prep A 90%	intact	5-10%	debris				
	E4-3	MD												
	C4-3	MD												
	B4-3	MD					Prep B 70%	intact	5-10%	debris				
B	H3-1	MD												
	G3-1	MD												
	F3-1	MD												
	E3-1	MD												

LA = Libby-type amphibole

OA = Other (non-Libby type) amphibole

C = Chrysotile

NAM = Non-asbestos material

Reservoirs Environmental, Inc.
TEM Asbestos Structure Count

Laboratory name:	REI
Instrument	JEOL 100 CX N (S)
Voltage (KV)	100 KV
Magnification	20KX 10KX
Grid opening area (mm ²)	0.01
Scale: 1L =	0.28 μ m
Scale: 1D =	0.056 μ m
Primary filter area (mm ²)	385
Secondary Filter Area (mm ²)	
QA Type	

Client:	R+R
Sample Type (A=Air, D=Dust):	A
Air volume (L) or dust area (cm ²)	949
Date received by lab	6/13/12
Lab Job Number:	237906
Lab Sample Number:	886249

Analyzed by	JK
Analysis date	6/13/12
Method (D=Direct, I=Indirect, IA=Indirect, ashed)	D
Counting rules (ISO, AHERA, ASTM)	AH
Grid storage location	Month Analyzed
Scope Alignment	Date Analyzed

F-Factor Calculation (Indirect Preps Only):

Fraction of primary filter used	
Total Resuspension Volume (ml)	
Volume Applied to secondary filter (ml)	

Grid	Grid Opening	Structure Type	No. of Structures		Dimensions		Identification	Mineral Class			Sketch/Comments	1 = yes, blank = no		
			Primary	Total	Length	Width		Amphibole	C	NAM		Sketch	Photo	EDS
A	H3-4	ND												
	G3-4	ND					Prep A 90% intact 5-10% debris							
	F3-4	ND												
	E3-4	ND					Prep B NA							
	C3-4	ND												
B	G3-4	ND												
	F3-4	ND												
	E3-4	ND												
	C3-4	ND												

LA = Libby-type amphibole

OA = Other (non-Libby type) amphibole

C = Chrysotile

NAM = Non-asbestos material

Analytical Procedures – AHERA

Transmission electron microscopy/energy dispersive X-ray spectrometry/selected area electron diffraction (TEM/EDX/SAED) was employed in the analysis of the samples, which were collected on 25 mm mixed cellulose ester air filters. A portion of each filter was collapsed with acetone and etched in a plasma asher. The etched filter was then coated with a thin layer of carbon in a carbon side down. The sample was then placed inside a condensation washer and treated with acetone to remove the filter matrix and expose any inert material.

For each sample, enough grid openings on a 200 mesh TEM grid are analyzed to ensure an analytical sensitivity of at least 0.005 structures/cc. A minimum of four grid openings from two preparations are analyzed for each sample. The grid openings are searched for fibrous structures which, if present are analyzed by SAED and/or EDX (elemental analysis). The AHERA protocol requires SAED confirmation of enough chrysotile asbestos structures on each sample to cause the sample to exceed 70 structures/mm² (usually 4 or 5 structures). Both SAED and EDX confirmation are required of enough amphibole structures on each sample to cause the sample to exceed 70 structures/mm² (usually 4 or 5 structures) per sample. Either SAED or EDX is required for the remaining asbestos structures of either type. The morphology of each structure is determined and the length and the diameter of any asbestos structures are recorded. Asbestos fibers, bundles, cluster and matrices were identified and recorded. The asbestos structures have been defined in AHERA as follows:

Fiber:	is a structure having a minimum length greater than or equal to 0.5 micron with an aspect ratio of 5:1 or greater with substantially parallel sides.
Bundle:	is a structure composed of three or more fibers in parallel arrangement, with each fiber closer than the diameter of one fiber.
Cluster:	is a structure with fibers in random arrangements such that all fibers are intermixed and no single fiber is isolated from the group.
Matrix:	is a fiber or fibers with one end free and the other end embedded or hidden by a particulate. The exposed fiber end must meet the fiber definition given above.

If more than 50 asbestos structures are identified and confirmed on a sample, AHERA analysis may be terminated after completion of the grid opening, which contains the 50th structure. AHERA protocol requires the laboratory to reject any clearance sample which contains in excess of 25% total particulate loading or which appears to be unevenly loaded.

The AHERA protocol includes specific sampling requirements, including minimum numbers of samples and minimum air volumes. Specifically, the 70 structures/mm² clearance criteria is only allowed for sets five inside samples (collected in a group of 13 samples including: five outsides and three blanks) with volumes greater than 1200 liters (40 CFR Part 763, page 41894). Deviation from the AHERA sampling protocol may affect the validity of the analytical results. Analysis of samples collected by non-protocol methods are not accredited by NVLAP

Equations Used for Calculations

$$\text{Area Analyzed, mm}^2 = \# \text{ GO counted} \times \text{Average GO Area (mm)}$$

$$\text{Concentration, s/cc} = \frac{\# \text{ Asbestos Structures}}{\# \text{ GO Counted}} \times \frac{1}{\text{Volume (L)}} \times \frac{\text{Eff. Filter Area (mm}^2\text{)}}{\text{Average GO area (mm}^2\text{)}} \times \frac{1\text{L}}{1000\text{cc}}$$

$$\text{Filter loading, s/mm}^2 = \frac{\# \text{ Asbestos structures}}{\text{Area Analyzed (mm}^2\text{)}}$$

GO = TEM grid opening
