



NATIONWIDE ENVIRONMENTAL SERVICES, INC.

6th Avenue West Business Park
14818 W 6th Ave. Suite 5A
Golden, CO 80401

968748

February 26, 2021

Ms. Terese Van Donsel
Remedial Project Manager
U.S. Environmental Protection Agency
77 West Jackson Boulevard, SR-6J
Chicago, IL 60604

Mr. Brian Conrath
Illinois Environmental Protection Agency
1021 North Grand Avenue East
P.O. Box 19276
Springfield, IL 62794-9276

RE: Southeast Rockford Groundwater Contamination Site
Groundwater Monitoring Report
Semi-Annual Monitoring Event – November 2020

Ms. Van Donsel / Mr. Conrath:

We are providing the groundwater monitoring report presenting field sampling results, analytical data, and limited data interpretation summary for the semi-annual groundwater monitoring event performed at the Southeast Rockford Groundwater Contamination Site (the Site) in November 2020.

We note that this report for the referenced semi-annual monitoring event includes sample and analysis results for 1,4-dioxane, a monitored constituent that was added to the Site groundwater monitoring program in the second quarter 2020.

Please contact me at telephone (303) 232-2134 if you have any questions regarding the information provided or require any additional information.

Sincerely,

William B. Dotterer,
Sr. Project Manager

cc: Nadine Miller, City of Rockford

Enclosures

**Southeast Rockford
Groundwater Contamination Site**

**Groundwater Monitoring Report for
Semi-Annual Monitoring Event
November 2020**

Issued: February 2021



Nationwide Environmental Services, Inc.

Southeast Rockford Groundwater Contamination Site
Groundwater Monitoring Report

Overview

The second semi-annual monitoring event for calendar year 2020 was performed at the Southeast Rockford Groundwater Contamination Site (Site) in November 2020, pursuant to the sample schedule notice provided to the U.S. Environmental Protection Agency (USEPA) and the Illinois Environmental Protection Agency (IEPA) on October 30, 2020. The following report presents the analytical results for the second 2020 semi-annual monitoring event along with cumulative analytical results for prior monitoring events conducted at the Site. The next semi-annual groundwater monitoring event for the Site is scheduled for June 2021.

The principle intent of the Site groundwater monitoring program is: (1) to monitor groundwater quality for the ten chemicals of concern (COCs) identified for the Site (vinyl chloride (VC) was subsequently added to the monitoring regimen) at designated monitoring locations within the Site extents, relative to groundwater clean-up standards established under the Record of Decision (ROD OU2, 1995); and (2), generally assess the influence of identified Site source areas and associated remediation activities on aquifer restoration goals, to the extent possible under the Site groundwater monitoring program scope.

Field sampling activity and analytical procedures utilized for monitored VOCs at the Site have been performed in accordance with the approved Quality Assurance Project Plan (QAPP, 2017 rev. 1). The US EPA has requested that the City further characterize groundwater conditions at the Site and include monitoring for 1,4-dioxane in the site-wide monitoring regimen. Field sampling and sample analysis completed for the current monitoring event (November 2020) included 1,4-dioxane as a monitored constituent, and sampling and analytical activities were performed in accordance with the draft revision to the Quality Assurance Project Plan (QAPP, 2020 rev. 2.0) reviewed with the City of Rockford (City) staff and Agency representatives in April 2020 and issued to the City for approval in June 2020.

Field sampling for 1,4-dioxane was accomplished using the low stress (low flow) purge and sample collection procedure established for identified COCs at the Site. Sample analysis for 1,4-dioxane was performed by SPME and GC\MS with SIM. In accordance with the QAPP revision, laboratory Level IV data packages were generated in completing 1,4-dioxane analysis for collected samples, which are not included with the report because of the size of the document, but are available upon request.

The Site groundwater quality assessment component of the project scope consists of a limited narrative providing a comparison of groundwater monitoring data obtained during the current monitoring event to analytical data obtained during the prior monitoring event to identify any notable change in groundwater conditions that may have occurred in the intervening 6-month period. Such comparison of groundwater conditions is provided in following sections of this report and visually depicted in the cumulative Site COC concentration trend graphs.

NES continues to coordinate efforts with IEPA to share groundwater data obtained from common monitoring well locations at the Site. NES is not aware of IEPA sample collection from Site monitoring locations for the current reporting period and no comparative Site data from IEPA is presented in this report.

Semi-Annual Monitoring Event
November 2020

The results of the current groundwater monitoring event, pertinent Site information, groundwater monitoring laboratory data sheets, and supporting laboratory data validation summaries are presented in the report as follows:

- **Figure 1:** Groundwater Monitoring Network and Source Areas
- **Figure 2:** Total Volatile Organic Compounds Concentration Trends
- **Table 1a:** Summary of existing COC Analytical Results (current monitoring event)
- **Table 1b:** Summary of 1,4-dioxane Analytical Results (current monitoring event)
- **Table 2a:** Cumulative Groundwater Analytical Results for COC Analytical Results
- **Table 2b:** Cumulative Groundwater Analytical Results for 1,4-dioxane Analytical Results
- **Table 3:** Groundwater Elevations (current monitoring event)
- **Table 4:** Groundwater Monitoring Network Inventory
- **Appendix A:** Groundwater Monitoring Data Validation Summary & Laboratory Data Sheets
- **Appendix B:** Groundwater Monitoring Field Data Sheets

Monitoring Event Results

The laboratory data sheets and data quality summaries including relevant analytical quality assurance/quality control (QA/QC) criteria are provided in **Appendix A** of this report. The record of field sampling activities conducted during the current monitoring event are presented in the field sampling sheets provided in **Appendix B** of this report and contain pertinent field information, general site conditions, and low flow purge stabilization data. The following field condition was noted to occur during the current semi-annual monitoring event:

- MW-203 was sampled with a portable low flow sampling pump. The permanent well pump installed in the well has been removed by an unknown party.

The analytical results for groundwater samples collected during the current monitoring event include VOC analysis for the COCs identified for the Site (ROD OU2), as well as, VC by method VOA 8260C, and 1,4-dioxane analysis by SPME and GC\MS with SIM. Analytical results for VOC and 1,4-dioxane samples collected for the current monitoring event are presented in **Tables 1a and 1b**, respectively. The cumulative historical analytical results for VOCs in groundwater samples collected from the Site monitoring network (by monitoring well location) are presented in **Table 2a**. Cumulative reporting for 1,4-dioxane results is provided in **Table 2b**.

A series of graphs depicting historical total VOC concentrations for select monitoring wells are presented in **Figure 2** to show total VOC concentration trends occurring at these monitoring locations. The monitoring locations used for comparison to historical analytical data were selected based on their proximity to designated source areas. Although the graphs depict analytical results from 1999 to the present, the evaluation presented in this report for total VOCs in groundwater at the Site is principally devoted to the identification of changes, if any, from the previous semi-annual monitoring event conducted in June 2020. The 1,4-dioxane analytical results are not included in the concentration trend graphs presented in Figure 2 of this semi-annual monitoring report since the November 2020 monitoring event comprises only the second instance that 1,4-dioxane data has been generated for the Site under the current groundwater monitoring and reporting program. Concentration trend results for 1,4-dioxane will be provided in future Site monitoring reports.

The graphs presented in **Figure 2** reveal that fluctuations in total groundwater VOC concentrations have occurred over the period that the Site groundwater monitoring network has been sampled under the selected remedial action plan. The causal factors for VOC concentration variability are presumed to be source area remedial activities performed by others, variation in groundwater levels and flow paths, precipitation events resulting in aquifer recharge, groundwater pumping rates, etc.

Another observation made in reviewing historical site data compiled to date is that groundwater elevations measured across the Site during the current monitoring event are higher by some 5 to 10 feet from water levels measured at the same monitoring well locations during the same calendar period five years ago. The rise in groundwater elevation at the Site from prior periods is apparently consistent with general rise in regional groundwater elevations based on discussion with field personnel. NES is not in receipt of any specifics regarding past or ongoing remediation efforts addressing groundwater contamination source areas that would allow further interpretation of the groundwater data, other than the general observations presented in this report. Statistical analysis of groundwater monitoring data is not performed as a routine element in reporting groundwater monitoring results for the Site.

Groundwater Monitoring Data Evaluation

VOCs

Overall, total volatile organic compound (VOC) concentrations in groundwater have generally decreased across the Site since inception of the long-term monitoring program in March 1999. The ratios of parent VOC compound concentrations to associated breakdown product concentrations indicate conditions for biodegradation, comprising a component of natural attenuation, may be occurring at the Site. The reported detections of VC and chloroethane in groundwater samples are further indicators that natural attenuation of parent compounds may be occurring at the Site.

The level of total VOC concentrations found at certain monitoring well locations, relative to the previous monitoring event performed in June 2020, are summarized below. In that the current monitoring event is the second to include sample collection and analysis for 1,4-dioxane, no interpretation of data obtained for this monitored constituent is provided, other than to note the concentrations found in groundwater, relative to identified Site source areas. The noted monitoring well locations are located proximate to, or down-gradient from, identified source areas. The Site source areas are segregated by general geographic location within the Site for the purpose of this report.

East-Source Area 7

Generally, total VOC concentrations reported for groundwater monitoring locations near the Area 7 source area have decreased or remained relatively stable from the previous monitoring event, with the exception of the increases found to occur at MW-101C and MW-102C attributed to increases in 1,1-DCA and 1,1,1-TCA. Monitoring well locations at which VOC constituents in groundwater were found to occur above MCLs during the current reporting period are summarized below.

Location	MW101A	MW101B	MW101C	MW102A	MW102B	MW102C
Constituents	3	4	4	1	1	3

Location	MW133B	MW133C
Constituents	4	3

The analytical results for groundwater quality samples collected from well locations proximate to or downgradient from Area 7 which show material increases (>20%) in COC concentrations from the previous monitoring event are summarized below.

Monitoring Location	Compound	Current Conc. (ug/L)	Prior Conc. (ug/L)
MW 101A	1,1,1-TCA	91.4	23.7
	1,1-DCA	43.7	19.6
	1,1-DCE	8.4	2.2
	CFM	2.9	0.53
	cis-1,2-DCE	26.1	4.5
	PCE	6.6	1.4
	trans-1,2-DCE	1.8	0.65
	TCE	11.4	2.5

North-Source Areas 4, 9, 10, & 11

Total VOC concentrations reported for groundwater monitoring locations near Source Areas 4, 9, 10, & 11 in the northern extent of the Site have generally decreased or remained relatively stable from the previous monitoring event. Monitoring well locations at which VOC constituents in groundwater were found to occur above MCLs during the current reporting period are presented below.

Location	MW113A	MW113B	MW121	MW124	MW16
Constituents	3	3	2	2	3

The analytical results for groundwater quality samples collected from well locations proximate to or downgradient from Areas 4, 9, 10, & 11 which show material increases (>20%) in COC concentrations from the previous monitoring event are summarized below.

Monitoring Location	Compound	Current Conc. (ug/L)	Prior Conc. (ug/L)
MW 124	VC	2	1.2

West-Rock River

Total VOC concentrations reported for groundwater monitoring locations near the Rock River increased from the previous monitoring event. Monitoring well locations at which VOC constituents in groundwater were found to occur above MCLs during the current reporting period are presented below.

Location	MW117B	MW117D	MW204	MW205A	MW205B	MW206A
Constituents	2	2	2	2	2	2

Location	MW206B	MW206C
Constituents	3	3

The analytical results for groundwater quality samples collected from well locations proximate to the Rock River which show material increases (>20%) in COC concentrations from the previous monitoring event are summarized below.

Monitoring Location	Compound	Current Conc. (ug/L)	Prior Conc. (ug/L)
MW 203	PCE	2.6	2.1
MW 204	PCE	2.7	1.6
MW 206C	1,1-DCE	11.5	6.6
	TCE	7.6	3.4

1,4-dioxane

Sample collection and analysis for 1,4-dioxane was added to the Site groundwater monitoring program in the second quarter 2020, and the semi-annual monitoring event completed in June 2020 was the first sample event which included this compound. The analytical results obtained for 1,4-dioxane during the most recent monitoring event are presented in **Table 1b** and reveal that the compound was detected at all monitoring locations in the Site groundwater monitoring network above the reporting limit (0.5 ug/L) except at MW-47, MW-101D, MW-136, MW-200, MW-202, and MW-203. The highest concentrations of 1,4-dioxane were found

to occur at MW-102B (170 ug/l) and MW-133C (120 ug/L). These monitoring locations are situated to the north and west of Source Area 7.

Groundwater Monitoring Network Maintenance

The current condition and historical maintenance activity performed at monitoring locations comprising the Site groundwater monitoring network are presented in the monitoring well inventory (**Table 4**). In instances in which repairs or maintenance performed for monitoring well locations result in changes to the wellhead elevation or other characteristic, revisions are made to the monitoring well inventory to record such change in the condition or configuration of the individual monitoring wells.

In performing the semi-annual groundwater monitoring event completed in November 2020, field sampling personnel observed that the wellhead cover for MW-203 was damaged and required repair or replacement. Normally, replacement of the entire wellhead protective casing would be recommended in such instance however, MW-203 is located in a parking lot of an auto repair facility which operates 6 days a week. In addition, the monitoring wellhead is set in thickened concrete compatible with vehicle loading at the location, thus repair of the existing well head cover is recommended rather than replacement which would involve concrete collar removal and reinstallation. A separate submittal will be issued identifying the work scope and price to repair the wellhead cover for consideration by the City.

No other maintenance or repair items were identified for the groundwater monitoring network in completing the November 2020 semi-annual monitoring event.

FIGURES

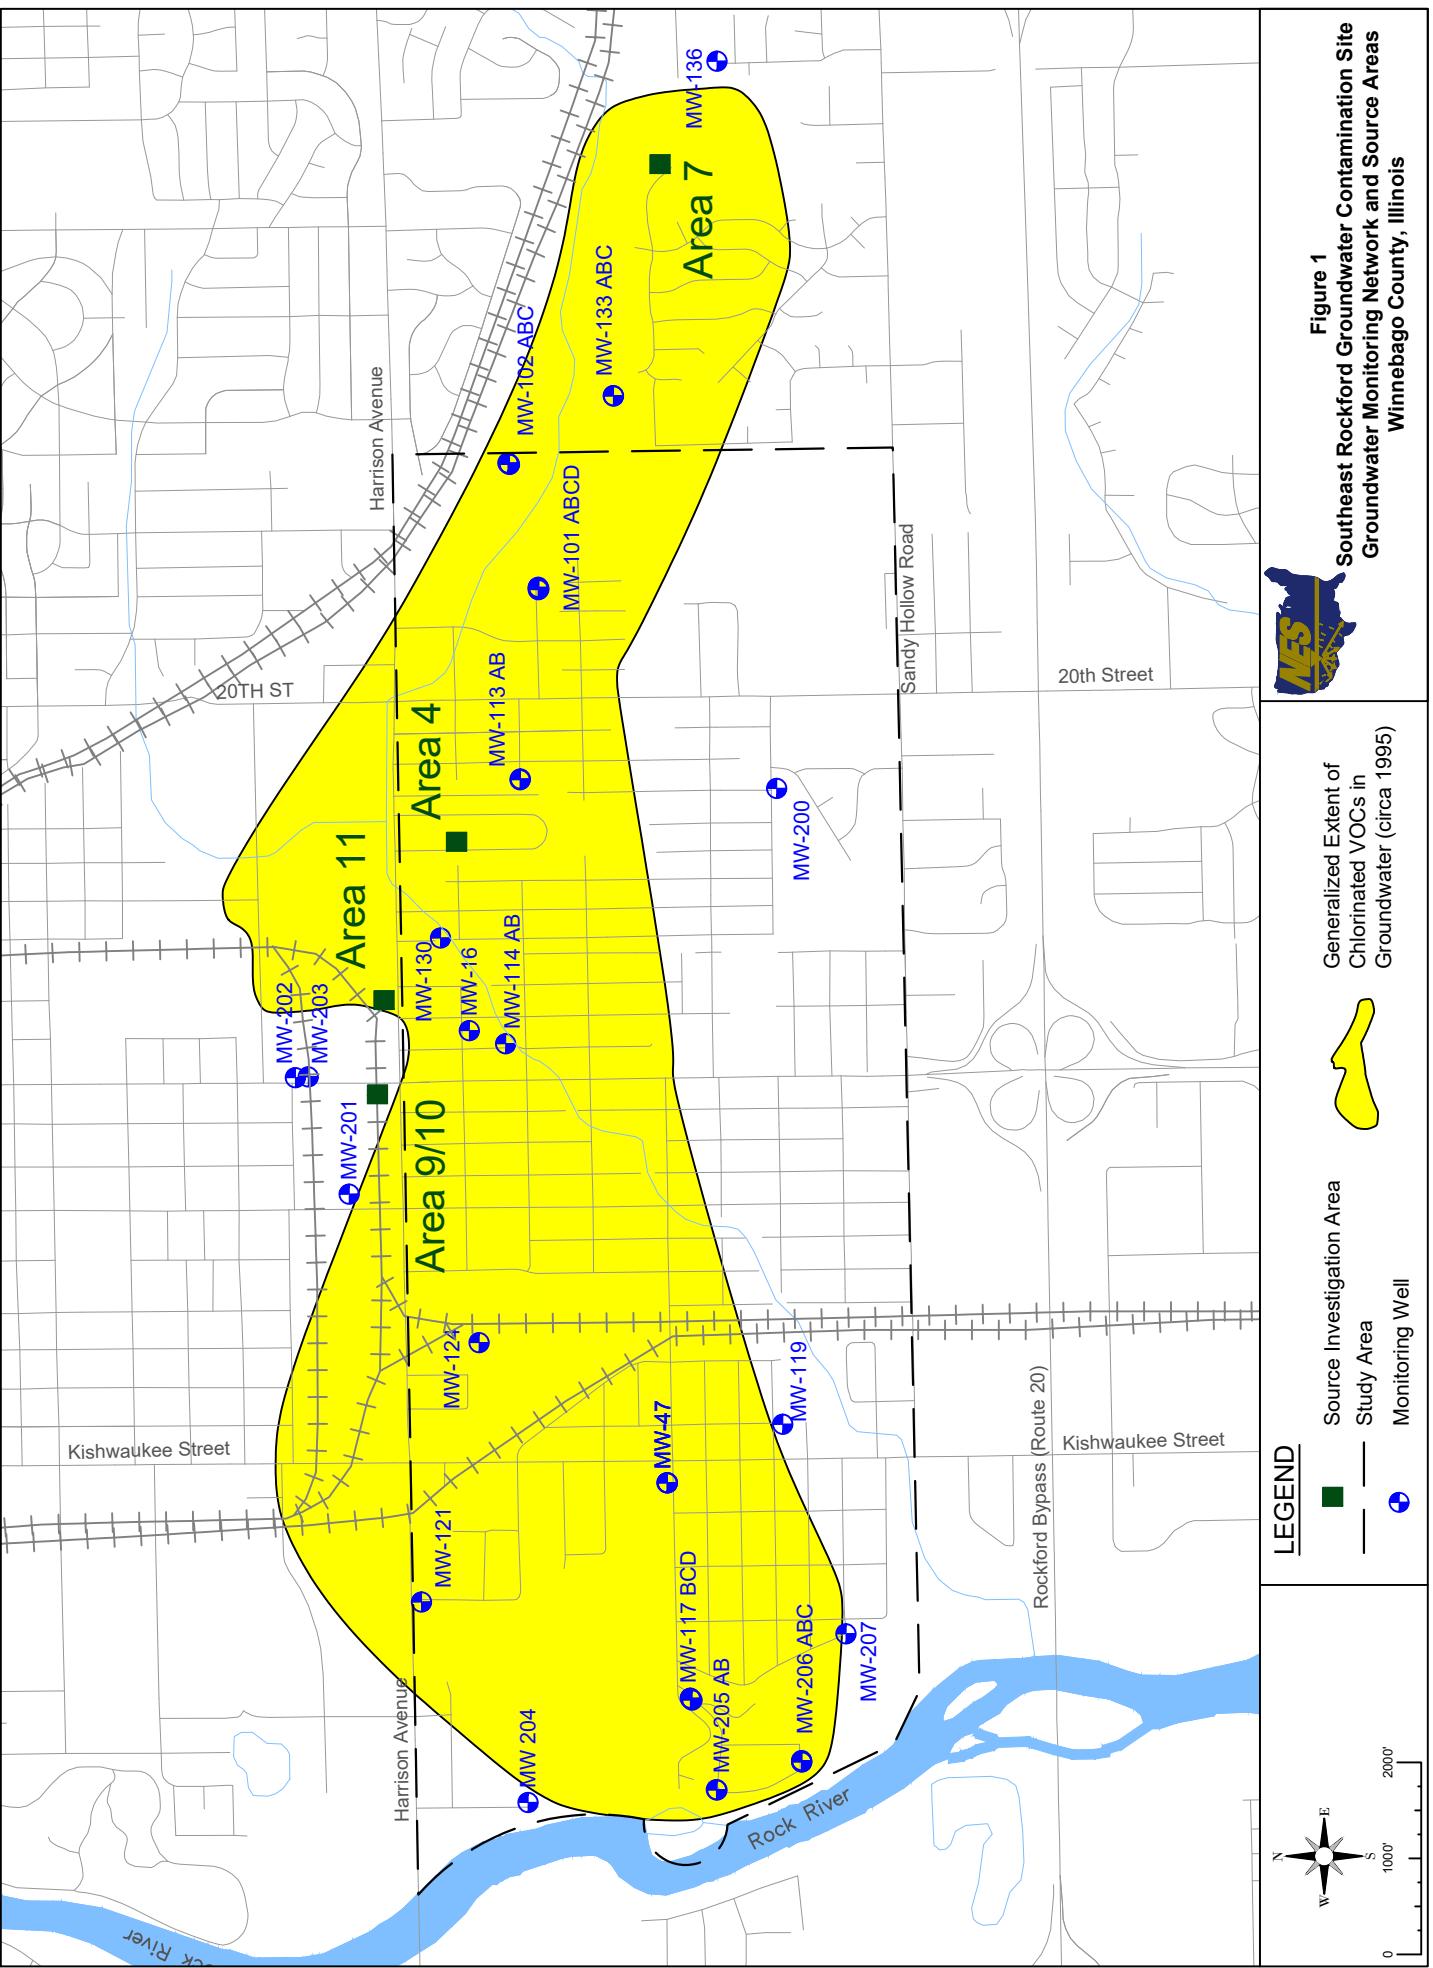


Figure 1
Southeast Rockford Groundwater Contamination Site
Groundwater Monitoring Network and Source Areas
Winnebago County, Illinois



Generalized Extent of
Chlorinated VOCs in
Groundwater (circa 1995)




LEGEND

■	Source Investigation Area
—	Study Area
●	Monitoring Well


N
E
S
W
0
1000' 2000'

**Figure 2 - Southeast Rockford Groundwater Contamination Site
Total Volatile Organic Compounds Concentration Trends
Monitoring Wells Near Area 7**

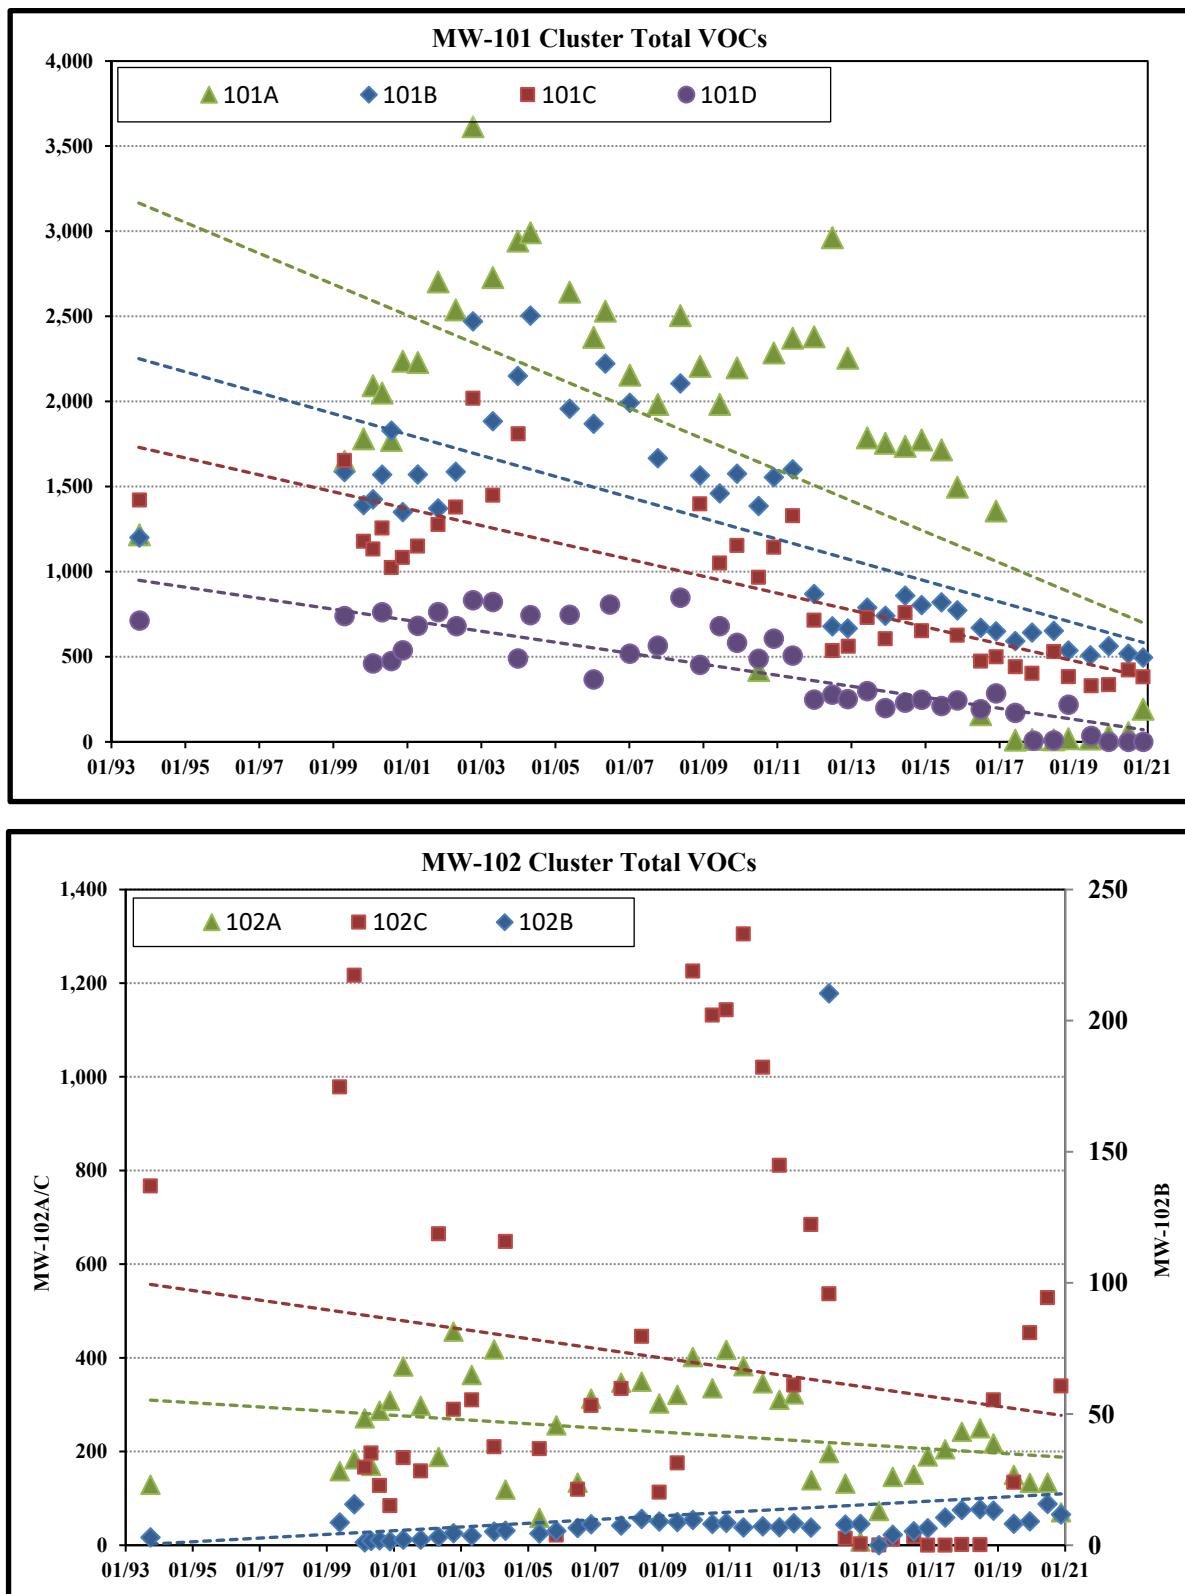



Y-axis = Total VOCs in micrograms per liter; X- axis = Sampling Date

**Figure 2 - Southeast Rockford Groundwater Contamination Site
Total Volatile Organic Compounds Concentration Trends
Monitoring Wells Near Area 7**

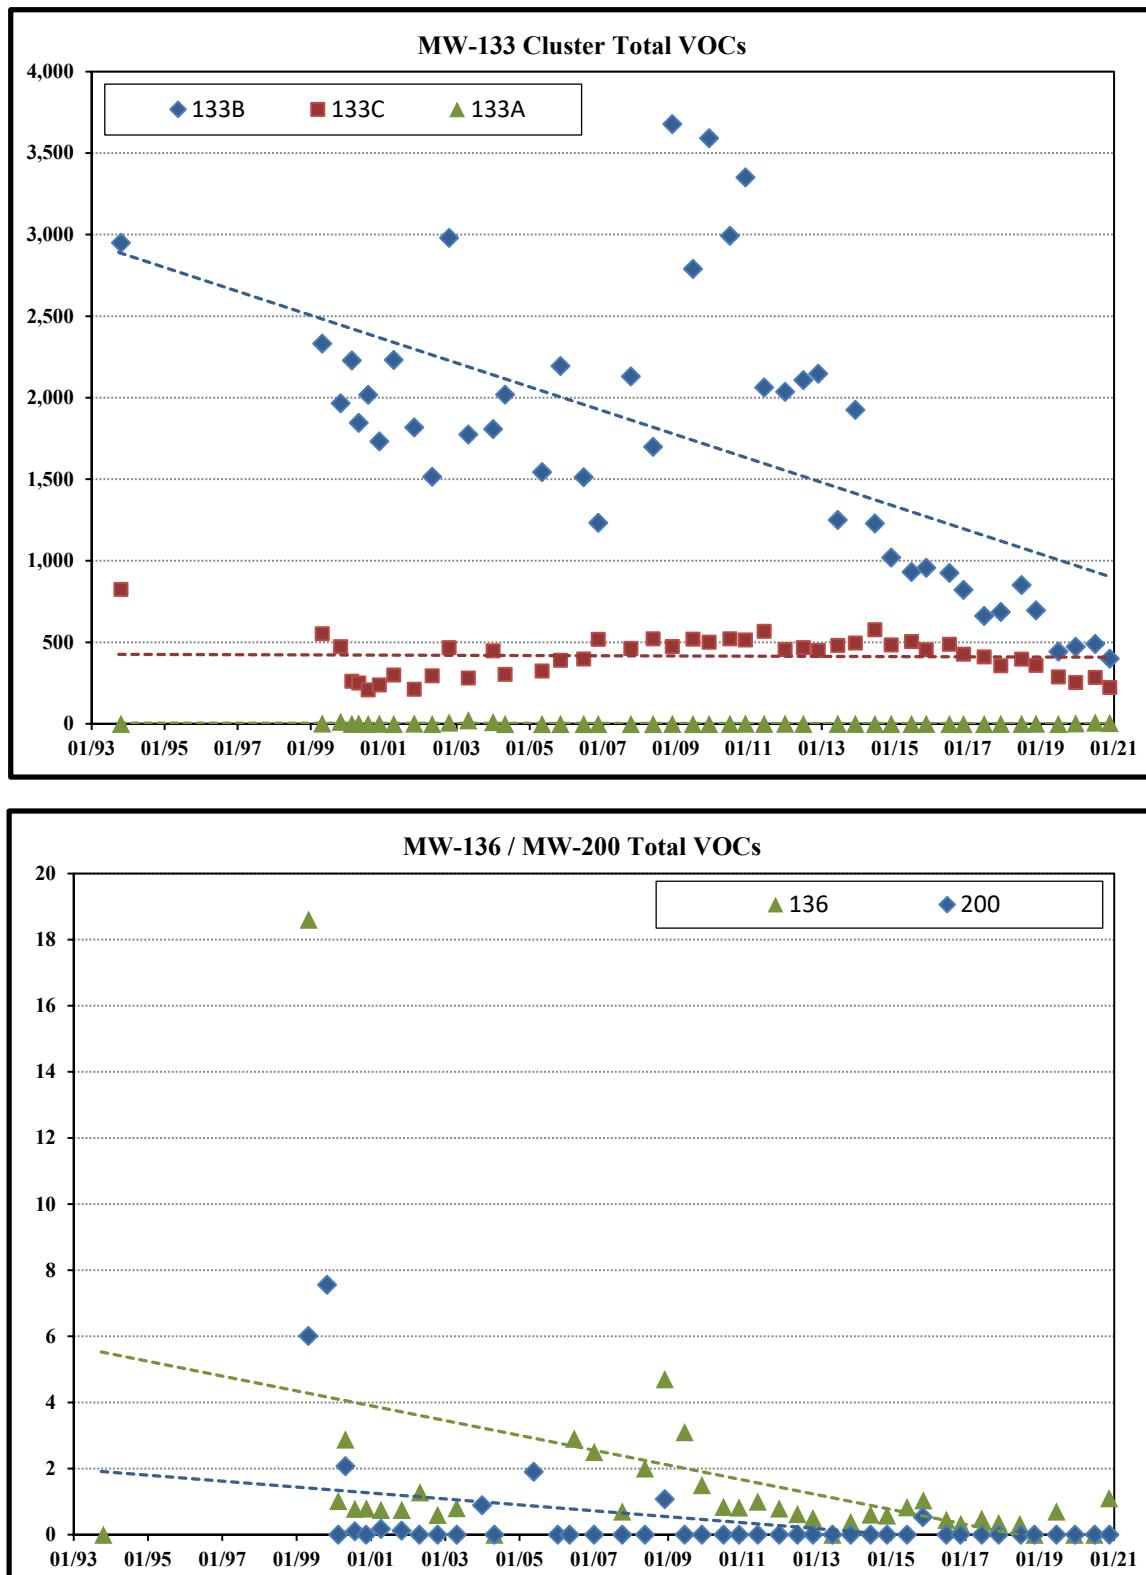


Y-axis = Total VOCs in micrograms per liter; X- axis = Sampling Date

**Figure 2 - Southeast Rockford Groundwater Contamination Site
Total Volatile Organic Compounds Concentration Trends
Monitoring Wells Near Areas 4, 9/10, 11**

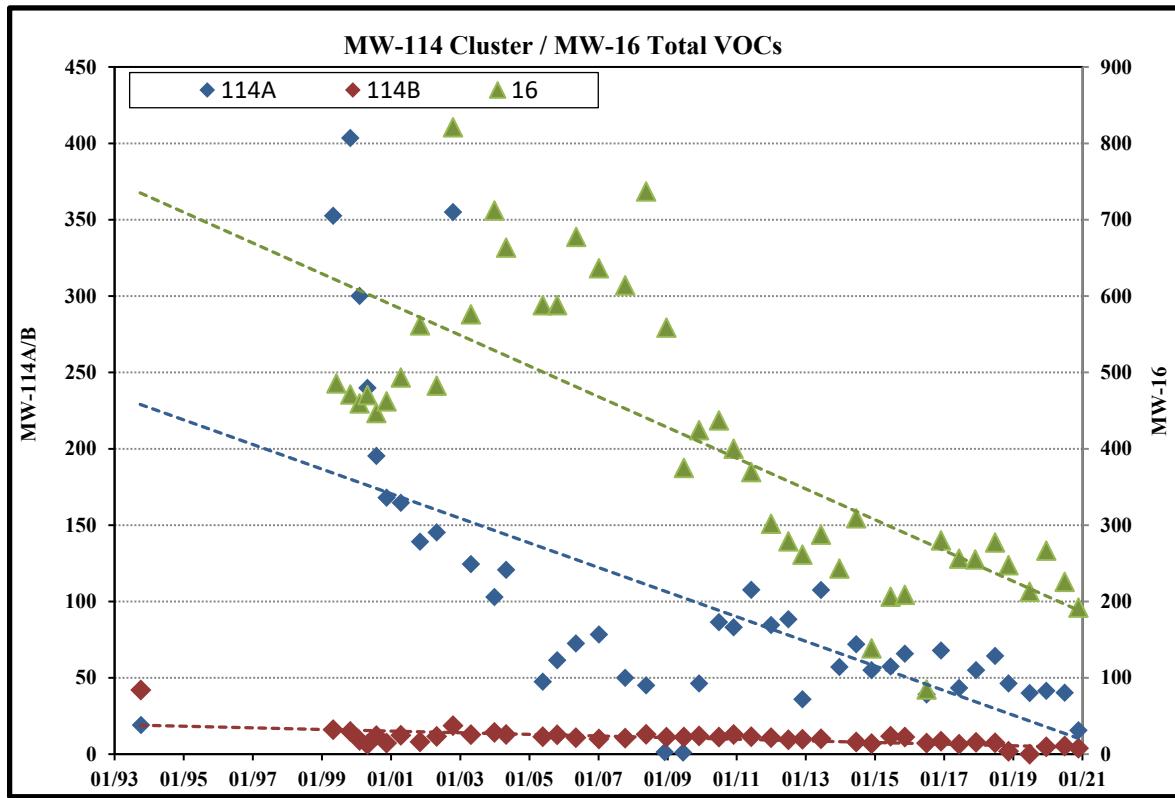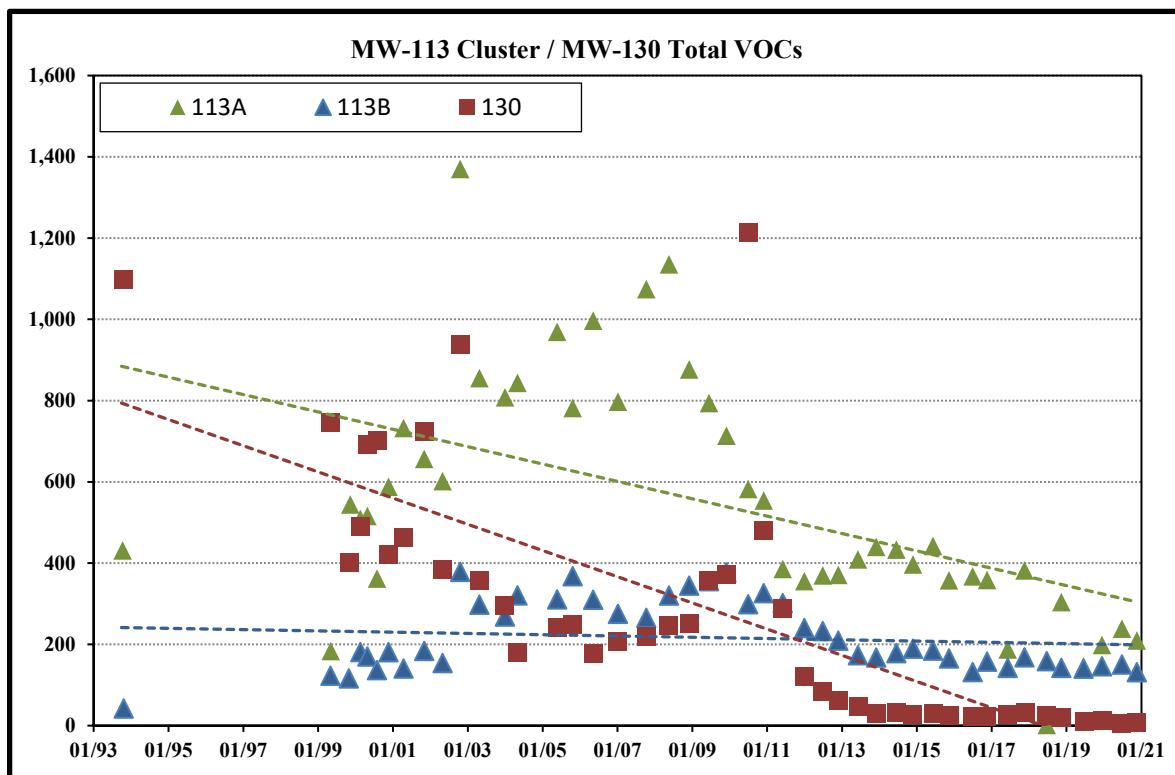


Y-axis = Total VOCs in micrograms per liter; X- axis = Sampling Date

**Figure 2 - Southeast Rockford Groundwater Contamination Site
Total Volatile Organic Compounds Concentration Trends
Monitoring Wells Near Areas 4, 9/10, 11**

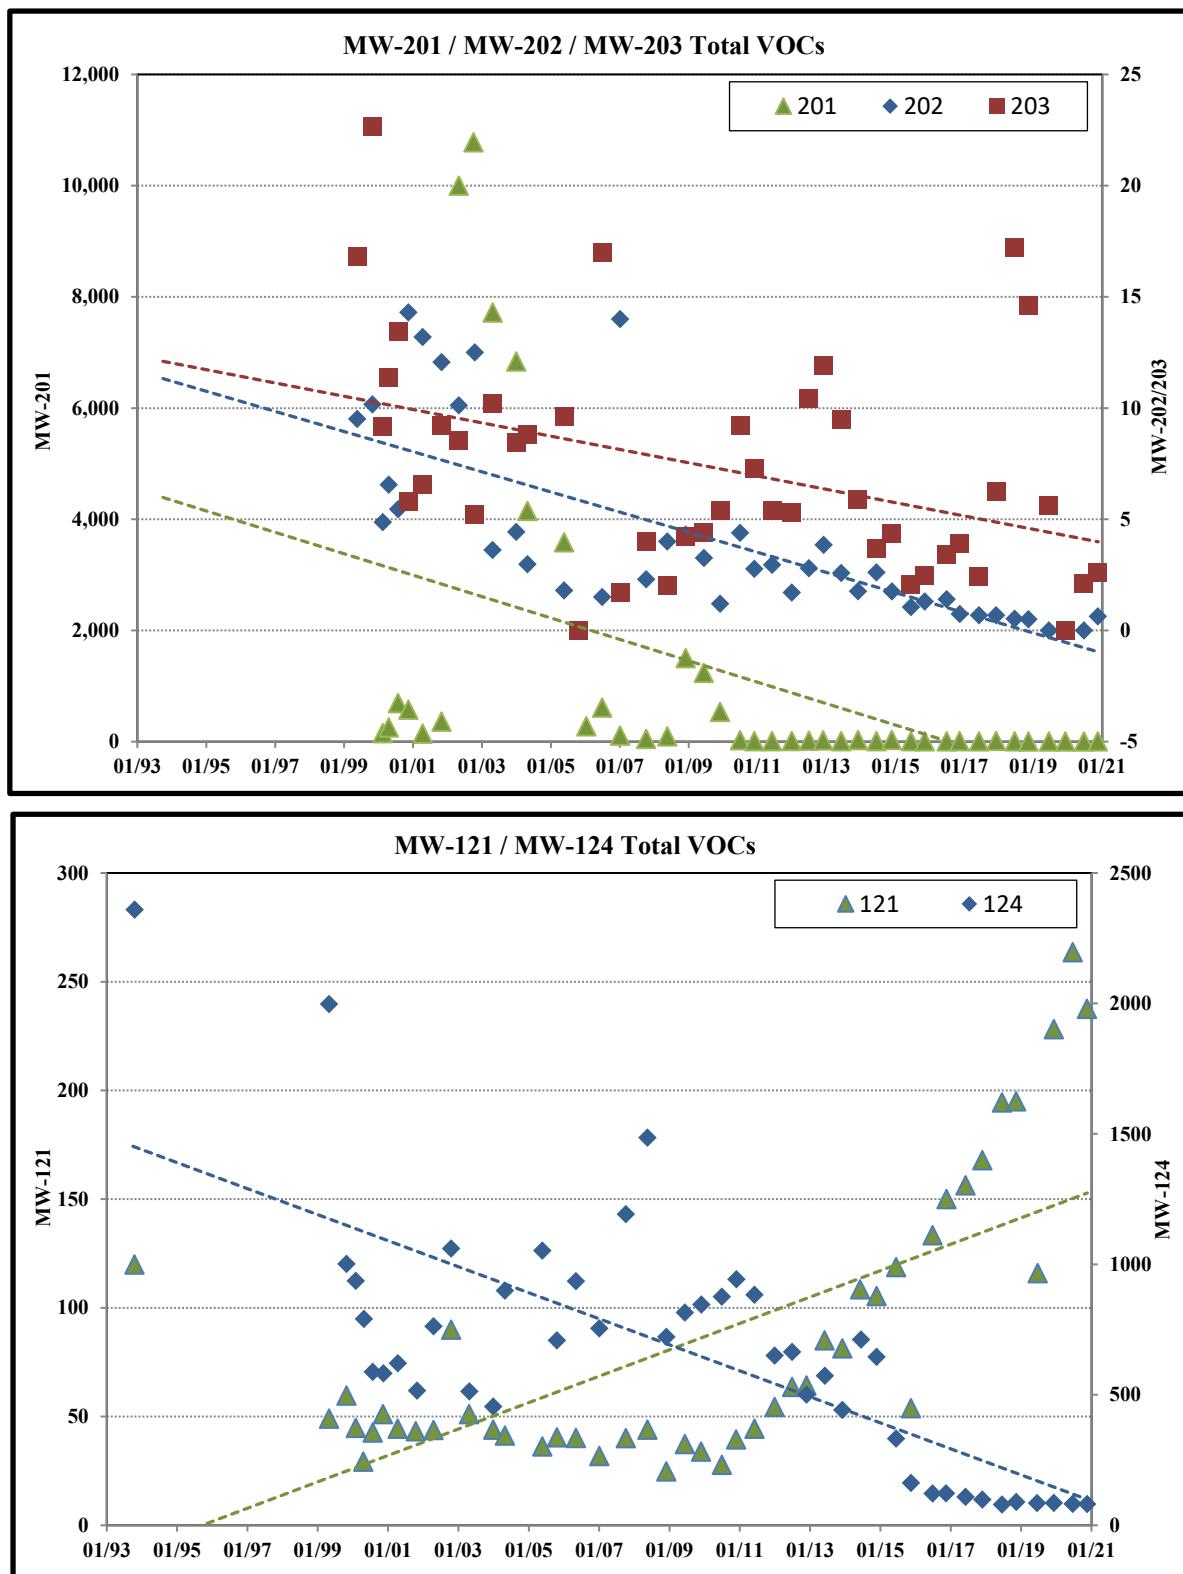


Y-axis = Total VOCs in micrograms per liter; X-axis = Sampling Date

**Figure 2 - Southeast Rockford Groundwater Contamination Site
Total Volatile Organic Compounds Concentration Trends
Monitoring Wells Near Rock River**

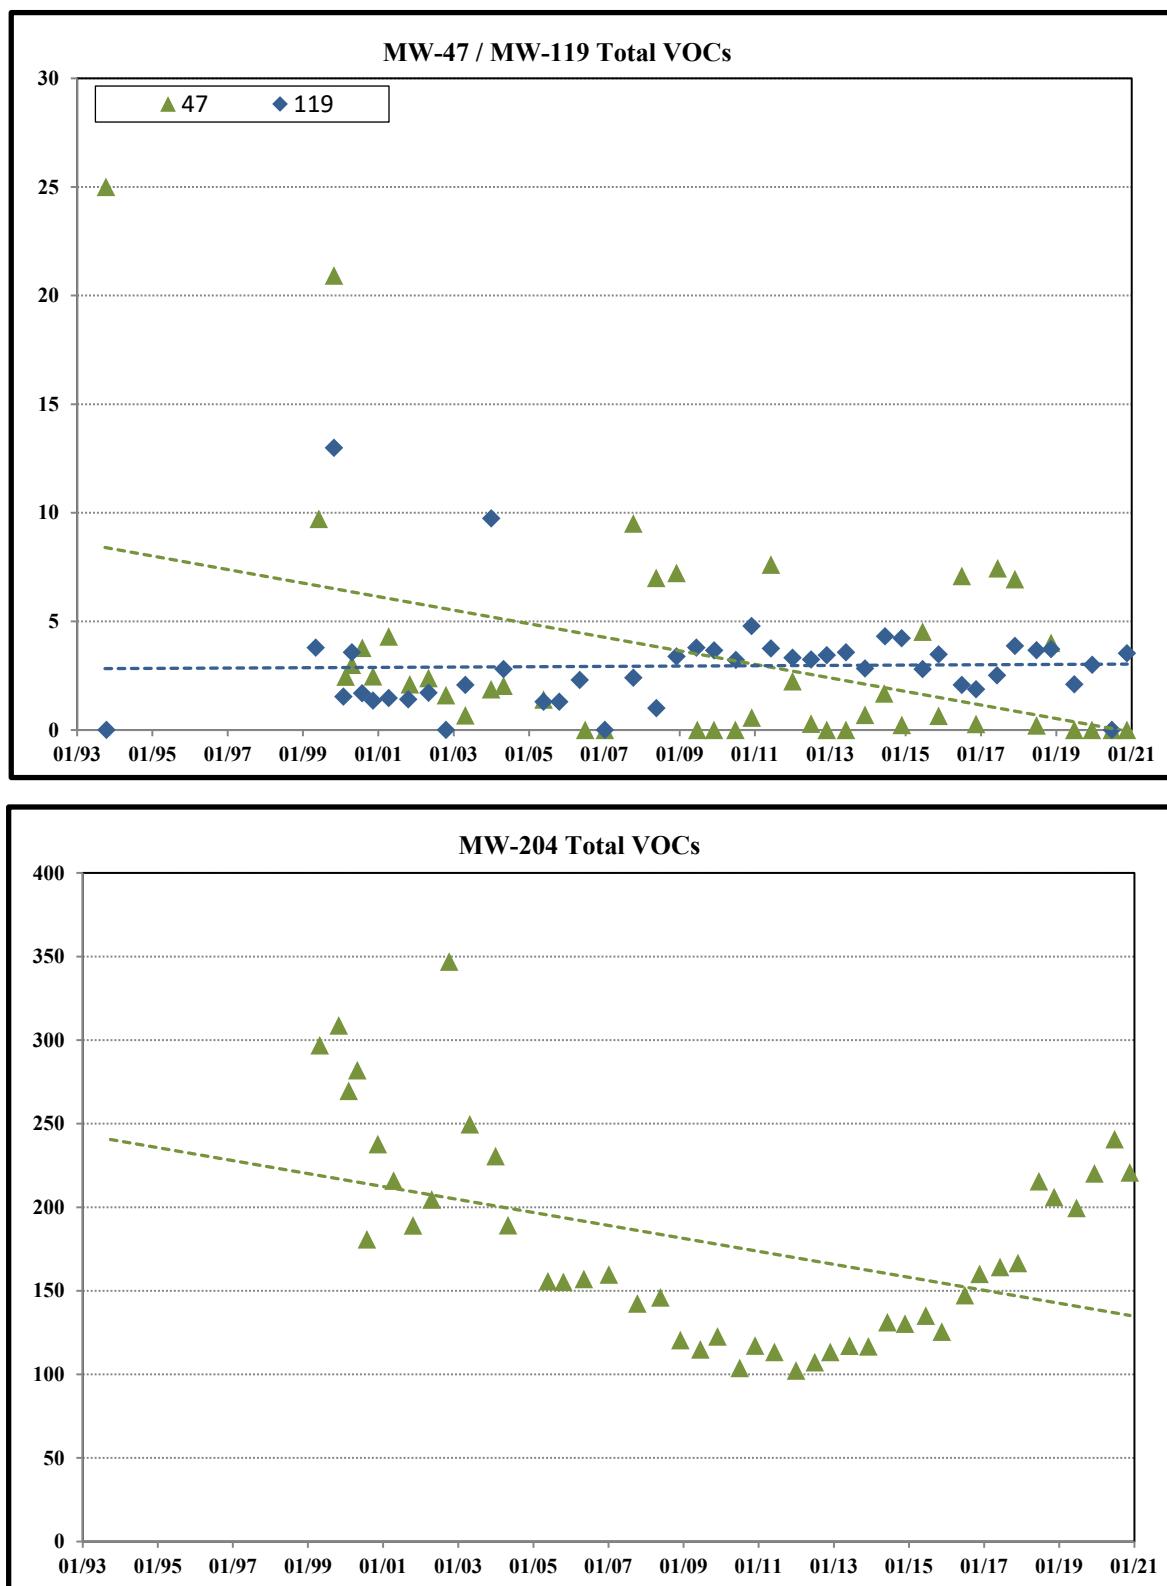

Y-axis = Total VOCs in micrograms per liter; X- axis = Sampling Date

**Figure 2 - Southeast Rockford Groundwater Contamination Site
Total Volatile Organic Compounds Concentration Trends
Monitoring Wells Near Rock River**

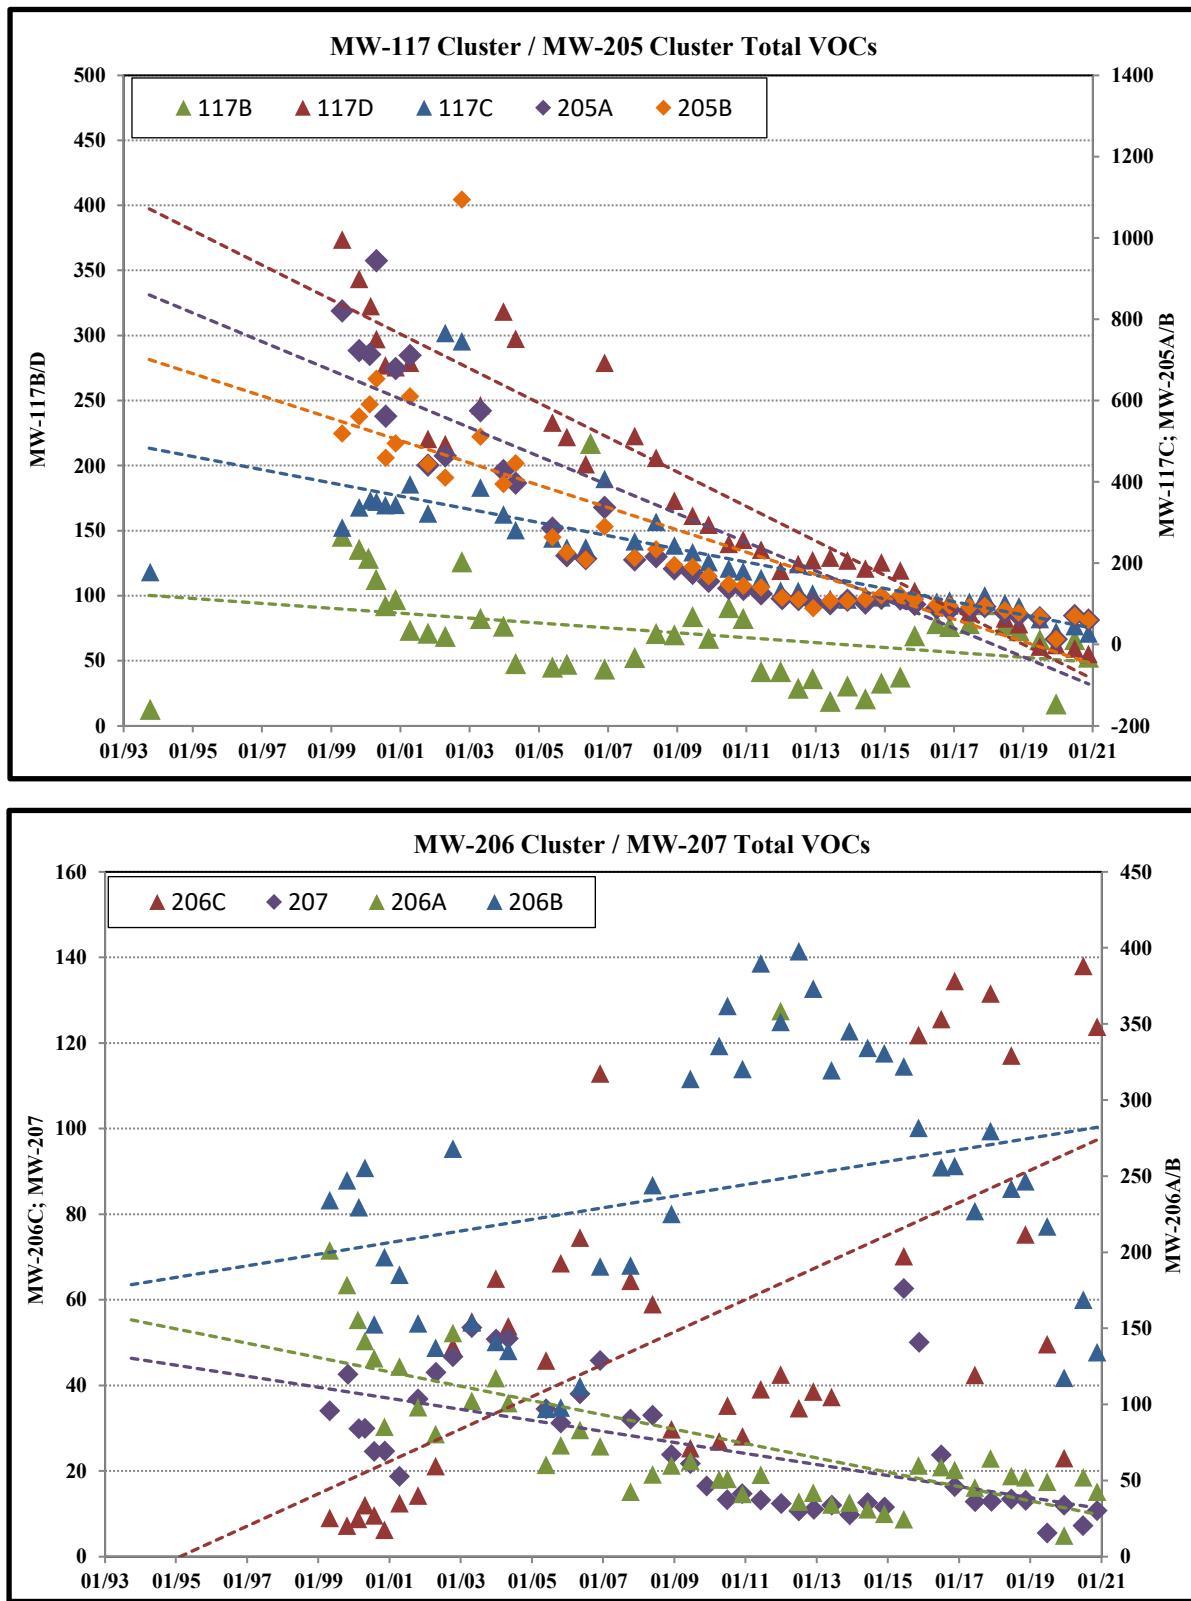

Y-axis = Total VOCs in micrograms per liter; X- axis = Sampling Date

TABLES

**Table 1a: Southeast Rockford Groundwater Contamination Site
Summary of Groundwater Analytical Results
Sampling Event # 44**

Well ID	Date	Sample Type	MCL	CFM NA	1,1-DCA NA	1,2-DCA 5	1,1-DCE 7	cl,2-DCE 70	tl,2-DCE 100	MC 5	PCE 5	1,1,1-TCA 200	TCE 5	VC 2	Total VOCs
MW-16	11/18/20		1 U	55.7	1 U	13.6	5.3	1.7	5 U	11.8	84.3	19.5	1 U	192	
MW-47	11/14/20		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	1 U	
MW-101A	11/16/20		2.9	43.7	1 U	8.4	26.1	1.8	5 U	6.6	91.4	11.4	1 U	192	
MW-101B	11/16/20		1 U	104	1 U	18.9	9.2	3.3	5 U	21.7	320	18.5	1 U	496	
MW-101C	11/16/20		1 U	72.2	1 U	12.9	6.8	2.3	5 U	12	267	8.8	1 U	382	
MW-101D	11/18/20		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	1 U	
MW-102A	11/16/20		1 U	23.8	1 U	1 U	27.3	1.8	5 U	1 U	12.6	5	1 U	71	
MW-102B	11/16/20		1 U	2.5	1 U	1 U	3.8	1 U	5 U	1 U	1 U	1 U	5.4	12	
MW-102C	11/16/20		1 U	113	1 U	20.3	46.5	2.8	5 U	3.8	141	10.3	2.3	340	
MW-113A	11/17/20		1 U	75.1	1 U	12.7	7.6	2	5 U	15.8	72.4	23.7	1 U	209	
MW-113B	11/17/20		1 U	57.3	1 U	11.5	27	1.4	5 U	4.2	10.3	16.9	2.6	131	
MW-114A	11/18/20		1 U	3.1	1 U	1.5	1.4	1 U	5 U	1 U	9.6	1 U	1 U	16	
MW-114B	11/18/20		1 U	1.7	1 U	1 U	1 U	1 U	5 U	1 U	1 U	2.2	1 U	4	
MW-114B	11/18/20	Fld Dup	1 U	1.6	1 U	1 U	0.86 J	1 U	5 U	1 U	1 U	2.1	1 U	5	
MW-117B	11/13/20		1 U	9.2	1 U	4.2	1 U	1 U	5 U	11.9	20.6	6.8	1 U	53	
MW-117C	11/13/20		1 U	11.7	1 U	2.1	0.9 J	1 U	5 U	3.4	6.9	2.2	1 U	27	
MW-117D	11/13/20		1 U	14.7	1 U	4.9	1 U	1 U	5 U	11.7	18.2	5.6	1 U	55	
MW-119	11/14/20		1 U	1.1	1 U	1 U	1 U	1 U	5 U	1 U	2	0.43 J	1 U	4	
MW-121	11/15/20		1 U	92.5	1 U	50.9	5.2	1	5 U	1.4	46.3	40.3	1 U	238	
MW-124	11/18/20		1 U	26	1 U	4.8	14.5	0.51 J	5 U	9	22.1	2.8	2	82	
MW-130	11/17/20		1 U	3.5	1 U	1 U	0.62 J	1 U	5 U	0.94 J	2.9	1 U	1 U	8	
MW-133A	11/18/20		1 U	1.9	1 U	1 U	1 U	1 U	5 U	1 U	3.9	1 U	1 U	6	

Table 1a: Southeast Rockford Groundwater Contamination Site
Summary of Groundwater Analytical Results
Sampling Event # 44

Well ID	Date	MCL	CFM NA	1,1-DCA NA	1,2-DCA 5	1,1-DCE 7	cl,2-DCE 70	t1,2-DCE 100	MC 5	PCE 5	1,1,1-TCA 200	TCE 5	VC 2	Total VOCs
MW-133B	11/18/20		1.4	71.3	1 U	35.8	23.2	2.8	5 U	42.7	203	19.6	1 U	400
MW-133C	11/18/20		2.2	33	1 U	26.5	31.6	1.2	5 U	17.5	69	42.4	1 U	223
MW-136	11/14/20		1.1	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	1
MW-200	11/17/20		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	
MW-201	11/15/20		1 U	1.1	1 U	1 U	1 U	1 U	5 U	1.6	1.1	0.37 J	1 U	4
MW-201	11/15/20	Fld Dupe	1 U	0.99 J	1 U	1 U	1 U	1 U	5 U	1.6	1.1	1 U	1 U	4
MW-202	11/15/20		1 U	1 U	1 U	1 U	1 U	1 U	5 U	0.63 J	1 U	1 U	1 U	1
MW-203	11/15/20		1 U	1 U	1 U	1 U	1 U	1 U	5 U	2.6	1 U	1 U	1 U	3
MW-204	11/17/20		1 U	55.7	1 U	36.3	15.8	0.75 J	5 U	2.7	34	75.5	1 U	221
MW-205A	11/13/20		1 U	18.2	1 U	5.1	1 J	1 U	5 U	12.9	16.9	6	1 U	60
MW-205B	11/13/20		1 U	18.2	1 U	5.6	0.93 J	1 U	5 U	12.6	16.8	6.2	1 U	60
MW-206A	11/13/20		1 U	9.4	1 U	3.3	1.4	1 U	5 U	7	15.4	5.5	0.52 J	43
MW-206B	11/13/20		1 U	23.4	1 U	23.9	20	1 U	5 U	21.2	28.3	17.5	1 U	134
MW-206C	11/13/20		1 U	34.5	1 U	11.5	46.5	1 U	5 U	0.49 J	1 U	7.6	23.2	124
MW-207	11/14/20		1 U	2.4	1 U	0.77 J	1 U	1 U	5 U	1.9	3.2	2.5	1 U	11

**Table 1a: Southeast Rockford Groundwater Contamination Site
Summary of Groundwater Analytical Results
Sampling Event # 44**

Results reported in micrograms per liter ($\mu\text{g/l}$)		
Highlighted results equal or exceed the Maximum Contaminant Level (MCL)		
CFM	Chloroform	
1,1-DCA	1,1-Dichloroethane	
1,2-DCA	1,2-Dichloroethane	
1,1-DCE	1,1-Dichloroethene	
cis-1,2-DCE	cis- 1,2-Dichloroethene	
trans-1,2-DCE	trans-1,2-Dichloroethene	
MC	Methylene Chloride	
PCE	Tetrachloroethene	
1,1,1-TCA	1,1,1-Trichloroethane	
TCE	Trichloroethene	
VC	Vinyl Chloride	
Total VOCs	Sum of Total Volatile Organic Compound Concentrations	
B	Concentration is less than the reporting limit but greater than the instrument detection limit.	
D	Reported concentration is based on an analysis requiring a secondary detection limit.	
E	The associated value exceeds the calibration range.	
J	The reported concentration is estimated.	
U	Analyte was not detected at or above the reporting limit.	
Field Duplicate	Field Duplicate	
Field Duplicate Dln	Field Duplicate Dilution	

**Table 1b: Southeast Rockford Groundwater Contamination Site
1,4-Dioxane Groundwater Analytical Results
Sampling Event # 44**

Well ID	Date	Sample Type	1,4-Dioxane
MW-16	11/18/20		20
MW-47	11/14/20		0.5 U
MW-101A	11/16/20		11
MW-101B	11/16/20		26
MW-101C	11/16/20		19
MW-101D	11/18/20		0.12 J
MW-102A	11/16/20		6.7
MW-102B	11/16/20		170
MW-102C	11/16/20		31
MW-113A	11/17/20		30
MW-113B	11/17/20		70
MW-114A	11/18/20		21
MW-114B	11/18/20		9.8
MW-114B	11/18/20	Fld Dupe	10
MW-117B	11/13/20		5.5
MW-117C	11/13/20		8.3
MW-117D	11/13/20		8.4
MW-119	11/14/20		4
MW-121	11/15/20		47
MW-124	11/18/20		5.3
MW-130	11/17/20		6.6
MW-133A	11/18/20		0.63
MW-133B	11/18/20		15
MW-133C	11/18/20		120
MW-136	11/14/20		0.5 U
MW-200	11/17/20		0.2 J
MW-201	11/15/20		0.89
MW-201	11/15/20	Fld Dupe	0.94
MW-202	11/15/20		0.5 U
MW-203	11/15/20		0.5 U
MW-204	11/17/20		25
MW-205A	11/13/20		7.7
MW-205B	11/13/20		7.5
MW-206A	11/13/20		5.5
MW-206B	11/13/20		26
MW-206C	11/13/20		52
MW-207	11/14/20		2.8

Results reported in micrograms per liter ($\mu\text{g/l}$)

J The reported concentration is estimated.

U Analyte was not detected at or above the reporting limit.

Fld Dupe Field Duplicate

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-16	06/01/99		3	76	1.2	24	140	1.8	2 U	5.4	170	64	1 U	485
MW-16	10/26/99		2.3 J	73	10 U	23	130	2.5 J	20 U	5.2 J	170	65	10 U	471
MW-16	01/31/00		2.3 J	75	10 U	2.2 J	120	16	20 U	5.9 J	170	68	10 U	459
MW-16	04/24/00		2.5 J	79	5 U	2 J	130 E	16	10 JB	5.7	170 E	65	5 U	480
MW-16	04/24/00	Dilution	50 DJB	75 D	50 U	50 U	130 D	17 DJ	100 DJB	5.3 DJ	160 D	62 D	2.8 DJ	602
MW-16	07/27/00		2.7	75	10 U	3.8	130	12	20 U	5.2	160	58	10 U	447
MW-16	11/13/00		2.2	87	10 U	20	150	2.8	20 U	5	140	55	10 U	462
MW-16	04/12/01		2.3	74	10 U	3.1	150	14	20 U	5.8	180	64	10 U	493
MW-16	10/31/01		2.5	88	10 U	10 U	160	22	20 U	7.1	210	72	10 U	562
MW-16	04/25/02		2.3	70	10 U	15	170	6.7	20 U	6.6	150	62	10 U	483
MW-16	10/15/02		20 U	130	20 U	98	240	22	40 U	20 U	240	91	1 U	821
MW-16	04/23/03	Dilution	20 U	75.6	20 U	24.6	200	20 U	40 U	20 U	172	75.3	20 U	548
MW-16	04/23/03		2.51	95.6 E	1.08	24.2	244 E	15.7	2 U	9.74	237 E	97.6 E	1 U	727
MW-16	12/26/03		2.48	93.9 E	1 U	32.2 E	209 E	13.9	1 U	9.45	208 E	77.8 E	1 U	647
MW-16	12/26/03	Dilution	10 U	93.9 D	10 U	31.7 D	247 D	10 U	10 U	9.14 JD	221 D	92.7 D	10 U	695
MW-16	12/26/03	Fld Dupe	2.55	96.3 E	10 U	34.5 E	230 E	10 U	10 U	7.88 JD	182 D	72.5 D	1 U	626
MW-16	04/28/04		20 U	100	20 U	30.1	254	20 U	40 U	20 U	202	77.3	20 U	663
MW-16	05/21/05		1.8	91	1 U	28	230	5.6	2 U	6.5	160	65	1 U	588
MW-16	10/20/05		1.8	91	1 U	28	230	5.6	2 U	6.5	160	65	1 U	588
MW-16	05/08/06		2	94	1 U	27	290	7.3	2 U	9.1	170	78	1 U	677
MW-16	01/04/07		5	94	5 U	24	280	5	10 U	5.3	160	63	5 U	636
MW-16	10/08/07		2	100	1	28	260	14	2 U	8	140	61	1 U	614
MW-16	05/17/08		20 U	130	20 U	39	320	20 U	40 U	20 U	170	78	20 U	737
MW-16	12/18/08	Dilution	1.3 J	100	1 J	2 U	240	35	0.7 J	4.6	120	56	2 U	559
MW-16	06/20/09	Dilution	1.6 J	110	2 U	2 U	39	6.8	2 U	5.5	170	42	2 U	375
MW-16	11/28/09	Dilution	1.6 J	110	2 U	7.9	56	6.9	0.88 J	6.1	180	55	2 U	424
MW-16	06/25/10		1.4	93	0.21 J	21	51	3.8	1 U	8.7	200	58	1 U	437
MW-16	11/27/10	Dilution	1.4 J	78	2 U	24	45	1.6 J	2 U	10	180	60	2 U	400
MW-16	06/01/11		1.2	81	1 U	19	40	3.2	1 U	11	160	54	1 U	369
MW-16	12/28/11		1.1	71	1 U	17	27	2.7	5 U	11	130	42	1 U	302
MW-16	06/28/12		1.1	72	1 U	5.2	25	3.3	5 U	11	120	41	1 U	279
MW-16	11/24/12		0.9 J	68	1 U	13	22	2.4	5 U	10	110	35	1 U	261
MW-16	06/07/13		0.89 J	75	1 U	19	21	2.5	5 U	12	120	37	1 U	287

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-16	12/19/13		0.8 J	73	1 U	17	18	2.2	5 U	9	93	30	1 U	243
MW-16	06/14/14		1	98	1 U	22	18	2.9	5 UB	11	120	36	1 U	309
MW-16	11/24/14		0.62 J	45	1 U	8.6	12	1.1	5 U	4.2	50	17	1 U	139
MW-16	06/13/15		0.74 J	73	1 U	14	13	2.1	5 U	5.4	75	23	1 U	206
MW-16	11/11/15		0.81 J	71	1 U	12	13	2.3	0.76 J	6.7	76	26	1 U	209
MW-16	06/28/16		0.43 J	33	1 U	2.8	9.4	0.67 J	5 U	2.3	26	10	1 U	85
MW-16	11/27/16		0.86 J	100	1 U	23	13	3.1	5 U	10	97	33	1 U	280
MW-16	06/05/17		0.79 J	93	1 U	22	11	2.8	5 U	9.5	89	28	1 U	256
MW-16	11/24/17		0.84 J	83.6	1 U	22.3	10.2	2.9	1 U	9	97.5	28.7	1 U	255
MW-16	06/21/18		0.82 J	88.4	1 U	15.9	11	2.7	1 U	10.7	116	31.6	1 U	277
MW-16	11/10/18		1 U	70.9	1 U	16	8.9	2.3	1 U	11.1	111	27.3	1 U	248
MW-16	06/22/19		1 U	63.2	1 U	15.9	7.5	2.1	5 U	10.1	90	23.8	1 U	213
MW-16	12/14/19		1	84.1	1 U	17.3	8.1	2.3	5 U	11.2	118	24.5	1 U	267
MW-16	06/25/20		0.76 J	66.1	1 U	16	6.6	2.2	5 U	11.8	99.9	22.2	1 U	226
MW-16	11/18/20		1 U	55.7	1 U	13.6	5.3	1.7	5 U	11.8	84.3	19.5	1 U	192
MW-47	10/06/93		1 U	5	1 U	2	3	1 U	2 U	1	9	5		25
MW-47	06/01/99		1 U	1.1	1 U	0.49	1.3	1 U	2 U	0.53	3.5	2.8	1 U	10
MW-47	10/27/99		1 U	1.1	1 U	0.87 J	4.5	0.05 J	2 U	2.2	6.5	5.7	1 U	21
MW-47	02/17/00		1 U	0.32 J	1 U	0.1 J	0.18 J	1 U	2 U	0.27 J	1	0.58 J	1 U	2
MW-47	04/18/00		1 U	0.53 J	1 U	0.18 J	0.36 J	1 U	2 U	0.27 J	1	0.66 J	1 U	3
MW-47	07/27/00		1 U	0.61	1 U	0.13	0.38	1 U	2 U	0.64	1.2	0.82	1 U	4
MW-47	11/08/00		0.17	0.55	1 U	0.1	0.25	1 U	2 U	0.45	0.58	0.37	1 U	2
MW-47	04/10/01		0.28	0.57	1 U	1	0.31	1 U	2 U	0.48	1.1	0.56	1 U	4
MW-47	10/31/01		0.92	0.21	1 U	1 U	1 U	1 U	2 U	0.38	0.34	0.25	1 U	2
MW-47	04/30/02		1.3	0.13	1 U	1 U	0.13	1 U	2 U	0.33	0.23	0.27	1 U	2
MW-47	10/17/02		1	1 U	1 U	1 U	1 U	1 U	0.6	1 U	1 U	1 U	1 U	2
MW-47	04/22/03		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	0.67 J	1 U	1 U	1
MW-47	12/28/03		1 U	1 U	1 U	0.51 J	1 U	1 U	1 U	0.77 J	0.59 J	1 U	1 U	2
MW-47	04/28/04		1 U	0.54	1 U	1 U	1 U	1 U	2 U	1 U	0.91	0.58	1 U	2
MW-47	05/21/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1.4	1 U	1 U	1
MW-47	06/28/06		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-47	01/05/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-47	10/08/07		1 U	2	1 U	0.9	2	1 U	2 U	0.6	3	1	1 U	10

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-47	05/17/08		1 U	1	1 U	1 U	1	1 U	2 U	1 U	4	1	1 U	7
MW-47	11/29/08		1 U	1.6	1 U	1 U	0.93 J	1 U	1 U	0.62 J	2.91	1.17	1 U	7
MW-47	11/29/08	Fld Dupe	0.15 J	1.58	1 U	0.34 J	0.96 J	1 U	1 U	0.61 J	2.89	1.15	1 U	8
MW-47	06/20/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	0
MW-47	11/28/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	0
MW-47	06/24/10		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	0
MW-47	11/29/10		1 U	0.27 J	1 U	1 U	1 U	1 U	1 U	1 U	0.3 J	1 U	1 U	1
MW-47	06/03/11		1 U	2	1 U	0.68 J	0.7 J	1 U	1 U	0.33 J	2.7	1.2	1 U	8
MW-47	12/29/11		1 U	0.35 J	1 U	1 U	1 U	1 U	5 U	0.4 J	0.85 J	0.64 J	1 U	2
MW-47	06/26/12		1 U	1 U	1 U	1 U	1 U	1 U	5 U	0.29 J	1 U	1 U	1 U	0
MW-47	11/25/12		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-47	05/31/13		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-47	12/01/13		1 U	0.35 J	1 U	1 U	1 U	1 U	5 U	1 U	0.34 J	1 U	1 U	1
MW-47	06/05/14		1 U	0.31 J	1 U	1 U	1 U	1 U	5 U	0.41 J	0.61 J	0.35 J	1 U	2
MW-47	06/05/14	Fld Dupe	1 U	0.29 J	1 U	1 U	1 U	1 U	5 U	0.35 J	0.57 J	0.35 J	1 U	2
MW-47	11/23/14		1 U	0.23 J	1 U	1 U	1 U	1 U	5 U	1 UB	1 U	1 U	1 U	0
MW-47	06/13/15		1 U	2.2	1 U	0.53 J	0.23 J	1 U	5 U	0.23 J	1.1	0.23 J	1 U	5
MW-47	11/15/15		1 U	1 U	1 U	1 U	1 U	1 U	0.45 J	0.2 J	1 U	1 U	1 U	1
MW-47	11/15/15	Fld Dupe	1 U	1 U	1 U	1 U	1 U	1 U	0.64 J	0.17 J	1 U	1 U	1 U	1
MW-47	06/27/16		1 U	2.7	1 U	0.89 J	0.34 J	1 U	5 U	1 U	2.5	0.66 J	1 U	7
MW-47	11/12/16		1 U	0.27 J	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-47	06/10/17		1 U	2.7	1 U	0.82 J	0.43 J	1 U	5 U	1 U	2.6	0.89 J	1 U	7
MW-47	11/24/17		1 U	2.5	1 U	0.84 J	0.41 J	1 U	1 U	1 U	2.3	0.89 J	1 U	7
MW-47	06/21/18		1 U	0.21 J	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	0
MW-47	11/10/18		1 U	1.5	1 U	0.38 J	1 U	1 U	1 U	1 U	1.4	0.73 J	1 U	4
MW-47	06/23/19		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-47	12/10/19		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-47	06/22/20		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-47	11/14/20		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-101A	10/04/93		4	150	17 U	43	190		17 U	17 U	650	180		1217
MW-101A	04/20/99		7.3	230	3.4	63	540	9.3	2 U	16	580	200	1 U	1649
MW-101A	10/25/99		5.6 J	240	50 U	64	620	7 J	100 U	14 J	610	220	50 U	1781

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-101A	01/27/00		6.2 J	270	50 U	61	690	40 J	100 U	15 J	740	270	50 U	2092
MW-101A	04/25/00		7 JB	240	50 U	65	720	7.8 J	100 JB	50 U	690	220	50 U	2050
MW-101A	07/26/00		6.1	210	20 U	51	730	10	40 U	4.4	620	140	20 U	1772
MW-101A	11/16/00		6.3	310	50 U	77	830	8.3	100 U	15	740	250	50 U	2237
MW-101A	04/13/01		5.6	240	50 U	81	780	8.6	100 U	14	830	270	50 U	2229
MW-101A	10/30/01		6.3	300	50 U	79	990	12	100 U	15	1000	300	50 U	2702
MW-101A	04/22/02		6.8	250	50 U	82	1000	11	100 U	18	890	280	50 U	2538
MW-101A	10/10/02		100 U	370	100 U	440	1200	100 U	200 U	64	1200	340	1 U	3614
MW-101A	04/23/03		6.28	320 E	1 U	125 E	1080 E	19.4	2 U	26.8 E	919 E	427 E	1 U	2923
MW-101A	04/23/03	Dilution	100 U	266	100 U	81.8 J	1110	100 U	200 U	100 U	909	309	100 U	2676
MW-101A	12/26/03		8.18	313 E	3.83	128 E	1080 E	21.8	1 U	51.7 E	796 E	344 E	1 U	2747
MW-101A	12/26/03	Dilution	100 U	268 D	100 U	101 D	1260 D	100 U	100 U	100 U	950 D	278 D	100 U	2857
MW-101A	04/28/04		100 U	265	100 U	98.1	1230	100 U	200 U	56.4	1040	302	100 U	2992
MW-101A	05/21/05		10 U	260	10 U	89	1100	13	20 U	80	850	250	10 U	2642
MW-101A	01/12/06		4.5	220	5 U	37	990	44	10 U	61	800	220	5 U	2377
MW-101A	05/08/06		4.4	25 U	1 U	76	1100	17	2 U	93	970	270	1 U	2530
MW-101A	01/04/07		10 U	180	10 U	48	840	21	20 U	56	820	190	10 U	2155
MW-101A	10/07/07		4	220	2	38	790	72	2 U	67	590	200	1 U	1983
MW-101A	05/17/08		50 U	260	50 U	100	1000	50 U	100	64	740	240	50 U	2504
MW-101A	11/28/08	Dilution	4.1 J	233	2.15 J	57.5	908	38.4	1.8 J	56.2	691	214	5 U	2206
MW-101A	06/10/09	Dilution	4.3 J	230	2 J	50	870	30	5 U	56	550	190	5 U	1982
MW-101A	11/27/09	Dilution	5.2 J	280	10 U	70	990	36	10 U	47	550	220	10 U	2198
MW-101A	06/28/10	Dilution	2 U	54	2 U	15	210	6	2 U	6.8	90	38	2 U	420
MW-101A	06/28/10	Fld Dupe	2 U	51	2 U	14	200	5.3	2 U	6.3	86	37	2 U	400
MW-101A	11/26/10	Dilution	3.2 J	280	10 U	68	1100	18	10 U	36	550	230	10 U	2285
MW-101A	05/31/11	Dilution	4.5 J	310	10 U	46	1200	75	10 U	36	510	190	10 U	2372
MW-101A	12/28/11	Dilution	4.3 J	290	2.8 J	62	1200	49	50 U	52	540	180	10 U	2380
MW-101A	12/28/11	Fld Dupe	4.3 J	290	10 U	64	1200	52	50 U	52	540	180	10 U	2382
MW-101A	06/25/12	Dilution	5.2 J	320	10 U	72	1600	66	2.7 J	56	650	190	10 U	2962
MW-101A	11/24/12	Dilution	3.4 J	240	10 U	39	1200	57	50 U	55	500	160	10 U	2254
MW-101A	06/04/13	Dilution	10 U	260	10 U	61	730	14	15 J	56	500	150	10 U	1786
MW-101A	06/04/13	Fld Dupe	3.1 J	270	5 U	66	750	16	8.3 J	58	540	160	5 U	1871
MW-101A	11/30/13	Dilution	3 J	260	5 U	70	610	14	25 UB	67	570	160	5 U	1754
MW-101A	06/14/14	Dilution	3.2 J	300	5 U	58	510	23	25 UB	72	620	150	5 U	1736

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-101A	11/24/14	Dilution	3.6 J	270	5 U	64	520	25	25 U	71	670	150	5 U	1774
MW-101A	11/24/14	Fld Dupe	3.5 J	270	5 U	50	510	35	25 U	71	670	150	5 U	1760
MW-101A	06/07/15	Dilution	3.4 J	280	0.9 J	65	420	16	25 UB	70	710	150	5 U	1715
MW-101A	11/10/15	Dilution	2.8 J	240	5 U	54	330	23	25 U	67	650	130	5 U	1497
MW-101A	06/28/16		5.5	28	1 U	5.8	25	1.6	0.48 J	6.7	75	12	1 U	160
MW-101A	11/27/16	Dilution	2.8 J	240	5 U	61	210	11	25 UB	62	660	110	5 U	1357
MW-101A	06/04/17		1.4	1.9	1 U	1 U	0.57 J	1 U	5 U	1.1	4.7	0.95 J	1 U	11
MW-101A	11/17/17		3.8	3.7	1 U	1 U	0.75 J	1 U	1 U	0.82 J	5	0.66 J	1 U	15
MW-101A	06/20/18		0.94 J	3.4	1 U	0.29 J	0.68 J	1 U	1 U	1.3	5.3	0.89 J	1 U	13
MW-101A	11/11/18		2.7	6.9	1 U	0.35 J	1.2	1 U	1 U	1	6.5	0.58 J	1 U	19
MW-101A	06/15/19	Fld Dupe	0.75 J	7.5	1 U	0.51 J	0.95 J	1 U	5 U	0.72 J	6.3	0.55 J	1 U	17
MW-101A	06/15/19		0.75 J	7.4	1 U	0.57 J	1	1 U	5 U	0.76 J	6.5	0.56 J	1 U	18
MW-101A	12/13/19		1 U	16.2	1 U	1 U	2.2	1 U	5 U	1 U	20.1	1 U	1 U	39
MW-101A	06/24/20		0.53 J	19.6	1 U	2.2	4.5	0.65 J	5 U	1.4	23.7	2.5	1 U	55
MW-101A	11/16/20		2.9	43.7	1 U	8.4	26.1	1.8	5 U	6.6	91.4	11.4	1 U	192
MW-101B	10/04/93		5	140	25 U	42	190		25 U	84	560	180		1201
MW-101B	04/20/99		3.6	150	10 U	36	520	10 U	20 U	45	690	140	10 U	1585
MW-101B	10/25/99		3.6 J	140	25 U	38	430	3.2 J	50 U	47	580	150	25 U	1392
MW-101B	01/27/00		50 U	140	50 U	33 J	490	50 U	100 U	42 J	570	150	50 U	1425
MW-101B	04/25/00		4.5 J	150	50 U	37 J	510	5.2 J	100 JB	33 J	590	140	50 U	1570
MW-101B	07/26/00		4.4	150	20 U	41	700	4	40 U	39	750	140	20 U	1828
MW-101B	11/16/00		3.3	170	25 U	35	550	3.9	50 U	18	450	120	25 U	1350
MW-101B	04/13/01		50 U	140	50 U	42	570	50 U	100 U	39	620	160	50 U	1571
MW-101B	10/30/01		3.5	150	25 U	33	580	4	50 U	21	440	140	25 U	1372
MW-101B	04/22/02		4.4	140	50 U	37	630	4.4	3.3	48	580	140	50 U	1587
MW-101B	10/10/02		50 U	230	50 U	290	850	50 U	100 U	80	840	180	1 U	2470
MW-101B	04/23/03		3.62	202 E	1 U	66 E	891 E	11.7	2 U	67.1 E	753 E	206 E	1 U	2200
MW-101B	04/23/03	Dilution	50 U	162	50 U	45 J	795	50 U	100 U	50.7	656	160	50 U	1869
MW-101B	12/26/03		4.11	222 E	1 U	70.1 E	893 E	13	1 U	68 E	671 E	180 E	1 U	2121
MW-101B	12/26/03	Dilution	100 U	188 D	100 U	100 U	963 D	100 U	100 U	100 U	696 D	148 D	100 U	1995
MW-101B	04/28/04		50 U	226	50 U	59.4	1140	50 U	100 U	61.8	843	174	50 U	2504
MW-101B	05/21/05		10 U	200	10 U	50	920	10 U	20 U	47	610	130	10 U	1957

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-101B	01/12/06		5 U	200	5 U	42	890	6.3	10 U	41	570	120	5 U	1869
MW-101B	05/08/06		10 U	230	10 U	52	1100	10 U	20 U	50	660	130	1 U	2222
MW-101B	01/04/07		10 U	210	10 U	46	950	10 U	20 U	46	620	120	10 U	1992
MW-101B	10/07/07		2	200	2	47	790	12	2 U	44	460	110	1 U	1667
MW-101B	05/17/08		50 U	240	50 U	64	960	50 U	100	52	560	130	50 U	2106
MW-101B	11/28/08	Dilution	2.4 J	181	1.75 J	36.2	760	7.45	1.35 J	41.1	438	96.3	5 U	1566
MW-101B	06/10/09	Dilution	3.1 J	160	1.8 J	31	750	7.1	5 U	36	390	81	5 U	1460
MW-101B	11/27/09	Dilution	2.6 J	170	5 U	37	840	8.4	5 U	37	400	81	5 U	1576
MW-101B	06/28/10	Dilution	10 U	130	10 U	35	790	9 J	10 U	32	320	70	10 U	1386
MW-101B	11/26/10	Dilution	10 U	130	10 U	36	850	10 U	10 U	32	430	77	10 U	1555
MW-101B	05/31/11	Dilution	5 U	140	5 U	32	910	6.2	5 U	30	420	63	5 U	1601
MW-101B	12/28/11	Dilution	1.7 J	120	0.86 J	26	270	5.5	10 U	25	380	40	2 U	869
MW-101B	06/25/12	Dilution	1.9 J	120	5 U	25	47	4.3 J	25 U	24	430	27	5 U	679
MW-101B	11/24/12	Dilution	1.4 J	120	2.5 U	26	33	4.1	0.88 J	25	430	26	2.5 U	666
MW-101B	06/04/13	Dilution	1.4 J	140	5 U	27	37	4.8 J	7.4 J	24	520	27	5 U	789
MW-101B	11/30/13	Dilution	1.6 J	130	5 U	28	32	4.1 J	25 UB	28	490	27	5 U	741
MW-101B	06/14/14	Dilution	1.8 J	170	5 U	30	33	5.8	25 UB	30	560	29	5 U	860
MW-101B	11/24/14	Dilution	1.9 J	150	5 U	30	26	5.3	25 U	31	530	30	5 U	804
MW-101B	06/07/15	Dilution	1.8 J	180	5 U	28	26	5.6	25 UB	29	520	30	5 U	820
MW-101B	11/10/15	Fld Dupe	1.4 J	160	5 U	29	22	5.6	25 U	30	520	28	5 U	796
MW-101B	11/10/15	Dilution	5 U	160	5 U	28	22	5.8	1.2 J	28	500	28	5 U	773
MW-101B	06/28/16	Dilution	5 U	140	5 U	27	19	4.4 J	25 U	26	430	24	5 U	670
MW-101B	11/27/16	Dilution	1.2 J	130	5 U	23	20	4.4 J	25 U	26	420	25	5 U	650
MW-101B	06/04/17	Dilution	5 U	130	5 U	22	13	4.2 J	25 UB	23	380	20	5 U	592
MW-101B	11/17/17	Dilution	5 U	143	5 U	23	15.8	4 J	5 U	24.5	408 J	23.7	5 U	642
MW-101B	11/17/17	Fld Dupe	5 U	131	5 U	22.6	14.8	4 J	5 U	22.3	378	20.4	5 U	593
MW-101B	06/20/18	Dilution	1.2 J	140	5 U	25.1	13.1	4.1 J	7.2	24.6	416 J	21.2	5 U	653
MW-101B	06/20/18	Fld Dupe	5 U	138	5 U	23.7	13.1	4.1 J	9	23.6	400 J	20.9	5 U	632
MW-101B	11/11/18	Dilution	5 U	109	5 U	19.2	11.7	3.3 J	5 U	23.6	352	18.7	5 U	538
MW-101B	06/15/19		0.83 J	114	1 U	20.4	11	3.5	5 U	21.6	321	16.7	1 U	509
MW-101B	12/13/19	Fld Dupe	1 U	117	1 U	20.4	10.7	3.5	5 U	21.8	372	17.9	1 U	563
MW-101B	12/13/19		1 U	112	1 U	19.3	10.7	3.3	5 U	20.9	379	17	1 U	562
MW-101B	06/24/20	Dilution	10 U	124	10 U	18.2	9.7 J	10 U	50 U	20.4	329	17	10 U	518
MW-101B	06/24/20	Fld Dupe	0.87 J	149	1 U	25.1	12.1	4.5	5 U	25.2	328	21.5	1 U	566

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-101B	11/16/20		1 U	104	1 U	18.9	9.2	3.3	5 U	21.7	320	18.5	1 U	496
MW-101C	10/06/93		100 U	140	100 U	59	210	100	100 U	72	650	190		1421
MW-101C	04/20/99		3.5	140	10 U	34	550	10 U	20 U	45	740	140	10 U	1653
MW-101C	10/25/99		3 J	110	25 U	31	380	2.5 J	50 U	42	480	130	25 U	1179
MW-101C	01/27/00		20 U	110	20 U	28	370	2.8 J	40 U	42	460	120	20 U	1133
MW-101C	04/25/00		3.9 J	120	50 U	28 J	420	3.5 J	100 JB	31 J	450	100	50 U	1256
MW-101C	07/26/00		3.6	110	20 U	25	390	2.7	40 U	21	390	82	20 U	1024
MW-101C	11/13/00		2.6	130	25 U	24	420	2.7	50 U	34	370	100	25 U	1083
MW-101C	04/12/01		2.5	100	25 U	27	420	3	50 U	37	450	110	25 U	1150
MW-101C	10/30/01		2.9	120	25 U	21	510	11	50 U	32	470	110	25 U	1277
MW-101C	04/22/02		3.2	120	25 U	31	570	4.2	50 U	41	490	120	25 U	1379
MW-101C	10/10/02		50 U	200	50 U	200	660	50 U	28	150	650	130	1 U	2018
MW-101C	04/23/03	Dilution	50 U	125	50 U	35.8 J	626	50 U	100 U	36.7 J	489	121	50 U	1434
MW-101C	04/23/03		3	157 E	1 U	44.3 E	750 E	12.1	2 U	42 E	602 E	152 E	1 U	1762
MW-101C	12/30/03		3.64	193 E	1 U	57.2 E	782 E	32.5 E	1 U	63.2 E	644 E	175 E	1 U	1951
MW-101C	12/30/03	Dilution	50 U	141 D	50 U	42.4 JD	775 D	50 U	50 U	44.7 JD	628 D	142 D	50 U	1773
MW-101C	11/26/08	Dilution	2.45 J	157	2.05 J	33.8	682	6.8	1.5 J	27.9	398	86.4	5 U	1398
MW-101C	06/10/09	Dilution	2.6 J	120	5 U	22	550	5.8	5 U	24	270	56	5 U	1050
MW-101C	11/27/09	Dilution	2.4 J	120	5 U	28	620	5.5	5 U	25	290	63	5 U	1154
MW-101C	06/28/10	Dilution	5 U	85	5 U	23	570	5.4	5 U	19	220	44	5 U	966
MW-101C	11/26/10	Dilution	1.9 J	98	1.8 J	24	640	5 U	5 U	20	310	48	5 U	1144
MW-101C	05/31/11	Dilution	5 U	110	5 U	25	780	5.4	5 U	21	340	47	5 U	1328
MW-101C	12/28/11	Dilution	1.4 J	92	2 U	20	260	4	10 U	18	290	29	2 U	714
MW-101C	06/25/12	Dilution	1.4 J	89	2.5 U	17	89	3.3	12 U	16	300	20	2.5 U	536
MW-101C	11/30/12	Dilution	1.3 J	99	2.5 U	20	40	3.6	12 U	18	360	20	2.5 U	562
MW-101C	11/30/12	Fld Dupe	1.4 J	99	5 U	20	40	3.6 J	25 U	18	360	20	5 U	562
MW-101C	06/04/13	Dilution	1.6 J	130	2.5 U	24	40	4.1	7.1 J	22	480	22	2.5 U	731
MW-101C	11/30/13	Dilution	5 U	110	5 U	22	30	3.6 J	25 UB	21	400	19	5 U	606
MW-101C	06/14/14	Dilution	1.5 J	150	2.5 U	25	32	4.5	12 UB	26	500	20	2.5 U	759
MW-101C	11/24/14	Dilution	1.7 J	120	5 U	25	27	4.4 J	25 U	25	430	20	5 U	653
MW-101C	11/10/15	Dilution	1.3 J	130	5 U	22	19	4.2 J	1.4 J	22	410	16	5 U	626
MW-101C	06/28/16	Dilution	0.88 J	100	2.5 U	19	17	3.2	12 U	18	300	14	1.8 J	474

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-101C	11/28/16	Dilution	1 J	110	2.5 U	18	15	3.6	12 UB	18	320	14	2.5 U	500
MW-101C	06/05/17	Dilution	0.85 J	100	2.5 U	17	11	3.2	12 UB	17	280	12	2.5 U	441
MW-101C	11/17/17	Dilution	0.75 J	92.1	2.5 U	15.2	10.5	2.7	2.5 U	14.6	256	10.6	2.5 U	402
MW-101C	06/20/18	Dilution	0.98 J	121	2 U	19.4	12.3	3.8	3.2	17.5	339	12.9	2 U	530
MW-101C	11/12/18	Fld Dupe	2.5 U	83.6	2.5 U	14.8	9.2	2.8	2.5 U	16.7	273	10.7	2.5 U	411
MW-101C	11/12/18	Dilution	2 U	78.5	2 U	13.4	8.3	2.7	2 U	15.1	255	9.8	2 U	383
MW-101C	06/24/19		1 U	65.1	1 U	12.3	6.7	2.2	5 U	12.8	222	8.7	1 U	330
MW-101C	12/13/19		1 U	70.6	1 U	12.8	6.9	1 U	5 U	12.1	225	8.2	1 U	336
MW-101C	06/24/20		0.61 J	90.3	1 U	16.6	7.7	2.6	5 U	14.3	280	10.1	1 U	422
MW-101C	11/16/20		1 U	72.2	1 U	12.9	6.8	2.3	5 U	12	267	8.8	1 U	382
MW-101D	10/06/93		50 U	72	50 U	34	130	50	50 U	31	300	96		713
MW-101D	04/21/99		2.6	80	5 U	24	230	5 U	10 U	23	300	80	5 U	740
MW-101D	01/27/00		1.6 J	42	10 U	14	130	1.5 J	20	18	180	54	10 U	461
MW-101D	04/25/00		2.4 JB	70	20 U	23	250	1.9 J	40 JB	23	270	81	20 U	761
MW-101D	07/26/00		2.5	60	1.2	14	180	1.1	20 U	2.9	180	33	10 U	475
MW-101D	11/16/00		2.2	76	1.3	17	210	1.3	20 U	3.8	180	46	10 U	538
MW-101D	04/13/01		2.2	66	10 U	21	250	1.9	20 U	18	250	73	10 U	682
MW-101D	10/30/01		2.3	70	20 U	22	260	2	40 U	26	300	80	20 U	762
MW-101D	04/30/02		2.5	66	20 U	22	260	2	40 U	20	240	67	20 U	680
MW-101D	10/10/02		20 U	100	20 U	94	280	20 U	40 U	20 U	300	58	1 U	832
MW-101D	04/23/03	Dilution	20 U	64.7	20 U	23.9	291	20 U	40 U	23	254	73.7	20 U	730
MW-101D	04/23/03		2.17	72.1 E	1 U	28.2 E	323 E	5.34	2 U	24.8	297 E	82.6 E	1 U	835
MW-101D	04/23/03	Fld Dupe	3	127	1 U	35.6 J	744 E	9.63	100 U	40.7 E	500	122	50 U	1582
MW-101D	12/28/03		1.87	47 E	0.88 J	19.8	184 E	8.27	1 U	19.2	202 E	58.3 E	1 U	541
MW-101D	12/28/03	Dilution	10 U	41.8 D	10 U	17.6 D	179 D	10 U	10 U	16 D	168 D	51.6 D	10 U	474
MW-101D	04/28/04		25 U	68	25 U	22.2	323	25 U	50 U	20.7	249	62.3	25 U	745
MW-101D	05/21/05		2	74	1 U	28	330	1 U	2 U	22	230	61	1 U	747
MW-101D	01/12/06		2 U	53	2 U	5	85	2 U	4 U	14	190	20	2 U	367
MW-101D	06/23/06		10 U	77	10 U	24	410	10 U	20 U	20	220	56	10 U	807
MW-101D	01/04/07		5	56	5 U	16	200	5 U	10 U	15	180	46	5 U	518
MW-101D	10/07/07		10 U	55	10 U	22	240	10 U	10 U	18	180	50	10 U	565
MW-101D	05/17/08		10 U	98	10 U	35	420 E	10 U	18 J	26	250 E	70	10 U	917
MW-101D	05/17/08	Dilution	25 U	81 D	25 U	28 D	380 D	25 U	50 U	25 U	220 D	60 D	25 U	769

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-101D	11/28/08	Dilution	1.46 J	41.6	0.58 J	15	199	1.94 J	0.62 J	16.4	137	39.3	2 U	453
MW-101D	06/10/09	Dilution	1.8 J	68	0.86 J	19	340	3.6	2 U	20	180	47	2 U	680
MW-101D	11/27/09	Dilution	1.5 J	64	2.5 U	18	290	4.1	2.5 U	16	150	39	2.5 U	583
MW-101D	06/28/10	Dilution	2.5 U	44	2.5 U	16	270	3.1	2.5 U	13	110	32	2.5 U	488
MW-101D	11/26/10	Dilution	1.4 J	51	1 J	18	320	0.62 J	2.5 U	17	160	38	2.5 U	607
MW-101D	05/31/11	Dilution	1.4 J	60	2 U	17	210	2.4	2 U	15	170	31	2 U	507
MW-101D	12/28/11		1	42	1 U	13	39	2.1	5 U	12	120	19	1 U	248
MW-101D	06/25/12		1.1	47	1 U	14	33	1.8	5 U	12	150	19	1 U	278
MW-101D	11/24/12		1	42	1 U	13	27	1.6	5 U	11	140	16	1 U	252
MW-101D	06/04/13		1.2	49	1 U	16	20	1.5	5 U	12	180	19	1 U	299
MW-101D	11/30/13		0.91 J	29	1 U	11	20	1	5 U	11	110	16	1 U	199
MW-101D	06/14/14		0.73 J	44	1 U	12	57	1.8	5 UB	11	86	18	0.19 J	231
MW-101D	11/24/14		0.71 J	53	1 U	14	63	2	5 U	9.6	90	15	0.28 J	248
MW-101D	06/07/15		0.49 J	49	0.2 J	9.8	51	1.8	5 UB	8.1	75	15	0.23 J	211
MW-101D	11/10/15		0.74 J	54	1 U	13	36	2	0.44 J	9.6	110	18	1 U	244
MW-101D	06/28/16		0.56 J	41	1 U	11	41	1.5	5 U	8.2	73	16	1 U	192
MW-101D	11/27/16		0.97 J	60	1 U	15	16	2	5 U	13	160	18	1 U	285
MW-101D	06/04/17		1 U	100	1 U	9.4	39	1.4	5 U	0.38 J	17	3.2	0.45 J	171
MW-101D	12/03/17		1 U	1.6	1 U	0.35 J	1.7	1 U	1 U	0.48 J	2	0.71 J	1 U	7
MW-101D	06/20/18		1 U	2.8	1 U	0.4 J	2.3	1 U	1 U	1 U	2.6	1 J	1 U	9
MW-101D	11/12/18		1 U	51.3	1 U	11.3	11.4	1.6	1 U	8.9	121	13.3	1 U	219
MW-101D	06/24/19	Dilution	10 U	10 U	10 U	10 U	10 U	10 U	50 U	10 U	35.2	10 U	10 U	35
MW-101D	12/13/19		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-101D	06/25/20		1 U	0.5 J	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	1
MW-101D	11/18/20		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-102A	09/28/93		2 U	26	2 U	4	32	2	23	2	34	6		129
MW-102A	05/20/99		1 U	43	0.25	1.2	54	1.8	2 U	0.6	51	6.3	1 U	158
MW-102A	10/25/99		0.15 J	43	5 U	2.5 J	61	1.7 J	10 U	3.1 J	57	15	5 U	183
MW-102A	02/16/00		5 U	64	5 U	2.8 J	90	3 J	10 U	5 U	97	14	5 U	271
MW-102A	04/25/00		5 U	43	5 U	1.5 J	49	1.4 J	10 JB	5 U	57	7.6	5 U	170
MW-102A	04/25/00	Fld Dupe	0.14 J	43	5 U	1.4 J	49	1.3 J	10 JB	5 U	57	7.7	5 U	170
MW-102A	07/26/00		10 U	71	10 U	2.7	95	2.5	20 U	10 U	100	16	10 U	287
MW-102A	11/16/00		5 U	91	5 U	2.8	110	2.7	10 U	5 U	88	14	5 U	309

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-102A	04/10/01		10 U	91	10 U	4.2	140	4.4	20 U	10 U	120	22	10 U	382
MW-102A	10/17/01		10 U	77	10 U	2.3	110	4.1	20 U	10 U	88	16	10 U	297
MW-102A	04/30/02		5 U	47	5 U	1.6	65	1.9	10 U	5 U	62	11	5 U	189
MW-102A	10/10/02		20 U	130	20 U	20 U	160	20 U	40 U	20 U	140	26	1 U	456
MW-102A	04/25/03		1 U	101 E	1 U	4.17	153 E	5.08	2 U	1 U	123 E	25.7 E	1 U	412
MW-102A	04/25/03	Dilution	10 U	92.9	10 U	10 U	137	10 U	20 U	10 U	102	22.2	10 U	354
MW-102A	12/26/03	Dilution	10 U	118 D	10 U	10 U	156 D	5.56 JD	10 U	10 U	114 D	22.4 D	10 U	416
MW-102A	12/26/03		1 U	108 E	1 U	4.14	145 E	5.89	1 U	1 U	111 E	20.1	1 U	394
MW-102A	04/28/04		2 U	39	2 U	2 U	34.2	1.45	4 U	2 U	37.3	6.93	2 U	119
MW-102A	05/02/05		1 U	19	1 U	1 U	16	0.84	2 U	1 U	19	3.5	1 U	58
MW-102A	05/02/05	Fld Dupe	1 U	24	1 U	1 J	21	1.1	2 U	1 U	21	4.3	1 U	72
MW-102A	11/02/05		1 U	71	1 U	1.9	110	5.1	2 U	1 U	57	11	1 U	256
MW-102A	06/22/06		1 U	39	1 U	0.98	54	1.9	2 U	1 U	31	6.6	1 U	133
MW-102A	11/16/06		1 U	73	1 U	1.8	120	3.3	2 U	1 U	100	15	1 U	313
MW-102A	10/08/07		10 U	64	10 U	4	150	5	9	10 U	95	20	10 U	347
MW-102A	05/19/08		10 U	68	10 U	10 U	150	10 U	20	10 U	93	18	10 U	349
MW-102A	11/26/08		0.18 J	58.1	0.32 J	2.81	137	4.14	1 U	1 U	82.6	17.6	1 U	303
MW-102A	06/11/09		0.19 J	66	0.26 J	2.6	150	4.1	1 U	1 U	82	16	1 U	321
MW-102A	11/27/09		1 U	96	1 U	3.5	190	5.3	1 U	1 U	89	18	1 U	402
MW-102A	06/28/10	Dilution	2 U	80	2 U	2.7	170	5.3	2 U	2 U	62	15	2 U	335
MW-102A	11/26/10	Dilution	2 U	99	2 U	3	200	5.3	2 U	2 U	90	20	2 U	417
MW-102A	11/26/10	Fld Dupe	2 U	95	2 U	2.7	200	4.9	2 U	2 U	87	19	2 U	409
MW-102A	06/01/11		1 U	94	1 U	2.2	190	6	1 U	1 U	74	16	1 U	382
MW-102A	12/28/11		1 U	90	1 U	1.9	170	6	5 U	1 U	63	15	1 U	346
MW-102A	06/27/12		1 U	79	1 U	1.4	160	5.1	5 U	1 U	52	13	1 U	311
MW-102A	11/30/12		1 U	82	1 U	1.6	160	5.7	5 U	1 U	59	14	1 U	322
MW-102A	06/10/13		1 U	40	1 U	0.63 J	70	2.6	5 U	0.57 J	19	5.9	1 U	139
MW-102A	12/18/13		1 U	58	1 U	0.77 J	100	4	5 U	1 U	27	7	1 U	197
MW-102A	06/13/14		1 U	44	1 U	0.46 J	65	2.7	5 UB	1 U	15	4.4	1 U	132
MW-102A	11/24/14		1 U	2.5	0.61 J	1 U	3.4	1 U	5 U	1 U	1 U	1 U	1.3	8
MW-102A	06/15/15		1 U	24	1 U	1 U	38	1.6	5 U	1 U	6.8	2.6	1 U	73
MW-102A	11/11/15		1 U	45	1 U	0.39 J	76	3.4	0.3 J	1 U	15	5.8	1 U	146
MW-102A	06/28/16		1 U	47	1 U	0.52 J	81	3.1	5 U	1 U	14	5.2	1 U	151

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-102A	11/26/16	Fld Dupe	1 U	61	1 U	0.52 J	110	4.2	5 U	1 U	19	7.2	1 U	202
MW-102A	11/26/16		1 U	60	1 U	0.49 J	100	4.1	5 U	1 U	18	7	1 U	190
MW-102A	06/05/17		1 U	64	1 U	0.62 J	110	4.2	5 U	1 U	19	7	1 U	205
MW-102A	12/02/17		1 U	70.4	1 U	0.81 J	131	4.9	1 U	1 U	26.3	8.9	1 U	242
MW-102A	06/20/18		1 U	76.9	1 U	0.93 J	128	5.5	1 U	1 U	29	9.5	1 U	250
MW-102A	11/12/18		1 U	68.4	1 U	0.85 J	103	4.9	1 U	1 U	30.1	10	1 U	217
MW-102A	06/22/19		1 U	59.5	1 U	1 U	50.5	3.5	5 U	1 U	29.2	7.6	1 U	150
MW-102A	12/13/19		1 U	51.1	1 U	1 U	49.2	3.1	5 U	1 U	22.7	7.1	1 U	133
MW-102A	06/24/20		1 U	55.4	1 U	0.47 J	42.3	3.1	5 U	1 U	24.4	8	1 U	134
MW-102A	11/16/20		1 U	23.8	1 U	1 U	27.3	1.8	5 U	1 U	12.6	5	1 U	71
MW-102B	09/28/93		1 U	1 U	1 U	1 U	1 U	1 U	3	1 U	1 U	1 U		3
MW-102B	05/20/99		1 U	0.99	0.63	0.32	2.1	1 U	2 U	1.1	1.4	2.1	1 U	9
MW-102B	10/25/99		1 U	0.93 J	0.66 J	0.4 J	2.7	1 U	2 U	2	5.1	3.7	0.14 J	16
MW-102B	02/16/00		1 U	0.32 J	0.47 J	1 U	0.28 J	1 U	2 U	1 U	1 U	1 U	1 U	1
MW-102B	04/25/00		1 U	0.36 J	0.49 J	1 U	0.48 J	1 U	2 U	1 U	0.2 J	0.09 J	1 U	2
MW-102B	07/26/00		1 U	0.62	0.54	1 U	0.54	1 U	2 U	1 U	1 U	1 U	0.19 J	2
MW-102B	11/16/00		1 U	0.76	1 U	1 U	0.62	1 U	2 U	1 U	1 U	1 U	0.17 J	2
MW-102B	11/16/00	Fld Dupe	1 U	0.74 J	0.6 J	1 U	0.59 J	1 U	2 U	1 U	1 U	1 U	0.16 J	2
MW-102B	04/10/01		1 U	0.71	0.61	1 U	0.71	1 U	2 U	1 U	1 U	1 U	0.11 J	2
MW-102B	10/17/01		1 U	0.83	1 U	1 U	1.2	1 U	2 U	1 U	1 U	1 U	0.13 J	2
MW-102B	04/30/02		1 U	1	0.58	1 U	1.4	0.13	2 U	1 U	1 U	1 U	0.089	3
MW-102B	10/10/02		1 U	2	1 U	1 U	2	1 U	0.6	1 U	1 U	1 U	1 U	5
MW-102B	04/25/03		1 U	1.35	1 U	1 U	2.27	1 U	2 U	1 U	1 U	1 U	1 U	4
MW-102B	12/26/03		1 U	1.64	0.64 J	1 U	2.9	1 U	1 U	1 U	1 U	1 U	1 U	5
MW-102B	04/28/04		1 U	1.73	0.62	1 U	3.2	1 U	2 U	1 U	1 U	1 U	1 U	6
MW-102B	05/02/05		1 U	1.6	0.48	1 U	2.4	1 U	2 U	1 U	1 U	1 U	1 U	4
MW-102B	11/02/05		1 U	1.9	1 U	1 U	3.5	1 U	2 U	1 U	1 U	1 U	1 U	5
MW-102B	06/22/06		1 U	2.3	1 U	1 U	4.3	1 U	2 U	1 U	1 U	1 U	1 U	7
MW-102B	11/16/06		1 U	3	1 U	1 U	5	1 U	2 U	1 U	1 U	1 U	1 U	8
MW-102B	10/08/07		1 U	3	0.5	1 U	4	1 U	2 U	1 U	1 U	1 U	1 U	8
MW-102B	05/19/08		1 U	4	1 U	1 U	6	1 U	2 U	1 U	1 U	1 U	1 U	10
MW-102B	11/26/08		1 U	2.8	0.66 J	1 U	5.11	0.28 J	1 U	1 U	1 U	1 U	0.18 J	9
MW-102B	06/11/09		1 U	3.2	0.65 J	1 U	5	1 U	1 U	1 U	1 U	1 U	1 U	9

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-102B	11/27/09		1 U	3.5	0.56 J	1 U	5.6	1 U	1 U	1 U	1 U	1 U	1 U	10
MW-102B	06/28/10		1 U	3	0.69 J	1 U	4.4	1 U	1 U	1 U	1 U	1 U	1 U	8
MW-102B	11/26/10		1 U	2.9	0.67 J	1 U	5	1 U	1 U	1 U	1 U	1 U	1 U	9
MW-102B	06/01/11		1 U	2.8	1 U	1 U	4	1 U	1 U	1 U	1 U	1 U	1 U	7
MW-102B	12/28/11		1 U	2.8	1 U	1 U	4.1	1 U	5 U	1 U	1 U	1 U	0.32 J	7
MW-102B	06/27/12		1 U	2.7	1 U	1 U	3.8	1 U	5 U	1 U	1 U	1 U	0.32 J	7
MW-102B	06/27/12	Fld Dupe	1 U	2.7	1 U	1 U	3.9	1 U	5 U	1 U	1 U	1 U	0.31 J	7
MW-102B	11/30/12		1 U	2.8	0.52 J	1 U	4.6	1 U	5 U	1 U	1 U	1 U	0.43 J	8
MW-102B	06/05/13		1 U	2.7	1 U	1 U	3.5	1 U	5 U	1 U	1 U	1 U	0.52 J	7
MW-102B	12/18/13		1 U	60	1 U	0.81 J	110	4.2	5 U	1 U	28	7.4	1 U	210
MW-102B	06/13/14		1 U	2.8	0.64 J	1 U	3.5	1 U	5 UB	1 U	1 U	1 U	0.92 J	8
MW-102B	11/24/14		1 U	2.6	0.8 J	1 U	3.5	1 U	5 U	1 U	1 U	1 U	1.2	8
MW-102B	06/15/15		1 U	1 U	1 U	1 U	1 U	1 U	5 UB	1 U	1 U	1 U	1 U	0
MW-102B	11/11/15		1 U	1.1	0.24 J	1 U	1.5	1 U	5 U	1 U	1 U	1 U	1.1	4
MW-102B	06/28/16		1 U	1.6	0.31 J	1 U	2.1	1 U	5 U	1 U	1 U	1 U	1.3	5
MW-102B	11/26/16		1 U	1.6	0.44 J	1 U	2.5	1 U	5 U	1 U	1 U	1 U	1.9	6
MW-102B	06/05/17		1 U	2.6	0.76 J	1 U	3.4	1 U	5 U	1 U	1 U	1 U	3.8	11
MW-102B	12/02/17		1 U	2.8	0.8 J	1 U	4.9	1 U	1 U	1 U	1 U	1 U	4.9	13
MW-102B	06/20/18		1 U	2.8	0.8 J	1 U	4.1	1 U	1 U	1 U	1 U	1 U	6	14
MW-102B	11/12/18		1 U	2.9	1 U	1 U	4.2	1 U	1 U	1 U	1 U	1 U	6.1	13
MW-102B	06/22/19		1 U	1 U	1 U	1 U	3.7	1 U	5 U	1 U	1 U	1 U	4.5	8
MW-102B	12/13/19		1 U	1 U	1 U	1 U	4	1 U	5 U	1 U	1 U	1 U	5.1	9
MW-102B	06/24/20		1 U	3.5	0.74 J	1 U	4.6	1 U	5 U	1 U	1 U	1 U	6.9	16
MW-102B	11/16/20		1 U	2.5	1 U	1 U	3.8	1 U	5 U	1 U	1 U	1 U	5.4	12
MW-102C	09/28/93		12 U	160	12 U	68	140	12 U	55	44	160	140		767
MW-102C	05/20/99		2.5	180	4	59	390	10 U	20 U	33	170	140	10 U	979
MW-102C	10/25/99		3 J	210	25 U	78	460	25 U	50 U	46	250	170	25 U	1217
MW-102C	02/16/00		0.66 J	32	0.91 J	12	61 E	0.57 J	0.38 J	5.9	60 E	26	2 U	199
MW-102C	02/16/00	Dilution	0.52 DJ	24 D	5 U	9 D	44 D	5 U	10 U	4.4 DJ	44 D	20 D	5 U	146
MW-102C	04/25/00		0.91 J	44	5 U	5.2	65	0.96 J	10 JB	0.67 J	60	10	5 U	197
MW-102C	07/26/00		0.64	29	0.8	4.5	39	0.41	4 U	0.99	44	8.2	2 U	128
MW-102C	11/16/00		0.32	19	2 U	4.5	28	0.26	4 U	1.1	23	8.3	2 U	84
MW-102C	04/10/01		0.94	48	5 U	2.6	39	5 U	10 U	0.8	90	5.4	5 U	187

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-102C	10/17/01		0.6	29	4 U	8.9	53	0.39	8 U	3.5	46	17	4 U	158
MW-102C	04/30/02		2.1	110	2.4	40	240	3.3	20 U	19	170	78	10 U	665
MW-102C	10/10/02		5 U	56	5 U	54	87	5 U	10 U	4 J	69	20	1 U	290
MW-102C	04/25/03		1.16	83.3 E	1.57	33 E	200 E	4	2 U	16.3	143 E	64.8 E	1 U	547
MW-102C	04/25/03	Dilution	10 U	48.4	10 U	18.6	112	10 U	20 U	7.94 J	73.2	34.9	10 U	295
MW-102C	12/26/03		0.6 J	40.4 E	0.76 J	9.18	69 E	1.04	1 U	1.6	60.2 E	16.3	1 U	199
MW-102C	12/26/03	Dilution	4 U	42.6 D	4 U	9.85 D	79.1 D	4 U	4 U	4 U	59 D	16.2 D	4 U	207
MW-102C	04/28/04		25 U	105	25 U	38.2	278	25 U	50 U	20.9	136	70.4	25 U	649
MW-102C	05/02/05		0.74	69	1.2	0.62	22	1 U	2 U	1.1	110	1.5	1 U	206
MW-102C	11/02/05		1 U	3.4	1 U	1.3	7.4	1 U	2 U	1 U	6.4	2.9	1 U	21
MW-102C	11/02/05	Fld Dupe	1 U	18	1 U	5.8	46	1 U	2 U	2.5 H	15	9.9	1 U	97
MW-102C	06/22/06		1 U	23	1 U	8.4	49	1 U	2 U	4.9	19	15	1 U	119
MW-102C	11/16/06		1 U	69	1.3	10	120	0.97 J	2 U	4	70	23	1 U	298
MW-102C	10/08/07	Fld Dupe	0.5 J	90 D	1	33 D	270 D	4	2 U	16	52 D	51 D	0.6 J	518
MW-102C	10/08/07		0.4	60	1	22	170	2	2 U	10	35	34	1 U	334
MW-102C	05/19/08		10 U	66	10 U	26	210	10 U	21	12	74	37	10 U	446
MW-102C	11/26/08		0.21 J	18.9	0.33 J	5.75	56.6	0.79 J	1 U	2.66	18.4	9.54	1 U	113
MW-102C	06/11/09		0.31 J	36	0.57 J	6.1	99	0.74 J	1 U	0.94 J	23	8.9	1 U	176
MW-102C	11/27/09	Dilution	10 U	210	10 U	59	760	6.7 J	10 U	22	94	74	10 U	1226
MW-102C	06/28/10	Dilution	5 U	160	5 U	53	740	6.8	5 U	18	89	65	5 U	1132
MW-102C	11/26/10	Dilution	10 U	170	3.2 J	51	720	10 U	10 U	21	110	68	10 U	1143
MW-102C	06/01/11	Dilution	5 U	200	5 U	50	870	7	5 U	25	90	63	5 U	1305
MW-102C	12/28/11	Dilution	0.95 J	160	5 U	40	670	5.6	25 U	17	80	47	5 U	1021
MW-102C	06/27/12	Dilution	1.2 J	130	5 U	33	550	4.4 J	25 U	7.3	55	30	5 U	811
MW-102C	11/30/12	Dilution	0.36 J	64	0.54 J	15	200	2	10 U	4.2	41	15	2 U	342
MW-102C	06/05/13	Dilution	0.7 J	150	2 U	36	360	4	6.2 J	10	84	33	0.8 J	685
MW-102C	12/18/13	Fld Dupe	0.65 J	160	1.1 J	37	300	4.4	7.1 J	8.2	77	28	1 J	624
MW-102C	12/18/13	Dilution	0.75 J	120	1.1 J	31	270	4	5 UB	7.3	78	24	0.58 J	537
MW-102C	06/13/14		1 U	5.3	1 U	0.76 J	6.5	1 U	5 UB	0.4 J	1.2	0.6 J	1 U	15
MW-102C	11/24/14		1 U	1	1 U	1 U	1.4	1 U	5 U	1 U	0.26 J	1 U	1 U	3
MW-102C	06/15/15		1 U	1 U	1 U	1 U	1 U	1 U	5 UB	1 U	0.29 J	1 U	1 U	0
MW-102C	11/11/15		1 U	2	1 U	1 U	1 U	1 U	0.48 J	0.31 J	10	1 U	1 U	13
MW-102C	06/28/16		1 U	3.6	1 U	0.7 J	2.4	1 U	5 U	1.1	9.1	1.4	1 U	18

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-102C	11/27/16		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-102C	06/05/17		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-102C	12/02/17		1 U	0.24 J	1 U	1 U	0.82 J	1 U	1 U	1 U	1 U	0.33 J	1 U	1
MW-102C	06/20/18		1 U	0.27 J	1 U	1 U	0.59 J	1 U	1 U	1 U	1 U	1 U	1 U	1
MW-102C	11/12/18		1 U	109	1 U	21.2	66.2	3	1 U	3.2	94.4	11.4	1.7	310
MW-102C	06/22/19		0.52 J	1 U	1 U	32.8	71.6	3.9	5 U	6.3	1 U	19.3	1 U	134
MW-102C	06/22/19	Fld Dupe	1 U	1 U	1 U	30.3	67.2	3.6	5 U	5.7	1 U	20	1 U	127
MW-102C	12/13/19		1 U	155	1 U	30.6	63.4	3.5	5 U	8.4	176	14.5	2.2	454
MW-102C	06/24/20		0.58 J	188	0.46 J	33.2	60	4.2	5 U	6.5	217	15.3	3.3	529
MW-102C	11/16/20		1 U	113	1 U	20.3	46.5	2.8	5 U	3.8	141	10.3	2.3	340
MW-113A	10/08/93		7 U	92	7 U	33	110	7 U	14 U	7 U	140	56		431
MW-113A	05/03/99		0.9	34	0.4	10	52	1.2	2 U	1.9	59	24	1 U	183
MW-113A	11/10/99		2.3 J	100	10 U	27	160	2.4 J	20	3.2 J	160	69	10 U	544
MW-113A	02/15/00		2.1 J	91	10 U	16	160	5.7 J	20 U	2.9 J	160	71	10 U	509
MW-113A	04/24/00		2.1 JB	92	10 U	5.1 J	160	13	20 JB	2.4 J	160	61	10 U	516
MW-113A	07/27/00		2.3	86	10 U	4	110	7.5	20 U	10 U	130	22	1 U	362
MW-113A	11/16/00		2.3	130	10 U	9.4	200	12	20 U	2.1	170	62	10 U	588
MW-113A	04/12/01		2.4	10	10 U	210	210	15	20 U	3.7	200	81	10 U	732
MW-113A	10/31/01		2.8	110	10 U	3	240	22	20 U	3.3	200	75	10 U	656
MW-113A	04/29/02		2.5	100	10 U	1.5	200	23	20 U	4.5	200	70	10 U	602
MW-113A	10/18/02		20 U	190	20 U	240	430	20 U	40 U	20 U	370	140	1 U	1370
MW-113A	04/23/03		2.84	139 E	1 U	27.6 E	371 E	18.2	2 U	8.11	306 E	126 E	1 U	999
MW-113A	04/23/03	Dilution	25 U	121	25 U	33.9	325	25 U	50 U	25 U	245	101	25 U	826
MW-113A	12/28/03		2.93	140 E	1.38	38.3 E	345 E	10.4	1 U	9.72	309 E	124 E	1 U	981
MW-113A	12/28/03	Dilution	20 U	109 D	20 U	31.4 D	318 D	20 U	20 U	20 U	232 D	92.9 D	20 U	783
MW-113A	04/28/04		25 U	123	25 U	32.4	360	25 U	50 U	25 U	239	89.1	25 U	844
MW-113A	04/28/04	Fld Dupe	3.09	123	1.6	35.9	371	37.9 E	2 U	10.3	240	96.8	1 U	920
MW-113A	05/21/05		5 U	140	5 U	45	410	5.7	10 U	8.1	260	100	5 U	969
MW-113A	10/20/05		2.6	110	1 U	22	330	17	2 U	8	210	82	1 U	782
MW-113A	05/08/06		2.3	110	1 U	32	470	9.1	20 U	10	270	93	1 U	996
MW-113A	01/04/07		10 U	110	10 U	27	430	10 U	20 U	10	210	10	10 U	797
MW-113A	10/08/07		2	150	1	46	480	15	2 U	10	260	110	1 U	1074
MW-113A	05/17/08		20 U	160	20 U	54	510 E	20 U	41	20 U	280	130	20 U	1175

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-113A	05/17/08	Dilution	40 U	140 D	40 U	48 D	470 D	40 U	80 U	40 U	250 D	110 D	40 U	1018
MW-113A	11/29/08	Dilution	2.2 J	135	1.5 J	7.25	369	40.6	1.7 J	10.5	210	98.6	5 U	876
MW-113A	06/11/09	Dilution	2.6 J	110	5 U	21	370	15	5 U	10	180	85	5 U	794
MW-113A	11/28/09	Dilution	1.5 J	110	2.5 U	1.7 J	290	44	2.5 U	12	170	84	2.5 U	713
MW-113A	06/29/10	Dilution	1.1 J	88	1 J	3.3	240	30	0.85 J	12	130	76	2.5 U	582
MW-113A	11/28/10	Dilution	0.95 J	85	0.7 J	17	250	11	2.5 U	12	110	67	2.5 U	554
MW-113A	06/01/11		0.96 J	88	1 U	2.4	90	14	1 U	13	120	57	1 U	385
MW-113A	12/29/11		1.1	95	1 U	16	50	4.3	5 U	13	130	46	1 U	355
MW-113A	06/25/12		1.1	100	1 U	14	48	5.3	5 U	13	140	48	1 U	369
MW-113A	11/24/12		1.2	110	1 U	14	43	4.4	5 U	13	140	45	1 U	371
MW-113A	06/04/13		1.2	120	1 U	26	40	3.9	5 U	13	160	45	1 U	409
MW-113A	11/30/13		1.2	140	1 U	33	37	4.4	5 UB	13	160	51	1 U	440
MW-113A	06/14/14		1.3	140	1 U	32	32	4.5	5 UB	14	160	49	1 U	433
MW-113A	11/24/14		1.3	140	1 U	18	31	5.2	5 U	11	140	50	1 U	397
MW-113A	06/07/15		1.3	140	1 U	30	30	4.6	5 UB	15	170	51	1 U	442
MW-113A	11/10/15		1.2	120	1 U	14	25	4.4	0.77 J	15	130	47	1 U	357
MW-113A	06/28/16		1.2	120	1 U	23	22	4	5 U	13	140	44	1 U	367
MW-113A	11/16/16		1.1	120	1 U	25	21	4	5 U	14	130	43	1 U	358
MW-113A	06/05/17		0.63 J	61	1 U	12	9.6	1.9	5 U	8	73	21	1 U	187
MW-113A	11/17/17		1.2	129	1 U	23.3	20.4	4.1	1 U	14.7	149	40.2	1 U	382
MW-113A	06/21/18		1 U	0.24 J	1 U	1 U	1 U	1 U	1 U	0.29 J	0.57 J	0.3 J	1 U	1
MW-113A	11/10/18		1 U	95	1 U	19.2	12.9	3.1	1 U	15.8	125	32.6	1 U	304
MW-113A	06/15/19		1 U	44.8	1 U	4.9	5.6	1.3	5 U	8	65.3	15.7	1 U	146
MW-113A	12/13/19		1 U	70	1 U	13.3	8.3	1 U	5 U	11.6	73.2	22	1 U	198
MW-113A	06/25/20		0.79 J	87.2	1 U	13.2	8.9	2.5	5 U	14.9	85.1	25.6	1 U	238
MW-113A	11/17/20		1 U	75.1	1 U	12.7	7.6	2	5 U	15.8	72.4	23.7	1 U	209
MW-113B	10/19/93		2 U	14	2 U	4	12	2 U	3 U	2 U	6	6		42
MW-113B	04/29/99		0.54	33	0.56	12	38	0.65	2 U	1.8	17	19	1 U	123
MW-113B	10/27/99		0.45 J	33	5 U	8.4	39	0.55 J	10 U	1.3 J	13	20	5 U	116
MW-113B	02/15/00		0.65 J	48	5 U	11	62	0.83 J	10 U	1.4 J	27	30	5 U	181
MW-113B	04/24/00		0.61 JB	43	5 U	11	56	0.98 J	10 JB	1.2 J	21	26	5 U	170
MW-113B	07/27/00		0.71	38	0.6	9.4	49	0.91	10 U	0.89	17	20	5 U	137
MW-113B	11/16/00		0.63	55	5 U	11	62	1.3	10 U	1.4	22	27	5 U	180

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-113B	04/12/01		0.56	40	5 U	8.9	53	1	10 U	5 U	17	20	5 U	140
MW-113B	10/31/01		0.64	50	5 U	12	67	1.1	10 U	5 U	24	29	5 U	184
MW-113B	04/29/02		0.6	39	5 U	9.8	60	0.97	10 U	1.3	19	23	5 U	154
MW-113B	10/18/02		10 U	84	10 U	88	120	10 U	5	10 U	39	42	1 U	378
MW-113B	04/23/03		1.05	77.3 E	1 U	23.3	143 E	6.06	2 U	3.77	65.8 E	55.8 E	2.2	378
MW-113B	04/23/03	Dilution	10 U	58.6	10 U	17.4	115	10 U	20 U	10 U	45.6	41.9	10 U	279
MW-113B	12/28/03		0.97 J	71.3 E	1 U	21.4	134 E	4.01	1 U	3.72	53.4 E	52.1 E	1.24	342
MW-113B	12/28/03	Dilution	10 U	65.1 D	10 U	19.1 D	129 D	10 U	10 U	10 U	43.1 D	45.9 D	10 U	302
MW-113B	04/28/04		10 U	70	10 U	19.8	143	10 U	20 U	10 U	44.9	42.7	10 U	320
MW-113B	05/21/05		1 U	64	1 U	19	140	1.8	2 U	2.9	39	39	4.8	311
MW-113B	10/20/05		1 U	78	1 U	22	170	1.9	2 U	3.8	45	47	1 U	368
MW-113B	05/08/06		1 U	64	1 U	21	140	1.9	2 U	3.6	33	37	9.2	310
MW-113B	01/04/07		1 U	61	1 U	20	120	1.7	2 U	3	30	38	1.4	275
MW-113B	10/08/07		0.5	56	0.6	17	120	2	2 U	3	21	30	15	265
MW-113B	05/17/08		10 U	66	10 U	19	140	10 U	19 J	10 U	25	34	17	320
MW-113B	11/29/08		0.71 J	71.3	0.92 J	20.4	169	2.15	1 U	3.49	28.8	41.5	6.2	344
MW-113B	06/11/09		0.73 J	71	0.87 J	19	180	2.2	1 U	3.6	29	42	6.9	355
MW-113B	11/28/09		0.69 J	77	0.76 J	22	190	2.5	1 U	3.9	31	41	8	377
MW-113B	06/29/10	Dilution	2 U	63	2 U	19	150	2.7	2 U	3	19	33	9	299
MW-113B	11/28/10	Dilution	2 U	67	0.8 J	19	160	3	2 U	4.2	26	37	8.8	326
MW-113B	06/01/11		0.46 J	66	0.61 J	18	140	2.3	1 U	4.1	23	36	11	301
MW-113B	12/29/11		0.42 J	59	0.63 J	16	100	2	5 U	3.9	19	30	8.9	240
MW-113B	06/25/12		0.48 J	60	1 U	14	98	1.9	5 U	3.6	17	28	9.4	232
MW-113B	11/24/12		0.34 J	59	0.46 J	14	78	1.8	5 U	3.7	18	26	7.5	209
MW-113B	06/04/13		0.27 J	55	1 U	12	58	1.4	5 U	2.5	12	20	12	173
MW-113B	11/30/13		0.3 J	53	0.36 J	12	56	1.4	5 U	2.7	11	21	9.6	167
MW-113B	06/14/14		0.28 J	63	0.42 J	14	52	1.7	5 UB	2.8	13	19	12	178
MW-113B	11/24/14		0.4 J	66	0.52 J	15	55	2.2	5 U	2.1	13	22	13	189
MW-113B	06/07/15		0.29 J	71	0.45 J	14	49	1.8	5 UB	3	12	22	11	185
MW-113B	11/10/15		0.26 J	61	0.38 J	13	42	1.8	0.56 J	2.2	12	20	12	165
MW-113B	06/28/16		1 U	53	0.35 J	11	32	1.4	5 U	1.7	7.7	15	9.5	132
MW-113B	11/16/16		1 U	63	0.4 J	13	38	1.7	5 U	2.3	11	18	9.7	157
MW-113B	06/05/17		1 U	59	0.41 J	13	35	1.5	5 U	2.6	7.1	17	6.2	142

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-113B	11/17/17		1 U	70.9	1 U	15	39.5	1.8	1 U	2.8	11.3	18.6	8.1	168
MW-113B	06/21/18		1 U	67.9	1 U	14.3	36.1	1.6	1 U	3.3	9.8	19.3	6.3	159
MW-113B	11/10/18		1 U	60.3	1 U	13	29.7	1.5	1 U	3	11.1	17.3	5.8	142
MW-113B	06/15/19		1 U	61.2	1 U	12.9	27	1.6	5 U	2.7	13.2	16.4	4.9	140
MW-113B	12/13/19		1 U	66.4	1 U	13.9	30.3	1 U	5 U	1 U	14.1	17	4.2	146
MW-113B	06/25/20		1 U	65.4	1 U	15.3	29.6	1.7	5 U	3.8	12.3	18.3	3.9	150
MW-113B	11/17/20		1 U	57.3	1 U	11.5	27	1.4	5 U	4.2	10.3	16.9	2.6	131
MW-114A	10/05/93		1 U	2	1 U	4	5	1 U	2 U	1 U	6	2		19
MW-114A	04/28/99		5 U	6.7	5 U	46	14	5 U	10 U	1.9 J	250	34	5 U	353
MW-114A	10/26/99		0.34 J	7.1 J	25 U	48	11 J	25 U	50 U	25 U	290	47	25 U	403
MW-114A	01/31/00		10 U	5 J	10 U	34	6.6 J	10 U	1.5 J	10 U	220	33	10 U	300
MW-114A	04/24/00		10 U	4.2 J	10 U	26	5.6 J	10 U	20 JB	10 U	160	24	10 U	240
MW-114A	07/27/00		10 U	3.9	10 U	24	5.4	10 U	20 U	10 U	140	22	10 U	195
MW-114A	11/13/00		10 U	4.2	10 U	20	4.7	10 U	20 U	10 U	120	19	10 U	168
MW-114A	04/12/01		5 U	2.7	5 U	18	3.9	5 U	10 U	5 U	120	20	5 U	165
MW-114A	10/31/01		5 U	2.5	5 U	15	3.6	5 U	10 U	5 U	100	18	5 U	139
MW-114A	04/25/02		5 U	3.1	5 U	16	4.1	5 U	10 U	5 U	100	22	5 U	145
MW-114A	04/25/02	Fld Dupe	5 U	3.1 J	5 U	16	4 J	5 U	10 U	5 U	100	22	5 U	145
MW-114A	10/15/02		10 U	10 U	10 U	140	7	10 U	20 U	10 U	170	38	1 U	355
MW-114A	04/23/03		1 U	3.28	1 U	13.4	4.09	1 U	2 U	1 U	94.6 E	23.5	1 U	139
MW-114A	04/23/03	Dilution	10 U	10 U	10 U	12.9	10 U	10 U	20 U	10 U	80.2	20.8	10 U	114
MW-114A	12/26/03		1 U	2.86	1 U	9.96	3.62	1 U	1 U	1 U	73.9 E	16.3	1 U	107
MW-114A	12/26/03	Dilution	4 U	2.86 JD	4 U	10.3 D	3.6 JD	4 U	4 U	4 U	70.1 D	15.9 D	4 U	103
MW-114A	04/28/04		5 U	3.69	5 U	12	4.25	5 U	10 U	5 U	79.9	20.8	5 U	121
MW-114A	05/21/05		1 U	2.5	1 U	5.7	3.3	1 U	2 U	1 U	28	7.9	1 U	47
MW-114A	10/20/05		1 U	2.6	1 U	7.2	2.9	1 U	2 U	1 U	39	9.8	1 U	62
MW-114A	05/06/06		1 U	3.4	1 U	9.4	3.7	1 U	2 U	1 U	44	12	1 U	73
MW-114A	01/04/07		1 U	3.5	1 U	11	3.3	1 U	2 U	1 U	51	9.6	1 U	78
MW-114A	10/08/07		1 U	2	1 U	7	2	1 U	2 U	2 U	34	5	1 U	50
MW-114A	05/17/08		2 U	2	2 U	5	3	2 U	3 J	2 U	28	4	2 U	45
MW-114A	11/29/08		1 U	0.28 J	1 U	1 U	1 U	1 U	1 U	1 U	1.09	1 U	1 U	1
MW-114A	06/11/09		0.16 J	1 U	1 U	1 U	1 U	1 U	1 U	1 U	0.9 J	1 U	1 U	1
MW-114A	11/28/09		0.46 J	1.9	1 U	3.9	1.3	1 U	1 U	1 U	36	2.7	1 U	46

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	5	7	70	100	5	5	200	5	2	
MW-114A	06/25/10		1 U	3.2	1 U	6.6	2.2	1 U	1 U	1 U	70	4.4	1 U	86
MW-114A	11/27/10		1 U	2.8	1 U	8.5	2.1	1 U	1 U	1 U	65	4.7	1 U	83
MW-114A	06/01/11		1 U	4.2	1 U	10	2.9	1 U	1 U	1 U	85	5.5	1 U	108
MW-114A	12/28/11		1 U	3.6	1 U	9.1	2.6	1 U	5 U	0.18 J	65	4.1	1 U	85
MW-114A	06/27/12		0.21 J	4.3	1 U	5.6	3	1 U	5 U	1 U	71	4.2	1 U	88
MW-114A	11/24/12		1 U	2.9	1 U	1.6	2.4	0.22 J	5 U	1 U	27	1.8	1 U	36
MW-114A	06/07/13		1 U	5.5	1 U	11	4.3	1 U	5 U	1 U	82	4.7	1 U	108
MW-114A	12/19/13		1 U	3.1	1 U	5.8	2.7	1 U	5 U	0.19 J	43	2.3	1 U	57
MW-114A	06/14/14		1 U	6.3	1 U	5.5	4.8	1 U	5 UB	0.23 J	52	3.1	1 U	72
MW-114A	11/24/14		1 U	4.6	1 U	4.9	4.1	1 U	5 U	0.27 J	38	3.1	1 U	55
MW-114A	06/13/15		1 U	5.6	1 U	5.7	5.1	1 U	5 U	0.27 J	38	2.7	1 U	57
MW-114A	11/11/15		1 U	6.5	1 U	4.7	5.3	0.33 J	0.39 J	0.31 J	45	3.2	1 U	66
MW-114A	06/28/16		1 U	3.5	1 U	4.1	2.3	1 U	5 U	0.27 J	27	1.9	1 U	39
MW-114A	11/27/16		1 U	6.5	1 U	7.1	4	1 U	5 U	0.36 J	47	2.9	1 U	68
MW-114A	06/05/17		1 U	5.5	1 U	4.9	4.2	1 U	5 U	1 U	27	1.8	1 U	43
MW-114A	12/02/17		1 U	6.4	1 U	5.9	3.8	1 U	1 U	0.31 J	36.1	2.5	1 U	55
MW-114A	06/21/18		1 U	9.4	1 U	6.4	4.9	1 U	1 U	0.34 J	40.6	2.7	1 U	64
MW-114A	11/10/18		1 U	7.2	1 U	4.7	3.5	1 U	1 U	0.31 J	28.6	2	1 U	46
MW-114A	06/22/19		1 U	7.2	1 U	4.5	3.2	1 U	5 U	1 U	23.5	1.6	1 U	40
MW-114A	12/14/19		1 U	7.5	1 U	3.7	3.2	1 U	5 U	1 U	25.7	1.4	1 U	42
MW-114A	06/25/20		1 U	6.4	1 U	4.1	2.5	1 U	5 U	1 U	25.7	1.5	1 U	40
MW-114A	11/18/20		1 U	3.1	1 U	1.5	1.4	1 U	5 U	1 U	9.6	1 U	1 U	16
MW-114B	10/04/93		2 U	14	2 U	4	12	2 U	3 U	2 U	6	6		42
MW-114B	04/28/99		1 U	0.89	1 U	0.6	3.3	1 U	2 U	1	4	6.2	1 U	16
MW-114B	10/26/99		1 U	1	1 U	0.46 J	3.3	1 U	2 U	0.66 J	1.2	8.2	1 U	15
MW-114B	01/31/00		1 U	0.81 J	1 U	0.18 J	2.3	1 U	2 U	1 U	1 U	5.7	1 U	9
MW-114B	04/24/00		1 U	0.68 J	1 U	0.11 J	1.7	1 U	2 JB	1 U	0.05 J	1.8	1 U	6
MW-114B	07/27/00		1 U	1	1 U	0.26	3	1 U	2 U	1 U	1 U	7.9	1 U	12
MW-114B	07/27/00	Fld Dupe	1 U	1	1 U	0.26 J	3	1 U	2 U	1 U	1 U	7.5	1 U	12
MW-114B	11/13/00		1 U	1.2	1 U	0.13	2.4	1 U	2 U	1 U	1 U	3.5	1 U	7
MW-114B	04/12/01		1 U	0.98	1 U	0.26	2.9	1 U	2 U	1 U	1 U	8.2	1 U	12
MW-114B	10/31/01		1 U	0.96	1 U	0.13	2.2	1 U	2 U	1 U	1 U	4.8	1 U	8
MW-114B	04/25/02		1 U	1.1	1 U	0.29	3	0.04	2 U	1 U	1 U	7.2	1 U	12

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-114B	10/15/02		1 U	2	3	1	3	1 U	0.6	1 U	1 U	9	1 U	19
MW-114B	04/23/03		1 U	1.15	1 U	1 U	2.84	1 U	2 U	1 U	1 U	8.8	1 U	13
MW-114B	12/26/03		1 U	1.25	1 U	1.07	2.98	1 U	1 U	1 U	1 U	8.91	1 U	14
MW-114B	04/28/04		1 U	1.21	1 U	1 U	2.87	1 U	2 U	1 U	1 U	8.82	1 U	13
MW-114B	05/21/05		1 U	1.5	1 U	1 U	2.3	1 U	2 U	1 U	1 U	7.6	1 U	11
MW-114B	10/20/05		1 U	1.6	1 U	1 U	2.3	1 U	2 U	1 U	1 U	8.8	1 U	13
MW-114B	05/06/06		1 U	1 U	1 U	1 U	2.1	1 U	2 U	1 U	1 U	8.7	1 U	11
MW-114B	01/04/07		1 U	1.4	1 U	1 U	1.8	1 U	2 U	1 U	1 U	6.7	1 U	10
MW-114B	01/04/07	Fld Dupe	1 U	1.6	1 U	1 U	1.8	1 U	2 U	1 U	1 U	6.4	1 U	10
MW-114B	10/08/07		1 U	2	1 U	0.5	2	1 U	2 U	1 U	1 U	6	1 U	11
MW-114B	05/17/08		1 U	2	1 U	1 U	2	1 U	2 U	1 U	1 U	9	1 U	13
MW-114B	12/18/08		1 U	1.6	1 U	0.67 J	2	1 U	1 U	1 U	1 U	6.8	1 U	11
MW-114B	06/20/09		1 U	1.8	1 U	0.67 J	2.2	1 U	1 U	1 U	1 U	6.5	1 U	11
MW-114B	11/28/09		1 U	2.2	1 U	1	2	1 U	1 U	1 U	1 U	6.7	1 U	12
MW-114B	11/28/09	Fld Dupe	1 U	2.4	1 U	0.93 J	1.9	1 U	1 U	1 U	1 U	6.8	1 U	12
MW-114B	06/25/10		1 U	2.1	1 U	0.84 J	2	1 U	1 U	1 U	1 U	6.3	1 U	11
MW-114B	06/25/10	Fld Dupe	1 U	2	1 U	0.81 J	1.9	1 U	1 U	1 U	1 U	6.3	1 U	11
MW-114B	11/27/10		1 U	1.8	1 U	1	2.3	1 U	1 U	1 U	1 U	7.8	1 U	13
MW-114B	06/01/11		1 U	1.6	1 U	1 U	2.1	1 U	1 U	1 U	1 U	7.7	1 U	11
MW-114B	06/01/11	Fld Dupe	1 U	1.6	1 U	1 U	2.1	1 U	1 U	1 U	1 U	7.4	1 U	11
MW-114B	12/28/11		1 U	1.3	1 U	0.54 J	2.2	1 U	5 U	1 U	1 U	6.7	1 U	11
MW-114B	06/28/12		1 U	1.1	1 U	1 U	1.8	1 U	5 U	1 U	1 U	6.5	1 U	9
MW-114B	06/28/12	Fld Dupe	1 U	1.1	1 U	0.41 J	1.8	1 U	5 U	1 U	1 U	6.7	1 U	10
MW-114B	11/24/12		1 U	1.3	1 U	0.44 J	1.9	1 U	5 U	1 U	1 U	6.1	1 U	10
MW-114B	11/24/12	Fld Dupe	1 U	1.3	1 U	0.38 J	1.8	1 U	5 U	1 U	1 U	5.8	1 U	9
MW-114B	06/07/13		1 U	1.2	1 U	1 U	1.9	1 U	5 U	1 U	1 U	6.9	1 U	10
MW-114B	06/14/14		1 U	1.5	1 U	1 U	1.5	1 U	5 UB	1 U	1 U	4.9	1 U	8
MW-114B	06/14/14	Fld Dupe	1 U	1.4	1 U	1 U	1.5	1 U	5 UB	1 U	1 U	4.6	1 U	8
MW-114B	11/24/14		1 U	1.4	1 U	1 U	1	1 U	5 U	0.28 J	0.24 J	4	1 U	7
MW-114B	06/13/15		1 U	2.2	1 U	0.67 J	1.7	1 U	5 U	0.53 J	1	5.6	1 U	12
MW-114B	06/13/15	Fld Dupe	1 U	2.1	1 U	0.69 J	1.7	1 U	5 UB	0.56 J	0.99 J	5.6	1 U	12
MW-114B	11/11/15		1 U	1.9	1 U	0.58 J	1.6	1 U	0.67 J	0.52 J	0.47 J	5.4	1 U	11
MW-114B	06/28/16		1 U	1.6	1 U	0.46 J	1.4	1 U	5 U	1 U	1 U	3.8	1 U	7

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-114B	06/28/16	Fld Dupe	1 U	1.6	1 U	0.34 J	1.5	1 U	5 U	1 U	1 U	4	1 U	7
MW-114B	11/27/16		1 U	1.9	1 U	0.46 J	1.5	1 U	5 U	1 U	1 U	4.6	1 U	8
MW-114B	06/05/17		1 U	1.5	1 U	0.39 J	1.2	1 U	5 U	1 U	1 U	3.4	1 U	6
MW-114B	06/05/17	Fld Dupe	1 U	1.7	1 U	0.43 J	1.4	1 U	5 U	1 U	1 U	3.7	1 U	7
MW-114B	12/02/17		1 U	1.8	1 U	0.46 J	1.6	1 U	1 U	1 U	1 U	3.9	1 U	8
MW-114B	06/21/18		1 U	1.9	1 U	0.5 J	1.3	1 U	1 U	1 U	1 U	3.7	1 U	7
MW-114B	11/10/18		1 U	0.57 J	1 U	1 U	0.43 J	1 U	1 U	1 U	1 U	0.86 J	1 U	2
MW-114B	06/22/19		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-114B	12/14/19		1 U	1.9	1 U	1 U	0.86 J	1 U	5 U	1 U	1 U	2	1 U	5
MW-114B	06/25/20		1 U	1.9	1 U	0.4 J	0.92 J	1 U	5 U	1 U	1 U	2.1	1 U	5
MW-114B	11/18/20		1 U	1.7	1 U	1 U	1 U	1 U	5 U	1 U	1 U	2.2	1 U	4
MW-114B	11/18/20	Fld Dupe	1 U	1.6	1 U	1 U	0.86 J	1 U	5 U	1 U	1 U	2.1	1 U	5
MW-117B	10/04/93		0.6	1 U	1 U	1 U	1	1 U	2 U	4	2	5		13
MW-117B	04/22/99		0.72	7.3	0.54	14	16	1 U	2 U	3.1	83	21	1 U	146
MW-117B	10/18/99		0.58 J	7.7	5 U	14	17	5 U	10	1.3 J	68	17	5 U	136
MW-117B	01/26/00		0.36 J	8	5 U	9.5	18	5 U	10	1.9 J	59	22	5 U	129
MW-117B	04/17/00		0.39 J	8.1	0.42 J	11	19	2 U	4 JB	1.6 J	49	19	0.07 J	113
MW-117B	07/24/00		0.49	6.6	2 U	9.6	15	2 U	4 U	1.7	42	17	2 U	92
MW-117B	11/07/00		0.42	10	2 U	11	18	2 U	4 U	1.7	37	19	2 U	97
MW-117B	04/09/01		0.37	5.8	2 U	7.3	13	0.25	4 U	1.8	28	17	2 U	74
MW-117B	10/15/01		0.35	7.1	2 U	7.5	16	2 U	4 U	1.3	23	16	2 U	71
MW-117B	04/16/02		0.3	5.9	0.22	7.3	15	0.2	2 U	1.7	22	16	1 U	69
MW-117B	10/07/02		5 U	8	5 U	54	20	5 U	10 U	3	25	16	1 U	126
MW-117B	04/22/03		1 U	7.55	1 U	10.4	20.1	0.61 J	2 U	2.31	23.1	18.4	1 U	82
MW-117B	12/22/03		0.99 J	5.96	1 U	9.38	18.7	0.53 J	1 U	2.25	21.8	16.9	1 U	77
MW-117B	04/28/04		0.73	3.77	1 U	4.76	11.5	1 U	2 U	2	13.5	11.5	1 U	48
MW-117B	05/21/05		1 U	4.5	1 U	5.7	13	1 U	2 U	1.6	11	9.4	1 U	45
MW-117B	10/19/05		1 U	4.7	1 U	5.6	14	1 U	2 U	1.8	12	9.3	1 U	47
MW-117B	06/28/06		1 U	21	1 U	23	70	1 U	2 U	24	56	23	1 U	217
MW-117B	11/21/06		1 U	3.6	1 U	4	11	1 U	2 U	2.1	12	11	1 U	44
MW-117B	10/06/07		0.4	6	1 U	8	8	1 U	2 U	2	16	12	1 U	52
MW-117B	05/17/08	Dilution	2 U	7 D	2 U	10 D	9 D	2 U	4 U	3 D	22 D	14 D	2 U	65
MW-117B	05/17/08		1 U	8	1 U	11	11	1 U	2 U	3	25 E	16	1 U	74

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-117B	11/28/08		0.38 J	7.91	1 U	8.73	8.11	1 U	1 U	4.99	24	15.8	1 U	70
MW-117B	06/09/09		0.49 J	11	1 U	12	7.9	1 U	1 U	4.5	31	17	1 U	84
MW-117B	11/24/09		0.42 J	8.5	1 U	9	5.1	1 U	1 U	5.3	24	15	1 U	67
MW-117B	06/24/10		0.32 J	12	1 U	12	6	1 U	1 U	6.5	37	17	1 U	91
MW-117B	11/24/10		0.31 J	11	1 U	8.1	4.6	1 U	1 U	8.4	31	19	1 U	82
MW-117B	05/31/11		1 U	4.7	1 U	3.9	2.2	1 U	1 U	7.8	13	10	1 U	42
MW-117B	12/22/11		0.29 J	8.7	1 U	4.5	1.8	1 U	5 U	6.7	11	8.7	1 U	42
MW-117B	06/26/12		0.3 J	5.9	1 U	2.6	0.77 J	1 U	5 U	5.9	7.8	5.7	1 U	29
MW-117B	11/25/12		0.35 J	10	1 U	3	1.1	1 U	5 U	5.7	10	6	1 U	36
MW-117B	05/30/13		0.27 J	3	1 U	1.6	0.6 J	1 U	5 U	5.2	4.4	3.7	1 U	19
MW-117B	11/29/13		0.39 J	8.4	1 U	3.1	0.9 J	1 U	5 U	5.5	7.4	4.9	1 U	31
MW-117B	06/05/14		0.21 J	4	1 U	1.9	0.55 J	1 U	5 U	5.4	5	3.6	1 U	21
MW-117B	11/21/14		0.3 J	11	1 U	3.7	0.82 J	1 U	5 U	4.8	7.9	4.4	1 U	33
MW-117B	06/08/15		0.31 J	11	1 U	4.4	1.2	1 U	5 UB	5.5	9	6.2	1 U	38
MW-117B	11/09/15		1 U	16	1 U	7.7	1.7	1 U	0.37 J	7	27	9.5	1 U	69
MW-117B	06/27/16		0.24 J	16	1 U	8.7	1.6	1 U	5 U	10	32	10	1 U	79
MW-117B	11/11/16		0.27 J	16	1 U	7.5	1.5	1 U	5 U	11	29	11	1 U	76
MW-117B	06/06/17		0.25 J	16	1 U	7.8	1.6	1 U	5 U	12	31	10	1 U	79
MW-117B	11/16/17		0.28 J	18.3	1 U	8.7	1.8	1 U	1 U	13.5	38.4 J	12.2	1 U	93
MW-117B	06/18/18		1 U	13.7	1 U	6.9	1.4	1 U	1 U	13.9	31.3	10.5	1 U	78
MW-117B	11/12/18		1 U	13.3	1 U	6.4	1.4	1 U	1 U	14.5	28.4	9.1	1 U	73
MW-117B	06/21/19		1 U	12.3	1 U	6.3	1 U	1 U	5 U	11.8	27.8	8.1	1 U	66
MW-117B	12/10/19		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	12.6	4.2	1 U	17
MW-117B	06/23/20		1 U	12.7	1 U	5.9	0.83 J	1 U	5 U	11.7	26.6	8.5	1 U	66
MW-117B	11/13/20		1 U	9.2	1 U	4.2	1 U	1 U	5 U	11.9	20.6	6.8	1 U	53
MW-117C	10/04/93		2 U	17	2 U	13	23	2 U	5 U	2 U	50	75		178
MW-117C	04/22/99		0.77	54	2.3	44	69	2 U	4 U	6	75	36	0.79 J	288
MW-117C	10/18/99		5 U	60	5 U	53	82	5 U	10 U	7.5	94	40	0.96 J	337
MW-117C	02/16/00		0.82 J	61	5 U	53	94	0.5 J	0.8 J	9.7	93	41	0.9 J	355
MW-117C	04/18/00		0.79 J	54	2.2 J	49	94	0.6 J	10 JB	10	91	39	0.82 J	351
MW-117C	07/24/00		1	55	2.4	48	99	1.1	10 U	8.7	89	38	0.63 J	343
MW-117C	11/07/00		0.79	69	2.4	50	100	5 U	10 U	8.8	78	34	0.74 J	344
MW-117C	04/09/01		0.84	57	2.3	59	120	0.82	10 U	12	99	42	0.72 J	394

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-117C	10/15/01		0.81	48	5 U	45	110	0.44	10 U	11	74	32	0.67 J	322
MW-117C	04/16/02		0.75	41	1.6	469	120	0.74	0.3	16	82	34	0.42 J	766
MW-117C	10/07/02		20 U	59	20 U	330	150	20 U	32	22	110	42	0.6 J	746
MW-117C	04/22/03		0.85 J	43.6 E	1.35	63.6 E	134 E	1.71	2 U	27.1 E	113 E	48 E	0.67 J	434
MW-117C	04/22/03	Dilution	10 U	40	10 U	58.2	123	10 U	20 U	23.1	93	44.3	10 U	382
MW-117C	12/22/03	Dilution	10 U	33.1 D	10 U	43.3 D	107 D	10 U	10 U	19.9 D	78.2 D	34.8 D	10 U	316
MW-117C	12/22/03		0.82 J	39.6 E	1.01	55.8 E	126 E	2.07	1 U	27.5 E	104 E	46.4 E	1 U	403
MW-117C	04/28/04		10 U	30.5	10 U	37	97.3	10 U	20 U	20.3	66.4	30.1	10 U	282
MW-117C	05/21/05		1 U	28	1 U	34	91	1 U	2 U	22	59	27	1 U	261
MW-117C	10/19/05		1 U	25	1 U	29	84	1 U	2 U	20	54	26	1 U	238
MW-117C	05/06/06		1 U	25	1 U	26	91	1 U	2 U	21	50	26	1 U	239
MW-117C	11/21/06		1 U	41	1 U	46	140	1 U	2 U	36	100	44	1 U	407
MW-117C	10/06/07		0.5	24	0.3	30	88	0.9	2 U	24	60	26	1 U	254
MW-117C	05/17/08		5 U	28	5 U	33	99	5 U	10	30	72	30	5 U	302
MW-117C	11/28/08		0.55 J	24.1	0.26 J	25.6	85.9	0.31 J	1 U	26.5	57.1	23.1	1 U	243
MW-117C	06/09/09		0.51 J	24	0.23 J	25	70	0.33 J	1 U	26	58	23	1 U	227
MW-117C	11/24/09		0.48 J	23	1 U	24	57	1 U	1 U	26	51	21	1 U	202
MW-117C	06/24/10		0.42 J	24	1 U	23	40	0.24 J	1 U	28	51	20	1 U	187
MW-117C	11/24/10		0.38 J	22	1 U	22	34	1 U	1 U	27	53	21	1 U	179
MW-117C	05/31/11		0.45 J	25	1 U	21	24	1 U	1 U	27	47	19	1 U	163
MW-117C	12/22/11		0.38 J	23	1 U	17	13	1 U	5 U	25	37	17	1 U	132
MW-117C	06/26/12		0.4 J	25	1 U	17	14	1 U	5 U	23	37	15	1 U	131
MW-117C	11/25/12		0.35 J	29	1 U	17	7.4	1 U	5 U	22	36	14	1 U	126
MW-117C	05/30/13		1 U	33	1 U	14	12	1 U	5 U	16	27	10	1 U	112
MW-117C	11/29/13		1 U	34	1 U	13	4.7	1 U	5 U	23	23	13	1 U	111
MW-117C	06/05/14		0.32 J	38	1 U	13	4.6	0.28 J	5 U	24	26	14	1 U	120
MW-117C	11/21/14		0.29 J	39	1 U	13	4.5	1 U	5 U	22	25	12	1 U	116
MW-117C	06/08/15		0.25 J	55	1 U	12	3.8	0.19 J	5 UB	21	19	12	1 U	123
MW-117C	11/09/15		0.26 J	50	1 U	11	3	0.31 J	0.49 J	18	24	11	1 U	118
MW-117C	06/27/16		0.24 J	44	1 U	11	2.1	1 U	5 U	16	23	8.8	1 U	105
MW-117C	11/11/16		0.29 J	46	1 U	11	2.2	1 U	5 U	15	24	9.4	1 U	108
MW-117C	06/06/17		0.23 J	45	1 U	11	2	1 U	5 UB	16	22	8.7	1 U	105
MW-117C	11/16/17		0.28 J	50.6	1 U	11.3	2.2	1 U	1 U	17.7	28.2 J	10.4	1 U	121

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-117C	06/18/18		1 U	40.4	1 U	10	1.8	1 U	1 U	17.3	23.5	8.9	1 U	102
MW-117C	11/12/18		1 U	34.2	1 U	9.2	1.6	1 U	1 U	17.5	23.4	8	1 U	94
MW-117C	06/21/19		1 U	28.4	1 U	6.7	4	1 U	5 U	7.5	10.9	4.6	1 U	62
MW-117C	12/10/19		1 U	23.2	1 U	1 U	1 U	1 U	5 U	1 U	6	2.7	1 U	32
MW-117C	06/23/20		1 U	20.5	1 U	3.7	1.1	1 U	5 U	5.6	10.6	3.5	0.47 J	45
MW-117C	11/13/20		1 U	11.7	1 U	2.1	0.9 J	1 U	5 U	3.4	6.9	2.2	1 U	27
MW-117D	04/22/99		0.74	46	2	50	110	2 U	4 U	17	110	38	2 U	374
MW-117D	10/18/99		10 U	39	10 U	44	110	10 U	1.5 J	17	97	35	10 U	344
MW-117D	02/17/00		0.8 J	34	1.4 J	41	100	5 U	10 U	19	91	35	0.45 J	323
MW-117D	04/18/00		0.63 J	29	1.1 J	35	90	5 U	10 JB	17	82	32	0.38 J	297
MW-117D	07/24/00		0.85	27	1.2	36	81	5 U	10 U	16	80	35	5 U	277
MW-117D	11/07/00		0.6	37	1	33	87	5 U	10 U	16	71	30	5 U	276
MW-117D	04/09/01		0.65	29	5 U	37	88	0.39	10 U	13	80	31	5 U	279
MW-117D	10/16/01		0.53	23	5 U	25	75	5 U	10 U	17	57	23	5 U	221
MW-117D	04/16/02		0.61	21	5 U	24	72	5 U	10 U	18	58	23	5 U	217
MW-117D	10/07/02		10 U	36	10 U	180	100	10 U	18	24	87	29	1 U	474
MW-117D	04/22/03		0.64 J	29.8 E	0.7 J	43.1 E	95.8 E	1 U	2 U	6.41	78.7 E	32.4 E	1 U	288
MW-117D	04/22/03	Dilution	5 U	28.3	5 U	36.7	83.1	5 U	10 U	4.62 J	64.5	26	5 U	243
MW-117D	12/22/03		0.61 J	28.1 E	1 U	30.4 E	102 E	1 U	1 U	30.1 E	84.2 E	31.2 E	1 U	307
MW-117D	12/22/03	Dilution	5 U	29 D	5 U	32.8 D	110 D	5 U	5 U	29.6 D	85.1 D	31.2 D	5 U	318
MW-117D	04/28/04		5 U	28.6	5 U	37.7	105	5 U	10 U	17.4	75.5	33.2	5 U	297
MW-117D	05/21/05		1 U	20	1 U	24	84	1 U	2 U	21	60	24	1 U	233
MW-117D	10/19/05		1 U	24	1 U	21	73	1 U	2 U	24	58	22	1 U	222
MW-117D	05/06/06		1 U	23	1 U	17	67	1 U	2 U	22	52	20	1 U	201
MW-117D	05/06/06	Fld Dupe	1 U	18	1 U	30	52	1 U	2 U	23	70	33	1 U	226
MW-117D	11/21/06		1 U	27	1 U	22	76	2.1	2 U	31	89	32	1 U	279
MW-117D	10/06/07		0.4	22	0.3	22	71	1	2 U	15	62	29	1 U	223
MW-117D	05/17/08		5 U	24	5 U	24	31	5 U	12	30	62	23	5 U	206
MW-117D	11/28/08		0.46 J	23.3	1 U	19.5	23.5	0.27 J	1 U	28.6	58	19.4	1 U	173
MW-117D	06/09/09		0.49 J	25	1 U	18	13	1 U	1 U	30	55	20	1 U	161
MW-117D	11/24/09		0.49 J	29	1 U	19	11	1 U	1 U	28	49	18	1 U	154
MW-117D	06/24/10		0.33 J	28	1 U	16	5.3	0.18 J	1 U	29	46	15	1 U	140
MW-117D	11/24/10		0.34 J	30	1 U	16	5.6	1 U	1 U	29	45	17	1 U	143

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-117D	05/31/11		1 U	37	1 U	13	5.4	1 U	1 U	26	39	15	1 U	135
MW-117D	12/22/11		0.34 J	38	1 U	10	3.8	1 U	5 U	23	31	13	1 U	119
MW-117D	06/26/12		0.41 J	43	1 U	11	2.8	1 U	5 U	22	33	12	1 U	124
MW-117D	11/25/12		0.32 J	48	1 U	12	3	1 U	5 U	19	34	11	1 U	127
MW-117D	05/30/13		0.31 J	52	1 U	11	2.9	1 U	5 U	17	36	10	1 U	129
MW-117D	11/29/13		0.33 J	51	1 U	12	2.9	1 U	5 UB	18	33	9.9	1 U	127
MW-117D	06/05/14		0.3 J	45	1 U	10	2.6	1 U	5 U	19	34	10	1 U	121
MW-117D	11/22/14		0.28 J	48	1 U	12	2.3	1 U	5 U	18	35	10	1 U	126
MW-117D	06/08/15		0.31 J	47	1 U	10	2.2	0.2 J	5 UB	19	31	9.6	1 U	119
MW-117D	11/09/15		0.28 J	38	1 U	8.6	2	0.2 J	0.66 J	18	27	8.9	1 U	104
MW-117D	06/27/16		1 U	35	1 U	8.6	1.7	1 U	5 U	15	26	8	1 U	94
MW-117D	11/11/16		0.23 J	34	1 U	8.2	1.7	1 U	0.25 J	14	26	8.2	1 U	93
MW-117D	06/06/17		1 U	31	1 U	7.6	1.6	1 U	5 U	16	24	7.3	1 U	88
MW-117D	11/16/17		0.23 J	36.8	1 U	8.6	1.7	1 U	1 U	15.4	27.9 J	8.3	1 U	99
MW-117D	06/18/18		1 U	28.4	1 U	7.5	1.6	1 U	1 U	14.9	22.7	7.3	1 U	82
MW-117D	11/12/18		1 U	24.5	1 U	6.9	1.5	1 U	1 U	15	23.1	7	1 U	78
MW-117D	06/21/19		1 U	19.1	1 U	6	1 U	1 U	5 U	11.4	18.7	5.7	1 U	61
MW-117D	12/10/19		1 U	18.7	1 U	5.1	1.1	1 U	5 U	13.5	18	5.8	1 U	62
MW-117D	06/23/20		1 U	18.8	1 U	5.1	1 U	1 U	5 U	10.6	19.3	5.7	1 U	60
MW-117D	11/13/20		1 U	14.7	1 U	4.9	1 U	1 U	5 U	11.7	18.2	5.6	1 U	55
MW-119	10/11/93		12 U	12 U	12 U	12 U	12 U	12 U	25 U	12 U	12 U	12 U		0
MW-119	05/03/99		1 U	1 U	1 U	1 U	0.36	1 U	2 U	0.63	1.8	1	5 U	4
MW-119	10/27/99		0.26 J	0.39 J	1 U	0.28 J	1.3	1 U	2 U	1.4	2.6	2	1 U	8
MW-119	01/26/00		0.19 J	0.21 J	1 U	1 U	1 U	1 U	2 U	0.18 J	0.75 J	0.2 J	1 U	2
MW-119	04/17/00		0.16 J	0.23 J	1 U	1 U	1 U	1 U	2 JB	0.19 J	0.79 J	0.2 J	1 U	4
MW-119	07/25/00		0.12	0.26	1 U	1 U	1 U	1 U	2 U	0.22	0.88	0.21	1 U	2
MW-119	11/08/00		1 U	0.27	1 U	1 U	1 U	1 U	2 U	0.18	0.72	0.18	1 U	1
MW-119	04/10/01		1 U	0.26	1 U	1 U	1 U	1 U	2 U	0.17	0.85	0.19	1 U	1
MW-119	10/16/01		0.1	0.29	1 U	1 U	1 U	1 U	2 U	0.15	0.71	0.16	1 U	1
MW-119	04/30/02		0.1	0.31	1 U	1 U	1 U	1 U	2 U	0.18	0.95	0.17	1 U	2
MW-119	10/17/02		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-119	04/22/03		1.07	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1	1 U	1 U	2
MW-119	12/30/03		7.22	0.67 J	1 U	0.54 J	0.59 J	1 U	1 U	1 U	0.72 J	1 U	1 U	10

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-119	04/28/04		1.67	0.51	1 U	1 U	1 U	1 U	2 U	1 U	0.62	1 U	1 U	3
MW-119	05/21/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1.3	1 U	1 U	1
MW-119	10/20/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1.3	1 U	1 U	1
MW-119	05/06/06		1 U	1.2	1 U	1 U	1 U	1 U	2 U	1 U	1.1	1 U	1 U	2
MW-119	01/04/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-119	10/08/07		1 U	1	1 U	1 U	0.4	1 U	2 U	1 U	1	1 U	1 U	2
MW-119	05/18/08		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1	1 U	1 U	1
MW-119	11/29/08		0.3 J	0.98 J	1 U	1 U	0.54 J	1 U	1 U	1 U	1.29	0.27 J	1 U	3
MW-119	06/10/09		0.64 J	1	1 U	1 U	0.66 J	1 U	1 U	1 U	1.2	0.29 J	1 U	4
MW-119	11/29/09		0.45 J	1.4	1 U	1 U	0.61 J	1 U	1 U	1 U	1.2	1 U	1 U	4
MW-119	06/29/10		1 U	0.92 J	1 U	1 U	1.2	1 U	1 U	1 U	1.1	1 U	1 U	3
MW-119	11/27/10		0.46 J	1.1	1 U	1 U	1.1	1 U	1 U	1 U	1.7	0.42 J	1 U	5
MW-119	06/03/11		0.32 J	0.97 J	1 U	1 U	0.69 J	1 U	1 U	1 U	1.4	0.37 J	1 U	4
MW-119	12/29/11		0.29 J	1	1 U	1 U	0.69 J	1 U	5 U	1 U	1	0.34 J	1 U	3
MW-119	06/27/12		0.29 J	0.97 J	1 U	1 U	0.88 J	1 U	5 U	1 U	1.1	1 U	1 U	3
MW-119	11/25/12		0.13 J	0.99 J	1 U	1 U	0.8 J	1 U	5 U	1 U	1.2	0.32 J	1 U	3
MW-119	05/31/13		1 U	1.3	1 U	1 U	0.97 J	1 U	5 U	1 U	1.3	1 U	1 U	4
MW-119	12/01/13		1 U	0.93 J	1 U	1 U	0.61 J	1 U	5 U	1 U	0.94 J	0.35 J	1 U	3
MW-119	06/14/14		0.25 J	1.6	1 U	1 U	0.57 J	1 U	5 UB	0.16 J	1.4	0.33 J	1 U	4
MW-119	11/22/14		0.29 J	1.4	1 U	1 U	0.47 J	1 U	5 U	1 UB	1.6	0.46 J	1 U	4
MW-119	06/13/15		1 U	1.1	1 U	1 U	0.33 J	1 U	5 U	1 U	1.1	0.27 J	1 U	3
MW-119	11/15/15		1 U	1	1 U	1 U	0.32 J	1 U	0.46 J	1 U	1.4	0.3 J	1 U	3
MW-119	06/27/16		1 U	0.76 J	1 U	1 U	1 U	1 U	5 U	1 U	1	0.31 J	1 U	2
MW-119	11/12/16		1 U	0.66 J	1 U	1 U	1 U	1 U	5 U	1 U	0.92 J	0.29 J	1 U	2
MW-119	06/04/17		1 U	1.1	1 U	1 U	0.31 J	1 U	5 U	1 U	1.1	1 U	1 U	3
MW-119	11/24/17		1 U	1.2	1 U	0.28 J	0.36 J	1 U	1 U	1 U	1.7	0.33 J	1 U	4
MW-119	06/21/18		1 U	1.3	1 U	1 U	0.38 J	1 U	1 U	1 U	1.6	0.39 J	1 U	4
MW-119	11/10/18		1 U	1.1	1 U	1 U	0.35 J	1 U	1 U	1 U	1.9	0.37 J	1 U	4
MW-119	06/23/19		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	2.1	1 U	1 U	2
MW-119	12/14/19		1 U	1	1 U	1 U	1 U	1 U	5 U	1 U	2	1 U	1 U	3
MW-119	06/22/20		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-119	11/14/20		1 U	1.1	1 U	1 U	1 U	1 U	5 U	1 U	2	0.43 J	1 U	4

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-121	10/15/93		2 U	2 U	2 U	2 U	27	2 U	5 U	4	7	82		120
MW-121	04/28/99		5 U	3.4	5 U	6	7.2	5 U	10 U	2.7	3.8	26	5 U	49
MW-121	10/26/99		0.67 J	3.8	0.78 J	8	8.4	0.15 J	2 U	3.4	5.5	33 E	1 U	64
MW-121	10/26/99	Dilution	2 U	3.2 D	0.67 DJ	6.6 D	6.8 D	0.1 DJ	4 U	2.9 D	4.4 D	29 D	2 U	54
MW-121	01/31/00		0.65 J	2.9	2 U	5.5	6.3	0.2 J	0.41 J	2.5	3.4	23	2 U	45
MW-121	04/18/00		0.55 J	2.8	0.72 J	3	5.6	0.22 J	2 JB	0.64 J	2.8	11	1 U	29
MW-121	07/25/00		0.68	3.5	0.82	4.4	6.8	0.39	2 U	1.8	4.3	20	1 U	43
MW-121	11/08/00		0.77	4.6	0.89	8	7	0.22	2 U	2.6	5.1	22	1 U	51
MW-121	04/10/01		0.78	3.7	0.82	2	6.7	0.68	2 U	2.3	5.5	22	1 U	44
MW-121	10/16/01		0.82	3.8	0.81	3.6	6.5	0.42	2 U	2.4	5.9	19	1 U	43
MW-121	04/17/02		0.75	3.8	0.07	3	6.1	0.58	2 U	2.6	6.9	20	0.064 J	44
MW-121	10/17/02		5 U	5	5 U	42	7	5 U	2 U	3	9	24	1 U	90
MW-121	04/22/03		0.65 J	4.3	0.55 J	7.28	5.74	1 U	2 U	2.85	7.18	22.6	1 U	51
MW-121	12/28/03		1 U	4.76	1 U	5.11	4.61	1 U	1 U	2.74	5.79	20.3	0.68 J	44
MW-121	04/28/04		0.52	4.37	1 U	4.58	4.79	1 U	2 U	2.43	5.84	18.8	1 U	41
MW-121	05/21/05		1 U	2.2	1 U	3.9	5.2	1 U	2 U	1.9	5.1	18	1 U	36
MW-121	05/21/05	Fld Dupe	1 U	2.4	1 U	4.8	5.3	1 U	2 U	2.1	6	20	1 U	41
MW-121	10/20/05		1 U	2.9	1 U	3.9	5.9	1 U	2 U	2.1	5.7	20	1 U	41
MW-121	05/06/06		1 U	2.5	1 U	3.3	5.3	1 U	2 U	2.3	4.8	22	1 U	40
MW-121	01/03/07		1 U	1.4	1 U	1.7	3	1 U	2 U	1.9	3.9	20	1 U	32
MW-121	10/07/07		0.7	2	1 U	2	6	0.4	2 U	2	5	22	1 U	40
MW-121	05/18/08		1 U	2	1 U	2	7	1 U	2 U	2	6	26 E	1 U	45
MW-121	05/18/08	Dilution	2 U	2 D	2 U	3 D	6 D	2 U	3 DJ	2 D	5 D	25 D	2 U	46
MW-121	11/29/08		0.56 J	1.36	1 U	1 U	3.42	0.55 J	1 U	1.84	2.67	14.4	1 U	25
MW-121	06/11/09		0.65 J	1.9	1 U	1 U	4.8	0.76 J	1 U	2.3	4	23	1 U	37
MW-121	11/25/09		0.63 J	2.1	1 U	1.8	4.3	1 U	1 U	2	3.1	20	1 U	34
MW-121	06/29/10		1 U	2.9	1 U	1.7	3.7	1 U	1 U	1.5	2	16	1 U	28
MW-121	11/25/10		0.6 J	4.6	1 U	2.5	4.3	1 U	1 U	2.1	3.4	22	1 U	40
MW-121	06/03/11		0.63 J	9.6	1 U	4.1	4.7	0.42 J	1 U	1.8	4.2	19	1 U	44
MW-121	12/29/11		0.75 J	15	1 U	6.9	4.9	0.51 J	5 U	1.8	6.6	18	1 U	54
MW-121	06/27/12		0.86 J	21	1 U	5.5	5.1	0.62 J	5 U	1.6	10	19	1 U	64
MW-121	11/25/12		0.76 J	23	1 U	3	5.3	0.74 J	5 U	1.5	12	18	1 U	64
MW-121	05/31/13		0.84 J	29	1 U	9.9	6.2	0.54 J	5 U	1.6	15	22	1 U	85

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-121	12/01/13		0.74 J	29	1 U	6.6	5.9	0.57 J	5 U	1.6	15	22	1 U	81
MW-121	06/04/14		0.82 J	37	1 U	13	7.1	0.71 J	5 U	1.9	22	26	1 U	109
MW-121	11/23/14		0.84 J	42	1 U	8.7	6.4	0.92 J	5 U	1.6	20	25	1 U	105
MW-121	06/13/15		0.74 J	45	1 U	18	5.8	0.62 J	5 UB	1.6	22	25	1 U	119
MW-121	11/15/15		0.27 J	16	1 U	5.5	1.9	1 U	0.71 J	1.5	11	17	1 U	54
MW-121	06/26/16		0.66 J	54	1 U	21	4.6	0.76 J	5 U	1.4	26	25	1 U	133
MW-121	11/17/16		0.71 J	61	1 U	22	4.9	0.75 J	5 U	1.7	30	29	1 U	150
MW-121	06/04/17		0.65 J	68	1 U	26	4.5	0.77 J	5 U	1.5	29	26	1 U	156
MW-121	11/24/17		0.63 J	68.7	1 U	31.4	4.7	0.81 J	1 U	1.4	31.6	28.7	1 U	168
MW-121	06/17/18		0.62 J	83.4	1 U	34.6	4.9	0.91 J	1 U	1.6	34.9	33.6	1 U	195
MW-121	11/11/18		1 U	79.7	1 U	38.2	4.7	0.93 J	1 U	1.6	37.5	32.4	1 U	195
MW-121	06/23/19		1 U	1 U	1 U	41.2	4.7	1 U	5 U	1 U	37.4	32.7	1 U	116
MW-121	12/08/19		1 U	101	1 U	41.2	5.4	1 U	5 U	1.5	43.4	35.7	1 U	228
MW-121	06/21/20		1 U	118	1 U	50.3	5.4	1.2	5 U	1.2	46.3	41.2	1 U	264
MW-121	11/15/20		1 U	92.5	1 U	50.9	5.2	1	5 U	1.4	46.3	40.3	1 U	238
MW-124	10/18/93		120 U	150	120 U	410	210		120 U	50	1400	140		2360
MW-124	04/28/99		10 U	75	10 U	97	1200	10 U	20 U	47	540	36	3.4 J	1998
MW-124	04/28/99	Fld Dupe	10 U	75	10 U	97	1100 D	10 U	20 JBU	47	540 D	36	3.4 J	1898
MW-124	10/27/99		50 U	50	50 U	41 J	560	50 U	8.2 J	28 J	280	28 J	6.9 J	1002
MW-124	01/31/00		25 U	95	25 U	36	540	25 U	50 U	12 J	190	20 J	44	937
MW-124	04/24/00		0.72 J	92	25 U	24 J	440	3.9 J	50 JB	3.8 J	100	14 J	63	791
MW-124	07/25/00		20 U	89	20 U	20	330	20 U	40 U	20 U	79	10	60	588
MW-124	11/13/00		20 U	110	20 U	20	300	20 U	40 U	2.7	75	12	63	583
MW-124	04/12/01		20 U	47	20 U	35	240	2.1	40 U	30	230	24	13 J	621
MW-124	10/29/01		10 U	98	10 U	19	190	1.4	20 U	6.2	110	16	76	517
MW-124	04/17/02		20 U	64	20 U	35	370	12	40 U	30	210	26	16 J	763
MW-124	04/17/02	Fld Dupe	20 U	65	20 U	41	370	5.7 J	40 U	30	200	20 U	18 J	730
MW-124	10/17/02		20 U	92	20 U	230	360	20 U	40 U	35	290	33	21	1061
MW-124	04/25/03		1 U	83.4 E	1.32	30 E	226 E	8.35	2 U	13.8	136 E	20.9	62.7 E	582
MW-124	04/25/03	Dilution	10 U	71.4	10 U	26.4	213	10 U	20 U	13.5	119	18.9	39.2	501
MW-124	12/28/03		1 U	109 E	1.34	22.8	174 E	6.96	1 U	11.2	116 E	19.2	67.2 E	528
MW-124	12/28/03	Dilution	10 U	83.2 D	10 U	20.1 D	176 D	10 U	10 U	10.6 D	94.7 D	15.6 D	40 D	440
MW-124	04/28/04		40 U	197	40 U	43.6	389	40 U	80 U	34.6	185	26.7	24 J	900

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-124	05/21/05		5 U	340	5 U	37	420	5 U	10 U	8.4	120	18	110	1053
MW-124	10/20/05		1 U	250	1 U	25	260	1.5	2 U	6.6	76	15	75 H	709
MW-124	05/06/06		1 U	320	1.2	29	370	1.5	2 U	15	120	18	61	936
MW-124	01/04/07		10 U	370	10 U	15	250	10 U	20 U	10 U	110	10	10 U	755
MW-124	10/07/07		1 U	620	0.7	28	300	4	2 U	8	100	12	120	1193
MW-124	05/18/08		40 U	870	40 U	42	320	40 U	80 U	40 U	190	40 U	64	1486
MW-124	11/29/08	Dilution	5 U	415	5 U	16.1	144	1.4 J	1.45 J	11.8	90	10.4	32.1	722
MW-124	06/10/09	Dilution	1 J	500	5 U	18	150	5 U	5 U	14	100	10	23	816
MW-124	11/29/09	Dilution	5 U	510	5 U	22	170	5 U	5 U	16	98	9.4	21	846
MW-124	06/29/10	Dilution	5 U	500	5 U	20	220	5 U	1.9 J	14	82	8.6	30	877
MW-124	11/27/10	Dilution	5 U	490	5 U	25	280	5 U	5 U	14	95	9.2	30	943
MW-124	06/03/11	Dilution	5 U	450	5 U	28	240	5 U	2.4 J	13	120	7.4	23	884
MW-124	12/29/11	Dilution	5 U	370	5 U	20	130	5 U	25 U	12	96	5.9	17	651
MW-124	06/27/12	Dilution	5 U	420	5 U	17	100	5 U	25 U	9.5	90	5.2	23	665
MW-124	11/25/12	Dilution	2 U	330	2 U	9.6	70	0.9 J	1 J	5.2	50	4.3	30	501
MW-124	06/04/13	Dilution	2.5 U	350	2.5 U	13	92	2.5 U	5.8 J	10	84	4.9	14	574
MW-124	12/01/13	Dilution	2.5 U	280	2.5 U	8.6	82	2.5 U	12 UB	7.4	40	4.1	20	442
MW-124	06/14/14	Dilution	2.5 U	480	2.5 U	9.2	120	0.9 J	12 UB	7.8	49	4.3	41	712
MW-124	11/23/14	Dilution	2.5 U	420	2.5 U	10	130	1.2 J	12 UB	7.8	41	4.9	31	646
MW-124	06/13/15	Dilution	2.5 U	200	2.5 U	6.6	63	0.8 J	12 UB	9.1	39	4.6	9.2	332
MW-124	11/15/15		1 U	85	1 U	4.8	29	0.56 J	5 UB	8	28	3.3	3.9	163
MW-124	06/26/16		1 U	53	1 U	5.6	18	0.53 J	5 U	9.1	30	3.5	2.2	122
MW-124	11/12/16		1 U	50	1 U	6	22	0.68 J	0.31 J	8.4	29	3.8	2.6	123
MW-124	11/17/16	Fld Dupe	1 U	37	1 U	4.7	17	0.51 J	5 U	8.1	29	3.8	2.3	102
MW-124	06/04/17		1 U	42	1 U	5.8	20	0.64 J	5 U	8.9	26	3.4	2.3	109
MW-124	11/24/17		1 U	35.5	1 U	6.3	18.6	0.71 J	1 U	8.2	24	3.4	2.1	99
MW-124	06/17/18		1 U	22.2	1 U	5.4	10.5	0.34 J	1 U	10.1	27.1	3.3	1.2	80
MW-124	11/12/18		1 U	26.9	1 U	5.5	14	0.55 J	1 U	10.3	28	3.2	1.3	90
MW-124	06/16/19		1 U	27.4	1 U	5.5	14.7	0.58 J	5 U	7.9	25.2	2.6	1.4	85
MW-124	12/08/19		1 U	31.4	1 U	4.9	15.5	1 U	5 U	8.1	23.1	2.7	1 U	86
MW-124	06/21/20		1 U	25.6	1 U	5.3	13.6	1 U	5 U	7.9	25.9	2.9	1.2	82
MW-124	11/18/20		1 U	26	1 U	4.8	14.5	0.51 J	5 U	9	22.1	2.8	2	82

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-130	10/19/93		67 U	26	67 U	10	25		8	67 U	1000	28		1097
MW-130	04/28/99		0.19	19	1 U	11	24	1 U	2 U	5.3	670	17	1 U	746
MW-130	04/28/99	Fld Dupe	0.17 J	18	1 U	10	23 DJ	1 U	2 U	5.3	670 D	17	1 U	743
MW-130	10/28/99		25 U	10 J	25 U	4.9 J	7.8 J	25 U	50 U	25 U	370	8.2 J	25 U	401
MW-130	02/16/00		25 U	11 J	25 U	3.6 J	7.5 J	25 U	50 U	25 U	460	8.5 J	25 U	491
MW-130	04/24/00		50 JB	12 J	50 U	3.1 J	7.7 J	50 U	100 JB	50 U	510	8.3 J	50 U	691
MW-130	07/27/00		20 U	13	20 U	3.3	7.7	20 U	40 U	20 U	670	8.5	20 U	703
MW-130	11/14/00		25 U	12	25 U	4.3	7.2	25 U	50 U	25 U	390	7	25 U	421
MW-130	04/12/01		20 U	10	20 U	20 U	5.7	20 U	40 U	20 U	440	6.2	20 U	462
MW-130	10/30/01		50 U	14	50	50 U	50 U	50 U	100 U	50 U	660	50 U	50 U	724
MW-130	10/30/01	Fld Dupe	50 U	15 J	50 U	50 U	6.5 J	50 U	100 U	50 U	610	8.1 J	50 U	640
MW-130	04/30/02		25 U	11	25 U	1.6	5.7	25 U	50 U	0.97	360	5.4	25 U	385
MW-130	10/17/02		50 U	50 U	50 U	54	50 U	50 U	43	50 U	840	50 U	1 U	937
MW-130	04/25/03	Dilution	20 U	11.6 J	20 U	20 U	20 U	20 U	40 U	20 U	322	20 U	20 U	334
MW-130	04/25/03		0.1 J	13	1 U	5.33	7.5	0.48 J	2 U	1.37	424 E	5.94	1 U	458
MW-130	04/25/03	Fld Dupe	0.11 J	13.2	1 U	20 U	7.84	20 U	2 U	20 U	341	20 U	20 U	362
MW-130	12/28/03		1 U	12.1	1 U	5.65	8.09	1 U	1 U	1.11	320 E	5.46	1 U	352
MW-130	12/28/03	Dilution	20 U	10.3 JD	20 U	20 U	20 U	20 U	20 U	20 U	263 D	20 U	20 U	273
MW-130	04/28/04		10 U	11	10 U	10 U	10.6	10 U	20 U	10 U	157	10 U	10 U	179
MW-130	05/21/05		1 U	14	1 U	4	11	1 U	2 U	1 U	210	3.5	1 U	243
MW-130	10/20/05		1 U	16	1 U	4.2	14	1 U	2 U	1 U	210	3.6	1 U	248
MW-130	05/08/06		1 U	16	1 U	4.1	14	1 U	2 U	1 U	140	3.6	1 U	178
MW-130	01/04/07		1 U	20	1 U	4.6	18	1 U	2 U	1 U	160	4.3	1 U	207
MW-130	10/07/07		1 U	17	1 U	5	21	0.6	2 U	0.6	170	4	1 U	218
MW-130	05/17/08		10 U	22	10 U	10 U	25	10 U	20 U	10 U	200	10 U	10 U	247
MW-130	11/29/08	Dilution	2 U	21.9	2 U	4.18	21	0.4 J	0.56 J	0.56 J	198	4.26	2 U	251
MW-130	06/11/09	Dilution	0.48 J	26	2 U	4.3	20	2 U	2 U	0.9 J	300	4.3	2 U	356
MW-130	11/29/09	Dilution	2 U	31	2 U	5.5	12	2 U	2 U	2 U	320	3.3	2 U	372
MW-130	06/29/10	Dilution	10 U	70	10 U	15	17	10 U	2.9 J	10 U	1100	7.6 J	10 U	1213
MW-130	11/27/10	Dilution	5 U	29	5 U	8.4	8.3	5 U	5 U	5 U	430	3.6 J	5 U	479
MW-130	06/03/11	Dilution	2.5 U	20	2.5 U	5.4	6.5	2.5 U	1 J	2.5 U	250	3.8	2.5 U	287
MW-130	12/28/11		1 U	9.7	1 U	2.7	4.1	1 U	5 U	0.68 J	100	2.7	1 U	120
MW-130	06/25/12		0.26 J	7.7	1 U	1.9	3	1 U	5 U	0.65 J	68	2.1	1 U	84

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-130	11/24/12		1 U	7.5	1 U	1.7	2.5	1 U	5 U	0.64 J	47	1.9	1 U	61
MW-130	06/07/13		1 U	7.6	1 U	1.5	2.2	1 U	5 U	0.7 J	32	1.8	1 U	46
MW-130	12/01/13		1 U	8.4	1 U	1.2	2.2	1 U	5 U	0.65 J	16	1.6	1 U	30
MW-130	06/14/14		1 U	12	1 U	1.4	2.5	0.29 J	5 UB	0.49 J	13	1.7	1 U	31
MW-130	11/23/14		0.34 J	12	1 U	1.5	2.5	1 U	5 U	1 UB	9.3	1.8	1 U	27
MW-130	06/13/15		0.34 J	9.7	1 U	1.4	2	0.25 J	5 U	0.53 J	13	1.6	1 U	29
MW-130	11/15/15		0.27 J	9.4	1 U	0.85 J	1.9	0.3 J	0.48 J	0.43 J	9.5	1.4	1 U	25
MW-130	06/28/16		0.24 J	9.7	1 U	1.4	2	1 U	5 U	0.44 J	7.4	1.5	1 U	23
MW-130	11/13/16		1 U	9.8	1 U	1.2	1.9	1 U	0.27 J	0.4 J	7.6	1.6	1 U	23
MW-130	06/05/17		1 U	12	1 U	1.9	2	1 U	5 U	0.45 J	9.1	1.5	1 U	27
MW-130	11/24/17		1 U	14.5	1 U	3.1	1.9	0.3 J	1 U	0.47 J	9.7	1.6	1 U	32
MW-130	06/21/18		1 U	11.3	1 U	2.7	1.9	1 U	1 U	0.39 J	6.3	1.6	1 U	24
MW-130	11/10/18		1 U	8.8	1 U	1.7	1.6	1 U	1 U	0.48 J	6.2	1.5	1 U	20
MW-130	06/22/19		1 U	5.3	1 U	1 U	1 U	1 U	5 U	1 U	4.2	1 U	1 U	10
MW-130	12/14/19		1 U	5.4	1 U	0.65 J	0.97 J	1 U	5 U	1 U	4.3	0.92 J	1 U	12
MW-130	06/22/20		1 U	4.3	1 U	1 U	1 U	1 U	5 U	1 U	1 U	0.65 J	1 U	5
MW-130	11/17/20		1 U	3.5	1 U	1 U	0.62 J	1 U	5 U	0.94 J	2.9	1 U	1 U	8
MW-133A	10/20/93		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	0.8	1 U		1
MW-133A	04/26/99		1 U	1 U	1 U	1 U	0.27	1 U	2 U	0.37	0.95	1.1	1 U	3
MW-133A	10/26/99		0.03 J	0.52 J	1 U	0.66 J	1.8	1 U	2 U	1	4.6	4.8	1 U	13
MW-133A	02/15/00		1 U	0.08 J	1 U	1 U	0.16 J	1 U	2 U	1 U	0.38 J	1 U	1 U	1
MW-133A	04/25/00		1 U	1 U	1 U	1 U	1 U	1 U	2 JB	1 U	0.35 J	1 U	1 U	2
MW-133A	07/27/00		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	10 U	0
MW-133A	11/16/00		1 U	1 U	1 U	1 U	0.49	1 U	2 U	1 U	0.81	0.11	1 U	1
MW-133A	04/10/01		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-133A	10/31/01		1 U	0.41	1 U	0.1	1.2	1 U	2 U	1 U	1	0.19	1 U	3
MW-133A	04/29/02		1 U	1 U	1 U	1 U	0.04	1 U	2 U	1 U	0.06	1 U	1 U	0
MW-133A	10/16/02		1 U	1	1 U	1 U	4	1 U	0.6	1 U	3	1 U	1 U	9
MW-133A	04/25/03		1 U	2.96	1 U	1.05	11.7	1 U	2 U	1 U	5.2	0.98 J	1 U	22
MW-133A	12/30/03		1 U	1.92	1 U	0.53 J	6.34	1 U	1 U	1 U	2.51	1 U	1 U	11
MW-133A	04/28/04		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-133A	05/02/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-133A	11/02/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-133A	06/22/06		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-133A	11/16/06		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-133A	10/07/07		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	0
MW-133A	05/17/08		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-133A	11/26/08		1 U	1 U	1 U	1 U	0.26 J	1 U	1 U	1 U	0.32 J	1 U	1 U	1
MW-133A	06/20/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	0
MW-133A	06/20/09	Fld Dupe	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	0
MW-133A	11/28/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	0
MW-133A	06/25/10		1 U	1 U	1 U	1 U	0.23 J	1 U	1 U	1 U	0.26 J	1 U	1 U	0
MW-133A	11/27/10		1 U	0.21 J	1 U	1 U	0.91 J	1 U	1 U	1 U	0.86 J	1 U	1 U	2
MW-133A	11/27/10	Fld Dupe	1 U	1 U	1 U	1 U	0.79 J	1 U	1 U	1 U	0.82 J	1 U	1 U	2
MW-133A	06/02/11		1 U	1 U	1 U	1 U	1 U	1 U	0.28 J	1 U	1 U	1 U	1 U	0
MW-133A	12/28/11		1 U	1 U	1 U	1 U	0.67 J	1 U	5 U	1 U	0.67 J	1 U	1 U	1
MW-133A	06/28/12		1 U	1 U	1 U	1 U	0.4 J	1 U	5 U	1 U	0.3 J	1 U	1 U	1
MW-133A	06/07/13		1 U	0.44 J	1 U	1 U	1 U	1 U	5 U	1 U	0.33 J	1 U	1 U	1
MW-133A	11/30/13		1 U	1 U	1 U	1 U	0.27 J	1 U	5 UB	1 U	0.39 J	1 U	1 U	1
MW-133A	06/13/14		1 U	1 U	1 U	1 U	1 U	1 U	5 UB	1 U	1 U	1 U	1 U	0
MW-133A	11/24/14		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-133A	06/15/15		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-133A	11/10/15		1 U	1 U	1 U	1 U	1 U	1 U	0.71 J	1 U	1 U	1 U	1 U	1
MW-133A	06/28/16		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-133A	11/16/16		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-133A	06/10/17		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-133A	11/24/17		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	0.34 J	1 U	1 U	0
MW-133A	06/21/18		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	0.31 J	1 U	1 U	0
MW-133A	11/11/18		1 U	0.34 J	1 U	1 U	1 U	1 U	1 U	1 U	0.76 J	1 U	1 U	1
MW-133A	06/23/19		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-133A	12/14/19		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	4	1 U	1 U	4
MW-133A	06/25/20		1 U	2.6	1 U	0.39 J	0.66 J	1 U	5 U	1 U	4	0.62 J	1 U	8
MW-133A	11/18/20		1 U	1.9	1 U	1 U	1 U	1 U	5 U	1 U	3.9	1 U	1 U	6
MW-133B	10/20/93		100 U	270	100 U	130	810		100 U	160	1200	380		2950
MW-133B	04/26/99		10	200	4.6	110	780	7	4 U	110	840	270	2 U	2332

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-133B	10/26/99		7.9 J	170	50 U	67	810	7.1 J	6.8 J	77	630	190	50 U	1966
MW-133B	02/15/00		9.3 J	180	50 U	100	840	50 U	100 U	120	730	250	50 U	2229
MW-133B	04/25/00		12 J	170	50 U	78	600	50 U	100 JB	76	620	190	50 U	1846
MW-133B	07/27/00		12	160	4.1	88	670	10	40 U	94	760	220	20 U	2018
MW-133B	11/16/00		11	200	25 U	88	530	9.5	50 U	94	570	230	25 U	1733
MW-133B	04/10/01		13	200	50 U	46	660	43	100 U	140	830	300	50 U	2232
MW-133B	10/31/01		12	180	50 U	7	510	49	100 U	110	700	250	50 U	1818
MW-133B	04/29/02		9.1	150	3.7	25 U	460	54	50 U	99	570	170	25 U	1516
MW-133B	10/16/02		50 U	250	50 U	650	820	50 U	31	140	800	290	1 U	2981
MW-133B	04/25/03		10.7	183 E	3.97	110 E	728 E	24.5	2 U	151 E	699 E	325 E	1 U	2235
MW-133B	04/25/03	Dilution	40 U	158	40 U	40.4	571	41.4	80 U	112	617	237	40 U	1777
MW-133B	12/30/03		9.91	162 E	1 U	93 E	562 E	16.3	1 U	122 E	510 E	250 E	1 U	1725
MW-133B	12/30/03	Dilution	50 U	151 D	50 U	81.6 D	623 D	50 U	50 U	109 D	577 D	240 D	50 U	1782
MW-133B	04/28/04		10 U	161	10 U	106	803	10 U	20 U	111	622	216	100 U	2019
MW-133B	05/02/05		5.6	120	5 U	70	630	17	10 U	81	460	160	5 U	1544
MW-133B	05/02/05	Fld Dupe	5.7	120	5 U	74	580	13	10 U	87	420	150	5 U	1450
MW-133B	11/02/05		8.2	180	5 U	98	930	28	10 U	110	620	220	5 U	2194
MW-133B	06/22/06	Fld Dupe	10 U	120	10 U	53	710	17	20 U	80	450	140	10 U	1570
MW-133B	06/22/06		10 U	110	10 U	54	720	11	20 U	68	430	120	10 U	1513
MW-133B	11/16/06		10 U	160	10 U	10 U	740	78	50 U	85	10 U	170	10 U	1233
MW-133B	10/07/07		6	160	3	84	930	38	2 U	110	600	200	1 U	2131
MW-133B	05/17/08		40 U	130	40 U	60	900	40 U	80 U	59	440	110	40 U	1699
MW-133B	11/26/08		8 J	308	5.4 J	12	1860	193	3.2 J	126	955	208	10 U	3679
MW-133B	06/20/09	Dilution	7.3 J	230	4.3 J	19	1400	140	10 U	110	710	170	10 U	2791
MW-133B	11/28/09	Dilution	7.8 J	280	20 U	100	2000	84	20 U	110	820	190	20 U	3592
MW-133B	06/25/10	Dilution	5.4 J	230	4 J	81	1700	47	20 U	96	680	150	20 U	2993
MW-133B	11/27/10	Dilution	20 U	240	20 U	120	1900	11 J	20 U	110	790	180	20 U	3351
MW-133B	06/02/11	Dilution	3.8 J	150	2.9 J	56	1200	29	11	70	420	120	10 U	2063
MW-133B	12/28/11	Dilution	4.9 J	180	3.9 J	5.3 J	1100	100	50 U	73	470	100	10 U	2037
MW-133B	06/28/12	Dilution	5.2 J	180	10 U	25	1200	60	11 J	65	470	92	10 U	2108
MW-133B	11/24/12	Dilution	6 J	160	3.3 J	49	1300	49	50 U	64	420	96	10 U	2147
MW-133B	06/07/13	Dilution	2.8 J	130	5 U	45	530	19	4.8 J	61	390	68	5 U	1251
MW-133B	11/30/13	Dilution	4 J	190	2.3 J	86	960	21	25 UB	74	490	98	5 U	1925
MW-133B	06/13/14	Dilution	4 J	160	1.3 J	58	430	20	25 UB	72	410	74	5 U	1229

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-133B	11/24/14	Dilution	4.4 J	170	5 U	48	160	12	25 U	78	480	68	5 U	1020
MW-133B	06/15/15	Dilution	4.4 J	170	5 U	50	140	11	5 UB	72	420	64	5 U	931
MW-133B	11/10/15	Dilution	3.4 J	170	5 U	50	110	11	2 J	67	490	54	5 U	957
MW-133B	06/28/16	Dilution	3 J	170	5 U	71	93	8.1	25 U	64	470	47	5 U	926
MW-133B	11/16/16	Dilution	2.8 J	150	5 U	47	74	6.8	25 UB	57	440	44	5 U	822
MW-133B	06/10/17	Dilution	2.7	130	2.5 U	31	66	7.2	3.7 J	53	330	37	1.7 J	662
MW-133B	11/24/17	Dilution	3.2	138	2.5 U	44.3	72.5	7.6	2.5 U	58.9	316	46.4	2.5 U	687
MW-133B	06/21/18	Dilution	2.6 J	159	5 U	65.2	57.4	6.4	8.6	58.7	460 J	33	5 U	851
MW-133B	11/11/18	Dilution	5 U	127	5 U	59.5	51.5	5.2	5 U	58.5	362	32.9	5 U	697
MW-133B	06/23/19		1.7	1 U	1 U	37.4	31.6	4.3	5 U	44.4	300	23.4	1 U	443
MW-133B	12/14/19		1.8	90.7	1 U	41	31.2	3.6	5 U	40.7	241	22.1	1 U	472
MW-133B	06/25/20		1.8	94	1 U	42.3	30.1	3.8	5 U	47.9	244	25.9	1 U	490
MW-133B	11/18/20		1.4	71.3	1 U	35.8	23.2	2.8	5 U	42.7	203	19.6	1 U	400
MW-133C	10/20/93		20 U	76	20 U	75	120		20 U	44	340	170		825
MW-133C	04/26/99		8.5	57	2.8	47	100	5 U	10 U	28	200	110	5 U	553
MW-133C	10/26/99		7.2 J	49	10 U	40	91	1.1 J	20 U	22	170	93	10 U	473
MW-133C	02/15/00		5.4	31	2.3 J	23	32	0.42 J	10 U	2.5 J	110	55	5 U	262
MW-133C	04/25/00		4.7 JB	28	10 U	21	28	0.34 J	20 JB	1.2 J	100	48	10 U	251
MW-133C	07/27/00		4.9	28	2.2	18	30	5 U	10 U	0.82	91	34	5 U	209
MW-133C	07/27/00	Fld Dupe	5.4	31	2.4 J	21	32	0.55 J	10 U	1 J	100	44	5 U	237
MW-133C	11/16/00		5.2	35	2.2	22	31	5 U	10 U	1.2	95	47	5 U	239
MW-133C	04/10/01		6.2	36	10 U	28	36	10 U	20 U	1.6	130	62	10 U	300
MW-133C	10/31/01		5.1	31	5 U	14	31	5 U	10 U	5 U	100	31	5 U	212
MW-133C	10/31/01	Fld Dupe	5.3	32	2 J	18	33	5 U	10 U	5 U	100	40	5 U	230
MW-133C	04/29/02		5.4	33	1.8	26	45	0.73	0.49	4.5	120	58	5 U	295
MW-133C	10/16/02	Fld Dupe	7	49 D	2 U	180 D	53 D	5	0.9 J	2	150 D	74 D	1 U	521
MW-133C	10/16/02		6	49	10 U	150	51	10 U	6	10 U	140	66	1 U	468
MW-133C	04/25/03		5.34	33.5 E	1.86	29.9 E	42.1 E	1.04	2 U	2.41	137 E	72.2 E	1 U	325
MW-133C	04/25/03	Dilution	5.04 J	31.6	10 U	26.5	39.2	10 U	20 U	10 U	113	60.7	10 U	276
MW-133C	12/30/03		6.43	40.7 E	2.01	36.8 E	55.5 E	0.8 J	1 U	3.02	166 E	83 E	1 U	394
MW-133C	12/30/03	Dilution	5.64 JD	143 D	10 U	32.5 D	49.5 D	10 U	10 U	10 U	136 D	74.4 D	10 U	441
MW-133C	04/28/04		5.42	34.7	10 U	29.2	47.2	10 U	20 U	10 U	124	63.7	10 U	304

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	5	7	70	100	5	5	200	5	2	
MW-133C	05/02/05		5.7	37	1.8	31	53	0.59	2 U	2.6	130	63	1 U	325
MW-133C	11/02/05		6.5	46	5 U	43	70	5 U	10 U	5 U	150	75	5 U	391
MW-133C	06/22/06		7.3	44	1 U	42	71	1.3	2 U	4.3	150	78	1 U	398
MW-133C	11/16/06		7.7	61	1.9	23	86	3.5	2 U	5.1	220	110	1 U	518
MW-133C	10/07/07		7	50	2	51	88	2	2 U	5	170	88	1 U	463
MW-133C	05/17/08		8 U	60	8 U	62	120	8 U	16 U	8 U	200 E	100	8 U	542
MW-133C	05/17/08	Dilution	10 U	57 D	10 U	58 D	110 D	10 U	20 U	10 U	180 D	94 D	10 U	499
MW-133C	05/17/08	Fld Dupe	7	60 D	2	58 E	110 E	20 U	20 DJ	20 U	200 E	110 D	1 U	567
MW-133C	11/26/08		7.82	53.6	1.92	24.6	96.9	6.93	0.23 J	6.06	182	94.8	1 U	475
MW-133C	06/20/09		7.4	59	2	36	110	9.7	1 U	6	190	100	1 U	520
MW-133C	11/28/09		7.1	58	1.8	53	110	1.2	1 U	6.2	170	94	1 U	501
MW-133C	06/25/10		6.9	54	1.8	50	130	1.3	1 U	8.6	180	89	1 U	522
MW-133C	11/27/10		6.1	47	1.8	46	130	0.3 J	1 U	10	180	94	1 U	515
MW-133C	06/02/11		6.3	56	1.8	51	180	1.5	0.47 J	16	160	95	1 U	568
MW-133C	12/28/11		5.8	50	1.8	41	130	2	5 U	9.7	140	76	1 U	456
MW-133C	06/28/12		5.7	51	1.6	40	130	1.7	5 U	6.6	150	81	1 U	468
MW-133C	11/24/12		5.3	49	1.6	41	130	1.5	5 U	6.6	140	75	1 U	450
MW-133C	06/07/13		5.3	52	1.3	47	130	1.6	5 U	7.5	160	77	1 U	482
MW-133C	11/30/13		5.2	52	1.3	46	140	1.4	5 UB	7.5	160	83	1 U	496
MW-133C	06/13/14		6.8	68	1.6	53	160	2.1	5 UB	8.5	190	88	1 U	578
MW-133C	11/24/14		5.8	58	1.3	47	130	2.2	5 U	6.6	150	83	1 U	484
MW-133C	06/15/15		5.5	56	1.3	45	130	2.5	5 UB	8.6	170	86	1 U	505
MW-133C	11/10/15		4.9	54	0.98 J	44	100	2.1	0.66 J	13	150	85	1 U	455
MW-133C	06/28/16		5	64	0.85 J	55	100	2.3	5 U	23	160	78	1 U	488
MW-133C	11/16/16		4.8	54	0.91 J	43	82	1.9	5 UB	12	150	79	1 U	428
MW-133C	06/10/17		4.4	56	0.87 J	45	76	2	5 U	15	140	71	1 U	410
MW-133C	06/10/17	Fld Dupe	4.3	55	0.77 J	45	75	2.1	5 U	16	140	69	1 U	407
MW-133C	11/24/17		4	46.3	0.57 J	41.1	63.4	1.7	1 U	12.9	120	66.8	1 U	357
MW-133C	06/21/18		4.1	56.2	0.7 J	43.7	68.1	2	1 U	17	133	72.2	1 U	397
MW-133C	11/11/18		3.6	49.3	1 U	42.7	57.1	1.8	1 U	22	121	61.7	1 U	359
MW-133C	06/23/19		3	42	1 U	30.6	44	1 U	5 U	11.5	103	53.7	1 U	288
MW-133C	12/14/19		2.8	38.9	1 U	31.1	37.3	1 U	5 U	13.8	83.4	46.3	1 U	254
MW-133C	06/25/20		2.9	46.7	0.57 J	33.2	38	1.7	5 U	15.7	92.4	54.1	1 U	285
MW-133C	11/18/20		2.2	33	1 U	26.5	31.6	1.2	5 U	17.5	69	42.4	1 U	223

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-136	10/19/93		5 U	5 U	5 U	5 U	5 U	5 U	10 U	5 U	5 U	5 U	5 U	0
MW-136	04/29/99		0.37	0.35	1 U	0.88	3.5	1 U	2 U	1.7	8	3.8	1 U	19
MW-136	10/28/99		1.5	0.34 J	1 U	0.37 J	1.1	0.03 J	2 U	1.4	16	2.4	1 U	23
MW-136	02/15/00		0.74 J	1 U	1 U	1 U	1 U	1 U	2 U	1 U	0.28 J	1 U	1 U	1
MW-136	04/25/00		0.57 JB	1 U	1 U	1 U	1 U	1 U	2 JB	1 U	0.31 J	1 U	1 U	3
MW-136	07/27/00		0.48	1 U	1 U	1 U	1 U	1 U	2 U	1 U	0.3	1 U	1 U	1
MW-136	11/17/00		0.5	1 U	1 U	1 U	1 U	1 U	2 U	1 U	0.29	1 U	1 U	1
MW-136	04/10/01		0.45	1 U	1 U	1 U	1 U	1 U	2 U	1 U	0.3	1 U	1 U	1
MW-136	10/31/01		0.45	1 U	1 U	1 U	1 U	1 U	2 U	1 U	0.3	1 U	1 U	1
MW-136	04/29/02		0.45	1 U	1 U	1 U	1 U	1 U	2 U	0.53	0.3	1 U	1 U	1
MW-136	10/18/02		0.6	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	1
MW-136	04/23/03		0.8 J	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	1
MW-136	04/28/04		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-136	06/23/06		1.1	1 U	1 U	1 U	1 U	1 U	1 U	1.8	1 U	1 U	1 U	3
MW-136	01/05/07		2.5	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	3
MW-136	10/07/07		1 U	1 U	1 U	1 U	1 U	1 U	0.7	1 U	1 U	1 U	1 U	1
MW-136	05/18/08		2	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	2
MW-136	11/29/08		4.5	1 U	1 U	1 U	1 U	0.2 J	1 U	1 U	1 U	1 U	1 U	5
MW-136	06/11/09		3.1	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	3
MW-136	11/28/09		1.5	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	2
MW-136	06/29/10		0.84 J	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1
MW-136	11/28/10		0.82 J	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1
MW-136	06/01/11		1	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1
MW-136	12/29/11		0.79 J	1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1
MW-136	06/25/12		0.62 J	1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1
MW-136	11/24/12		0.5 J	1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1
MW-136	06/04/13		1 U	1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	0
MW-136	11/30/13		0.38 J	1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	0
MW-136	06/13/14		0.38 J	1 U	1 U	1 U	1 U	1 U	1 U	5 UB	1 U	0.23 J	1 U	1
MW-136	11/23/14		0.58 J	1 U	1 U	1 U	1 U	1 U	1 U	5 UB	1 U	1 U	1 U	1
MW-136	06/07/15		0.83 J	1 U	1 U	1 U	1 U	1 U	1 U	5 UB	1 U	1 U	1 U	1
MW-136	11/15/15		0.49 J	1 U	1 U	1 U	1 U	1 U	1 U	0.55 J	1 U	1 U	1 U	1

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-136	06/28/16		0.45 J	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-136	11/16/16		0.32 J	1 U	1 U	1 U	1 U	1 U	5 UB	1 U	1 U	1 U	1 U	0
MW-136	06/10/17		0.48 J	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-136	11/24/17		0.35 J	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	0
MW-136	06/20/18		0.32 J	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	0
MW-136	11/11/18		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	0
MW-136	06/15/19		0.26 J	1 U	1 U	1 U	1 U	0.44 J	1 U	5 U	1 U	1 U	1 U	1
MW-136	12/08/19		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-136	06/22/20		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-136	11/14/20		1.1	1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1
MW-200	04/26/99		1 U	1 U	1 U	0.34	0.66	1 U	2 U	0.61	2.2	2.2	1 U	6
MW-200	10/27/99		1 U	1 U	1 U	0.26 J	1.3	1 U	2 U	1.1	1.9	1.8	1 U	6
MW-200	02/15/00		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-200	04/25/00		1 U	1 U	1 U	1 U	1 U	1 U	2 JB	1 U	0.07 J	1 U	1 U	2
MW-200	07/27/00		1 U	1 U	1 U	1 U	0.1	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-200	11/14/00		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-200	04/10/01		1 U	1 U	1 U	1 U	0.17	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-200	10/29/01		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	0.12	1 U	0
MW-200	04/22/02		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-200	10/18/02		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-200	04/25/03		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-200	12/30/03		1 U	1 U	1 U	0.89 J	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1
MW-200	04/28/04		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-200	04/28/04	Fld Dupe	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	0
MW-200	05/21/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1.9	1 U	1 U	2
MW-200	01/12/06		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-200	05/08/06		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-200	01/04/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-200	10/08/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-200	05/18/08		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-200	11/29/08		1 U	1 U	1 U	1 U	0.69 J	1 U	1 U	1 U	0.21 J	0.17 J	1 U	1
MW-200	06/11/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	0
MW-200	11/28/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	0

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-200	06/29/10		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	0
MW-200	11/28/10		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	0
MW-200	05/31/11		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	0
MW-200	12/29/11		1 U	1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	0
MW-200	06/25/12		1 U	1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	0
MW-200	11/24/12		1 U	1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	0
MW-200	06/04/13		1 U	1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	0
MW-200	12/01/13		1 U	1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	0
MW-200	06/14/14		1 U	1 U	1 U	1 U	1 U	1 U	1 U	5 UB	1 U	1 U	1 U	0
MW-200	11/23/14		1 U	1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	0
MW-200	06/07/15		1 U	1 U	1 U	1 U	1 U	1 U	1 U	5 UB	1 U	1 U	1 U	0
MW-200	11/10/15		1 U	1 U	1 U	1 U	1 U	1 U	1 U	0.53 J	1 U	1 U	1 U	1
MW-200	06/28/16		1 U	1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	0
MW-200	11/13/16		1 U	1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	0
MW-200	06/10/17		1 U	1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	0
MW-200	11/24/17		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	0
MW-200	06/30/18		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	0
MW-200	11/10/18		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	0
MW-200	06/15/19		1 U	1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	0
MW-200	12/14/19		1 U	1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	0
MW-200	06/25/20		1 U	1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	0
MW-200	11/17/20		1 U	1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	0
MW-201	02/16/00		5 U	48	5 U	1.1 J	85	5 U	10 U	5 U	4.5 J	8.3	5.6	153
MW-201	04/18/00		10 U	120	10 U	1.9 J	87	0.78 J	20 JB	10 U	4.9 J	15	7.2 J	257
MW-201	04/18/00	Fld Dupe	0.29 J	130	10 U	2.3 J	93	0.74 J	20 JB	10 U	5.8 J	12	5.8 J	270
MW-201	07/25/00		20 U	330	20 U	6.8	220	20 U	40 U	20 U	110	4.5	22	693
MW-201	11/13/00		20 U	340	20 U	5.2	180	20 U	40 U	20 U	39	4.9	7.1 J	576
MW-201	04/12/01		5 U	43	5 U	1.6	60	0.64	10 U	5 U	12	19	5.8	142
MW-201	04/12/01	Fld Dupe	5 U	43	5 U	1.6 J	60	0.64 J	10 U	5 U	12	18	5.5	141
MW-201	10/29/01		10 U	150	10 U	3.6	120	10 U	20 U	10 U	55	25	4.8 J	358
MW-201	04/30/02		5	5500	250 U	130	2600	250 U	500 U	250 U	1700	13	50 J	9998
MW-201	10/03/02		500 U	7100	500 U	480	2200	500 U	1000 U	500 U	970	500 U	28 E	.0778
MW-201	10/03/02	Fld Dupe	1 U	7700	1 U	420 J	2200	7	2 U	1 U	1000	26 E	50 E	1403

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-201	04/25/03		0.05 J	1410 E	1 U	52.8 E	989 E	20.3	2 U	0.29 J	452 E	28.9 E	108 E	3061
MW-201	04/25/03	Dilution	500 U	6350	500 U	500 U	863	500 U	1000 U	500 U	294 J	500 U	500 U	7507
MW-201	12/30/03		1 U	1580 E	1 U	15	123 E	1 U	1 U	1 U	175 E	2.99	39.4 E	1935
MW-201	12/30/03	Dilution	400 U	6480 D	400 U	400 U	400 U	400 U	400 U	400 U	400 U	400 U	400 U	6480
MW-201	12/30/03	Fld Dupe	1 U	1430 E	400 U	13.4	90.9 E	400 U	1 U	1 U	400 U	400 U	400 U	1534
MW-201	04/28/04		500 U	4150	500 U	500 U	500 U	500 U	1000 U	500 U	500 U	500 U	500 U	4150
MW-201	05/21/05		25 U	3500	25 U	25 U	58	25 U	50 U	25 U	26	25 U	25 U	3584
MW-201	01/12/06		1 U	230	1 U	1.2	23	1 U	2 U	1 U	8.8	14	1 U	277
MW-201	06/28/06		10 U	550	10 U	10 U	16	10 U	20 U	10 U	32	14	10 U	612
MW-201	01/05/07		1 U	80	1 U	1 U	5.1	1 U	2 U	1 U	20	2.8	1 U	108
MW-201	10/08/07		1 U	20	1 U	2	2	1 U	2 U	6	7	9	1	47
MW-201	05/18/08		1 U	64 E	1 U	2	11	1 U	2 U	1 U	7	10	8	102
MW-201	05/18/08	Dilution	4 U	55 D	4 U	4 U	9 D	4 U	8 U	4 U	6 D	9 D	6 D	85
MW-201	11/29/08	Dilution	2 J	1460	10 U	10 U	7.1 J	10 U	4.4 J	10 U	14.2	7.7 J	6.2 J	1502
MW-201	11/29/08	Fld Dupe	10 U	1580	10 U	10 U	5.5 J	10 U	3.1 J	10 U	12.5	7.1 J	5.6 J	1614
MW-201	06/10/09	Dilution	2 J	1200	10 U	10 U	16	10 U	10 U	10 U	10	7.7 J	10 U	1236
MW-201	06/10/09	Fld Dupe	10 U	1200	10 U	10 U	9.8 J	10 U	10 U	10 U	7.4 J	5.7 J	10 U	1223
MW-201	11/29/09	Fld Dupe	10 U	500	10 U	10 U	5.7 J	10 U	10 U	10 U	36	10 U	9.3 J	551
MW-201	11/29/09	Dilution	10 U	480	10 U	10 U	6.4 J	10 U	10 U	10 U	37	10 U	10	533
MW-201	06/29/10		1 U	12	1 U	1 U	5	1 U	1 U	0.53 J	4.4	1.1	0.91 J	24
MW-201	11/28/10		1 U	2.7	1 U	0.43 J	0.75 J	1 U	1 U	0.93 J	3.4	1.2	1 U	9
MW-201	06/03/11		1 U	2.2	1 U	1 U	0.69 J	1 U	1 U	1.3	3.4	0.85 J	1 U	8
MW-201	06/03/11	Fld Dupe	1 U	2.2	1 U	1 U	0.63 J	1 U	0.26 J	1.2	3.4	0.87 J	1 U	9
MW-201	12/29/11		1 U	3.7	1 U	1 U	3.3	1 U	5 U	1.7	2.4	0.73 J	1 U	12
MW-201	12/29/11	Fld Dupe	1 U	3.6	1 U	1 U	3.3	1 U	5 U	1.8	2.4	0.77 J	1 U	12
MW-201	06/27/12		1 U	8	1 U	1 U	0.75 J	1 U	5 U	1.9	5.8	0.44 J	1 U	17
MW-201	11/25/12		1 U	5	1 U	1 U	1	1 U	5 U	0.85 J	15	0.31 J	1 U	22
MW-201	06/05/13		1 U	1.5	1 U	1 U	0.42 J	1 U	5 U	0.73 J	5.6	0.36 J	1 U	9
MW-201	12/01/13		1 U	4.8	1 U	0.56 J	1.7	1 U	5 U	2.9	16	1.8	1 U	28
MW-201	06/14/14		1 U	2.9	1 U	1 U	0.62 J	1 U	5 UB	1.1	4	0.34 J	1 U	9
MW-201	11/23/14	Fld Dupe	1 U	6.1	1 U	0.82 J	2.8	1 U	5 U	1.5	18	1.2	1 U	30
MW-201	11/23/14		1 U	6.5	1 U	0.83 J	3.2	1 U	5 U	1.7	18	1.4	1 U	32
MW-201	06/14/15		1 U	1.7	1 U	1 U	0.4 J	1 U	5 U	1.3	2.9	0.38 J	1 U	7

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-201	11/08/15		1 U	1.2	1 U	1 U	0.37 J	1 U	0.78 J	0.9 J	2.4	0.33 J	1 U	6
MW-201	06/26/16		1 U	1.4	1 U	1 U	0.49 J	1 U	5 U	1.1	2	0.37 J	1 U	5
MW-201	06/26/16	Fld Dupe	1 U	1.4	1 U	1 U	0.47 J	1 U	5 U	0.98 J	2.1	0.45 J	1 U	5
MW-201	11/12/16		1 U	1.7	1 U	1 U	0.78 J	1 U	5 U	1.2	2.4	0.5 J	1 U	7
MW-201	11/12/16	Fld Dupe	1 U	1.6	1 U	1 U	0.71 J	1 U	5 U	1.2	2.4	0.48 J	1 U	6
MW-201	06/05/17		1 U	0.98 J	1 U	1 U	0.67 J	1 U	5 U	1.3	1.7	0.63 J	1 U	5
MW-201	12/03/17		1 U	3.2	1 U	0.52 J	0.95 J	1 U	1 U	3.3	4.7	1.1	1 U	14
MW-201	06/17/18		1 U	1	1 U	1 U	0.5 J	1 U	1 U	1.3	0.69 J	0.35 J	1 U	4
MW-201	06/17/18	Fld Dupe	1 U	0.98 J	1 U	1 U	0.49 J	1 U	1 U	1.3	0.66 J	0.37 J	1 U	4
MW-201	11/11/18		1 U	0.85 J	1 U	1 U	0.26 J	1 U	1 U	1.4	1	1 U	1 U	4
MW-201	11/11/18	Fld Dupe	1 U	0.84 J	1 U	1 U	1 U	1 U	1 U	1.3	1	0.29 J	1 U	3
MW-201	06/16/19		1 U	0.57 J	1 U	1 U	1 U	1 U	5 U	2	0.92 J	1 U	1 U	3
MW-201	12/08/19		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1.9	1 U	1 U	1 U	2
MW-201	12/08/19	Fld Dupe	1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-201	06/21/20		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1.8	1 U	1 U	1 U	2
MW-201	06/21/20	Fld Dupe	1 U	1 U	1 U	1 U	1 U	1 U	5 U	1.6	1 U	1 U	1 U	2
MW-201	11/15/20		1 U	1.1	1 U	1 U	1 U	1 U	5 U	1.6	1.1	0.37 J	1 U	4
MW-201	11/15/20	Fld Dupe	1 U	0.99 J	1 U	1 U	1 U	1 U	5 U	1.6	1.1	1 U	1 U	4
MW-202	05/20/99		1 U	1 U	1 U	1 U	0.81	1 U	2 U	4.6	2	2.1	1 U	10
MW-202	10/28/99		1 U	1 U	1 U	0.18 J	0.68 J	1 U	2 U	5	2.2	2.1	1 U	10
MW-202	02/16/00		1 U	1 U	1 U	1 U	1 U	1 U	2 U	3.6	0.77 J	0.5 J	1 U	5
MW-202	04/18/00		0.25 J	1 U	1 U	1 U	1 U	1 U	2 JB	3.1	0.65 J	0.55 J	1 U	7
MW-202	07/27/00		0.48	1 U	1 U	1 U	1 U	1 U	2 U	3.5	0.72	0.75	1 U	5
MW-202	11/13/00		1 U	1 U	1 U	1 U	1 U	1 U	2 U	14	0.11	0.19	1 U	14
MW-202	04/12/01		1 U	1 U	1 U	1 U	1 U	1 U	2 U	13	0.08	0.11	1 U	13
MW-202	10/29/01		1 U	1 U	1 U	1 U	1 U	1 U	2 U	12	0.06	1 U	1 U	12
MW-202	04/30/02		1 U	1 U	1 U	1 U	1 U	1 U	2 U	10	1 U	0.12	1 U	10
MW-202	10/17/02		1 U	1 U	1 U	1 U	1 U	1 U	0.5	12	1 U	1 U	1 U	13
MW-202	04/24/03		1 U	1 U	1 U	1 U	1 U	1 U	2 U	2.82	1 U	0.8 J	1 U	4
MW-202	12/30/03		1 U	1 U	1 U	0.54 J	1 U	1 U	1 U	2.78	1 U	1.11	1 U	4
MW-202	04/28/04		1 U	1 U	1 U	1 U	1 U	1 U	2 U	2.3	1 U	0.68	1 U	3
MW-202	05/21/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1.8	1 U	1 U	1 U	2
MW-202	10/21/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-202	06/28/06		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1.5	1 U	1 U	1 U	2
MW-202	01/05/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	14	1 U	1 U	1 U	14
MW-202	10/08/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1	1	0.3	1 U	2
MW-202	05/19/08		1 U	1 U	1 U	1 U	1 U	1 U	2 U	4	1 U	1 U	1 U	4
MW-202	11/29/08		0.3 J	0.95 J	1 U	1 U	1 U	1 U	1 U	1.26	1.15	0.65 J	1 U	4
MW-202	06/11/09		1 U	0.46 J	1 U	1 U	1 U	1 U	1 U	1.2	1	0.6 J	1 U	3
MW-202	11/29/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1.2	1 U	1 U	1 U	1
MW-202	06/29/10		1 U	0.7 J	1 U	1 U	1 U	1 U	1 U	1.6	1.3	0.79 J	1 U	4
MW-202	11/28/10		1 U	1 U	1 U	1 U	1 U	1 U	1 U	2.1	0.67 J	1 U	1 U	3
MW-202	06/03/11		1 U	0.35 J	1 U	1 U	1 U	1 U	1 U	1.5	0.45 J	0.39 J	1 U	3
MW-202	12/29/11		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1.2	0.22 J	0.28 J	1 U	2
MW-202	06/27/12		1 U	0.46 J	1 U	1 U	1 U	1 U	1 U	1.4	0.94 J	1 U	1 U	3
MW-202	11/30/12		1 U	0.45 J	1 U	1 U	1 U	1 U	1 U	2.1	1	0.3 J	1 U	4
MW-202	06/05/13		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1.7	0.51 J	0.37 J	1 U	3
MW-202	12/01/13		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1.1	0.66 J	1 U	1 U	2
MW-202	06/14/14		1 U	0.44 J	1 U	1 U	1 U	1 U	5 UB	1.4	0.39 J	0.38 J	1 U	3
MW-202	11/24/14		1 U	0.43 J	1 U	1 U	1 U	1 U	5 U	0.97 J	1 U	0.35 J	1 U	2
MW-202	06/14/15		1 U	1 U	1 U	1 U	1 U	1 U	5 U	0.84 J	0.21 J	1 U	1 U	1
MW-202	11/08/15		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1	0.3 J	1 U	1 U	1
MW-202	06/26/16		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1.1	0.3 J	1 U	1 U	1
MW-202	11/13/16		1 U	1 U	1 U	1 U	1 U	1 U	5 U	0.74 J	1 U	1 U	1 U	1
MW-202	06/04/17		1 U	1 U	1 U	1 U	1 U	1 U	5 U	0.68 J	1 U	1 U	1 U	1
MW-202	12/03/17		1 U	1 U	1 U	1 U	1 U	1 U	1 U	0.68 J	1 U	1 U	1 U	1
MW-202	06/17/18		1 U	1 U	1 U	1 U	1 U	1 U	1 U	0.52 J	1 U	1 U	1 U	1
MW-202	11/11/18		1 U	1 U	1 U	1 U	1 U	1 U	1 U	0.5 J	1 U	1 U	1 U	1
MW-202	06/16/19		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-202	12/08/19		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-202	06/21/20		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-202	11/15/20		1 U	1 U	1 U	1 U	1 U	1 U	5 U	0.63 J	1 U	1 U	1 U	1
MW-203	05/20/99		1 U	1 U	1 U	1 U	0.67	1 U	2 U	14	0.92	1.2	1 U	17
MW-203	10/28/99		0.08 J	0.28 J	1 U	0.42 J	1.5	0.06 J	2 U	15	2.7	2.6	1 U	23
MW-203	02/15/00		1 U	1 U	1 U	1 U	0.13 J	1 U	2 U	8.6	0.26 J	0.16 J	1 U	9
MW-203	04/18/00		1 U	1 U	1 U	1 U	0.07 J	1 U	2 U	11	0.14 J	0.17 J	1 U	11

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-203	07/27/00		1 U	1 U	1 U	1 U	1 U	1 U	2 U	13	0.2	0.24	1 U	13
MW-203	11/13/00		0.82	1 U	1 U	1 U	1 U	1 U	2 U	3.5	0.66	0.81	1 U	6
MW-203	04/12/01		1.8	1 U	1 U	1 U	1 U	1 U	2 U	3.2	0.81	0.76	1 U	7
MW-203	10/29/01		4.3	0.19	1 U	1 U	1 U	1 U	2 U	3.1	0.76	0.84	1 U	9
MW-203	04/30/02		4.1	0.12	1 U	1 U	1 U	1 U	2 U	3	0.69	0.63	1 U	9
MW-203	10/17/02		1	1 U	1 U	1 U	1 U	1 U	0.5	3	1 U	0.7	1 U	5
MW-203	04/24/03		1 U	1 U	1 U	1 U	1 U	1 U	2 U	10.2	1 U	1 U	1 U	10
MW-203	12/30/03		1 U	1 U	1 U	1 U	1 U	1 U	1 U	8.43	1 U	1 U	1 U	8
MW-203	04/28/04		1 U	1 U	1 U	1 U	1 U	1 U	2 U	8.79	1 U	1 U	1 U	9
MW-203	05/21/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	9.6	1 U	1 U	1 U	10
MW-203	10/21/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-203	06/28/06		1 U	1 U	1 U	1 U	1 U	1 U	2 U	17	1 U	1 U	1 U	17
MW-203	01/05/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1.7	1 U	1 U	1 U	2
MW-203	10/08/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	4	1 U	1 U	1 U	4
MW-203	05/18/08		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1	1	1 U	1 U	2
MW-203	05/18/08	Fld Dupe	1 U	1 U	1 U	1 U	1 U	1 U	2 U	1	1	1 U	1 U	2
MW-203	11/29/08		0.15 J	0.45 J	1 U	1 U	1 U	1 U	1 U	3.11	0.19 J	0.33 J	1 U	4
MW-203	06/11/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	4.4	1 U	1 U	1 U	4
MW-203	11/29/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	5.4	1 U	1 U	1 U	5
MW-203	06/29/10		1 U	1 U	1 U	1 U	1 U	1 U	0.32 J	8.9	1 U	1 U	1 U	9
MW-203	11/28/10		1 U	1 U	1 U	1 U	1 U	1 U	1 U	7.3	1 U	1 U	1 U	7
MW-203	06/03/11		1 U	1 U	1 U	1 U	1 U	1 U	0.27 J	5.1	1 U	1 U	1 U	5
MW-203	12/29/11		1 U	1 U	1 U	1 U	1 U	1 U	5 U	5.1	1 U	0.19 J	1 U	5
MW-203	06/28/12		1 U	1 U	1 U	1 U	1 U	1 U	5 U	10	1 U	0.41 J	1 U	10
MW-203	11/30/12		1 U	0.19 J	1 U	1 U	1 U	1 U	5 U	11	0.36 J	0.34 J	1 U	12
MW-203	06/10/13		1 U	1 U	1 U	1 U	1 U	1 U	5 U	9.5	1 U	1 U	1 U	10
MW-203	12/01/13		1 U	1 U	1 U	1 U	1 U	1 U	5 U	5.9	1 U	1 U	1 U	6
MW-203	06/14/14		1 U	0.35 J	1 U	1 U	0.21 J	1 U	5 UB	2.6	0.31 J	0.23 J	1 U	4
MW-203	11/24/14		1 U	1 U	1 U	1 U	1 U	1 U	5 U	4.1	0.24 J	1 U	1 U	4
MW-203	06/14/15		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1.5	0.21 J	0.37 J	1 U	2
MW-203	11/08/15		1 U	1 U	1 U	1 U	1 U	1 U	0.39 J	2.1	1 U	1 U	1 U	2
MW-203	06/26/16		1 U	1 U	1 U	1 U	1 U	1 U	5 U	3.4	1 U	1 U	1 U	3
MW-203	11/13/16		1 U	1 U	1 U	1 U	1 U	1 U	5 U	3.9	1 U	1 U	1 U	4

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-203	06/04/17		1 U	1 U	1 U	1 U	1 U	1 U	5 U	2.4	1 U	1 U	1 U	2
MW-203	12/03/17		1 U	1 U	1 U	1 U	1 U	1 U	1 U	5.9	1 U	0.35 J	1 U	6
MW-203	06/17/18		1 U	1 U	1 U	1 U	1 U	1 U	1 U	16.8	1 U	0.43 J	1 U	17
MW-203	11/11/18		1 U	1 U	1 U	1 U	1 U	1 U	1 U	14.6	1 U	1 U	1 U	15
MW-203	06/16/19		1 U	1 U	1 U	1 U	1 U	1 U	5 U	5.6	1 U	1 U	1 U	6
MW-203	12/08/19		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-203	06/21/20		1 U	1 U	1 U	1 U	1 U	1 U	5 U	2.1	1 U	1 U	1 U	2
MW-203	11/15/20		1 U	1 U	1 U	1 U	1 U	1 U	5 U	2.6	1 U	1 U	1 U	3
MW-204	04/23/99		20 U	20 U	20 U	6.2	56	20 U	40 U	20 U	4.7	230	20 U	297
MW-204	10/26/99		10 U	5.2 J	4.5 J	8.6 J	51	0.55 J	20 U	2.4 J	5.4 J	230	1.1 J	309
MW-204	01/31/00		0.67 J	5 J	5.3 J	8.2 J	41	10 U	2 J	2.4 J	4.2 J	200	0.85 J	270
MW-204	04/24/00		0.92 J	4.9 J	5.7 J	9.2 J	44	10 U	20 JB	2 J	4 J	190	1.2 J	282
MW-204	07/25/00		1.1	4.4	5.7	6.9	38	10 U	20 U	1.3	3.4	120	10 U	181
MW-204	11/08/00		10 U	6.5	6.8	11	37	10 U	20 U	2.4	4	170	10 U	238
MW-204	04/12/01		10 U	5	6	11	27	10 U	20 U	2.4	4.5	160	10 U	216
MW-204	10/16/01		10 U	5.4	10 U	13	23	10 U	20 U	2.8	4.9	140	10 U	189
MW-204	04/17/02		0.77	6.9	10	18	20	10 U	20 U	2.9	6	140	0.041 J	205
MW-204	10/03/02		20 U	14	20 U	140	23	20 U	40 U	20 U	20 U	170	1 U	347
MW-204	04/22/03		0.59 J	8.21	9.93	28.4 E	28.6 E	0.61 J	2 U	3.9	9.93	192 E	0.76 J	283
MW-204	04/22/03	Dilution	10 U	7.58 J	9.49 J	23.9	26.8	10 U	20 U	10 U	9.28 J	165	10 U	242
MW-204	12/28/03		0.58 J	8.14	9.41	26.3 E	28.8 E	1 U	1 U	3.83	11.3	163 E	0.8 J	252
MW-204	12/28/03	Dilution	10 U	7.65 JD	8.32 JD	21.8 D	23.7 D	10 U	10 U	10 U	9.1 JD	151 D	10 U	222
MW-204	04/28/04		10 U	6.41	8.07	21	20.7	10 U	20 U	10 U	8.96	124	10 U	189
MW-204	05/21/05		1 U	6	5.9	22	13	1 U	2 U	2.8	10	96	1 U	156
MW-204	10/19/05		1 U	6.2	5.7	20	15	1 U	2 U	2.3	9.1	97	1 U	155
MW-204	05/06/06		1 U	5.7	4.4	21	13	1 U	2 U	2.9	10	100	1 U	157
MW-204	01/03/07		1 U	6	3.5	22	15	1 U	2 U	3.2	10	100	1 U	160
MW-204	10/07/07		0.5	6	3	19	15	0.5	2 U	3	10	85	0.4 J	142
MW-204	10/07/07	Fld Dupe	0.5 J	5	3	18	15	0.4 J	2 U	3	9	82 D	1 U	136
MW-204	05/18/08		4 U	6	4 U	20	20	4 U	8 U	4 U	9	91	4 U	146
MW-204	11/29/08		0.65 J	4.9	2.07	13.6	14.4	0.29 J	1 U	2.64	7.61	74	0.32 J	120
MW-204	06/11/09		0.67 J	4.3	1.4	11	14	0.4 J	1 U	2.6	7.2	73	0.31 J	115
MW-204	11/25/09		0.65 J	5.8	1.8	14	20	1 U	1 U	2.6	6.2	71	0.56 J	123

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-204	06/29/10		1 U	5.2	1.3	12	18	1 U	1 U	2	4.3	61	1 U	104
MW-204	11/25/10		0.54 J	5.3	1.5	11	24	1 U	1 U	2.5	6.4	66	1 U	117
MW-204	06/02/11		0.5 J	5.9	1.3	11	26	0.4 J	1 U	2.1	5.9	60	0.25 J	113
MW-204	12/29/11		0.55 J	5.3	1.3	10	26	0.52 J	5 U	2	5.6	51	1 U	102
MW-204	06/27/12		0.63 J	5.5	1.2	7.1	30	1.3	5 U	1.7	5.8	54	1 U	107
MW-204	11/25/12		0.45 J	6	1.2	12	33	0.64 J	5 U	1.8	7.3	51	1 U	113
MW-204	05/31/13		0.46 J	6.5	1	12	36	0.5 J	5 U	1.7	7.9	51	1 U	117
MW-204	05/31/13	Fld Dupe	0.45 J	6.4	0.97 J	12	36	0.41 J	5 U	1.7	7.8	51	1 U	117
MW-204	12/01/13		0.33 J	6.2	0.75 J	12	37	0.47 J	5 U	1.6	6.4	52	1 U	117
MW-204	06/04/14		0.3 J	8.6	0.7 J	15	40	0.52 J	5 U	1.9	12	52	0.18 J	131
MW-204	11/23/14		0.38 J	9.8	0.94 J	16	40	0.78 J	5 U	1.4	10	51	1 U	130
MW-204	06/13/15		0.32 J	12	0.6 J	19	36	0.56 J	5 U	1.6	14	51	1 U	135
MW-204	11/15/15		0.35 J	13	0.47 J	19	28	0.62 J	0.55 J	1.5	14	48	1 U	125
MW-204	06/26/16		0.45 J	15	0.47 J	26	37	0.61 J	5 U	1.5	18	48	0.3 J	147
MW-204	11/17/16		0.46 J	22	0.35 J	29	28	0.59 J	5 U	1.7	24	54	1 U	160
MW-204	06/04/17		0.47 J	20	0.45 J	32	36	0.68 J	5 U	1.6	21	52	1 U	164
MW-204	11/24/17		0.44 J	23.3	0.33 J	32	30.5	0.72 J	1 U	1.5	23.4	54.4	1 U	167
MW-204	06/17/18		0.48 J	45.2	1 U	40.4	25.2	0.72 J	1 U	1.7	30.8	71	1 U	216
MW-204	11/11/18		1 U	39.9	1 U	38.8	23.2	0.69 J	1 U	1.8	32.4	69.2	1 U	206
MW-204	06/17/19		1 U	45.8	1 U	37.1	18.9	0.82 J	5 U	1.5	32.4	63	1 U	200
MW-204	12/08/19		1 U	52	1 U	37.1	20.1	1 U	5 U	1.9	34.8	74.3	1 U	220
MW-204	06/21/20		1 U	61.7	1 U	40.6	18	0.73 J	5 U	1.6	37	81.1	1 U	241
MW-204	11/17/20		1 U	55.7	1 U	36.3	15.8	0.75 J	5 U	2.7	34	75.5	1 U	221
MW-205A	04/22/99		0.88	23	4.4	100	49	5 U	10 U	3.9	570	69	5 U	820
MW-205A	10/21/99		1.1 J	23 J	25 U	110	57	25 U	50 U	3.4 J	460	68	25 U	723
MW-205A	02/07/00		25 U	22 J	3.5 J	110	56	25 U	50 U	3.6 J	450	68	25 U	713
MW-205A	04/18/00		50 U	23 J	50 U	140	61	50 U	100 JB	50 U	540	80	50 U	944
MW-205A	07/25/00		20 U	19	3.5	92	50	20 U	40 U	20 U	350	47	20 U	562
MW-205A	11/07/00		25 U	27	25 U	120	56	25 U	50 U	25 U	410	66	25 U	679
MW-205A	04/09/01		20 U	23	20 U	130	56	20 U	40 U	4.3	430	68	20 U	711
MW-205A	10/16/01		1.1	18	20 U	87	44	20 U	40 U	2.1	240	49	20 U	441
MW-205A	04/16/02		1.1	17	20 U	79	43	20 U	40 U	6.7	270	47	20 U	464
MW-205A	10/07/02		50 U	50 U	50 U	690	53	50 U	84	110	310	49	1 U	1296

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-205A	04/22/03		0.78 J	21	2.39	122 E	51.2 E	1 U	2 U	7.15	397 E	72.8 E	1 U	674
MW-205A	04/22/03	Dilution	25 U	19.8 J	25 U	111	46.6	25 U	50 U	25 U	322	64.3	25 U	564
MW-205A	12/22/03		0.69 J	19.7	1.48	95.6 E	52.7 E	1 U	1 U	11.3	308 E	64.3 E	1 U	554
MW-205A	12/22/03	Dilution	20 U	15.4 JD	20 U	71.9 D	38.5 D	20 U	20 U	20 U	237 D	47.1 D	20 U	410
MW-205A	04/28/04		20 U	15.8	20 U	68.7	39.9	20 U	40 U	20 U	229	43.9	20 U	397
MW-205A	05/21/05		1 U	15	1 U	51	43	1 U	2 U	11	130	36	1 U	286
MW-205A	10/19/05		1 U	13	1 U	35	38	1 U	2 U	11	89	32	1 U	218
MW-205A	05/06/06		1 U	14	1 U	29	37	1 U	2 U	18	81	32	1 U	211
MW-205A	11/21/06		1 U	13	1 U	49	47	1 U	2 U	17	160	51	1 U	337
MW-205A	10/06/07		0.5	12	0.4	31	39	1 U	2 U	16	75	34	1 U	208
MW-205A	05/18/08		4 U	13	4 U	27	48	4 U	8 U	20	73	35	4 U	216
MW-205A	11/28/08		0.49 J	11.9	0.29 J	21.3	41.5	1 U	1 U	20.2	59.5	30.8	1 U	186
MW-205A	06/09/09		0.45 J	10	0.27 J	19	36	1 U	1 U	19	60	30	1 U	175
MW-205A	11/25/09		0.48 J	11	1 U	19	32	1 U	1 U	20	46	27	1 U	155
MW-205A	06/24/10		0.35 J	11	1 U	16	25	1 U	1 U	22	41	23	1 U	138
MW-205A	11/25/10		0.38 J	13	1 U	16	18	1 U	1 U	23	41	24	1 U	135
MW-205A	06/02/11		0.34 J	15	1 U	15	13	1 U	1 U	23	36	22	1 U	124
MW-205A	01/08/12		0.31 J	20	1 U	14	7.4	1 U	5 U	24	31	16	1 U	113
MW-205A	06/28/12		0.4 J	21	1 U	13	5.7	1 U	5 U	24	30	16	1 U	110
MW-205A	12/02/12		0.26 J	20	1 U	11	4.6	1 U	5 U	24	27	15	1 U	102
MW-205A	05/31/13		0.26 J	20	1 U	11	5.3	1 U	5 U	23	25	16	1 U	101
MW-205A	11/29/13		0.27 J	27	1 U	12	4.4	1 U	5 UB	26	24	15	1 U	109
MW-205A	06/05/14		0.3 J	23	1 U	10	4.6	1 U	5 U	25	24	15	1 U	102
MW-205A	11/22/14		0.29 J	36	1 U	12	2.7	1 U	5 U	22	27	14	1 U	114
MW-205A	06/08/15		0.34 J	37	1 U	10	2.6	1 U	5 UB	23	25	14	1 U	112
MW-205A	11/09/15		0.27 J	31	1 U	9.1	2.5	1 U	0.49 J	19	24	12	1 U	98
MW-205A	06/27/16		0.27 J	30	1 U	8.8	2.2	1 U	5 U	17	21	11	1 U	90
MW-205A	11/11/16		0.26 J	26	1 U	8.1	2.2	1 U	5 U	16	21	12	1 U	86
MW-205A	06/06/17		0.24 J	25	1 U	7.9	1.7	1 U	5 U	18	20	11	1 U	84
MW-205A	11/16/17		0.27 J	29.8	1 U	8.6	1.9	1 U	1 U	19.1	21.5 J	11.6	1 U	93
MW-205A	06/18/18		1 U	21.1	1 U	7.6	1.6	1 U	1 U	17.7	19.6	10.6	1 U	78
MW-205A	11/09/18		1 U	18.2	1 U	6.4	1.3	1 U	1 U	17.2	18.4	9.3	1 U	71
MW-205A	06/21/19		1 U	21.7	1 U	6.5	1 U	1 U	5 U	13.9	16	7.4	1 U	66

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-205A	12/10/19		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	8.7	4.5	1 U	13
MW-205A	06/23/20		1 U	24.6	1 U	6.2	1.1	1 U	5 U	14.1	18	7.1	1 U	71
MW-205A	11/13/20		1 U	18.2	1 U	5.1	1 J	1 U	5 U	12.9	16.9	6	1 U	60
MW-205B	04/22/99		0.73	23	3.4	74	47	5 U	10 U	3.5	310	57	5 U	519
MW-205B	10/21/99		25 U	23 J	25 U	82	54	25 U	50 U	3.4 J	340	58	25 U	560
MW-205B	02/07/00		25 U	24 J	25 U	86	57	25 U	50 U	3.8 J	360	60	25 U	591
MW-205B	04/18/00		20 U	26	20 U	90	59	20 U	40 JB	3.8 J	370	65	20 U	654
MW-205B	07/25/00		20 U	23	20 U	70	52	20 U	40 U	20 U	270	44	20 U	459
MW-205B	11/07/00		20 U	31	2.9	79	55	20 U	40 U	3.6	270	53	20 U	495
MW-205B	04/09/01		20 U	31	20 U	110	68	20 U	40 U	4.5	330	67	20 U	611
MW-205B	10/16/01		20 U	21	20 U	73	50	20 U	40 U	5.1	250	45	20 U	444
MW-205B	04/16/02		0.82	22	10 U	59	53	1.4	0.7	5.8	220	48	10 U	411
MW-205B	10/07/02		50 U	50 U	50 U	470	65	50 U	90	110	310	49	1 U	1094
MW-205B	04/22/03	Dilution	20 U	23.7	20 U	93.1	57.3	20 U	40 U	10 J	262	60.4	20 U	507
MW-205B	04/22/03		0.75 J	24.2	1.79	92.4 E	59.6 E	1 U	2 U	11.4	303 E	63.8 E	1 U	557
MW-205B	12/22/03		0.7 J	21.6	1.36	70.5 E	53.8 E	0.55 J	1 U	13	239 E	52.1 E	1 U	453
MW-205B	12/22/03	Dilution	20 U	18.7 JD	20 U	64.9 D	47.1 D	20 U	20 U	10.5 JD	201 D	44.6 D	20 U	387
MW-205B	04/28/04		20 U	22.4	20 U	75.5	54.4	20 U	40 U	11.4	233	49.3	20 U	446
MW-205B	05/21/05		1 U	17	1 U	43	47	1 U	2 U	13	110	34	1 U	264
MW-205B	10/19/05		1 U	17	1 U	32	43	1 U	2 U	14	89	31	1 U	226
MW-205B	05/06/06		1 U	18	1 U	26	52	1 U	2 U	23	59	31	1 U	209
MW-205B	11/21/06		1 U	18	1 U	39	71	1 U	2 U	23	95	44	1 U	290
MW-205B	10/06/07		0.4	15	0.4	30	52	1 U	2 U	18	66	31	1 U	213
MW-205B	05/18/08		4 U	16	4 U	30	63	4 U	8 U	22	69	34	4 U	234
MW-205B	11/28/08		0.49 J	15	0.38 J	19.9	43.1	1 U	1 U	12.8	79.4	24.6	1 U	196
MW-205B	06/09/09		0.49 J	15	0.25 J	21	44	1 U	1 U	18	63	29	1 U	191
MW-205B	11/25/09		0.55 J	14	1 U	21	37	1 U	1 U	21	47	27	1 U	168
MW-205B	06/24/10		0.38 J	14	0.16 J	17	29	1 U	1 U	22	43	23	1 U	149
MW-205B	11/25/10		0.41 J	15	1 U	17	23	1 U	1 U	23	42	24	1 U	144
MW-205B	06/02/11		0.38 J	17	1 U	18	21	1 U	1 U	23	39	22	1 U	140
MW-205B	01/08/12		0.32 J	20	1 U	14	11	1 U	5 U	23	31	16	1 U	115
MW-205B	06/28/12		0.43 J	21	1 U	13	8.2	1 U	5 U	23	30	15	1 U	111
MW-205B	12/02/12		0.32 J	20	1 U	10	6	1 U	5 U	16	25	12	1 U	89

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-205B	05/31/13		0.32 J	23	1 U	12	7	1 U	5 U	23	27	15	1 U	107
MW-205B	11/29/13		0.26 J	27	1 U	12	5.4	1 U	5 UB	25	24	14	1 U	108
MW-205B	06/05/14		0.3 J	30	1 U	11	4.8	1 U	5 U	26	25	14	1 U	111
MW-205B	11/22/14		0.3 J	38	1 U	13	4.1	1 U	5 U	23	28	14	1 U	120
MW-205B	06/08/15		0.36 J	42	1 U	11	4.1	1 U	5 UB	23	27	14	1 U	121
MW-205B	11/09/15		0.35 J	38	1 U	11	4.2	1 U	0.28 J	20	26	12	1 U	112
MW-205B	06/27/16		0.24 J	33	1 U	10	2.8	1 U	5 U	18	23	11	1 U	98
MW-205B	11/11/16		0.27 J	33	1 U	9.9	2.5	1 U	5 U	17	22	11	1 U	96
MW-205B	06/06/17		0.26 J	30	1 U	9.8	2.2	1 U	5 U	18	21	11	1 U	92
MW-205B	11/16/17		0.25 J	31.3	1 U	9.3	1.9	1 U	1 U	18.5	22.3 J	11.2	1 U	95
MW-205B	06/18/18		1 U	26.5	1 U	8.7	1.6	1 U	1 U	17.3	19.8	10.3	1 U	84
MW-205B	11/09/18		1 U	23.6	1 U	7.9	1.4	1 U	1 U	17.6	18.6	9.2	1 U	78
MW-205B	06/21/19		1 U	23.2	1 U	7.4	1 U	1 U	5 U	14.4	16.4	7.6	1 U	69
MW-205B	12/10/19		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	8.8	4.1	1 U	13
MW-205B	06/23/20		1 U	24.5	1 U	6.5	1	1 U	5 U	13.2	17.8	7.1	1 U	70
MW-205B	11/13/20		1 U	18.2	1 U	5.6	0.93 J	1 U	5 U	12.6	16.8	6.2	1 U	60
MW-206A	04/23/99		0.64	8.5	0.75	22	23	2 U	4 U	9.3	100	37	2 U	201
MW-206A	10/20/99		10 U	9.8 J	10 U	21	21	10 U	20 U	6.6 J	87	33	10 U	178
MW-206A	02/07/00		0.55 J	10	5 U	14	20	5 U	10 U	7	79	25	5 U	156
MW-206A	04/18/00		0.55 J	9.6	5 U	12	20	0.36 J	10 JB	5.2	62	22	5 U	142
MW-206A	07/25/00		0.72	9.4	5 U	14	21	5 U	10 U	3.1	66	16	5 U	130
MW-206A	11/07/00		5 U	12	5 U	5.9	13	5 U	10 U	0.84	46	7.6	5 U	85
MW-206A	04/09/01		0.66	9.7	5 U	13	20	5 U	10 U	4.5	55	22	5 U	125
MW-206A	10/16/01		0.49	8.8	2 U	9.9	18	2 U	0.34	3.5	39	18	2 U	98
MW-206A	04/16/02		0.39	7.1	2 U	7.1	15	0.39	4 U	3.4	31	16	2 U	80
MW-206A	10/08/02		5 U	11	5 U	57	23	5 U	10 U	3	35	18	1 U	147
MW-206A	04/21/03		0.87 J	11.8	1 U	11.7	30.3 E	1.05	2 U	3.48	31.1 E	18.1	1 U	108
MW-206A	04/21/03	Dilution	2 U	11	2 U	11.1	28.4	2 U	4 U	3.17	26.9	17	2 U	98
MW-206A	12/22/03		1.04	14.5	1 U	13.9	38.4 E	1.4	1 U	3.99	35.8 E	19	1 U	128
MW-206A	12/22/03	Dilution	2 U	12.4 D	2 U	11.4 D	33.6 D	1.11 JD	2 U	3.36 D	29.8 D	16.5 D	2 U	108
MW-206A	04/28/04		1.28	10.7	2 U	11.1	31.6	2 U	4 U	3.65	27.4	15.1	2 U	101
MW-206A	05/21/05		1.1	5.6	1 U	6.7	16	1 U	2 U	2.9	17	11	1 U	60
MW-206A	10/19/05		1 U	8.1	1 U	8.8	23	1 U	2 U	3.1	19	11	1 U	73

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-206A	05/06/06		1 U	9.2	1 U	9.1	25	1 U	2 U	3.8	23	13	1 U	83
MW-206A	11/27/06		1.1	9	1 U	8.2	14	1 U	2 U	4.2	22	14	1 U	73
MW-206A	10/06/07		0.6	5	1 U	5	6	1 U	2 U	3	14	9	1 U	43
MW-206A	05/18/08		1 U	6	1 U	8	7	1 U	2 U	4	18	11	1 U	54
MW-206A	11/28/08		0.28 J	13	0.19 J	7.54	9.43	0.21 J	1 U	1.95	17.9	7.85	1.59	60
MW-206A	06/10/09		0.41 J	11	1 U	7.5	7.3	1 U	1 U	2.8	23	9.9	0.97 J	63
MW-206A	04/01/10		0.27 J	7.6	1 U	6.8	4.2	1 U	1 U	3.7	18	10	1 U	51
MW-206A	06/25/10		0.28 J	8.3	1 U	7.1	4.2	1 U	1 U	3.8	18	9.3	1 U	51
MW-206A	11/29/10		0.16 J	13	1 U	4.4	4.5	1 U	1 U	1.5	9.7	4.3	3.6	41
MW-206A	06/02/11		0.27 J	12	1 U	6.8	3.8	1 U	0.27 J	3.4	17	9.6	0.55 J	54
MW-206A	12/22/11		0.93 J	75	2.2	76	100	1 U	5 U	7.3	52	44	0.92 J	358
MW-206A	06/26/12		0.6 J	7.8	1 U	3.7	1.8	1 U	5 U	4.4	11	6.9	1 U	36
MW-206A	11/23/12		0.42 J	12	1 U	3.8	2	1 U	5 U	5.5	12	6.2	1 U	42
MW-206A	05/30/13		0.38 J	9.9	1 U	3.4	1.7	1 U	5 U	4.9	8.6	5.4	1 U	34
MW-206A	11/29/13		0.32 J	9.1	1 U	3.9	1.8	1 U	5 UB	5.6	9.1	5.5	0.22 J	36
MW-206A	11/29/13	Fld Dupe	0.35 J	9.1	1 U	4	1.8	1 U	5 UB	5.7	8.8	5.6	0.21 J	36
MW-206A	06/05/14		0.51 J	6.7	1 U	2.8	1.2	1 U	5 U	6.2	8.3	5.3	1 U	31
MW-206A	11/22/14		0.5 J	7.2	1 U	3	1.2	1 U	5 U	5	6.7	4.5	1 U	28
MW-206A	06/08/15		0.49 J	6.5	1 U	2.2	0.8 J	1 U	5 UB	5	5.5	4	1 U	24
MW-206A	11/09/15		0.33 J	13	1 U	7.9	1.3	1 U	0.44 J	6.9	18	12	1 U	60
MW-206A	06/27/16		0.25 J	14	1 U	7.1	3.3	1 U	5 U	4.6	20	9.2	0.36 J	59
MW-206A	11/11/16		0.23 J	14	1 U	5.7	2.4	1 U	5 U	5.5	20	8.5	0.49 J	57
MW-206A	06/06/17		1 U	14	1 U	4.6	3.4	1 U	5 UB	4	13	5.7	0.71 J	45
MW-206A	11/16/17		1 U	20	1 U	5.7	4	1 U	1 U	5.8	19.7 J	7.4	1.8	64
MW-206A	06/18/18		1 U	13.9	1 U	5.4	1.7	1 U	1 U	6.5	17.7	7.2	0.56 J	53
MW-206A	11/09/18		1 U	12.3	1 U	4.8	2.8	1 U	1 U	6.4	17	6.7	2	52
MW-206A	06/21/19		1 U	13.1	1 U	4.5	2.1	1 U	5 U	5.3	17.6	6.6	1 U	49
MW-206A	12/10/19		1 U	1 U	1 U	1 U	1 U	1 U	5 U	2.8	7.5	3.5	1 U	14
MW-206A	06/23/20		1 U	14.1	1 U	4.8	1.9	1 U	5 U	6.5	18.1	6.2	0.55 J	52
MW-206A	11/13/20		1 U	9.4	1 U	3.3	1.4	1 U	5 U	7	15.4	5.5	0.52 J	43
MW-206B	04/23/99		10 U	5.1	10 U	2.5	59	10 U	20 U	13	4.6	150	10 U	234
MW-206B	10/20/99		10 U	9.1 J	10 U	4.9 J	54	10 U	1.3 J	9.6 J	8.4 J	160	10 U	247

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-206B	02/17/00		10 U	13	10 U	8.8 J	36	10 U	20 U	5.8 J	16	150	10 U	230
MW-206B	04/18/00		0.62 J	14	10 U	9 J	40	0.28 J	20 JB	5.6 J	16	150	10 U	256
MW-206B	07/25/00		0.6	12	5 U	6	36	5 U	10 U	0.98	11	86	5 U	153
MW-206B	11/07/00		5 U	17	5 U	8.4	34	5 U	10 U	3.3	14	120	5 U	197
MW-206B	04/09/01		0.51	14	5 U	9.1	33	5 U	10 U	2.5	16	110	5 U	185
MW-206B	10/16/01		0.62	14	5 U	11	26	5 U	10 U	1.7	20	80	5 U	153
MW-206B	04/16/02		0.69	12	5 U	10	23	5 U	10 U	1.5	20	70	5 U	137
MW-206B	10/08/02		5 U	22	5 U	76	31	5 U	4	5 U	35	100	1 U	268
MW-206B	04/22/03		0.83 J	16.2	0.7 J	16.8	22.1	1 U	2 U	1.35	32.5 E	75.7 E	1 U	166
MW-206B	04/22/03	Dilution	5 U	15.1	5 U	15.7	20.5	5 U	10 U	5 U	27.2	68.7	5 U	147
MW-206B	12/22/03		0.88 J	17.3	0.71 J	18.2	21.5	1 U	1 U	1.34	34 E	68.8 E	1 U	163
MW-206B	12/22/03	Dilution	4 U	14.8 D	4 U	14 D	17.4 D	4 U	4 U	4 U	26.5 D	54.5 D	4 U	127
MW-206B	04/28/04		4 U	16	4 U	14.2	19.5	4 U	8 U	4 U	26.3	59.2	4 U	135
MW-206B	05/21/05		1 U	16	1 U	13	13	1 U	2 U	1 U	22	33	1 U	97
MW-206B	10/19/05		1 U	16	1 U	12	13	1 U	2 U	1 U	22	35	1 U	98
MW-206B	05/06/06		1 U	24	1 U	17	15	1 U	2 U	1 U	24	32	1 U	112
MW-206B	11/27/06		1 U	47	1.4	31	21	1 U	2 U	1.2	44	45	1 U	191
MW-206B	11/27/06	Fld Dupe	1 U	7.1	1 U	5	18	1 U	2 U	1 U	1 U	71	1 U	101
MW-206B	10/06/07		0.8	50	1	39	32	1 U	2 U	1	39	28	0.5 J	191
MW-206B	05/18/08		4 U	56	4 U	46	50	4 U	8 U	4 U	44	48	4 U	244
MW-206B	11/28/08		0.92 J	57.7	1.74	40.9	45.8	0.2 J	1 U	1.71	39.9	35.6	0.72 J	225
MW-206B	06/10/09		1	79	2.3	63	70	0.33 J	1 U	3.3	57	37	0.86 J	314
MW-206B	04/01/10		0.97 J	77	2.3	77	76	0.57 J	1 U	4.4	58	38	1.2	335
MW-206B	06/25/10		1	84	2.4	77	90	0.39 J	1 U	4.9	64	37	1.1	362
MW-206B	11/29/10		0.92 J	78	2.3	71	72	0.53 J	1 U	5.5	55	34	1.1	320
MW-206B	06/02/11		1.1	91	2.7	83	98	0.39 J	0.27 J	7.2	61	44	1.1	390
MW-206B	12/22/11		0.93 J	72	2.2	75	100	1 U	5 U	7.3	50	43	0.96 J	351
MW-206B	06/26/12		1	69	2.4	80	130	0.44 J	5 U	10	58	46	0.86 J	398
MW-206B	11/23/12		0.86 J	55	2.1	74	130	0.4 J	5 U	14	55	41	0.8 J	373
MW-206B	05/30/13		0.79 J	58	2	64	100	1 U	5 U	10	48	36	0.74 J	320
MW-206B	11/29/13		0.7 J	51	1.4	69	130	0.37 J	5 U	15	40	35	2.7	345
MW-206B	06/05/14		0.79 J	50	1.5	60	120	0.47 J	5 U	17	44	39	1.6	334
MW-206B	11/22/14		0.82 J	44	1.2	60	120	0.36 J	5 U	20	46	38	0.39 J	331
MW-206B	06/08/15		0.87 J	45	1.2	53	120	0.53 J	5 UB	21	42	38	0.42 J	322

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-206B	11/09/15		0.81 J	36	0.76 J	46	110	0.44 J	0.44 J	20	37	30	0.3 J	282
MW-206B	06/27/16		0.6 J	32	0.61 J	42	99	0.36 J	5 U	20	33	28	0.29 J	256
MW-206B	11/11/16		0.66 J	31	0.61 J	42	97	0.35 J	5 U	21	33	31	1 U	257
MW-206B	06/06/17		0.51 J	31	0.67 J	40	88	0.33 J	5 U	17	25	24	0.47 J	227
MW-206B	11/16/17		0.69 J	34.1	1 U	41.9	109	0.33 J	1 U	26.5	34.1 J	32.9	1 U	280
MW-206B	06/18/18		0.47 J	33.2	1 U	35.1	104	0.39 J	1 U	17.9	22.9	24.5	3.2	242
MW-206B	11/09/18		1 U	29.1	1 U	37.9	93.9	0.33 J	1 U	27.2	30.1	28.1	1 U	247
MW-206B	06/21/19		1 U	27	1 U	31.9	84.7	1 U	5 U	21.5	28	23.9	1 U	217
MW-206B	12/10/19		1 U	16.5	1 U	17.6	41.4	1 U	5 U	13.4	14.6	14	1 U	118
MW-206B	06/23/20		1 U	28	1 U	29.3	39.4	1 U	5 U	20.9	29.8	21.4	1 U	169
MW-206B	11/13/20		1 U	23.4	1 U	23.9	20	1 U	5 U	21.2	28.3	17.5	1 U	134
MW-206C	04/23/99		1 U	1 U	1 U	0.31	2.7	1 U	2 U	0.41	1.5	4.1	1 U	9
MW-206C	10/20/99		1 U	0.18 J	1 U	0.15 J	2.3	1 U	2 U	1 U	0.26 J	4.3	1 U	7
MW-206C	02/07/00		1 U	1 U	1 U	1 U	3.5	1 U	2 U	1 U	1 U	5.3	1 U	9
MW-206C	04/18/00		1 U	1 U	1 U	1 U	4	1 U	2 JB	1 U	1 U	6	1 U	12
MW-206C	07/25/00		1 U	1 U	1 U	1.3	4.8	1 U	2 U	1 U	1 U	3.5	1 U	10
MW-206C	11/07/00		1 U	0.14	1 U	0.12	2.3	1 U	2 U	1 U	0.29	3.4	1 U	6
MW-206C	11/07/00	Fld Dupe	1 U	0.14 J	1 U	0.12 J	2.3	1 U	2 U	1 U	0.28 J	3.3	1 U	6
MW-206C	04/09/01		1 U	0.36	1 U	0.28	4.3	1 U	2 U	0.25	0.7	6.6	1 U	12
MW-206C	04/09/01	Fld Dupe	1 U	0.33 J	1 U	0.26 J	4.2	1 U	2 U	0.26 J	0.48 J	6.3	1 U	12
MW-206C	10/16/01		1 U	0.24	1 U	0.11	5.9	1 U	2 U	0.2	0.18	7.6	1 U	14
MW-206C	04/16/02		1 U	1 U	1 U	0.17	6.9	1 U	2 U	0.06	1 U	14	1 U	21
MW-206C	10/08/02		5 U	5 U	5 U	5 U	15	5 U	4	5 U	5 U	30	1 U	49
MW-206C	04/22/03	Dilution	2.5 U	2.5 U	2.5 U	2.5 U	13.2	2.5 U	5 U	2.5 U	2.5 U	39.1	2.5 U	52
MW-206C	04/22/03		1 U	0.86 J	1 U	0.55 J	14.4	1 U	2 U	1 U	1 U	43 E	1 U	59
MW-206C	12/22/03	Dilution	4 U	4 U	4 U	4 U	14 D	4 U	4 U	4 U	4 U	44.7 D	4 U	59
MW-206C	12/22/03		1 U	1.37	1 U	1.68	16.6	0.61 J	1 U	1 U	1 U	53 E	1 U	73
MW-206C	04/28/04		2 U	1.21	2 U	2 U	14.9	2 U	4 U	2 U	2 U	37.7	2 U	54
MW-206C	05/21/05		1 U	1.5	1 U	1.1	9.2	1 U	2 U	1 U	1 U	34	1 U	46
MW-206C	10/19/05		1 U	3.8	1 U	2.6	15	1 U	0.1	1 U	1 U	47	1 U	69
MW-206C	05/06/06		1 U	5	1 U	3.5	14	1 U	2 U	1 U	1 U	52	1 U	75
MW-206C	11/27/06		1 U	6.5	1 U	4.4	17	1 U	2 U	1 U	1 U	85	1 U	113

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-206C	10/06/07		1 U	5	1 U	4	11	1 U	2 U	0.4	1 U	44	1 U	64
MW-206C	05/18/08		2 U	5	2 U	4	12	2 U	4 U	2 U	2 U	38	2 U	59
MW-206C	11/28/08		1 U	3.11	1 U	2.01	5.23	1 U	1 U	1 U	1 U	19.4	1 U	30
MW-206C	06/10/09		1 U	2.7	1 U	1.8	4.8	1 U	1 U	1 U	1 U	16	1 U	25
MW-206C	04/01/10		1 U	3.4	1 U	2.7	4.8	1 U	1 U	1 U	1 U	16	1 U	27
MW-206C	06/25/10		1 U	5.2	1 U	3.6	6.5	1 U	1 U	1 U	1 U	20	1 U	35
MW-206C	11/29/10		1 U	3.9	1 U	3.1	5.1	1 U	1 U	1 U	1 U	16	1 U	28
MW-206C	06/02/11		1 U	6	1 U	3.9	6.9	1 U	0.26 J	1 U	1 U	22	1 U	39
MW-206C	12/22/11		1 U	6.3	1 U	4.4	7.5	1 U	5 U	0.3 J	1 U	24	1 U	43
MW-206C	06/26/12		1 U	5.8	1 U	3.8	6.1	1 U	5 U	1 U	1 U	19	1 U	35
MW-206C	11/23/12		1 U	7.1	1 U	5.1	7.1	1 U	5 U	0.24 J	1 U	19	1 U	39
MW-206C	05/30/13		1 U	7.5	1 U	4.9	6.9	1 U	5 U	1 U	1 U	18	1 U	37
MW-206C	06/08/15		1 U	18	0.44 J	12	16	1 U	5 UB	0.5 J	1 U	23	0.26 J	70
MW-206C	06/08/15	Fld Dupe	1 U	18	0.45 J	12	16	1 U	5 UB	0.45 J	1 U	23	0.3 J	70
MW-206C	11/09/15		1 U	33	0.53 J	24	31	1 U	5 U	0.64 J	1 U	32	0.67 J	122
MW-206C	06/27/16		1 U	33	0.67 J	26	36	1 U	5 U	0.38 J	1 U	28	1.5	126
MW-206C	11/11/16		1 U	35	0.77 J	28	38	1 U	5 U	0.62 J	1 U	30	2.1	134
MW-206C	06/06/17		1 U	13	0.34 J	6.4	19	1 U	5 U	1 U	1 U	0.69 J	3	42
MW-206C	11/16/17	Fld Dupe	1 U	43.6	1.2	3.7	15.7	0.35 J	1 U	1 U	1 U	2.8	65.1	132
MW-206C	11/16/17		1 U	43.5	1.2	3.9	15.9	0.33 J	1 U	1 U	1 U	3	63.7	132
MW-206C	06/18/18		1 U	38.5	0.83 J	1 U	1.3	1 U	1 U	1 U	1 U	1 U	76.4	117
MW-206C	11/09/18		1 U	20.9	1 U	6.9	24.5	1 U	1 U	0.59 J	1 U	6.9	15.5	75
MW-206C	06/21/19		1 U	17.5	1 U	1 U	5.5	1 U	5 U	1 U	1 U	1 U	26.6	50
MW-206C	12/10/19		1 U	1 U	1 U	1 U	5.2	1 U	5 U	1 U	1 U	1 U	17.8	23
MW-206C	06/23/20		1 U	42.9	1 U	6.6	41.5	1 U	5 U	1 U	1 U	3.4	43.6	138
MW-206C	11/13/20		1 U	34.5	1 U	11.5	46.5	1 U	5 U	0.49 J	1 U	7.6	23.2	124
MW-207	04/23/99		0.39	0.76	2 U	2 U	1.6	2 U	4 U	2.6	2.7	26	2 U	34
MW-207	10/27/99		0.59 J	1.3	1 U	0.74 J	5.1	0.06 J	2 U	3.9	5.9	25	1 U	43
MW-207	02/17/00		0.54 J	1.1	1 U	0.22 J	1.2	1 U	2 U	2.8	2	22	1 U	30
MW-207	04/18/00		0.62 J	1.2	1 U	0.1 J	1.2	0.1 J	2 JB	2.7	2	20	1 U	30
MW-207	07/25/00		0.63	1.3	1 U	1 U	1.4	0.16	2 U	2.1	2	17	1 U	25
MW-207	11/08/00		0.71	2.1	1 U	0.24	1.4	1 U	2 U	2.3	1.9	16	1 U	25
MW-207	04/10/01		0.6	1.5	1 U	1 U	3.2	0.44	2 U	0.51	1.5	11	1 U	19

Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-207	10/16/01		0.44	5.3	1 U	0.13	3.4	0.33	2 U	1	4.2	22	1 U	37
MW-207	04/17/02		0.36	6.2	2 U	0.26	3.7	0.39	4 U	1.4	5.7	25	1 U	43
MW-207	10/08/02		1 U	8	1 U	6	5	1 U	0.8	0.9	5	21	1 U	47
MW-207	04/22/03		0.54 J	7.42	1 U	1.8	5.09	1 U	2 U	2.5	8.37	29.3 E	1 U	55
MW-207	04/22/03	Dilution	2 U	7.05	2 U	2.13	4.88	2 U	4 U	2.3	7.6	27.8	2 U	52
MW-207	12/28/03		0.53 J	6.12	1 U	2.64	4.5	1 U	1 U	2.58	8.64	29.4 E	1 U	54
MW-207	12/28/03	Dilution	2 U	5.68 D	2 U	2.18 D	3.78 D	2 U	2 U	2.21 D	7.19 D	25.8 D	2 U	47
MW-207	04/28/04		2 U	5.87	2 U	1.85	4.26	2 U	4 U	2.67	8.24	28.1	2 U	51
MW-207	05/21/05		1 U	4.3	1 U	1.7	3	1 U	2 U	2.1	5.4	18	1 U	35
MW-207	05/21/05	Fld Dupe	1 U	4.4	1 U	1.6	3	1 U	2 U	2	5.3	18	1 U	34
MW-207	10/19/05		1 U	4.5	1 U	1 U	2.7	1 U	2 U	1.3	5.7	17	1 U	31
MW-207	05/06/06		1 U	5.2	1 U	1.8	3.3	1 U	2 U	2	6.7	19	1 U	38
MW-207	11/27/06		1 U	5.7	1 U	1.1	3.1	1 U	2 U	2.6	9.3	24	1 U	46
MW-207	10/07/07		0.4	4	1 U	0.7	3	1 U	1 U	2	7	15	1 U	32
MW-207	05/18/08		1 U	4	1 U	2	3	1 U	2 U	2	7	15	1 U	33
MW-207	11/29/08		0.36 J	2.97	1 U	1 U	1.89	0.27 J	1 U	1.98	5.58	10.8	1 U	24
MW-207	06/10/09		0.31 J	2.4	1 U	0.65 J	1.8	1 U	1 U	2.1	4.6	9.9	1 U	22
MW-207	11/25/09		1 U	1.6	1 U	0.6 J	1.2	1 U	1 U	2.2	3.5	7.4	1 U	17
MW-207	06/24/10		0.18 J	1.3	1 U	0.52 J	1	1 U	1 U	1.9	2.8	5.6	1 U	13
MW-207	11/25/10		0.22 J	1.3	1 U	0.72 J	1.3	1 U	1 U	2.2	3	6	1 U	15
MW-207	06/02/11		1 U	1.5	1 U	0.6 J	1.2	1 U	0.3 J	1.6	2.8	5.2	1 U	13
MW-207	12/29/11		0.19 J	1.5	1 U	0.57 J	1.4	1 U	5 U	1.7	2.6	4.4	1 U	12
MW-207	06/26/12		0.27 J	1.4	1 U	0.4 J	1.2	1 U	5 U	1.3	2.2	3.9	1 U	11
MW-207	11/30/12		0.22 J	1.4	1 U	0.53 J	1.2	1 U	5 U	1.4	2.3	4	1 U	11
MW-207	05/31/13		1 U	1.8	1 U	0.5 J	1.4	1 U	5 U	1.4	2.4	4.5	1 U	12
MW-207	12/01/13		1 U	1.3	1 U	0.35 J	1.2	1 U	5 U	1.4	1.8	3.7	1 U	10
MW-207	06/04/14		0.29 J	1.7	1 U	0.64 J	1.3	1 U	5 U	1.5	2.7	4.5	1 U	13
MW-207	11/23/14		0.28 J	1.8	1 U	0.58 J	1.2	1 U	5 U	1.4	2.3	4	1 U	12
MW-207	06/08/15		0.63 J	18	1 U	7.6	3.2	0.23 J	5 UB	0.98 J	19	13	1 U	63
MW-207	11/15/15		0.55 J	17	1 U	0.45 J	2.7	0.49 J	5 U	1.2	19	8.7	1 U	50
MW-207	06/27/16		0.35 J	5.4	1 U	1.7	1.6	1 U	5 U	1.3	6	7.4	1 U	24
MW-207	11/12/16		0.31 J	2.9	1 U	1.3	1.2	1 U	0.25 J	1.4	3.8	5.2	1 U	16
MW-207	06/10/17		0.31 J	2.8	1 U	0.81 J	1.2	1 U	5 U	1.6	2.8	3.3	1 U	13

**Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results**

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
			MCL	NA	NA	5	7	70	100	5	5	200	5	
MW-207	11/24/17		1 U	2.7	1 U	1.4	1.1	1 U	1 U	2	2.9	2.8	1 U	13
MW-207	06/18/18		0.26 J	3.5	1 U	0.55 J	1.2	1 U	1 U	2.3	2.8	2.8	1 U	13
MW-207	11/10/18		1 U	3	1 U	0.92 J	1.1	1 U	1 U	2.4	2.9	2.8	1 U	13
MW-207	06/21/19		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	3	2.5	1 U	6
MW-207	12/10/19		1 U	2.9	1 U	1 U	0.88 J	1 U	5 U	2.2	3.1	2.9	1 U	12
MW-207	06/22/20		1 U	2.9	1 U	1 U	1 U	1 U	5 U	1.8	1 U	2.5	1 U	7
MW-207	11/14/20		1 U	2.4	1 U	0.77 J	1 U	1 U	5 U	1.9	3.2	2.5	1 U	11

**Table 2a: Southeast Rockford Groundwater Contamination Site
Cumulative Groundwater Analytical Results**

Results reported in micrograms per liter ($\mu\text{g/l}$)

Highlighted results equal or exceed the Maximum Contaminant Level (MCL), where applicable

CFM	Chloroform
1,1-DCA	1,1-Dichloroethane
1,2-DCA	1,2-Dichloroethane
1,1-DCE	1,1-Dichloroethene
c1,2-DCE	cis- 1,2-Dichloroethene
t1,2-DCE	trans-1,2-Dichloroethene
MC	Methylene Chloride
PCE	Tetrachloroethene
1,1,1-TCA	1,1,1-Trichloroethane
TCE	Trichloroethene
VC	Vinyl Chloride
Total VOCs	Sum of Total Volatile Organic Compound Concentrations

- B Concentration is less than the reporting limit but greater than the instrument detection limit.
- D Reported concentration is based on an analysis requiring a secondary detection limit.
- E The associated value exceeds the calibration range.
- J The reported concentration is estimated.
- U Analyte was not detected at or above the reporting limit.

Sample Type reported as undiluted, investigative sample unless stated otherwise

Fld Dupe Field Duplicate

Table 2b: Southeast Rockford Groundwater Contamination Site
Cumulative 1,4-Dioxane Groundwater Analytical Results

Well ID	Date	Sample Type	1,4-Dioxane
MW-101A	06/24/20		7
MW-101A	11/16/20		11
MW-101B	06/24/20	Fld Dupe	25
MW-101B	06/24/20		25
MW-101B	11/16/20		26
MW-101C	06/24/20		16
MW-101C	11/16/20		19
MW-101D	06/25/20		0.25 J
MW-101D	11/18/20		0.12 J
MW-102A	06/24/20		15
MW-102A	11/16/20		6.7
MW-102B	06/24/20		170
MW-102B	11/16/20		170
MW-102C	06/24/20		36
MW-102C	11/16/20		31
MW-113A	06/25/20		30
MW-113A	11/17/20		30
MW-113B	06/25/20		69
MW-113B	11/17/20		70
MW-114A	06/25/20		22
MW-114A	11/18/20		21
MW-114B	06/25/20		10
MW-114B	11/18/20		9.8
MW-114B	11/18/20	Fld Dupe	10
MW-117B	06/23/20		5.4
MW-117B	11/13/20		5.5
MW-117C	06/23/20		8.4
MW-117C	11/13/20		8.3
MW-117D	06/23/20		8.9
MW-117D	11/13/20		8.4
MW-119	06/22/20		2.1
MW-119	11/14/20		4
MW-121	06/21/20		48
MW-121	11/15/20		47

Table 2b: Southeast Rockford Groundwater Contamination Site
Cumulative 1,4-Dioxane Groundwater Analytical Results

Well ID	Date	Sample Type	1,4-Dioxane
MW-124	06/21/20		5.4
MW-124	11/18/20		5.3
MW-130	06/22/20		7.3
MW-130	11/17/20		6.6
MW-133A	06/25/20		0.87
MW-133A	11/18/20		0.63
MW-133B	06/25/20		16
MW-133B	11/18/20		15
MW-133C	06/25/20		150
MW-133C	11/18/20		120
MW-136	06/22/20		0.5 U
MW-136	11/14/20		0.5 U
MW-16	06/25/20		22
MW-16	11/18/20		20
MW-200	06/25/20		0.5 U
MW-200	11/17/20		0.2 J
MW-201	06/21/20	Fld Dupe	0.65
MW-201	06/21/20		0.63
MW-201	11/15/20		0.89
MW-201	11/15/20	Fld Dupe	0.94
MW-202	06/21/20		0.11 J
MW-202	11/15/20		0.5 U
MW-203	06/21/20		0.5 U
MW-203	11/15/20		0.5 U
MW-204	06/21/20		27
MW-204	11/17/20		25
MW-205A	06/23/20		7.9
MW-205A	11/13/20		7.7
MW-205B	06/23/20		7.6
MW-205B	11/13/20		7.5
MW-206A	06/23/20		5.3
MW-206A	11/13/20		5.5
MW-206B	06/23/20		29
MW-206B	11/13/20		26

Table 2b: Southeast Rockford Groundwater Contamination Site
Cumulative 1,4-Dioxane Groundwater Analytical Results

Well ID	Date	Sample Type	1,4-Dioxane
MW-206C	06/23/20		53
MW-206C	11/13/20		52
MW-207	06/22/20		3.2
MW-207	11/14/20		2.8
MW-47	06/22/20		0.23 J
MW-47	11/14/20		0.5 U

Results reported in micrograms per liter ($\mu\text{g/l}$)

J The reported concentration is estimated.

U Analyte was not detected at or above the reporting limit.

Fld Dupe Field Duplicate

**Table 3: Southeast Rockford Groundwater Contamination Site
Groundwater Elevations**

Station Identification	Measurement Date	Water Level (ft TOC)	Groundwater Elevation (ft amsl)	Total Depth (ft TOC)	Comments
MW-16	11/18/20	19.46	708.45	62.36	
MW-47	11/14/20	39.93	695.73	54.49	
MW-101A	11/16/20	38.45	727.17	90.34	
MW-101B	11/16/20	39.40	727.22	153.74	
MW-101C	11/16/20	39.30	727.18	174.89	
MW-101D	11/18/20	41.70	723.26	212.72	
MW-102A	11/16/20	17.83	770.60	37.69	
MW-102B	11/16/20	32.25	756.36	100.50	
MW-102C	11/16/20	33.64	756.23	187.42	
MW-113A	11/17/20	50.88	715.66	104.50	
MW-113B	11/17/20	51.59	715.06	155.26	
MW-114A	11/18/20	23.81	703.08	97.48	
MW-114B	11/18/20	25.29	699.73	222.58	Collected field duplicate FD-2
MW-117B	11/13/20	5.18	691.08	89.50	
MW-117C	11/13/20	3.81	692.30	158.31	
MW-117D	11/13/20	3.42	692.68	200.20	
MW-119	11/14/20	22.92	696.05	62.41	
MW-121	11/15/20	20.31	696.67	67.55	
MW-124	11/18/20	33.18	698.12	102.76	
MW-130	11/17/20	19.94	708.01	38.17	
MW-133A	11/18/20	27.53	752.65	37.85	
MW-133B	11/18/20	25.62	754.71	61.49	
MW-133C	11/18/20	21.52	758.77	98.49	
MW-136	11/14/20	34.32	800.45	44.33	
MW-200	11/17/20	45.38	714.78	89.93	
MW-201	11/15/20	27.52	701.51	50.15	Collected field duplicate FD-1
MW-202	11/15/20	26.37	703.25	50.01	
MW-203	11/15/20	25.85	703.24	49.35	
MW-204	11/17/20	26.25	690.96	88.96	
MW-205A	11/13/20	5.38	691.24	110.27	
MW-205B	11/13/20	5.47	691.25	150.05	Clear
MW-206A	11/13/20	8.35	685.35	90.24	Cloudy
MW-206B	11/13/20	6.58	686.68	129.94	
MW-206C	11/13/20	6.36	686.70	251.31	
MW-207	11/14/20	34.65	689.52	90.81	

ft amsl Feet above mean sea level

ft TOC Feet from Top of Casing

**Table 4 - Southeast Rockford Groundwater Contamination Site
Groundwater Monitoring Network**

Well ID	Easting	Northing	TOC Elevation (ft ams) ¹	Total Depth (ft TOC) ²	Total Depth (ft bgs)	Location Description		Maintenance Log
						East of Kinsey Street, north of drain canal	Brooke Rd. 1/2 Block West of Kishwaukee Intersection. In shoulder on North side of road.	
MW-16	2593475.34	2030401.25	725.57	62.25	62.36		flush mount 2014; surveyed 01/1/15	
MW-47	2588765.03	2028342.66	735.23	54.16	24.49			
MW-101A	2598084.40	2029633.41	765.62	90.35	90.35			
MW-101B	2598093.32	2029632.50	766.62	153.74	150.10	Northeast corner of Laude and 24th Street		
MW-101C	2598076.01	2029635.69	766.48	174.89	172.00			
MW-101D	2598066.94	2029632.19	764.96	212.72	212.80		Replaced bladder, drop tube, tubing from bump to drop tube, and intake screen 2018	
MW-102A ³	25993371.95	2029932.56	782.69	34.69	35.00		new flush mount 2016; Replaced bladder & reinstalled pump 2018	
MW-102B	25993380.00	2029930.00	783.01	97.70	98.00	South of RR tracks, east of Laude Street (Owens-Corning Property)	new flush mount 2016	
MW-102C ³	25993388.00	2029939.00	783.13	183.85	184.30		new flush mount 2016; Replaced bladder in pump and intake screen 2018	
MW-113A	2596096.44	2029869.64	766.54	104.50	105.00			
MW-113B	2596038.18	2029873.56	766.65	155.26	155.00	West of Willis and 18th Street		
MW-114A	2593333.10	2030016.18	725.15	94.70	95.00		flush mount 2017	
MW-114B	2593338.00	2030023.51	725.24	219.84	220.00	Corner of Willis and Kinsey Street	flush mount 2014	
MW-117B	2586515.64	2028092.93	696.26	89.50	89.50			
MW-117C	2586522.28	2028099.95	696.11	158.31	159.50	Brooke Rd meridian, West of Grant Park Blvd.		
MW-117D	2586502.42	2028081.65	696.10	200.00	200.00		TOS from well completion	
MW-119	25893374.24	2027137.22	718.97	62.41	59.50	Corner of Sawyer and South 4th Street		
MW-121	2587523.45	2030898.78	716.98	67.55	64.50	Corner of Harrison Ave. and Olsen Street		
MW-124	2590224.67	2030300.32	731.30	102.76	100.00	South of Park Court, west of railroad track		
MW-130	2594440.11	2030701.27	727.95	38.17	37.50	Corner of Alton Ave. and Sewell Street		
MW-133A	2600083.74	2028900.38	780.18	37.85	35.00			
MW-133B	26000054.59	2028906.98	780.33	61.49	58.00	West end of Balsam Lane		
MW-133C	2600090.11	2028901.64	780.29	98.49	96.00			
MW-136	2603572.26	2027821.67	834.77	44.33	45.00	North end of New England Drive		
MW-200	2595998.62	2027199.13	760.16	89.93	90.00	Southeast corner of 7th Street and Sawyer		
MW-201	2591771.57	2031653.69	728.51	49.80	50.00	Northeast Corner of Rockford Products Parking lot on the East side of 9th St., North of Harrison Ave.	Replaced existing flush protective casing with new, heavy-duty flush protective casing 2018	
MW-202	2592985.38	203213.06	729.62	50.01	50.00	West of 11th Street, South of Harrison Ave.; 23rd Street (Abe Peckarsky property, parking lot)	Replaced existing flush protective casing with new, heavy-duty flush protective casing 2018	
MW-203	259293.40	2022079.04	729.09	49.35	50.00	West of 11th Street, South of Harrison Ave.; 23rd Street (Abe Peckarsky property, parking lot)		
MW-204	258345.61	2029789.39	717.21	88.96	90.00	South end of Faulnd Street		
MW-205A ¹	2583564.99	2027820.78	696.69	112.90	110.50	North of Broke Rd, east of Rock River	stickup mount 2016	
MW-205B ¹	2583567.66	2027827.74	696.92	150.31	150.00		stickup mount 2016	
MW-206A	2583871.82	2026940.34	693.70	90.24	90.50		wellhead rearrangement - modified from flush to stick-up June 2020	
MW-206B	2583856.13	2026938.65	693.26	129.94	130.50	Between River Blvd. and the Rock River	wellhead rearrangement - modified from flush to stick-up June 2020	
MW-206C	2583860.69	2026940.21	693.53	249.34	250.00		Reset casing and concrete seal - 2016, wellhead rearrangement - modified from flush to stick-up June 2020	
MW-207	2587190.96	2026478.18	724.17	90.81	90.00	Corner of Martin Road & Grant Park Blvd.		

¹ Checked against Table 3.1 of 1998 NES work Plan

² From field reports

³ See main text

From NES well completion forms
calculated TOC elevation, from ground surface and stickup
adjusted to reflect 06/06/17 survey

APPENDIX A

Groundwater Monitoring
Data Validation Summary & Laboratory Data Sheets

Data Quality Control Criteria Review Summary

SDG Number: 50273460**Project Number:** 1016-2**Site:** SE Rockford, Semi-annual (Second 2020)**Contractor Lab:** Pace Analytical Services**Validator:** Maggie Mandell**Sample Date:** 11/13/20 - 11/16/20**Sample Matrix:** Groundwater**Validation Date:** 12/15/20**Analytical Methods:** Volatiles by EPA SW-846 5030B/8260
1,4-Dioxane by SPME and GC\MS (SIM)**Sample Designations:**

MW-101A	MW-117B	MW-201	MW-206B
MW-101B	MW-117C	MW-202	MW-206C
MW-101C	MW-117D	MW-203	MW-207
MW-102A	MW-119	MW-205A	MW-47
MW-102B	MW-121	MW-205B	FD-1
MW-102C	MW-136	MW-206A	Trip Blank

The analytical data were reviewed in accordance with the analytical methods and the Environmental Protection Agency (EPA) Contract Laboratory Program (CLP) National Functional Guidelines. The review included comparing quality control (QC) values provided on the laboratory QC forms to method QC criteria. Review of the raw data was not performed.

Quality Control Summary

QC Review Item	Evaluation [#]
Completeness	X
Case Narrative	X
Chain of Custody (COC) Forms	X
Sample Preservation	X
Holding Times	X
Laboratory Blank Results	X
System Monitoring Compounds (Surrogate) Results	X
Matrix Spike/Matrix Duplicate (MS/MSD) Results	X
Laboratory Control Sample (LCS) Results	X
Method Specific Quality Control (QC) Results *	X
System Performance	X
Field Quality Control Results **	1
Other	NA

See validation summary comment

X Acceptable, no qualification necessary

NR Not required

NA Not applicable

* The reviewer has indicated in the comments, if necessary, the method specific QC results included in the data package that were reviewed.

** Field QC may include field duplicates, trip blanks, rinse blanks, field blanks, and equipment blank samples as required by project specific criteria.

Data for the above samples are:

Action required by Project Manager

- Acceptable for use
 Acceptable for use as qualified
 Unacceptable for use

- Yes
 No

Data Validation Summary Comments:

- 1. Field Quality Control Samples** – One field duplicate was collected during this sampling event. The RPD is not necessarily calculated if both the primary and duplicate results are not five times greater than the reporting limit. The RPD between the investigative and duplicate samples was less than or equal to 11%. The RPD values only consider the comparison of two concentrations reported above the reporting limit. Qualification is not necessary.

Overall Assessment of Data:

The Pace Work Order Report #50273460 is 100% complete. The data usability is based on EPA's guidance documents. No problems were identified with reported data and analytical performance was within specified limits. The data are acceptable and meet the project's data quality objectives.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site

Pace Project No.: 50273460

Sample: MW101A	Lab ID: 50273460022	Collected: 11/16/20 15:34	Received: 11/17/20 09:20	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	7.0	1		11/20/20 01:09	67-64-1	
Benzene	ND	ug/L	1.0	0.34	1		11/20/20 01:09	71-43-2	
Bromochloromethane	ND	ug/L	1.0	1.0	1		11/20/20 01:09	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.87	1		11/20/20 01:09	75-27-4	
Bromoform	ND	ug/L	1.0	0.21	1		11/20/20 01:09	75-25-2	
Bromomethane	ND	ug/L	5.0	0.90	1		11/20/20 01:09	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	1.3	1		11/20/20 01:09	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.92	1		11/20/20 01:09	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.31	1		11/20/20 01:09	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.33	1		11/20/20 01:09	108-90-7	
Chloroethane	ND	ug/L	2.0	0.45	1		11/20/20 01:09	75-00-3	
Chloroform	2.9	ug/L	1.0	0.99	1		11/20/20 01:09	67-66-3	
Chloromethane	ND	ug/L	2.0	0.92	1		11/20/20 01:09	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	1.0	1		11/20/20 01:09	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.25	1		11/20/20 01:09	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.23	1		11/20/20 01:09	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/20/20 01:09	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.32	1		11/20/20 01:09	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/20/20 01:09	106-46-7	
1,1-Dichloroethane	43.7	ug/L	1.0	0.34	1		11/20/20 01:09	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.21	1		11/20/20 01:09	107-06-2	
1,1-Dichloroethene	8.4	ug/L	1.0	0.67	1		11/20/20 01:09	75-35-4	
cis-1,2-Dichloroethene	26.1	ug/L	1.0	0.87	1		11/20/20 01:09	156-59-2	
trans-1,2-Dichloroethene	1.8	ug/L	1.0	0.87	1		11/20/20 01:09	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.38	1		11/20/20 01:09	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.32	1		11/20/20 01:09	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.24	1		11/20/20 01:09	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.29	1		11/20/20 01:09	100-41-4	
2-Hexanone	ND	ug/L	20.0	1.1	1		11/20/20 01:09	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.67	1		11/20/20 01:09	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	0.87	1		11/20/20 01:09	108-10-1	
Styrene	ND	ug/L	1.0	0.34	1		11/20/20 01:09	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.16	1		11/20/20 01:09	79-34-5	
Tetrachloroethene	6.6	ug/L	1.0	0.21	1		11/20/20 01:09	127-18-4	
Toluene	ND	ug/L	1.0	0.31	1		11/20/20 01:09	108-88-3	
1,1,1-Trichloroethane	91.4	ug/L	1.0	0.23	1		11/20/20 01:09	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.19	1		11/20/20 01:09	79-00-5	
Trichloroethene	11.4	ug/L	1.0	0.37	1		11/20/20 01:09	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.42	1		11/20/20 01:09	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.3	1		11/20/20 01:09	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	97	%.	85-116		1		11/20/20 01:09	460-00-4	
Dibromofluoromethane (S)	105	%.	75-120		1		11/20/20 01:09	1868-53-7	
Toluene-d8 (S)	98	%.	83-111		1		11/20/20 01:09	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site

Pace Project No.: 50273460

Sample: MW101B	Lab ID: 50273460023	Collected: 11/16/20 16:08	Received: 11/17/20 09:20	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	7.0	1		11/20/20 00:10	67-64-1	
Benzene	ND	ug/L	1.0	0.34	1		11/20/20 00:10	71-43-2	
Bromochloromethane	ND	ug/L	1.0	1.0	1		11/20/20 00:10	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.87	1		11/20/20 00:10	75-27-4	
Bromoform	ND	ug/L	1.0	0.21	1		11/20/20 00:10	75-25-2	
Bromomethane	ND	ug/L	5.0	0.90	1		11/20/20 00:10	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	1.3	1		11/20/20 00:10	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.92	1		11/20/20 00:10	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.31	1		11/20/20 00:10	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.33	1		11/20/20 00:10	108-90-7	
Chloroethane	ND	ug/L	2.0	0.45	1		11/20/20 00:10	75-00-3	
Chloroform	ND	ug/L	1.0	0.99	1		11/20/20 00:10	67-66-3	
Chloromethane	ND	ug/L	2.0	0.92	1		11/20/20 00:10	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	1.0	1		11/20/20 00:10	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.25	1		11/20/20 00:10	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.23	1		11/20/20 00:10	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/20/20 00:10	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.32	1		11/20/20 00:10	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/20/20 00:10	106-46-7	
1,1-Dichloroethane	104	ug/L	1.0	0.34	1		11/20/20 00:10	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.21	1		11/20/20 00:10	107-06-2	
1,1-Dichloroethene	18.9	ug/L	1.0	0.67	1		11/20/20 00:10	75-35-4	
cis-1,2-Dichloroethene	9.2	ug/L	1.0	0.87	1		11/20/20 00:10	156-59-2	
trans-1,2-Dichloroethene	3.3	ug/L	1.0	0.87	1		11/20/20 00:10	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.38	1		11/20/20 00:10	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.32	1		11/20/20 00:10	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.24	1		11/20/20 00:10	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.29	1		11/20/20 00:10	100-41-4	
2-Hexanone	ND	ug/L	20.0	1.1	1		11/20/20 00:10	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.67	1		11/20/20 00:10	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	0.87	1		11/20/20 00:10	108-10-1	
Styrene	ND	ug/L	1.0	0.34	1		11/20/20 00:10	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.16	1		11/20/20 00:10	79-34-5	
Tetrachloroethene	21.7	ug/L	1.0	0.21	1		11/20/20 00:10	127-18-4	
Toluene	ND	ug/L	1.0	0.31	1		11/20/20 00:10	108-88-3	
1,1,1-Trichloroethane	320	ug/L	10.0	2.2	10		11/20/20 19:18	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.19	1		11/20/20 00:10	79-00-5	
Trichloroethene	18.5	ug/L	1.0	0.37	1		11/20/20 00:10	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.42	1		11/20/20 00:10	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.3	1		11/20/20 00:10	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	98	%.	85-116		1		11/20/20 00:10	460-00-4	
Dibromofluoromethane (S)	112	%.	75-120		1		11/20/20 00:10	1868-53-7	
Toluene-d8 (S)	97	%.	83-111		1		11/20/20 00:10	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site

Pace Project No.: 50273460

Sample: MW101C	Lab ID: 50273460021	Collected: 11/16/20 14:55	Received: 11/17/20 09:20	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	7.0	1		11/19/20 23:41	67-64-1	
Benzene	ND	ug/L	1.0	0.34	1		11/19/20 23:41	71-43-2	
Bromochloromethane	ND	ug/L	1.0	1.0	1		11/19/20 23:41	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.87	1		11/19/20 23:41	75-27-4	
Bromoform	ND	ug/L	1.0	0.21	1		11/19/20 23:41	75-25-2	
Bromomethane	ND	ug/L	5.0	0.90	1		11/19/20 23:41	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	1.3	1		11/19/20 23:41	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.92	1		11/19/20 23:41	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.31	1		11/19/20 23:41	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.33	1		11/19/20 23:41	108-90-7	
Chloroethane	ND	ug/L	2.0	0.45	1		11/19/20 23:41	75-00-3	
Chloroform	ND	ug/L	1.0	0.99	1		11/19/20 23:41	67-66-3	
Chloromethane	ND	ug/L	2.0	0.92	1		11/19/20 23:41	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	1.0	1		11/19/20 23:41	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.25	1		11/19/20 23:41	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.23	1		11/19/20 23:41	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 23:41	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.32	1		11/19/20 23:41	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 23:41	106-46-7	
1,1-Dichloroethane	72.2	ug/L	1.0	0.34	1		11/19/20 23:41	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.21	1		11/19/20 23:41	107-06-2	
1,1-Dichloroethene	12.9	ug/L	1.0	0.67	1		11/19/20 23:41	75-35-4	
cis-1,2-Dichloroethene	6.8	ug/L	1.0	0.87	1		11/19/20 23:41	156-59-2	
trans-1,2-Dichloroethene	2.3	ug/L	1.0	0.87	1		11/19/20 23:41	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.38	1		11/19/20 23:41	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.32	1		11/19/20 23:41	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.24	1		11/19/20 23:41	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.29	1		11/19/20 23:41	100-41-4	
2-Hexanone	ND	ug/L	20.0	1.1	1		11/19/20 23:41	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.67	1		11/19/20 23:41	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	0.87	1		11/19/20 23:41	108-10-1	
Styrene	ND	ug/L	1.0	0.34	1		11/19/20 23:41	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.16	1		11/19/20 23:41	79-34-5	
Tetrachloroethene	12.0	ug/L	1.0	0.21	1		11/19/20 23:41	127-18-4	
Toluene	ND	ug/L	1.0	0.31	1		11/19/20 23:41	108-88-3	
1,1,1-Trichloroethane	267	ug/L	1.0	0.23	1		11/19/20 23:41	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.19	1		11/19/20 23:41	79-00-5	
Trichloroethene	8.8	ug/L	1.0	0.37	1		11/19/20 23:41	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.42	1		11/19/20 23:41	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.3	1		11/19/20 23:41	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	98	%.	85-116		1		11/19/20 23:41	460-00-4	
Dibromofluoromethane (S)	109	%.	75-120		1		11/19/20 23:41	1868-53-7	
Toluene-d8 (S)	98	%.	83-111		1		11/19/20 23:41	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site

Pace Project No.: 50273460

Sample: MW102A	Lab ID: 50273460018	Collected: 11/16/20 12:55	Received: 11/17/20 09:20	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	7.0	1		11/19/20 22:14	67-64-1	
Benzene	ND	ug/L	1.0	0.34	1		11/19/20 22:14	71-43-2	
Bromochloromethane	ND	ug/L	1.0	1.0	1		11/19/20 22:14	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.87	1		11/19/20 22:14	75-27-4	
Bromoform	ND	ug/L	1.0	0.21	1		11/19/20 22:14	75-25-2	
Bromomethane	ND	ug/L	5.0	0.90	1		11/19/20 22:14	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	1.3	1		11/19/20 22:14	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.92	1		11/19/20 22:14	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.31	1		11/19/20 22:14	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.33	1		11/19/20 22:14	108-90-7	
Chloroethane	ND	ug/L	2.0	0.45	1		11/19/20 22:14	75-00-3	
Chloroform	ND	ug/L	1.0	0.99	1		11/19/20 22:14	67-66-3	
Chloromethane	ND	ug/L	2.0	0.92	1		11/19/20 22:14	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	1.0	1		11/19/20 22:14	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.25	1		11/19/20 22:14	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.23	1		11/19/20 22:14	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 22:14	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.32	1		11/19/20 22:14	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 22:14	106-46-7	
1,1-Dichloroethane	23.8	ug/L	1.0	0.34	1		11/19/20 22:14	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.21	1		11/19/20 22:14	107-06-2	
1,1-Dichloroethene	ND	ug/L	1.0	0.67	1		11/19/20 22:14	75-35-4	
cis-1,2-Dichloroethene	27.3	ug/L	1.0	0.87	1		11/19/20 22:14	156-59-2	
trans-1,2-Dichloroethene	1.8	ug/L	1.0	0.87	1		11/19/20 22:14	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.38	1		11/19/20 22:14	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.32	1		11/19/20 22:14	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.24	1		11/19/20 22:14	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.29	1		11/19/20 22:14	100-41-4	
2-Hexanone	ND	ug/L	20.0	1.1	1		11/19/20 22:14	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.67	1		11/19/20 22:14	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	0.87	1		11/19/20 22:14	108-10-1	
Styrene	ND	ug/L	1.0	0.34	1		11/19/20 22:14	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.16	1		11/19/20 22:14	79-34-5	
Tetrachloroethene	ND	ug/L	1.0	0.21	1		11/19/20 22:14	127-18-4	
Toluene	ND	ug/L	1.0	0.31	1		11/19/20 22:14	108-88-3	
1,1,1-Trichloroethane	12.6	ug/L	1.0	0.23	1		11/19/20 22:14	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.19	1		11/19/20 22:14	79-00-5	
Trichloroethene	5.0	ug/L	1.0	0.37	1		11/19/20 22:14	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.42	1		11/19/20 22:14	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.3	1		11/19/20 22:14	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	99	%.	85-116		1		11/19/20 22:14	460-00-4	
Dibromofluoromethane (S)	105	%.	75-120		1		11/19/20 22:14	1868-53-7	
Toluene-d8 (S)	98	%.	83-111		1		11/19/20 22:14	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site

Pace Project No.: 50273460

Sample: MW102B **Lab ID: 50273460019** Collected: 11/16/20 13:33 Received: 11/17/20 09:20 Matrix: Water

Parameters	Results	Units	Report		Prepared	Analyzed	CAS No.	Qual					
			Limit	MDL									
8260 MSV Low Level								Analytical Method: EPA 5030B/8260					
Pace Analytical Services - Indianapolis													
Acetone	ND	ug/L	20.0	7.0	1			11/19/20 22:43 67-64-1					
Benzene	ND	ug/L	1.0	0.34	1			11/19/20 22:43 71-43-2					
Bromochloromethane	ND	ug/L	1.0	1.0	1			11/19/20 22:43 74-97-5					
Bromodichloromethane	ND	ug/L	1.0	0.87	1			11/19/20 22:43 75-27-4					
Bromoform	ND	ug/L	1.0	0.21	1			11/19/20 22:43 75-25-2					
Bromomethane	ND	ug/L	5.0	0.90	1			11/19/20 22:43 74-83-9					
2-Butanone (MEK)	ND	ug/L	20.0	1.3	1			11/19/20 22:43 78-93-3					
Carbon disulfide	ND	ug/L	5.0	0.92	1			11/19/20 22:43 75-15-0					
Carbon tetrachloride	ND	ug/L	1.0	0.31	1			11/19/20 22:43 56-23-5					
Chlorobenzene	ND	ug/L	1.0	0.33	1			11/19/20 22:43 108-90-7					
Chloroethane	1.3J	ug/L	2.0	0.45	1			11/19/20 22:43 75-00-3					
Chloroform	ND	ug/L	1.0	0.99	1			11/19/20 22:43 67-66-3					
Chloromethane	ND	ug/L	2.0	0.92	1			11/19/20 22:43 74-87-3					
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	1.0	1			11/19/20 22:43 96-12-8					
Dibromochloromethane	ND	ug/L	1.0	0.25	1			11/19/20 22:43 124-48-1					
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.23	1			11/19/20 22:43 106-93-4					
1,2-Dichlorobenzene	ND	ug/L	1.0	0.28	1			11/19/20 22:43 95-50-1					
1,3-Dichlorobenzene	ND	ug/L	1.0	0.32	1			11/19/20 22:43 541-73-1					
1,4-Dichlorobenzene	ND	ug/L	1.0	0.28	1			11/19/20 22:43 106-46-7					
1,1-Dichloroethane	2.5	ug/L	1.0	0.34	1			11/19/20 22:43 75-34-3					
1,2-Dichloroethane	ND	ug/L	1.0	0.21	1			11/19/20 22:43 107-06-2					
1,1-Dichloroethene	ND	ug/L	1.0	0.67	1			11/19/20 22:43 75-35-4					
cis-1,2-Dichloroethene	3.8	ug/L	1.0	0.87	1			11/19/20 22:43 156-59-2					
trans-1,2-Dichloroethene	ND	ug/L	1.0	0.87	1			11/19/20 22:43 156-60-5					
1,2-Dichloropropane	ND	ug/L	1.0	0.38	1			11/19/20 22:43 78-87-5					
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.32	1			11/19/20 22:43 10061-01-5					
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.24	1			11/19/20 22:43 10061-02-6					
Ethylbenzene	ND	ug/L	1.0	0.29	1			11/19/20 22:43 100-41-4					
2-Hexanone	ND	ug/L	20.0	1.1	1			11/19/20 22:43 591-78-6					
Methylene Chloride	ND	ug/L	5.0	0.67	1			11/19/20 22:43 75-09-2					
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	0.87	1			11/19/20 22:43 108-10-1					
Styrene	ND	ug/L	1.0	0.34	1			11/19/20 22:43 100-42-5					
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.16	1			11/19/20 22:43 79-34-5					
Tetrachloroethene	ND	ug/L	1.0	0.21	1			11/19/20 22:43 127-18-4					
Toluene	ND	ug/L	1.0	0.31	1			11/19/20 22:43 108-88-3					
1,1,1-Trichloroethane	ND	ug/L	1.0	0.23	1			11/19/20 22:43 71-55-6					
1,1,2-Trichloroethane	ND	ug/L	1.0	0.19	1			11/19/20 22:43 79-00-5					
Trichloroethene	ND	ug/L	1.0	0.37	1			11/19/20 22:43 79-01-6					
Vinyl chloride	5.4	ug/L	1.0	0.42	1			11/19/20 22:43 75-01-4					
Xylene (Total)	ND	ug/L	3.0	1.3	1			11/19/20 22:43 1330-20-7					
Surrogates													
4-Bromofluorobenzene (S)	98	%.	85-116		1			11/19/20 22:43 460-00-4					
Dibromofluoromethane (S)	103	%.	75-120		1			11/19/20 22:43 1868-53-7					
Toluene-d8 (S)	98	%.	83-111		1			11/19/20 22:43 2037-26-5					

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site

Pace Project No.: 50273460

Sample: MW102C	Lab ID: 50273460020	Collected: 11/16/20 14:15	Received: 11/17/20 09:20	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level		Analytical Method: EPA 5030B/8260							
		Pace Analytical Services - Indianapolis							
Acetone	ND	ug/L	20.0	7.0	1		11/19/20 23:12	67-64-1	
Benzene	ND	ug/L	1.0	0.34	1		11/19/20 23:12	71-43-2	
Bromochloromethane	ND	ug/L	1.0	1.0	1		11/19/20 23:12	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.87	1		11/19/20 23:12	75-27-4	
Bromoform	ND	ug/L	1.0	0.21	1		11/19/20 23:12	75-25-2	
Bromomethane	ND	ug/L	5.0	0.90	1		11/19/20 23:12	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	1.3	1		11/19/20 23:12	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.92	1		11/19/20 23:12	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.31	1		11/19/20 23:12	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.33	1		11/19/20 23:12	108-90-7	
Chloroethane	ND	ug/L	2.0	0.45	1		11/19/20 23:12	75-00-3	
Chloroform	ND	ug/L	1.0	0.99	1		11/19/20 23:12	67-66-3	
Chloromethane	ND	ug/L	2.0	0.92	1		11/19/20 23:12	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	1.0	1		11/19/20 23:12	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.25	1		11/19/20 23:12	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.23	1		11/19/20 23:12	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 23:12	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.32	1		11/19/20 23:12	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 23:12	106-46-7	
1,1-Dichloroethane	113	ug/L	1.0	0.34	1		11/19/20 23:12	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.21	1		11/19/20 23:12	107-06-2	
1,1-Dichloroethene	20.3	ug/L	1.0	0.67	1		11/19/20 23:12	75-35-4	
cis-1,2-Dichloroethene	46.5	ug/L	1.0	0.87	1		11/19/20 23:12	156-59-2	
trans-1,2-Dichloroethene	2.8	ug/L	1.0	0.87	1		11/19/20 23:12	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.38	1		11/19/20 23:12	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.32	1		11/19/20 23:12	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.24	1		11/19/20 23:12	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.29	1		11/19/20 23:12	100-41-4	
2-Hexanone	ND	ug/L	20.0	1.1	1		11/19/20 23:12	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.67	1		11/19/20 23:12	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	0.87	1		11/19/20 23:12	108-10-1	
Styrene	ND	ug/L	1.0	0.34	1		11/19/20 23:12	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.16	1		11/19/20 23:12	79-34-5	
Tetrachloroethene	3.8	ug/L	1.0	0.21	1		11/19/20 23:12	127-18-4	
Toluene	ND	ug/L	1.0	0.31	1		11/19/20 23:12	108-88-3	
1,1,1-Trichloroethane	141	ug/L	1.0	0.23	1		11/19/20 23:12	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.19	1		11/19/20 23:12	79-00-5	
Trichloroethene	10.3	ug/L	1.0	0.37	1		11/19/20 23:12	79-01-6	
Vinyl chloride	2.3	ug/L	1.0	0.42	1		11/19/20 23:12	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.3	1		11/19/20 23:12	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	98	%.	85-116		1		11/19/20 23:12	460-00-4	
Dibromofluoromethane (S)	106	%.	75-120		1		11/19/20 23:12	1868-53-7	
Toluene-d8 (S)	97	%.	83-111		1		11/19/20 23:12	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site

Pace Project No.: 50273460

Sample: MW117B	Lab ID: 50273460008	Collected: 11/13/20 17:07	Received: 11/17/20 09:20	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	7.0	1		11/19/20 17:22	67-64-1	
Benzene	ND	ug/L	1.0	0.34	1		11/19/20 17:22	71-43-2	
Bromochloromethane	ND	ug/L	1.0	1.0	1		11/19/20 17:22	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.87	1		11/19/20 17:22	75-27-4	
Bromoform	ND	ug/L	1.0	0.21	1		11/19/20 17:22	75-25-2	
Bromomethane	ND	ug/L	5.0	0.90	1		11/19/20 17:22	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	1.3	1		11/19/20 17:22	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.92	1		11/19/20 17:22	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.31	1		11/19/20 17:22	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.33	1		11/19/20 17:22	108-90-7	
Chloroethane	ND	ug/L	2.0	0.45	1		11/19/20 17:22	75-00-3	
Chloroform	ND	ug/L	1.0	0.99	1		11/19/20 17:22	67-66-3	
Chloromethane	ND	ug/L	2.0	0.92	1		11/19/20 17:22	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	1.0	1		11/19/20 17:22	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.25	1		11/19/20 17:22	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.23	1		11/19/20 17:22	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 17:22	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.32	1		11/19/20 17:22	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 17:22	106-46-7	
1,1-Dichloroethane	9.2	ug/L	1.0	0.34	1		11/19/20 17:22	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.21	1		11/19/20 17:22	107-06-2	
1,1-Dichloroethene	4.2	ug/L	1.0	0.67	1		11/19/20 17:22	75-35-4	
cis-1,2-Dichloroethene	ND	ug/L	1.0	0.87	1		11/19/20 17:22	156-59-2	
trans-1,2-Dichloroethene	ND	ug/L	1.0	0.87	1		11/19/20 17:22	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.38	1		11/19/20 17:22	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.32	1		11/19/20 17:22	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.24	1		11/19/20 17:22	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.29	1		11/19/20 17:22	100-41-4	
2-Hexanone	ND	ug/L	20.0	1.1	1		11/19/20 17:22	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.67	1		11/19/20 17:22	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	0.87	1		11/19/20 17:22	108-10-1	
Styrene	ND	ug/L	1.0	0.34	1		11/19/20 17:22	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.16	1		11/19/20 17:22	79-34-5	
Tetrachloroethene	11.9	ug/L	1.0	0.21	1		11/19/20 17:22	127-18-4	
Toluene	ND	ug/L	1.0	0.31	1		11/19/20 17:22	108-88-3	
1,1,1-Trichloroethane	20.6	ug/L	1.0	0.23	1		11/19/20 17:22	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.19	1		11/19/20 17:22	79-00-5	
Trichloroethene	6.8	ug/L	1.0	0.37	1		11/19/20 17:22	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.42	1		11/19/20 17:22	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.3	1		11/19/20 17:22	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	98	%.	85-116		1		11/19/20 17:22	460-00-4	
Dibromofluoromethane (S)	104	%.	75-120		1		11/19/20 17:22	1868-53-7	
Toluene-d8 (S)	98	%.	83-111		1		11/19/20 17:22	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site

Pace Project No.: 50273460

Sample: MW117C	Lab ID: 50273460007	Collected: 11/13/20 16:39	Received: 11/17/20 09:20	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	7.0	1		11/19/20 16:53	67-64-1	
Benzene	ND	ug/L	1.0	0.34	1		11/19/20 16:53	71-43-2	
Bromochloromethane	ND	ug/L	1.0	1.0	1		11/19/20 16:53	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.87	1		11/19/20 16:53	75-27-4	
Bromoform	ND	ug/L	1.0	0.21	1		11/19/20 16:53	75-25-2	
Bromomethane	ND	ug/L	5.0	0.90	1		11/19/20 16:53	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	1.3	1		11/19/20 16:53	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.92	1		11/19/20 16:53	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.31	1		11/19/20 16:53	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.33	1		11/19/20 16:53	108-90-7	
Chloroethane	9.1	ug/L	2.0	0.45	1		11/19/20 16:53	75-00-3	
Chloroform	ND	ug/L	1.0	0.99	1		11/19/20 16:53	67-66-3	
Chloromethane	ND	ug/L	2.0	0.92	1		11/19/20 16:53	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	1.0	1		11/19/20 16:53	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.25	1		11/19/20 16:53	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.23	1		11/19/20 16:53	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 16:53	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.32	1		11/19/20 16:53	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 16:53	106-46-7	
1,1-Dichloroethane	11.7	ug/L	1.0	0.34	1		11/19/20 16:53	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.21	1		11/19/20 16:53	107-06-2	
1,1-Dichloroethene	2.1	ug/L	1.0	0.67	1		11/19/20 16:53	75-35-4	
cis-1,2-Dichloroethene	0.90J	ug/L	1.0	0.87	1		11/19/20 16:53	156-59-2	
trans-1,2-Dichloroethene	ND	ug/L	1.0	0.87	1		11/19/20 16:53	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.38	1		11/19/20 16:53	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.32	1		11/19/20 16:53	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.24	1		11/19/20 16:53	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.29	1		11/19/20 16:53	100-41-4	
2-Hexanone	ND	ug/L	20.0	1.1	1		11/19/20 16:53	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.67	1		11/19/20 16:53	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	0.87	1		11/19/20 16:53	108-10-1	
Styrene	ND	ug/L	1.0	0.34	1		11/19/20 16:53	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.16	1		11/19/20 16:53	79-34-5	
Tetrachloroethene	3.4	ug/L	1.0	0.21	1		11/19/20 16:53	127-18-4	
Toluene	ND	ug/L	1.0	0.31	1		11/19/20 16:53	108-88-3	
1,1,1-Trichloroethane	6.9	ug/L	1.0	0.23	1		11/19/20 16:53	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.19	1		11/19/20 16:53	79-00-5	
Trichloroethene	2.2	ug/L	1.0	0.37	1		11/19/20 16:53	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.42	1		11/19/20 16:53	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.3	1		11/19/20 16:53	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	98	%.	85-116		1		11/19/20 16:53	460-00-4	
Dibromofluoromethane (S)	104	%.	75-120		1		11/19/20 16:53	1868-53-7	
Toluene-d8 (S)	97	%.	83-111		1		11/19/20 16:53	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site

Pace Project No.: 50273460

Sample: MW117D	Lab ID: 50273460006	Collected: 11/13/20 16:13	Received: 11/17/20 09:20	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	7.0	1		11/19/20 16:24	67-64-1	
Benzene	ND	ug/L	1.0	0.34	1		11/19/20 16:24	71-43-2	
Bromochloromethane	ND	ug/L	1.0	1.0	1		11/19/20 16:24	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.87	1		11/19/20 16:24	75-27-4	
Bromoform	ND	ug/L	1.0	0.21	1		11/19/20 16:24	75-25-2	
Bromomethane	ND	ug/L	5.0	0.90	1		11/19/20 16:24	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	1.3	1		11/19/20 16:24	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.92	1		11/19/20 16:24	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.31	1		11/19/20 16:24	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.33	1		11/19/20 16:24	108-90-7	
Chloroethane	ND	ug/L	2.0	0.45	1		11/19/20 16:24	75-00-3	
Chloroform	ND	ug/L	1.0	0.99	1		11/19/20 16:24	67-66-3	
Chloromethane	ND	ug/L	2.0	0.92	1		11/19/20 16:24	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	1.0	1		11/19/20 16:24	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.25	1		11/19/20 16:24	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.23	1		11/19/20 16:24	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 16:24	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.32	1		11/19/20 16:24	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 16:24	106-46-7	
1,1-Dichloroethane	14.7	ug/L	1.0	0.34	1		11/19/20 16:24	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.21	1		11/19/20 16:24	107-06-2	
1,1-Dichloroethene	4.9	ug/L	1.0	0.67	1		11/19/20 16:24	75-35-4	
cis-1,2-Dichloroethene	ND	ug/L	1.0	0.87	1		11/19/20 16:24	156-59-2	
trans-1,2-Dichloroethene	ND	ug/L	1.0	0.87	1		11/19/20 16:24	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.38	1		11/19/20 16:24	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.32	1		11/19/20 16:24	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.24	1		11/19/20 16:24	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.29	1		11/19/20 16:24	100-41-4	
2-Hexanone	ND	ug/L	20.0	1.1	1		11/19/20 16:24	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.67	1		11/19/20 16:24	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	0.87	1		11/19/20 16:24	108-10-1	
Styrene	ND	ug/L	1.0	0.34	1		11/19/20 16:24	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.16	1		11/19/20 16:24	79-34-5	
Tetrachloroethene	11.7	ug/L	1.0	0.21	1		11/19/20 16:24	127-18-4	
Toluene	ND	ug/L	1.0	0.31	1		11/19/20 16:24	108-88-3	
1,1,1-Trichloroethane	18.2	ug/L	1.0	0.23	1		11/19/20 16:24	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.19	1		11/19/20 16:24	79-00-5	
Trichloroethene	5.6	ug/L	1.0	0.37	1		11/19/20 16:24	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.42	1		11/19/20 16:24	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.3	1		11/19/20 16:24	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	98	%.	85-116		1		11/19/20 16:24	460-00-4	
Dibromofluoromethane (S)	104	%.	75-120		1		11/19/20 16:24	1868-53-7	
Toluene-d8 (S)	97	%.	83-111		1		11/19/20 16:24	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site
Pace Project No.: 50273460

Sample: MW119	Lab ID: 50273460011	Collected: 11/14/20 11:10	Received: 11/17/20 09:20	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	7.0	1		11/19/20 18:50	67-64-1	
Benzene	ND	ug/L	1.0	0.34	1		11/19/20 18:50	71-43-2	
Bromochloromethane	ND	ug/L	1.0	1.0	1		11/19/20 18:50	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.87	1		11/19/20 18:50	75-27-4	
Bromoform	ND	ug/L	1.0	0.21	1		11/19/20 18:50	75-25-2	
Bromomethane	ND	ug/L	5.0	0.90	1		11/19/20 18:50	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	1.3	1		11/19/20 18:50	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.92	1		11/19/20 18:50	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.31	1		11/19/20 18:50	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.33	1		11/19/20 18:50	108-90-7	
Chloroethane	ND	ug/L	2.0	0.45	1		11/19/20 18:50	75-00-3	
Chloroform	ND	ug/L	1.0	0.99	1		11/19/20 18:50	67-66-3	
Chloromethane	ND	ug/L	2.0	0.92	1		11/19/20 18:50	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	1.0	1		11/19/20 18:50	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.25	1		11/19/20 18:50	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.23	1		11/19/20 18:50	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 18:50	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.32	1		11/19/20 18:50	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 18:50	106-46-7	
1,1-Dichloroethane	1.1	ug/L	1.0	0.34	1		11/19/20 18:50	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.21	1		11/19/20 18:50	107-06-2	
1,1-Dichloroethene	ND	ug/L	1.0	0.67	1		11/19/20 18:50	75-35-4	
cis-1,2-Dichloroethene	ND	ug/L	1.0	0.87	1		11/19/20 18:50	156-59-2	
trans-1,2-Dichloroethene	ND	ug/L	1.0	0.87	1		11/19/20 18:50	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.38	1		11/19/20 18:50	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.32	1		11/19/20 18:50	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.24	1		11/19/20 18:50	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.29	1		11/19/20 18:50	100-41-4	
2-Hexanone	ND	ug/L	20.0	1.1	1		11/19/20 18:50	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.67	1		11/19/20 18:50	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	0.87	1		11/19/20 18:50	108-10-1	
Styrene	ND	ug/L	1.0	0.34	1		11/19/20 18:50	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.16	1		11/19/20 18:50	79-34-5	
Tetrachloroethene	ND	ug/L	1.0	0.21	1		11/19/20 18:50	127-18-4	
Toluene	ND	ug/L	1.0	0.31	1		11/19/20 18:50	108-88-3	
1,1,1-Trichloroethane	2.0	ug/L	1.0	0.23	1		11/19/20 18:50	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.19	1		11/19/20 18:50	79-00-5	
Trichloroethene	0.43J	ug/L	1.0	0.37	1		11/19/20 18:50	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.42	1		11/19/20 18:50	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.3	1		11/19/20 18:50	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	98	%.	85-116		1		11/19/20 18:50	460-00-4	
Dibromofluoromethane (S)	104	%.	75-120		1		11/19/20 18:50	1868-53-7	
Toluene-d8 (S)	98	%.	83-111		1		11/19/20 18:50	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site

Pace Project No.: 50273460

Sample: MW121	Lab ID: 50273460017	Collected: 11/15/20 16:17	Received: 11/17/20 09:20	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	7.0	1		11/19/20 21:45	67-64-1	
Benzene	ND	ug/L	1.0	0.34	1		11/19/20 21:45	71-43-2	
Bromochloromethane	ND	ug/L	1.0	1.0	1		11/19/20 21:45	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.87	1		11/19/20 21:45	75-27-4	
Bromoform	ND	ug/L	1.0	0.21	1		11/19/20 21:45	75-25-2	
Bromomethane	ND	ug/L	5.0	0.90	1		11/19/20 21:45	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	1.3	1		11/19/20 21:45	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.92	1		11/19/20 21:45	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.31	1		11/19/20 21:45	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.33	1		11/19/20 21:45	108-90-7	
Chloroethane	ND	ug/L	2.0	0.45	1		11/19/20 21:45	75-00-3	
Chloroform	ND	ug/L	1.0	0.99	1		11/19/20 21:45	67-66-3	
Chloromethane	ND	ug/L	2.0	0.92	1		11/19/20 21:45	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	1.0	1		11/19/20 21:45	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.25	1		11/19/20 21:45	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.23	1		11/19/20 21:45	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 21:45	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.32	1		11/19/20 21:45	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 21:45	106-46-7	
1,1-Dichloroethane	92.5	ug/L	1.0	0.34	1		11/19/20 21:45	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.21	1		11/19/20 21:45	107-06-2	
1,1-Dichloroethene	50.9	ug/L	1.0	0.67	1		11/19/20 21:45	75-35-4	
cis-1,2-Dichloroethene	5.2	ug/L	1.0	0.87	1		11/19/20 21:45	156-59-2	
trans-1,2-Dichloroethene	1.0	ug/L	1.0	0.87	1		11/19/20 21:45	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.38	1		11/19/20 21:45	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.32	1		11/19/20 21:45	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.24	1		11/19/20 21:45	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.29	1		11/19/20 21:45	100-41-4	
2-Hexanone	ND	ug/L	20.0	1.1	1		11/19/20 21:45	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.67	1		11/19/20 21:45	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	0.87	1		11/19/20 21:45	108-10-1	
Styrene	ND	ug/L	1.0	0.34	1		11/19/20 21:45	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.16	1		11/19/20 21:45	79-34-5	
Tetrachloroethene	1.4	ug/L	1.0	0.21	1		11/19/20 21:45	127-18-4	
Toluene	ND	ug/L	1.0	0.31	1		11/19/20 21:45	108-88-3	
1,1,1-Trichloroethane	46.3	ug/L	1.0	0.23	1		11/19/20 21:45	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.19	1		11/19/20 21:45	79-00-5	
Trichloroethene	40.3	ug/L	1.0	0.37	1		11/19/20 21:45	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.42	1		11/19/20 21:45	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.3	1		11/19/20 21:45	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	99	%.	85-116		1		11/19/20 21:45	460-00-4	
Dibromofluoromethane (S)	104	%.	75-120		1		11/19/20 21:45	1868-53-7	
Toluene-d8 (S)	98	%.	83-111		1		11/19/20 21:45	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site
Pace Project No.: 50273460

Sample: MW136	Lab ID: 50273460012	Collected: 11/14/20 13:43	Received: 11/17/20 09:20	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	7.0	1		11/19/20 19:19	67-64-1	
Benzene	ND	ug/L	1.0	0.34	1		11/19/20 19:19	71-43-2	
Bromochloromethane	ND	ug/L	1.0	1.0	1		11/19/20 19:19	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.87	1		11/19/20 19:19	75-27-4	
Bromoform	ND	ug/L	1.0	0.21	1		11/19/20 19:19	75-25-2	
Bromomethane	ND	ug/L	5.0	0.90	1		11/19/20 19:19	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	1.3	1		11/19/20 19:19	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.92	1		11/19/20 19:19	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.31	1		11/19/20 19:19	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.33	1		11/19/20 19:19	108-90-7	
Chloroethane	ND	ug/L	2.0	0.45	1		11/19/20 19:19	75-00-3	
Chloroform	1.1	ug/L	1.0	0.99	1		11/19/20 19:19	67-66-3	
Chloromethane	ND	ug/L	2.0	0.92	1		11/19/20 19:19	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	1.0	1		11/19/20 19:19	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.25	1		11/19/20 19:19	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.23	1		11/19/20 19:19	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 19:19	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.32	1		11/19/20 19:19	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 19:19	106-46-7	
1,1-Dichloroethane	ND	ug/L	1.0	0.34	1		11/19/20 19:19	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.21	1		11/19/20 19:19	107-06-2	
1,1-Dichloroethene	ND	ug/L	1.0	0.67	1		11/19/20 19:19	75-35-4	
cis-1,2-Dichloroethene	ND	ug/L	1.0	0.87	1		11/19/20 19:19	156-59-2	
trans-1,2-Dichloroethene	ND	ug/L	1.0	0.87	1		11/19/20 19:19	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.38	1		11/19/20 19:19	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.32	1		11/19/20 19:19	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.24	1		11/19/20 19:19	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.29	1		11/19/20 19:19	100-41-4	
2-Hexanone	ND	ug/L	20.0	1.1	1		11/19/20 19:19	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.67	1		11/19/20 19:19	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	0.87	1		11/19/20 19:19	108-10-1	
Styrene	ND	ug/L	1.0	0.34	1		11/19/20 19:19	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.16	1		11/19/20 19:19	79-34-5	
Tetrachloroethene	ND	ug/L	1.0	0.21	1		11/19/20 19:19	127-18-4	
Toluene	ND	ug/L	1.0	0.31	1		11/19/20 19:19	108-88-3	
1,1,1-Trichloroethane	ND	ug/L	1.0	0.23	1		11/19/20 19:19	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.19	1		11/19/20 19:19	79-00-5	
Trichloroethene	ND	ug/L	1.0	0.37	1		11/19/20 19:19	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.42	1		11/19/20 19:19	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.3	1		11/19/20 19:19	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	99	%.	85-116		1		11/19/20 19:19	460-00-4	
Dibromofluoromethane (S)	103	%.	75-120		1		11/19/20 19:19	1868-53-7	
Toluene-d8 (S)	99	%.	83-111		1		11/19/20 19:19	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site
Pace Project No.: 50273460

Sample: MW201	Lab ID: 50273460015	Collected: 11/15/20 15:32	Received: 11/17/20 09:20	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	7.0	1		11/19/20 20:46	67-64-1	
Benzene	ND	ug/L	1.0	0.34	1		11/19/20 20:46	71-43-2	
Bromochloromethane	ND	ug/L	1.0	1.0	1		11/19/20 20:46	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.87	1		11/19/20 20:46	75-27-4	
Bromoform	ND	ug/L	1.0	0.21	1		11/19/20 20:46	75-25-2	
Bromomethane	ND	ug/L	5.0	0.90	1		11/19/20 20:46	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	1.3	1		11/19/20 20:46	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.92	1		11/19/20 20:46	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.31	1		11/19/20 20:46	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.33	1		11/19/20 20:46	108-90-7	
Chloroethane	ND	ug/L	2.0	0.45	1		11/19/20 20:46	75-00-3	
Chloroform	ND	ug/L	1.0	0.99	1		11/19/20 20:46	67-66-3	
Chloromethane	ND	ug/L	2.0	0.92	1		11/19/20 20:46	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	1.0	1		11/19/20 20:46	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.25	1		11/19/20 20:46	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.23	1		11/19/20 20:46	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 20:46	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.32	1		11/19/20 20:46	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 20:46	106-46-7	
1,1-Dichloroethane	1.1	ug/L	1.0	0.34	1		11/19/20 20:46	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.21	1		11/19/20 20:46	107-06-2	
1,1-Dichloroethene	ND	ug/L	1.0	0.67	1		11/19/20 20:46	75-35-4	
cis-1,2-Dichloroethene	ND	ug/L	1.0	0.87	1		11/19/20 20:46	156-59-2	
trans-1,2-Dichloroethene	ND	ug/L	1.0	0.87	1		11/19/20 20:46	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.38	1		11/19/20 20:46	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.32	1		11/19/20 20:46	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.24	1		11/19/20 20:46	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.29	1		11/19/20 20:46	100-41-4	
2-Hexanone	ND	ug/L	20.0	1.1	1		11/19/20 20:46	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.67	1		11/19/20 20:46	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	0.87	1		11/19/20 20:46	108-10-1	
Styrene	ND	ug/L	1.0	0.34	1		11/19/20 20:46	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.16	1		11/19/20 20:46	79-34-5	
Tetrachloroethene	1.6	ug/L	1.0	0.21	1		11/19/20 20:46	127-18-4	
Toluene	ND	ug/L	1.0	0.31	1		11/19/20 20:46	108-88-3	
1,1,1-Trichloroethane	1.1	ug/L	1.0	0.23	1		11/19/20 20:46	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.19	1		11/19/20 20:46	79-00-5	
Trichloroethene	0.37J	ug/L	1.0	0.37	1		11/19/20 20:46	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.42	1		11/19/20 20:46	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.3	1		11/19/20 20:46	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	98	%.	85-116		1		11/19/20 20:46	460-00-4	
Dibromofluoromethane (S)	103	%.	75-120		1		11/19/20 20:46	1868-53-7	
Toluene-d8 (S)	98	%.	83-111		1		11/19/20 20:46	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site
Pace Project No.: 50273460

Sample: MW202	Lab ID: 50273460014	Collected: 11/15/20 14:36	Received: 11/17/20 09:20	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	7.0	1		11/19/20 20:17	67-64-1	
Benzene	ND	ug/L	1.0	0.34	1		11/19/20 20:17	71-43-2	
Bromochloromethane	ND	ug/L	1.0	1.0	1		11/19/20 20:17	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.87	1		11/19/20 20:17	75-27-4	
Bromoform	ND	ug/L	1.0	0.21	1		11/19/20 20:17	75-25-2	
Bromomethane	ND	ug/L	5.0	0.90	1		11/19/20 20:17	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	1.3	1		11/19/20 20:17	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.92	1		11/19/20 20:17	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.31	1		11/19/20 20:17	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.33	1		11/19/20 20:17	108-90-7	
Chloroethane	ND	ug/L	2.0	0.45	1		11/19/20 20:17	75-00-3	
Chloroform	ND	ug/L	1.0	0.99	1		11/19/20 20:17	67-66-3	
Chloromethane	ND	ug/L	2.0	0.92	1		11/19/20 20:17	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	1.0	1		11/19/20 20:17	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.25	1		11/19/20 20:17	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.23	1		11/19/20 20:17	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 20:17	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.32	1		11/19/20 20:17	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 20:17	106-46-7	
1,1-Dichloroethane	ND	ug/L	1.0	0.34	1		11/19/20 20:17	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.21	1		11/19/20 20:17	107-06-2	
1,1-Dichloroethene	ND	ug/L	1.0	0.67	1		11/19/20 20:17	75-35-4	
cis-1,2-Dichloroethene	ND	ug/L	1.0	0.87	1		11/19/20 20:17	156-59-2	
trans-1,2-Dichloroethene	ND	ug/L	1.0	0.87	1		11/19/20 20:17	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.38	1		11/19/20 20:17	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.32	1		11/19/20 20:17	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.24	1		11/19/20 20:17	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.29	1		11/19/20 20:17	100-41-4	
2-Hexanone	ND	ug/L	20.0	1.1	1		11/19/20 20:17	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.67	1		11/19/20 20:17	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	0.87	1		11/19/20 20:17	108-10-1	
Styrene	ND	ug/L	1.0	0.34	1		11/19/20 20:17	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.16	1		11/19/20 20:17	79-34-5	
Tetrachloroethene	0.63J	ug/L	1.0	0.21	1		11/19/20 20:17	127-18-4	
Toluene	ND	ug/L	1.0	0.31	1		11/19/20 20:17	108-88-3	
1,1,1-Trichloroethane	ND	ug/L	1.0	0.23	1		11/19/20 20:17	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.19	1		11/19/20 20:17	79-00-5	
Trichloroethene	ND	ug/L	1.0	0.37	1		11/19/20 20:17	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.42	1		11/19/20 20:17	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.3	1		11/19/20 20:17	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	100	%.	85-116		1		11/19/20 20:17	460-00-4	
Dibromofluoromethane (S)	103	%.	75-120		1		11/19/20 20:17	1868-53-7	
Toluene-d8 (S)	98	%.	83-111		1		11/19/20 20:17	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site
Pace Project No.: 50273460

Sample: MW203	Lab ID: 50273460013	Collected: 11/15/20 12:35	Received: 11/17/20 09:20	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level		Analytical Method: EPA 5030B/8260							
		Pace Analytical Services - Indianapolis							
Acetone	ND	ug/L	20.0	7.0	1		11/19/20 19:48	67-64-1	
Benzene	ND	ug/L	1.0	0.34	1		11/19/20 19:48	71-43-2	
Bromochloromethane	ND	ug/L	1.0	1.0	1		11/19/20 19:48	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.87	1		11/19/20 19:48	75-27-4	
Bromoform	ND	ug/L	1.0	0.21	1		11/19/20 19:48	75-25-2	
Bromomethane	ND	ug/L	5.0	0.90	1		11/19/20 19:48	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	1.3	1		11/19/20 19:48	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.92	1		11/19/20 19:48	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.31	1		11/19/20 19:48	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.33	1		11/19/20 19:48	108-90-7	
Chloroethane	ND	ug/L	2.0	0.45	1		11/19/20 19:48	75-00-3	
Chloroform	ND	ug/L	1.0	0.99	1		11/19/20 19:48	67-66-3	
Chloromethane	ND	ug/L	2.0	0.92	1		11/19/20 19:48	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	1.0	1		11/19/20 19:48	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.25	1		11/19/20 19:48	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.23	1		11/19/20 19:48	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 19:48	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.32	1		11/19/20 19:48	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 19:48	106-46-7	
1,1-Dichloroethane	ND	ug/L	1.0	0.34	1		11/19/20 19:48	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.21	1		11/19/20 19:48	107-06-2	
1,1-Dichloroethene	ND	ug/L	1.0	0.67	1		11/19/20 19:48	75-35-4	
cis-1,2-Dichloroethene	ND	ug/L	1.0	0.87	1		11/19/20 19:48	156-59-2	
trans-1,2-Dichloroethene	ND	ug/L	1.0	0.87	1		11/19/20 19:48	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.38	1		11/19/20 19:48	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.32	1		11/19/20 19:48	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.24	1		11/19/20 19:48	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.29	1		11/19/20 19:48	100-41-4	
2-Hexanone	ND	ug/L	20.0	1.1	1		11/19/20 19:48	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.67	1		11/19/20 19:48	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	0.87	1		11/19/20 19:48	108-10-1	
Styrene	ND	ug/L	1.0	0.34	1		11/19/20 19:48	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.16	1		11/19/20 19:48	79-34-5	
Tetrachloroethene	2.6	ug/L	1.0	0.21	1		11/19/20 19:48	127-18-4	
Toluene	ND	ug/L	1.0	0.31	1		11/19/20 19:48	108-88-3	
1,1,1-Trichloroethane	ND	ug/L	1.0	0.23	1		11/19/20 19:48	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.19	1		11/19/20 19:48	79-00-5	
Trichloroethene	ND	ug/L	1.0	0.37	1		11/19/20 19:48	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.42	1		11/19/20 19:48	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.3	1		11/19/20 19:48	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	98	%.	85-116		1		11/19/20 19:48	460-00-4	
Dibromofluoromethane (S)	103	%.	75-120		1		11/19/20 19:48	1868-53-7	
Toluene-d8 (S)	97	%.	83-111		1		11/19/20 19:48	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site

Pace Project No.: 50273460

Sample: MW205A	Lab ID: 50273460004	Collected: 11/13/20 14:39	Received: 11/17/20 09:20	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	3.6	1		11/19/20 22:58	67-64-1	
Benzene	ND	ug/L	1.0	0.35	1		11/19/20 22:58	71-43-2	
Bromochloromethane	ND	ug/L	1.0	0.36	1		11/19/20 22:58	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.28	1		11/19/20 22:58	75-27-4	
Bromoform	ND	ug/L	1.0	0.21	1		11/19/20 22:58	75-25-2	
Bromomethane	ND	ug/L	5.0	0.46	1		11/19/20 22:58	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	1.4	1		11/19/20 22:58	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.26	1		11/19/20 22:58	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.22	1		11/19/20 22:58	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.34	1		11/19/20 22:58	108-90-7	
Chloroethane	ND	ug/L	2.0	0.72	1		11/19/20 22:58	75-00-3	
Chloroform	ND	ug/L	1.0	0.39	1		11/19/20 22:58	67-66-3	
Chloromethane	ND	ug/L	2.0	0.42	1		11/19/20 22:58	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	0.61	1		11/19/20 22:58	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.26	1		11/19/20 22:58	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.19	1		11/19/20 22:58	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 22:58	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.33	1		11/19/20 22:58	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.33	1		11/19/20 22:58	106-46-7	
1,1-Dichloroethane	18.2	ug/L	1.0	0.34	1		11/19/20 22:58	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.27	1		11/19/20 22:58	107-06-2	
1,1-Dichloroethene	5.1	ug/L	1.0	0.26	1		11/19/20 22:58	75-35-4	
cis-1,2-Dichloroethene	1.0J	ug/L	1.0	0.36	1		11/19/20 22:58	156-59-2	
trans-1,2-Dichloroethene	ND	ug/L	1.0	0.37	1		11/19/20 22:58	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.36	1		11/19/20 22:58	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.31	1		11/19/20 22:58	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.24	1		11/19/20 22:58	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.31	1		11/19/20 22:58	100-41-4	
2-Hexanone	ND	ug/L	20.0	0.88	1		11/19/20 22:58	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.79	1		11/19/20 22:58	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	0.81	1		11/19/20 22:58	108-10-1	
Styrene	ND	ug/L	1.0	0.32	1		11/19/20 22:58	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.14	1		11/19/20 22:58	79-34-5	
Tetrachloroethene	12.9	ug/L	1.0	0.24	1		11/19/20 22:58	127-18-4	
Toluene	ND	ug/L	1.0	0.33	1		11/19/20 22:58	108-88-3	
1,1,1-Trichloroethane	16.9	ug/L	1.0	0.22	1		11/19/20 22:58	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.25	1		11/19/20 22:58	79-00-5	
Trichloroethene	6.0	ug/L	1.0	0.34	1		11/19/20 22:58	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.45	1		11/19/20 22:58	75-01-4	
Xylene (Total)	ND	ug/L	3.0	0.71	1		11/19/20 22:58	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	96	%.	85-116		1		11/19/20 22:58	460-00-4	
Dibromofluoromethane (S)	104	%.	75-120		1		11/19/20 22:58	1868-53-7	
Toluene-d8 (S)	98	%.	83-111		1		11/19/20 22:58	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site

Pace Project No.: 50273460

Sample: MW205B	Lab ID: 50273460005	Collected: 11/13/20 15:30	Received: 11/17/20 09:20	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level		Analytical Method: EPA 5030B/8260							
		Pace Analytical Services - Indianapolis							
Acetone	ND	ug/L	20.0	7.0	1		11/19/20 08:36	67-64-1	
Benzene	ND	ug/L	1.0	0.34	1		11/19/20 08:36	71-43-2	
Bromochloromethane	ND	ug/L	1.0	1.0	1		11/19/20 08:36	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.87	1		11/19/20 08:36	75-27-4	
Bromoform	ND	ug/L	1.0	0.21	1		11/19/20 08:36	75-25-2	
Bromomethane	ND	ug/L	5.0	0.90	1		11/19/20 08:36	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	1.3	1		11/19/20 08:36	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.92	1		11/19/20 08:36	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.31	1		11/19/20 08:36	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.33	1		11/19/20 08:36	108-90-7	
Chloroethane	ND	ug/L	2.0	0.45	1		11/19/20 08:36	75-00-3	
Chloroform	ND	ug/L	1.0	0.99	1		11/19/20 08:36	67-66-3	
Chloromethane	ND	ug/L	2.0	0.92	1		11/19/20 08:36	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	1.0	1		11/19/20 08:36	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.25	1		11/19/20 08:36	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.23	1		11/19/20 08:36	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 08:36	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.32	1		11/19/20 08:36	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 08:36	106-46-7	
1,1-Dichloroethane	18.2	ug/L	1.0	0.34	1		11/19/20 08:36	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.21	1		11/19/20 08:36	107-06-2	
1,1-Dichloroethene	5.6	ug/L	1.0	0.67	1		11/19/20 08:36	75-35-4	
cis-1,2-Dichloroethene	0.93J	ug/L	1.0	0.87	1		11/19/20 08:36	156-59-2	
trans-1,2-Dichloroethene	ND	ug/L	1.0	0.87	1		11/19/20 08:36	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.38	1		11/19/20 08:36	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.32	1		11/19/20 08:36	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.24	1		11/19/20 08:36	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.29	1		11/19/20 08:36	100-41-4	
2-Hexanone	ND	ug/L	20.0	1.1	1		11/19/20 08:36	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.67	1		11/19/20 08:36	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	0.87	1		11/19/20 08:36	108-10-1	
Styrene	ND	ug/L	1.0	0.34	1		11/19/20 08:36	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.16	1		11/19/20 08:36	79-34-5	
Tetrachloroethene	12.6	ug/L	1.0	0.21	1		11/19/20 08:36	127-18-4	
Toluene	ND	ug/L	1.0	0.31	1		11/19/20 08:36	108-88-3	
1,1,1-Trichloroethane	16.8	ug/L	1.0	0.23	1		11/19/20 08:36	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.19	1		11/19/20 08:36	79-00-5	
Trichloroethene	6.2	ug/L	1.0	0.37	1		11/19/20 08:36	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.42	1		11/19/20 08:36	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.3	1		11/19/20 08:36	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	97	%.	85-116		1		11/19/20 08:36	460-00-4	
Dibromofluoromethane (S)	103	%.	75-120		1		11/19/20 08:36	1868-53-7	
Toluene-d8 (S)	98	%.	83-111		1		11/19/20 08:36	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site

Pace Project No.: 50273460

Sample: MW206A	Lab ID: 50273460001	Collected: 11/13/20 12:31	Received: 11/17/20 09:20	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	3.6	1		11/19/20 22:28	67-64-1	
Benzene	ND	ug/L	1.0	0.35	1		11/19/20 22:28	71-43-2	
Bromochloromethane	ND	ug/L	1.0	0.36	1		11/19/20 22:28	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.28	1		11/19/20 22:28	75-27-4	
Bromoform	ND	ug/L	1.0	0.21	1		11/19/20 22:28	75-25-2	
Bromomethane	ND	ug/L	5.0	0.46	1		11/19/20 22:28	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	1.4	1		11/19/20 22:28	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.26	1		11/19/20 22:28	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.22	1		11/19/20 22:28	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.34	1		11/19/20 22:28	108-90-7	
Chloroethane	ND	ug/L	2.0	0.72	1		11/19/20 22:28	75-00-3	
Chloroform	ND	ug/L	1.0	0.39	1		11/19/20 22:28	67-66-3	
Chloromethane	ND	ug/L	2.0	0.42	1		11/19/20 22:28	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	0.61	1		11/19/20 22:28	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.26	1		11/19/20 22:28	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.19	1		11/19/20 22:28	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 22:28	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.33	1		11/19/20 22:28	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.33	1		11/19/20 22:28	106-46-7	
1,1-Dichloroethane	9.4	ug/L	1.0	0.34	1		11/19/20 22:28	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.27	1		11/19/20 22:28	107-06-2	
1,1-Dichloroethene	3.3	ug/L	1.0	0.26	1		11/19/20 22:28	75-35-4	
cis-1,2-Dichloroethene	1.4	ug/L	1.0	0.36	1		11/19/20 22:28	156-59-2	
trans-1,2-Dichloroethene	ND	ug/L	1.0	0.37	1		11/19/20 22:28	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.36	1		11/19/20 22:28	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.31	1		11/19/20 22:28	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.24	1		11/19/20 22:28	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.31	1		11/19/20 22:28	100-41-4	
2-Hexanone	ND	ug/L	20.0	0.88	1		11/19/20 22:28	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.79	1		11/19/20 22:28	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	0.81	1		11/19/20 22:28	108-10-1	
Styrene	ND	ug/L	1.0	0.32	1		11/19/20 22:28	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.14	1		11/19/20 22:28	79-34-5	
Tetrachloroethene	7.0	ug/L	1.0	0.24	1		11/19/20 22:28	127-18-4	
Toluene	ND	ug/L	1.0	0.33	1		11/19/20 22:28	108-88-3	
1,1,1-Trichloroethane	15.4	ug/L	1.0	0.22	1		11/19/20 22:28	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.25	1		11/19/20 22:28	79-00-5	
Trichloroethene	5.5	ug/L	1.0	0.34	1		11/19/20 22:28	79-01-6	
Vinyl chloride	0.52J	ug/L	1.0	0.45	1		11/19/20 22:28	75-01-4	
Xylene (Total)	ND	ug/L	3.0	0.71	1		11/19/20 22:28	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	97	%.	85-116		1		11/19/20 22:28	460-00-4	
Dibromofluoromethane (S)	103	%.	75-120		1		11/19/20 22:28	1868-53-7	
Toluene-d8 (S)	100	%.	83-111		1		11/19/20 22:28	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site

Pace Project No.: 50273460

Sample: MW206B	Lab ID: 50273460002	Collected: 11/13/20 13:14	Received: 11/17/20 09:20	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	7.0	1		11/19/20 07:08	67-64-1	
Benzene	ND	ug/L	1.0	0.34	1		11/19/20 07:08	71-43-2	
Bromochloromethane	ND	ug/L	1.0	1.0	1		11/19/20 07:08	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.87	1		11/19/20 07:08	75-27-4	
Bromoform	ND	ug/L	1.0	0.21	1		11/19/20 07:08	75-25-2	
Bromomethane	ND	ug/L	5.0	0.90	1		11/19/20 07:08	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	1.3	1		11/19/20 07:08	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.92	1		11/19/20 07:08	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.31	1		11/19/20 07:08	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.33	1		11/19/20 07:08	108-90-7	
Chloroethane	ND	ug/L	2.0	0.45	1		11/19/20 07:08	75-00-3	
Chloroform	ND	ug/L	1.0	0.99	1		11/19/20 07:08	67-66-3	
Chloromethane	ND	ug/L	2.0	0.92	1		11/19/20 07:08	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	1.0	1		11/19/20 07:08	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.25	1		11/19/20 07:08	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.23	1		11/19/20 07:08	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 07:08	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.32	1		11/19/20 07:08	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 07:08	106-46-7	
1,1-Dichloroethane	23.4	ug/L	1.0	0.34	1		11/19/20 07:08	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.21	1		11/19/20 07:08	107-06-2	
1,1-Dichloroethene	23.9	ug/L	1.0	0.67	1		11/19/20 07:08	75-35-4	
cis-1,2-Dichloroethene	20.0	ug/L	1.0	0.87	1		11/19/20 07:08	156-59-2	
trans-1,2-Dichloroethene	ND	ug/L	1.0	0.87	1		11/19/20 07:08	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.38	1		11/19/20 07:08	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.32	1		11/19/20 07:08	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.24	1		11/19/20 07:08	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.29	1		11/19/20 07:08	100-41-4	
2-Hexanone	ND	ug/L	20.0	1.1	1		11/19/20 07:08	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.67	1		11/19/20 07:08	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	0.87	1		11/19/20 07:08	108-10-1	
Styrene	ND	ug/L	1.0	0.34	1		11/19/20 07:08	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.16	1		11/19/20 07:08	79-34-5	
Tetrachloroethene	21.2	ug/L	1.0	0.21	1		11/19/20 07:08	127-18-4	
Toluene	ND	ug/L	1.0	0.31	1		11/19/20 07:08	108-88-3	
1,1,1-Trichloroethane	28.3	ug/L	1.0	0.23	1		11/19/20 07:08	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.19	1		11/19/20 07:08	79-00-5	
Trichloroethene	17.5	ug/L	1.0	0.37	1		11/19/20 07:08	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.42	1		11/19/20 07:08	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.3	1		11/19/20 07:08	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	99	%.	85-116		1		11/19/20 07:08	460-00-4	
Dibromofluoromethane (S)	104	%.	75-120		1		11/19/20 07:08	1868-53-7	
Toluene-d8 (S)	99	%.	83-111		1		11/19/20 07:08	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site

Pace Project No.: 50273460

Sample: MW206C	Lab ID: 50273460003	Collected: 11/13/20 13:54	Received: 11/17/20 09:20	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	7.0	1		11/19/20 07:37	67-64-1	
Benzene	ND	ug/L	1.0	0.34	1		11/19/20 07:37	71-43-2	
Bromochloromethane	ND	ug/L	1.0	1.0	1		11/19/20 07:37	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.87	1		11/19/20 07:37	75-27-4	
Bromoform	ND	ug/L	1.0	0.21	1		11/19/20 07:37	75-25-2	
Bromomethane	ND	ug/L	5.0	0.90	1		11/19/20 07:37	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	1.3	1		11/19/20 07:37	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.92	1		11/19/20 07:37	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.31	1		11/19/20 07:37	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.33	1		11/19/20 07:37	108-90-7	
Chloroethane	ND	ug/L	2.0	0.45	1		11/19/20 07:37	75-00-3	
Chloroform	ND	ug/L	1.0	0.99	1		11/19/20 07:37	67-66-3	
Chloromethane	ND	ug/L	2.0	0.92	1		11/19/20 07:37	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	1.0	1		11/19/20 07:37	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.25	1		11/19/20 07:37	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.23	1		11/19/20 07:37	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 07:37	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.32	1		11/19/20 07:37	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 07:37	106-46-7	
1,1-Dichloroethane	34.5	ug/L	1.0	0.34	1		11/19/20 07:37	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.21	1		11/19/20 07:37	107-06-2	
1,1-Dichloroethene	11.5	ug/L	1.0	0.67	1		11/19/20 07:37	75-35-4	
cis-1,2-Dichloroethene	46.5	ug/L	1.0	0.87	1		11/19/20 07:37	156-59-2	
trans-1,2-Dichloroethene	ND	ug/L	1.0	0.87	1		11/19/20 07:37	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.38	1		11/19/20 07:37	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.32	1		11/19/20 07:37	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.24	1		11/19/20 07:37	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.29	1		11/19/20 07:37	100-41-4	
2-Hexanone	ND	ug/L	20.0	1.1	1		11/19/20 07:37	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.67	1		11/19/20 07:37	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	0.87	1		11/19/20 07:37	108-10-1	
Styrene	ND	ug/L	1.0	0.34	1		11/19/20 07:37	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.16	1		11/19/20 07:37	79-34-5	
Tetrachloroethene	0.49J	ug/L	1.0	0.21	1		11/19/20 07:37	127-18-4	
Toluene	ND	ug/L	1.0	0.31	1		11/19/20 07:37	108-88-3	
1,1,1-Trichloroethane	ND	ug/L	1.0	0.23	1		11/19/20 07:37	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.19	1		11/19/20 07:37	79-00-5	
Trichloroethene	7.6	ug/L	1.0	0.37	1		11/19/20 07:37	79-01-6	
Vinyl chloride	23.2	ug/L	1.0	0.42	1		11/19/20 07:37	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.3	1		11/19/20 07:37	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	98	%.	85-116		1		11/19/20 07:37	460-00-4	
Dibromofluoromethane (S)	103	%.	75-120		1		11/19/20 07:37	1868-53-7	
Toluene-d8 (S)	100	%.	83-111		1		11/19/20 07:37	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site
Pace Project No.: 50273460

Sample: MW207	Lab ID: 50273460010	Collected: 11/14/20 10:35	Received: 11/17/20 09:20	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	7.0	1		11/19/20 18:21	67-64-1	
Benzene	ND	ug/L	1.0	0.34	1		11/19/20 18:21	71-43-2	
Bromochloromethane	ND	ug/L	1.0	1.0	1		11/19/20 18:21	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.87	1		11/19/20 18:21	75-27-4	
Bromoform	ND	ug/L	1.0	0.21	1		11/19/20 18:21	75-25-2	
Bromomethane	ND	ug/L	5.0	0.90	1		11/19/20 18:21	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	1.3	1		11/19/20 18:21	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.92	1		11/19/20 18:21	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.31	1		11/19/20 18:21	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.33	1		11/19/20 18:21	108-90-7	
Chloroethane	ND	ug/L	2.0	0.45	1		11/19/20 18:21	75-00-3	
Chloroform	ND	ug/L	1.0	0.99	1		11/19/20 18:21	67-66-3	
Chloromethane	ND	ug/L	2.0	0.92	1		11/19/20 18:21	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	1.0	1		11/19/20 18:21	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.25	1		11/19/20 18:21	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.23	1		11/19/20 18:21	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 18:21	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.32	1		11/19/20 18:21	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 18:21	106-46-7	
1,1-Dichloroethane	2.4	ug/L	1.0	0.34	1		11/19/20 18:21	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.21	1		11/19/20 18:21	107-06-2	
1,1-Dichloroethene	0.77J	ug/L	1.0	0.67	1		11/19/20 18:21	75-35-4	
cis-1,2-Dichloroethene	ND	ug/L	1.0	0.87	1		11/19/20 18:21	156-59-2	
trans-1,2-Dichloroethene	ND	ug/L	1.0	0.87	1		11/19/20 18:21	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.38	1		11/19/20 18:21	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.32	1		11/19/20 18:21	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.24	1		11/19/20 18:21	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.29	1		11/19/20 18:21	100-41-4	
2-Hexanone	ND	ug/L	20.0	1.1	1		11/19/20 18:21	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.67	1		11/19/20 18:21	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	0.87	1		11/19/20 18:21	108-10-1	
Styrene	ND	ug/L	1.0	0.34	1		11/19/20 18:21	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.16	1		11/19/20 18:21	79-34-5	
Tetrachloroethene	1.9	ug/L	1.0	0.21	1		11/19/20 18:21	127-18-4	
Toluene	ND	ug/L	1.0	0.31	1		11/19/20 18:21	108-88-3	
1,1,1-Trichloroethane	3.2	ug/L	1.0	0.23	1		11/19/20 18:21	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.19	1		11/19/20 18:21	79-00-5	
Trichloroethene	2.5	ug/L	1.0	0.37	1		11/19/20 18:21	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.42	1		11/19/20 18:21	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.3	1		11/19/20 18:21	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	99	%.	85-116		1		11/19/20 18:21	460-00-4	
Dibromofluoromethane (S)	103	%.	75-120		1		11/19/20 18:21	1868-53-7	
Toluene-d8 (S)	98	%.	83-111		1		11/19/20 18:21	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site
Pace Project No.: 50273460

Sample: MW47	Lab ID: 50273460009	Collected: 11/14/20 09:36	Received: 11/17/20 09:20	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	7.0	1		11/19/20 17:51	67-64-1	
Benzene	ND	ug/L	1.0	0.34	1		11/19/20 17:51	71-43-2	
Bromochloromethane	ND	ug/L	1.0	1.0	1		11/19/20 17:51	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.87	1		11/19/20 17:51	75-27-4	
Bromoform	ND	ug/L	1.0	0.21	1		11/19/20 17:51	75-25-2	
Bromomethane	ND	ug/L	5.0	0.90	1		11/19/20 17:51	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	1.3	1		11/19/20 17:51	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.92	1		11/19/20 17:51	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.31	1		11/19/20 17:51	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.33	1		11/19/20 17:51	108-90-7	
Chloroethane	ND	ug/L	2.0	0.45	1		11/19/20 17:51	75-00-3	
Chloroform	ND	ug/L	1.0	0.99	1		11/19/20 17:51	67-66-3	
Chloromethane	ND	ug/L	2.0	0.92	1		11/19/20 17:51	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	1.0	1		11/19/20 17:51	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.25	1		11/19/20 17:51	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.23	1		11/19/20 17:51	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 17:51	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.32	1		11/19/20 17:51	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 17:51	106-46-7	
1,1-Dichloroethane	ND	ug/L	1.0	0.34	1		11/19/20 17:51	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.21	1		11/19/20 17:51	107-06-2	
1,1-Dichloroethene	ND	ug/L	1.0	0.67	1		11/19/20 17:51	75-35-4	
cis-1,2-Dichloroethene	ND	ug/L	1.0	0.87	1		11/19/20 17:51	156-59-2	
trans-1,2-Dichloroethene	ND	ug/L	1.0	0.87	1		11/19/20 17:51	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.38	1		11/19/20 17:51	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.32	1		11/19/20 17:51	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.24	1		11/19/20 17:51	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.29	1		11/19/20 17:51	100-41-4	
2-Hexanone	ND	ug/L	20.0	1.1	1		11/19/20 17:51	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.67	1		11/19/20 17:51	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	0.87	1		11/19/20 17:51	108-10-1	
Styrene	ND	ug/L	1.0	0.34	1		11/19/20 17:51	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.16	1		11/19/20 17:51	79-34-5	
Tetrachloroethene	ND	ug/L	1.0	0.21	1		11/19/20 17:51	127-18-4	
Toluene	ND	ug/L	1.0	0.31	1		11/19/20 17:51	108-88-3	
1,1,1-Trichloroethane	ND	ug/L	1.0	0.23	1		11/19/20 17:51	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.19	1		11/19/20 17:51	79-00-5	
Trichloroethene	ND	ug/L	1.0	0.37	1		11/19/20 17:51	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.42	1		11/19/20 17:51	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.3	1		11/19/20 17:51	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	99	%.	85-116		1		11/19/20 17:51	460-00-4	
Dibromofluoromethane (S)	103	%.	75-120		1		11/19/20 17:51	1868-53-7	
Toluene-d8 (S)	97	%.	83-111		1		11/19/20 17:51	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site
Pace Project No.: 50273460

Sample: FD-1	Lab ID: 50273460016	Collected: 11/15/20 15:35	Received: 11/17/20 09:20	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	7.0	1		11/19/20 21:15	67-64-1	
Benzene	ND	ug/L	1.0	0.34	1		11/19/20 21:15	71-43-2	
Bromochloromethane	ND	ug/L	1.0	1.0	1		11/19/20 21:15	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.87	1		11/19/20 21:15	75-27-4	
Bromoform	ND	ug/L	1.0	0.21	1		11/19/20 21:15	75-25-2	
Bromomethane	ND	ug/L	5.0	0.90	1		11/19/20 21:15	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	1.3	1		11/19/20 21:15	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.92	1		11/19/20 21:15	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.31	1		11/19/20 21:15	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.33	1		11/19/20 21:15	108-90-7	
Chloroethane	ND	ug/L	2.0	0.45	1		11/19/20 21:15	75-00-3	
Chloroform	ND	ug/L	1.0	0.99	1		11/19/20 21:15	67-66-3	
Chloromethane	ND	ug/L	2.0	0.92	1		11/19/20 21:15	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	1.0	1		11/19/20 21:15	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.25	1		11/19/20 21:15	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.23	1		11/19/20 21:15	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 21:15	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.32	1		11/19/20 21:15	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 21:15	106-46-7	
1,1-Dichloroethane	0.99J	ug/L	1.0	0.34	1		11/19/20 21:15	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.21	1		11/19/20 21:15	107-06-2	
1,1-Dichloroethene	ND	ug/L	1.0	0.67	1		11/19/20 21:15	75-35-4	
cis-1,2-Dichloroethene	ND	ug/L	1.0	0.87	1		11/19/20 21:15	156-59-2	
trans-1,2-Dichloroethene	ND	ug/L	1.0	0.87	1		11/19/20 21:15	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.38	1		11/19/20 21:15	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.32	1		11/19/20 21:15	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.24	1		11/19/20 21:15	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.29	1		11/19/20 21:15	100-41-4	
2-Hexanone	ND	ug/L	20.0	1.1	1		11/19/20 21:15	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.67	1		11/19/20 21:15	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	0.87	1		11/19/20 21:15	108-10-1	
Styrene	ND	ug/L	1.0	0.34	1		11/19/20 21:15	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.16	1		11/19/20 21:15	79-34-5	
Tetrachloroethene	1.6	ug/L	1.0	0.21	1		11/19/20 21:15	127-18-4	
Toluene	ND	ug/L	1.0	0.31	1		11/19/20 21:15	108-88-3	
1,1,1-Trichloroethane	1.1	ug/L	1.0	0.23	1		11/19/20 21:15	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.19	1		11/19/20 21:15	79-00-5	
Trichloroethene	ND	ug/L	1.0	0.37	1		11/19/20 21:15	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.42	1		11/19/20 21:15	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.3	1		11/19/20 21:15	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	99	%.	85-116		1		11/19/20 21:15	460-00-4	
Dibromofluoromethane (S)	103	%.	75-120		1		11/19/20 21:15	1868-53-7	
Toluene-d8 (S)	98	%.	83-111		1		11/19/20 21:15	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site

Pace Project No.: 50273460

Sample: Trip Blank	Lab ID: 50273460024	Collected: 11/16/20 00:00	Received: 11/17/20 09:20	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	3.6	1		11/19/20 23:27	67-64-1	
Benzene	ND	ug/L	1.0	0.35	1		11/19/20 23:27	71-43-2	
Bromochloromethane	ND	ug/L	1.0	0.36	1		11/19/20 23:27	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.28	1		11/19/20 23:27	75-27-4	
Bromoform	ND	ug/L	1.0	0.21	1		11/19/20 23:27	75-25-2	
Bromomethane	ND	ug/L	5.0	0.46	1		11/19/20 23:27	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	1.4	1		11/19/20 23:27	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.26	1		11/19/20 23:27	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.22	1		11/19/20 23:27	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.34	1		11/19/20 23:27	108-90-7	
Chloroethane	ND	ug/L	2.0	0.72	1		11/19/20 23:27	75-00-3	
Chloroform	ND	ug/L	1.0	0.39	1		11/19/20 23:27	67-66-3	
Chloromethane	ND	ug/L	2.0	0.42	1		11/19/20 23:27	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	0.61	1		11/19/20 23:27	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.26	1		11/19/20 23:27	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.19	1		11/19/20 23:27	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.28	1		11/19/20 23:27	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.33	1		11/19/20 23:27	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.33	1		11/19/20 23:27	106-46-7	
1,1-Dichloroethane	ND	ug/L	1.0	0.34	1		11/19/20 23:27	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.27	1		11/19/20 23:27	107-06-2	
1,1-Dichloroethene	ND	ug/L	1.0	0.26	1		11/19/20 23:27	75-35-4	
cis-1,2-Dichloroethene	ND	ug/L	1.0	0.36	1		11/19/20 23:27	156-59-2	
trans-1,2-Dichloroethene	ND	ug/L	1.0	0.37	1		11/19/20 23:27	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.36	1		11/19/20 23:27	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.31	1		11/19/20 23:27	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.24	1		11/19/20 23:27	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.31	1		11/19/20 23:27	100-41-4	
2-Hexanone	ND	ug/L	20.0	0.88	1		11/19/20 23:27	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.79	1		11/19/20 23:27	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	0.81	1		11/19/20 23:27	108-10-1	
Styrene	ND	ug/L	1.0	0.32	1		11/19/20 23:27	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.14	1		11/19/20 23:27	79-34-5	
Tetrachloroethene	ND	ug/L	1.0	0.24	1		11/19/20 23:27	127-18-4	
Toluene	ND	ug/L	1.0	0.33	1		11/19/20 23:27	108-88-3	
1,1,1-Trichloroethane	ND	ug/L	1.0	0.22	1		11/19/20 23:27	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.25	1		11/19/20 23:27	79-00-5	
Trichloroethene	ND	ug/L	1.0	0.34	1		11/19/20 23:27	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.45	1		11/19/20 23:27	75-01-4	
Xylene (Total)	ND	ug/L	3.0	0.71	1		11/19/20 23:27	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	97	%.	85-116		1		11/19/20 23:27	460-00-4	
Dibromofluoromethane (S)	102	%.	75-120		1		11/19/20 23:27	1868-53-7	
Toluene-d8 (S)	100	%.	83-111		1		11/19/20 23:27	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273460
Project Manager: Melanie Booms

MW101A (50273460022)

A204708-22 (Water)

Date Sampled

11/16/2020 15:34

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011155

1,4-Dioxane	11	0.057	0.50	ug/L	1	11/21/2020	11/21/2020 13:29	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			<i>102 %</i>	<i>68.1-127</i>		<i>11/21/2020</i>	<i>11/21/2020 13:29</i>	<i>EPA 8260B</i>

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273460
Project Manager: Melanie Booms

MW101B (50273460023)

A204708-23 (Water)

Date Sampled

11/16/2020 16:08

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011155

1,4-Dioxane	26	0.057	0.50	ug/L	1	11/20/2020	11/21/2020 13:51	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			<i>102 %</i>	<i>68.1-127</i>		<i>11/20/2020</i>	<i>11/21/2020 13:51</i>	<i>EPA 8260B</i>

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273460
Project Manager: Melanie Booms

MW101C (50273460021)

A204708-21 (Water)

Date Sampled

11/16/2020 14:55

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011155

1,4-Dioxane	19	0.057	0.50	ug/L	1	11/21/2020	11/21/2020 13:09	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>		<i>100 %</i>		<i>68.1-127</i>		<i>11/21/2020</i>	<i>11/21/2020 13:09</i>	<i>EPA 8260B</i>

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273460
Project Manager: Melanie Booms

MW102A (50273460018)

A204708-18 (Water)

Date Sampled
11/16/2020 12:55

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011155

1,4-Dioxane	6.7	0.057	0.50	ug/L	1	11/20/2020	11/21/2020 12:06	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			<i>102 %</i>	<i>68.1-127</i>		<i>11/20/2020</i>	<i>11/21/2020 12:06</i>	<i>EPA 8260B</i>

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273460
Project Manager: Melanie Booms

MW102B (50273460019)

A204708-19 (Water)

Date Sampled

11/16/2020 13:33

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011155

1,4-Dioxane	170	0.057	0.50	ug/L	1	11/20/2020	11/21/2020 12:26	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			<i>105 %</i>	<i>68.1-127</i>		<i>11/20/2020</i>	<i>11/21/2020 12:26</i>	<i>EPA 8260B</i>

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273460
Project Manager: Melanie Booms

MW102C (50273460020)

A204708-20 (Water)

Date Sampled

11/16/2020 14:15

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011155

1,4-Dioxane	31	0.057	0.50	ug/L	1	11/21/2020	11/21/2020 12:48	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			<i>101 %</i>	<i>68.1-127</i>		<i>11/21/2020</i>	<i>11/21/2020 12:48</i>	<i>EPA 8260B</i>

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273460
Project Manager: Melanie Booms

MW117B (50273460008)

A204708-08 (Water)

Date Sampled

11/13/2020 17:07

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011155

1,4-Dioxane	5.5	0.057	0.50	ug/L	1	11/20/2020	11/20/2020 22:19	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			<i>102 %</i>	<i>68.1-127</i>		<i>11/20/2020</i>	<i>11/20/2020 22:19</i>	<i>EPA 8260B</i>

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273460
Project Manager: Melanie Booms

MW117C (50273460007)

A204708-07 (Water)

Date Sampled

11/13/2020 16:39

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011155

1,4-Dioxane	8.3	0.057	0.50	ug/L	1	11/20/2020	11/20/2020 21:58	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			<i>105 %</i>	<i>68.1-127</i>		<i>11/20/2020</i>	<i>11/20/2020 21:58</i>	<i>EPA 8260B</i>

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273460
Project Manager: Melanie Booms

MW117D (50273460006)

A204708-06 (Water)

Date Sampled

11/13/2020 16:13

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011155

1,4-Dioxane	8.4	0.057	0.50	ug/L	1	11/20/2020	11/20/2020 21:37	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			<i>102 %</i>	<i>68.1-127</i>		<i>11/20/2020</i>	<i>11/20/2020 21:37</i>	<i>EPA 8260B</i>

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273460
Project Manager: Melanie Booms

MW119 (50273460011)

A204708-11 (Water)

Date Sampled

11/14/2020 11:10

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011155

1,4-Dioxane	4.0	0.057	0.50	ug/L	1	11/20/2020	11/21/2020 01:49	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			<i>103 %</i>	<i>68.1-127</i>		<i>11/20/2020</i>	<i>11/21/2020 01:49</i>	<i>EPA 8260B</i>

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273460
Project Manager: Melanie Booms

MW121 (50273460017)

A204708-17 (Water)

Date Sampled

11/15/2020 16:17

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011155

1,4-Dioxane	47	0.057	0.50	ug/L	1	11/20/2020	11/21/2020 11:44	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			89.4 %	68.1-127		11/20/2020	11/21/2020 11:44	EPA 8260B

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273460
Project Manager: Melanie Booms

MW136 (50273460012)

A204708-12 (Water)

Date Sampled

11/14/2020 13:43

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011155

1,4-Dioxane	ND	0.057	0.50	ug/L	1	11/20/2020	11/21/2020 02:09	EPA 8260B	U
<i>Surrogate: 1,3-Dioxane</i>									

</

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273460
Project Manager: Melanie Booms

MW201 (50273460015)

A204708-15 (Water)

Date Sampled

11/15/2020 15:32

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011155

1,4-Dioxane	0.89	0.057	0.50	ug/L	1	11/20/2020	11/21/2020 03:12	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			<i>105 %</i>	<i>68.1-127</i>		<i>11/20/2020</i>	<i>11/21/2020 03:12</i>	<i>EPA 8260B</i>

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273460
Project Manager: Melanie Booms

MW202 (50273460014)

A204708-14 (Water)

Date Sampled
11/15/2020 14:36

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011155

1,4-Dioxane	ND	0.057	0.50	ug/L	1	11/20/2020	11/21/2020 02:51	EPA 8260B	U
<i>Surrogate: 1,3-Dioxane</i>									

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273460
Project Manager: Melanie Booms

MW203 (50273460013)

A204708-13 (Water)

Date Sampled
11/15/2020 12:35

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011155

1,4-Dioxane	ND	0.057	0.50	ug/L	1	11/20/2020	11/21/2020 02:30	EPA 8260B	U
-------------	----	-------	------	------	---	------------	------------------	-----------	---

Surrogate: 1,3-Dioxane

108 %

68.1-127

11/20/2020

11/21/2020 02:30

EPA 8260B

U

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273460
Project Manager: Melanie Booms

MW205A (50273460004)

A204708-04 (Water)

Date Sampled

11/13/2020 14:39

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011155

1,4-Dioxane	7.7	0.057	0.50	ug/L	1	11/20/2020	11/20/2020 20:55	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			<i>102 %</i>	<i>68.1-127</i>		<i>11/20/2020</i>	<i>11/20/2020 20:55</i>	<i>EPA 8260B</i>

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273460
Project Manager: Melanie Booms

MW205B (50273460005)

A204708-05 (Water)

Date Sampled

11/13/2020 15:30

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011155

1,4-Dioxane	7.5	0.057	0.50	ug/L	1	11/20/2020	11/20/2020 21:16	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			<i>102 %</i>	<i>68.1-127</i>		<i>11/20/2020</i>	<i>11/20/2020 21:16</i>	<i>EPA 8260B</i>

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273460
Project Manager: Melanie Booms

MW206A (50273460001)

A204708-01 (Water)

Date Sampled
11/13/2020 12:31

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011154

1,4-Dioxane	5.5	0.057	0.50	ug/L	1	11/20/2020	11/20/2020 19:53	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			108 %	68.1-127		11/20/2020	11/20/2020 19:53	EPA 8260B

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273460
Project Manager: Melanie Booms

MW206B (50273460002)

A204708-02 (Water)

Date Sampled

11/13/2020 13:14

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011154

1,4-Dioxane	26	0.057	0.50	ug/L	1	11/20/2020	11/20/2020 20:13	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			<i>103 %</i>	<i>68.1-127</i>		<i>11/20/2020</i>	<i>11/20/2020 20:13</i>	<i>EPA 8260B</i>

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273460
Project Manager: Melanie Booms

MW206C (50273460003)

A204708-03 (Water)

Date Sampled

11/13/2020 13:54

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011154

1,4-Dioxane	52	0.057	0.50	ug/L	1	11/20/2020	11/20/2020 20:34	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			<i>105 %</i>	<i>68.1-127</i>		<i>11/20/2020</i>	<i>11/20/2020 20:34</i>	<i>EPA 8260B</i>

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273460
Project Manager: Melanie Booms

MW207 (50273460010)

A204708-10 (Water)

Date Sampled
11/14/2020 10:35

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011155

1,4-Dioxane	2.8	0.057	0.50	ug/L	1	11/20/2020	11/20/2020 23:01	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			<i>102 %</i>	<i>68.1-127</i>		<i>11/20/2020</i>	<i>11/20/2020 23:01</i>	<i>EPA 8260B</i>

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273460
Project Manager: Melanie Booms

MW47 (50273460009)

A204708-09 (Water)

Date Sampled

11/14/2020 09:36

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011155

1,4-Dioxane	ND	0.057	0.50	ug/L	1	11/20/2020	11/20/2020 22:40	EPA 8260B	U
<i>Surrogate: 1,3-Dioxane</i>									

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273460
Project Manager: Melanie Booms

FD-1 (50273460016)

Date Sampled

A204708-16 (Water)

11/15/2020 15:35

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011155

1,4-Dioxane	0.94	0.057	0.50	ug/L	1	11/20/2020	11/21/2020 03:54	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			<i>108 %</i>	<i>68.1-127</i>		<i>11/20/2020</i>	<i>11/21/2020 03:54</i>	<i>EPA 8260B</i>

Data Quality Control Criteria Review Summary

SDG Number: 50273899**Project Number:** 1016-2**Site:** SE Rockford, Semi-annual (Second 2020)**Contractor Lab:** Pace Analytical Services**Validator:** Maggie Mandell**Sample Date:** 11/17/20 - 11/18/20**Sample Matrix:** Groundwater**Validation Date:** 12/15/20**Analytical Methods:** Volatiles by EPA SW-846 5030B/8260
1,4-Dioxane by SPME and GC\MS (SIM)**Sample Designations:**

MW-101D	MW-130	MW-204	
MW-113A	MW-133A	FD-2	
MW-113B	MW-133B	Trip Blank	
MW-114A	MW-133C		
MW-114B	MW-16		
MW-124	MW-200		

The analytical data were reviewed in accordance with the analytical methods and the Environmental Protection Agency (EPA) Contract Laboratory Program (CLP) National Functional Guidelines. The review included comparing quality control (QC) values provided on the laboratory QC forms to method QC criteria. Review of the raw data was not performed.

Quality Control Summary

QC Review Item	Evaluation [#]
Completeness	X
Case Narrative	X
Chain of Custody (COC) Forms	X
Sample Preservation	X
Holding Times	X
Laboratory Blank Results	X
System Monitoring Compounds (Surrogate) Results	X
Matrix Spike/Matrix Duplicate (MS/MSD) Results	X
Laboratory Control Sample (LCS) Results	X
Method Specific Quality Control (QC) Results *	X
System Performance	X
Field Quality Control Results **	1
Other	NA

See validation summary comment

X Acceptable, no qualification necessary

NR Not required

NA Not applicable

* The reviewer has indicated in the comments, if necessary, the method specific QC results included in the data package that were reviewed.

** Field QC may include field duplicates, trip blanks, rinse blanks, field blanks, and equipment blank samples as required by project specific criteria.

Data for the above samples are:

Action required by Project Manager

- Acceptable for use
 Acceptable for use as qualified
 Unacceptable for use

- Yes
 No

Data Validation Summary Comments:

- 1. Field Quality Control Samples** – One field duplicate was collected during this sampling event. The RPD is not necessarily calculated if both the primary and duplicate results are not five times greater than the reporting limit. The RPD between the investigative and duplicate samples was less than or equal to 6%. The RPD values only consider the comparison of two concentrations reported above the reporting limit. Qualification is not necessary.

Overall Assessment of Data:

The Pace Work Order Report #50273899 is 100% complete. The data usability is based on EPA's guidance documents. No problems were identified with reported data and analytical performance was within specified limits. The data are acceptable and meet the project's data quality objectives.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site

Pace Project No.: 50273899

Sample: MW101D	Lab ID: 50273899006	Collected: 11/18/20 07:58	Received: 11/20/20 09:30	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	1.7	1		11/24/20 04:49	67-64-1	
Benzene	ND	ug/L	1.0	0.51	1		11/24/20 04:49	71-43-2	
Bromochloromethane	ND	ug/L	1.0	0.53	1		11/24/20 04:49	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.62	1		11/24/20 04:49	75-27-4	
Bromoform	ND	ug/L	1.0	0.75	1		11/24/20 04:49	75-25-2	
Bromomethane	ND	ug/L	5.0	1.2	1		11/24/20 04:49	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	2.0	1		11/24/20 04:49	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.56	1		11/24/20 04:49	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.50	1		11/24/20 04:49	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.54	1		11/24/20 04:49	108-90-7	
Chloroethane	ND	ug/L	2.0	0.65	1		11/24/20 04:49	75-00-3	
Chloroform	ND	ug/L	1.0	0.64	1		11/24/20 04:49	67-66-3	
Chloromethane	ND	ug/L	2.0	1.0	1		11/24/20 04:49	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	0.82	1		11/24/20 04:49	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.53	1		11/24/20 04:49	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.49	1		11/24/20 04:49	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.48	1		11/24/20 04:49	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.48	1		11/24/20 04:49	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.54	1		11/24/20 04:49	106-46-7	
1,1-Dichloroethane	ND	ug/L	1.0	0.51	1		11/24/20 04:49	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.51	1		11/24/20 04:49	107-06-2	
1,1-Dichloroethene	ND	ug/L	1.0	0.55	1		11/24/20 04:49	75-35-4	
cis-1,2-Dichloroethene	ND	ug/L	1.0	0.50	1		11/24/20 04:49	156-59-2	
trans-1,2-Dichloroethene	ND	ug/L	1.0	0.49	1		11/24/20 04:49	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.65	1		11/24/20 04:49	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.56	1		11/24/20 04:49	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.57	1		11/24/20 04:49	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.54	1		11/24/20 04:49	100-41-4	
2-Hexanone	ND	ug/L	20.0	2.6	1		11/24/20 04:49	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.97	1		11/24/20 04:49	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	1.7	1		11/24/20 04:49	108-10-1	
Styrene	ND	ug/L	1.0	0.58	1		11/24/20 04:49	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.49	1		11/24/20 04:49	79-34-5	
Tetrachloroethene	ND	ug/L	1.0	0.61	1		11/24/20 04:49	127-18-4	
Toluene	ND	ug/L	1.0	0.51	1		11/24/20 04:49	108-88-3	
1,1,1-Trichloroethane	ND	ug/L	1.0	0.63	1		11/24/20 04:49	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.44	1		11/24/20 04:49	79-00-5	
Trichloroethene	ND	ug/L	1.0	0.63	1		11/24/20 04:49	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.72	1		11/24/20 04:49	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.1	1		11/24/20 04:49	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	90	%.	85-116		1		11/24/20 04:49	460-00-4	
Dibromofluoromethane (S)	105	%.	75-120		1		11/24/20 04:49	1868-53-7	
Toluene-d8 (S)	102	%.	83-111		1		11/24/20 04:49	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site

Pace Project No.: 50273899

Sample: MW113A	Lab ID: 50273899002	Collected: 11/17/20 10:07	Received: 11/20/20 09:30	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	1.7	1		11/24/20 02:39	67-64-1	
Benzene	ND	ug/L	1.0	0.51	1		11/24/20 02:39	71-43-2	
Bromochloromethane	ND	ug/L	1.0	0.53	1		11/24/20 02:39	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.62	1		11/24/20 02:39	75-27-4	
Bromoform	ND	ug/L	1.0	0.75	1		11/24/20 02:39	75-25-2	
Bromomethane	ND	ug/L	5.0	1.2	1		11/24/20 02:39	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	2.0	1		11/24/20 02:39	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.56	1		11/24/20 02:39	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.50	1		11/24/20 02:39	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.54	1		11/24/20 02:39	108-90-7	
Chloroethane	ND	ug/L	2.0	0.65	1		11/24/20 02:39	75-00-3	
Chloroform	ND	ug/L	1.0	0.64	1		11/24/20 02:39	67-66-3	
Chloromethane	ND	ug/L	2.0	1.0	1		11/24/20 02:39	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	0.82	1		11/24/20 02:39	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.53	1		11/24/20 02:39	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.49	1		11/24/20 02:39	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.48	1		11/24/20 02:39	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.48	1		11/24/20 02:39	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.54	1		11/24/20 02:39	106-46-7	
1,1-Dichloroethane	75.1	ug/L	1.0	0.51	1		11/24/20 02:39	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.51	1		11/24/20 02:39	107-06-2	
1,1-Dichloroethene	12.7	ug/L	1.0	0.55	1		11/24/20 02:39	75-35-4	
cis-1,2-Dichloroethene	7.6	ug/L	1.0	0.50	1		11/24/20 02:39	156-59-2	
trans-1,2-Dichloroethene	2.0	ug/L	1.0	0.49	1		11/24/20 02:39	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.65	1		11/24/20 02:39	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.56	1		11/24/20 02:39	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.57	1		11/24/20 02:39	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.54	1		11/24/20 02:39	100-41-4	
2-Hexanone	ND	ug/L	20.0	2.6	1		11/24/20 02:39	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.97	1		11/24/20 02:39	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	1.7	1		11/24/20 02:39	108-10-1	
Styrene	ND	ug/L	1.0	0.58	1		11/24/20 02:39	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.49	1		11/24/20 02:39	79-34-5	
Tetrachloroethene	15.8	ug/L	1.0	0.61	1		11/24/20 02:39	127-18-4	
Toluene	ND	ug/L	1.0	0.51	1		11/24/20 02:39	108-88-3	
1,1,1-Trichloroethane	72.4	ug/L	1.0	0.63	1		11/24/20 02:39	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.44	1		11/24/20 02:39	79-00-5	
Trichloroethene	23.7	ug/L	1.0	0.63	1		11/24/20 02:39	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.72	1		11/24/20 02:39	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.1	1		11/24/20 02:39	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	91	%.	85-116		1		11/24/20 02:39	460-00-4	
Dibromofluoromethane (S)	105	%.	75-120		1		11/24/20 02:39	1868-53-7	
Toluene-d8 (S)	101	%.	83-111		1		11/24/20 02:39	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site
Pace Project No.: 50273899

Sample: MW113B	Lab ID: 50273899003	Collected: 11/17/20 10:48	Received: 11/20/20 09:30	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	1.7	1		11/24/20 03:12	67-64-1	
Benzene	ND	ug/L	1.0	0.51	1		11/24/20 03:12	71-43-2	
Bromochloromethane	ND	ug/L	1.0	0.53	1		11/24/20 03:12	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.62	1		11/24/20 03:12	75-27-4	
Bromoform	ND	ug/L	1.0	0.75	1		11/24/20 03:12	75-25-2	
Bromomethane	ND	ug/L	5.0	1.2	1		11/24/20 03:12	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	2.0	1		11/24/20 03:12	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.56	1		11/24/20 03:12	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.50	1		11/24/20 03:12	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.54	1		11/24/20 03:12	108-90-7	
Chloroethane	ND	ug/L	2.0	0.65	1		11/24/20 03:12	75-00-3	
Chloroform	ND	ug/L	1.0	0.64	1		11/24/20 03:12	67-66-3	
Chloromethane	ND	ug/L	2.0	1.0	1		11/24/20 03:12	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	0.82	1		11/24/20 03:12	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.53	1		11/24/20 03:12	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.49	1		11/24/20 03:12	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.48	1		11/24/20 03:12	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.48	1		11/24/20 03:12	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.54	1		11/24/20 03:12	106-46-7	
1,1-Dichloroethane	57.3	ug/L	1.0	0.51	1		11/24/20 03:12	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.51	1		11/24/20 03:12	107-06-2	
1,1-Dichloroethene	11.5	ug/L	1.0	0.55	1		11/24/20 03:12	75-35-4	
cis-1,2-Dichloroethene	27.0	ug/L	1.0	0.50	1		11/24/20 03:12	156-59-2	
trans-1,2-Dichloroethene	1.4	ug/L	1.0	0.49	1		11/24/20 03:12	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.65	1		11/24/20 03:12	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.56	1		11/24/20 03:12	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.57	1		11/24/20 03:12	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.54	1		11/24/20 03:12	100-41-4	
2-Hexanone	ND	ug/L	20.0	2.6	1		11/24/20 03:12	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.97	1		11/24/20 03:12	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	1.7	1		11/24/20 03:12	108-10-1	
Styrene	ND	ug/L	1.0	0.58	1		11/24/20 03:12	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.49	1		11/24/20 03:12	79-34-5	
Tetrachloroethene	4.2	ug/L	1.0	0.61	1		11/24/20 03:12	127-18-4	
Toluene	ND	ug/L	1.0	0.51	1		11/24/20 03:12	108-88-3	
1,1,1-Trichloroethane	10.3	ug/L	1.0	0.63	1		11/24/20 03:12	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.44	1		11/24/20 03:12	79-00-5	
Trichloroethene	16.9	ug/L	1.0	0.63	1		11/24/20 03:12	79-01-6	
Vinyl chloride	2.6	ug/L	1.0	0.72	1		11/24/20 03:12	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.1	1		11/24/20 03:12	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	91	%.	85-116		1		11/24/20 03:12	460-00-4	
Dibromofluoromethane (S)	104	%.	75-120		1		11/24/20 03:12	1868-53-7	
Toluene-d8 (S)	103	%.	83-111		1		11/24/20 03:12	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site

Pace Project No.: 50273899

Sample: MW114A	Lab ID: 50273899011	Collected: 11/18/20 13:55	Received: 11/20/20 09:30	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	1.7	1		11/24/20 08:06	67-64-1	
Benzene	ND	ug/L	1.0	0.51	1		11/24/20 08:06	71-43-2	
Bromochloromethane	ND	ug/L	1.0	0.53	1		11/24/20 08:06	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.62	1		11/24/20 08:06	75-27-4	
Bromoform	ND	ug/L	1.0	0.75	1		11/24/20 08:06	75-25-2	
Bromomethane	ND	ug/L	5.0	1.2	1		11/24/20 08:06	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	2.0	1		11/24/20 08:06	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.56	1		11/24/20 08:06	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.50	1		11/24/20 08:06	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.54	1		11/24/20 08:06	108-90-7	
Chloroethane	ND	ug/L	2.0	0.65	1		11/24/20 08:06	75-00-3	
Chloroform	ND	ug/L	1.0	0.64	1		11/24/20 08:06	67-66-3	
Chloromethane	ND	ug/L	2.0	1.0	1		11/24/20 08:06	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	0.82	1		11/24/20 08:06	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.53	1		11/24/20 08:06	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.49	1		11/24/20 08:06	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.48	1		11/24/20 08:06	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.48	1		11/24/20 08:06	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.54	1		11/24/20 08:06	106-46-7	
1,1-Dichloroethane	3.1	ug/L	1.0	0.51	1		11/24/20 08:06	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.51	1		11/24/20 08:06	107-06-2	
1,1-Dichloroethene	1.5	ug/L	1.0	0.55	1		11/24/20 08:06	75-35-4	
cis-1,2-Dichloroethene	1.4	ug/L	1.0	0.50	1		11/24/20 08:06	156-59-2	
trans-1,2-Dichloroethene	ND	ug/L	1.0	0.49	1		11/24/20 08:06	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.65	1		11/24/20 08:06	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.56	1		11/24/20 08:06	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.57	1		11/24/20 08:06	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.54	1		11/24/20 08:06	100-41-4	
2-Hexanone	ND	ug/L	20.0	2.6	1		11/24/20 08:06	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.97	1		11/24/20 08:06	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	1.7	1		11/24/20 08:06	108-10-1	
Styrene	ND	ug/L	1.0	0.58	1		11/24/20 08:06	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.49	1		11/24/20 08:06	79-34-5	
Tetrachloroethene	ND	ug/L	1.0	0.61	1		11/24/20 08:06	127-18-4	
Toluene	ND	ug/L	1.0	0.51	1		11/24/20 08:06	108-88-3	
1,1,1-Trichloroethane	9.6	ug/L	1.0	0.63	1		11/24/20 08:06	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.44	1		11/24/20 08:06	79-00-5	
Trichloroethene	ND	ug/L	1.0	0.63	1		11/24/20 08:06	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.72	1		11/24/20 08:06	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.1	1		11/24/20 08:06	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	91	%.	85-116		1		11/24/20 08:06	460-00-4	
Dibromofluoromethane (S)	104	%.	75-120		1		11/24/20 08:06	1868-53-7	
Toluene-d8 (S)	102	%.	83-111		1		11/24/20 08:06	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site
Pace Project No.: 50273899

Sample: MW114B	Lab ID: 50273899012	Collected: 11/18/20 14:36	Received: 11/20/20 09:30	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	1.7	1		11/24/20 08:38	67-64-1	
Benzene	ND	ug/L	1.0	0.51	1		11/24/20 08:38	71-43-2	
Bromochloromethane	ND	ug/L	1.0	0.53	1		11/24/20 08:38	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.62	1		11/24/20 08:38	75-27-4	
Bromoform	ND	ug/L	1.0	0.75	1		11/24/20 08:38	75-25-2	
Bromomethane	ND	ug/L	5.0	1.2	1		11/24/20 08:38	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	2.0	1		11/24/20 08:38	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.56	1		11/24/20 08:38	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.50	1		11/24/20 08:38	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.54	1		11/24/20 08:38	108-90-7	
Chloroethane	ND	ug/L	2.0	0.65	1		11/24/20 08:38	75-00-3	
Chloroform	ND	ug/L	1.0	0.64	1		11/24/20 08:38	67-66-3	
Chloromethane	ND	ug/L	2.0	1.0	1		11/24/20 08:38	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	0.82	1		11/24/20 08:38	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.53	1		11/24/20 08:38	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.49	1		11/24/20 08:38	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.48	1		11/24/20 08:38	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.48	1		11/24/20 08:38	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.54	1		11/24/20 08:38	106-46-7	
1,1-Dichloroethane	1.7	ug/L	1.0	0.51	1		11/24/20 08:38	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.51	1		11/24/20 08:38	107-06-2	
1,1-Dichloroethene	ND	ug/L	1.0	0.55	1		11/24/20 08:38	75-35-4	
cis-1,2-Dichloroethene	ND	ug/L	1.0	0.50	1		11/24/20 08:38	156-59-2	
trans-1,2-Dichloroethene	ND	ug/L	1.0	0.49	1		11/24/20 08:38	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.65	1		11/24/20 08:38	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.56	1		11/24/20 08:38	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.57	1		11/24/20 08:38	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.54	1		11/24/20 08:38	100-41-4	
2-Hexanone	ND	ug/L	20.0	2.6	1		11/24/20 08:38	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.97	1		11/24/20 08:38	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	1.7	1		11/24/20 08:38	108-10-1	
Styrene	ND	ug/L	1.0	0.58	1		11/24/20 08:38	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.49	1		11/24/20 08:38	79-34-5	
Tetrachloroethene	ND	ug/L	1.0	0.61	1		11/24/20 08:38	127-18-4	
Toluene	ND	ug/L	1.0	0.51	1		11/24/20 08:38	108-88-3	
1,1,1-Trichloroethane	ND	ug/L	1.0	0.63	1		11/24/20 08:38	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.44	1		11/24/20 08:38	79-00-5	
Trichloroethene	2.2	ug/L	1.0	0.63	1		11/24/20 08:38	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.72	1		11/24/20 08:38	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.1	1		11/24/20 08:38	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	91	%.	85-116		1		11/24/20 08:38	460-00-4	
Dibromofluoromethane (S)	105	%.	75-120		1		11/24/20 08:38	1868-53-7	
Toluene-d8 (S)	103	%.	83-111		1		11/24/20 08:38	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site
Pace Project No.: 50273899

Sample: MW124	Lab ID: 50273899010	Collected: 11/18/20 13:10	Received: 11/20/20 09:30	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	1.7	1		11/24/20 07:33	67-64-1	
Benzene	ND	ug/L	1.0	0.51	1		11/24/20 07:33	71-43-2	
Bromochloromethane	ND	ug/L	1.0	0.53	1		11/24/20 07:33	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.62	1		11/24/20 07:33	75-27-4	
Bromoform	ND	ug/L	1.0	0.75	1		11/24/20 07:33	75-25-2	
Bromomethane	ND	ug/L	5.0	1.2	1		11/24/20 07:33	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	2.0	1		11/24/20 07:33	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.56	1		11/24/20 07:33	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.50	1		11/24/20 07:33	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.54	1		11/24/20 07:33	108-90-7	
Chloroethane	ND	ug/L	2.0	0.65	1		11/24/20 07:33	75-00-3	
Chloroform	ND	ug/L	1.0	0.64	1		11/24/20 07:33	67-66-3	
Chloromethane	ND	ug/L	2.0	1.0	1		11/24/20 07:33	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	0.82	1		11/24/20 07:33	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.53	1		11/24/20 07:33	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.49	1		11/24/20 07:33	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.48	1		11/24/20 07:33	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.48	1		11/24/20 07:33	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.54	1		11/24/20 07:33	106-46-7	
1,1-Dichloroethane	26.0	ug/L	1.0	0.51	1		11/24/20 07:33	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.51	1		11/24/20 07:33	107-06-2	
1,1-Dichloroethene	4.8	ug/L	1.0	0.55	1		11/24/20 07:33	75-35-4	
cis-1,2-Dichloroethene	14.5	ug/L	1.0	0.50	1		11/24/20 07:33	156-59-2	
trans-1,2-Dichloroethene	0.51J	ug/L	1.0	0.49	1		11/24/20 07:33	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.65	1		11/24/20 07:33	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.56	1		11/24/20 07:33	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.57	1		11/24/20 07:33	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.54	1		11/24/20 07:33	100-41-4	
2-Hexanone	ND	ug/L	20.0	2.6	1		11/24/20 07:33	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.97	1		11/24/20 07:33	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	1.7	1		11/24/20 07:33	108-10-1	
Styrene	ND	ug/L	1.0	0.58	1		11/24/20 07:33	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.49	1		11/24/20 07:33	79-34-5	
Tetrachloroethene	9.0	ug/L	1.0	0.61	1		11/24/20 07:33	127-18-4	
Toluene	ND	ug/L	1.0	0.51	1		11/24/20 07:33	108-88-3	
1,1,1-Trichloroethane	22.1	ug/L	1.0	0.63	1		11/24/20 07:33	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.44	1		11/24/20 07:33	79-00-5	
Trichloroethene	2.8	ug/L	1.0	0.63	1		11/24/20 07:33	79-01-6	
Vinyl chloride	2.0	ug/L	1.0	0.72	1		11/24/20 07:33	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.1	1		11/24/20 07:33	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	92	%.	85-116		1		11/24/20 07:33	460-00-4	
Dibromofluoromethane (S)	106	%.	75-120		1		11/24/20 07:33	1868-53-7	
Toluene-d8 (S)	102	%.	83-111		1		11/24/20 07:33	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site
Pace Project No.: 50273899

Sample: MW130	Lab ID: 50273899005	Collected: 11/17/20 16:36	Received: 11/20/20 09:30	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	1.7	1		11/24/20 04:17	67-64-1	
Benzene	ND	ug/L	1.0	0.51	1		11/24/20 04:17	71-43-2	
Bromochloromethane	ND	ug/L	1.0	0.53	1		11/24/20 04:17	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.62	1		11/24/20 04:17	75-27-4	
Bromoform	ND	ug/L	1.0	0.75	1		11/24/20 04:17	75-25-2	
Bromomethane	ND	ug/L	5.0	1.2	1		11/24/20 04:17	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	2.0	1		11/24/20 04:17	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.56	1		11/24/20 04:17	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.50	1		11/24/20 04:17	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.54	1		11/24/20 04:17	108-90-7	
Chloroethane	ND	ug/L	2.0	0.65	1		11/24/20 04:17	75-00-3	
Chloroform	ND	ug/L	1.0	0.64	1		11/24/20 04:17	67-66-3	
Chloromethane	ND	ug/L	2.0	1.0	1		11/24/20 04:17	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	0.82	1		11/24/20 04:17	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.53	1		11/24/20 04:17	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.49	1		11/24/20 04:17	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.48	1		11/24/20 04:17	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.48	1		11/24/20 04:17	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.54	1		11/24/20 04:17	106-46-7	
1,1-Dichloroethane	3.5	ug/L	1.0	0.51	1		11/24/20 04:17	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.51	1		11/24/20 04:17	107-06-2	
1,1-Dichloroethene	ND	ug/L	1.0	0.55	1		11/24/20 04:17	75-35-4	
cis-1,2-Dichloroethene	0.62J	ug/L	1.0	0.50	1		11/24/20 04:17	156-59-2	
trans-1,2-Dichloroethene	ND	ug/L	1.0	0.49	1		11/24/20 04:17	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.65	1		11/24/20 04:17	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.56	1		11/24/20 04:17	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.57	1		11/24/20 04:17	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.54	1		11/24/20 04:17	100-41-4	
2-Hexanone	ND	ug/L	20.0	2.6	1		11/24/20 04:17	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.97	1		11/24/20 04:17	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	1.7	1		11/24/20 04:17	108-10-1	
Styrene	ND	ug/L	1.0	0.58	1		11/24/20 04:17	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.49	1		11/24/20 04:17	79-34-5	
Tetrachloroethene	0.94J	ug/L	1.0	0.61	1		11/24/20 04:17	127-18-4	
Toluene	ND	ug/L	1.0	0.51	1		11/24/20 04:17	108-88-3	
1,1,1-Trichloroethane	2.9	ug/L	1.0	0.63	1		11/24/20 04:17	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.44	1		11/24/20 04:17	79-00-5	
Trichloroethene	ND	ug/L	1.0	0.63	1		11/24/20 04:17	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.72	1		11/24/20 04:17	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.1	1		11/24/20 04:17	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	92	%.	85-116		1		11/24/20 04:17	460-00-4	
Dibromofluoromethane (S)	107	%.	75-120		1		11/24/20 04:17	1868-53-7	
Toluene-d8 (S)	102	%.	83-111		1		11/24/20 04:17	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site

Pace Project No.: 50273899

Sample: MW133A	Lab ID: 50273899007	Collected: 11/18/20 11:12	Received: 11/20/20 09:30	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	1.7	1		11/24/20 05:55	67-64-1	
Benzene	ND	ug/L	1.0	0.51	1		11/24/20 05:55	71-43-2	
Bromochloromethane	ND	ug/L	1.0	0.53	1		11/24/20 05:55	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.62	1		11/24/20 05:55	75-27-4	
Bromoform	ND	ug/L	1.0	0.75	1		11/24/20 05:55	75-25-2	
Bromomethane	ND	ug/L	5.0	1.2	1		11/24/20 05:55	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	2.0	1		11/24/20 05:55	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.56	1		11/24/20 05:55	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.50	1		11/24/20 05:55	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.54	1		11/24/20 05:55	108-90-7	
Chloroethane	ND	ug/L	2.0	0.65	1		11/24/20 05:55	75-00-3	
Chloroform	ND	ug/L	1.0	0.64	1		11/24/20 05:55	67-66-3	
Chloromethane	ND	ug/L	2.0	1.0	1		11/24/20 05:55	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	0.82	1		11/24/20 05:55	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.53	1		11/24/20 05:55	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.49	1		11/24/20 05:55	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.48	1		11/24/20 05:55	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.48	1		11/24/20 05:55	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.54	1		11/24/20 05:55	106-46-7	
1,1-Dichloroethane	1.9	ug/L	1.0	0.51	1		11/24/20 05:55	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.51	1		11/24/20 05:55	107-06-2	
1,1-Dichloroethene	ND	ug/L	1.0	0.55	1		11/24/20 05:55	75-35-4	
cis-1,2-Dichloroethene	ND	ug/L	1.0	0.50	1		11/24/20 05:55	156-59-2	
trans-1,2-Dichloroethene	ND	ug/L	1.0	0.49	1		11/24/20 05:55	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.65	1		11/24/20 05:55	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.56	1		11/24/20 05:55	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.57	1		11/24/20 05:55	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.54	1		11/24/20 05:55	100-41-4	
2-Hexanone	ND	ug/L	20.0	2.6	1		11/24/20 05:55	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.97	1		11/24/20 05:55	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	1.7	1		11/24/20 05:55	108-10-1	
Styrene	ND	ug/L	1.0	0.58	1		11/24/20 05:55	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.49	1		11/24/20 05:55	79-34-5	
Tetrachloroethene	ND	ug/L	1.0	0.61	1		11/24/20 05:55	127-18-4	
Toluene	ND	ug/L	1.0	0.51	1		11/24/20 05:55	108-88-3	
1,1,1-Trichloroethane	3.9	ug/L	1.0	0.63	1		11/24/20 05:55	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.44	1		11/24/20 05:55	79-00-5	
Trichloroethene	ND	ug/L	1.0	0.63	1		11/24/20 05:55	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.72	1		11/24/20 05:55	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.1	1		11/24/20 05:55	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	91	%.	85-116		1		11/24/20 05:55	460-00-4	
Dibromofluoromethane (S)	102	%.	75-120		1		11/24/20 05:55	1868-53-7	
Toluene-d8 (S)	102	%.	83-111		1		11/24/20 05:55	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site

Pace Project No.: 50273899

Sample: MW133B	Lab ID: 50273899008	Collected: 11/18/20 11:53	Received: 11/20/20 09:30	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	1.7	1		11/24/20 06:28	67-64-1	
Benzene	ND	ug/L	1.0	0.51	1		11/24/20 06:28	71-43-2	
Bromochloromethane	ND	ug/L	1.0	0.53	1		11/24/20 06:28	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.62	1		11/24/20 06:28	75-27-4	
Bromoform	ND	ug/L	1.0	0.75	1		11/24/20 06:28	75-25-2	
Bromomethane	ND	ug/L	5.0	1.2	1		11/24/20 06:28	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	2.0	1		11/24/20 06:28	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.56	1		11/24/20 06:28	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.50	1		11/24/20 06:28	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.54	1		11/24/20 06:28	108-90-7	
Chloroethane	ND	ug/L	2.0	0.65	1		11/24/20 06:28	75-00-3	
Chloroform	1.4	ug/L	1.0	0.64	1		11/24/20 06:28	67-66-3	
Chloromethane	ND	ug/L	2.0	1.0	1		11/24/20 06:28	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	0.82	1		11/24/20 06:28	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.53	1		11/24/20 06:28	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.49	1		11/24/20 06:28	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.48	1		11/24/20 06:28	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.48	1		11/24/20 06:28	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.54	1		11/24/20 06:28	106-46-7	
1,1-Dichloroethane	71.3	ug/L	1.0	0.51	1		11/24/20 06:28	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.51	1		11/24/20 06:28	107-06-2	
1,1-Dichloroethene	35.8	ug/L	1.0	0.55	1		11/24/20 06:28	75-35-4	
cis-1,2-Dichloroethene	23.2	ug/L	1.0	0.50	1		11/24/20 06:28	156-59-2	
trans-1,2-Dichloroethene	2.8	ug/L	1.0	0.49	1		11/24/20 06:28	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.65	1		11/24/20 06:28	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.56	1		11/24/20 06:28	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.57	1		11/24/20 06:28	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.54	1		11/24/20 06:28	100-41-4	
2-Hexanone	ND	ug/L	20.0	2.6	1		11/24/20 06:28	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.97	1		11/24/20 06:28	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	1.7	1		11/24/20 06:28	108-10-1	
Styrene	ND	ug/L	1.0	0.58	1		11/24/20 06:28	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.49	1		11/24/20 06:28	79-34-5	
Tetrachloroethene	42.7	ug/L	1.0	0.61	1		11/24/20 06:28	127-18-4	
Toluene	ND	ug/L	1.0	0.51	1		11/24/20 06:28	108-88-3	
1,1,1-Trichloroethane	203	ug/L	1.0	0.63	1		11/24/20 06:28	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.44	1		11/24/20 06:28	79-00-5	
Trichloroethene	19.6	ug/L	1.0	0.63	1		11/24/20 06:28	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.72	1		11/24/20 06:28	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.1	1		11/24/20 06:28	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	90	%.	85-116		1		11/24/20 06:28	460-00-4	
Dibromofluoromethane (S)	107	%.	75-120		1		11/24/20 06:28	1868-53-7	
Toluene-d8 (S)	102	%.	83-111		1		11/24/20 06:28	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site

Pace Project No.: 50273899

Sample: MW133C	Lab ID: 50273899009	Collected: 11/18/20 12:29	Received: 11/20/20 09:30	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	1.7	1		11/24/20 07:00	67-64-1	
Benzene	ND	ug/L	1.0	0.51	1		11/24/20 07:00	71-43-2	
Bromochloromethane	ND	ug/L	1.0	0.53	1		11/24/20 07:00	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.62	1		11/24/20 07:00	75-27-4	
Bromoform	ND	ug/L	1.0	0.75	1		11/24/20 07:00	75-25-2	
Bromomethane	ND	ug/L	5.0	1.2	1		11/24/20 07:00	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	2.0	1		11/24/20 07:00	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.56	1		11/24/20 07:00	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.50	1		11/24/20 07:00	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.54	1		11/24/20 07:00	108-90-7	
Chloroethane	ND	ug/L	2.0	0.65	1		11/24/20 07:00	75-00-3	
Chloroform	2.2	ug/L	1.0	0.64	1		11/24/20 07:00	67-66-3	
Chloromethane	ND	ug/L	2.0	1.0	1		11/24/20 07:00	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	0.82	1		11/24/20 07:00	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.53	1		11/24/20 07:00	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.49	1		11/24/20 07:00	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.48	1		11/24/20 07:00	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.48	1		11/24/20 07:00	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.54	1		11/24/20 07:00	106-46-7	
1,1-Dichloroethane	33.0	ug/L	1.0	0.51	1		11/24/20 07:00	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.51	1		11/24/20 07:00	107-06-2	
1,1-Dichloroethene	26.5	ug/L	1.0	0.55	1		11/24/20 07:00	75-35-4	
cis-1,2-Dichloroethene	31.6	ug/L	1.0	0.50	1		11/24/20 07:00	156-59-2	
trans-1,2-Dichloroethene	1.2	ug/L	1.0	0.49	1		11/24/20 07:00	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.65	1		11/24/20 07:00	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.56	1		11/24/20 07:00	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.57	1		11/24/20 07:00	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.54	1		11/24/20 07:00	100-41-4	
2-Hexanone	ND	ug/L	20.0	2.6	1		11/24/20 07:00	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.97	1		11/24/20 07:00	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	1.7	1		11/24/20 07:00	108-10-1	
Styrene	ND	ug/L	1.0	0.58	1		11/24/20 07:00	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.49	1		11/24/20 07:00	79-34-5	
Tetrachloroethene	17.5	ug/L	1.0	0.61	1		11/24/20 07:00	127-18-4	
Toluene	ND	ug/L	1.0	0.51	1		11/24/20 07:00	108-88-3	
1,1,1-Trichloroethane	69.0	ug/L	1.0	0.63	1		11/24/20 07:00	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.44	1		11/24/20 07:00	79-00-5	
Trichloroethene	42.4	ug/L	1.0	0.63	1		11/24/20 07:00	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.72	1		11/24/20 07:00	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.1	1		11/24/20 07:00	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	91	%.	85-116		1		11/24/20 07:00	460-00-4	
Dibromofluoromethane (S)	107	%.	75-120		1		11/24/20 07:00	1868-53-7	
Toluene-d8 (S)	101	%.	83-111		1		11/24/20 07:00	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site
Pace Project No.: 50273899

Sample: MW200	Lab ID: 50273899004	Collected: 11/17/20 11:28	Received: 11/20/20 09:30	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	1.7	1		11/24/20 03:44	67-64-1	
Benzene	ND	ug/L	1.0	0.51	1		11/24/20 03:44	71-43-2	
Bromochloromethane	ND	ug/L	1.0	0.53	1		11/24/20 03:44	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.62	1		11/24/20 03:44	75-27-4	
Bromoform	ND	ug/L	1.0	0.75	1		11/24/20 03:44	75-25-2	
Bromomethane	ND	ug/L	5.0	1.2	1		11/24/20 03:44	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	2.0	1		11/24/20 03:44	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.56	1		11/24/20 03:44	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.50	1		11/24/20 03:44	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.54	1		11/24/20 03:44	108-90-7	
Chloroethane	ND	ug/L	2.0	0.65	1		11/24/20 03:44	75-00-3	
Chloroform	ND	ug/L	1.0	0.64	1		11/24/20 03:44	67-66-3	
Chloromethane	ND	ug/L	2.0	1.0	1		11/24/20 03:44	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	0.82	1		11/24/20 03:44	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.53	1		11/24/20 03:44	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.49	1		11/24/20 03:44	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.48	1		11/24/20 03:44	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.48	1		11/24/20 03:44	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.54	1		11/24/20 03:44	106-46-7	
1,1-Dichloroethane	ND	ug/L	1.0	0.51	1		11/24/20 03:44	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.51	1		11/24/20 03:44	107-06-2	
1,1-Dichloroethene	ND	ug/L	1.0	0.55	1		11/24/20 03:44	75-35-4	
cis-1,2-Dichloroethene	ND	ug/L	1.0	0.50	1		11/24/20 03:44	156-59-2	
trans-1,2-Dichloroethene	ND	ug/L	1.0	0.49	1		11/24/20 03:44	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.65	1		11/24/20 03:44	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.56	1		11/24/20 03:44	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.57	1		11/24/20 03:44	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.54	1		11/24/20 03:44	100-41-4	
2-Hexanone	ND	ug/L	20.0	2.6	1		11/24/20 03:44	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.97	1		11/24/20 03:44	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	1.7	1		11/24/20 03:44	108-10-1	
Styrene	ND	ug/L	1.0	0.58	1		11/24/20 03:44	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.49	1		11/24/20 03:44	79-34-5	
Tetrachloroethene	ND	ug/L	1.0	0.61	1		11/24/20 03:44	127-18-4	
Toluene	ND	ug/L	1.0	0.51	1		11/24/20 03:44	108-88-3	
1,1,1-Trichloroethane	ND	ug/L	1.0	0.63	1		11/24/20 03:44	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.44	1		11/24/20 03:44	79-00-5	
Trichloroethene	ND	ug/L	1.0	0.63	1		11/24/20 03:44	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.72	1		11/24/20 03:44	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.1	1		11/24/20 03:44	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	91	%.	85-116		1		11/24/20 03:44	460-00-4	
Dibromofluoromethane (S)	107	%.	75-120		1		11/24/20 03:44	1868-53-7	
Toluene-d8 (S)	102	%.	83-111		1		11/24/20 03:44	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site

Pace Project No.: 50273899

Sample: MW16	Lab ID: 50273899014	Collected: 11/18/20 15:11	Received: 11/20/20 09:30	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	5.0	1		11/24/20 08:22	67-64-1	
Benzene	ND	ug/L	1.0	0.68	1		11/24/20 08:22	71-43-2	
Bromochloromethane	ND	ug/L	1.0	0.60	1		11/24/20 08:22	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.49	1		11/24/20 08:22	75-27-4	
Bromoform	ND	ug/L	1.0	0.68	1		11/24/20 08:22	75-25-2	
Bromomethane	ND	ug/L	5.0	5.0	1		11/24/20 08:22	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	2.0	1		11/24/20 08:22	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.51	1		11/24/20 08:22	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.63	1		11/24/20 08:22	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.61	1		11/24/20 08:22	108-90-7	
Chloroethane	ND	ug/L	2.0	0.66	1		11/24/20 08:22	75-00-3	
Chloroform	ND	ug/L	1.0	0.66	1		11/24/20 08:22	67-66-3	
Chloromethane	ND	ug/L	2.0	0.61	1		11/24/20 08:22	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	2.2	1		11/24/20 08:22	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.54	1		11/24/20 08:22	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.51	1		11/24/20 08:22	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.60	1		11/24/20 08:22	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.52	1		11/24/20 08:22	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.58	1		11/24/20 08:22	106-46-7	
1,1-Dichloroethane	55.7	ug/L	1.0	0.66	1		11/24/20 08:22	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.67	1		11/24/20 08:22	107-06-2	
1,1-Dichloroethene	13.6	ug/L	1.0	0.59	1		11/24/20 08:22	75-35-4	
cis-1,2-Dichloroethene	5.3	ug/L	1.0	0.69	1		11/24/20 08:22	156-59-2	
trans-1,2-Dichloroethene	1.7	ug/L	1.0	0.62	1		11/24/20 08:22	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.71	1		11/24/20 08:22	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.55	1		11/24/20 08:22	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.15	1		11/24/20 08:22	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.56	1		11/24/20 08:22	100-41-4	
2-Hexanone	ND	ug/L	20.0	2.4	1		11/24/20 08:22	591-78-6	
Methylene Chloride	ND	ug/L	5.0	1.0	1		11/24/20 08:22	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	4.3	1		11/24/20 08:22	108-10-1	
Styrene	ND	ug/L	1.0	0.55	1		11/24/20 08:22	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.47	1		11/24/20 08:22	79-34-5	
Tetrachloroethene	11.8	ug/L	1.0	0.71	1		11/24/20 08:22	127-18-4	
Toluene	ND	ug/L	1.0	0.57	1		11/24/20 08:22	108-88-3	
1,1,1-Trichloroethane	84.3	ug/L	1.0	0.53	1		11/24/20 08:22	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.36	1		11/24/20 08:22	79-00-5	
Trichloroethene	19.5	ug/L	1.0	0.60	1		11/24/20 08:22	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.39	1		11/24/20 08:22	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.3	1		11/24/20 08:22	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	94	%.	85-116		1		11/24/20 08:22	460-00-4	
Dibromofluoromethane (S)	106	%.	75-120		1		11/24/20 08:22	1868-53-7	
Toluene-d8 (S)	96	%.	83-111		1		11/24/20 08:22	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site
Pace Project No.: 50273899

Sample: MW204	Lab ID: 50273899001	Collected: 11/17/20 08:50	Received: 11/20/20 09:30	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	1.7	1		11/24/20 09:11	67-64-1	
Benzene	ND	ug/L	1.0	0.51	1		11/24/20 09:11	71-43-2	
Bromochloromethane	ND	ug/L	1.0	0.53	1		11/24/20 09:11	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.62	1		11/24/20 09:11	75-27-4	
Bromoform	ND	ug/L	1.0	0.75	1		11/24/20 09:11	75-25-2	
Bromomethane	ND	ug/L	5.0	1.2	1		11/24/20 09:11	74-83-9	R1
2-Butanone (MEK)	ND	ug/L	20.0	2.0	1		11/24/20 09:11	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.56	1		11/24/20 09:11	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.50	1		11/24/20 09:11	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.54	1		11/24/20 09:11	108-90-7	
Chloroethane	ND	ug/L	2.0	0.65	1		11/24/20 09:11	75-00-3	
Chloroform	ND	ug/L	1.0	0.64	1		11/24/20 09:11	67-66-3	
Chloromethane	ND	ug/L	2.0	1.0	1		11/24/20 09:11	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	0.82	1		11/24/20 09:11	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.53	1		11/24/20 09:11	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.49	1		11/24/20 09:11	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.48	1		11/24/20 09:11	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.48	1		11/24/20 09:11	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.54	1		11/24/20 09:11	106-46-7	
1,1-Dichloroethane	55.7	ug/L	1.0	0.51	1		11/24/20 09:11	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.51	1		11/24/20 09:11	107-06-2	
1,1-Dichloroethene	36.3	ug/L	1.0	0.55	1		11/24/20 09:11	75-35-4	
cis-1,2-Dichloroethene	15.8	ug/L	1.0	0.50	1		11/24/20 09:11	156-59-2	
trans-1,2-Dichloroethene	0.75J	ug/L	1.0	0.49	1		11/24/20 09:11	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.65	1		11/24/20 09:11	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.56	1		11/24/20 09:11	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.57	1		11/24/20 09:11	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.54	1		11/24/20 09:11	100-41-4	
2-Hexanone	ND	ug/L	20.0	2.6	1		11/24/20 09:11	591-78-6	
Methylene Chloride	ND	ug/L	5.0	0.97	1		11/24/20 09:11	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	1.7	1		11/24/20 09:11	108-10-1	
Styrene	ND	ug/L	1.0	0.58	1		11/24/20 09:11	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.49	1		11/24/20 09:11	79-34-5	
Tetrachloroethene	2.7	ug/L	1.0	0.61	1		11/24/20 09:11	127-18-4	
Toluene	ND	ug/L	1.0	0.51	1		11/24/20 09:11	108-88-3	
1,1,1-Trichloroethane	34.0	ug/L	1.0	0.63	1		11/24/20 09:11	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.44	1		11/24/20 09:11	79-00-5	
Trichloroethene	75.5	ug/L	1.0	0.63	1		11/24/20 09:11	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.72	1		11/24/20 09:11	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.1	1		11/24/20 09:11	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	90	%.	85-116		1		11/24/20 09:11	460-00-4	
Dibromofluoromethane (S)	106	%.	75-120		1		11/24/20 09:11	1868-53-7	
Toluene-d8 (S)	103	%.	83-111		1		11/24/20 09:11	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site
Pace Project No.: 50273899

Sample: FD-2	Lab ID: 50273899013		Collected: 11/18/20 14:40	Received: 11/20/20 09:30	Matrix: Water				
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	5.0	1		11/24/20 07:17	67-64-1	
Benzene	ND	ug/L	1.0	0.68	1		11/24/20 07:17	71-43-2	
Bromochloromethane	ND	ug/L	1.0	0.60	1		11/24/20 07:17	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.49	1		11/24/20 07:17	75-27-4	
Bromoform	ND	ug/L	1.0	0.68	1		11/24/20 07:17	75-25-2	
Bromomethane	ND	ug/L	5.0	5.0	1		11/24/20 07:17	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	2.0	1		11/24/20 07:17	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.51	1		11/24/20 07:17	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.63	1		11/24/20 07:17	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.61	1		11/24/20 07:17	108-90-7	
Chloroethane	ND	ug/L	2.0	0.66	1		11/24/20 07:17	75-00-3	
Chloroform	ND	ug/L	1.0	0.66	1		11/24/20 07:17	67-66-3	
Chloromethane	ND	ug/L	2.0	0.61	1		11/24/20 07:17	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	2.2	1		11/24/20 07:17	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.54	1		11/24/20 07:17	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.51	1		11/24/20 07:17	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.60	1		11/24/20 07:17	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.52	1		11/24/20 07:17	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.58	1		11/24/20 07:17	106-46-7	
1,1-Dichloroethane	1.6	ug/L	1.0	0.66	1		11/24/20 07:17	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.67	1		11/24/20 07:17	107-06-2	
1,1-Dichloroethene	ND	ug/L	1.0	0.59	1		11/24/20 07:17	75-35-4	
cis-1,2-Dichloroethene	0.86J	ug/L	1.0	0.69	1		11/24/20 07:17	156-59-2	
trans-1,2-Dichloroethene	ND	ug/L	1.0	0.62	1		11/24/20 07:17	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.71	1		11/24/20 07:17	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.55	1		11/24/20 07:17	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.15	1		11/24/20 07:17	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.56	1		11/24/20 07:17	100-41-4	
2-Hexanone	ND	ug/L	20.0	2.4	1		11/24/20 07:17	591-78-6	
Methylene Chloride	ND	ug/L	5.0	1.0	1		11/24/20 07:17	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	4.3	1		11/24/20 07:17	108-10-1	
Styrene	ND	ug/L	1.0	0.55	1		11/24/20 07:17	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.47	1		11/24/20 07:17	79-34-5	
Tetrachloroethene	ND	ug/L	1.0	0.71	1		11/24/20 07:17	127-18-4	
Toluene	ND	ug/L	1.0	0.57	1		11/24/20 07:17	108-88-3	
1,1,1-Trichloroethane	ND	ug/L	1.0	0.53	1		11/24/20 07:17	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.36	1		11/24/20 07:17	79-00-5	
Trichloroethene	2.1	ug/L	1.0	0.60	1		11/24/20 07:17	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.39	1		11/24/20 07:17	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.3	1		11/24/20 07:17	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	95	%.	85-116		1		11/24/20 07:17	460-00-4	
Dibromofluoromethane (S)	106	%.	75-120		1		11/24/20 07:17	1868-53-7	
Toluene-d8 (S)	97	%.	83-111		1		11/24/20 07:17	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

ANALYTICAL RESULTS

Project: SE Rockford, IL Site

Pace Project No.: 50273899

Sample: Trip Blank	Lab ID: 50273899015	Collected: 11/18/20 00:00	Received: 11/20/20 09:30	Matrix: Water					
Parameters	Results	Units	Report Limit	MDL	DF	Prepared	Analyzed	CAS No.	Qual
8260 MSV Low Level	Analytical Method: EPA 5030B/8260 Pace Analytical Services - Indianapolis								
Acetone	ND	ug/L	20.0	5.0	1		11/24/20 08:55	67-64-1	
Benzene	ND	ug/L	1.0	0.68	1		11/24/20 08:55	71-43-2	
Bromochloromethane	ND	ug/L	1.0	0.60	1		11/24/20 08:55	74-97-5	
Bromodichloromethane	ND	ug/L	1.0	0.49	1		11/24/20 08:55	75-27-4	
Bromoform	ND	ug/L	1.0	0.68	1		11/24/20 08:55	75-25-2	
Bromomethane	ND	ug/L	5.0	5.0	1		11/24/20 08:55	74-83-9	
2-Butanone (MEK)	ND	ug/L	20.0	2.0	1		11/24/20 08:55	78-93-3	
Carbon disulfide	ND	ug/L	5.0	0.51	1		11/24/20 08:55	75-15-0	
Carbon tetrachloride	ND	ug/L	1.0	0.63	1		11/24/20 08:55	56-23-5	
Chlorobenzene	ND	ug/L	1.0	0.61	1		11/24/20 08:55	108-90-7	
Chloroethane	ND	ug/L	2.0	0.66	1		11/24/20 08:55	75-00-3	
Chloroform	ND	ug/L	1.0	0.66	1		11/24/20 08:55	67-66-3	
Chloromethane	ND	ug/L	2.0	0.61	1		11/24/20 08:55	74-87-3	
1,2-Dibromo-3-chloropropane	ND	ug/L	10.0	2.2	1		11/24/20 08:55	96-12-8	
Dibromochloromethane	ND	ug/L	1.0	0.54	1		11/24/20 08:55	124-48-1	
1,2-Dibromoethane (EDB)	ND	ug/L	1.0	0.51	1		11/24/20 08:55	106-93-4	
1,2-Dichlorobenzene	ND	ug/L	1.0	0.60	1		11/24/20 08:55	95-50-1	
1,3-Dichlorobenzene	ND	ug/L	1.0	0.52	1		11/24/20 08:55	541-73-1	
1,4-Dichlorobenzene	ND	ug/L	1.0	0.58	1		11/24/20 08:55	106-46-7	
1,1-Dichloroethane	ND	ug/L	1.0	0.66	1		11/24/20 08:55	75-34-3	
1,2-Dichloroethane	ND	ug/L	1.0	0.67	1		11/24/20 08:55	107-06-2	
1,1-Dichloroethene	ND	ug/L	1.0	0.59	1		11/24/20 08:55	75-35-4	
cis-1,2-Dichloroethene	ND	ug/L	1.0	0.69	1		11/24/20 08:55	156-59-2	
trans-1,2-Dichloroethene	ND	ug/L	1.0	0.62	1		11/24/20 08:55	156-60-5	
1,2-Dichloropropane	ND	ug/L	1.0	0.71	1		11/24/20 08:55	78-87-5	
cis-1,3-Dichloropropene	ND	ug/L	1.0	0.55	1		11/24/20 08:55	10061-01-5	
trans-1,3-Dichloropropene	ND	ug/L	1.0	0.15	1		11/24/20 08:55	10061-02-6	
Ethylbenzene	ND	ug/L	1.0	0.56	1		11/24/20 08:55	100-41-4	
2-Hexanone	ND	ug/L	20.0	2.4	1		11/24/20 08:55	591-78-6	
Methylene Chloride	ND	ug/L	5.0	1.0	1		11/24/20 08:55	75-09-2	
4-Methyl-2-pentanone (MIBK)	ND	ug/L	20.0	4.3	1		11/24/20 08:55	108-10-1	
Styrene	ND	ug/L	1.0	0.55	1		11/24/20 08:55	100-42-5	
1,1,2,2-Tetrachloroethane	ND	ug/L	1.0	0.47	1		11/24/20 08:55	79-34-5	
Tetrachloroethene	ND	ug/L	1.0	0.71	1		11/24/20 08:55	127-18-4	
Toluene	ND	ug/L	1.0	0.57	1		11/24/20 08:55	108-88-3	
1,1,1-Trichloroethane	ND	ug/L	1.0	0.53	1		11/24/20 08:55	71-55-6	
1,1,2-Trichloroethane	ND	ug/L	1.0	0.36	1		11/24/20 08:55	79-00-5	
Trichloroethene	ND	ug/L	1.0	0.60	1		11/24/20 08:55	79-01-6	
Vinyl chloride	ND	ug/L	1.0	0.39	1		11/24/20 08:55	75-01-4	
Xylene (Total)	ND	ug/L	3.0	1.3	1		11/24/20 08:55	1330-20-7	
Surrogates									
4-Bromofluorobenzene (S)	96	%.	85-116		1		11/24/20 08:55	460-00-4	
Dibromofluoromethane (S)	106	%.	75-120		1		11/24/20 08:55	1868-53-7	
Toluene-d8 (S)	98	%.	83-111		1		11/24/20 08:55	2037-26-5	

REPORT OF LABORATORY ANALYSIS

This report shall not be reproduced, except in full,
without the written consent of Pace Analytical Services, LLC.

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273899
Project Manager: Melanie Booms

MW101D (50273899006)

A204718-06 (Water)

Date Sampled
11/18/2020 07:58

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011157

1,4-Dioxane	0.12	0.057	0.50	ug/L	1	11/21/2020	11/23/2020 13:07	EPA 8260B	J
--------------------	-------------	-------	------	------	---	------------	------------------	-----------	---

Surrogate: 1,3-Dioxane

96.5 %

68.1-127

11/21/2020

11/23/2020 13:07

EPA 8260B

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273899
Project Manager: Melanie Booms

MW113A (50273899002)

A204718-02 (Water)

Date Sampled
11/17/2020 10:07

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011157

1,4-Dioxane	30	0.057	0.50	ug/L	1	11/21/2020	11/23/2020 11:43	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			91.8 %	68.1-127		11/21/2020	11/23/2020 11:43	EPA 8260B

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273899
Project Manager: Melanie Booms

MW113B (50273899003)

A204718-03 (Water)

Date Sampled
11/17/2020 10:48

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011157

1,4-Dioxane	70	0.057	0.50	ug/L	1	11/21/2020	11/23/2020 12:03	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			88.9 %	68.1-127		11/21/2020	11/23/2020 12:03	EPA 8260B

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273899
Project Manager: Melanie Booms

MW114A (50273899011)

A204718-11 (Water)

Date Sampled
11/18/2020 13:55

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011157

1,4-Dioxane	21	0.057	0.50	ug/L	1	11/21/2020	11/23/2020 15:12	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			89.2 %	68.1-127		11/21/2020	11/23/2020 15:12	EPA 8260B

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273899
Project Manager: Melanie Booms

MW114B (50273899012)

A204718-12 (Water)

Date Sampled
11/18/2020 14:36

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011157

1,4-Dioxane	9.8	0.057	0.50	ug/L	1	11/21/2020	11/23/2020 15:32	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			87.1 %	68.1-127		11/21/2020	11/23/2020 15:32	EPA 8260B

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273899
Project Manager: Melanie Booms

MW124 (50273899010)

A204718-10 (Water)

Date Sampled

11/18/2020 13:10

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011157

1,4-Dioxane	5.3	0.057	0.50	ug/L	1	11/21/2020	11/23/2020 14:51	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			92.9 %	68.1-127		11/21/2020	11/23/2020 14:51	EPA 8260B

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273899
Project Manager: Melanie Booms

MW130 (50273899005)

A204718-05 (Water)

Date Sampled

11/17/2020 16:36

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011157

1,4-Dioxane	6.6	0.057	0.50	ug/L	1	11/21/2020	11/23/2020 12:45	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			88.9 %	68.1-127		11/21/2020	11/23/2020 12:45	EPA 8260B

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273899
Project Manager: Melanie Booms

MW133A (50273899007)

A204718-07 (Water)

Date Sampled

11/18/2020 11:12

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011157

1,4-Dioxane	0.63	0.057	0.50	ug/L	1	11/21/2020	11/23/2020 13:27	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			91.6 %	68.1-127		11/21/2020	11/23/2020 13:27	EPA 8260B

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273899
Project Manager: Melanie Booms

MW133B (50273899008)

A204718-08 (Water)

Date Sampled

11/18/2020 11:53

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011157

1,4-Dioxane	15	0.057	0.50	ug/L	1	11/21/2020	11/23/2020 13:48	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			91.1 %	68.1-127		11/21/2020	11/23/2020 13:48	EPA 8260B

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273899
Project Manager: Melanie Booms

MW133C (50273899009)

A204718-09 (Water)

Date Sampled

11/18/2020 12:29

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011157

1,4-Dioxane	120	0.057	0.50	ug/L	1	11/21/2020	11/23/2020 14:30	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			89.1 %	68.1-127		11/21/2020	11/23/2020 14:30	EPA 8260B

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273899
Project Manager: Melanie Booms

MW200 (50273899004)

A204718-04 (Water)

Date Sampled

11/17/2020 11:28

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011157

1,4-Dioxane	0.20	0.057	0.50	ug/L	1	11/21/2020	11/23/2020 12:25	EPA 8260B	J
--------------------	-------------	-------	------	------	---	------------	------------------	-----------	---

Surrogate: 1,3-Dioxane

98.3 %

68.1-127

11/21/2020

11/23/2020 12:25

EPA 8260B

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273899
Project Manager: Melanie Booms

MW16 (50273899014)

Date Sampled

A204718-14 (Water)

11/18/2020 15:11

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011157

1,4-Dioxane	20	0.057	0.50	ug/L	1	11/21/2020	11/23/2020 16:14	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			88.4 %	68.1-127		11/21/2020	11/23/2020 16:14	EPA 8260B

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273899
Project Manager: Melanie Booms

MW204 (50273899001)

A204718-01 (Water)

Date Sampled
11/17/2020 08:50

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011157

1,4-Dioxane	25	0.057	0.50	ug/L	1	11/21/2020	11/23/2020 17:17	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			85.5 %	68.1-127		11/21/2020	11/23/2020 17:17	EPA 8260B

Pace Analytical
5560 Corporate Exchange Ct. SE
Grand Rapids MI, 49512

Project: SE Rockford, IL Site
Project Number: 50273899
Project Manager: Melanie Booms

FD-2 (50273899013)

A204718-13 (Water)

Date Sampled

11/18/2020 14:40

Analyte	Result	Limit of Detection	Limit of Quantitation	Units	Dilution	Prepared	Analyzed	Method	Qualifiers
---------	--------	--------------------	-----------------------	-------	----------	----------	----------	--------	------------

Pace Analytical - Madison

1,4-Dioxane by SPME GC/MS

Preparation Batch: A011157

1,4-Dioxane	10	0.057	0.50	ug/L	1	11/21/2020	11/23/2020 15:54	EPA 8260B
<i>Surrogate: 1,3-Dioxane</i>			80.7 %	68.1-127		11/21/2020	11/23/2020 15:54	EPA 8260B

APPENDIX B

Groundwater Monitoring
Field Data Sheets

SE ROCKFORD SAMPLING REPORT

Site Conditions

Period: **FALL 2020**

Type: Routine Semi-Annual; Monitoring Well Network

Sample dates: NOV 13 – NOV 18

Sample ship dates: NOV 16; NOV 19 via FedEx priority overnight

Weather: Cold & Ptly Cloudy, highs in 30's degrees F, periods of scattered light rain/snow.

Sampler: Pat Egan

Visitors: none

Method: Low Flow Micropurge

Observations

Field Duplicate: FD-1 = MW201

FD-2 = MW114B

One Trip Blank was submitted with each shipment (samples were submitted in two shipment(s)

Exceptions

- MW203 was sampled with a portable low flow sampling pump (routine). The permanent well pump installed in the well was removed by an unknown party.

Maintenance Observations/issues


- Need to replace lock on MW102D
- Need to repair/replace MW203 protective casing cover (7" valve box type) was damaged/broken.

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Stickup (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-16
Casing Stickup (Ft.)	-0.028	Purge Method Low Flow Micro Purge		Container 40 mL VOA Vial	Sample Date 18-Nov-20
Total Well Depth (Ft.) TOC	62.36	Purge Equip QED Air Diaphragm		Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	19.46	Field Analysis Method Flow Thru Analysis - 250 mL		Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	42.93	Field Analysis Equip YSI 556 MSP		Sampling Period FALL 20	

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HH:MM	Standard Units	mg/l	°C	mV	µS/cm	NTU	mL/min	(Ft.) TOC	
14:54									
14:55	7.32	5.72	11.92	15.2	1321.55	36	400	19.48	cloudy
14:57	7.31	5.77	11.91	19.1	1321.95		400		
15:00	7.32	5.73	11.93	22.7	1322.84		400		
15:02	7.34	5.78	11.92	25.7	1323.06		400		
15:04	7.34	5.78	11.89	29.0	1323.60		400		
15:05	7.32	5.79	11.87	31.6	1323.97		400		
15:06	7.32	5.84	11.87	33.0	1323.54		400		
15:07	7.33	5.83	11.87	33.9	1323.58		400		
15:08	7.32	5.80	11.85	35.6	1323.54		400		
15:09	7.32	5.83	11.82	37.5	1324.02		400	19.5	clear
15:10	7.30	5.83	11.83	39.8	1323.39		400		
15:11	7.31	5.85	11.84	40.8	1322.96		400		
MINUTES									
17.0	-0.01	0.23%	0.18%	3.24	-0.08%		6.80		
									TOTAL LITERS

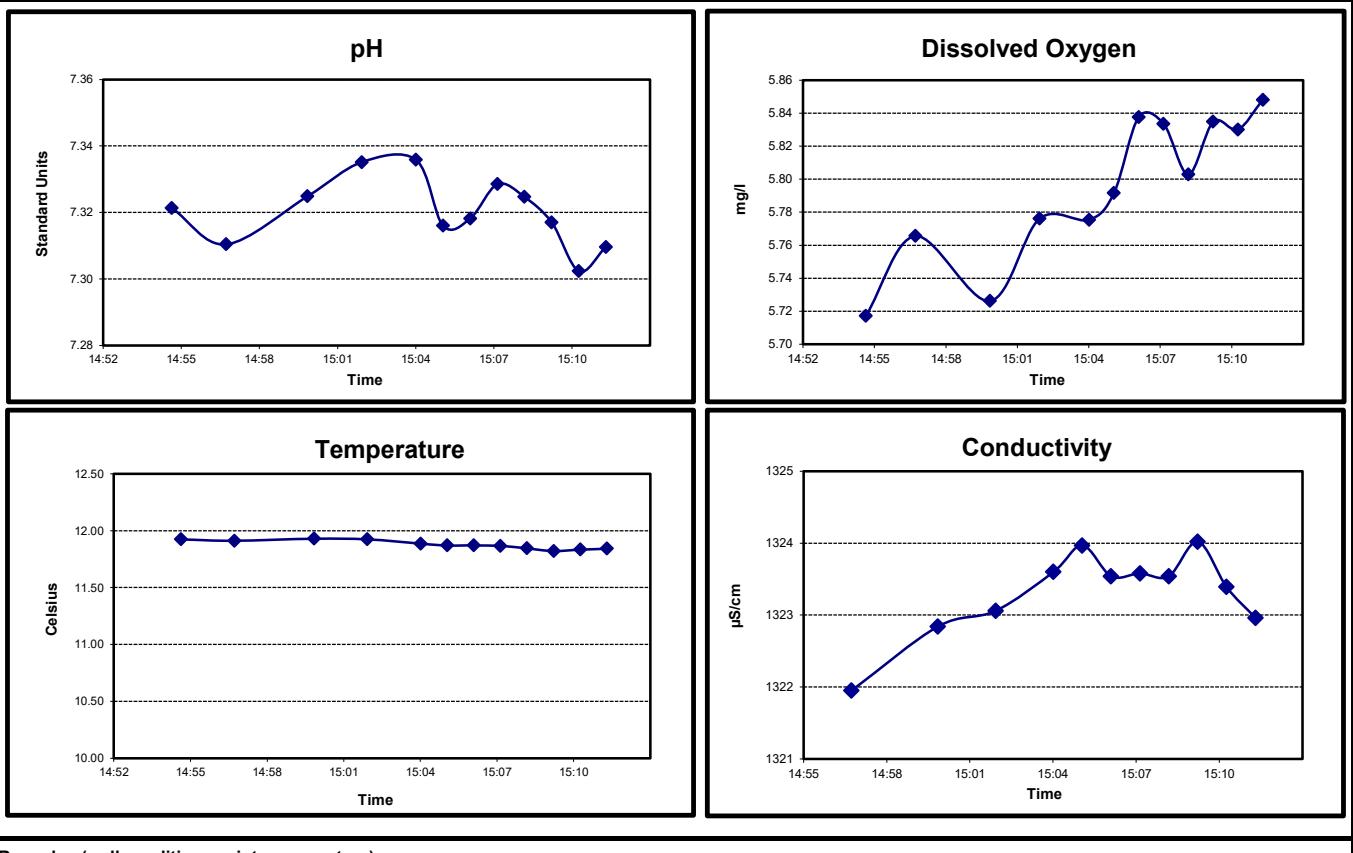





Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW-47
Casing Stickup (Ft.)	-0.063	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	14-Nov-20
Total Well Depth (Ft.) TOC	54.49	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	39.93	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	
Water Thickness (Ft.)	14.62	Field Analysis Equip	YSI 556 MSP	Sampling Period	FALL 20		None

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
9:16									
9:17	7.51	10.03	11.45	190.6	1079.69	57	380	39.97	cloudy
9:19	7.48	7.74	11.48	188.4	1073.20		380		
9:21	7.46	7.49	11.49	187.9	1076.60		380		
9:24	7.44	7.56	11.51	187.8	1083.32		380	40.02	slightly cloudy
9:24	7.44	7.56	11.51	187.8	1083.32		380	40.02	slightly cloudy
9:25	7.45	7.54	11.39	187.3	1085.31		380		
9:26	7.40	7.54	11.54	190.0	1085.96		380		
9:27	7.43	7.59	11.57	188.1	1087.01		380		
9:28	7.44	7.63	11.58	187.5	1084.71		380		
9:29	7.44	7.63	11.57	187.4	1084.45		380	40.1	slightly cloudy
9:30	7.43	7.60	11.56	187.6	1085.03		380		
9:31	7.44	7.59	11.49	187.1	1085.81		380		
MINUTES									TOTAL LITERS
15.0	0.00	-0.50%	-0.69%	-0.25	0.12%			5.70	

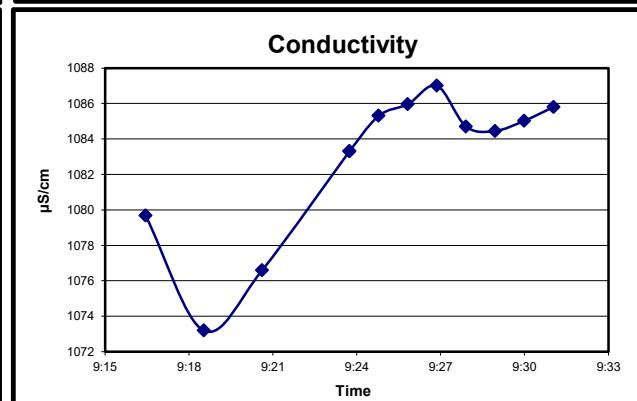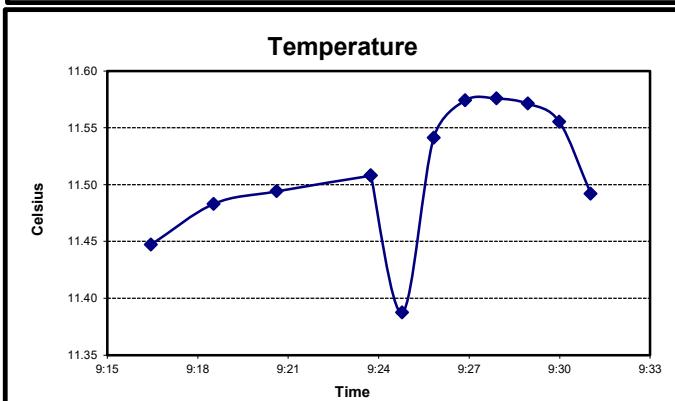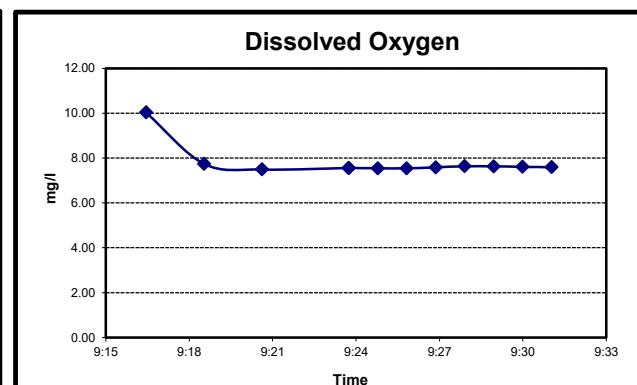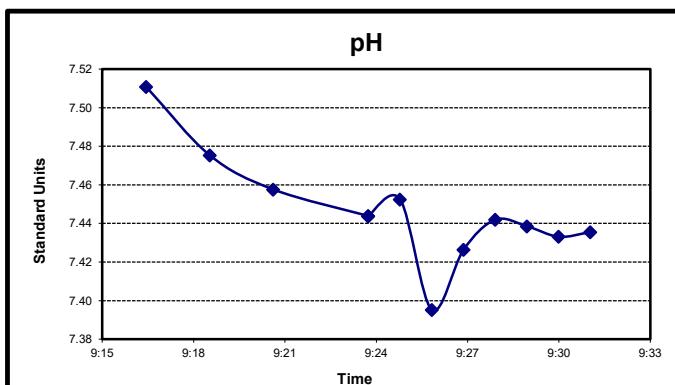


Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-101A
Casing Stickup (Ft.)	1.45	Purge Method	Low Flow Micro Purge	Container 40 mL VOA Vial	Sample Date 16-Nov-20
Total Well Depth (Ft.) TOC	90.34	Purge Equip	QED Air Diaphragm	Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	38.45	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	50.44	Field Analysis Equip	YSI 556 MSP	Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
15:12									
15:13	7.17	7.55	10.50	92.9	1183.69	63	500	38.45	clear
15:17	7.16	7.55	10.47	96.2	1183.72		500		
15:20	7.17	7.54	10.47	98.1	1182.75		500		
15:23	7.17	7.42	10.46	100.1	1181.86		500		
15:24	7.16	7.38	10.46	100.9	1181.41		500		
15:25	7.16	7.29	10.46	101.5	1181.06		500		
15:26	7.16	7.27	10.45	102.2	1180.30		500		
15:27	7.16	7.24	10.45	102.9	1179.68		500		
15:28	7.16	7.23	10.45	103.6	1179.20		500		
15:29	7.15	7.20	10.44	104.1	1178.57		500		
15:30	7.15	7.13	10.43	104.7	1177.51		500	38.49	clear
15:31	7.15	7.10	10.44	105.1	1176.57		500		
MINUTES									TOTAL LITERS
19.0	0.00	-1.47%	0.01%	0.98	-0.17%			9.50	

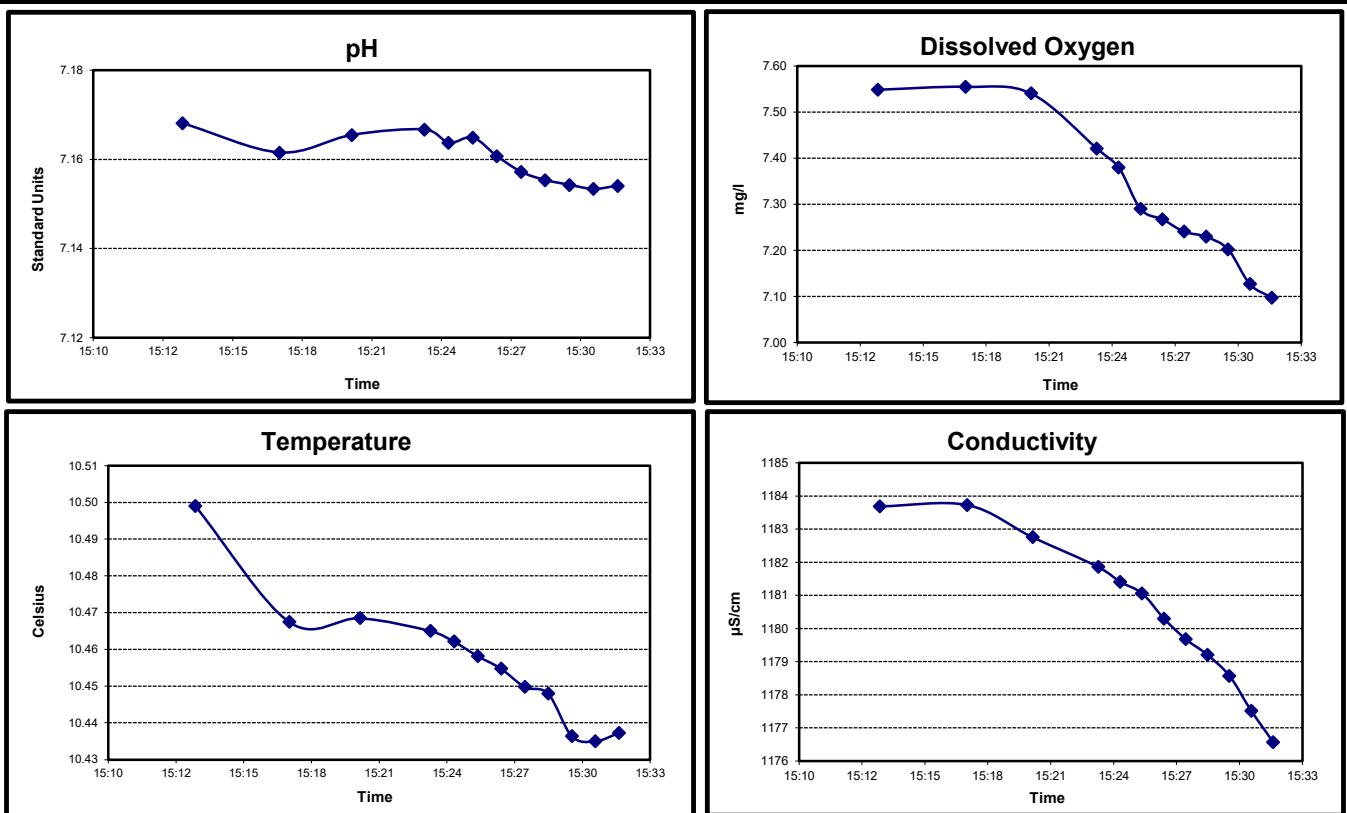


Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-101B
Casing Stickup (Ft.)	2.16	Purge Method Low Flow Micro Purge		Container 40 mL VOA Vial	Sample Date 16-Nov-20
Total Well Depth (Ft.) TOC	153.74	Purge Equip QED Air Diaphragm		Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	39.4	Field Analysis Method Flow Thru Analysis - 250 mL		Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	112.18	Field Analysis Equip YSI 556 MSP		Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
15:45									
15:46	7.39	0.80	10.21	103.9	1025.97	54	500	39.46	clear
15:48	7.37	0.56	10.18	99.8	1029.24		500		
15:51	7.34	0.65	10.18	93.3	1028.92		500		
15:55	7.31	0.98	10.17	87.0	1027.11		500		
15:57	7.30	1.21	10.15	84.5	1026.16		500		
15:58	7.28	1.24	10.15	84.0	1025.74		500		
15:59	7.27	1.32	10.15	83.1	1025.10		500		
16:00	7.27	1.35	10.17	82.2	1024.01		500		
16:01	7.27	1.36	10.16	81.7	1024.01		500		
16:02	7.26	1.42	10.16	81.5	1024.02		500		
16:03	7.26	1.46	10.16	80.6	1023.17		500	39.61	clear
16:04	7.26	1.50	10.16	80.0	1023.24		500		
MINUTES									TOTAL LITERS
18.0	0.00	5.23%	-0.06%	-1.44	-0.08%			9.00	

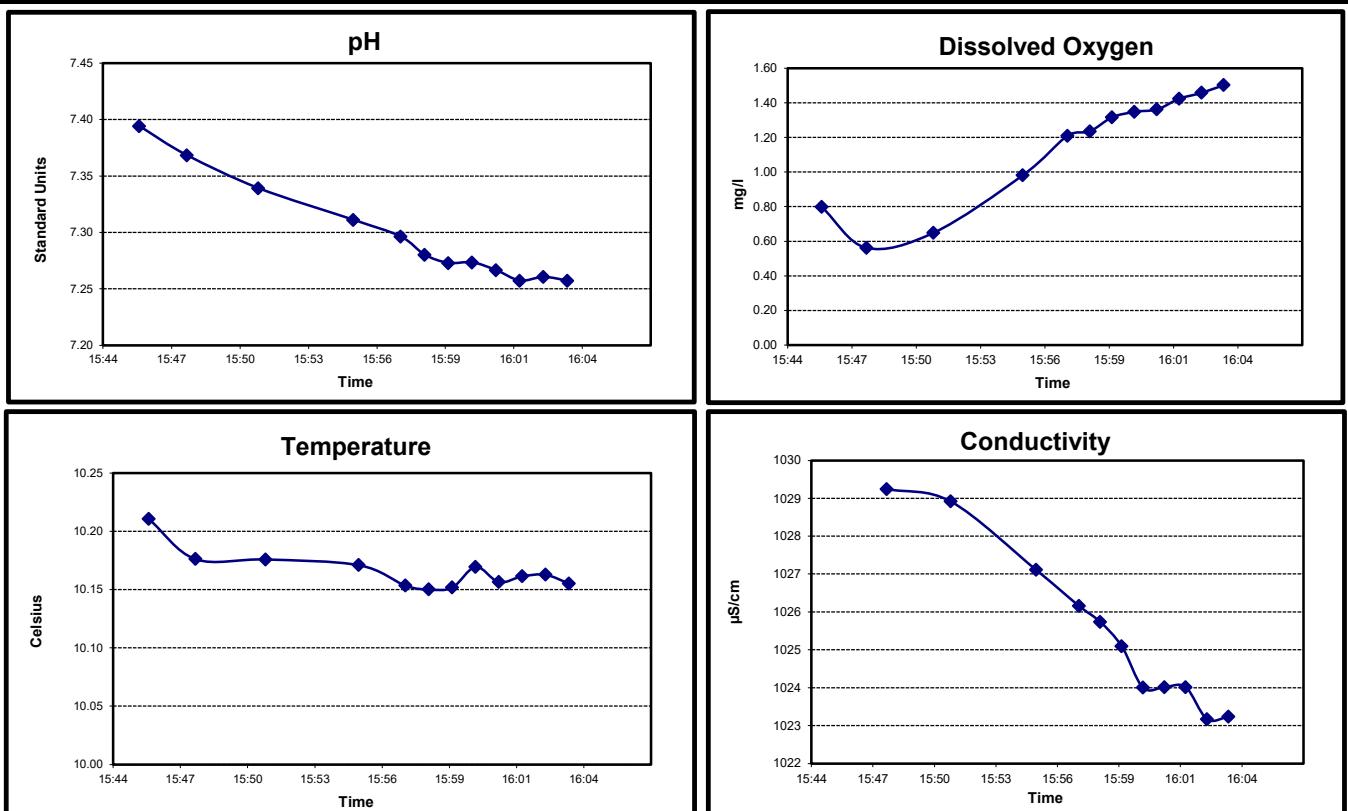

Remarks: (well condition, maintenance, etc...)


FD-2 = field duplicate for MW-101B collected

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-101C
Casing Stickup (Ft.)	1.12	Purge Method		Container 40 mL VOA Vial	Sample Date 16-Nov-20
Total Well Depth (Ft.) TOC	174.89	Purge Equip QED Air Diaphragm		Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	39.3	Field Analysis Method Flow Thru Analysis - 250 mL		Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	134.47	Field Analysis Equip YSI 556 MSP		Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
14:30									
14:31	7.01	3.34	10.21	64.9	960.78	45	500	39.33	clear
14:33	6.98	2.64	10.19	60.6	985.99		500		
14:35	6.99	2.41	10.18	55.6	994.09		500		
14:40	7.05	2.33	10.17	47.0	996.84		500		
14:42	7.05	2.34	10.19	45.4	996.18		500		
14:43	7.06	2.35	10.19	44.6	996.42		500		
14:44	7.07	2.35	10.18	43.9	996.58		500		
14:45	7.07	2.34	10.18	43.4	996.38		500		
14:46	7.07	2.33	10.19	43.2	995.65		500		
14:47	7.08	2.33	10.18	42.9	996.20		500		
14:48	7.08	2.34	10.19	42.6	995.94		500		
14:49	7.09	2.34	10.18	42.4	996.32		500	39.35	clear
MINUTES									TOTAL LITERS
19.0	0.01	0.22%	-0.04%	-0.52	0.01%				9.50

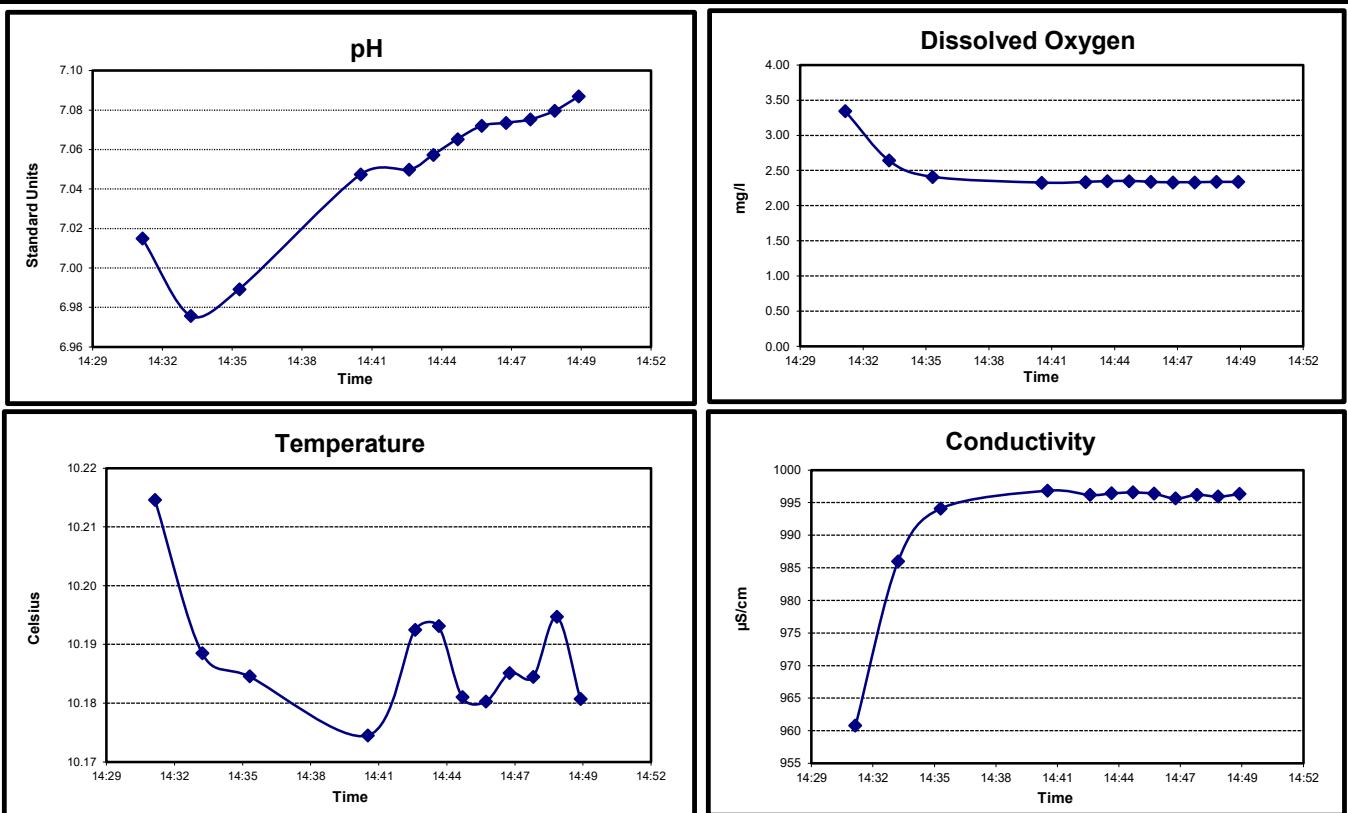


Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-101D
Casing Stickup (Ft.)	0.89	Purge Method Low Flow Micro Purge		Container 40 mL VOA Vial	Sample Date 18-Nov-20
Total Well Depth (Ft.) TOC	212.72	Purge Equip QED Air Diaphragm		Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	41.7	Field Analysis Method Flow Thru Analysis - 250 mL		Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	170.13	Field Analysis Equip YSI 556 MSP		Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
7:37									
7:38	8.62	0.83	10.24	108.3	119.88	84	350	41.73	cloudy
7:40	8.60	0.76	10.26	107.8	119.74		350		
7:42	8.57	0.74	10.27	107.3	119.70		350		
7:47	8.52	0.72	10.28	106.1	119.68		350		
7:49	8.51	0.71	10.28	105.2	119.61		350	41.74	cloudy
7:50	8.50	0.72	10.27	104.9	119.66		350		
7:51	8.50	0.71	10.26	104.5	119.63		350		
7:52	8.50	0.70	10.30	103.9	119.61		350		
7:53	8.49	0.70	10.29	103.5	119.62		350		
7:54	8.49	0.66	10.30	102.6	119.61		350		
7:55	8.48	0.68	10.31	102.7	119.62		350	41.74	cloudy
7:56	8.48	0.68	10.26	101.5	119.69		350		
MINUTES									TOTAL LITERS
19.0	-0.01	2.85%	-0.32%	-1.16	0.07%			6.65	

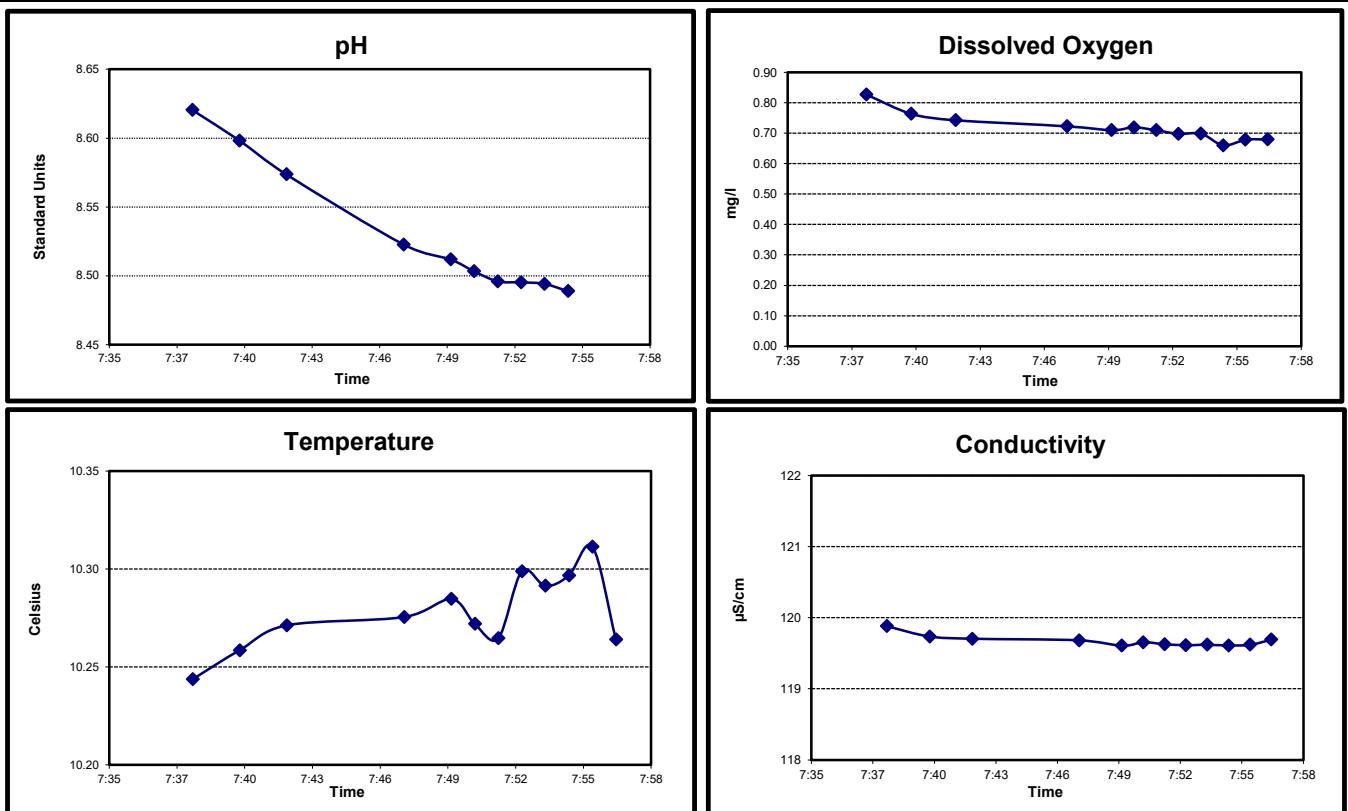


Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-102A
Casing Stickup (Ft.)	-0.47	Purge Method		Container 40 mL VOA Vial	Sample Date 16-Nov-20
Total Well Depth (Ft.) TOC	37.69	Purge Equip QED Air Diaphragm		Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	17.83	Field Analysis Method Flow Thru Analysis - 250 mL		Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	20.33	Field Analysis Equip YSI 556 MSP		Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
12:35									
12:36	7.01	1.46	12.65	-34.4	3773.15	47	420	17.86	slightly cloudy
12:38	7.01	1.44	12.66	-40.2	3775.36		420		
12:40	7.00	1.41	12.69	-43.9	3776.33		420		
12:44	6.99	1.36	12.65	-50.1	3767.23		420		
12:47	6.99	1.33	12.59	-53.7	3758.38		420		
12:48	6.98	1.32	12.55	-54.3	3752.98		420		
12:49	6.98	1.31	12.55	-54.8	3750.58		420		
12:50	6.97	1.29	12.53	-54.4	3743.12		420		
12:51	6.98	1.28	12.53	-53.9	3738.40		420		
12:52	6.97	1.28	12.56	-53.4	3731.12		420		
12:53	6.97	1.27	12.59	-53.9	3721.76		420	18.02	clear
12:54	7.02	1.25	12.60	-54.5	3716.67		420		
MINUTES									TOTAL LITERS
19.0	0.05	-2.34%	0.28%	-1.03	-0.39%			7.98	

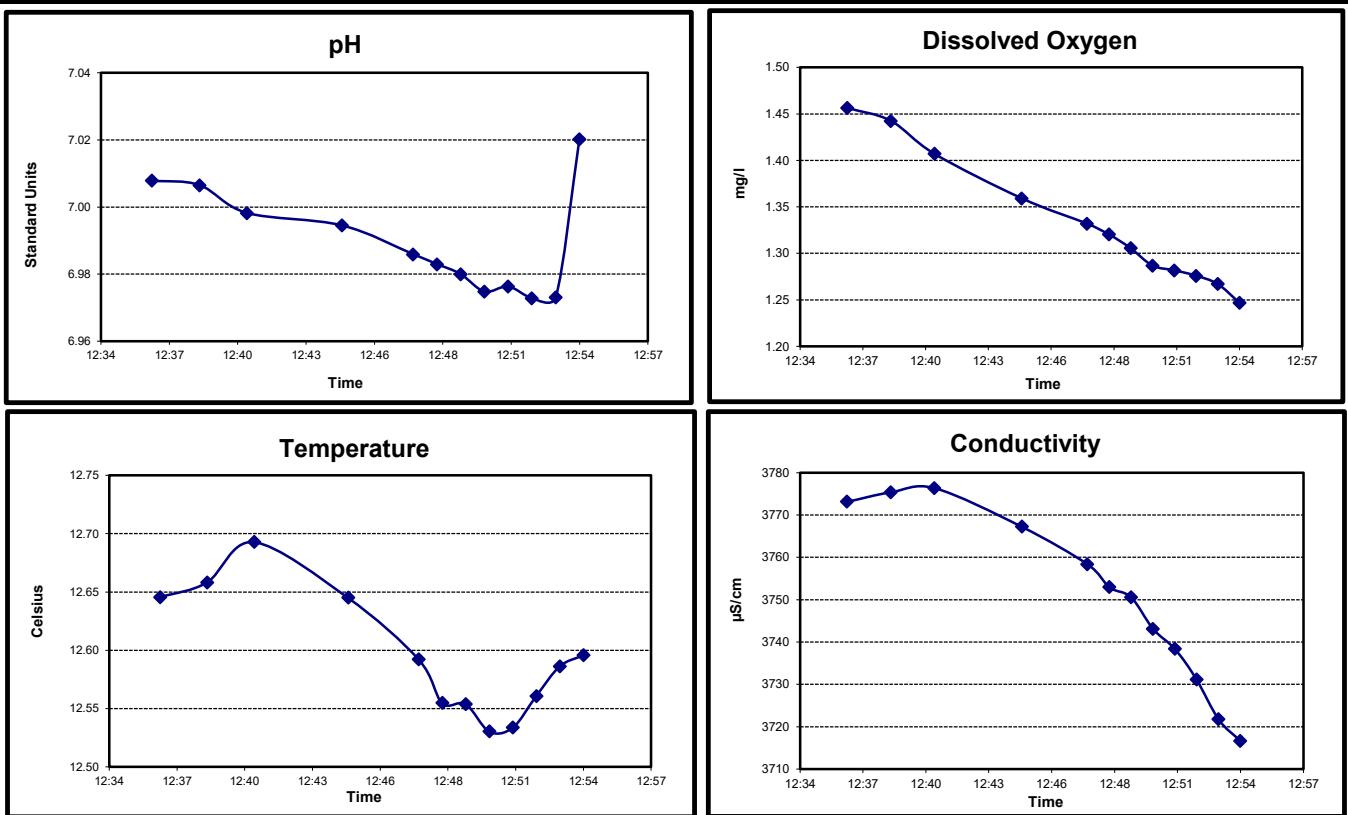


Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW-102B
Casing Stickup (Ft.)	-0.68	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	16-Nov-20
Total Well Depth (Ft.) TOC	100.5	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	32.25	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	
Water Thickness (Ft.)	68.93	Field Analysis Equip	YSI 556 MSP	Sampling Period	FALL 20		None

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
13:13									
13:14	6.92	0.60	10.35	-42.5	936.25	35	420	32.3	Slightly cloudy
13:16	6.93	0.55	10.33	-42.4	935.95		420		
13:19	6.95	0.50	10.34	-44.2	937.30		420		
13:22	7.00	0.46	10.37	-50.4	939.53		420	32.36	clear
13:24	7.07	0.46	10.43	-53.8	941.29		420		
13:25	7.08	0.46	10.46	-54.1	941.08		420		
13:26	7.11	0.45	10.42	-55.9	942.51		420		
13:27	7.13	0.45	10.38	-55.8	943.21		420		
13:28	7.13	0.46	10.35	-54.6	943.79		420		
13:29	7.13	0.45	10.36	-54.3	943.47		420		
13:30	7.13	0.45	10.35	-54.0	943.65		420	32.42	clear
13:31	7.12	0.46	10.34	-53.0	943.89		420		
MINUTES									TOTAL LITERS
18.0	-0.01	1.49%	-0.18%	1.29	0.04%				7.56

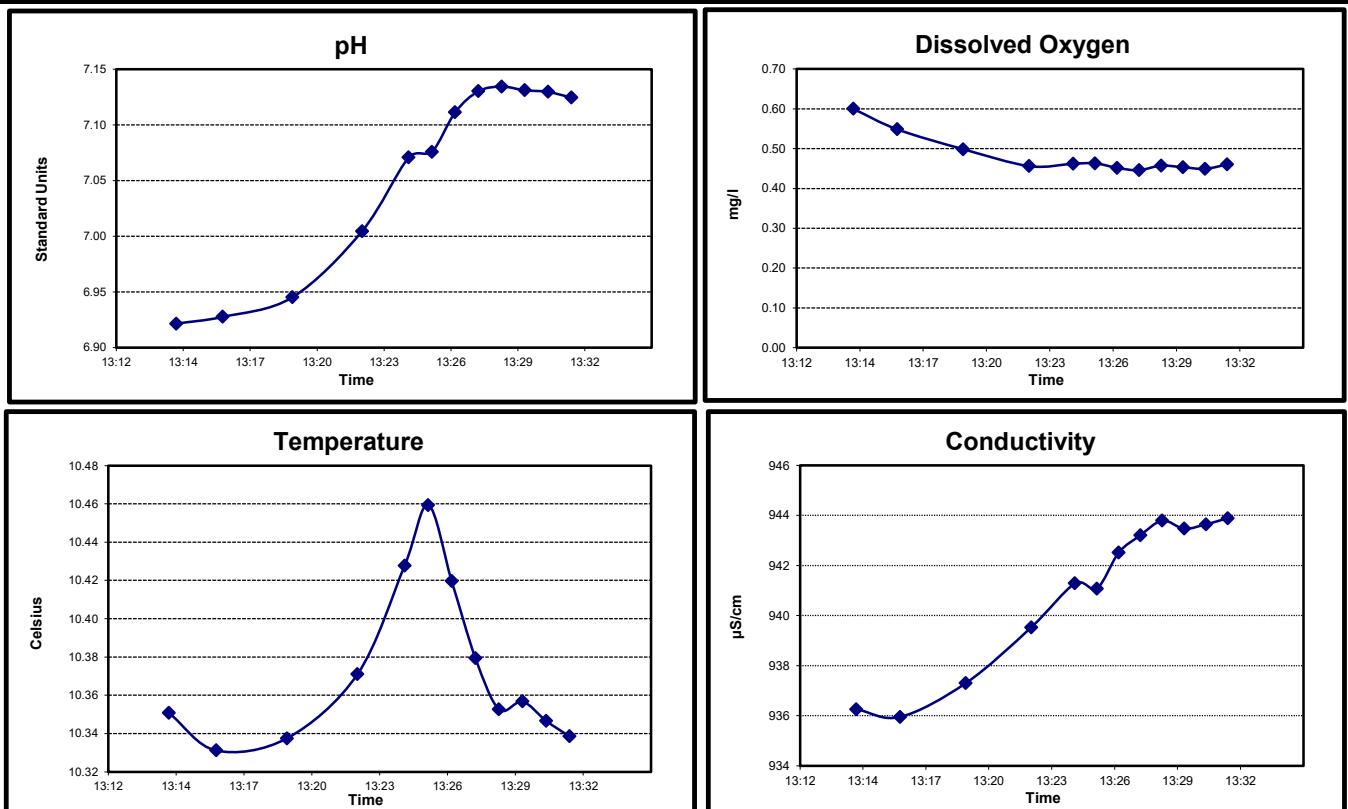


Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-102C
Casing Stickup (Ft.)	-0.43	Purge Method	Low Flow Micro Purge	Container 40 mL VOA Vial	Sample Date 16-Nov-20
Total Well Depth (Ft.) TOC	187.42	Purge Equip	QED Air Diaphragm	Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	33.64	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	154.21	Field Analysis Equip	YSI 556 MSP	Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond μS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
13:51									
13:52	7.43	0.46	11.00	-45.1	654.86	81	450	33.68	slightly cloudy
13:54	7.42	0.43	11.08	-47.3	664.13		450		
13:57	7.43	0.42	11.06	-50.4	688.49		450		
14:00	7.42	0.40	10.90	-52.3	731.43		450		
14:03	7.38	0.40	10.91	-44.5	765.87		450		
14:04	7.34	0.42	10.91	-43.1	775.71		450	33.75	slightly cloudy
14:05	7.31	0.42	11.01	-43.6	782.64		450		
14:06	7.29	0.42	11.07	-45.5	791.59		450		
14:07	7.32	0.41	11.01	-49.4	799.81		450		
14:08	7.33	0.41	11.01	-51.5	805.88		450		
14:09	7.35	0.41	10.95	-53.2	812.92		450		
14:10	7.35	0.42	10.90	-54.0	818.62		450	33.82	slightly cloudy
MINUTES									TOTAL LITERS
19.0	0.02	1.48%	-0.98%	-2.47	1.56%			8.55	

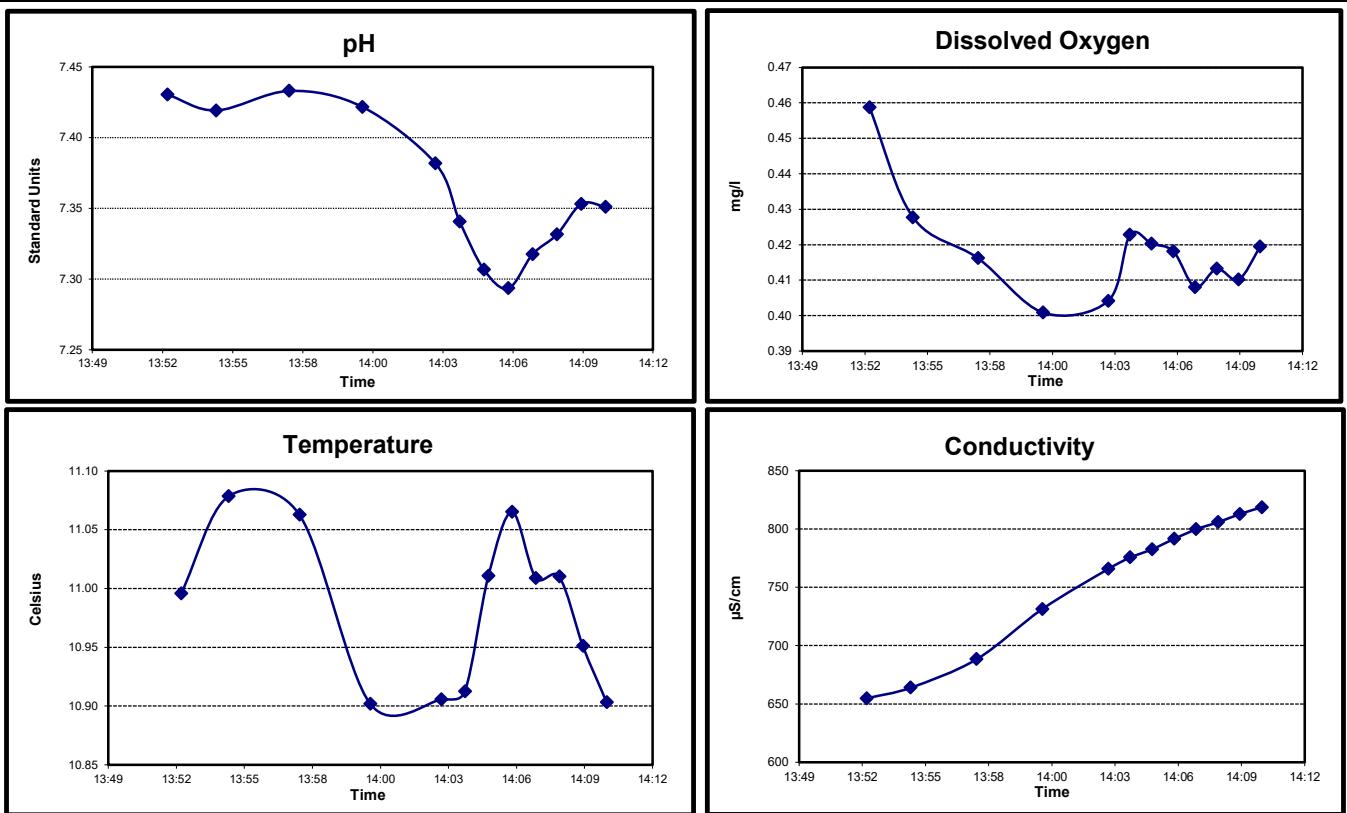





Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-113A
Casing Stickup (Ft.)	-1.06	Purge Method	Low Flow Micro Purge	Container 40 mL VOA Vial	Sample Date 17-Nov-20
Total Well Depth (Ft.) TOC	104.5	Purge Equip	QED Air Diaphragm	Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	50.88	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	54.68	Field Analysis Equip	YSI 556 MSP	Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
9:43									
9:44	7.42	2.33	10.73	126.8	1143.46	88	400	50.91	Slightly cloudy
9:46	7.41	2.36	10.67	126.5	1143.90		400		
9:49	7.40	2.33	10.77	126.2	1142.72		400		
9:52	7.39	2.30	10.76	125.6	1143.48		400		
9:55	7.38	2.33	10.76	124.6	1143.25		400		
9:56	7.39	2.30	10.78	124.3	1143.15		400		
9:57	7.38	2.30	10.76	123.9	1143.83		400		
9:58	7.38	2.30	10.78	123.3	1143.43		400		
9:59	7.37	2.31	10.75	123.2	1143.83		400		
10:00	7.37	2.31	10.77	122.8	1143.26		400		
10:01	7.37	2.35	10.77	122.5	1143.00		400	51.83	Slightly cloudy
10:02	7.37	2.29	10.77	121.8	1143.45		400		
MINUTES									TOTAL LITERS
19.0	0.00	-0.55%	-0.03%	-0.99	0.02%				7.60

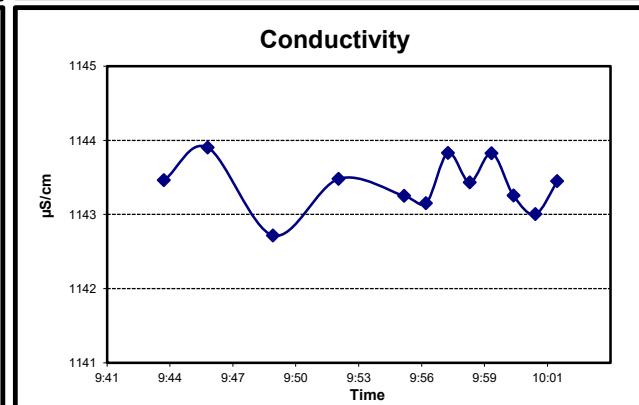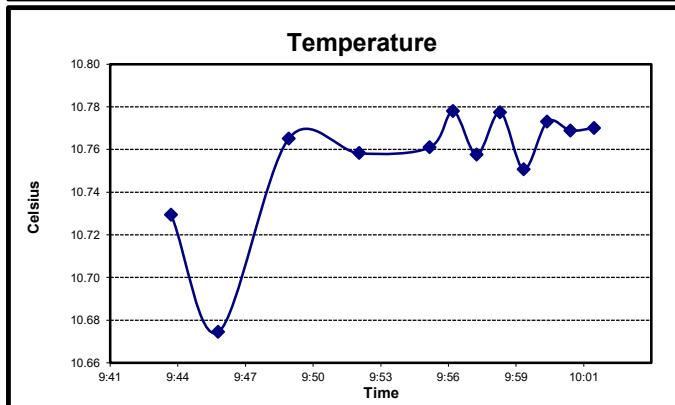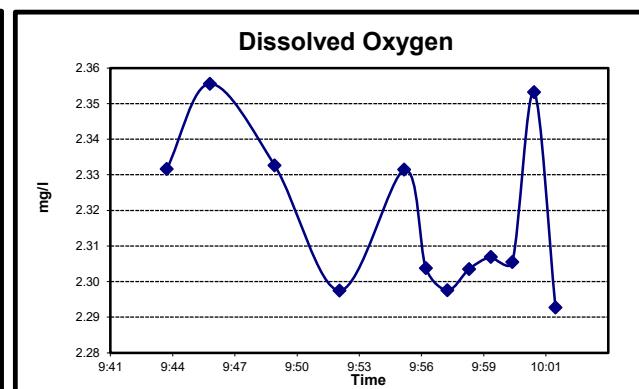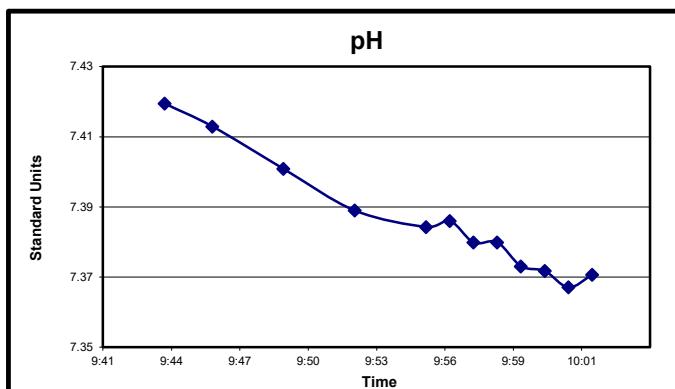


Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-113B
Casing Stickup (Ft.)	-0.43	Purge Method	Low Flow Micro Purge	Container 40 mL VOA Vial	Sample Date 17-Nov-20
Total Well Depth (Ft.) TOC	155.26	Purge Equip	QED Air Diaphragm	Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	51.59	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	104.10	Field Analysis Equip	YSI 556 MSP	Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
10:27									
10:28	7.46	0.50	10.64	-6.9	924.77	74	430	51.61	slightly cloudy
10:30	7.47	0.53	10.64	-20.4	924.39		430		
10:33	7.46	0.53	10.61	-36.2	924.84		430		
10:36	7.46	0.52	10.67	-47.2	922.47		430		
10:39	7.45	0.54	10.63	-56.0	922.14		430		
10:40	7.45	0.52	10.66	-58.6	920.92		430		
10:41	7.45	0.53	10.64	-60.6	921.04		430		
10:42	7.45	0.54	10.67	-62.8	920.27		430		
10:43	7.45	0.51	10.65	-64.9	920.36		430		
10:44	7.45	0.52	10.65	-66.5	919.84		430		
10:45	7.45	0.52	10.64	-68.2	919.54		430	51.73	slightly cloudy
10:46	7.47	0.53	10.62	-69.5	918.94		430		
MINUTES									TOTAL LITERS
19.0	0.02	1.73%	-0.25%	-2.95	-0.10%				8.17

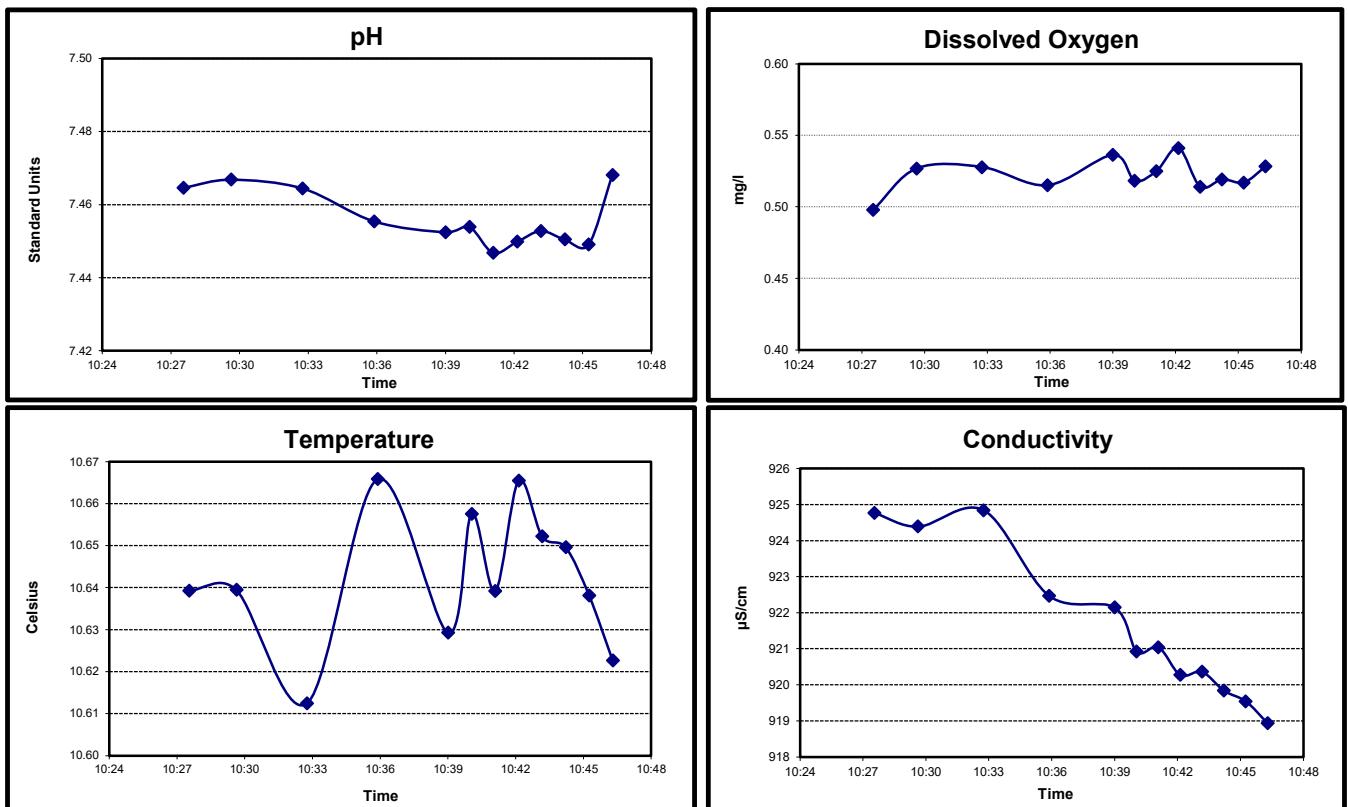


Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-114A
Casing Stickup (Ft.)	2.45	Purge Method		Container 40 mL VOA Vial	Sample Date 18-Nov-20
Total Well Depth (Ft.) TOC	97.48	Purge Equip QED Air Diaphragm		Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	23.81	Field Analysis Method Flow Thru Analysis - 250 mL		Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	71.22	Field Analysis Equip YSI 556 MSP		Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
13:34									
13:35	7.74	3.31	12.69	42.7	1428.55	78	390	23.86	slightly cloudy
13:37	7.75	2.28	12.79	38.2	1398.76		390		
13:40	7.74	2.06	12.72	32.3	1367.51		390		
13:43	7.74	1.95	12.61	27.0	1356.39		390	23.91	slightly cloudy
13:46	7.66	2.00	12.34	27.3	1343.39		390		
13:47	7.63	2.03	12.31	27.5	1342.44		390		
13:48	7.63	2.04	12.29	25.8	1343.06		390		
13:49	7.66	2.00	12.31	23.2	1340.98		390		
13:50	7.66	2.08	12.39	22.3	1339.08		390		
13:51	7.67	2.14	12.36	21.1	1340.84		390		
13:52	7.65	2.15	12.43	21.7	1337.21		390	23.98	
13:53	7.65	2.16	12.36	22.0	1339.36		390		
MINUTES									TOTAL LITERS
19.0	-0.02	0.90%	0.02%	0.91	-0.11%				7.41

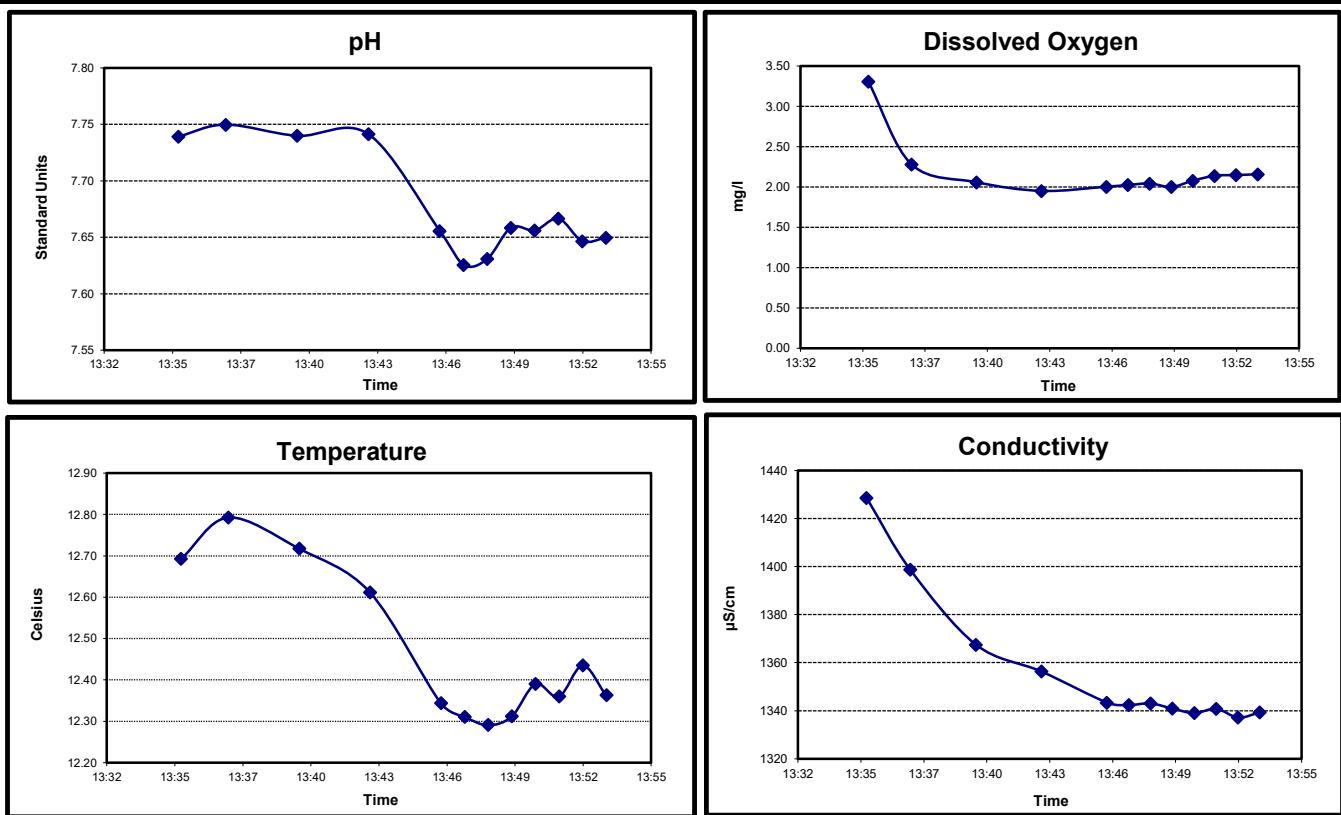


Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW-114B
Casing Stickup (Ft.)	-0.24	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	18-Nov-20
Total Well Depth (Ft.) TOC	222.58	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	25.29	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	
Water Thickness (Ft.)	197.53	Field Analysis Equip	YSI 556 MSP	Sampling Period	FALL 20		None

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
14:14									FD-2 - duplicate sample collected
14:15	8.69	0.60	12.00	-111.8	958.03	35	360		
14:17	8.75	0.54	11.85	-128.9	961.79		360		
14:20	8.74	0.47	11.76	-144.1	961.86		360		
14:23	8.72	0.38	11.87	-154.8	960.67		360	25.36	slightly cloudy
14:26	8.78	0.34	11.93	-164.0	960.69		360		
14:27	8.81	0.32	11.94	-167.7	961.53		360		
14:28	8.82	0.29	11.98	-170.6	961.67		360		
14:29	8.84	0.30	12.01	-174.3	961.79		360		
14:30	8.83	0.30	12.10	-175.9	960.90		360		
14:31	8.88	0.30	12.20	-181.1	960.55		360		
14:32	8.89	0.29	12.22	-183.8	961.28		360	25.38	clear
14:33	8.92	0.28	12.22	-187.8	962.20		360		
MINUTES									TOTAL LITERS
19.0	0.03	-9.36%	0.23%	-6.73	0.17%			6.84	

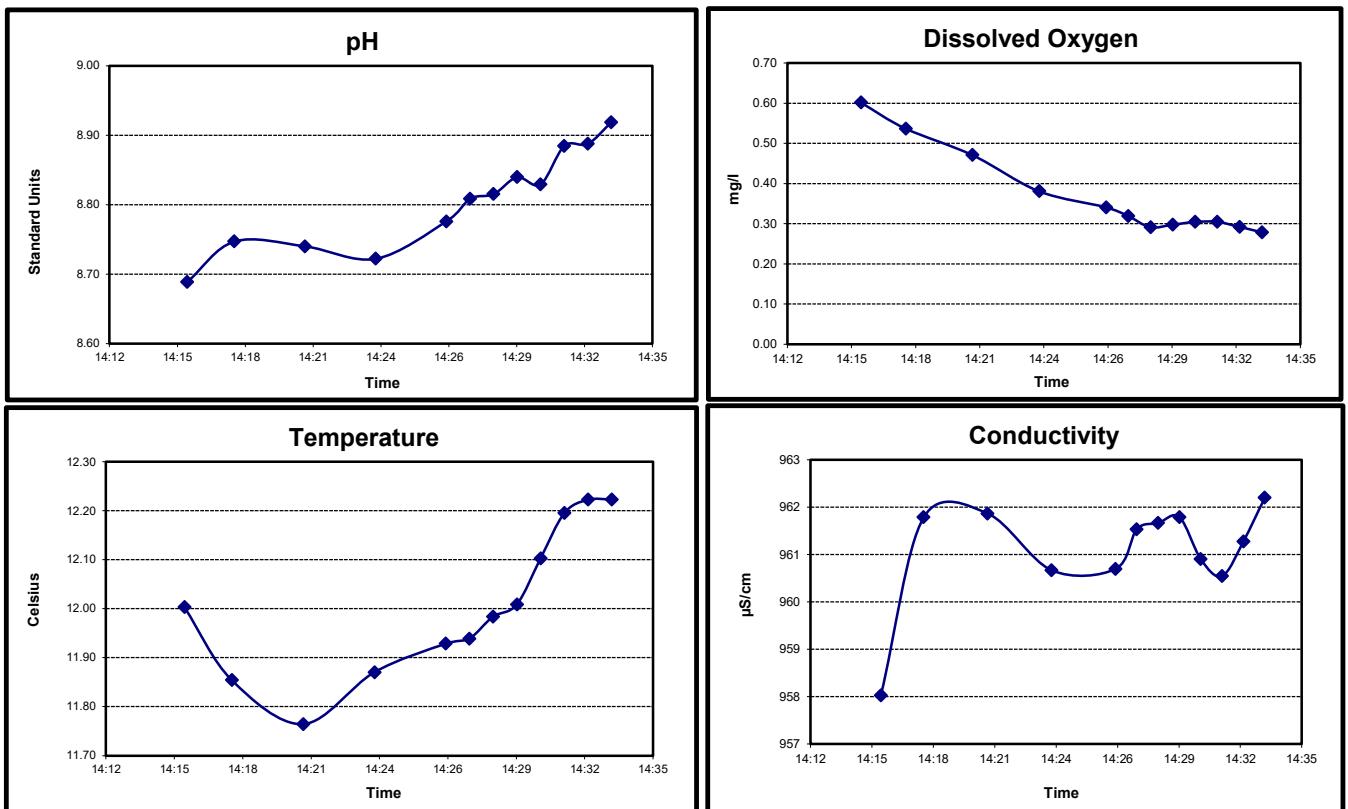


Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-117B
Casing Stickup (Ft.)	-0.45	Purge Method	Low Flow Micro Purge	Container 40 mL VOA Vial	Sample Date 13-Nov-20
Total Well Depth (Ft.) TOC	89.5	Purge Equip	QED Air Diaphragm	Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	5.18	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	84.77	Field Analysis Equip	YSI 556 MSP	Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
16:38									
16:39	7.29	3.21	11.97	17.2	1309.86	35	500	5.18	clear
16:41	7.29	0.83	11.99	18.5	1340.02		500		
16:44	7.24	0.73	11.98	18.0	1339.47		500		
16:47	7.23	0.95	11.97	17.7	1331.20		500		
16:47	7.23	0.95	11.97	17.7	1331.20		500		
16:48	7.21	0.99	11.98	19.5	1327.55		500		
16:49	7.23	1.06	11.96	19.4	1325.58		500		
16:50	7.21	1.07	11.96	21.1	1324.18		500		
16:51	7.22	1.12	11.95	21.2	1323.14		500	5.19	clear
16:52	7.20	1.15	11.96	23.5	1321.69		500		
16:53	7.22	1.17	11.95	23.5	1320.77		500		
16:54	7.20	1.18	11.96	25.5	1319.81		500		
MINUTES									
16.0	0.00	2.88%	0.03%	2.04	-0.14%			8.00	

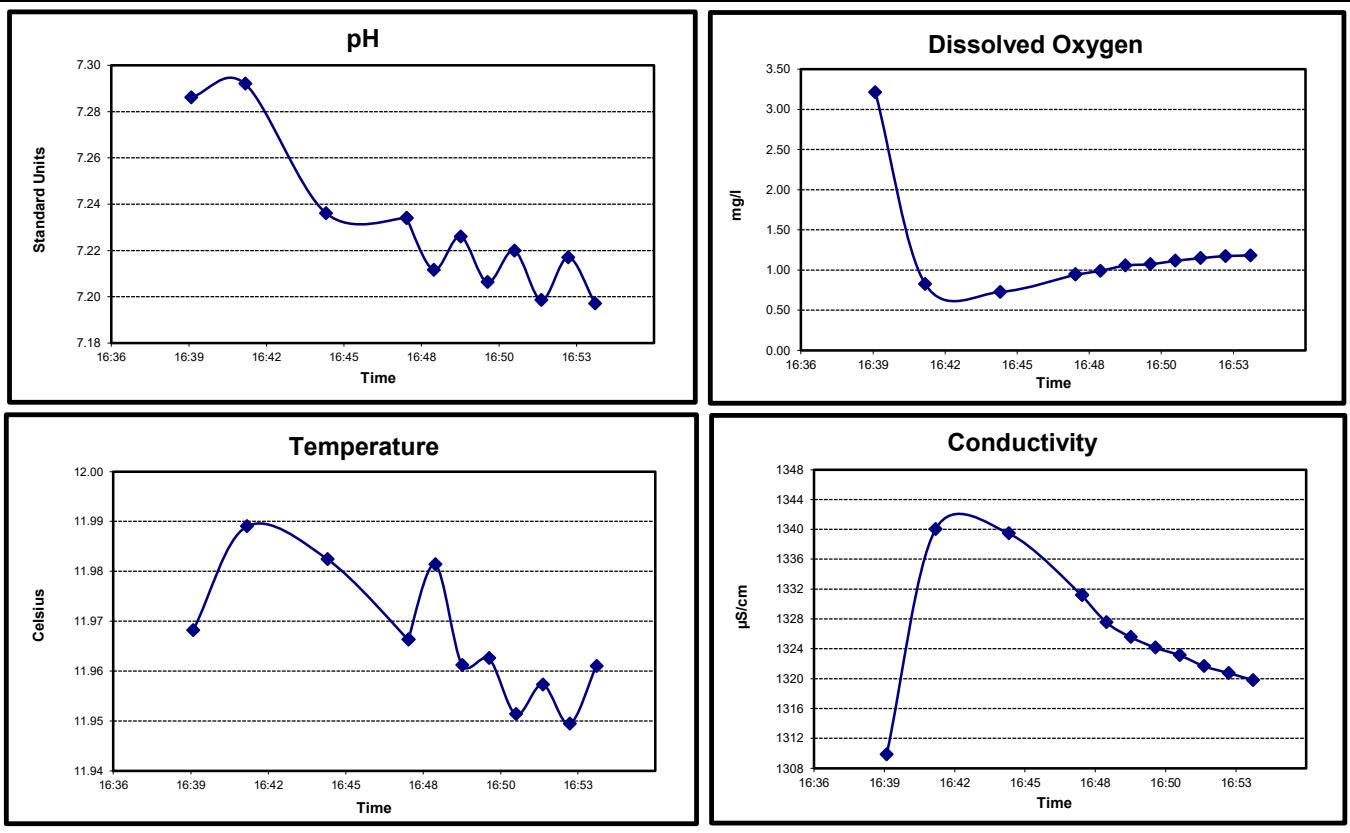


Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-117C
Casing Stickup (Ft.)	-0.63	Purge Method	Low Flow Micro Purge	Container 40 mL VOA Vial	Sample Date 13-Nov-20
Total Well Depth (Ft.) TOC	158.31	Purge Equip	QED Air Diaphragm	Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	3.81	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	155.13	Field Analysis Equip	YSI 556 MSP	Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
16:16									
16:17	7.09	1.42	12.09	68.9	1266.76	26	500	3.81	clear
16:19	7.26	0.58	12.13	59.0	1257.66		500		
16:22	7.26	0.47	12.09	55.4	1298.92		500		
16:24	7.22	0.46	12.09	54.0	1303.58		500		
16:26	7.19	0.46	12.06	52.2	1275.84		500	3.81	clear
16:28	7.17	0.48	12.05	49.2	1241.17		500		
16:29	7.17	0.47	12.06	47.0	1232.26		500		
16:30	7.16	0.48	12.06	44.5	1228.11		500		
16:31	7.17	0.49	12.10	41.3	1225.29		500		
16:32	7.17	0.50	12.06	37.9	1228.15		500		
16:33	7.17	0.50	12.12	33.9	1230.03		500		
16:34	7.17	0.50	12.06	29.8	1235.80		500		
MINUTES									TOTAL LITERS
18.0	0.01	1.16%	0.00%	-8.18	0.62%				9.00

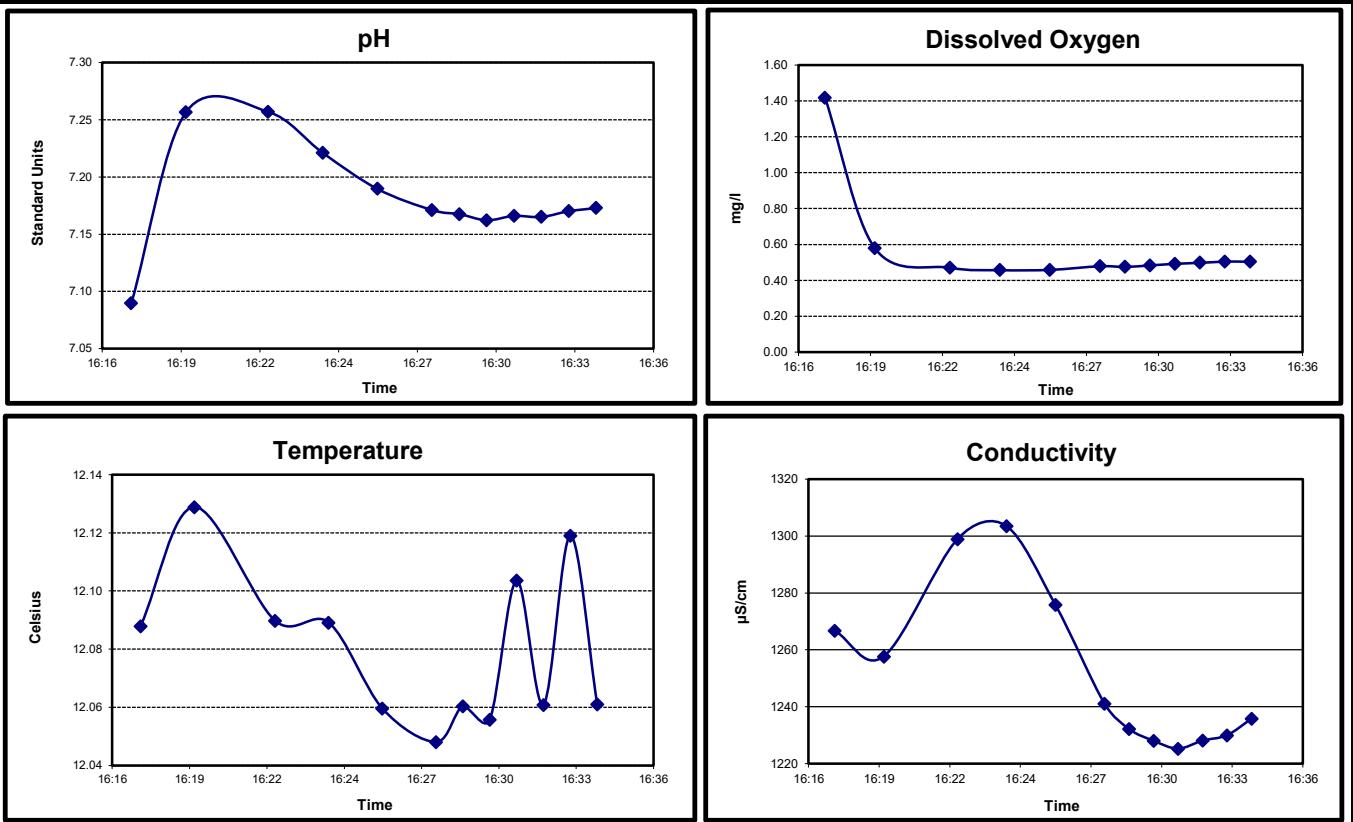


Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-117D
Casing Stickup (Ft.)	-0.3	Purge Method	Low Flow Micro Purge	Container 40 mL VOA Vial	Sample Date 13-Nov-20
Total Well Depth (Ft.) TOC	200.2	Purge Equip	QED Air Diaphragm	Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	3.42	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	197.08	Field Analysis Equip	YSI 556 MSP	Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
15:53									
15:54	7.22	1.53	12.22	70.3	1326.72	19	500	3.42	clear
15:55	7.22	1.50	12.20	68.9	1326.68	19	500		
15:56	7.21	1.49	12.20	68.0	1327.04	19	500		
15:57	7.21	1.45	12.22	66.6	1326.22	19	500		
15:59	7.21	1.41	12.19	64.7	1327.18	19	500		
16:01	7.22	1.38	12.15	62.6	1327.79	19	500		
16:02	7.21	1.37	12.13	62.7	1327.91	19	500	3.42	clear
16:03	7.19	1.38	12.09	62.9	1327.58	19	500		
16:04	7.18	1.38	12.14	62.9	1325.77	19	500		
16:05	7.18	1.36	12.12	62.4	1326.75	19	500		
16:06	7.18	1.32	12.13	62.3	1326.61	19	500		
16:07	7.18	1.34	12.11	61.7	1327.12	19	500		
MINUTES									TOTAL LITERS
14.0	0.00	-1.74%	-0.05%	-0.68	0.03%				7.00

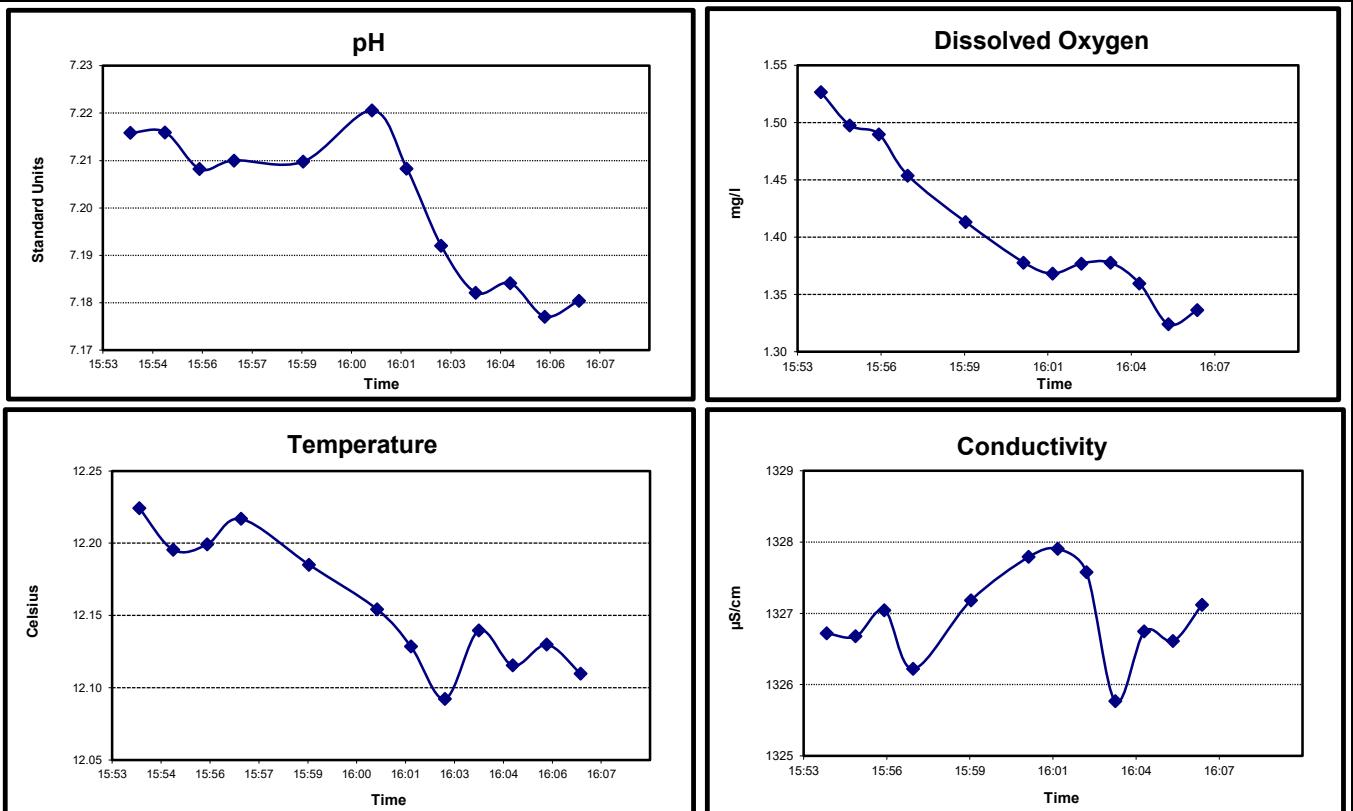


Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-119
Casing Stickup (Ft.)	3.25	Purge Method		Container 40 mL VOA Vial	Sample Date 14-Nov-20
Total Well Depth (Ft.) TOC	62.41	Purge Equip QED Air Diaphragm		Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	22.92	Field Analysis Method Flow Thru Analysis - 250 mL		Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	36.24	Field Analysis Equip YSI 556 MSP		Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond μS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
10:48									
10:49	7.23	14.81	7.52	204.1	11.67	81	350	22.98	slightly cloudy
10:51	7.31	7.21	10.94	202.3	1216.67		350		
10:54	7.49	3.63	11.03	184.2	1262.29		350		
10:56	7.48	3.32	11.06	183.3	1272.28		350		
10:57	7.47	3.27	11.04	183.2	1275.06		350		
10:58	7.45	3.24	11.09	183.4	1275.15		350		
10:59	7.45	3.21	11.06	183.1	1277.49		350	23.12	slightly cloudy
11:00	7.45	3.20	11.05	182.8	1278.40		350		
11:01	7.44	3.18	11.04	182.8	1278.57		350		
11:02	7.43	3.15	11.06	182.9	1278.11		350		
11:03	7.43	3.09	11.05	182.4	1278.79		350	23.18	clear
11:04	7.43	3.11	11.01	181.9	1279.61		350		
MINUTES									TOTAL LITERS
16.0	0.00	-1.34%	-0.48%	-1.02	0.12%			5.60	

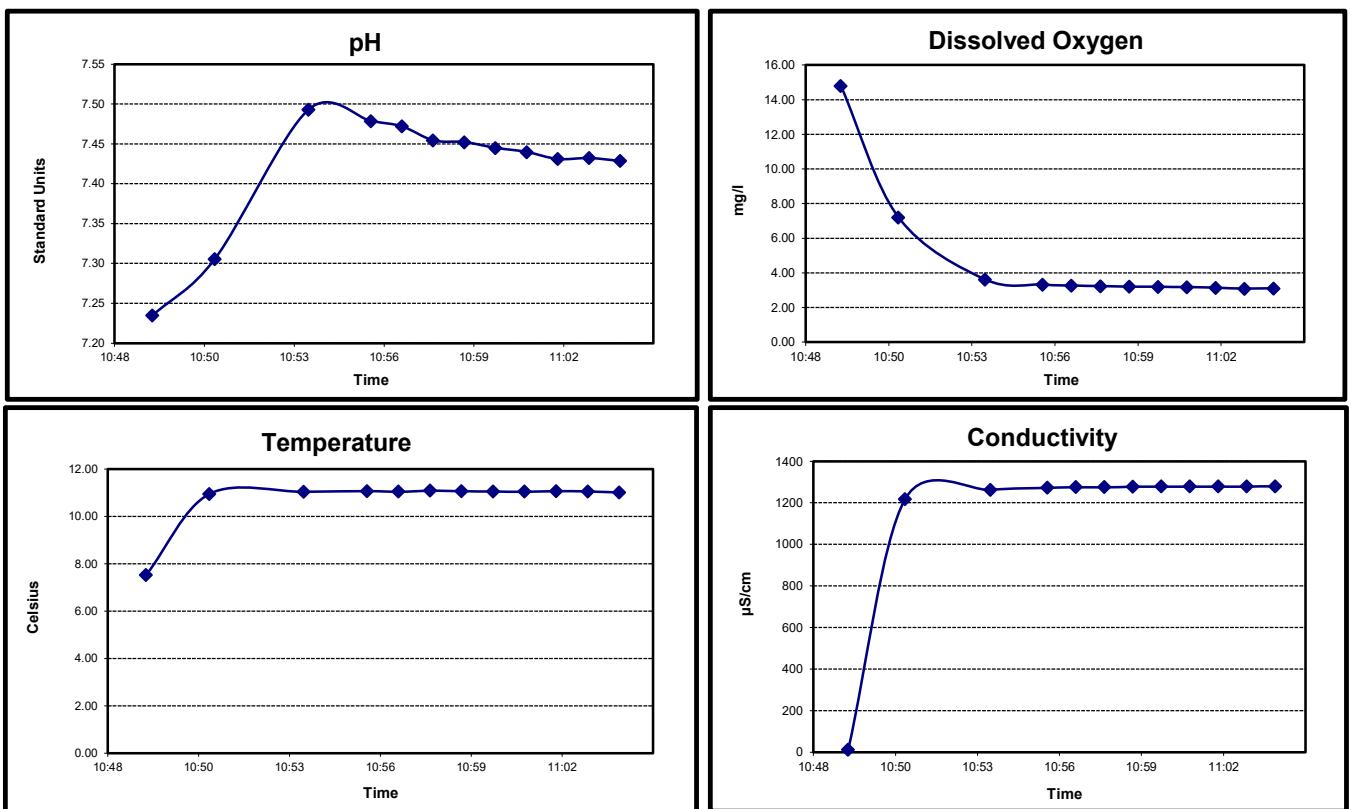





Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW-121
Casing Stickup (Ft.)	2.53	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	15-Nov-20
Total Well Depth (Ft.) TOC	67.55	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	20.31	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	
Water Thickness (Ft.)	44.71	Field Analysis Equip	YSI 556 MSP	Sampling Period	FALL 20		None

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
15:55									
15:56	7.34	5.53	11.87	215.2	1317.11	97	410		
15:58	7.40	3.25	11.95	206.8	1321.61		410		
16:01	7.39	2.21	11.99	204.2	1322.79		410		
16:04	7.37	2.08	11.98	203.0	1322.53		410		
16:07	7.36	2.08	11.96	201.7	1322.04		410		
16:08	7.35	2.07	11.95	201.3	1322.24		410		
16:09	7.35	2.08	11.95	200.8	1321.91		410		
16:10	7.35	2.07	11.96	200.4	1321.51		410		
16:11	7.34	2.09	11.94	200.0	1322.19		410		
16:12	7.35	2.11	11.96	199.2	1321.44		410		
16:13	7.33	2.07	11.97	198.9	1321.17		410		
16:14	7.35	2.08	11.94	198.3	1321.66		410		
MINUTES									TOTAL LITERS
19.0	0.00	-1.47%	-0.11%	-0.89	0.02%				7.79

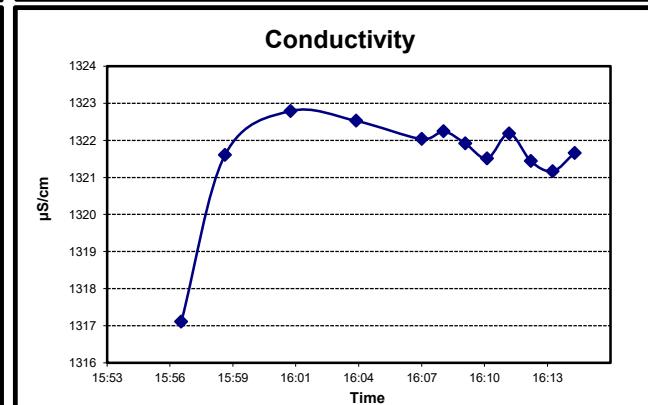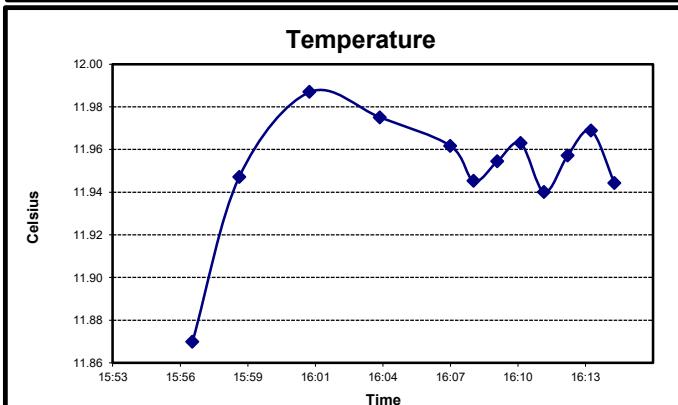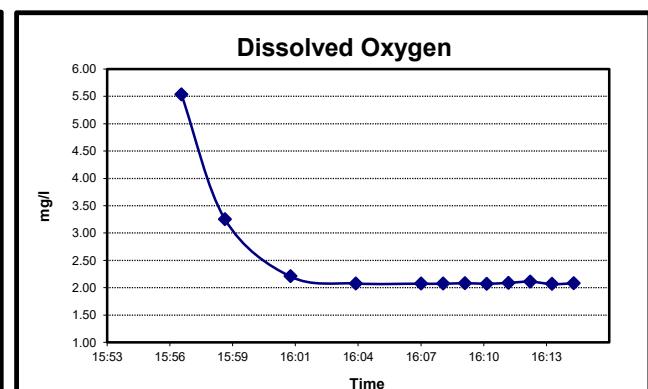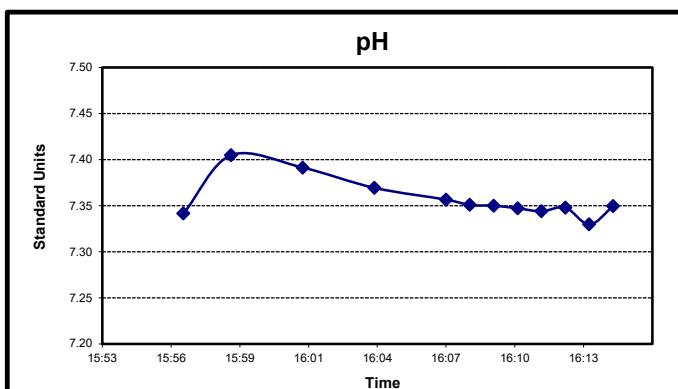


Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-124
Casing Stickup (Ft.)	2.17	Purge Method		Container 40 mL VOA Vial	Sample Date 18-Nov-20
Total Well Depth (Ft.) TOC	102.76	Purge Equip QED Air Diaphragm		Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	33.18	Field Analysis Method Flow Thru Analysis - 250 mL		Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	67.41	Field Analysis Equip YSI 556 MSP		Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
12:49									
12:50	7.36	1.41	12.40	85.4	1295.14	46	400	33.2	slightly cloudy
12:52	7.46	0.87	12.42	34.3	1250.95		400		
12:55	7.48	0.49	12.42	-10.3	1245.91		400		
12:58	7.44	0.39	12.44	-29.3	1279.50		400	33.36	slightly cloudy
13:01	7.43	0.30	12.41	-44.5	1303.08		400		
13:02	7.42	0.30	12.40	-46.0	1307.97		400		
13:03	7.42	0.30	12.40	-47.5	1312.71		400		
13:04	7.40	0.29	12.41	-48.1	1317.80		400		
13:05	7.41	0.28	12.40	-49.5	1323.19		400		
13:06	7.39	0.28	12.41	-49.7	1328.95		400		
13:07	7.40	0.28	12.39	-52.1	1336.87		400	33.42	slightly cloudy
13:08	7.38	0.29	12.40	-53.5	1339.79		400		
MINUTES									TOTAL LITERS
19.0	-0.01	1.57%	-0.12%	-3.85	0.81%			7.60	

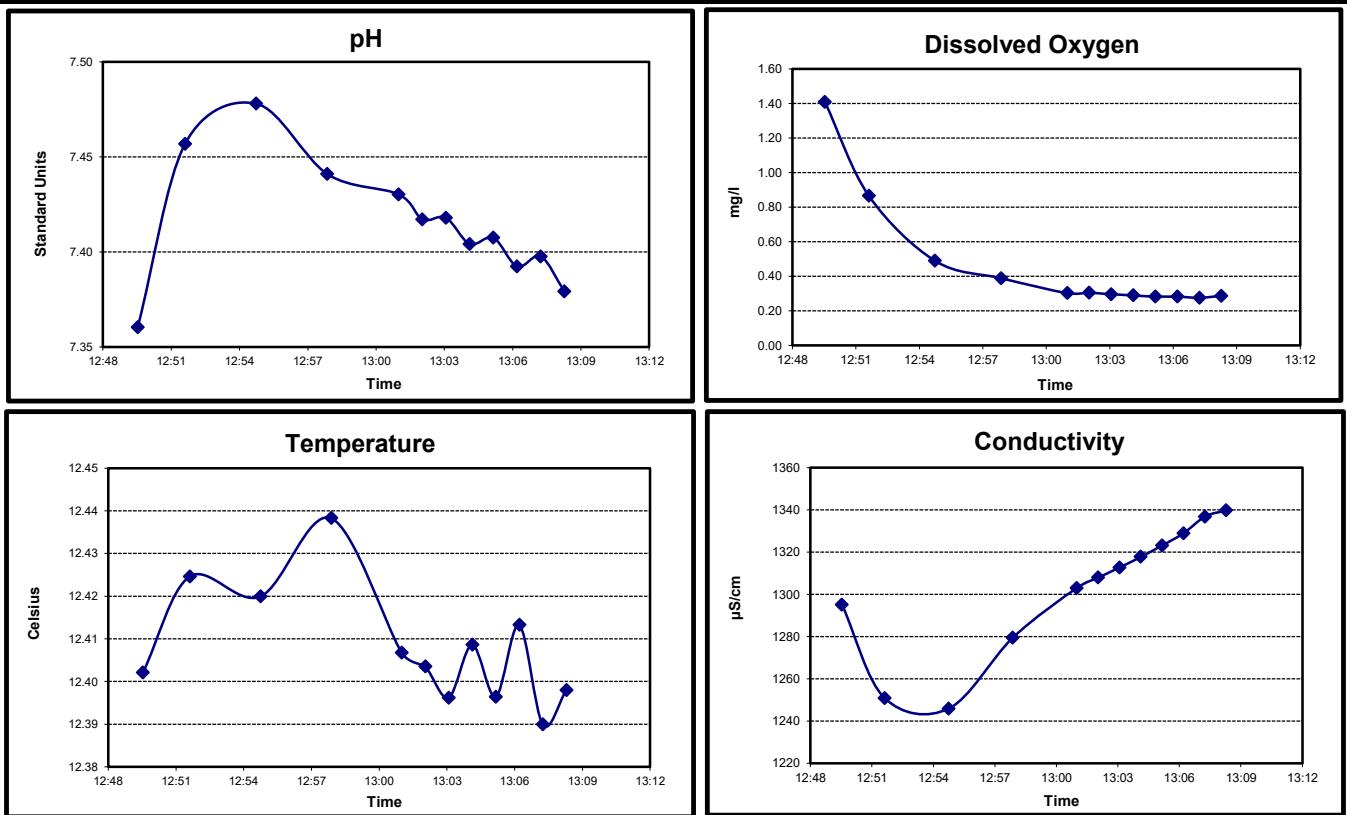


Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-130
Casing Stickup (Ft.)	-0.3	Purge Method	Low Flow Micro Purge	Container 40 mL VOA Vial	Sample Date 17-Nov-20
Total Well Depth (Ft.) TOC	38.17	Purge Equip	QED Air Diaphragm	Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	19.94	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	18.53	Field Analysis Equip	YSI 556 MSP	Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
16:14									
16:15	7.62	5.03	11.55	143.8	1282.85	89	390	19.98	slightly cloudy
16:17	7.36	2.57	11.69	140.8	1246.94		390		
16:20	7.27	2.36	11.80	133.7	1243.33		390		
16:23	7.27	2.51	11.81	125.5	1251.78		390	20.05	clear
16:24	7.27	2.48	11.83	123.0	1253.89		390		
16:25	7.28	2.55	11.81	120.3	1256.09		390		
16:26	7.28	2.57	11.83	117.9	1257.22		390		
16:27	7.28	2.61	11.82	115.4	1257.95		390		
16:28	7.28	2.60	11.84	113.3	1258.85		390		
16:31	7.29	2.73	11.83	107.3	1260.79		390		
16:32	7.29	2.68	11.85	105.7	1261.23		390	20.14	
16:33	7.29	2.77	11.83	104.1	1261.65		390		
MINUTES									TOTAL LITERS
19.0	0.00	1.62%	0.03%	-3.20	0.07%				7.41

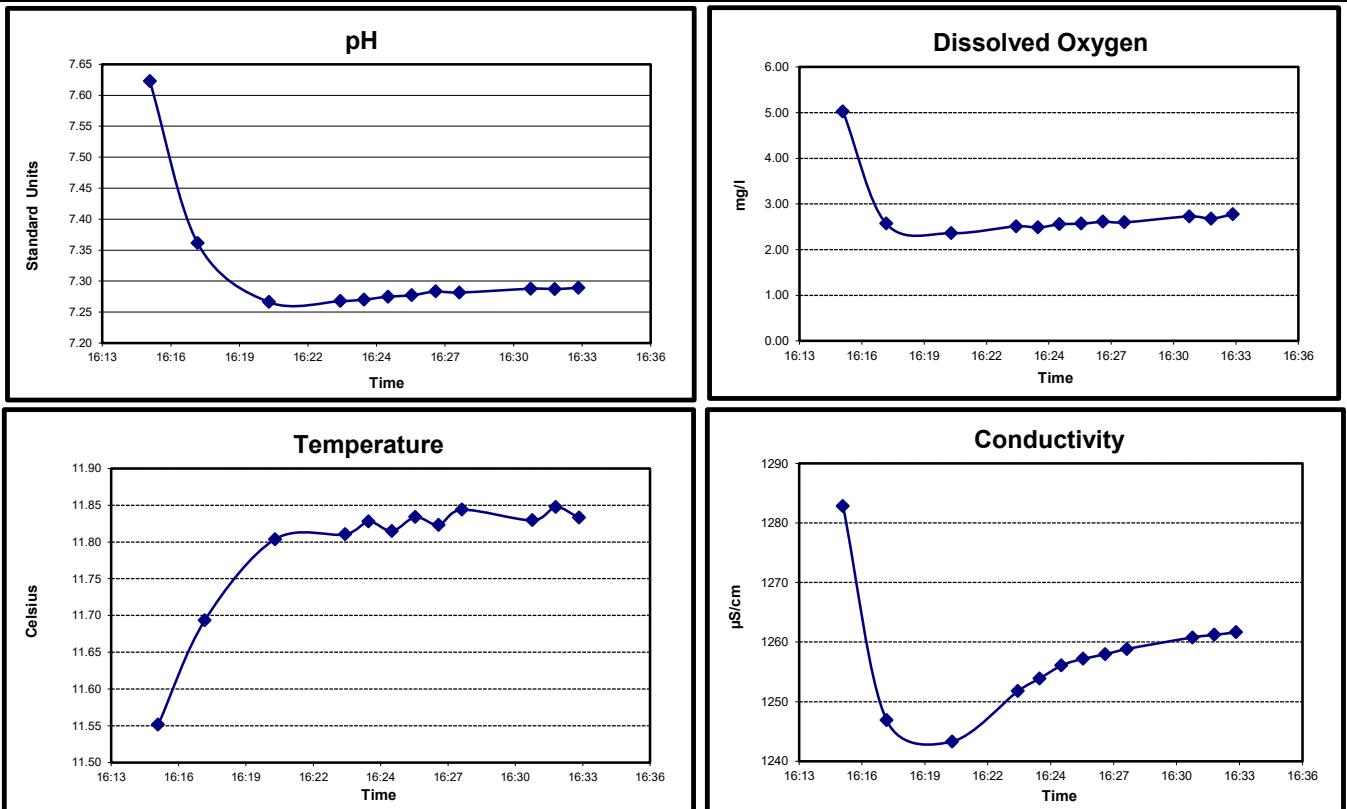


Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-133A
Casing Stickup (Ft.)	2.3	Purge Method		Container 40 mL VOA Vial	Sample Date 18-Nov-20
Total Well Depth (Ft.) TOC	37.85	Purge Equip QED Air Diaphragm		Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	27.53	Field Analysis Method Flow Thru Analysis - 250 mL		Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	8.02	Field Analysis Equip YSI 556 MSP		Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
10:50									
10:51	7.45	7.98	10.14	181.4	752.71	38	400	27.56	clear
10:53	7.46	8.22	10.13	180.1	752.89		400		
10:56	7.45	8.50	10.07	179.2	752.15		400		
10:59	7.44	8.63	10.10	179.5	753.22		400		
11:00	7.45	8.68	10.04	178.9	752.70		400	27.61	clear
11:01	7.44	8.74	10.03	178.8	752.22		400		
11:02	7.41	8.71	10.09	180.1	751.78		400		
11:03	7.40	8.69	10.15	180.7	752.91		400		
11:04	7.42	8.66	10.18	179.4	753.41		400		
11:07	7.44	8.79	10.14	177.8	753.33		400		
11:08	7.44	8.78	10.14	178.0	753.75		400	27.64	clear
11:09	7.43	8.81	10.13	177.9	754.17		400		
MINUTES									
19.0	-0.01	0.15%	-0.01%	0.16	0.11%			7.60	
TOTAL LITERS									

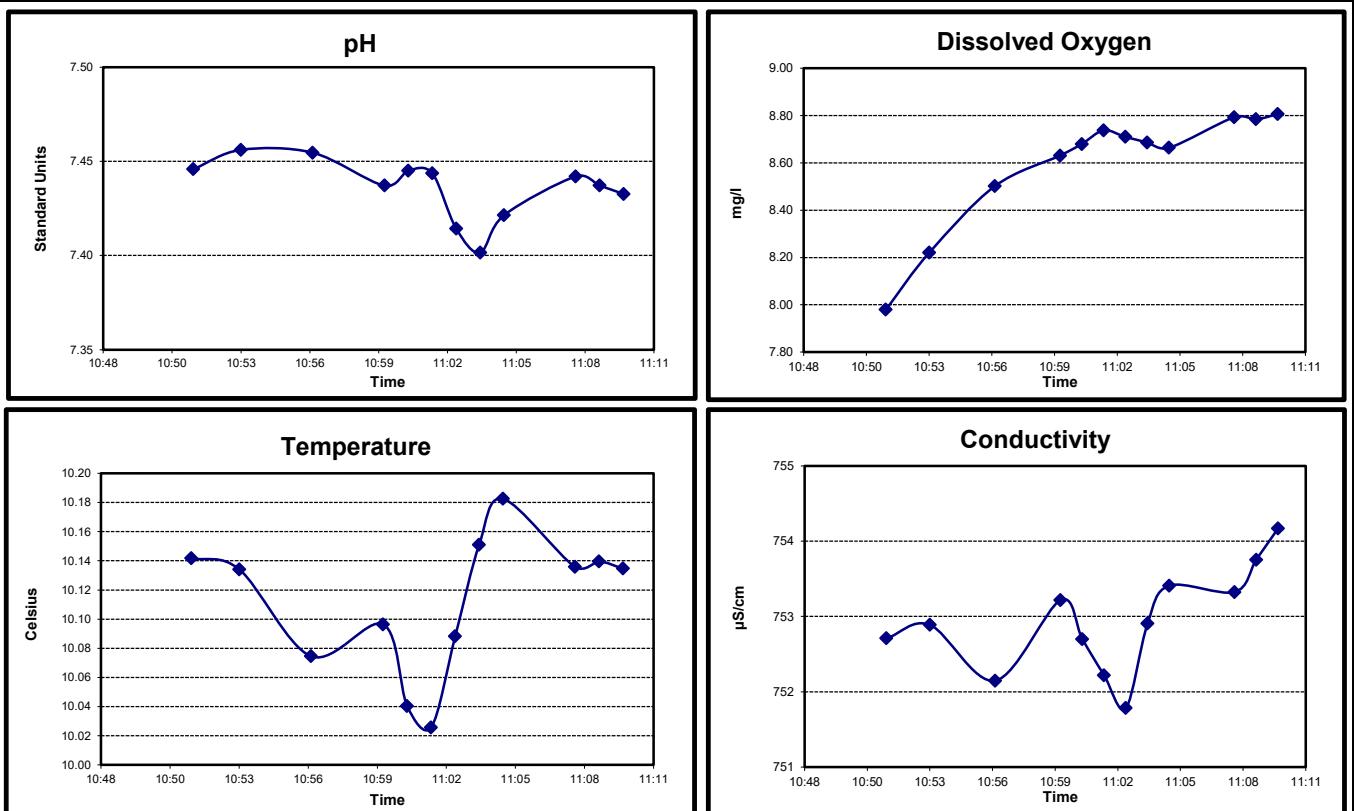





Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-133B
Casing Stickup (Ft.)	2.51	Purge Method		Container 40 mL VOA Vial	Sample Date 18-Nov-20
Total Well Depth (Ft.) TOC	61.49	Purge Equip QED Air Diaphragm		Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	25.62	Field Analysis Method Flow Thru Analysis - 250 mL		Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	33.36	Field Analysis Equip YSI 556 MSP		Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
11:31									
11:32	7.32	4.93	10.14	173.7	1091.28	67	420	25.65	slightly cloudy
11:34	7.40	4.85	10.11	168.9	1090.85		420		
11:37	7.37	4.83	10.16	166.7	1091.47		420		
11:40	7.35	4.80	10.19	165.8	1091.42		420		
11:43	7.35	4.84	10.16	163.7	1091.84		420		
11:44	7.34	4.83	10.18	163.4	1091.87		420		
11:45	7.35	4.83	10.16	162.2	1091.64		420		
11:46	7.34	4.82	10.14	162.2	1091.15		420		
11:47	7.33	4.84	10.15	162.3	1090.86		420		
11:48	7.34	4.79	10.19	161.8	1090.73		420		
11:49	7.35	4.81	10.16	160.8	1090.62		420	25.73	slightly cloudy
11:50	7.34	4.81	10.12	160.9	1090.51		420		
MINUTES									TOTAL LITERS
19.0	0.00	0.41%	-0.67%	-0.87	-0.02%				7.98

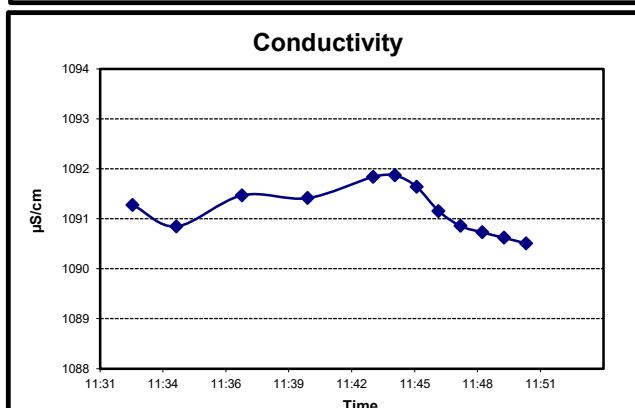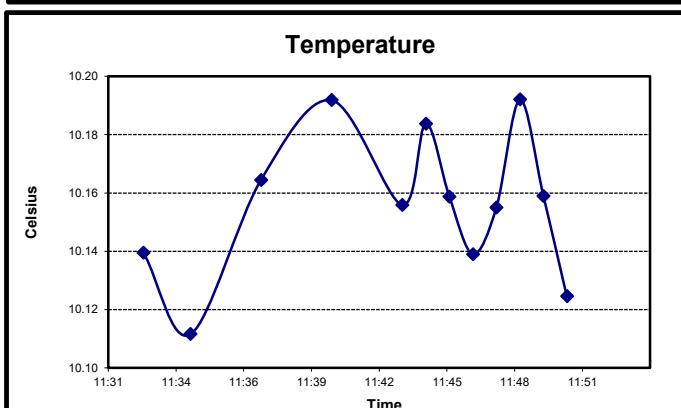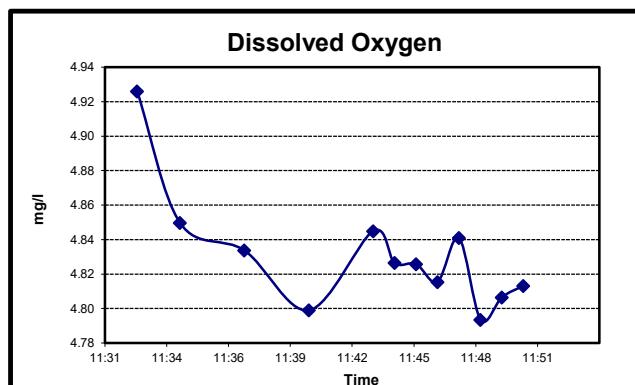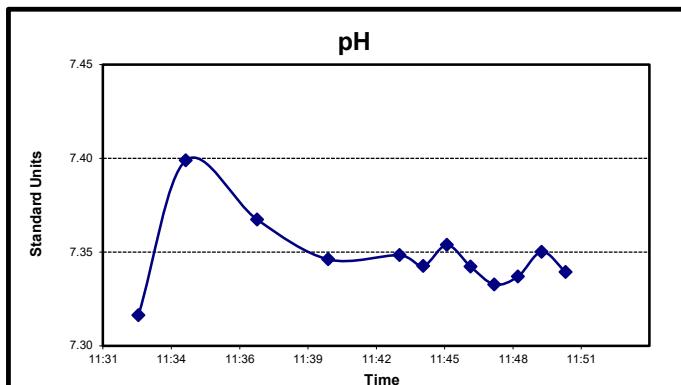





Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-133C
Casing Stickup (Ft.)	2.37	Purge Method		Container 40 mL VOA Vial	Sample Date 18-Nov-20
Total Well Depth (Ft.) TOC	98.49	Purge Equip QED Air Diaphragm		Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	21.52	Field Analysis Method Flow Thru Analysis - 250 mL		Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	74.60	Field Analysis Equip YSI 556 MSP		Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
12:06									
12:07	7.35	1.13	10.46	148.8	810.74	38	430		
12:09	7.32	1.62	10.40	148.7	839.22		430		
12:12	7.32	2.22	10.39	147.1	880.50		430		
12:15	7.34	2.61	10.39	144.1	906.73		430		
12:18	7.33	2.98	10.39	143.5	927.85		430		
12:19	7.33	3.02	10.40	143.3	932.70		430		
12:20	7.34	3.13	10.39	142.3	937.84		430		
12:21	7.33	3.16	10.40	142.3	939.85		430		
12:22	7.35	3.19	10.39	141.2	944.23		430		
12:23	7.33	3.24	10.39	141.5	947.60		430		
12:24	7.33	3.32	10.38	141.7	949.70		430		
12:25	7.32	3.33	10.41	141.4	950.79		430	21.64	clear
MINUTES						TOTAL LITERS			
19.0	-0.02	2.85%	0.16%	-0.16	0.33%	8.17			

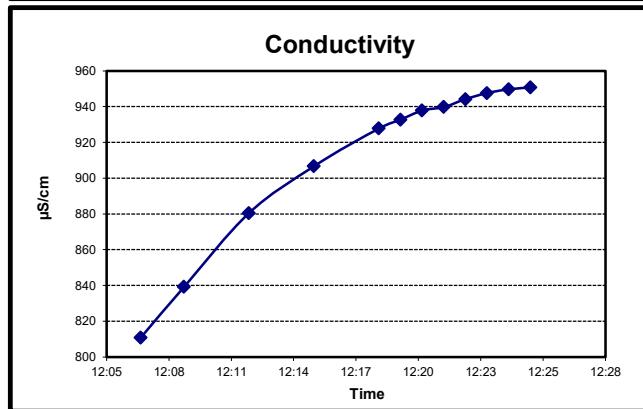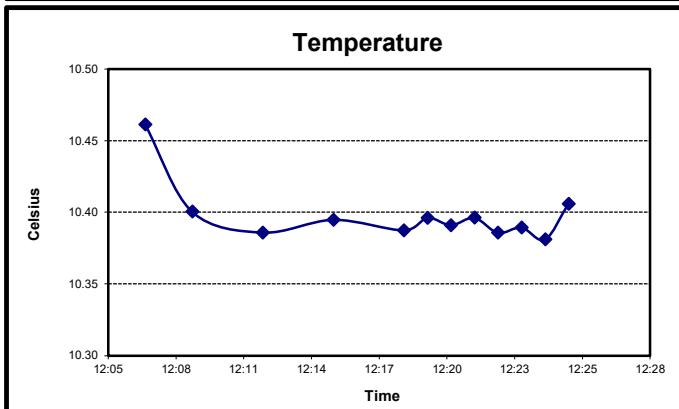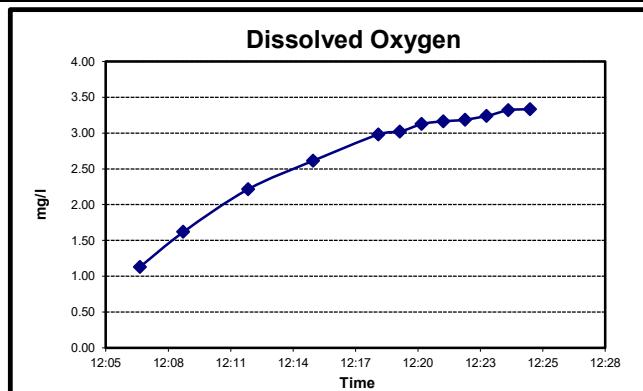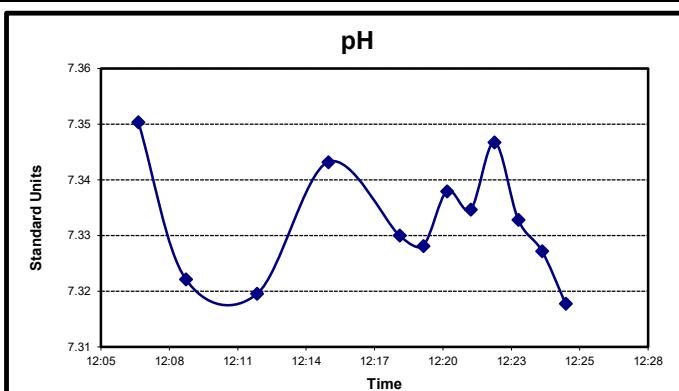


Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-136
Casing Stickup (Ft.)	-0.42	Purge Method	Low Flow Micro Purge	Container 40 mL VOA Vial	Sample Date 14-Nov-20
Total Well Depth (Ft.) TOC	44.33	Purge Equip	QED Air Diaphragm	Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	34.32	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	10.43	Field Analysis Equip	YSI 556 MSP	Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
13:26									
13:27	7.30	5.13	11.34	180.6	1155.93	52	400	34.35	slightly cloudy
13:29	7.26	5.66	11.34	182.5	1183.91		400		
13:32	7.23	5.97	11.36	184.7	1231.88		400		
13:35	7.22	6.13	11.38	185.8	1254.17		400		
13:37	7.22	6.21	11.36	186.5	1266.72		400		
13:39	7.21	6.31	11.36	187.1	1271.57		400		
13:40	7.21	6.30	11.38	187.3	1274.35		400		
13:41	7.21	6.29	11.37	187.6	1278.27		400		
13:42	7.21	6.32	11.36	187.7	1280.54		400		
13:43	7.21	6.36	11.36	187.8	1282.48		400	34.42	clear
13:44	7.21	6.37	11.35	188.2	1284.42		400		
13:45	7.22	6.36	11.33	188.5	1286.00		400		
MINUTES									TOTAL LITERS
19.0	0.01	-0.04%	-0.18%	0.66	0.27%				7.60

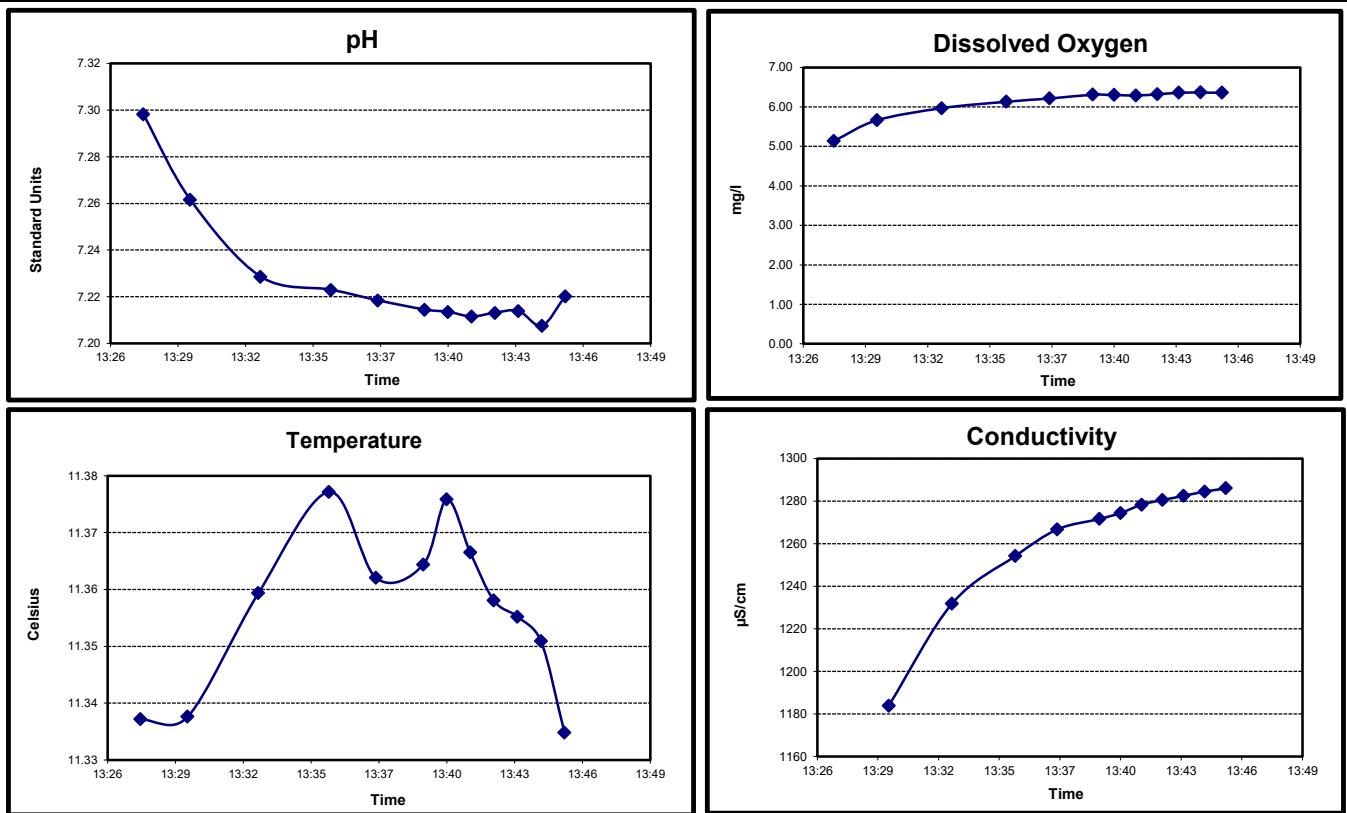


Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-200
Casing Stickup (Ft.)	1.15	Purge Method		Container 40 mL VOA Vial	Sample Date 17-Nov-20
Total Well Depth (Ft.) TOC	89.93	Purge Equip QED Air Diaphragm		Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	45.38	Field Analysis Method Flow Thru Analysis - 250 mL		Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	43.40	Field Analysis Equip YSI 556 MSP		Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
11:05									
11:06	7.16	7.88	11.21	-5.0	1625.45	69	440	45.4	slightly cloudy
11:08	7.30	7.81	11.22	-29.3	1548.01		440		
11:11	7.34	7.33	11.24	-35.2	1496.86		440		
11:14	7.34	6.66	11.28	-33.3	1458.89		440		
11:17	7.34	6.06	11.24	-31.1	1428.01		440		
11:18	7.33	5.89	11.26	-30.1	1420.38		440		
11:19	7.32	5.76	11.26	-29.4	1416.23		440		
11:20	7.32	5.70	11.24	-28.4	1412.48		440		
11:21	7.33	5.61	11.22	-28.0	1410.45		440		
11:22	7.33	5.55	11.24	-27.8	1406.09		440		
11:23	7.33	5.47	11.26	-27.1	1402.26		440		
11:24	7.32	5.39	11.27	-26.3	1397.92		440	45.56	slightly cloudy
MINUTES									TOTAL LITERS
19.0	-0.01	-3.08%	0.28%	1.47	-0.58%				8.36

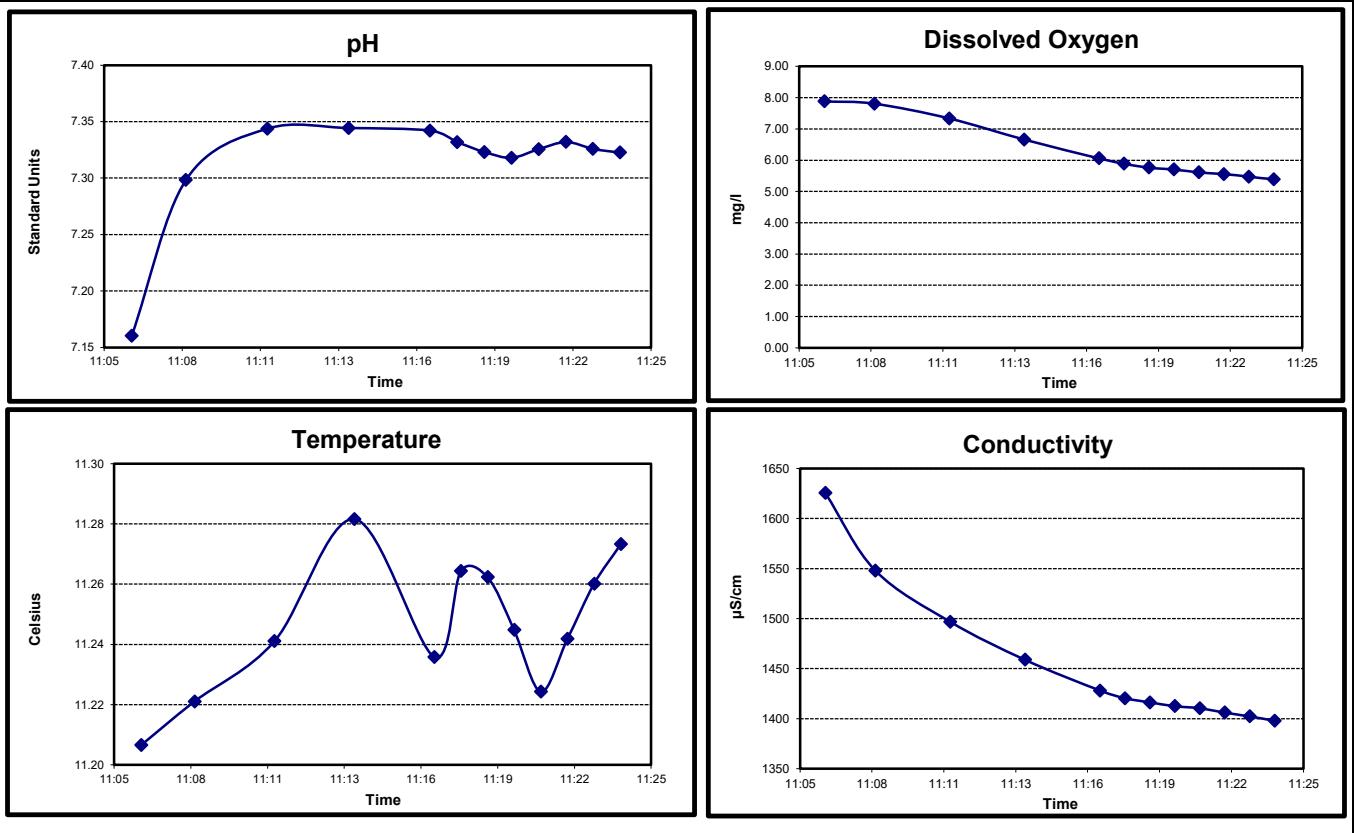


Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-201
Casing Stickup (Ft.)	-0.32	Purge Method	Low Flow Micro Purge	Container 40 mL VOA Vial	Sample Date 15-Nov-20
Total Well Depth (Ft.) TOC	50.15	Purge Equip	QED Air Diaphragm	Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	27.52	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	22.95	Field Analysis Equip	YSI 556 MSP	Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
15:13									
15:14	7.63	13.13	12.81	205.6	1137.41	28	450	27.55	clear
15:15	7.67	13.17	12.74	203.9	1140.11		450		
15:17	7.65	13.29	13.01	205.5	1138.60		450		
15:19	7.71	13.68	13.03	203.2	1140.88		450		
15:20	7.71	13.78	13.04	203.1	1140.28		450		
15:21	7.72	13.87	13.03	203.6	1140.57		450		
15:22	7.70	13.93	13.03	204.6	1141.25		450		
15:24	7.71	13.91	13.08	205.4	1140.74		450		
15:26	7.70	14.07	13.02	206.1	1142.18		450		
15:28	7.71	13.91	13.06	207.0	1142.24		450		
15:30	7.71	13.98	13.05	207.9	1143.61		450		
15:32	7.69	13.84	13.04	208.2	1144.45		450		
MINUTES									TOTAL LITERS
18.0	-0.01	-0.50%	-0.18%	1.25	0.19%				8.10

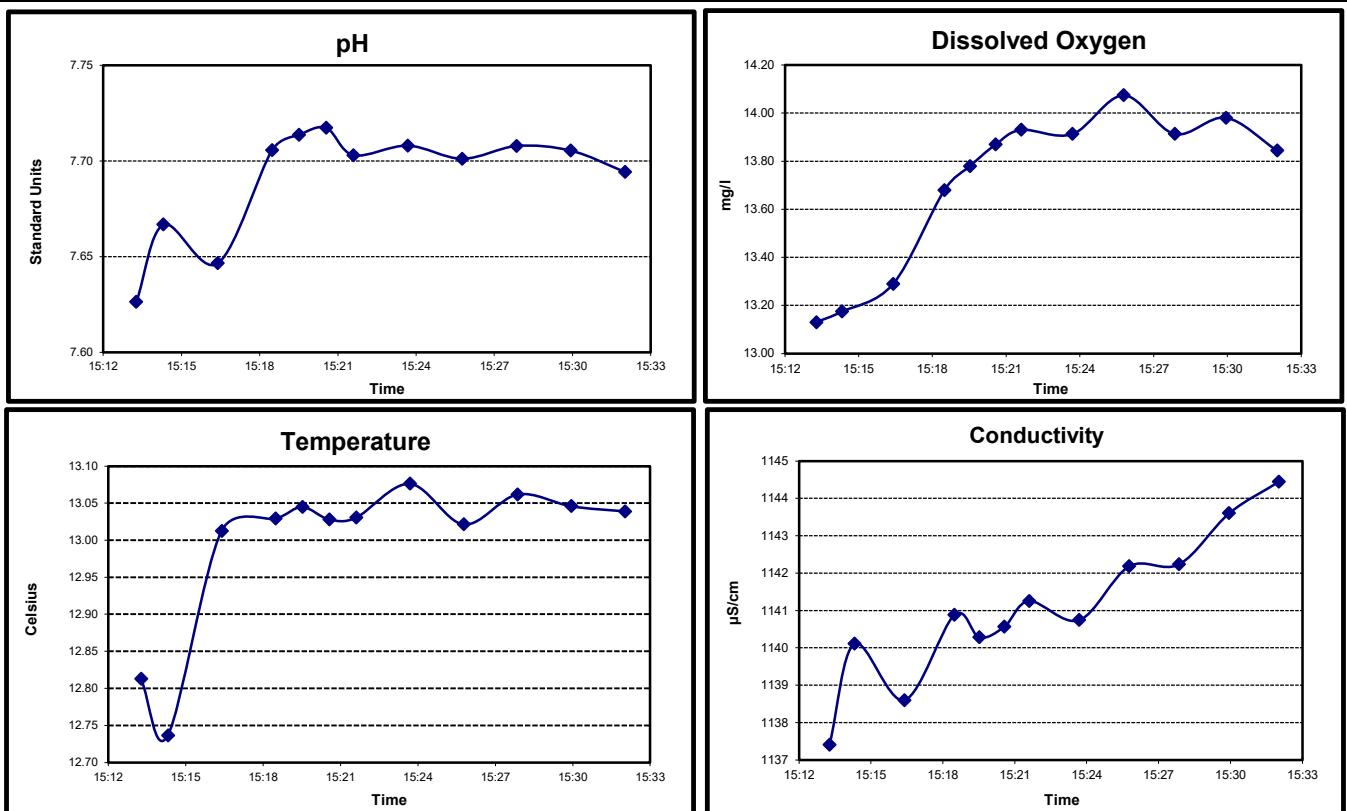

Remarks: (well condition, maintenance, etc...)


FD-1 = field duplicate for MW-201 collected

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-202
Casing Stickup (Ft.)	-0.32	Purge Method	Low Flow Micro Purge	Container 40 mL VOA Vial	Sample Date 15-Nov-20
Total Well Depth (Ft.) TOC	50.01	Purge Equip	QED Air Diaphragm	Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	26.37	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	23.96	Field Analysis Equip	YSI 556 MSP	Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
14:15									
14:16	7.41	1.20	13.21	206.6	1176.57	29	400		
14:17	7.41	1.08	13.18	206.1	1183.50		400	26.4	slightly cloudy
14:19	7.39	1.04	13.25	205.7	1191.66		400		
14:22	7.38	1.06	13.10	202.7	1199.32		400		
14:24	7.37	0.91	13.41	200.8	1196.77		400		
14:27	7.38	0.86	12.88	197.1	1205.17		400	26.49	clear
14:29	7.34	0.79	13.10	196.8	1199.20		400		
14:30	7.36	0.80	13.01	195.1	1200.32		400		
14:31	7.36	0.80	12.84	194.2	1202.04		400		
14:32	7.35	0.79	12.60	193.6	1203.58		400	26.53	clear
14:33	7.30	0.81	12.83	195.5	1194.61		400		
14:34	7.30	0.78	12.78	194.8	1196.55		400		
MINUTES									TOTAL LITERS
19.0	-0.06	-0.46%	1.35%	1.22	-0.59%			7.60	

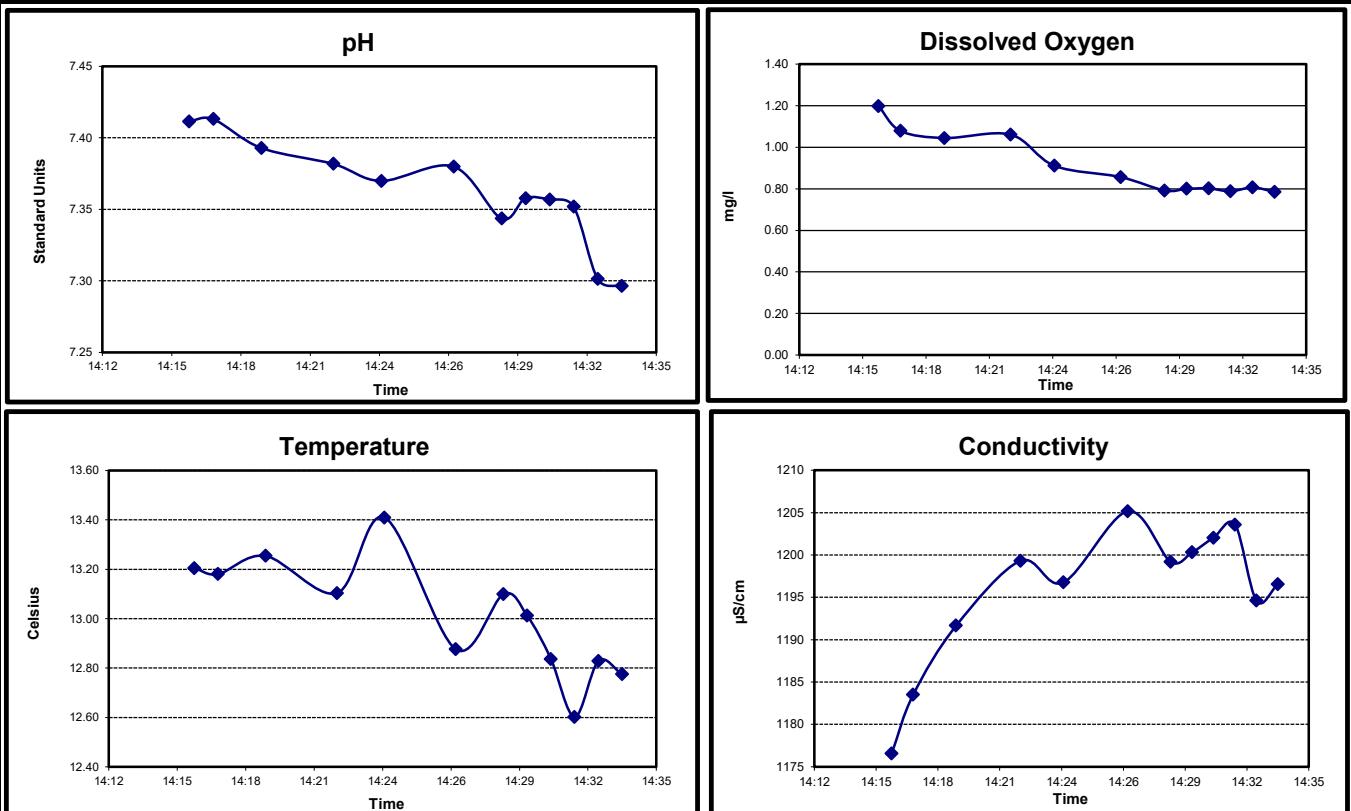





Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-203
Casing Stickup (Ft.)	-0.58	Purge Method	Low Flow Micro Purge	Container 40 mL VOA Vial	Sample Date 15-Nov-20
Total Well Depth (Ft.) TOC	49.35	Purge Equip	QED Air Diaphragm	Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	25.85	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	24.08	Field Analysis Equip	YSI 556 MSP	Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond μS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
12:13									
12:14	7.45	10.03	12.88	184.7	596.29	37	300	25.9	slightly cloudy
12:16	7.42	9.79	12.88	187.2	633.62		300		
12:19	7.39	9.80	12.89	190.1	688.87		300		
12:22	7.38	9.69	13.01	192.5	721.44		300		
12:25	7.36	9.25	12.97	194.4	744.01		300		
12:26	7.34	9.11	12.93	195.6	750.43		300		
12:27	7.33	9.13	13.01	195.9	755.92		300		
12:28	7.33	9.11	12.90	196.6	760.77		300		
12:29	7.32	9.01	12.97	197.1	764.70		300		
12:30	7.33	9.07	12.96	197.5	770.05		300		
12:31	7.31	9.03	12.92	198.1	775.72		300	25.98	clear
12:32	7.33	8.93	12.91	197.9	779.64		300		
MINUTES									
19.0	0.00	-1.55%	-0.44%	0.42	1.23%		5.70		
TOTAL LITERS									

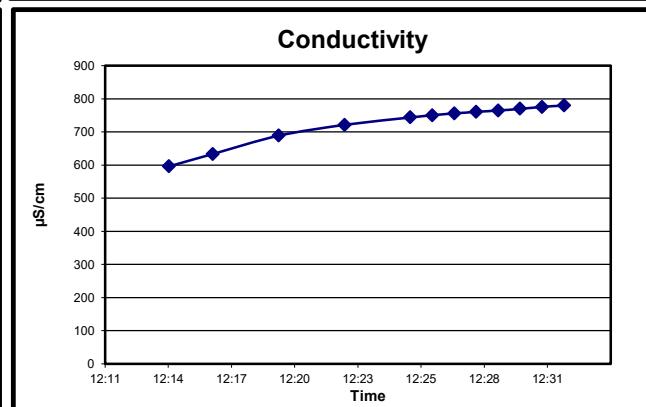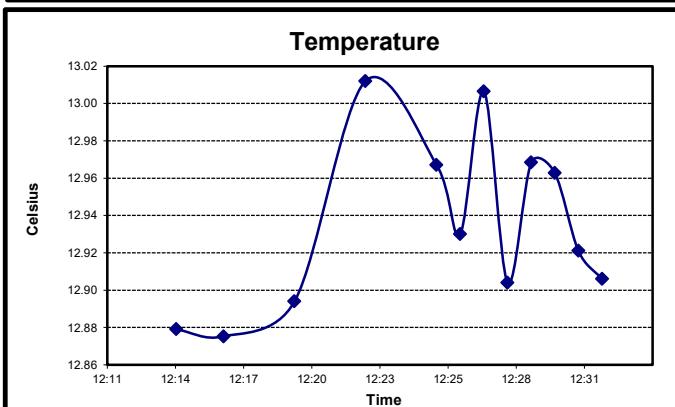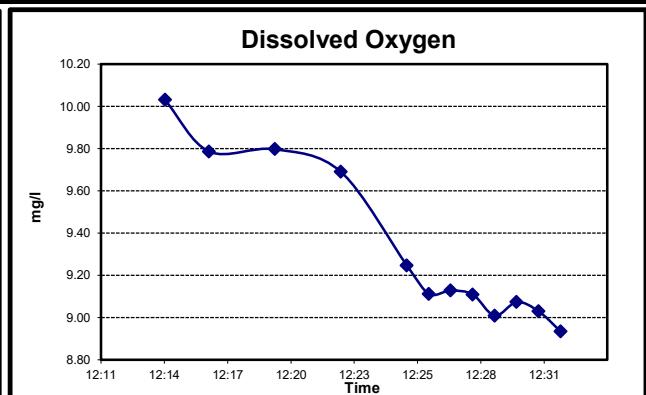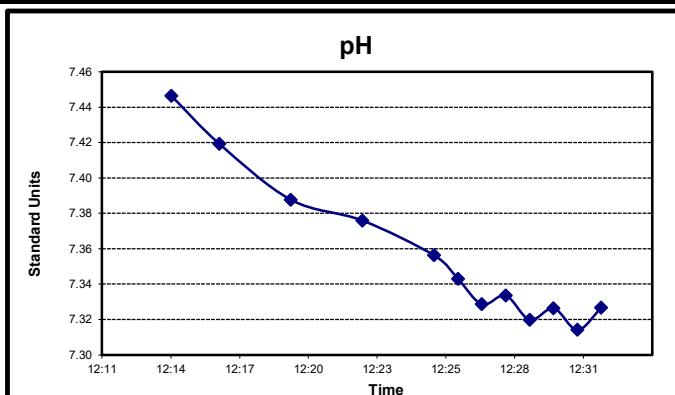


Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-204
Casing Stickup (Ft.)	-0.39	Purge Method	Low Flow Micro Purge	Container 40 mL VOA Vial	Sample Date 17-Nov-20
Total Well Depth (Ft.) TOC	88.96	Purge Equip	QED Air Diaphragm	Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	26.25	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	63.10	Field Analysis Equip	YSI 556 MSP	Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
8:27									
8:28	7.59	3.76	12.05	131.9	1137.00	75	450	26.3	slightly cloudy
8:30	7.54	1.29	12.12	129.9	1141.07		450		
8:33	7.49	0.92	12.21	128.2	1140.71		450		
8:36	7.46	0.92	12.16	127.1	1141.80		450		
8:39	7.43	0.85	12.20	125.9	1140.73		450		
8:40	7.42	0.85	12.20	125.7	1140.95		450		
8:41	7.42	0.81	12.25	125.0	1140.10		450		
8:42	7.41	0.83	12.23	124.6	1140.45		450		
8:43	7.41	0.80	12.22	124.0	1140.54		450		
8:44	7.41	0.81	12.18	123.5	1141.60		450		
8:45	7.40	0.81	12.17	122.9	1141.13		450	26.45	clear
8:46	7.39	0.79	12.18	122.7	1140.38		450		
MINUTES									TOTAL LITERS
19.0	-0.01	-2.71%	0.00%	-0.72	-0.11%			8.55	

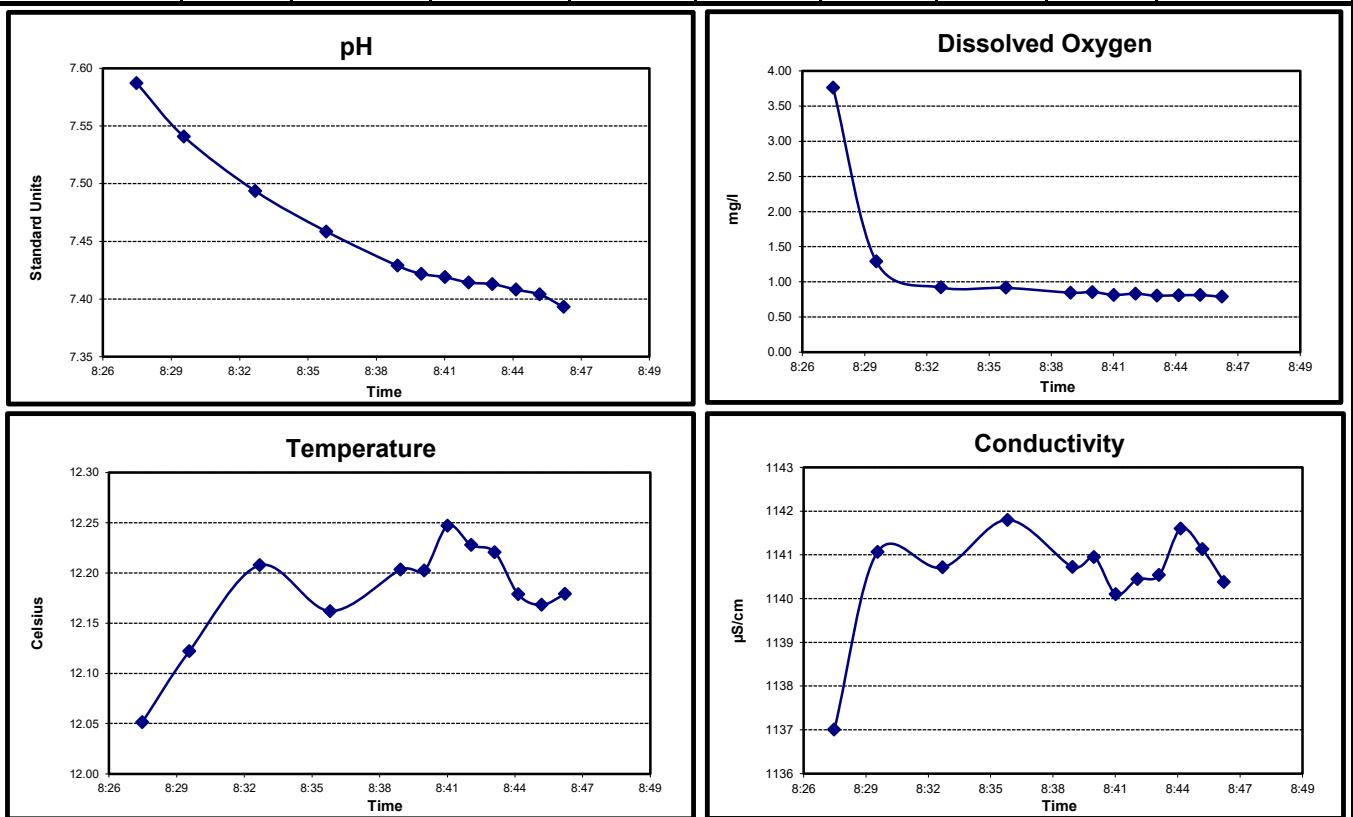


Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-205A
Casing Stickup (Ft.)	3.15	Purge Method		Container 40 mL VOA Vial	Sample Date 13-Nov-20
Total Well Depth (Ft.) TOC	110.27	Purge Equip QED Air Diaphragm		Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	5.38	Field Analysis Method Flow Thru Analysis - 250 mL		Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	101.74	Field Analysis Equip YSI 556 MSP		Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
14:13									
14:14	7.35	1.38	12.24	32.8	1297.13	25	480	5.38	clear
14:16	7.35	1.06	12.31	26.3	1300.34		480		
14:19	7.33	1.01	12.42	20.6	1305.36		480		
14:22	7.31	0.88	12.41	17.4	1311.12		480		
14:25	7.28	0.76	12.47	14.5	1312.88		480		
14:27	7.29	0.71	12.43	10.9	1315.64		480	5.39	clear
14:28	7.28	0.69	12.40	10.5	1316.84		480		
14:29	7.27	0.68	12.41	10.0	1316.90		480		
14:30	7.26	0.65	12.44	9.2	1316.23		480		
14:31	7.27	0.66	12.42	8.0	1317.24		480		
14:32	7.27	0.65	12.45	7.8	1317.17		480	5.4	clear
14:33	7.26	0.63	12.46	9.0	1316.95		480		
MINUTES									TOTAL LITERS
20.0	-0.01	-4.57%	0.34%	1.00	-0.02%				9.60

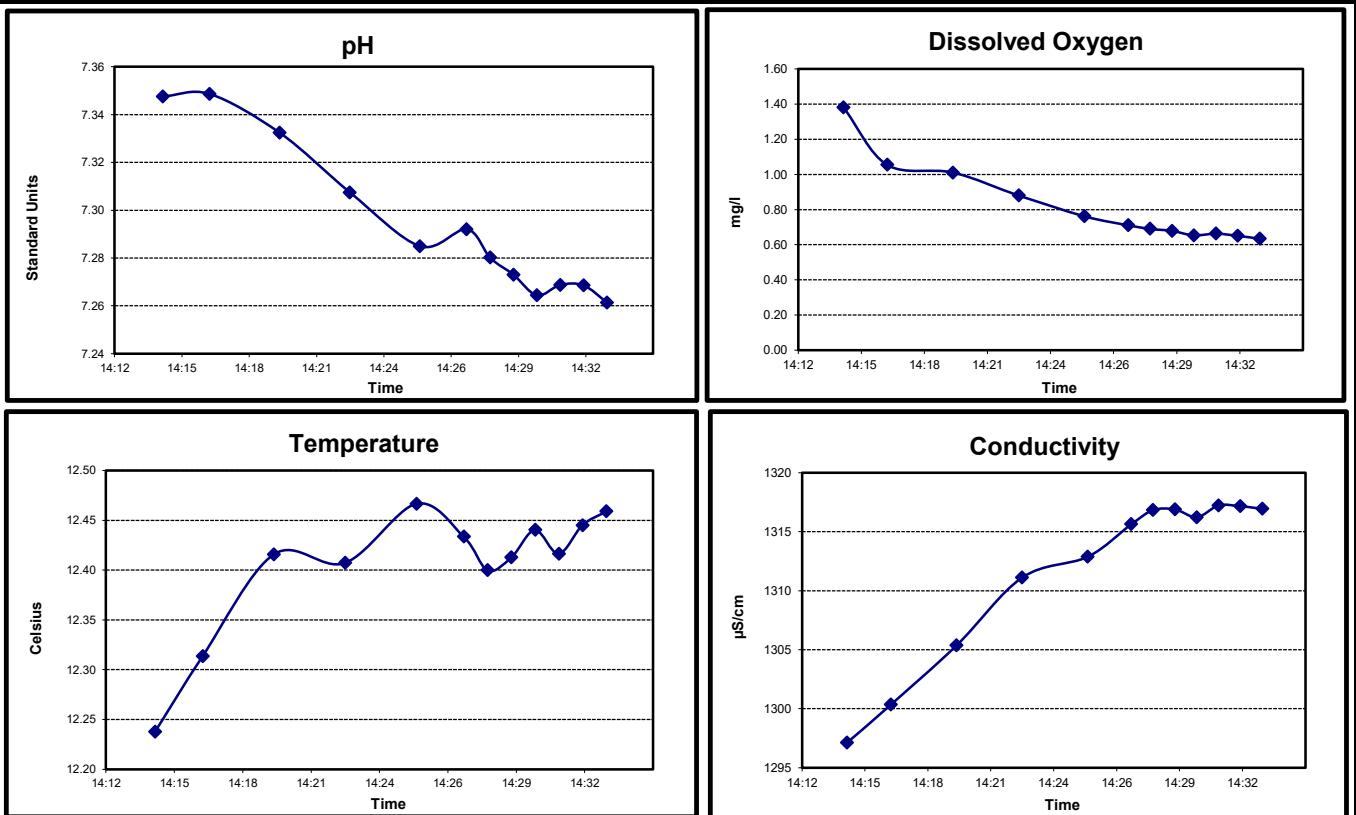





Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-205B
Casing Stickup (Ft.)	3.5	Purge Method		Container 40 mL VOA Vial	Sample Date 13-Nov-20
Total Well Depth (Ft.) TOC	150.05	Purge Equip QED Air Diaphragm		Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	5.47	Field Analysis Method Flow Thru Analysis - 250 mL		Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	141.08	Field Analysis Equip YSI 556 MSP		Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
14:59									clear
15:00	7.23	0.98	12.13	12.0	1289.56	23	500	5.47	
15:02	7.25	1.04	12.10	11.1	1290.02		500		
15:05	7.25	0.94	12.11	10.4	1289.46		500		
15:08	7.24	1.13	12.08	12.3	1288.50		500		
15:11	7.25	1.06	12.08	12.4	1288.81		500		
15:12	7.24	0.99	12.11	12.8	1289.21		500	5.47	clear
15:13	7.25	0.93	12.11	12.4	1289.08		500		
15:14	7.26	0.85	12.11	11.0	1288.27		500		
15:15	7.25	0.90	12.12	11.6	1287.80		500		
15:16	7.24	0.97	12.13	12.4	1287.08		500		
15:17	7.24	1.04	12.11	13.1	1287.19		500		
15:18	7.25	1.09	12.11	13.2	1287.48		500		
MINUTES									TOTAL LITERS
19.0	0.00	10.99%	-0.14%	0.80	0.03%				9.50

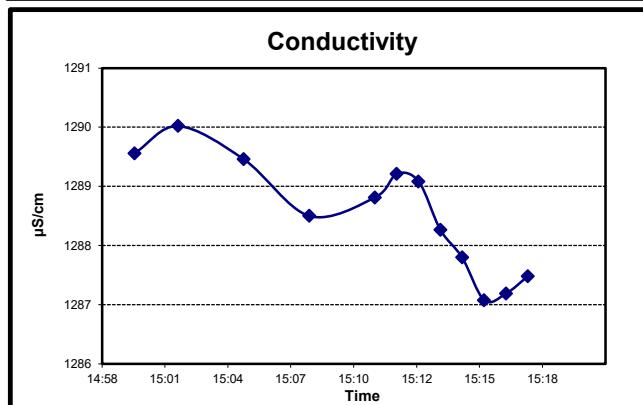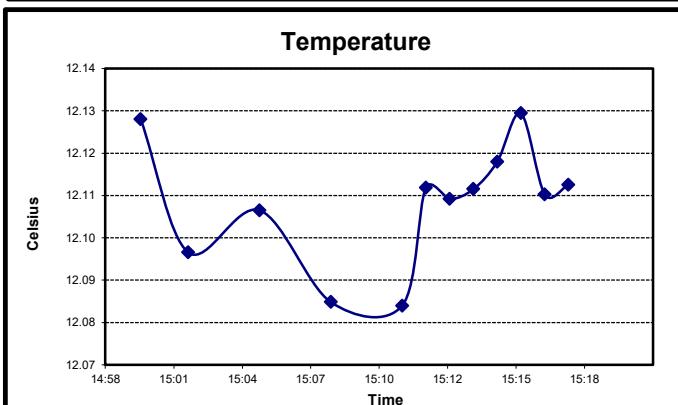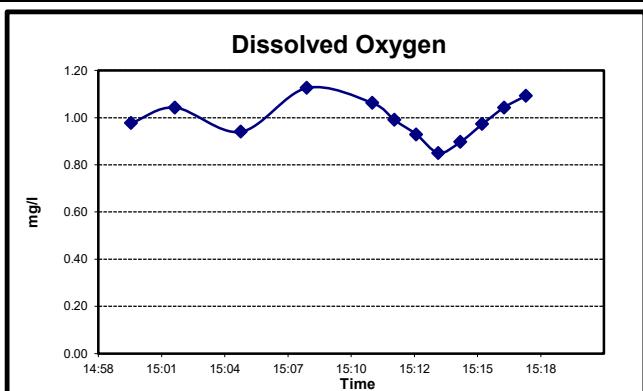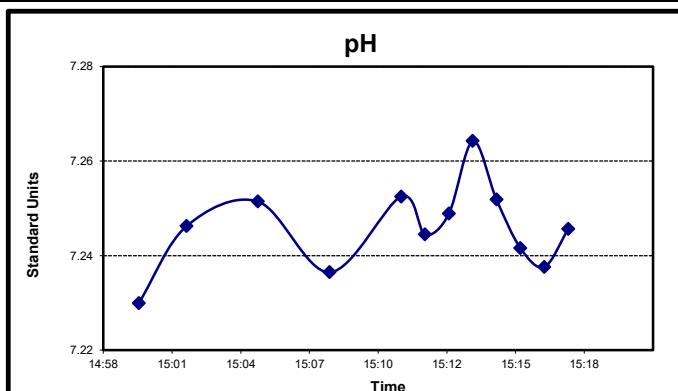





Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-206A
Casing Stickup (Ft.)	3.61	Purge Method		Container 40 mL VOA Vial	Sample Date 13-Nov-20
Total Well Depth (Ft.) TOC	90.24	Purge Equip QED Air Diaphragm		Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	8.35	Field Analysis Method Flow Thru Analysis - 250 mL		Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	78.28	Field Analysis Equip YSI 556 MSP		Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
12:11									cloudy
12:12	7.10	1.57	11.72	-44.7	1256.90	89	500	8.38	
12:14	7.11	1.50	11.72	-51.1	1257.14		500		
12:17	7.14	1.37	11.71	-58.9	1257.39		500		
12:20	7.14	1.29	11.71	-63.6	1257.35		500		
12:23	7.15	1.23	11.72	-67.7	1257.93		500		
12:24	7.16	1.19	11.74	-69.1	1257.72		500		
12:25	7.18	1.18	11.73	-70.9	1257.77		500		
12:26	7.18	1.17	11.73	-71.8	1257.76		500	8.38	
12:27	7.17	1.13	11.73	-72.0	1258.00		500		
12:28	7.16	1.11	11.74	-72.6	1257.63		500		
12:29	7.16	1.10	11.72	-72.8	1258.07		500		
12:30	7.16	1.10	11.72	-73.4	1259.04		500		
MINUTES									
19.0	-0.01	-1.29%	-0.23%	-0.76	0.11%			9.50	
TOTAL LITERS									

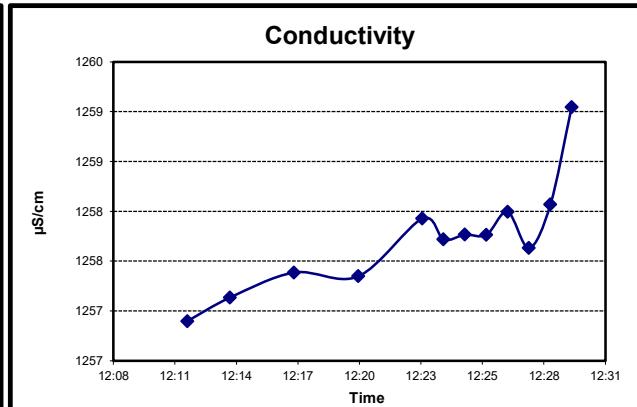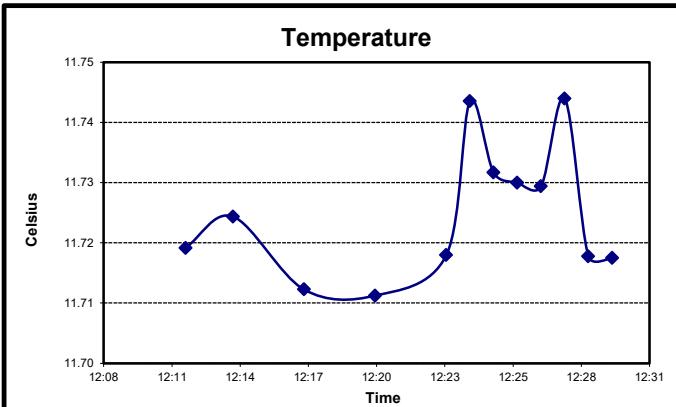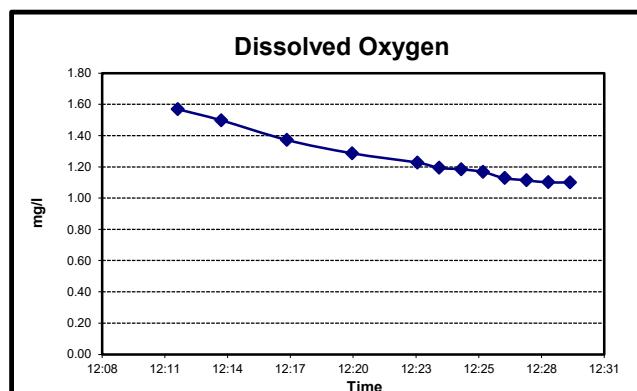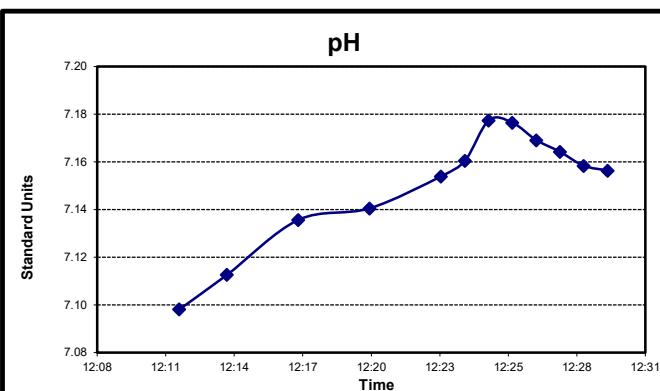


Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-206B
Casing Stickup (Ft.)	3.71	Purge Method		Container 40 mL VOA Vial	Sample Date 13-Nov-20
Total Well Depth (Ft.) TOC	129.94	Purge Equip QED Air Diaphragm		Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	6.58	Field Analysis Method Flow Thru Analysis - 250 mL		Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	119.65	Field Analysis Equip YSI 556 MSP		Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
12:53									
12:54	7.30	0.85	11.65	-45.3	1098.78	37	500	6.58	clear
12:56	7.29	0.84	11.66	-46.9	1096.56		500		
12:59	7.28	0.83	11.64	-47.2	1097.75		500		
13:02	7.29	0.81	11.66	-48.9	1097.74		500	6.59	clear
13:05	7.19	1.19	11.66	-39.7	1092.16		500		
13:06	7.20	1.36	11.66	-36.0	1091.82		500		
13:07	7.22	1.45	11.63	-33.7	1091.97		500		
13:08	7.24	1.50	11.63	-32.6	1091.45		500		
13:09	7.26	1.54	11.63	-31.1	1091.42		500	6.59	
13:10	7.26	1.60	11.61	-29.2	1091.11		500		clear
13:11	7.26	1.62	11.60	-27.1	1091.21		500		
13:12	7.25	1.61	11.60	-25.1	1091.52		500		
MINUTES									TOTAL LITERS
19.0	-0.01	0.93%	-0.09%	4.07	0.04%			9.50	

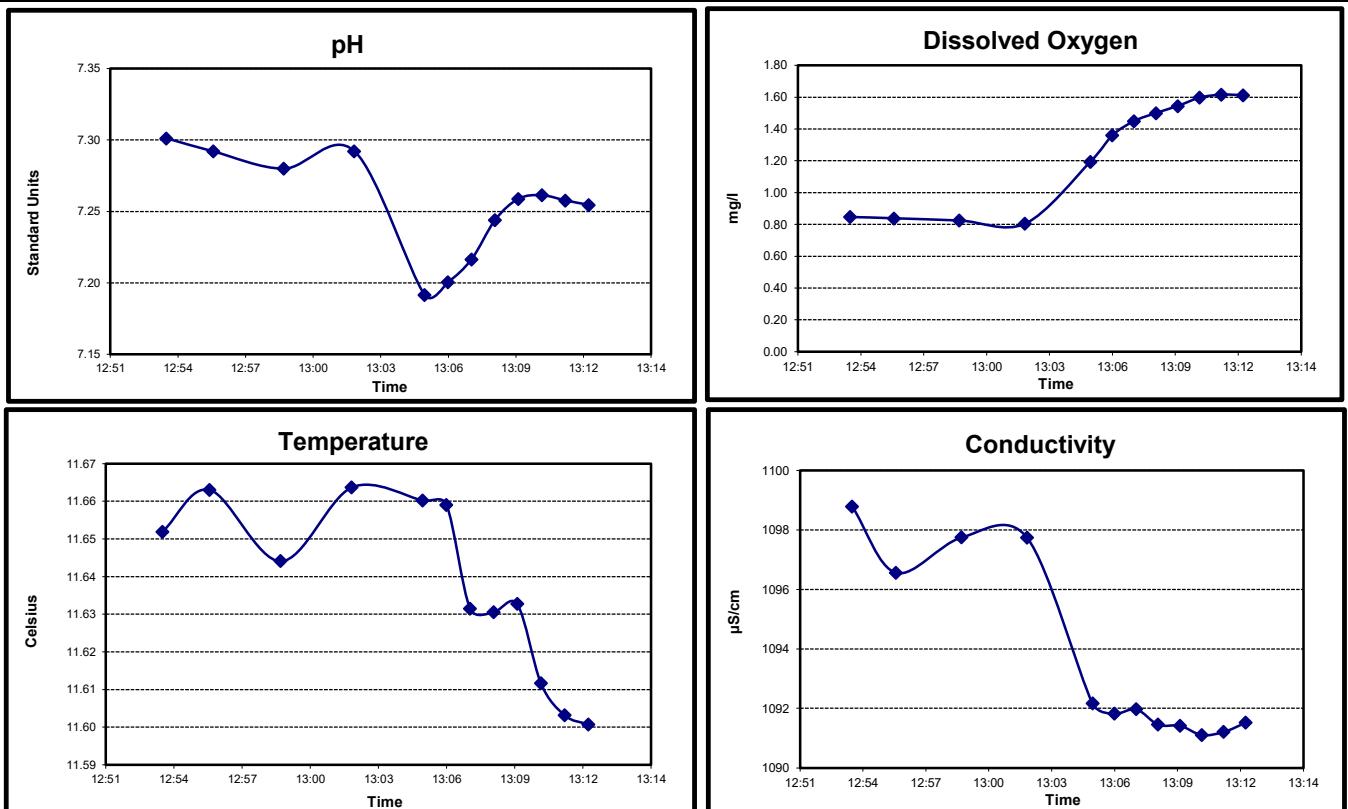


Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-206C
Casing Stickup (Ft.)	4.16	Purge Method	Low Flow Micro Purge	Container 40 mL VOA Vial	Sample Date 13-Nov-20
Total Well Depth (Ft.) TOC	251.31	Purge Equip	QED Air Diaphragm	Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	6.36	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	240.79	Field Analysis Equip	YSI 556 MSP	Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
13:31									
13:32	7.07	1.08	11.42	-46.9	938.14	21	500		
13:34	7.08	1.02	11.43	-51.2	937.97		500		
13:37	7.08	0.99	11.44	-55.3	937.96		500		
13:40	7.10	0.98	11.42	-59.8	937.35		500		
13:43	7.09	0.94	11.37	-61.7	937.18		500		
13:44	7.09	0.95	11.36	-62.1	937.17		500		clear
13:45	7.10	0.96	11.38	-63.0	936.95		500		
13:46	7.10	0.95	11.38	-63.1	937.06		500		
13:47	7.10	0.99	11.39	-63.4	936.79		500		
13:48	7.10	0.98	11.39	-64.1	936.80		500		
13:49	7.11	0.93	11.38	-65.6	936.30		500	6.36	
13:50	7.11	0.93	11.38	-65.8	936.08		500		clear
MINUTES									TOTAL LITERS
19.0	0.01	-5.26%	-0.04%	-1.76	-0.08%				9.50

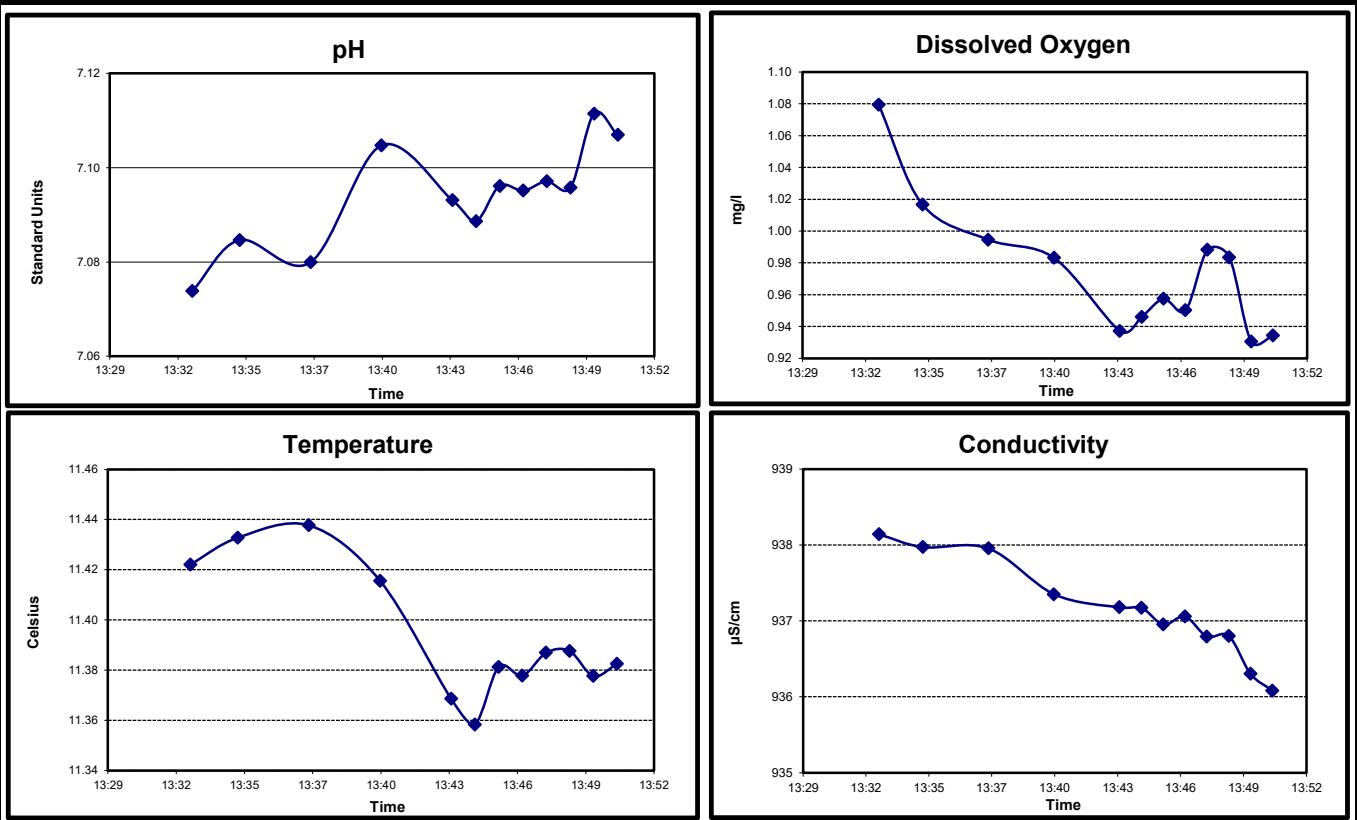


Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis VOCs (SW-846 8260)	Well ID: MW-207
Casing Stickup (Ft.)	-0.3	Purge Method	Low Flow Micro Purge	Container 40 mL VOA Vial	Sample Date 14-Nov-20
Total Well Depth (Ft.) TOC	90.81	Purge Equip	QED Air Diaphragm	Sample Type Grab (Groundwater)	Sampled by: Patrick Egan
Static Water Level (Ft.) TOC	34.65	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation HCl / Ice	Site Visitors: None
Water Thickness (Ft.)	56.46	Field Analysis Equip	YSI 556 MSP	Sampling Period FALL 20	

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond µS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
10:14									
10:15	7.35	6.67	11.25	185.8	1190.39	79	400	34.68	Red cloudy
10:17	7.34	6.67	11.23	186.1	1190.86		400		
10:20	7.34	6.63	11.26	186.0	1190.00		400		
10:23	7.34	6.59	11.24	186.0	1190.55		400		
10:26	7.34	6.66	11.26	185.9	1189.62		400		
10:27	7.34	6.64	11.28	185.9	1189.62		400		
10:28	7.34	6.70	11.26	185.7	1190.63		400		
10:29	7.34	6.60	11.26	185.7	1190.62		400		
10:30	7.34	6.67	11.24	185.9	1191.05		400		
10:31	7.34	6.65	11.21	185.7	1191.18		400	34.79	slightly cloudy
10:32	7.34	6.64	11.23	185.9	1190.24		400		
10:33	7.33	6.67	11.24	186.2	1189.87		400		
MINUTES									TOTAL LITERS
19.0	-0.01	0.21%	0.30%	0.55	-0.11%				7.60

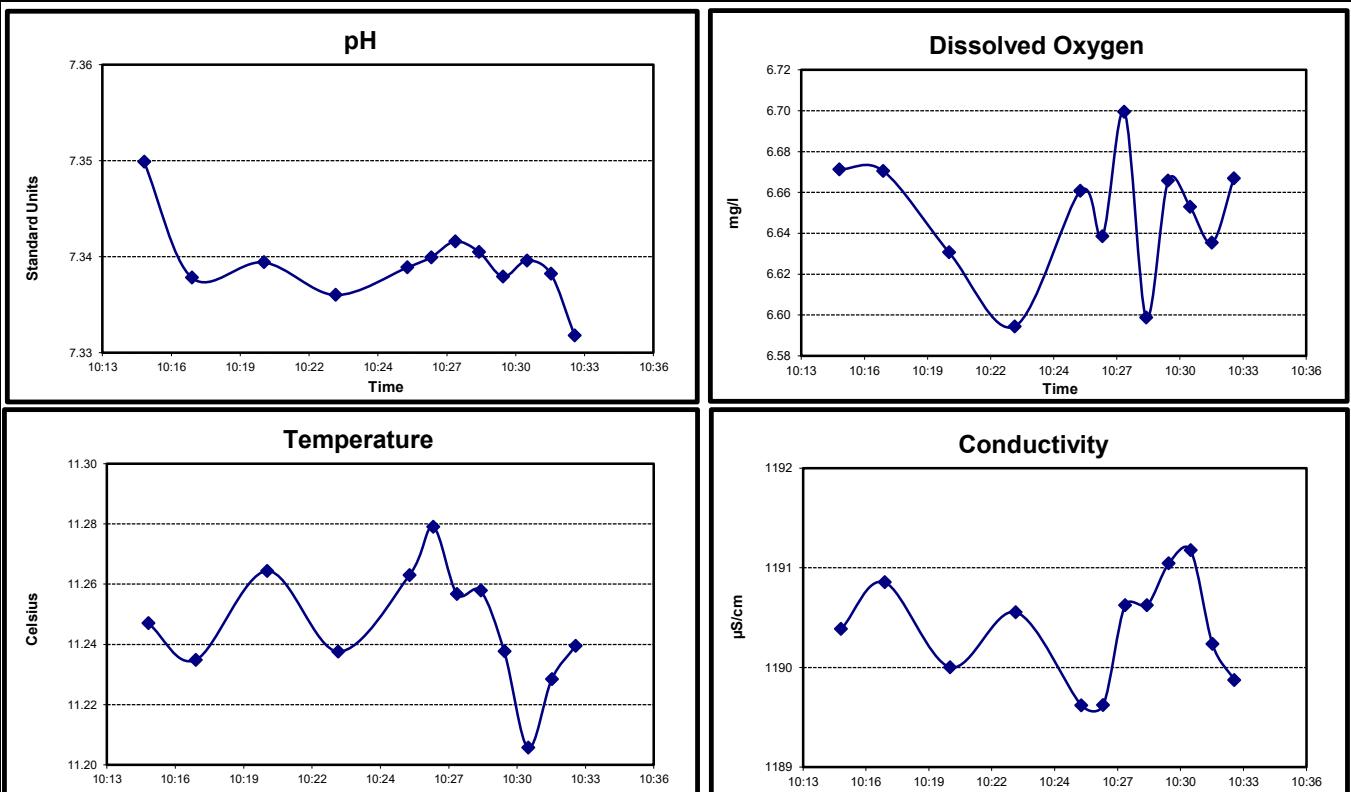

Remarks: (well condition, maintenance, etc...)
