

CAPE MAY MOBIL  
1381 WASHINGTON ST  
CAPE MAY, NJ 08204  
609-884-4848

# facsimile transmittal

To: MR. FRANK SPINA  
From: BARNEY LINN  
Re: CAPE MAY EXXON  
CC:

Fax: 212 637 3953  
Date 7/28/04  
Pages: 3

Urgent

For Review

Please Comment

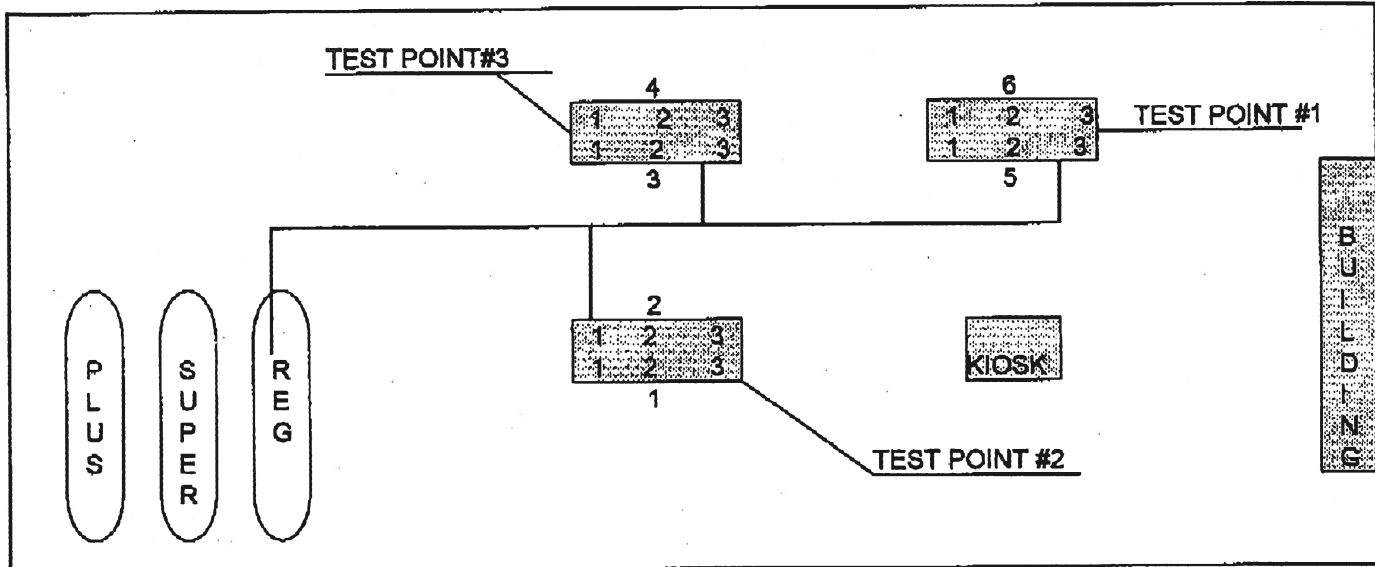
Please Reply

Please Recycle

/  
CALLED MR. LINN JULY 29, 2004  
TO CONFIRM. FC -1114 will be  
Recinded.

# MAGTECH TESTING

## STAGE II PRESSURE DROP AND LIQUID BLOCKAGE CERTIFICATION TEST

COMPANY TESTED CAPE MAY EXXONSTAGE 2 SYS. BALANCEDADDRESS RT.109TESTER MAGTECH TESTINGCITY, COUNTY CAPE MAY, NJ.DATE OF TEST September 27, 2003

### PRESSURE DROP TEST DATA

PRODUCT NOZZLE FLOWMETER CUBIC FT. HR. COMMENTS  
 20 60 100

PRODUCT	NOZZLE	20	60	100	COMMENTS
SUPREME	1	.02	.18	.40	PASSED
PLUS	2	.04	.18	.42	PASSED
REG UNL	3	.04	.18	.46	PASSED

### LIQUID BLOCKAGE TEST

TEST POINT 1			TEST POINT 2			TEST POINT 3		
60 CFH.	DRY	WET	60 CFH.	DRY	WET	60 CFH.	DRY	WET
	.02	.02		.01	.01		.03	.03

STAGE #2 **363449598**

# Riggins

3938 S. Main Rd. Vineland, NJ 08360

1-800-642-9148

856-825-7600

FAX: 856-825-2270

## AVO EVALUATION CHART

LOCATION

SERVICE COMPANY

DATE

Cape May ExxonRIGGINS INC.04/14/04

Technician Performing Test

JEFF ANDERSON

TECH #

148603260

Type Of Leak Detectors Tested (check all that apply)

☐ XLD P/N 116036-5☐ XLP P/N 116035-5☐ BFLD (XL MODEL) P/N116039-5☒ DLD P/N 116017-5☐ PLD P/N 116030-5☐ BFLD P/N 116012-5☐ OTHER \_\_\_\_\_☐ FX1☒ FX2

	SERIAL NUMBER	RESILIENCY	OPENING TIME	TEST LEAK RATE ML/Min	Metering PSI	pass ? Yes or No
1	116007877	11oz	2sec	3.6 ph 6.02 pm	12 psi	yes
2	10390751	11oz	2sec	3.6 ph 6.02 pm	12 psi	yes
3	211887126	11oz	2sec	3.6 ph 6.02 pm	12 psi	yes
4						
5						
6						
7						

Gasoline • Diesel • Heating Oil



(Date)
