NATIONWIDE ENVIRONMENTAL SERVICES, INC.

6th Avenue West Business Park
14818 W 6th Ave. Suite 5A
Golden, CO 80401

US EPA RECORDS CENTER REGION 5
452117

February 1, 2013

Mr. Tim Drexler
Remedial Project Manager
U.S. Environmental Protection Agency
77 West Jackson Boulevard, HSRM-6J
Chicago, IL 60604

Mr. Doyle W. Wilson
Illinois Environmental Protection Agency
1021 North Grand Avenue East
P.O. Box 19276
Springfield, IL 62794-9276

RE: Southeast Rockford Ground Water NPL Site
Ground Water Monitoring Report
Semi-Annual Monitoring Event – November/December 2012

Gentlemen:

Nationwide Environmental Services, Inc. (NES) is submitting the semi-annual monitoring report presenting the analytical data and data interpretation summary for ground water quality monitoring samples collected at the Southeast Rockford Ground Water NPL Site (the Site) during the November/December 2012 semi-annual monitoring event. This report includes data reporting information to address comments and suggestions received from USEPA on the semi-annual reports submitted for prior monitoring events. Ground water monitoring data will be submitted in an MS Excel™ file separately via e-mail. The pertinent Site information and monitoring data are presented in the report as follows:

- The locations of the monitoring wells comprising the Site ground water monitoring network are shown in **Figure 1**.
- The analytical results are summarized in **Table 1** and present concentrations for the chemicals of concern (COC) identified in Section VI of the Site Record of Decision (ROD) and for vinyl chloride.
- The historical analytical results for samples collected from the Site ground water monitoring network, by monitoring well location, are presented in **Table 2**.
- The ground water elevations for this sampling event are presented in **Table 3**.
- The validated laboratory data sheets and data quality summaries including relevant analytical quality assurance/quality control (QA/QC) are provided in **Appendix A**.
- The field sampling sheets containing field sampling information for the current monitoring event are contained in **Appendix B**.

NES continues to coordinate efforts with IEPA to share ground water data obtained from common monitoring well locations at the Site. NES is not aware of IEPA sample collection from Site monitoring locations since 2008, and therefore, no comparative Site data from IEPA is presented in this report.

The field sampling activity and analytical procedures utilized for the current monitoring event were performed in accordance with the 2008 amended Quality Assurance Project Plan and the 2010 amended Field Sampling Plan. A few minor issues occurred during the event that resulted in a departure from established procedures as follows:

- MW-133A was dry; therefore, a sample was not collected from this monitoring location.
- Access to MW-205A/B was limited; therefore, a bailer was used to collect samples from these monitoring locations instead of the low flow sampling equipment..

A series of graphs depicting historical total volatile organic compound (VOC) concentrations for select wells are enclosed to show the trends of total VOC concentrations occurring at these monitoring locations. Although the graphs depict analytical results from 1999 and forward, the evaluation of the total VOCs presented in this report focuses mainly on changes, if any, from the previous semi-annual sampling event. The graphs show fluctuation of total VOCs in ground water that are likely caused by the effects of various factors such as source area remedial activities performed by others, variation in ground water levels, precipitation events, etc. However, NES is not aware of any specifics that would allow an interpretation of the data, other than the general observations presented in the following section.

Monitoring Data Review

Overall, total VOC concentrations have generally decreased across the Site since inception of the long-term monitoring program in March 1999. The ratios of parent VOC compound concentrations to associated breakdown product concentrations indicate biodegradation, comprising one component of natural attenuation, may be occurring at the Site. The presence of vinyl chloride, chloroethane, and chloromethane in ground water samples are further indicators that natural attenuation may be occurring at the Site.

The status of total VOC concentrations at certain monitoring well locations, relative to the previous monitoring event (June 2012), are summarized below. The noted monitoring well locations are located proximate to, or down-gradient from, identified source areas. The Site source areas are segregated by general geographic location within the Site for the purpose of this report.

East-Source Area 7

The majority of total VOC concentrations reported for ground water monitoring locations near the Area 7 source area have generally decreased or remained relatively stable from the previous sampling event except as noted. Relative increases in individual VOC concentrations did occur in the water quality samples collected from MW-101C, MW-102A/B, and MW-133B. Several VOCs at MW-101C, MW-102A, and MW-133B were reported above the maximum contaminant level (MCL).

North-Source Areas 4, 9, 10, & 11

The majority of total VOC concentrations reported for ground water monitoring locations in the identified areas have generally decreased or remained relatively stable from the previous sampling event except as noted. Relative increases in individual VOC concentrations did occur in the water quality samples collected from MW-201, MW-202, and MW-203. However, only tetrachloroethene (PCE) at MW-203 was reported above the MCL.

West-Rock River

Total VOC concentrations reported for ground water monitoring locations in the area bordering the east side of the Rock River have generally decreased or remained stable from the previous sampling event except as noted. Relative increases in specific constituent VOC concentrations, comprising COC identified at the site, did occur in the water quality samples collected from MW-117B, MW-117D, MW-119, MW-204, MW-206A, MW-206C, and MW-207. Several VOCs were reported above the MCL at these wells with the exception of the at MW-119 and MW-207 locations.

Please contact me at telephone (303) 232-2134 if you have any questions regarding the information provided or require any additional information.

Sincerely,

William B. Dotterer,
Sr. Project Manager

cc: Nadine Miller, City of Rockford

Enclosures

Figures

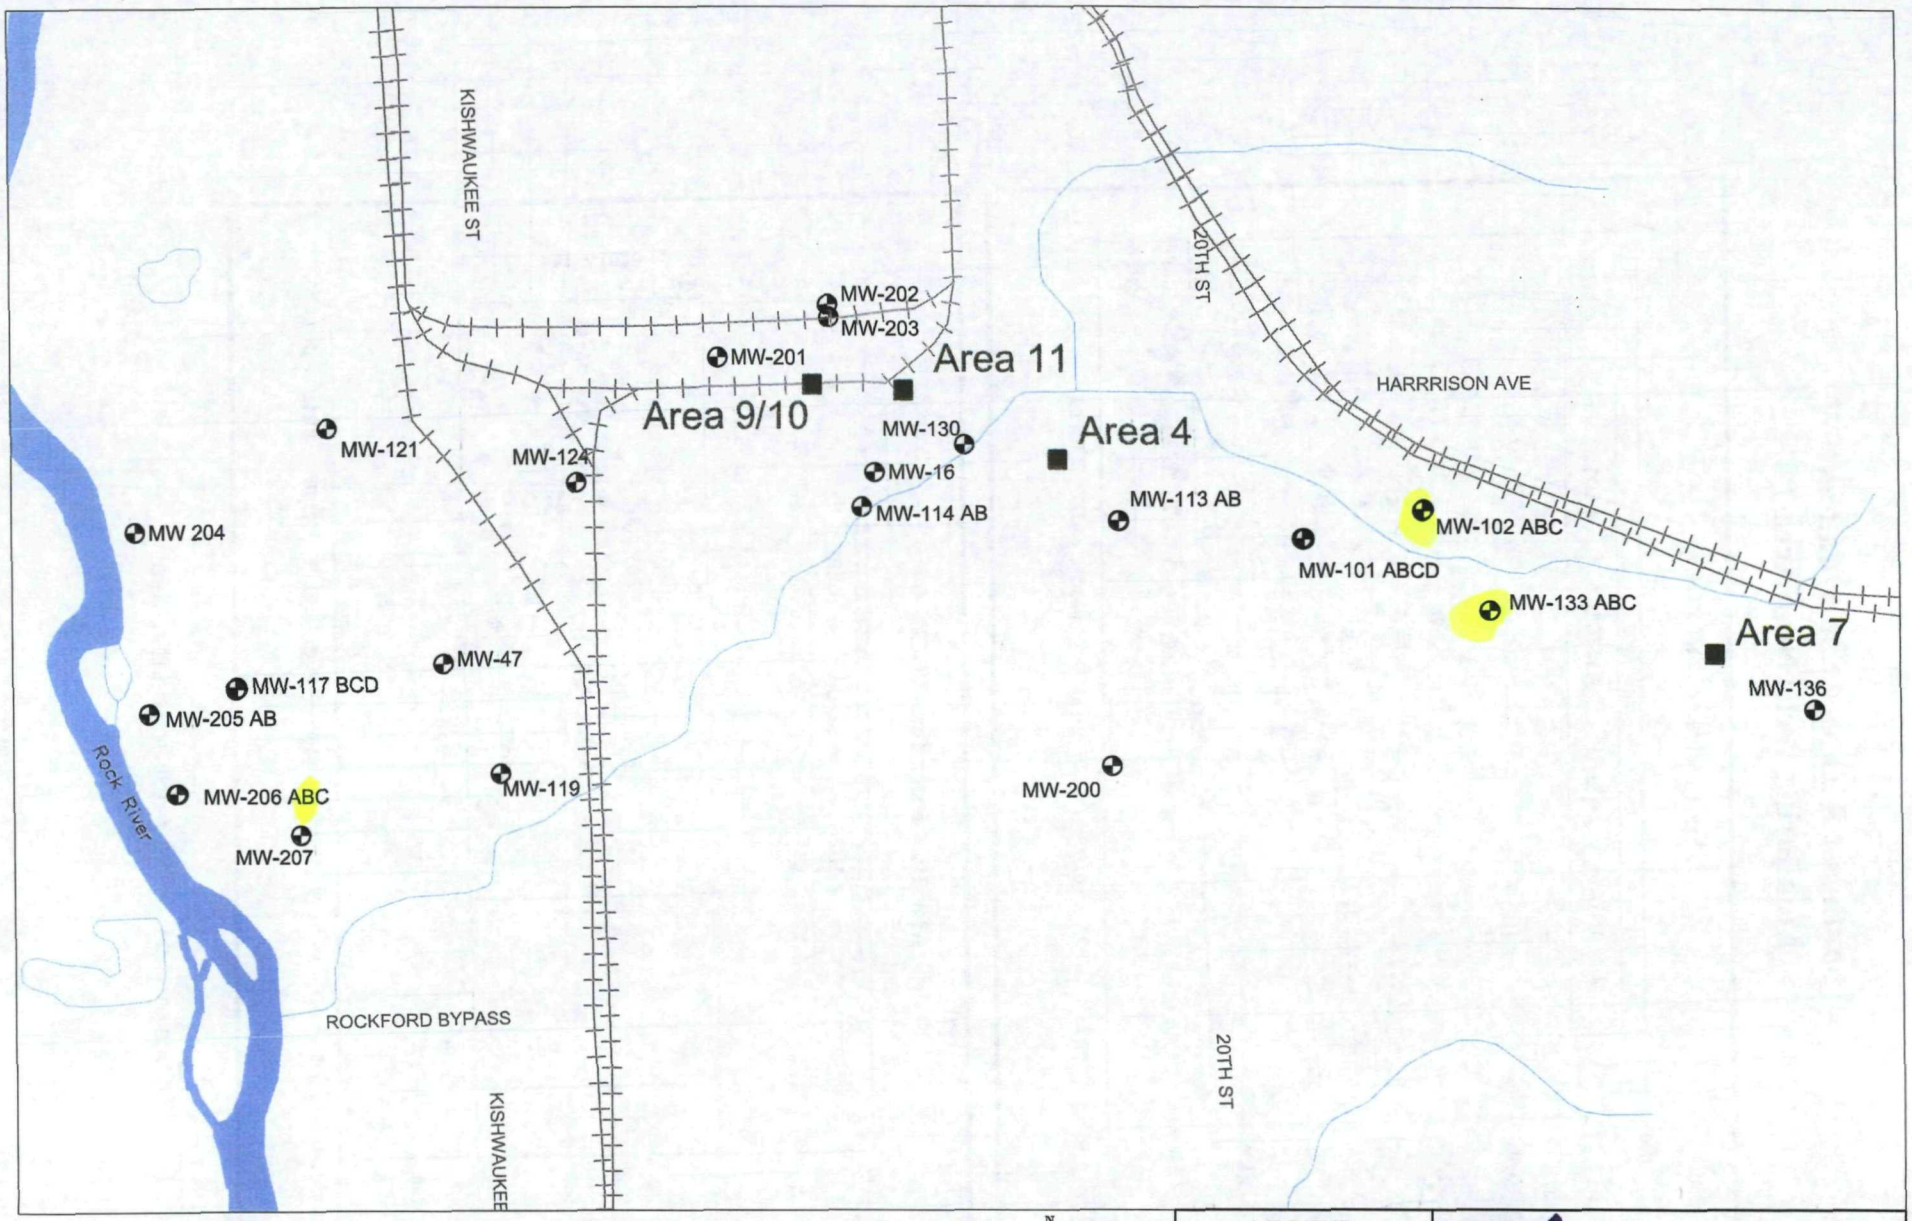

N
W E
S
0 1000' 2000'

LEGEND

Monitoring Well

Area

Figure 1
Southeast Rockford NPL Site
Ground Water Monitoring Network
and Source Locations
Winnebago County, Illinois

Southeast Rockford Superfund Site
Monitoring Wells Near Area 7

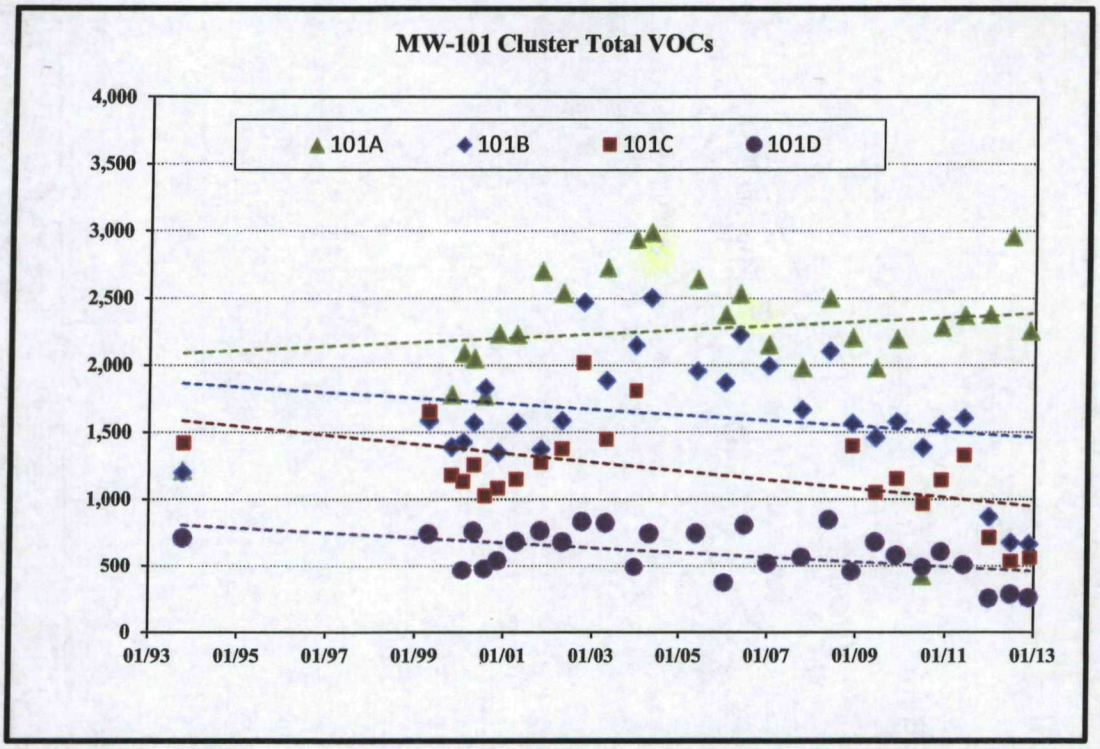

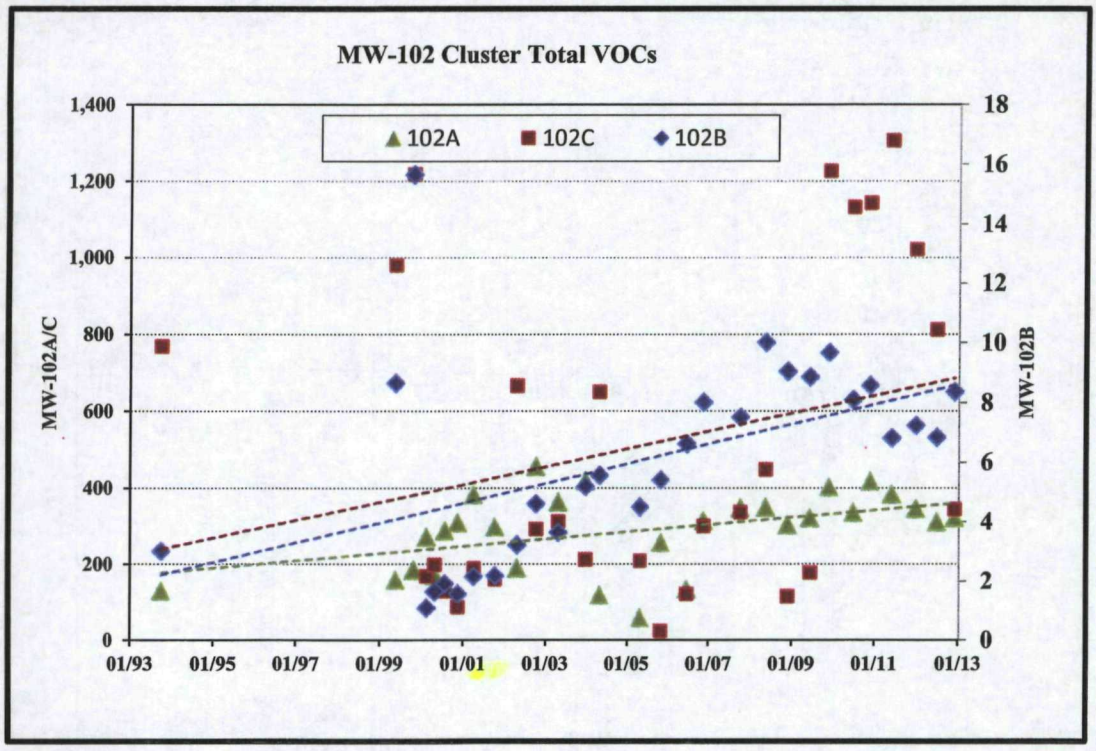

Y-axis = Total VOCs in parts per billion; X- axis = Sampling Date

Southeast Rockford Superfund Site
Monitoring Wells Near Area 7

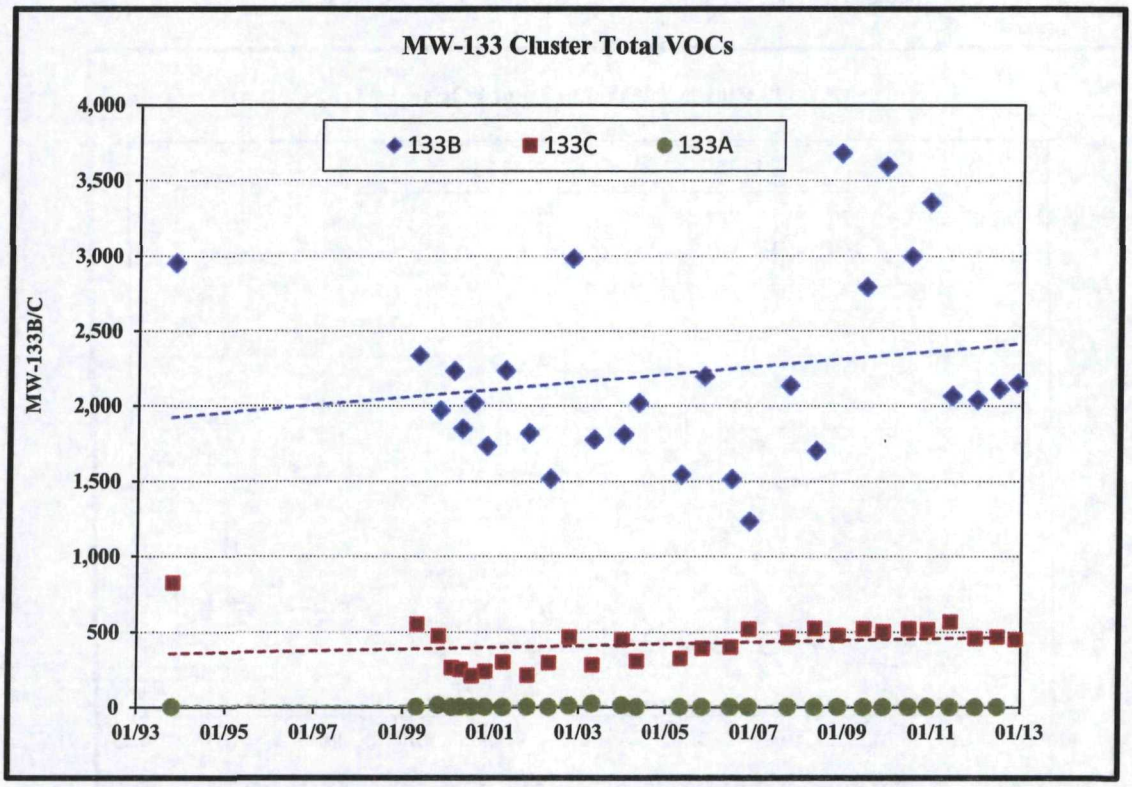

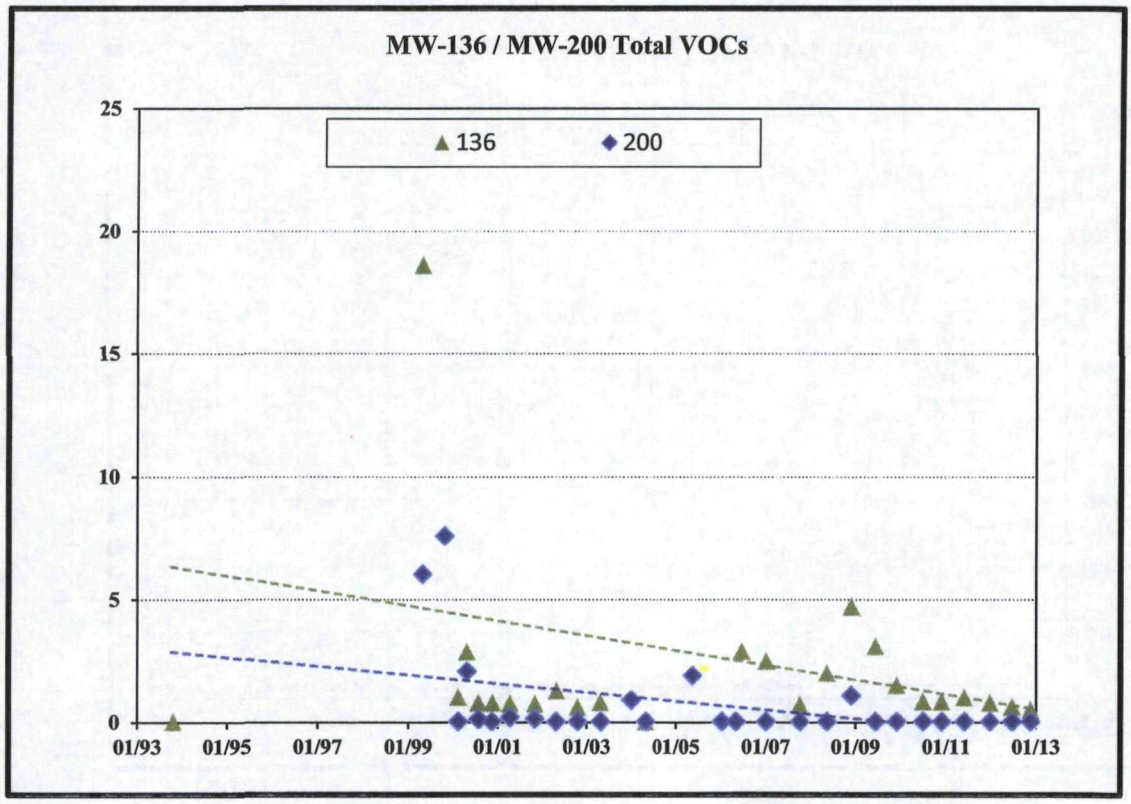

Y-axis = Total VOCs in parts per billion; X- axis = Sampling Date

Southeast Rockford Superfund Site
Monitoring Wells Near Areas 4, 9/10, 11

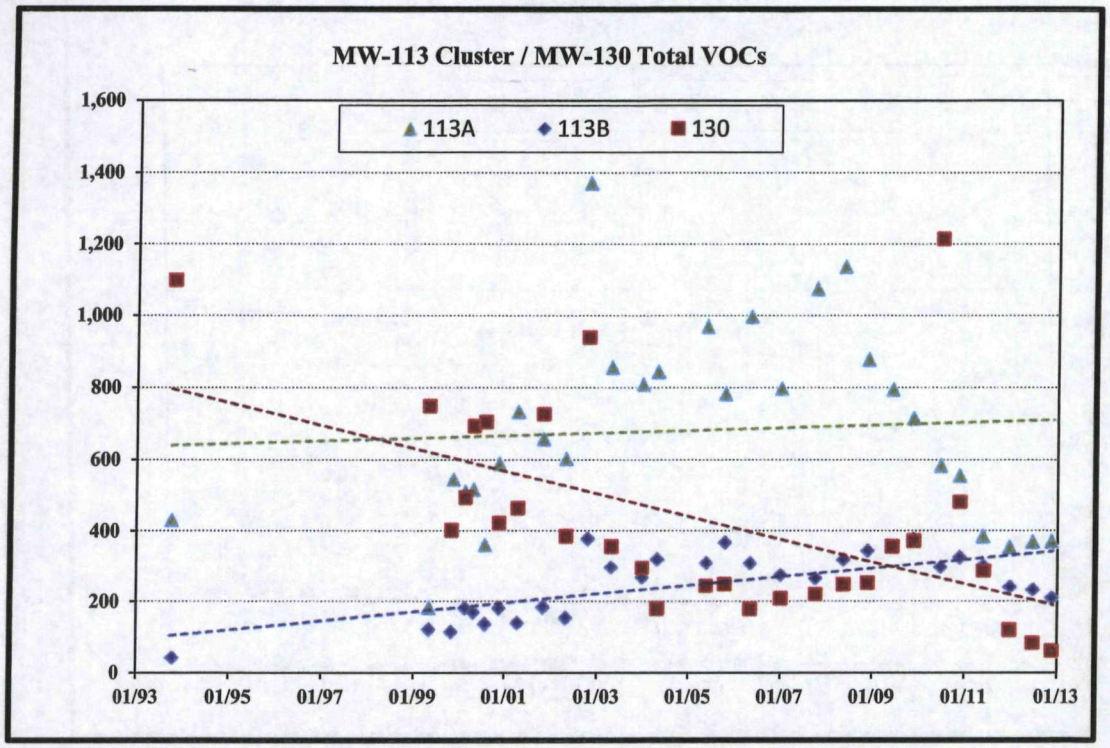

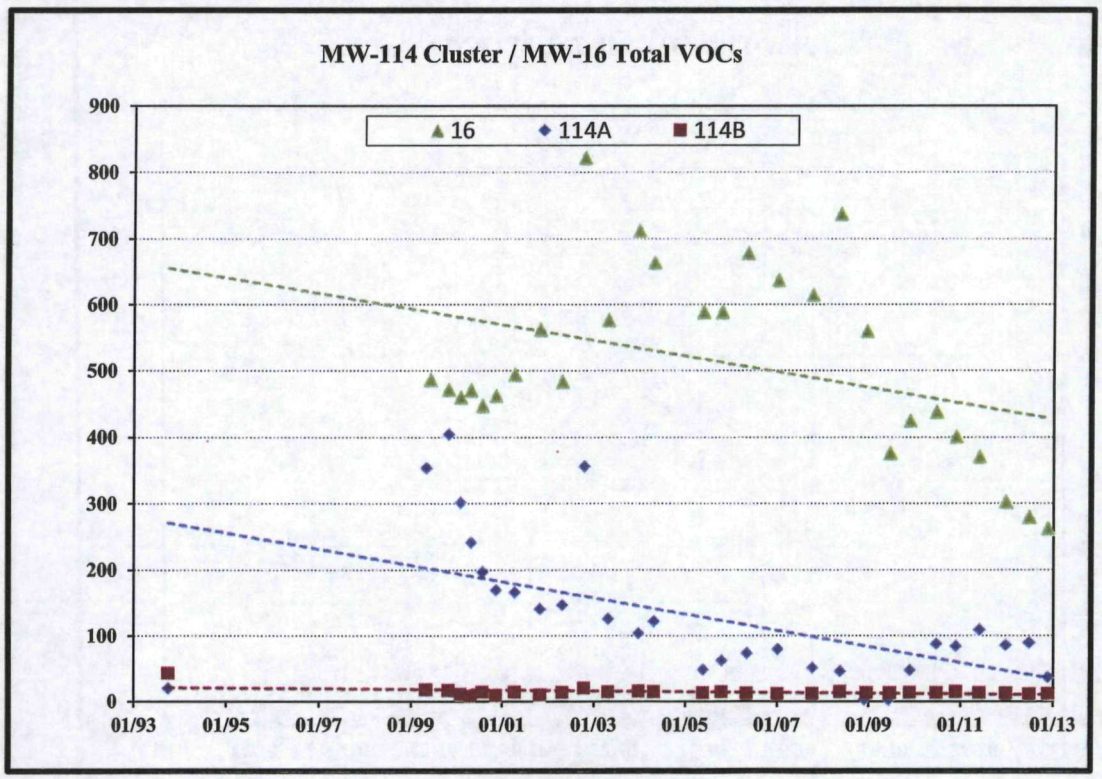

Y-axis = Total VOCs in parts per billion; X- axis = Sampling Date

Southeast Rockford Superfund Site
Monitoring Wells Near Areas 4, 9/10, 11

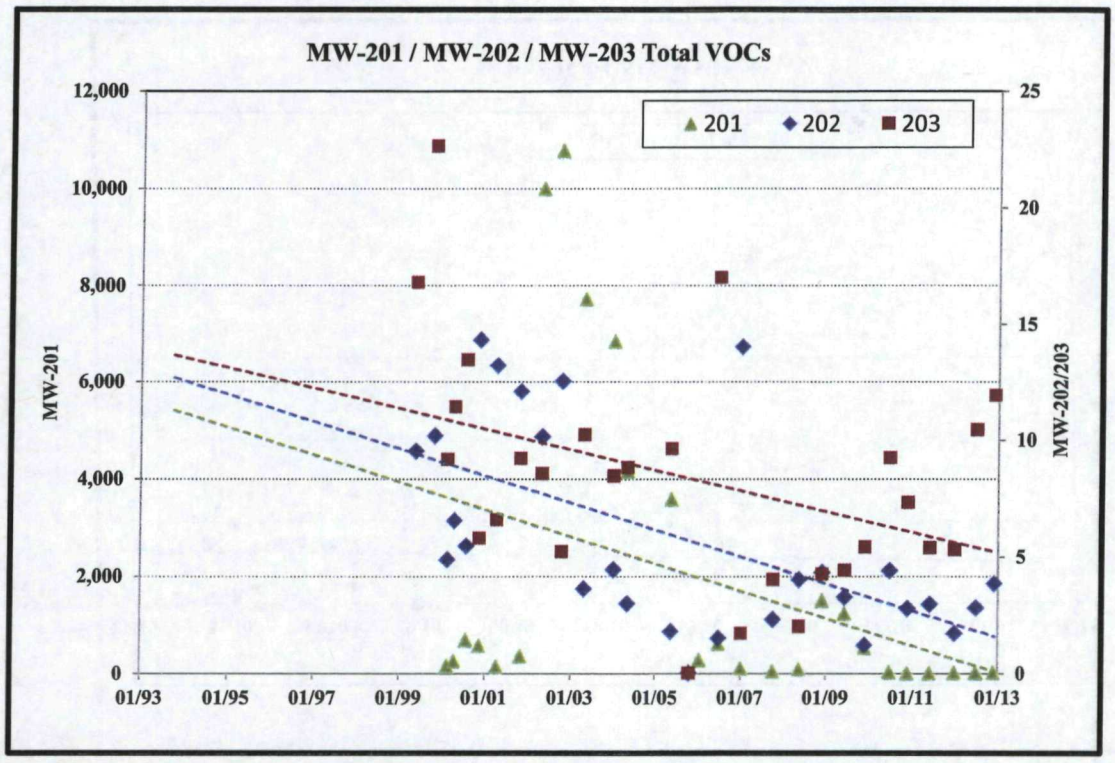

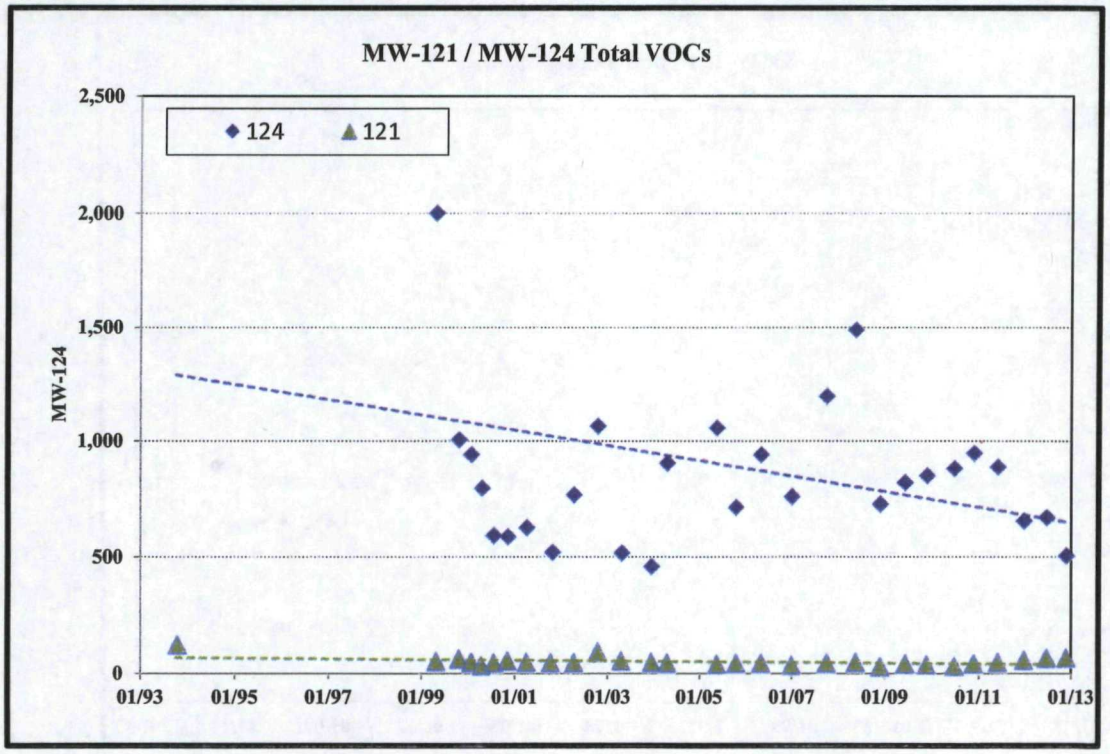

Y-axis = Total VOCs in parts per billion; X- axis = Sampling Date

Southeast Rockford Superfund Site
Monitoring Wells Near Rock River

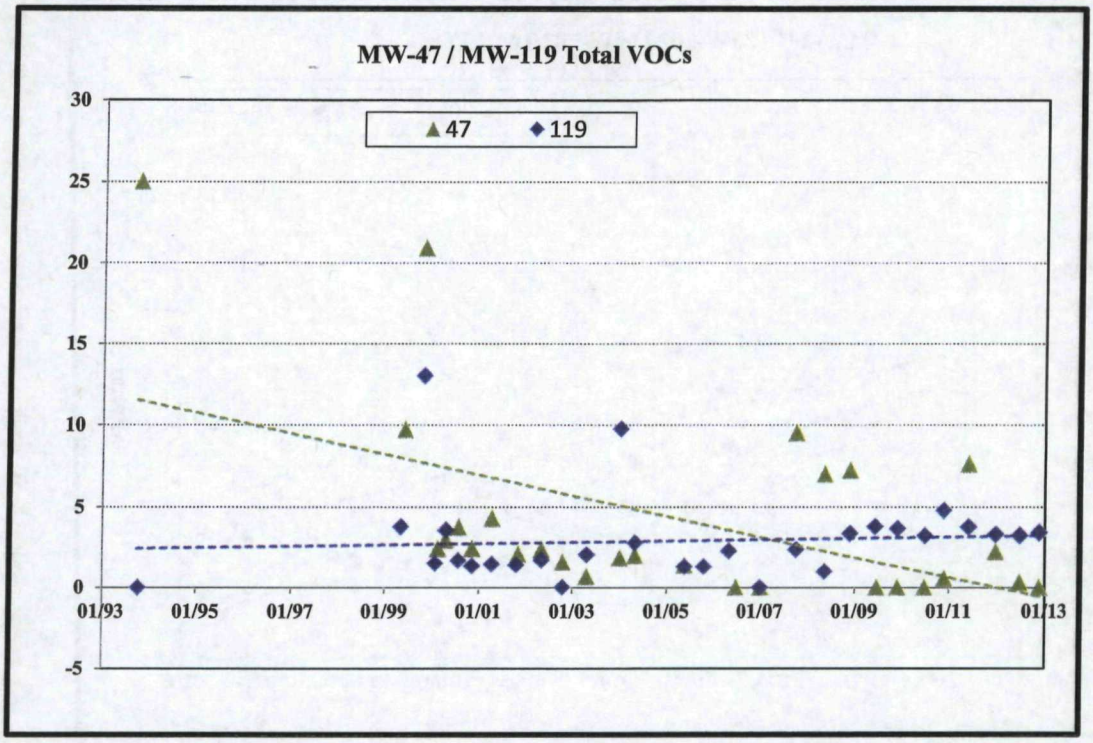

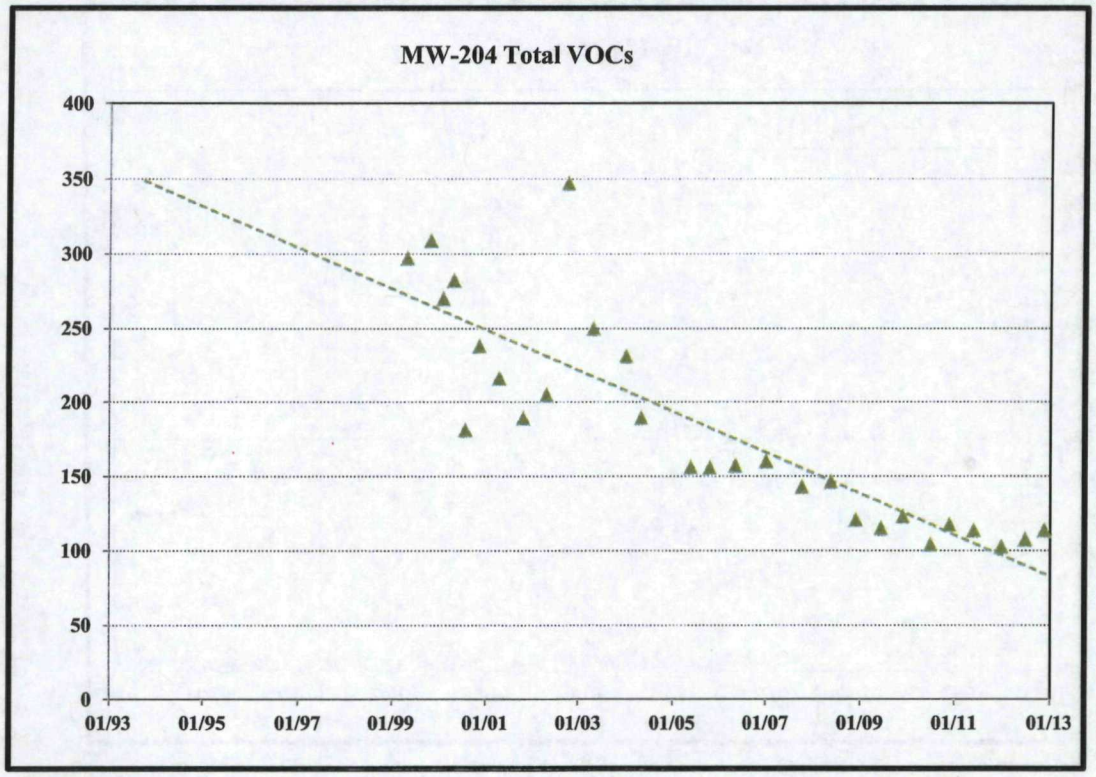

Y-axis = Total VOCs in parts per billion; X- axis = Sampling Date

Southeast Rockford Superfund Site
Monitoring Wells Near Rock River

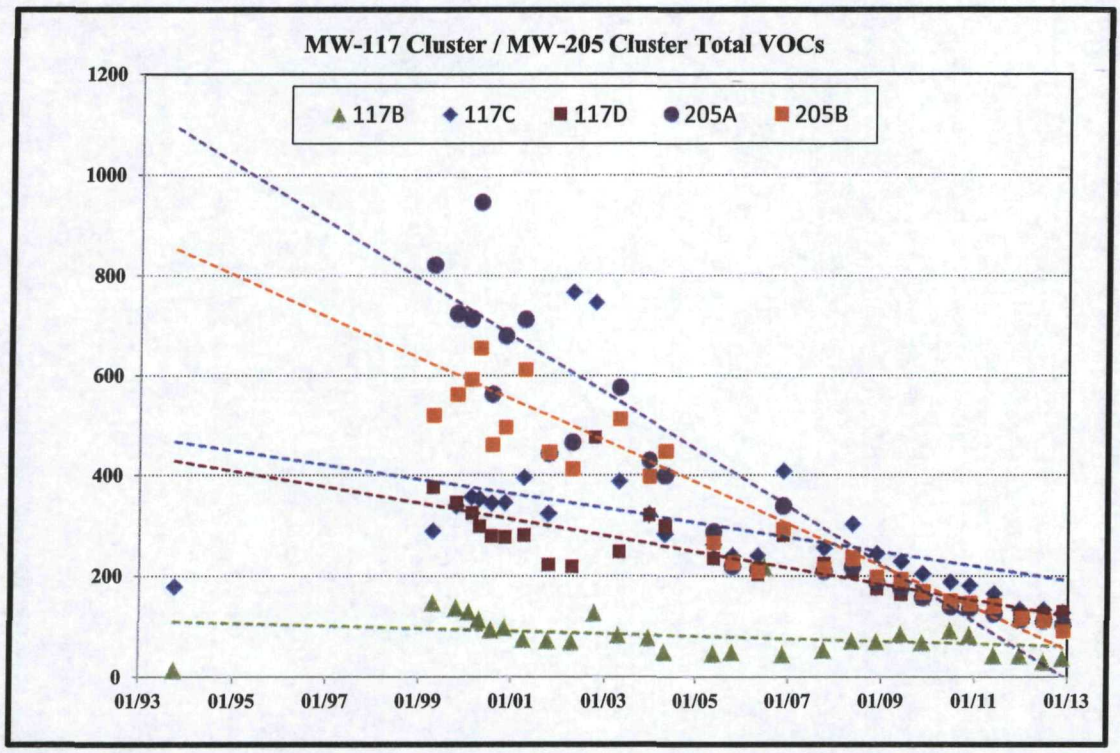

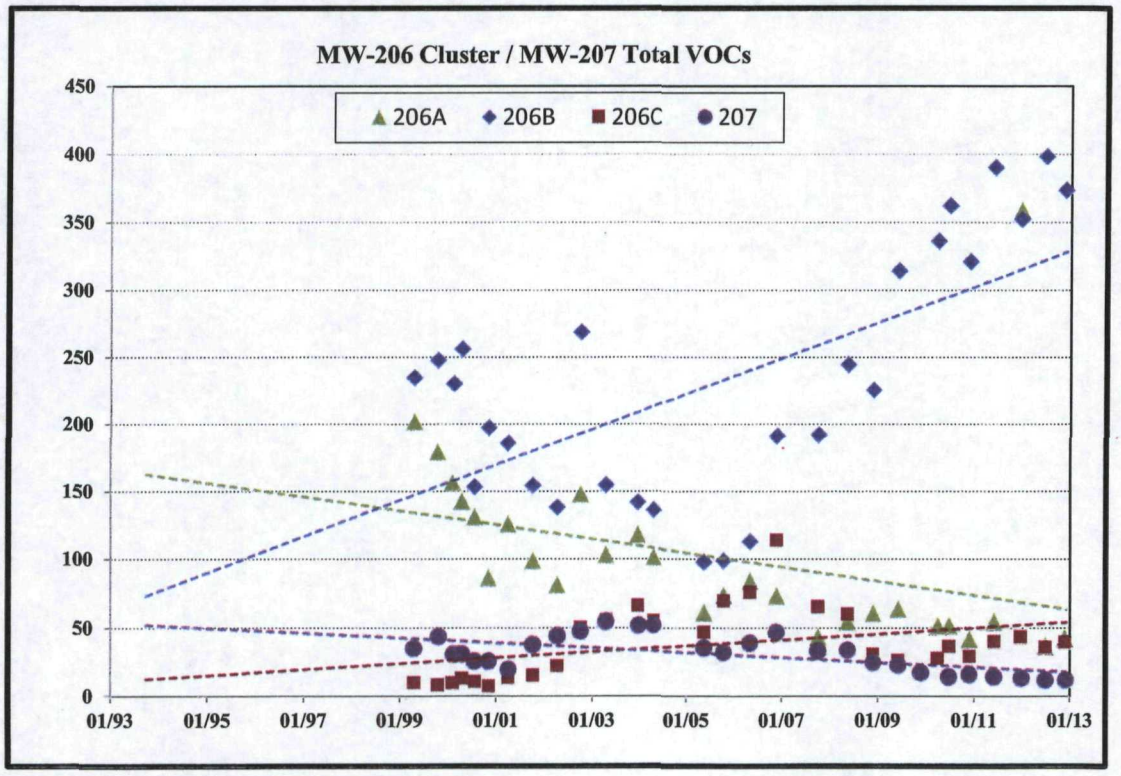

Y-axis = Total VOCs in parts per billion; X- axis = Sampling Date

Tables

Table 1: Southeast Rockford NPL Site
Summary of Groundwater Analytical Results
Sampling Event #28

Compound	MCL	MW-16 11/24/12	MW-47 11/25/12	MW-101A 11/24/12	MW-101B 11/24/12	MW-101C 11/30/12	MW-101D 11/24/12	MW-102A 11/30/12	MW-102B 11/30/12
Chloroform	N/A	0.9J	1.0U	3.4J	1.4J	1.3J	1	1.0U	1.0U
1,1-Dichloroethane	N/A	68	1.0U	240	120	99	42	82	2.8
1,2-Dichloroethane	5	1.0U	1.0U	10U	2.5U	2.5U	1.0U	1.0U	0.52J
1,1-Dichloroethene	7	**13**	1.0U	**39**	**26**	**20**	**13**	1.6	1.0U
cis-1,2-Dichloroethene	70	22	1.0U	**1200**	33	40	27	**160**	4.6
trans-1,2-Dichloroethene	100	2.4	1.0U	57	4.1	3.6	1.6	5.7	1.0U
Methylene Chloride	5	5.0U	5.0U	50U	0.88J	12U	5.0U	5.0U	5.0U
Tetrachloroethene	5	**10**	1.0U	**55**	**25**	**18**	**11**	1.0U	1.0U
1,1,1-Trichloroethane	200	110	1.0U	**500**	**430**	**360**	140	59	1.0U
Trichloroethene	5	**35**	1.0U	**160**	**26**	**20**	**16**	**14**	1.0U
Vinyl chloride	2	1.0U	1.0U	10U	2.5U	2.5U	1.0U	1.0U	0.43J

Compound	MCL	MW-102C 11/24/12	MW-113A 11/24/12	MW-113B 11/24/12	MW-114A 11/24/12	MW-114B 11/24/12	MW-117B 11/25/12	MW-117C 11/25/12	MW-117D 11/25/12
Chloroform	N/A	0.36J	1.2	0.34J	1.0U	1.0U	0.35J	0.35J	0.32J
1,1-Dichloroethane	N/A	64	110	59	2.9	1.3	10	29	48
1,2-Dichloroethane	5	0.54J	1.0U	0.46J	1.0U	1.0U	1.0U	1.0U	1.0U
1,1-Dichloroethene	7	**15**	**14**	**14**	1.6	0.44J	3	**17**	**12**
cis-1,2-Dichloroethene	70	**200**	43	**78**	2.4	1.9	1.1	7.4	3
trans-1,2-Dichloroethene	100	2	4.4	1.8	0.22J	1.0U	1.0U	1.0U	1.0U
Methylene Chloride	5	10U	5.0U	5.0U	5.0U	5.0U	5.0U	5.0U	5.0U
Tetrachloroethene	5	4.2	**13**	3.7	1.0U	1.0U	**5.7**	**22**	**19**
1,1,1-Trichloroethane	200	41	140	18	27	1.0U	10	36	34
Trichloroethene	5	**15**	**45**	**26**	1.8	**6.1**	**6**	**14**	**11**
Vinyl chloride	2	2.0U	1.0U	**7.5**	1.0U	1.0U	1.0U	1.0U	1.0U

Table 1: Southeast Rockford NPL Site
Summary of Groundwater Analytical Results
Sampling Event #28

Compound	MCL	MW-119 11/30/12	MW-121 11/25/12	MW-124 11/25/12	MW-130 11/24/12	MW-133A	MW-133B 11/24/12	MW-133C 11/24/12	MW-136 11/24/12
Chloroform	N/A	0.13J	0.76J	2.0U	1.0U	NS	6.0J	5.3	0.5J
1,1-Dichloroethane	N/A	0.99J	23	330	7.5	NS	160	49	1.0U
1,2-Dichloroethane	5	1.0U	1.0U	2.0U	1.0U	NS	3.3J	1.6	1.0U
1,1-Dichloroethene	7	1.0U	3	**9.6**	1.7	NS	**49**	**41**	1.0U
cis-1,2-Dichloroethene	70	0.8J	5.3	**70**	2.5	NS	**1300**	**130**	1.0U
trans-1,2-Dichloroethene	100	1.0U	0.74J	0.9J	1.0U	NS	49	1.5	1.0U
Methylene Chloride	5	5.0U	5.0U	1.0J	5.0U	NS	50U	5.0U	5.0U
Tetrachloroethene	5	1.0U	1.5	**5.2**	0.64J	NS	**64**	**6.6**	1.0U
1,1,1-Trichloroethane	200	1.2	12	50	47	NS	**420**	140	1.0U
Trichloroethene	5	0.32J	**18**	4.3	1.9	NS	**96**	**75**	1.0U
Vinyl chloride	2	1.0U	1.0U	**30**	1.0U	NS	10U	1.0U	1.0U

Compound	MCL	MW-200 11/24/12	MW-201 11/25/12	MW-202 11/30/12	MW-203 11/30/12	MW-204 11/25/12	MW-205A 12/02/12	MW-205B 12/02/12	MW-206A 11/23/12
Chloroform	N/A	1.0U	1.0U	1.0U	1.0U	0.45J	0.26J	0.32J	0.42J
1,1-Dichloroethane	N/A	1.0U	5	0.45J	0.19J	6	20	20	12
1,2-Dichloroethane	5	1.0U	1.0U	1.0U	1.0U	1.2	1.0U	1.0U	1.0U
1,1-Dichloroethene	7	1.0U	1.0U	1.0U	1.0U	**12**	**11**	**10**	3.8
cis-1,2-Dichloroethene	70	1.0U	1	1.0U	1.0U	33	4.6	6	2
trans-1,2-Dichloroethene	100	1.0U	1.0U	1.0U	1.0U	0.64J	1.0U	1.0U	1.0U
Methylene Chloride	5	5.0U	5.0U	5.0U	5.0U	5.0U	5.0U	5.0U	5.0U
Tetrachloroethene	5	1.0U	0.85J	2.1	**11**	1.8	**24**	**16**	**5.5**
1,1,1-Trichloroethane	200	1.0U	15	1	0.36J	7.3	27	25	12
Trichloroethene	5	1.0U	0.31J	0.3J	0.34J	**51**	**15**	**12**	**6.2**
Vinyl chloride	2	1.0U	1.0U	1.0U	1.0U	1.0U	1.0U	1.0U	1.0U

Table 1: Southeast Rockford NPL Site
Summary of Groundwater Analytical Results
Sampling Event #28

Compound	MCL	MW-206B 11/23/12	MW-206C 11/23/12	MW-207 11/30/12	MW-101C(d) 11/30/12	MW-114B(d) 11/24/12
Chloroform	N/A	0.86J	1.0U	0.22J	1.4J	1.0U
1,1-Dichloroethane	N/A	55	7.1	1.4	99	1.3
1,2-Dichloroethane	5	2.1	1.0U	1.0U	5.0U	1.0U
1,1-Dichloroethene	7	**74**	5.1	0.53J	20	0.38J
cis-1,2-Dichloroethene	70	**130**	7.1	1.2	40	1.8
trans-1,2-Dichloroethene	100	0.4J	1.0U	1.0U	3.6J	1.0U
Methylene Chloride	5	5.0U	5.0U	5.0U	25U	5.0U
Tetrachloroethene	5	**14**	0.24J	1.4	18	1.0U
1,1,1-Trichloroethane	200	55	1.0U	2.3	360	1.0U
Trichloroethene	5	**41**	**19**	4	20	5.8
Vinyl chloride	2	0.8J	1.0U	1.0U	5.0U	1.0U

(d) Field duplicate
All units in micrograms per liter (µg/l) or parts per billion (ppb)
Bold value and outlined cell denotes analytical result > than MCL

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-16	06/01/99		3	76	1.2	24	140	1.8	2 U	5.4	170	64	1 U	**485**
MW-16	10/26/99		2.3 J	73	10 U	23	130	2.5 J	20 U	5.2 J	170	65	10 U	**471**
MW-16	01/31/00		2.3 J	75	10 U	2.2 J	120	16	20 U	5.9 J	170	68	10 U	**459**
MW-16	04/24/00		2.5 J	79	5 U	2 J	130 E	16	10 JB	5.7	170 E	65	5 U	**480**
MW-16	04/24/00	Dilution	50 DJB	75 D	50 U	50 U	130 D	17 DJ	100 DJB	5.3 DJ	160 D	62 D	2.8 DJ	**602**
MW-16	07/27/00		2.7	75	10 U	3.8	130	12	20 U	5.2	160	58	10 U	**447**
MW-16	11/13/00		2.2	87	10 U	20	150	2.8	20 U	5	140	55	10 U	**462**
MW-16	04/12/01		2.3	74	10 U	3.1	150	14	20 U	5.8	180	64	10 U	**493**
MW-16	10/31/01		2.5	88	10 U	10 U	160	22	20 U	7.1	210	72	10 U	**562**
MW-16	04/25/02		2.3	70	10 U	15	170	6.7	20 U	6.6	150	62	10 U	**483**
MW-16	10/15/02		20 U	130	20 U	98	240	22	40 U	20 U	240	91	1 U	**821**
MW-16	04/23/03		2.51	95.6 E	1.08	24.2	244 E	15.7	2 U	9.74	237 E	97.6 E	1 U	**727**
MW-16	04/23/03	Dilution	20 U	75.6	20 U	24.6	200	20 U	40 U	20 U	172	75.3	20 U	**548**
MW-16	12/26/03		2.48	93.9 E	1 U	32.2 E	209 E	13.9	1 U	9.45	208 E	77.8 E	1 U	**647**
MW-16	12/26/03	Dilution	10 U	93.9 D	10 U	31.7 D	247 D	10 U	10 U	9.14 JD	221 D	92.7 E	10 U	**695**
MW-16	12/26/03	Fld Dupe	10 U	96.3 E	1 U	30.5 D	230 E	10 U	1 U	9.85	220 E	84.4 E	10 U	**671**
MW-16	04/28/04		20 U	100	20 U	30.1	254	20 U	40 U	20 U	202	77.3	20 U	**663**
MW-16	05/21/05		1.8	91	1 U	28	230	5.6	2 U	6.5	160	65	1 U	**588**
MW-16	10/20/05		1.8	91	1 U	28	230	5.6	2 U	6.5	160	65	1 U	**588**
MW-16	05/08/06		2	94	1 U	27	290	7.3	2 U	9.1	170	78	1 U	**677**
MW-16	01/04/07		5	94	5 U	24	280	5	10 U	5.3	160	63	5 U	**636**
MW-16	10/08/07		2	100	1	28	260	14	2 U	8	140	61	1 U	**614**
MW-16	05/17/08		20 U	130	20 U	39	320	20 U	40 U	20 U	170	78	20 U	**737**
MW-16	12/18/08	Dilution	1.3 J	100	1 J	2 U	240	35	0.7 J	4.6	120	56	2 U	**559**
MW-16	06/20/09	Dilution	1.6 J	110	2 U	2 U	39	6.8	2 U	5.5	170	42	2 U	**375**
MW-16	11/28/09	Dilution	1.6 J	110	2 U	7.9	56	6.9	0.88 J	6.1	180	55	2 U	**424**
MW-16	06/25/10		1.4	93	0.21 J	21	51	3.8	1 U	8.7	200	58	1 U	**437**
MW-16	11/27/10	Dilution	1.4 J	78	2 U	24	45	1.6 J	2 U	10	180	60	2 U	**400**
MW-16	06/01/11		1.2	81	1 U	19	40	3.2	1 U	11	160	54	1 U	**369**
MW-16	12/28/11		1.1	71	1 U	17	27	2.7	5 U	11	130	42	1 U	**302**
MW-16	06/28/12		1.1	72	1 U	5.2	25	3.3	5 U	11	120	41	1 U	**279**
MW-16	11/24/12		0.9 J	68	1 U	13	22	2.4	5 U	10	110	35	1 U	**261**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-47	10/06/93		1 U	5	1 U	2	3	1 U	2 U	1	9	5		**25**
MW-47	06/01/99		1 U	1.1	1 U	0.49	1.3	1 U	2 U	0.53	3.5	2.8	1 U	**10**
MW-47	10/27/99		1 U	1.1	1 U	0.87 J	4.5	0.05 J	2 U	2.2	6.5	5.7	1 U	**21**
MW-47	02/17/00		1 U	0.32 J	1 U	0.1 J	0.18 J	1 U	2 U	0.27 J	1	0.58 J	1 U	**2**
MW-47	04/18/00		1 U	0.53 J	1 U	0.18 J	0.36 J	1 U	2 U	0.27 J	1	0.66 J	1 U	**3**
MW-47	07/27/00		1 U	0.61	1 U	0.13	0.38	1 U	2 U	0.64	1.2	0.82	1 U	**4**
MW-47	11/08/00		0.17	0.55	1 U	0.1	0.25	1 U	2 U	0.45	0.58	0.37	1 U	**2**
MW-47	04/10/01		0.28	0.57	1 U	1	0.31	1 U	2 U	0.48	1.1	0.56	1 U	**4**
MW-47	10/31/01		0.92	0.21	1 U	1 U	1 U	1 U	2 U	0.38	0.34	0.25	1 U	**2**
MW-47	04/30/02		1.3	0.13	1 U	1 U	0.13	1 U	2 U	0.33	0.23	0.27	1 U	**2**
MW-47	10/17/02		1	1 U	1 U	1 U	1 U	1 U	0.6	1 U	1 U	1 U	1 U	**2**
MW-47	04/22/03		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	0.67 J	1 U	1 U	**1**
MW-47	12/28/03		1 U	1 U	1 U	0.51 J	1 U	1 U	1 U	0.77 J	0.59 J	1 U	1 U	**2**
MW-47	04/28/04		1 U	0.54	1 U	1 U	1 U	1 U	2 U	1 U	0.91	0.58	1 U	**2**
MW-47	05/21/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1.4	1 U	1 U	**1**
MW-47	06/28/06		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-47	01/05/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-47	10/08/07		1 U	2	1 U	0.9	2	1 U	2 U	0.6	3	1	1 U	**10**
MW-47	05/17/08		1 U	1	1 U	1 U	1	1 U	2 U	1 U	4	1	1 U	**7**
MW-47	11/29/08	Fld Dupe	0.15 J	1.58	1 U	0.34 J	0.96 J	1 U	1 U	0.61 J	2.89	1.15	1 U	**8**
MW-47	11/29/08		1 U	1.6	1 U	1 U	0.93 J	1 U	1 U	0.62 J	2.91	1.17	1 U	**7**
MW-47	06/20/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**0**
MW-47	11/28/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**0**
MW-47	06/24/10		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**0**
MW-47	11/29/10		1 U	0.27 J	1 U	1 U	1 U	1 U	1 U	1 U	0.3 J	1 U	1 U	**1**
MW-47	06/03/11		1 U	2	1 U	0.68 J	0.7 J	1 U	1 U	0.33 J	2.7	1.2	1 U	**8**
MW-47	12/29/11		1 U	0.35 J	1 U	1 U	1 U	1 U	5 U	0.4 J	0.85 J	0.64 J	1 U	**2**
MW-47	06/26/12		1 U	1 U	1 U	1 U	1 U	1 U	5 U	0.29 J	1 U	1 U	1 U	**0**
MW-47	11/25/12		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	**0**
MW-101A	10/04/93		4	150	17 U	43	190		17 U	17 U	650	180		**1217**
MW-101A	04/20/99		7.3	230	3.4	63	540	9.3	2 U	16	580	200	1 U	**1649**
MW-101A	10/25/99		5.6 J	240	50 U	64	620	7 J	100 U	14 J	610	220	50 U	**1781**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-101A	01/27/00		6.2 J	270	50 U	61	690	40 J	100 U	15 J	740	270	50 U	**2092**
MW-101A	04/25/00		7 JB	240	50 U	65	720	7.8 J	100 JB	50 U	690	220	50 U	**2050**
MW-101A	07/26/00		6.1	210	20 U	51	730	10	40 U	4.4	620	140	20 U	**1772**
MW-101A	11/16/00		6.3	310	50 U	77	830	8.3	100 U	15	740	250	50 U	**2237**
MW-101A	04/13/01		5.6	240	50 U	81	780	8.6	100 U	14	830	270	50 U	**2229**
MW-101A	10/30/01		6.3	300	50 U	79	990	12	100 U	15	1000	300	50 U	**2702**
MW-101A	04/22/02		6.8	250	50 U	82	1000	11	100 U	18	890	280	50 U	**2538**
MW-101A	10/10/02		100 U	370	100 U	440	1200	100 U	200 U	64	1200	340	1 U	**3614**
MW-101A	04/23/03		6.28	320 E	1 U	125 E	1080 E	19.4	2 U	26.8 E	919 E	427 E	1 U	**2923**
MW-101A	04/23/03	Dilution	100 U	266	100 U	81.8 J	1110	100 U	200 U	100 U	909	309	100 U	**2676**
MW-101A	12/26/03	Dilution	100 U	268 D	100 U	101 D	1260 D	100 U	100 U	100 U	950 D	278 D	100 U	**2857**
MW-101A	12/26/03		8.18	313 E	3.83	128 E	1080 E	21.8	1 U	51.7 E	796 E	344 E	1 U	**2747**
MW-101A	04/28/04		100 U	265	100 U	98.1	1230	100 U	200 U	56.4	1040	302	100 U	**2992**
MW-101A	05/21/05		10 U	260	10 U	89	1100	13	20 U	80	850	250	10 U	**2642**
MW-101A	01/12/06		4.5	220	5 U	37	990	44	10 U	61	800	220	5 U	**2377**
MW-101A	05/08/06		4.4	25 U	1 U	76	1100	17	2 U	93	970	270	1 U	**2530**
MW-101A	01/04/07		10 U	180	10 U	48	840	21	20 U	56	820	190	10 U	**2155**
MW-101A	10/07/07		4	220	2	38	790	72	2 U	67	590	200	1 U	**1983**
MW-101A	05/17/08		50 U	260	50 U	100	1000	50 U	100	64	740	240	50 U	**2504**
MW-101A	11/28/08	Dilution	4.1 J	233	2.15 J	57.5	908	38.4	1.8 J	56.2	691	214	5 U	**2206**
MW-101A	06/10/09	Dilution	4.3 J	230	2 J	50	870	30	5 U	56	550	190	5 U	**1982**
MW-101A	11/27/09	Dilution	5.2 J	280	10 U	70	990	36	10 U	47	550	220	10 U	**2198**
MW-101A	06/28/10	Dilution	2 U	54	2 U	15	210	6	2 U	6.8	90	38	2 U	**420**
MW-101A	06/28/10	Fld Dupe	2 U	51	2 U	14	200	5.3	2 U	6.3	86	37	2 U	**400**
MW-101A	11/26/10	Dilution	3.2 J	280	10 U	68	1100	18	10 U	36	550	230	10 U	**2285**
MW-101A	05/31/11	Dilution	4.5 J	310	10 U	46	1200	75	10 U	36	510	190	10 U	**2372**
MW-101A	12/28/11	Dilution	4.3 J	290	2.8 J	62	1200	49	50 U	52	540	180	10 U	**2380**
MW-101A	12/28/11	Fld Dupe	4.3 J	290	10 U	64	1200	52	50 U	52	540	180	10 U	**2382**
MW-101A	06/25/12	Dilution	5.2 J	320	10 U	72	1600	66	2.7 J	56	650	190	10 U	**2962**
MW-101A	11/24/12	Dilution	3.4 J	240	10 U	39	1200	57	50 U	55	500	160	10 U	**2254**
MW-101B	10/04/93		5	140	25 U	42	190		25 U	84	560	180		**1201**
MW-101B	04/20/99		3.6	150	10 U	36	520	10 U	20 U	45	690	140	10 U	**1585**
MW-101B	10/25/99		3.6 J	140	25 U	38	430	3.2 J	50 U	47	580	150	25 U	**1392**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-101B	01/27/00		50 U	140	50 U	33 J	490	50 U	100 U	42 J	570	150	50 U	**1425**
MW-101B	04/25/00		4.5 J	150	50 U	37 J	510	5.2 J	100 JB	33 J	590	140	50 U	**1570**
MW-101B	07/26/00		4.4	150	20 U	41	700	4	40 U	39	750	140	20 U	**1828**
MW-101B	11/16/00		3.3	170	25 U	35	550	3.9	50 U	18	450	120	25 U	**1350**
MW-101B	04/13/01		50 U	140	50 U	42	570	50 U	100 U	39	620	160	50 U	**1571**
MW-101B	10/30/01		3.5	150	25 U	33	580	4	50 U	21	440	140	25 U	**1372**
MW-101B	04/22/02		4.4	140	50 U	37	630	4.4	3.3	48	580	140	50 U	**1587**
MW-101B	10/10/02		50 U	230	50 U	290	850	50 U	100 U	80	840	180	1 U	**2470**
MW-101B	04/23/03		3.62	202 E	1 U	66 E	891 E	11.7	2 U	67.1 E	753 E	206 E	1 U	**2200**
MW-101B	04/23/03	Dilution	50 U	162	50 U	45 J	795	50 U	100 U	50.7	656	160	50 U	**1869**
MW-101B	12/26/03		4.11	222 E	1 U	70.1 E	893 E	13	1 U	68 E	671 E	180 E	1 U	**2121**
MW-101B	12/26/03	Dilution	100 U	188 D	100 U	100 U	963 D	100 U	100 U	100 U	696 D	148 D	100 U	**1995**
MW-101B	04/28/04		50 U	226	50 U	59.4	1140	50 U	100 U	61.8	843	174	50 U	**2504**
MW-101B	05/21/05		10 U	200	10 U	50	920	10 U	20 U	47	610	130	10 U	**1957**
MW-101B	01/12/06		5 U	200	5 U	42	890	6.3	10 U	41	570	120	5 U	**1869**
MW-101B	05/08/06		10 U	230	10 U	52	1100	10 U	20 U	50	660	130	1 U	**2222**
MW-101B	01/04/07		10 U	210	10 U	46	950	10 U	20 U	46	620	120	10 U	**1992**
MW-101B	10/07/07		2	200	2	47	790	12	2 U	44	460	110	1 U	**1667**
MW-101B	05/17/08		50 U	240	50 U	64	960	50 U	100	52	560	130	50 U	**2106**
MW-101B	11/28/08	Dilution	2.4 J	181	1.75 J	36.2	760	7.45	1.35 J	41.1	438	96.3	5 U	**1566**
MW-101B	06/10/09	Dilution	3.1 J	160	1.8 J	31	750	7.1	5 U	36	390	81	5 U	**1460**
MW-101B	11/27/09	Dilution	2.6 J	170	5 U	37	840	8.4	5 U	37	400	81	5 U	**1576**
MW-101B	06/28/10	Dilution	10 U	130	10 U	35	790	9 J	10 U	32	320	70	10 U	**1386**
MW-101B	11/26/10	Dilution	10 U	130	10 U	36	850	10 U	10 U	32	430	77	10 U	**1555**
MW-101B	05/31/11	Dilution	5 U	140	5 U	32	910	6.2	5 U	30	420	63	5 U	**1601**
MW-101B	12/28/11	Dilution	1.7 J	120	0.86 J	26	270	5.5	10 U	25	380	40	2 U	**869**
MW-101B	06/25/12	Dilution	1.9 J	120	5 U	25	47	4.3 J	25 U	24	430	27	5 U	**679**
MW-101B	11/24/12	Dilution	1.4 J	120	2.5 U	26	33	4.1	0.88 J	25	430	26	2.5 U	**666**
MW-101C	10/06/93		100 U	140	100 U	59	210	100	100 U	72	650	190		**1421**
MW-101C	04/20/99		3.5	140	10 U	34	550	10 U	20 U	45	740	140	10 U	**1653**
MW-101C	10/25/99		3 J	110	25 U	31	380	2.5 J	50 U	42	480	130	25 U	**1179**
MW-101C	01/27/00		20 U	110	20 U	28	370	2.8 J	40 U	42	460	120	20 U	**1133**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-101C	04/25/00		3.9 J	120	50 U	28 J	420	3.5 J	100 JB	31 J	450	100	50 U	**1256**
MW-101C	07/26/00		3.6	110	20 U	25	390	2.7	40 U	21	390	82	20 U	**1024**
MW-101C	11/13/00		2.6	130	25 U	24	420	2.7	50 U	34	370	100	25 U	**1083**
MW-101C	04/12/01		2.5	100	25 U	27	420	3	50 U	37	450	110	25 U	**1150**
MW-101C	10/30/01		2.9	120	25 U	21	510	11	50 U	32	470	110	25 U	**1277**
MW-101C	04/22/02		3.2	120	25 U	31	570	4.2	50 U	41	490	120	25 U	**1379**
MW-101C	10/10/02		50 U	200	50 U	200	660	50 U	28	150	650	130	1 U	**2018**
MW-101C	04/23/03		3	157 E	1 U	44.3 E	750 E	12.1	2 U	42 E	602 E	152 E	1 U	**1762**
MW-101C	04/23/03	Dilution	50 U	125	50 U	35.8 J	626	50 U	100 U	36.7 J	489	121	50 U	**1434**
MW-101C	12/30/03		3.64	193 E	1 U	57.2 E	782 E	32.5 E	1 U	63.2 E	644 E	175 E	1 U	**1951**
MW-101C	12/30/03	Dilution	50 U	141 D	50 U	42.4 JD	775 D	50 U	50 U	44.7 JD	628 D	142 D	50 U	**1773**
MW-101C	11/26/08	Dilution	2.45 J	157	2.05 J	33.8	682	6.8	1.5 J	27.9	398	86.4	5 U	**1398**
MW-101C	06/10/09	Dilution	2.6 J	120	5 U	22	550	5.8	5 U	24	270	56	5 U	**1050**
MW-101C	11/27/09	Dilution	2.4 J	120	5 U	28	620	5.5	5 U	25	290	63	5 U	**1154**
MW-101C	06/28/10	Dilution	5 U	85	5 U	23	570	5.4	5 U	19	220	44	5 U	**966**
MW-101C	11/26/10	Dilution	1.9 J	98	1.8 J	24	640	5 U	5 U	20	310	48	5 U	**1144**
MW-101C	05/31/11	Dilution	5 U	110	5 U	25	780	5.4	5 U	21	340	47	5 U	**1328**
MW-101C	12/28/11	Dilution	1.4 J	92	2 U	20	260	4	10 U	18	290	29	2 U	**714**
MW-101C	06/25/12	Dilution	1.4 J	89	2.5 U	17	89	3.3	12 U	16	300	20	2.5 U	**536**
MW-101C	11/30/12	Dilution	1.3 J	99	2.5 U	20	40	3.6	12 U	18	360	20	2.5 U	**562**
MW-101C	11/30/12	Fld Dupe	1.4 J	99	5 U	20	40	3.6 J	25 U	18	360	20	5 U	**562**
MW-101D	10/06/93		50 U	72	50 U	34	130	50	50 U	31	300	96		**713**
MW-101D	04/21/99		2.6	80	5 U	24	230	5 U	10 U	23	300	80	5 U	**740**
MW-101D	01/27/00		1.6 J	42	10 U	14	130	1.5 J	20	18	180	54	10 U	**461**
MW-101D	04/25/00		2.4 JB	70	20 U	23	250	1.9 J	40 JB	23	270	81	20 U	**761**
MW-101D	07/26/00		2.5	60	1.2	14	180	1.1	20 U	2.9	180	33	10 U	**475**
MW-101D	11/16/00		2.2	76	1.3	17	210	1.3	20 U	3.8	180	46	10 U	**538**
MW-101D	04/13/01		2.2	66	10 U	21	250	1.9	20 U	18	250	73	10 U	**682**
MW-101D	10/30/01		2.3	70	20 U	22	260	2	40 U	26	300	80	20 U	**762**
MW-101D	04/30/02		2.5	66	20 U	22	260	2	40 U	20	240	67	20 U	**680**
MW-101D	10/10/02		20 U	100	20 U	94	280	20 U	40 U	20 U	300	58	1 U	**832**
MW-101D	04/23/03	Dilution	20 U	64.7	20 U	23.9	291	20 U	40 U	23	254	73.7	20 U	**730**
MW-101D	04/23/03		2.17	72.1 E	1 U	28.2 E	323 E	5.34	2 U	24.8	297 E	82.6 E	1 U	**835**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-101D	04/23/03	Fld Dupe	3	155 E	1 U	44.3 E	744 E	50 U	2 U	40.7 E	500	122	1 U	**1609**
MW-101D	12/28/03	Dilution	10 U	41.8 D	10 U	17.6 D	179 D	10 U	10 U	16 D	168 D	51.6 D	10 U	**474**
MW-101D	12/28/03		1.87	47 E	0.88 J	19.8	184 E	8.27	1 U	19.2	202 E	58.3 E	1 U	**541**
MW-101D	04/28/04		25 U	68	25 U	22.2	323	25 U	50 U	20.7	249	62.3	25 U	**745**
MW-101D	05/21/05		2	74	1 U	28	330	1 U	2 U	22	230	61	1 U	**747**
MW-101D	01/12/06		2 U	53	2 U	5	85	2 U	4 U	14	190	20	2 U	**367**
MW-101D	06/23/06		10 U	77	10 U	24	410	10 U	20 U	20	220	56	10 U	**807**
MW-101D	01/04/07		5	56	5 U	16	200	5 U	10 U	15	180	46	5 U	**518**
MW-101D	10/07/07		10 U	55	10 U	22	240	10 U	10 U	18	180	50	10 U	**565**
MW-101D	05/17/08	Dilution	25 U	81 D	25 U	28 D	380 D	25 U	50 U	25 U	220 D	60 D	25 U	**769**
MW-101D	05/17/08		10 U	98	10 U	35	420 E	10 U	18 J	26	250 E	70	10 U	**917**
MW-101D	11/28/08	Dilution	1.46 J	41.6	0.58 J	15	199	1.94 J	0.62 J	16.4	137	39.3	2 U	**453**
MW-101D	06/10/09	Dilution	1.8 J	68	0.86 J	19	340	3.6	2 U	20	180	47	2 U	**680**
MW-101D	11/27/09	Dilution	1.5 J	64	2.5 U	18	290	4.1	2.5 U	16	150	39	2.5 U	**583**
MW-101D	06/28/10	Dilution	2.5 U	44	2.5 U	16	270	3.1	2.5 U	13	110	32	2.5 U	**488**
MW-101D	11/26/10	Dilution	1.4 J	51	1 J	18	320	0.62 J	2.5 U	17	160	38	2.5 U	**607**
MW-101D	05/31/11	Dilution	1.4 J	60	2 U	17	210	2.4	2 U	15	170	31	2 U	**507**
MW-101D	12/28/11		1	42	1 U	13	39	2.1	5 U	12	120	19	1 U	**248**
MW-101D	06/25/12		1.1	47	1 U	14	33	1.8	5 U	12	150	19	1 U	**278**
MW-101D	11/24/12		1	42	1 U	13	27	1.6	5 U	11	140	16	1 U	**252**
MW-102A	09/28/93		2 U	26	2 U	4	32	2	23	2	34	6		**129**
MW-102A	05/20/99		1 U	43	0.25	1.2	54	1.8	2 U	0.6	51	6.3	1 U	**158**
MW-102A	10/25/99		0.15 J	43	5 U	2.5 J	61	1.7 J	10 U	3.1 J	57	15	5 U	**183**
MW-102A	02/16/00		5 U	64	5 U	2.8 J	90	3 J	10 U	5 U	97	14	5 U	**271**
MW-102A	04/25/00	Fld Dupe	0.14 J	43	5 U	1.4 J	49	1.3 J	10 JB	5 U	57	7.7	5 U	**170**
MW-102A	04/25/00		5 U	43	5 U	1.5 J	49	1.4 J	10 JB	5 U	57	7.6	5 U	**170**
MW-102A	07/26/00		10 U	71	10 U	2.7	95	2.5	20 U	10 U	100	16	10 U	**287**
MW-102A	11/16/00		5 U	91	5 U	2.8	110	2.7	10 U	5 U	88	14	5 U	**309**
MW-102A	04/10/01		10 U	91	10 U	4.2	140	4.4	20 U	10 U	120	22	10 U	**382**
MW-102A	10/17/01		10 U	77	10 U	2.3	110	4.1	20 U	10 U	88	16	10 U	**297**
MW-102A	04/30/02		5 U	47	5 U	1.6	65	1.9	10 U	5 U	62	11	5 U	**189**
MW-102A	10/10/02		20 U	130	20 U	20 U	160	20 U	40 U	20 U	140	26	1 U	**456**
MW-102A	04/25/03	Dilution	10 U	92.9	10 U	10 U	137	10 U	20 U	10 U	102	22.2	10 U	**354**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-102A	04/25/03		1 U	101 E	1 U	4.17	153 E	5.08	2 U	1 U	123 E	25.7 E	1 U	**412**
MW-102A	12/26/03		1 U	108 E	1 U	4.14	145 E	5.89	1 U	1 U	111 E	20.1	1 U	**394**
MW-102A	12/26/03	Dilution	10 U	118 D	10 U	10 U	156 D	5.56 JD	10 U	10 U	114 D	22.4 D	10 U	**416**
MW-102A	04/28/04		2 U	39	2 U	2 U	34.2	1.45	4 U	2 U	37.3	6.93	2 U	**119**
MW-102A	05/02/05		1 U	19	1 U	1 U	16	0.84	2 U	1 U	19	3.5	1 U	**58**
MW-102A	05/02/05	Fld Dupe	1 U	24	1 U	1 J	21	1.1	2 U	1 U	21	4.3	1 U	**72**
MW-102A	11/02/05		1 U	71	1 U	1.9	110	5.1	2 U	1 U	57	11	1 U	**256**
MW-102A	06/22/06		1 U	39	1 U	0.98	54	1.9	2 U	1 U	31	6.6	1 U	**133**
MW-102A	11/16/06		1 U	73	1 U	1.8	120	3.3	2 U	1 U	100	15	1 U	**313**
MW-102A	10/08/07		10 U	64	10 U	4	150	5	9	10 U	95	20	10 U	**347**
MW-102A	05/19/08		10 U	68	10 U	10 U	150	10 U	20	10 U	93	18	10 U	**349**
MW-102A	11/26/08		0.18 J	58.1	0.32 J	2.81	137	4.14	1 U	1 U	82.6	17.6	1 U	**303**
MW-102A	06/11/09		0.19 J	66	0.26 J	2.6	150	4.1	1 U	1 U	82	16	1 U	**321**
MW-102A	11/27/09		1 U	96	1 U	3.5	190	5.3	1 U	1 U	89	18	1 U	**402**
MW-102A	06/28/10	Dilution	2 U	80	2 U	2.7	170	5.3	2 U	2 U	62	15	2 U	**335**
MW-102A	11/26/10	Dilution	2 U	99	2 U	3	200	5.3	2 U	2 U	90	20	2 U	**417**
MW-102A	11/26/10	Fld Dupe	2 U	95	2 U	2.7	200	4.9	2 U	2 U	87	19	2 U	**409**
MW-102A	06/01/11		1 U	94	1 U	2.2	190	6	1 U	1 U	74	16	1 U	**382**
MW-102A	12/28/11		1 U	90	1 U	1.9	170	6	5 U	1 U	63	15	1 U	**346**
MW-102A	06/27/12		1 U	79	1 U	1.4	160	5.1	5 U	1 U	52	13	1 U	**311**
MW-102A	11/30/12		1 U	82	1 U	1.6	160	5.7	5 U	1 U	59	14	1 U	**322**
MW-102B	09/28/93		1 U	1 U	1 U	1 U	1 U	1 U	3	1 U	1 U	1 U		**3**
MW-102B	05/20/99		1 U	0.99	0.63	0.32	2.1	1 U	2 U	1.1	1.4	2.1	1 U	**9**
MW-102B	10/25/99		1 U	0.93 J	0.66 J	0.4 J	2.7	1 U	2 U	2	5.1	3.7	0.14 J	**16**
MW-102B	02/16/00		1 U	0.32 J	0.47 J	1 U	0.28 J	1 U	2 U	1 U	1 U	1 U	1 U	**1**
MW-102B	04/25/00		1 U	0.36 J	0.49 J	1 U	0.48 J	1 U	2 U	1 U	0.2 J	0.09 J	1 U	**2**
MW-102B	07/26/00		1 U	0.62	0.54	1 U	0.54	1 U	2 U	1 U	1 U	1 U	0.19 J	**2**
MW-102B	11/16/00	Fld Dupe	1 U	0.74 J	0.6 J	1 U	0.59 J	1 U	2 U	1 U	1 U	1 U	0.16 J	**2**
MW-102B	11/16/00		1 U	0.76	1 U	1 U	0.62	1 U	2 U	1 U	1 U	1 U	0.17 J	**2**
MW-102B	04/10/01		1 U	0.71	0.61	1 U	0.71	1 U	2 U	1 U	1 U	1 U	0.11 J	**2**
MW-102B	10/17/01		1 U	0.83	1 U	1 U	1.2	1 U	2 U	1 U	1 U	1 U	0.13 J	**2**
MW-102B	04/30/02		1 U	1	0.58	1 U	1.4	0.13	2 U	1 U	1 U	1 U	0.089	**3**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2 _	
MW-102B	10/10/02		1 U	2	1 U	1 U	2	1 U	0.6	1 U	1 U	1 U	1 U	**5**
MW-102B	04/25/03		1 U	1.35	1 U	1 U	2.27	1 U	2 U	1 U	1 U	1 U	1 U	**4**
MW-102B	12/26/03		1 U	1.64	0.64 J	1 U	2.9	1 U	1 U	1 U	1 U	1 U	1 U	**5**
MW-102B	04/28/04		1 U	1.73	0.62	1 U	3.2	1 U	2 U	1 U	1 U	1 U	1 U	**6**
MW-102B	05/02/05		1 U	1.6	0.48	1 U	2.4	1 U	2 U	1 U	1 U	1 U	1 U	**4**
MW-102B	11/02/05		1 U	1.9	1 U	1 U	3.5	1 U	2 U	1 U	1 U	1 U	1 U	**5**
MW-102B	06/22/06		1 U	2.3	1 U	1 U	4.3	1 U	2 U	1 U	1 U	1 U	1 U	**7**
MW-102B	11/16/06		1 U	3	1 U	1 U	5	1 U	2 U	1 U	1 U	1 U	1 U	**8**
MW-102B	10/08/07		1 U	3	0.5	1 U	4	1 U	2 U	1 U	1 U	1 U	1 U	**8**
MW-102B	05/19/08		1 U	4	1 U	1 U	6	1 U	2 U	1 U	1 U	1 U	1 U	**10**
MW-102B	11/26/08		1 U	2.8	0.66 J	1 U	5.11	0.28 J	1 U	1 U	1 U	1 U	0.18 J	**9**
MW-102B	06/11/09		1 U	3.2	0.65 J	1 U	5	1 U	1 U	1 U	1 U	1 U	1 U	**9**
MW-102B	11/27/09		1 U	3.5	0.56 J	1 U	5.6	1 U	1 U	1 U	1 U	1 U	1 U	**10**
MW-102B	06/28/10		1 U	3	0.69 J	1 U	4.4	1 U	1 U	1 U	1 U	1 U	1 U	**8**
MW-102B	11/26/10		1 U	2.9	0.67 J	1 U	5	1 U	1 U	1 U	1 U	1 U	1 U	**9**
MW-102B	06/01/11		1 U	2.8	1 U	1 U	4	1 U	1 U	1 U	1 U	1 U	1 U	**7**
MW-102B	12/28/11		1 U	2.8	1 U	1 U	4.1	1 U	5 U	1 U	1 U	1 U	0.32 J	**7**
MW-102B	06/27/12		1 U	2.7	1 U	1 U	3.8	1 U	5 U	1 U	1 U	1 U	0.32 J	**7**
MW-102B	06/27/12	Fld Dupe	1 U	2.7	1 U	1 U	3.9	1 U	5 U	1 U	1 U	1 U	0.31 J	**7**
MW-102B	11/30/12		1 U	2.8	0.52 J	1 U	4.6	1 U	5 U	1 U	1 U	1 U	0.43 J	**8**
MW-102C	09/28/93		12 U	160	12 U	68	140	12 U	55	44	160	140		**767**
MW-102C	05/20/99		2.5	180	4	59	390	10 U	20 U	33	170	140	10 U	**979**
MW-102C	10/25/99		3 J	210	25 U	78	460	25 U	50 U	46	250	170	25 U	**1217**
MW-102C	02/16/00		0.66 J	32	0.91 J	12	61 E	0.57 J	0.38 J	5.9	60 E	26	2 U	**199**
MW-102C	02/16/00	Dilution	0.52 DJ	24 D	5 U	9 D	44 D	5 U	10 U	4.4 DJ	44 D	20 D	5 U	**146**
MW-102C	04/25/00		0.91 J	44	5 U	5.2	65	0.96 J	10 JB	0.67 J	60	10	5 U	**197**
MW-102C	07/26/00		0.64	29	0.8	4.5	39	0.41	4 U	0.99	44	8.2	2 U	**128**
MW-102C	11/16/00		0.32	19	2 U	4.5	28	0.26	4 U	1.1	23	8.3	2 U	**84**
MW-102C	04/10/01		0.94	48	5 U	2.6	39	5 U	10 U	0.8	90	5.4	5 U	**187**
MW-102C	10/17/01		0.6	29	4 U	8.9	53	0.39	8 U	3.5	46	17	4 U	**158**
MW-102C	04/30/02		2.1	110	2.4	40	240	3.3	20 U	19	170	78	10 U	**665**
MW-102C	10/10/02		5 U	56	5 U	54	87	5 U	10 U	4 J	69	20	1 U	**290**
MW-102C	04/25/03		1.16	83.3 E	1.57	33 E	200 E	4	2 U	16.3	143 E	64.8 E	1 U	**547**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	MCL –Sample Type	CFM NA	1,1-DCA NA	1,2-DCA 5	1,1-DCE 7	c1,2-DCE 70	t1,2-DCE 100	MC 5	PCE 5	1,1,1-TCA 200	TCE 5	VC 2	Total VOCs
MW-102C	04/25/03	Dilution	10 U	48.4	10 U	18.6	112	10 U	20 U	7.94 J	73.2	34.9	10 U	**295**
MW-102C	12/26/03		0.6 J	40.4 E	0.76 J	9.18	69 E	1.04	1 U	1.6	60.2 E	16.3	1 U	**199**
MW-102C	12/26/03	Dilution	4 U	42.6 D	4 U	9.85 D	79.1 D	4 U	4 U	4 U	59 D	16.2 D	4 U	**207**
MW-102C	04/28/04		25 U	105	25 U	38.2	278	25 U	50 U	20.9	136	70.4	25 U	**649**
MW-102C	05/02/05		0.74	69	1.2	0.62	22	1 U	2 U	1.1	110	1.5	1 U	**206**
MW-102C	11/02/05		1 U	3.4	1 U	1.3	7.4	1 U	2 U	1 U	6.4	2.9	1 U	**21**
MW-102C	11/02/05	Fld Dupe	1 U	18	1 U	5.8	46	1 U	2 U	2.5 H	15	9.9	1 U	**97**
MW-102C	06/22/06		1 U	23	1 U	8.4	49	1 U	2 U	4.9	19	15	1 U	**119**
MW-102C	11/16/06		1 U	69	1.3	10	120	0.97 J	2 U	4	70	23	1 U	**298**
MW-102C	10/08/07		0.4	60	1	22	170	2	2 U	10	35	34	1 U	**334**
MW-102C	10/08/07	Fld Dupe	0.5 J	90 D	1	33 D	270 D	4	2 U	16	52 D	51 D	0.6 J	**518**
MW-102C	05/19/08		10 U	66	10 U	26	210	10 U	21	12	74	37	10 U	**446**
MW-102C	11/26/08		0.21 J	18.9	0.33 J	5.75	56.6	0.79 J	1 U	2.66	18.4	9.54	1 U	**113**
MW-102C	06/11/09		0.31 J	36	0.57 J	6.1	99	0.74 J	1 U	0.94 J	23	8.9	1 U	**176**
MW-102C	11/27/09	Dilution	10 U	210	10 U	59	760	6.7 J	10 U	22	94	74	10 U	**1226**
MW-102C	06/28/10	Dilution	5 U	160	5 U	53	740	6.8	5 U	18	89	65	5 U	**1132**
MW-102C	11/26/10	Dilution	10 U	170	3.2 J	51	720	10 U	10 U	21	110	68	10 U	**1143**
MW-102C	06/01/11	Dilution	5 U	200	5 U	50	870	7	5 U	25	90	63	5 U	**1305**
MW-102C	12/28/11	Dilution	0.95 J	160	5 U	40	670	5.6	25 U	17	80	47	5 U	**1021**
MW-102C	06/27/12	Dilution	1.2 J	130	5 U	33	550	4.4 J	25 U	7.3	55	30	5 U	**811**
MW-102C	11/30/12	Dilution	0.36 J	64	0.54 J	15	200	2	10 U	4.2	41	15	2 U	**342**
MW-113A	10/08/93		7 U	92	7 U	33	110	7 U	14 U	7 U	140	56		**431**
MW-113A	05/03/99		0.9	34	0.4	10	52	1.2	2 U	1.9	59	24	1 U	**183**
MW-113A	11/10/99		2.3 J	100	10 U	27	160	2.4 J	20	3.2 J	160	69	10 U	**544**
MW-113A	02/15/00		2.1 J	91	10 U	16	160	5.7 J	20 U	2.9 J	160	71	10 U	**509**
MW-113A	04/24/00		2.1 JB	92	10 U	5.1 J	160	13	20 JB	2.4 J	160	61	10 U	**516**
MW-113A	07/27/00		2.3	86	10 U	4	110	7.5	20 U	10 U	130	22	1 U	**362**
MW-113A	11/16/00		2.3	130	10 U	9.4	200	12	20 U	2.1	170	62	10 U	**588**
MW-113A	04/12/01		2.4	10	10 U	210	210	15	20 U	3.7	200	81	10 U	**732**
MW-113A	10/31/01		2.8	110	10 U	3	240	22	20 U	3.3	200	75	10 U	**656**
MW-113A	04/29/02		2.5	100	10 U	1.5	200	23	20 U	4.5	200	70	10 U	**602**
MW-113A	10/18/02		20 U	190	20 U	240	430	20 U	40 U	20 U	370	140	1 U	**1370**
MW-113A	04/23/03		2.84	139 E	1 U	27.6 E	371 E	18.2	2 U	8.11	306 E	126 E	1 U	**999**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-113A	04/23/03	Dilution	25 U	121	25 U	33.9	325	25 U	50 U	25 U	245	101	25 U	**826**
MW-113A	12/28/03		2.93	140 E	1.38	38.3 E	345 E	10.4	1 U	9.72	309 E	124 E	1 U	**981**
MW-113A	12/28/03	Dilution	20 U	109 D	20 U	31.4 D	318 D	20 U	20 U	20 U	232 D	92.9 D	20 U	**783**
MW-113A	04/28/04		25 U	123	25 U	32.4	360	25 U	50 U	25 U	239	89.1	25 U	**844**
MW-113A	04/28/04	Fld Dupe	3.09	123	1.6	35.9	371	37.9 E	2 U	10.3	240	96.8	1 U	**920**
MW-113A	05/21/05		5 U	140	5 U	45	410	5.7	10 U	8.1	260	100	5 U	**969**
MW-113A	10/20/05		2.6	110	1 U	22	330	17	2 U	8	210	82	1 U	**782**
MW-113A	05/08/06		2.3	110	1 U	32	470	9.1	20 U	10	270	93	1 U	**996**
MW-113A	01/04/07		10 U	110	10 U	27	430	10 U	20 U	10	210	10	10 U	**797**
MW-113A	10/08/07		2	150	1	46	480	15	2 U	10	260	110	1 U	**1074**
MW-113A	05/17/08		20 U	160	20 U	54	510 E	20 U	41	20 U	280	130	20 U	**1175**
MW-113A	05/17/08	Dilution	40 U	140 D	40 U	48 D	470 D	40 U	80 U	40 U	250 D	110 D	40 U	**1018**
MW-113A	11/29/08	Dilution	2.2 J	135	1.5 J	7.25	369	40.6	1.7 J	10.5	210	98.6	5 U	**876**
MW-113A	06/11/09	Dilution	2.6 J	110	5 U	21	370	15	5 U	10	180	85	5 U	**794**
MW-113A	11/28/09	Dilution	1.5 J	110	2.5 U	1.7 J	290	44	2.5 U	12	170	84	2.5 U	**713**
MW-113A	06/29/10	Dilution	1.1 J	88	1 J	3.3	240	30	0.85 J	12	130	76	2.5 U	**582**
MW-113A	11/28/10	Dilution	0.95 J	85	0.7 J	17	250	11	2.5 U	12	110	67	2.5 U	**554**
MW-113A	06/01/11		0.96 J	88	1 U	2.4	90	14	1 U	13	120	57	1 U	**385**
MW-113A	12/29/11		1.1	95	1 U	16	50	4.3	5 U	13	130	46	1 U	**355**
MW-113A	06/25/12		1.1	100	1 U	14	48	5.3	5 U	13	140	48	1 U	**369**
MW-113A	11/24/12		1.2	110	1 U	14	43	4.4	5 U	13	140	45	1 U	**371**
MW-113B	10/19/93		2 U	14	2 U	4	12	2 U	3 U	2 U	6	6		**42**
MW-113B	04/29/99		0.54	33	0.56	12	38	0.65	2 U	1.8	17	19	1 U	**123**
MW-113B	10/27/99		0.45 J	33	5 U	8.4	39	0.55 J	10 U	1.3 J	13	20	5 U	**116**
MW-113B	02/15/00		0.65 J	48	5 U	11	62	0.83 J	10 U	1.4 J	27	30	5 U	**181**
MW-113B	04/24/00		0.61 JB	43	5 U	11	56	0.98 J	10 JB	1.2 J	21	26	5 U	**170**
MW-113B	07/27/00		0.71	38	0.6	9.4	49	0.91	10 U	0.89	17	20	5 U	**137**
MW-113B	11/16/00		0.63	55	5 U	11	62	1.3	10 U	1.4	22	27	5 U	**180**
MW-113B	04/12/01		0.56	40	5 U	8.9	53	1	10 U	5 U	17	20	5 U	**140**
MW-113B	10/31/01		0.64	50	5 U	12	67	1.1	10 U	5 U	24	29	5 U	**184**
MW-113B	04/29/02		0.6	39	5 U	9.8	60	0.97	10 U	1.3	19	23	5 U	**154**
MW-113B	10/18/02		10 U	84	10 U	88	120	10 U	5	10 U	39	42	1 U	**378**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
			–											
MW-113B	04/23/03	Dilution	10 U	58.6	10 U	17.4	115	10 U	20 U	10 U	45.6	41.9	10 U	**279**
MW-113B	04/23/03		1.05	77.3 E	1 U	23.3	143 E	6.06	2 U	3.77	65.8 E	55.8 E	2.2	**378**
MW-113B	12/28/03		0.97 J	71.3 E	1 U	21.4	134 E	4.01	1 U	3.72	53.4 E	52.1 E	1.24	**342**
MW-113B	12/28/03	Dilution	10 U	65.1 D	10 U	19.1 D	129 D	10 U	10 U	10 U	43.1 D	45.9 E	10 U	**302**
MW-113B	04/28/04		10 U	70	10 U	19.8	143	10 U	20 U	10 U	44.9	42.7	10 U	**320**
MW-113B	05/21/05		1 U	64	1 U	19	140	1.8	2 U	2.9	39	39	4.8	**311**
MW-113B	10/20/05		1 U	78	1 U	22	170	1.9	2 U	3.8	45	47	1 U	**368**
MW-113B	05/08/06		1 U	64	1 U	21	140	1.9	2 U	3.6	33	37	9.2	**310**
MW-113B	01/04/07		1 U	61	1 U	20	120	1.7	2 U	3	30	38	1.4	**275**
MW-113B	10/08/07		0.5	56	0.6	17	120	2	2 U	3	21	30	15	**265**
MW-113B	05/17/08		10 U	66	10 U	19	140	10 U	19 J	10 U	25	34	17	**320**
MW-113B	11/29/08		0.71 J	71.3	0.92 J	20.4	169	2.15	1 U	3.49	28.8	41.5	6.2	**344**
MW-113B	06/11/09		0.73 J	71	0.87 J	19	180	2.2	1 U	3.6	29	42	6.9	**355**
MW-113B	11/28/09		0.69 J	77	0.76 J	22	190	2.5	1 U	3.9	31	41	8	**377**
MW-113B	06/29/10	Dilution	2 U	63	2 U	19	150	2.7	2 U	3	19	33	9	**299**
MW-113B	11/28/10	Dilution	2 U	67	0.8 J	19	160	3	2 U	4.2	26	37	8.8	**326**
MW-113B	06/01/11		0.46 J	66	0.61 J	18	140	2.3	1 U	4.1	23	36	11	**301**
MW-113B	12/29/11		0.42 J	59	0.63 J	16	100	2	5 U	3.9	19	30	8.9	**240**
MW-113B	06/25/12		0.48 J	60	1 U	14	98	1.9	5 U	3.6	17	28	9.4	**232**
MW-113B	11/24/12		0.34 J	59	0.46 J	14	78	1.8	5 U	3.7	18	26	7.5	**209**
MW-114A	10/05/93		1 U	2	1 U	4	5	1 U	2 U	1 U	6	2		**19**
MW-114A	04/28/99		5 U	6.7	5 U	46	14	5 U	10 U	1.9 J	250	34	5 U	**353**
MW-114A	10/26/99		0.34 J	7.1 J	25 U	48	11 J	25 U	50 U	25 U	290	47	25 U	**403**
MW-114A	01/31/00		10 U	5 J	10 U	34	6.6 J	10 U	1.5 J	10 U	220	33	10 U	**300**
MW-114A	04/24/00		10 U	4.2 J	10 U	26	5.6 J	10 U	20 JB	10 U	160	24	10 U	**240**
MW-114A	07/27/00		10 U	3.9	10 U	24	5.4	10 U	20 U	10 U	140	22	10 U	**195**
MW-114A	11/13/00		10 U	4.2	10 U	20	4.7	10 U	20 U	10 U	120	19	10 U	**168**
MW-114A	04/12/01		5 U	2.7	5 U	18	3.9	5 U	10 U	5 U	120	20	5 U	**165**
MW-114A	10/31/01		5 U	2.5	5 U	15	3.6	5 U	10 U	5 U	100	18	5 U	**139**
MW-114A	04/25/02		5 U	3.1	5 U	16	4.1	5 U	10 U	5 U	100	22	5 U	**145**
MW-114A	04/25/02	Fld Dupe	5 U	3.1 J	5 U	16	4 J	5 U	10 U	5 U	100	22	5 U	**145**
MW-114A	10/15/02		10 U	10 U	10 U	140	7	10 U	20 U	10 U	170	38	1 U	**355**
MW-114A	04/23/03	Dilution	10 U	10 U	10 U	12.9	10 U	10 U	20 U	10 U	80.2	20.8	10 U	**114**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-114A	04/23/03		1 U	3.28	1 U	13.4	4.09	1 U	2 U	1 U	94.6 E	23.5	1 U	**139**
MW-114A	12/26/03	Dilution	4 U	2.86 JD	4 U	10.3 D	3.6 JD	4 U	4 U	4 U	70.1 D	15.9 E	4 U	**103**
MW-114A	12/26/03		1 U	2.86	1 U	9.96	3.62	1 U	1 U	1 U	73.9 E	16.3	1 U	**107**
MW-114A	04/28/04		5 U	3.69	5 U	12	4.25	5 U	10 U	5 U	79.9	20.8	5 U	**121**
MW-114A	05/21/05		1 U	2.5	1 U	5.7	3.3	1 U	2 U	1 U	28	7.9	1 U	**47**
MW-114A	10/20/05		1 U	2.6	1 U	7.2	2.9	1 U	2 U	1 U	39	9.8	1 U	**62**
MW-114A	05/06/06		1 U	3.4	1 U	9.4	3.7	1 U	2 U	1 U	44	12	1 U	**73**
MW-114A	01/04/07		1 U	3.5	1 U	11	3.3	1 U	2 U	1 U	51	9.6	1 U	**78**
MW-114A	10/08/07		1 U	2	1 U	7	2	1 U	2 U	2 U	34	5	1 U	**50**
MW-114A	05/17/08		2 U	2	2 U	5	3	2 U	3 J	2 U	28	4	2 U	**45**
MW-114A	11/29/08		1 U	0.28 J	1 U	1 U	1 U	1 U	1 U	1 U	1.09	1 U	1 U	**1**
MW-114A	06/11/09		0.16 J	1 U	1 U	1 U	1 U	1 U	1 U	1 U	0.9 J	1 U	1 U	**1**
MW-114A	11/28/09		0.46 J	1.9	1 U	3.9	1.3	1 U	1 U	1 U	36	2.7	1 U	**46**
MW-114A	06/25/10		1 U	3.2	1 U	6.6	2.2	1 U	1 U	1 U	70	4.4	1 U	**86**
MW-114A	11/27/10		1 U	2.8	1 U	8.5	2.1	1 U	1 U	1 U	65	4.7	1 U	**83**
MW-114A	06/01/11		1 U	4.2	1 U	10	2.9	1 U	1 U	1 U	85	5.5	1 U	**108**
MW-114A	12/28/11		1 U	3.6	1 U	9.1	2.6	1 U	5 U	0.18 J	65	4.1	1 U	**85**
MW-114A	06/27/12		0.21 J	4.3	1 U	5.6	3	1 U	5 U	1 U	71	4.2	1 U	**88**
MW-114A	11/24/12		1 U	2.9	1 U	1.6	2.4	0.22 J	5 U	1 U	27	1.8	1 U	**36**
MW-114B	10/04/93		2 U	14	2 U	4	12	2 U	3 U	2 U	6	6		**42**
MW-114B	04/28/99		1 U	0.89	1 U	0.6	3.3	1 U	2 U	1	4	6.2	1 U	**16**
MW-114B	10/26/99		1 U	1	1 U	0.46 J	3.3	1 U	2 U	0.66 J	1.2	8.2	1 U	**15**
MW-114B	01/31/00		1 U	0.81 J	1 U	0.18 J	2.3	1 U	2 U	1 U	1 U	5.7	1 U	**9**
MW-114B	04/24/00		1 U	0.68 J	1 U	0.11 J	1.7	1 U	2 JB	1 U	0.05 J	1.8	1 U	**6**
MW-114B	07/27/00	Fld Dupe	1 U	1	1 U	0.26 J	3	1 U	2 U	1 U	1 U	7.5	1 U	**12**
MW-114B	07/27/00		1 U	1	1 U	0.26	3	1 U	2 U	1 U	1 U	7.9	1 U	**12**
MW-114B	11/13/00		1 U	1.2	1 U	0.13	2.4	1 U	2 U	1 U	1 U	3.5	1 U	**7**
MW-114B	04/12/01		1 U	0.98	1 U	0.26	2.9	1 U	2 U	1 U	1 U	8.2	1 U	**12**
MW-114B	10/31/01		1 U	0.96	1 U	0.13	2.2	1 U	2 U	1 U	1 U	4.8	1 U	**8**
MW-114B	04/25/02		1 U	1.1	1 U	0.29	3	0.04	2 U	1 U	1 U	7.2	1 U	**12**
MW-114B	10/15/02		1 U	2	3	1	3	1 U	0.6	1 U	1 U	9	1 U	**19**
MW-114B	04/23/03		1 U	1.15	1 U	1 U	2.84	1 U	2 U	1 U	1 U	8.8	1 U	**13**
MW-114B	12/26/03		1 U	1.25	1 U	1.07	2.98	1 U	1 U	1 U	1 U	8.91	1 U	**14**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-114B	04/28/04		1 U	1.21	1 U	1 U	2.87	1 U	2 U	1 U	1 U	8.82	1 U	**13**
MW-114B	05/21/05		1 U	1.5	1 U	1 U	2.3	1 U	2 U	1 U	1 U	7.6	1 U	**11**
MW-114B	10/20/05		1 U	1.6	1 U	1 U	2.3	1 U	2 U	1 U	1 U	8.8	1 U	**13**
MW-114B	05/06/06		1 U	1 U	1 U	1 U	2.1	1 U	2 U	1 U	1 U	8.7	1 U	**11**
MW-114B	01/04/07		1 U	1.4	1 U	1 U	1.8	1 U	2 U	1 U	1 U	6.7	1 U	**10**
MW-114B	01/04/07	Fld Dupe	1 U	1.6	1 U	1 U	1.8	1 U	2 U	1 U	1 U	6.4	1 U	**10**
MW-114B	10/08/07		1 U	2	1 U	0.5	2	1 U	2 U	1 U	1 U	6	1 U	**11**
MW-114B	05/17/08		1 U	2	1 U	1 U	2	1 U	2 U	1 U	1 U	9	1 U	**13**
MW-114B	12/18/08		1 U	1.6	1 U	0.67 J	2	1 U	1 U	1 U	1 U	6.8	1 U	**11**
MW-114B	06/20/09		1 U	1.8	1 U	0.67 J	2.2	1 U	1 U	1 U	1 U	6.5	1 U	**11**
MW-114B	11/28/09		1 U	2.2	1 U	1	2	1 U	1 U	1 U	1 U	6.7	1 U	**12**
MW-114B	11/28/09	Fld Dupe	1 U	2.4	1 U	0.93 J	1.9	1 U	1 U	1 U	1 U	6.8	1 U	**12**
MW-114B	06/25/10	Fld Dupe	1 U	2	1 U	0.81 J	1.9	1 U	1 U	1 U	1 U	6.3	1 U	**11**
MW-114B	06/25/10		1 U	2.1	1 U	0.84 J	2	1 U	1 U	1 U	1 U	6.3	1 U	**11**
MW-114B	11/27/10		1 U	1.8	1 U	1	2.3	1 U	1 U	1 U	1 U	7.8	1 U	**13**
MW-114B	06/01/11		1 U	1.6	1 U	1 U	2.1	1 U	1 U	1 U	1 U	7.7	1 U	**11**
MW-114B	06/01/11	Fld Dupe	1 U	1.6	1 U	1 U	2.1	1 U	1 U	1 U	1 U	7.4	1 U	**11**
MW-114B	12/28/11		1 U	1.3	1 U	0.54 J	2.2	1 U	5 U	1 U	1 U	6.7	1 U	**11**
MW-114B	06/28/12	Fld Dupe	1 U	1.1	1 U	0.41 J	1.8	1 U	5 U	1 U	1 U	6.7	1 U	**10**
MW-114B	06/28/12		1 U	1.1	1 U	1 U	1.8	1 U	5 U	1 U	1 U	6.5	1 U	**9**
MW-114B	11/24/12	Fld Dupe	1 U	1.3	1 U	0.38 J	1.8	1 U	5 U	1 U	1 U	5.8	1 U	**9**
MW-114B	11/24/12		1 U	1.3	1 U	0.44 J	1.9	1 U	5 U	1 U	1 U	6.1	1 U	**10**
MW-117B	10/04/93		0.6	1 U	1 U	1 U	1	1 U	2 U	4	2	5		**13**
MW-117B	04/22/99		0.72	7.3	0.54	14	16	1 U	2 U	3.1	83	21	1 U	**146**
MW-117B	10/18/99		0.58 J	7.7	5 U	14	17	5 U	10	1.3 J	68	17	5 U	**136**
MW-117B	01/26/00		0.36 J	8	5 U	9.5	18	5 U	10	1.9 J	59	22	5 U	**129**
MW-117B	04/17/00		0.39 J	8.1	0.42 J	11	19	2 U	4 JB	1.6 J	49	19	0.07 J	**113**
MW-117B	07/24/00		0.49	6.6	2 U	9.6	15	2 U	4 U	1.7	42	17	2 U	**92**
MW-117B	11/07/00		0.42	10	2 U	11	18	2 U	4 U	1.7	37	19	2 U	**97**
MW-117B	04/09/01		0.37	5.8	2 U	7.3	13	0.25	4 U	1.8	28	17	2 U	**74**
MW-117B	10/15/01		0.35	7.1	2 U	7.5	16	2 U	4 U	1.3	23	16	2 U	**71**
MW-117B	04/16/02		0.3	5.9	0.22	7.3	15	0.2	2 U	1.7	22	16	1 U	**69**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-117B	10/07/02		5 U	8	5 U	54	20	5 U	10 U	3	25	16	1 U	**126**
MW-117B	04/22/03		1 U	7.55	1 U	10.4	20.1	0.61 J	2 U	2.31	23.1	18.4	1 U	**82**
MW-117B	12/22/03		0.99 J	5.96	1 U	9.38	18.7	0.53 J	1 U	2.25	21.8	16.9	1 U	**77**
MW-117B	04/28/04		0.73	3.77	1 U	4.76	11.5	1 U	2 U	2	13.5	11.5	1 U	**48**
MW-117B	05/21/05		1 U	4.5	1 U	5.7	13	1 U	2 U	1.6	11	9.4	1 U	**45**
MW-117B	10/19/05		1 U	4.7	1 U	5.6	14	1 U	2 U	1.8	12	9.3	1 U	**47**
MW-117B	06/28/06		1 U	21	1 U	23	70	1 U	2 U	24	56	23	1 U	**217**
MW-117B	11/21/06		1 U	3.6	1 U	4	11	1 U	2 U	2.1	12	11	1 U	**44**
MW-117B	10/06/07		0.4	6	1 U	8	8	1 U	2 U	2	16	12	1 U	**52**
MW-117B	05/17/08		1 U	8	1 U	11	11	1 U	2 U	3	25 E	16	1 U	**74**
MW-117B	05/17/08	Dilution	2 U	7 D	2 U	10 D	9 D	2 U	4 U	3 D	22 D	14 D	2 U	**65**
MW-117B	11/28/08		0.38 J	7.91	1 U	8.73	8.11	1 U	1 U	4.99	24	15.8	1 U	**70**
MW-117B	06/09/09		0.49 J	11	1 U	12	7.9	1 U	1 U	4.5	31	17	1 U	**84**
MW-117B	11/24/09		0.42 J	8.5	1 U	9	5.1	1 U	1 U	5.3	24	15	1 U	**67**
MW-117B	06/24/10		0.32 J	12	1 U	12	6	1 U	1 U	6.5	37	17	1 U	**91**
MW-117B	11/24/10		0.31 J	11	1 U	8.1	4.6	1 U	1 U	8.4	31	19	1 U	**82**
MW-117B	05/31/11		1 U	4.7	1 U	3.9	2.2	1 U	1 U	7.8	13	10	1 U	**42**
MW-117B	12/22/11		0.29 J	8.7	1 U	4.5	1.8	1 U	5 U	6.7	11	8.7	1 U	**42**
MW-117B	06/26/12		0.3 J	5.9	1 U	2.6	0.77 J	1 U	5 U	5.9	7.8	5.7	1 U	**29**
MW-117B	11/25/12		0.35 J	10	1 U	3	1.1	1 U	5 U	5.7	10	6	1 U	**36**
MW-117C	10/04/93		2 U	17	2 U	13	23	2 U	5 U	2 U	50	75		**178**
MW-117C	04/22/99		0.77	54	2.3	44	69	2 U	4 U	6	75	36	0.79 J	**288**
MW-117C	10/18/99		5 U	60	5 U	53	82	5 U	10 U	7.5	94	40	0.96 J	**337**
MW-117C	02/16/00		0.82 J	61	5 U	53	94	0.5 J	0.8 J	9.7	93	41	0.9 J	**355**
MW-117C	04/18/00		0.79 J	54	2.2 J	49	94	0.6 J	10 JB	10	91	39	0.82 J	**351**
MW-117C	07/24/00		1	55	2.4	48	99	1.1	10 U	8.7	89	38	0.63 J	**343**
MW-117C	11/07/00		0.79	69	2.4	50	100	5 U	10 U	8.8	78	34	0.74 J	**344**
MW-117C	04/09/01		0.84	57	2.3	59	120	0.82	10 U	12	99	42	0.72 J	**394**
MW-117C	10/15/01		0.81	48	5 U	45	110	0.44	10 U	11	74	32	0.67 J	**322**
MW-117C	04/16/02		0.75	41	1.6	469	120	0.74	0.3	16	82	34	0.42 J	**766**
MW-117C	10/07/02		20 U	59	20 U	330	150	20 U	32	22	110	42	0.6 J	**746**
MW-117C	04/22/03	Dilution	10 U	40	10 U	58.2	123	10 U	20 U	23.1	93	44.3	10 U	**382**
MW-117C	04/22/03		0.85 J	43.6 E	1.35	63.6 E	134 E	1.71	2 U	27.1 E	113 E	48 E	0.67 J	**434**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-117C	12/22/03		0.82 J	39.6 E	1.01	55.8 E	126 E	2.07	1 U	27.5 E	104 E	46.4 E	1 U	**403**
MW-117C	12/22/03	Dilution	10 U	33.1 D	10 U	43.3 D	107 D	10 U	10 U	19.9 D	78.2 D	34.8 D	10 U	**316**
MW-117C	04/28/04		10 U	30.5	10 U	37	97.3	10 U	20 U	20.3	66.4	30.1	10 U	**282**
MW-117C	05/21/05		1 U	28	1 U	34	91	1 U	2 U	22	59	27	1 U	**261**
MW-117C	10/19/05		1 U	25	1 U	29	84	1 U	2 U	20	54	26	1 U	**238**
MW-117C	05/06/06		1 U	25	1 U	26	91	1 U	2 U	21	50	26	1 U	**239**
MW-117C	11/21/06		1 U	41	1 U	46	140	1 U	2 U	36	100	44	1 U	**407**
MW-117C	10/06/07		0.5	24	0.3	30	88	0.9	2 U	24	60	26	1 U	**254**
MW-117C	05/17/08		5 U	28	5 U	33	99	5 U	10	30	72	30	5 U	**302**
MW-117C	11/28/08		0.55 J	24.1	0.26 J	25.6	85.9	0.31 J	1 U	26.5	57.1	23.1	1 U	**243**
MW-117C	06/09/09		0.51 J	24	0.23 J	25	70	0.33 J	1 U	26	58	23	1 U	**227**
MW-117C	11/24/09		0.48 J	23	1 U	24	57	1 U	1 U	26	51	21	1 U	**202**
MW-117C	06/24/10		0.42 J	24	1 U	23	40	0.24 J	1 U	28	51	20	1 U	**187**
MW-117C	11/24/10		0.38 J	22	1 U	22	34	1 U	1 U	27	53	21	1 U	**179**
MW-117C	05/31/11		0.45 J	25	1 U	21	24	1 U	1 U	27	47	19	1 U	**163**
MW-117C	12/22/11		0.38 J	23	1 U	17	13	1 U	5 U	25	37	17	1 U	**132**
MW-117C	06/26/12		0.4 J	25	1 U	17	14	1 U	5 U	23	37	15	1 U	**131**
MW-117C	11/25/12		0.35 J	29	1 U	17	7.4	1 U	5 U	22	36	14	1 U	**126**
MW-117D	04/22/99		0.74	46	2	50	110	2 U	4 U	17	110	38	2 U	**374**
MW-117D	10/18/99		10 U	39	10 U	44	110	10 U	1.5 J	17	97	35	10 U	**344**
MW-117D	02/17/00		0.8 J	34	1.4 J	41	100	5 U	10 U	19	91	35	0.45 J	**323**
MW-117D	04/18/00		0.63 J	29	1.1 J	35	90	5 U	10 JB	17	82	32	0.38 J	**297**
MW-117D	07/24/00		0.85	27	1.2	36	81	5 U	10 U	16	80	35	5 U	**277**
MW-117D	11/07/00		0.6	37	1	33	87	5 U	10 U	16	71	30	5 U	**276**
MW-117D	04/09/01		0.65	29	5 U	37	88	0.39	10 U	13	80	31	5 U	**279**
MW-117D	10/16/01		0.53	23	5 U	25	75	5 U	10 U	17	57	23	5 U	**221**
MW-117D	04/16/02		0.61	21	5 U	24	72	5 U	10 U	18	58	23	5 U	**217**
MW-117D	10/07/02		10 U	36	10 U	180	100	10 U	18	24	87	29	1 U	**474**
MW-117D	04/22/03		0.64 J	29.8 E	0.7 J	43.1 E	95.8 E	1 U	2 U	6.41	78.7 E	32.4 E	1 U	**288**
MW-117D	04/22/03	Dilution	5 U	28.3	5 U	36.7	83.1	5 U	10 U	4.62 J	64.5	26	5 U	**243**
MW-117D	12/22/03		0.61 J	28.1 E	1 U	30.4 E	102 E	1 U	1 U	30.1 E	84.2 E	31.2 E	1 U	**307**
MW-117D	12/22/03	Dilution	5 U	29 D	5 U	32.8 D	110 D	5 U	5 U	29.6 D	85.1 D	31.2 D	5 U	**318**
MW-117D	04/28/04		5 U	28.6	5 U	37.7	105	5 U	10 U	17.4	75.5	33.2	5 U	**297**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-117D	05/21/05		1 U	20	1 U	24	84	1 U	2 U	21	60	24	1 U	**233**
MW-117D	10/19/05		1 U	24	1 U	21	73	1 U	2 U	24	58	22	1 U	**222**
MW-117D	05/06/06		1 U	23	1 U	17	67	1 U	2 U	22	52	20	1 U	**201**
MW-117D	05/06/06	Fld Dupe	1 U	18	1 U	30	52	1 U	2 U	23	70	33	1 U	**226**
MW-117D	11/21/06		1 U	27	1 U	22	76	2.1	2 U	31	89	32	1 U	**279**
MW-117D	10/06/07		0.4	22	0.3	22	71	1	2 U	15	62	29	1 U	**223**
MW-117D	05/17/08		5 U	24	5 U	24	31	5 U	12	30	62	23	5 U	**206**
MW-117D	11/28/08		0.46 J	23.3	1 U	19.5	23.5	0.27 J	1 U	28.6	58	19.4	1 U	**173**
MW-117D	06/09/09		0.49 J	25	1 U	18	13	1 U	1 U	30	55	20	1 U	**161**
MW-117D	11/24/09		0.49 J	29	1 U	19	11	1 U	1 U	28	49	18	1 U	**154**
MW-117D	06/24/10		0.33 J	28	1 U	16	5.3	0.18 J	1 U	29	46	15	1 U	**140**
MW-117D	11/24/10		0.34 J	30	1 U	16	5.6	1 U	1 U	29	45	17	1 U	**143**
MW-117D	05/31/11		1 U	37	1 U	13	5.4	1 U	1 U	26	39	15	1 U	**135**
MW-117D	12/22/11		0.34 J	38	1 U	10	3.8	1 U	5 U	23	31	13	1 U	**119**
MW-117D	06/26/12		0.41 J	43	1 U	11	2.8	1 U	5 U	22	33	12	1 U	**124**
MW-117D	11/25/12		0.32 J	48	1 U	12	3	1 U	5 U	19	34	11	1 U	**127**
MW-119	10/11/93		12 U	12 U	12 U	12 U	12 U	12 U	25 U	12 U	12 U	12 U		**0**
MW-119	05/03/99		1 U	1 U	1 U	1 U	0.36	1 U	2 U	0.63	1.8	1	5 U	**4**
MW-119	10/27/99		0.25 J	0.39 J	1 U	0.28 J	1.4	1 U	2 U	1.4	2.6	2	1 U	**8**
MW-119	01/26/00		0.19 J	0.21 J	1 U	1 U	1 U	1 U	2 U	0.18 J	0.75 J	0.2 J	1 U	**2**
MW-119	04/17/00		0.16 J	0.23 J	1 U	1 U	1 U	1 U	2 JB	0.19 J	0.79 J	0.2 J	1 U	**4**
MW-119	07/25/00		0.12	0.26	1 U	1 U	1 U	1 U	2 U	0.22	0.88	0.21	1 U	**2**
MW-119	11/08/00		1 U	0.27	1 U	1 U	1 U	1 U	2 U	0.18	0.72	0.18	1 U	**1**
MW-119	04/10/01		1 U	0.26	1 U	1 U	1 U	1 U	2 U	0.17	0.85	0.19	1 U	**1**
MW-119	10/16/01		0.1	0.29	1 U	1 U	1 U	1 U	2 U	0.15	0.71	0.16	1 U	**1**
MW-119	04/30/02		0.1	0.31	1 U	1 U	1 U	1 U	2 U	0.18	0.95	0.17	1 U	**2**
MW-119	10/17/02		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-119	04/22/03		1.07	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1	1 U	1 U	**2**
MW-119	12/30/03		7.22	0.67 J	1 U	0.54 J	0.59 J	1 U	1 U	1 U	0.72 J	1 U	1 U	**10**
MW-119	04/28/04		1.67	0.51	1 U	1 U	1 U	1 U	2 U	1 U	0.62	1 U	1 U	**3**
MW-119	05/21/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1.3	1 U	1 U	**1**
MW-119	10/20/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1.3	1 U	1 U	**1**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-119	05/06/06		1 U	1.2	1 U	1 U	1 U	1 U	2 U	1 U	1.1	1 U	1 U	**2**
MW-119	01/04/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-119	10/08/07		1 U	1	1 U	1 U	0.4	1 U	2 U	1 U	1	1 U	1 U	**2**
MW-119	05/18/08		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1	1 U	1 U	**1**
MW-119	11/29/08		0.3 J	0.98 J	1 U	1 U	0.54 J	1 U	1 U	1 U	1.29	0.27 J	1 U	**3**
MW-119	06/10/09		0.64 J	1	1 U	1 U	0.66 J	1 U	1 U	1.U	1.2	0.29 J	1 U	**4**
MW-119	11/29/09		0.45 J	1.4	1 U	1 U	0.61 J	1 U	1 U	1 U	1.2	1 U	1 U	**4**
MW-119	06/29/10		1 U	0.92 J	1 U	1 U	1.2	1 U	1 U	1 U	1.1	1 U	1 U	**3**
MW-119	11/27/10		0.46 J	1.1	1 U	1 U	1.1	1 U	1 U	1 U	1.7	0.42 J	1 U	**5**
MW-119	06/03/11		0.32 J	0.97 J	1 U	1 U	0.69 J	1 U	1 U	1 U	1.4	0.37 J	1 U	**4**
MW-119	12/29/11		0.29 J	1	1 U	1 U	0.69 J	1 U	5 U	1 U	1	0.34 J	1 U	**3**
MW-119	06/27/12		0.29 J	0.97 J	1 U	1 U	0.88 J	1 U	5 U	1 U	1.1	1 U	1 U	**3**
MW-119	11/25/12		0.13 J	0.99 J	1 U	1 U	0.8 J	1 U	5 U	1 U	1.2	0.32 J	1 U	**3**
MW-121	10/15/93		2 U	2 U	2 U	2 U	27	2 U	5 U	4	7	82		**120**
MW-121	04/28/99		5 U	3.4	5 U	6	7.2	5 U	10 U	2.7	3.8	26	5 U	**49**
MW-121	10/26/99		0.67 J	3.8	0.78 J	8	8.4	0.15 J	2 U	3.4	5.5	33 E	1 U	**64**
MW-121	10/26/99	Dilution	2 U	3.2 D	0.67 DJ	6.6 D	6.8 D	0.1 DJ	4 U	2.9 D	4.4 D	29 D	2 U	**54**
MW-121	01/31/00		0.65 J	2.9	2 U	5.5	6.3	0.2 J	0.41 J	2.5	3.4	23	2 U	**45**
MW-121	04/18/00		0.55 J	2.8	0.72 J	3	5.6	0.22 J	2 JB	0.64 J	2.8	11	1 U	**29**
MW-121	07/25/00		0.68	3.5	0.82	4.4	6.8	0.39	2 U	1.8	4.3	20	1 U	**43**
MW-121	11/08/00		0.77	4.6	0.89	8	7	0.22	2 U	2.6	5.1	22	1 U	**51**
MW-121	04/10/01		0.78	3.7	0.82	2	6.7	0.68	2 U	2.3	5.5	22	1 U	**44**
MW-121	10/16/01		0.82	3.8	0.81	3.6	6.5	0.42	2 U	2.4	5.9	19	1 U	**43**
MW-121	04/17/02		0.75	3.8	0.07	3	6.1	0.58	2 U	2.6	6.9	20	0.064 J	**44**
MW-121	10/17/02		5 U	5	5 U	42	7	5 U	2 U	3	9	24	1 U	**90**
MW-121	04/22/03		0.65 J	4.3	0.55 J	7.28	5.74	1 U	2 U	2.85	7.18	22.6	1 U	**51**
MW-121	12/28/03		1 U	4.76	1 U	5.11	4.61	1 U	1 U	2.74	5.79	20.3	0.68 J	**44**
MW-121	04/28/04		0.52	4.37	1 U	4.58	4.79	1 U	2 U	2.43	5.84	18.8	1 U	**41**
MW-121	05/21/05		1 U	2.2	1 U	3.9	5.2	1 U	2 U	1.9	5.1	18	1 U	**36**
MW-121	05/21/05	Fld Dupe	1 U	2.4	1 U	4.8	5.3	1 U	2 U	2.1	6	20	1 U	**41**
MW-121	10/20/05		1 U	2.9	1 U	3.9	5.9	1 U	2 U	2.1	5.7	20	1 U	**41**
MW-121	05/06/06		1 U	2.5	1 U	3.3	5.3	1 U	2 U	2.3	4.8	22	1 U	**40**
MW-121	01/03/07		1 U	1.4	1 U	1.7	3	1 U	2 U	1.9	3.9	20	1 U	**32**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-121	10/07/07		0.7	2	1 U	2	6	0.4	2 U	2	5	22	1 U	**40**
MW-121	05/18/08		1 U	2	1 U	2	7	1 U	2 U	2	6	26 E	1 U	**45**
MW-121	05/18/08	Dilution	2 U	2 D	2 U	3 D	6 D	2 U	3 DJ	2 D	5 D	25 D	2 U	**46**
MW-121	11/29/08		0.56 J	1.36	1 U	1 U	3.42	0.55 J	1 U	1.84	2.67	14.4	1 U	**25**
MW-121	06/11/09		0.65 J	1.9	1 U	1 U	4.8	0.76 J	1 U	2.3	4	23	1 U	**37**
MW-121	11/25/09		0.63 J	2.1	1 U	1.8	4.3	1 U	1 U	2	3.1	20	1 U	**34**
MW-121	06/29/10		1 U	2.9	1 U	1.7	3.7	1 U	1 U	1.5	2	16	1 U	**28**
MW-121	11/25/10		0.6 J	4.6	1 U	2.5	4.3	1 U	1 U	2.1	3.4	22	1 U	**40**
MW-121	06/03/11		0.63 J	9.6	1 U	4.1	4.7	0.42 J	1 U	1.8	4.2	19	1 U	**44**
MW-121	12/29/11		0.75 J	15	1 U	6.9	4.9	0.51 J	5 U	1.8	6.6	18	1 U	**54**
MW-121	06/27/12		0.86 J	21	1 U	5.5	5.1	0.62 J	5 U	1.6	10	19	1 U	**64**
MW-121	11/25/12		0.76 J	23	1 U	3	5.3	0.74 J	5 U	1.5	12	18	1 U	**64**
MW-124	10/18/93		120 U	150	120 U	410	210		120 U	50	1400	140		**2360**
MW-124	04/28/99		10 U	75	10 U	97	1200	10 U	20 U	47	540	36	3.4 J	**1998**
MW-124	04/28/99	Fld Dupe	10 U	75	10 U	97	1100 D	10 U	20 JBU	47	540 D	36	3.4 J	**1898**
MW-124	10/27/99		50 U	50	50 U	41 J	560	50 U	8.2 J	28 J	280	28 J	6.9 J	**1002**
MW-124	01/31/00		25 U	95	25 U	36	540	25 U	50 U	12 J	190	20 J	44	**937**
MW-124	04/24/00		0.72 J	92	25 U	24 J	440	3.9 J	50 JB	3.8 J	100	14 J	63	**791**
MW-124	07/25/00		20 U	89	20 U	20	330	20 U	40 U	20 U	79	10	60	**588**
MW-124	11/13/00		20 U	110	20 U	20	300	20 U	40 U	2.7	75	12	63	**583**
MW-124	04/12/01		20 U	47	20 U	35	240	2.1	40 U	30	230	24	13 J	**621**
MW-124	10/29/01		10 U	98	10 U	19	190	1.4	20 U	6.2	110	16	76	**517**
MW-124	04/17/02		20 U	64	20 U	35	370	12	40 U	30	210	26	16 J	**763**
MW-124	04/17/02	Fld Dupe	20 U	65	20 U	41	370	5.7 J	40 U	30	200	20 U	18 J	**730**
MW-124	10/17/02		20 U	92	20 U	230	360	20 U	40 U	35	290	33	21	**1061**
MW-124	04/25/03		1 U	83.4 E	1.32	30 E	226 E	8.35	2 U	13.8	136 E	20.9	62.7 E	**582**
MW-124	04/25/03	Dilution	10 U	71.4	10 U	26.4	213	10 U	20 U	13.5	119	18.9	39.2	**501**
MW-124	12/28/03		1 U	109 E	1.34	22.8	174 E	6.96	1 U	11.2	116 E	19.2	67.2 E	**528**
MW-124	12/28/03	Dilution	10 U	83.2 D	10 U	20.1 D	176 D	10 U	10 U	10.6 D	94.7 D	15.6 D	40 D	**440**
MW-124	04/28/04		40 U	197	40 U	43.6	389	40 U	80 U	34.6	185	26.7	24 J	**900**
MW-124	05/21/05		5 U	340	5 U	37	420	5 U	10 U	8.4	120	18	110	**1053**
MW-124	10/20/05		1 U	250	1 U	25	260	1.5	2 U	6.6	76	15	75 H	**709**
MW-124	05/06/06		1 U	320	1.2	29	370	1.5	2 U	15	120	18	61	**936**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-124	01/04/07		10 U	370	10 U	15	250	10 U	20 U	10 U	110	10	10 U	**755**
MW-124	10/07/07		1 U	620	0.7	28	300	4	2 U	8	100	12	120	**1193**
MW-124	05/18/08		40 U	870	40 U	42	320	40 U	80 U	40 U	190	40 U	64	**1486**
MW-124	11/29/08	Dilution	5 U	415	5 U	16.1	144	1.4 J	1.45 J	11.8	90	10.4	32.1	**722**
MW-124	06/10/09	Dilution	1 J	500	5 U	18	150	5 U	5 U	14	100	10	23	**816**
MW-124	11/29/09	Dilution	5 U	510	5 U	22	170	5 U	5 U	16	98	9.4	21	**846**
MW-124	06/29/10	Dilution	5 U	500	5 U	20	220	5 U	1.9 J	14	82	8.6	30	**877**
MW-124	11/27/10	Dilution	5 U	490	5 U	25	280	5 U	5 U	14	95	9.2	30	**943**
MW-124	06/03/11	Dilution	5 U	450	5 U	28	240	5 U	2.4 J	13	120	7.4	23	**884**
MW-124	12/29/11	Dilution	5 U	370	5 U	20	130	5 U	25 U	12	96	5.9	17	**651**
MW-124	06/27/12	Dilution	5 U	420	5 U	17	100	5 U	25 U	9.5	90	5.2	23	**665**
MW-124	11/25/12	Dilution	2 U	330	2 U	9.6	70	0.9 J	1 J	5.2	50	4.3	30	**501**
MW-130	10/19/93		67 U	26	67 U	10	25		8	67 U	1000	28		**1097**
MW-130	04/28/99		0.19	19	1 U	11	24	1 U	2 U	5.3	670	17	1 U	**746**
MW-130	04/28/99	Fld Dupe	0.17 J	18	1 U	10	23 DJ	1 U	2 U	5.3	670 D	17	1 U	**743**
MW-130	10/28/99		25 U	10 J	25 U	4.9 J	7.8 J	25 U	50 U	25 U	370	8.2 J	25 U	**401**
MW-130	02/16/00		25 U	11 J	25 U	3.6 J	7.5 J	25 U	50 U	25 U	460	8.5 J	25 U	**491**
MW-130	04/24/00		50 JB	12 J	50 U	3.1 J	7.7 J	50 U	100 JB	50 U	510	8.3 J	50 U	**691**
MW-130	07/27/00		20 U	13	20 U	3.3	7.7	20 U	40 U	20 U	670	8.5	20 U	**703**
MW-130	11/14/00		25 U	12	25 U	4.3	7.2	25 U	50 U	25 U	390	7	25 U	**421**
MW-130	04/12/01		20 U	10	20 U	20 U	5.7	20 U	40 U	20 U	440	6.2	20 U	**462**
MW-130	10/30/01	Fld Dupe	50 U	15 J	50 U	50 U	6.5 J	50 U	100 U	50 U	610	8.1 J	50 U	**640**
MW-130	10/30/01		50 U	14	50	50 U	50 U	50 U	100 U	50 U	660	50 U	50 U	**724**
MW-130	04/30/02		25 U	11	25 U	1.6	5.7	25 U	50 U	0.97	360	5.4	25 U	**385**
MW-130	10/17/02		50 U	50 U	50 U	54	50 U	50 U	43	50 U	840	50 U	1 U	**937**
MW-130	04/25/03		0.1 J	13	1 U	5.33	7.5	0.48 J	2 U	1.37	424 E	5.94	1 U	**458**
MW-130	04/25/03	Dilution	20 U	11.6 J	20 U	20 U	20 U	20 U	40 U	20 U	322	20 U	20 U	**334**
MW-130	04/25/03	Fld Dupe	0.11 J	13.2	1 U	5.68	7.84	0.43 J	2 U	1.37	341	20 U	20 U	**370**
MW-130	12/28/03		1 U	12.1	1 U	5.65	8.09	1 U	1 U	1.11	320 E	5.46	1 U	**352**
MW-130	12/28/03	Dilution	20 U	10.3 JD	20 U	20 U	20 U	20 U	20 U	20 U	263 D	20 U	20 U	**273**
MW-130	04/28/04		10 U	11	10 U	10 U	10.6	10 U	20 U	10 U	157	10 U	10 U	**179**
MW-130	05/21/05		1 U	14	1 U	4	11	1 U	2 U	1 U	210	3.5	1 U	**243**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-130	10/20/05		1 U	16	1 U	4.2	14	1 U	2 U	1 U	210	3.6	1 U	**248**
MW-130	05/08/06		1 U	16	1 U	4.1	14	1 U	2 U	1 U	140	3.6	1 U	**178**
MW-130	01/04/07		1 U	20	1 U	4.6	18	1 U	2 U	1 U	160	4.3	1 U	**207**
MW-130	10/07/07		1 U	17	1 U	5	21	0.6	2 U	0.6	170	4	1 U	**218**
MW-130	05/17/08		10 U	22	10 U	10 U	25	10 U	20 U	10 U	200	10 U	10 U	**247**
MW-130	11/29/08	Dilution	2 U	21.9	2 U	4.18	21	0.4 J	0.56 J	0.56 J	198	4.26	2 U	**251**
MW-130	06/11/09	Dilution	0.48 J	26	2 U	4.3	20	2 U	2 U	0.9 J	300	4.3	2 U	**356**
MW-130	11/29/09	Dilution	2 U	31	2 U	5.5	12	2 U	2 U	2 U	320	3.3	2 U	**372**
MW-130	06/29/10	Dilution	10 U	70	10 U	15	17	10 U	2.9 J	10 U	1100	7.6 J	10 U	**1213**
MW-130	11/27/10	Dilution	5 U	29	5 U	8.4	8.3	5 U	5 U	5 U	430	3.6 J	5 U	**479**
MW-130	06/03/11	Dilution	2.5 U	20	2.5 U	5.4	6.5	2.5 U	1 J	2.5 U	250	3.8	2.5 U	**287**
MW-130	12/28/11		1 U	9.7	1 U	2.7	4.1	1 U	5 U	0.68 J	100	2.7	1 U	**120**
MW-130	06/25/12		0.26 J	7.7	1 U	1.9	3	1 U	5 U	0.65 J	68	2.1	1 U	**84**
MW-130	11/24/12		1 U	7.5	1 U	1.7	2.5	1 U	5 U	0.64 J	47	1.9	1 U	**61**
MW-133A	10/20/93		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	0.8	1 U		**1**
MW-133A	04/26/99		1 U	1 U	1 U	1 U	0.27	1 U	2 U	0.37	0.95	1.1	1 U	**3**
MW-133A	10/26/99		0.03 J	0.52 J	1 U	0.66 J	1.8	1 U	2 U	1	4.6	4.8	1 U	**13**
MW-133A	02/15/00		1 U	0.08 J	1 U	1 U	0.16 J	1 U	2 U	1 U	0.38 J	1 U	1 U	**1**
MW-133A	04/25/00		1 U	1 U	1 U	1 U	1 U	1 U	2 JB	1 U	0.35 J	1 U	1 U	**2**
MW-133A	07/27/00		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	10 U	**0**
MW-133A	11/16/00		1 U	1 U	1 U	1 U	0.49	1 U	2 U	1 U	0.81	0.11	1 U	**1**
MW-133A	04/10/01		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-133A	10/31/01		1 U	0.41	1 U	0.1	1.2	1 U	2 U	1 U	1	0.19	1 U	**3**
MW-133A	04/29/02		1 U	1 U	1 U	1 U	0.04	1 U	2 U	1 U	0.06	1 U	1 U	**0**
MW-133A	10/16/02		1 U	1	1 U	1 U	4	1 U	0.6	1 U	3	1 U	1 U	**9**
MW-133A	04/25/03		1 U	2.96	1 U	1.05	11.7	1 U	2 U	1 U	5.2	0.98 J	1 U	**22**
MW-133A	12/30/03		1 U	1.92	1 U	0.53 J	6.34	1 U	1 U	1 U	2.51	1 U	1 U	**11**
MW-133A	04/28/04		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-133A	05/02/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-133A	11/02/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-133A	06/22/06		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-133A	11/16/06		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-133A	10/07/07		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**0**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-133A	05/17/08		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-133A	11/26/08		1 U	1 U	1 U	1 U	0.26 J	1 U	1 U	1 U	0.32 J	1 U	1 U	**1**
MW-133A	06/20/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**0**
MW-133A	06/20/09	Fld Dupe	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**0**
MW-133A	11/28/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**0**
MW-133A	06/25/10		1 U	1 U	1 U	1 U	0.23 J	1 U	1 U	1 U	0.26 J	1 U	1 U	**0**
MW-133A	11/27/10		1 U	0.21 J	1 U	1 U	0.91 J	1 U	1 U	1 U	0.86 J	1 U	1 U	**2**
MW-133A	11/27/10	Fld Dupe	1 U	1 U	1 U	1 U	0.79 J	1 U	1 U	1 U	0.82 J	1 U	1 U	**2**
MW-133A	06/02/11		1 U	1 U	1 U	1 U	1 U	1 U	0.28 J	1 U	1 U	1 U	1 U	**0**
MW-133A	12/28/11		1 U	1 U	1 U	1 U	0.67 J	1 U	5 U	1 U	0.67 J	1 U	1 U	**1**
MW-133A	06/28/12		1 U	1 U	1 U	1 U	0.4 J	1 U	5 U	1 U	0.3 J	1 U	1 U	**1**
MW-133B	10/20/93		100 U	270	100 U	130	810		100 U	160	1200	380		**2950**
MW-133B	04/26/99		10	200	4.6	110	780	7	4 U	110	840	270	2 U	**2332**
MW-133B	10/26/99		7.9 J	170	50 U	67	810	7.1 J	6.8 J	77	630	190	50 U	**1966**
MW-133B	02/15/00		9.3 J	180	50 U	100	840	50 U	100 U	120	730	250	50 U	**2229**
MW-133B	04/25/00		12 J	170	50 U	78	600	50 U	100 JB	76	620	190	50 U	**1846**
MW-133B	07/27/00		12	160	4.1	88	670	10	40 U	94	760	220	20 U	**2018**
MW-133B	11/16/00		11	200	25 U	88	530	9.5	50 U	94	570	230	25 U	**1733**
MW-133B	04/10/01		13	200	50 U	46	660	43	100 U	140	830	300	50 U	**2232**
MW-133B	10/31/01		12	180	50 U	7	510	49	100 U	110	700	250	50 U	**1818**
MW-133B	04/29/02		9.1	150	3.7	25 U	460	54	50 U	99	570	170	25 U	**1516**
MW-133B	10/16/02		50 U	250	50 U	650	820	50 U	31	140	800	290	1 U	**2981**
MW-133B	04/25/03	Dilution	40 U	158	40 U	40.4	571	41.4	80 U	112	617	237	40 U	**1777**
MW-133B	04/25/03		10.7	183 E	3.97	110 E	728 E	24.5	2 U	151 E	699 E	325 E	1 U	**2235**
MW-133B	12/30/03		9.91	162 E	1 U	93 E	562 E	16.3	1 U	122 E	510 E	250 E	1 U	**1725**
MW-133B	12/30/03	Dilution	50 U	151 D	50 U	81.6 D	623 D	50 U	50 U	109 D	577 D	240 D	50 U	**1782**
MW-133B	04/28/04		10 U	161	10 U	106	803	10 U	20 U	111	622	216	100 U	**2019**
MW-133B	05/02/05		5.6	120	5 U	70	630	17	10 U	81	460	160	5 U	**1544**
MW-133B	05/02/05	Fld Dupe	5.7	120	5 U	74	580	13	10 U	87	420	150	5 U	**1450**
MW-133B	11/02/05		8.2	180	5 U	98	930	28	10 U	110	620	220	5 U	**2194**
MW-133B	06/22/06		10 U	110	10 U	54	720	11	20 U	68	430	120	10 U	**1513**
MW-133B	06/22/06	Fld Dupe	10 U	120	10 U	53	710	17	20 U	80	450	140	10 U	**1570**
MW-133B	11/16/06		10 U	160	10 U	10 U	740	78	50 U	85	10 U	170	10 U	**1233**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-133B	10/07/07		6	160	3	84	930	38	2 U	110	600	200	1 U	**2131**
MW-133B	05/17/08		40 U	130	40 U	60	900	40 U	80 U	59	440	110	40 U	**1699**
MW-133B	11/26/08		8 J	308	5.4 J	12	1860	193	3.2 J	126	955	208	10 U	**3679**
MW-133B	06/20/09	Dilution	7.3 J	230	4.3 J	19	1400	140	10 U	110	710	170	10 U	**2791**
MW-133B	11/28/09	Dilution	7.8 J	280	20 U	100	2000	84	20 U	110	820	190	20 U	**3592**
MW-133B	06/25/10	Dilution	5.4 J	230	4 J	81	1700	47	20 U	96	680	150	20 U	**2993**
MW-133B	11/27/10	Dilution	20 U	240	20 U	120	1900	11 J	20 U	110	790	180	20 U	**3351**
MW-133B	06/02/11	Dilution	3.8 J	150	2.9 J	56	1200	29	11	70	420	120	10 U	**2063**
MW-133B	12/28/11	Dilution	4.9 J	180	3.9 J	5.3 J	1100	100	50 U	73	470	100	10 U	**2037**
MW-133B	06/28/12	Dilution	5.2 J	180	10 U	25	1200	60	11 J	65	470	92	10 U	**2108**
MW-133B	11/24/12	Dilution	6 J	160	3.3 J	49	1300	49	50 U	64	420	96	10 U	**2147**
MW-133C	10/20/93		20 U	76	20 U	75	120		20 U	44	340	170		**825**
MW-133C	04/26/99		8.5	57	2.8	47	100	5 U	10 U	28	200	110	5 U	**553**
MW-133C	10/26/99		7.2 J	49	10 U	40	91	1.1 J	20 U	22	170	93	10 U	**473**
MW-133C	02/15/00		5.4	31	2.3 J	23	32	0.42 J	10 U	2.5 J	110	55	5 U	**262**
MW-133C	04/25/00		4.7 JB	28	10 U	21	28	0.34 J	20 JB	1.2 J	100	48	10 U	**251**
MW-133C	07/27/00		4.9	28	2.2	18	30	5 U	10 U	0.82	91	34	5 U	**209**
MW-133C	07/27/00	Fld Dupe	5.4	31	2.4 J	21	32	0.55 J	10 U	1 J	100	44	5 U	**237**
MW-133C	11/16/00		5.2	35	2.2	22	31	5 U	10 U	1.2	95	47	5 U	**239**
MW-133C	04/10/01		6.2	36	10 U	28	36	10 U	20 U	1.6	130	62	10 U	**300**
MW-133C	10/31/01		5.1	31	5 U	14	31	5 U	10 U	5 U	100	31	5 U	**212**
MW-133C	10/31/01	Fld Dupe	5.3	32	2 J	18	33	5 U	10 U	5 U	100	40	5 U	**230**
MW-133C	04/29/02		5.4	33	1.8	26	45	0.73	0.49	4.5	120	58	5 U	**295**
MW-133C	10/16/02	Fld Dupe	7	49 D	2 U	180 D	53 D	5	0.9 J	2	150 D	74 D	1 U	**521**
MW-133C	10/16/02		6	49	10 U	150	51	10 U	6	10 U	140	66	1 U	**468**
MW-133C	04/25/03		5.34	33.5 E	1.86	29.9 E	42.1 E	1.04	2 U	2.41	137 E	72.2 E	1 U	**325**
MW-133C	04/25/03	Dilution	5.04 J	31.6	10 U	26.5	39.2	10 U	20 U	10 U	113	60.7	10 U	**276**
MW-133C	12/30/03		6.43	40.7 E	2.01	36.8 E	55.5 E	0.8 J	1 U	3.02	166 E	83 E	1 U	**394**
MW-133C	12/30/03	Dilution	5.64 JD	143 D	10 U	32.5 D	49.5 D	10 U	10 U	10 U	136 D	74.4 E	10 U	**441**
MW-133C	04/28/04		5.42	34.7	10 U	29.2	47.2	10 U	20 U	10 U	124	63.7	10 U	**304**
MW-133C	05/02/05		5.7	37	1.8	31	53	0.59	2 U	2.6	130	63	1 U	**325**
MW-133C	11/02/05		6.5	46	5 U	43	70	5 U	10 U	5 U	150	75	5 U	**391**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-133C	06/22/06		7.3	44	1 U	42	71	1.3	2 U	4.3	150	78	1 U	**398**
MW-133C	11/16/06		7.7	61	1.9	23	86	3.5	2 U	5.1	220	110	1 U	**518**
MW-133C	10/07/07		7	50	2	51	88	2	2 U	5	170	88	1 U	**463**
MW-133C	05/17/08		8 U	60	8 U	62	120	8 U	16 U	8 U	200 E	100	8 U	**542**
MW-133C	05/17/08	Dilution	10 U	57 D	10 U	58 D	110 D	10 U	20 U	10 U	180 D	94 D	10 U	**499**
MW-133C	05/17/08	Fld Dupe	7	60 D	2	58 E	110 D	2	20 DJ	20 U	200 E	110 D	20 U	**569**
MW-133C	11/26/08		7.82	53.6	1.92	24.6	96.9	6.93	0.23 J	6.06	182	94.8	1 U	**475**
MW-133C	06/20/09		7.4	59	2	36	110	9.7	1 U	6	190	100	1 U	**520**
MW-133C	11/28/09		7.1	58	1.8	53	110	1.2	1 U	6.2	170	94	1 U	**501**
MW-133C	06/25/10		6.9	54	1.8	50	130	1.3	1 U	8.6	180	89	1 U	**522**
MW-133C	11/27/10		6.1	47	1.8	46	130	0.3 J	1 U	10	180	94	1 U	**515**
MW-133C	06/02/11		6.3	56	1.8	51	180	1.5	0.47 J	16	160	95	1 U	**568**
MW-133C	12/28/11		5.8	50	1.8	41	130	2	5 U	9.7	140	76	1 U	**456**
MW-133C	06/28/12		5.7	51	1.6	40	130	1.7	5 U	6.6	150	81	1 U	**468**
MW-133C	11/24/12		5.3	49	1.6	41	130	1.5	5 U	6.6	140	75	1 U	**450**
MW-136	10/19/93		5 U	5 U	5 U	5 U	5 U	5 U	10 U	5 U	5 U	5 U		**0**
MW-136	04/29/99		0.37	0.35	1 U	0.88	3.5	1 U	2 U	1.7	8	3.8	1 U	**19**
MW-136	10/28/99		1.5	0.34 J	1 U	0.37 J	1.1	0.03 J	2 U	1.4	16	2.4	1 U	**23**
MW-136	02/15/00		0.74 J	1 U	1 U	1 U	1 U	1 U	2 U	1 U	0.28 J	1 U	1 U	**1**
MW-136	04/25/00		0.57 JB	1 U	1 U	1 U	1 U	1 U	2 JB	1 U	0.31 J	1 U	1 U	**3**
MW-136	07/27/00		0.48	1 U	1 U	1 U	1 U	1 U	2 U	1 U	0.3	1 U	1 U	**1**
MW-136	11/17/00		0.5	1 U	1 U	1 U	1 U	1 U	2 U	1 U	0.29	1 U	1 U	**1**
MW-136	04/10/01		0.45	1 U	1 U	1 U	1 U	1 U	2 U	1 U	0.3	1 U	1 U	**1**
MW-136	10/31/01		0.45	1 U	1 U	1 U	1 U	1 U	2 U	1 U	0.3	1 U	1 U	**1**
MW-136	04/29/02		0.45	1 U	1 U	1 U	1 U	1 U	2 U	0.53	0.3	1 U	1 U	**1**
MW-136	10/18/02		0.6	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**1**
MW-136	04/23/03		0.8 J	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**1**
MW-136	04/28/04		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-136	06/23/06		1.1	1 U	1 U	1 U	1 U	1 U	1.8	1 U	1 U	1 U	1 U	**3**
MW-136	01/05/07		2.5	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**3**
MW-136	10/07/07		1 U	1 U	1 U	1 U	1 U	1 U	0.7	1 U	1 U	1 U	1 U	**1**
MW-136	05/18/08		2	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**2**
MW-136	11/29/08		4.5	1 U	1 U	1 U	0.2 J	1 U	1 U	1 U	1 U	1 U	1 U	**5**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-136	06/11/09		3.1	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**3**
MW-136	11/28/09		1.5	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**2**
MW-136	06/29/10		0.84 J	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**1**
MW-136	11/28/10		0.82 J	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**1**
MW-136	06/01/11		1	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**1**
MW-136	12/29/11		0.79 J	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	**1**
MW-136	06/25/12		0.62 J	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	**1**
MW-136	11/24/12		0.5 J	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	**1**
MW-200	04/26/99		1 U	1 U	1 U	0.34	0.66	1 U	2 U	0.61	2.2	2.2	1 U	**6**
MW-200	10/27/99		1 U	1 U	1 U	0.26 J	1.3	1 U	2 U	1.1	1.9	1.8	1 U	**6**
MW-200	02/15/00		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-200	04/25/00		1 U	1 U	1 U	1 U	1 U	1 U	2 JB	1 U	0.07 J	1 U	1 U	**2**
MW-200	07/27/00		1 U	1 U	1 U	1 U	0.1	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-200	11/14/00		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-200	04/10/01		1 U	1 U	1 U	1 U	0.17	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-200	10/29/01		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	0.12	1 U	**0**
MW-200	04/22/02		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-200	10/18/02		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-200	04/25/03		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-200	12/30/03		1 U	1 U	1 U	0.89 J	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**1**
MW-200	04/28/04	Fld Dupe	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**0**
MW-200	04/28/04		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-200	05/21/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1.9	1 U	1 U	**2**
MW-200	01/12/06		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-200	05/08/06		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-200	01/04/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-200	10/08/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-200	05/18/08		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-200	11/29/08		1 U	1 U	1 U	1 U	0.69 J	1 U	1 U	1 U	0.21 J	0.17 J	1 U	**1**
MW-200	06/11/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**0**
MW-200	11/28/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**0**
MW-200	06/29/10		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**0**
MW-200	11/28/10		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**0**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-200	05/31/11		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**0**
MW-200	12/29/11		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	**0**
MW-200	06/25/12		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	**0**
MW-200	11/24/12		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	**0**
MW-201	02/16/00		5 U	48	5 U	1.1 J	85	5 U	10 U	5 U	4.5 J	8.3	5.6	**153**
MW-201	04/18/00		10 U	120	10 U	1.9 J	87	0.78 J	20 JB	10 U	4.9 J	15	7.2 J	**257**
MW-201	04/18/00	Fld Dupe	0.29 J	130	10 U	2.3 J	93	0.74 J	20 JB	10 U	5.8 J	12	5.8 J	**270**
MW-201	07/25/00		20 U	330	20 U	6.8	220	20 U	40 U	20 U	110	4.5	22	**693**
MW-201	11/13/00		20 U	340	20 U	5.2	180	20 U	40 U	20 U	39	4.9	7.1 J	**576**
MW-201	04/12/01		5 U	43	5 U	1.6	60	0.64	10 U	5 U	12	19	5.8	**142**
MW-201	04/12/01	Fld Dupe	5 U	43	5 U	1.6 J	60	0.64 J	10 U	5 U	12	18	5.5	**141**
MW-201	10/29/01		10 U	150	10 U	3.6	120	10 U	20 U	10 U	55	25	4.8 J	**358**
MW-201	04/30/02		5	5500	250 U	130	2600	250 U	500 U	250 U	1700	13	50 J	**9998**
MW-201	10/03/02	Fld Dupe	1 U	7700	1 U	420 J	2200	7	2 U	1 U	1000	26 E	50 E	**1403**
MW-201	10/03/02		500 U	7100	500 U	480	2200	500 U	1000 U	500 U	970	500 U	28 E	**0778**
MW-201	04/25/03		0.05 J	1410 E	1 U	52.8 E	989 E	20.3	2 U	0.29 J	452 E	28.9 E	108 E	**3061**
MW-201	04/25/03	Dilution	500 U	6350	500 U	500 U	863	500 U	1000 U	500 U	294 J	500 U	500 U	**7507**
MW-201	12/30/03		1 U	1580 E	1 U	15	123 E	1 U	1 U	1 U	175 E	2.99	39.4 E	**1935**
MW-201	12/30/03	Dilution	400 U	6480 D	400 U	400 U	400 U	400 U	400 U	400 U	400 U	400 U	400 U	**6480**
MW-201	12/30/03	Fld Dupe	400 U	6030 D	1 U	400 U	400 U	400 U	1 U	1 U	400 U	2.12	400 U	**6032**
MW-201	04/28/04		500 U	4150	500 U	500 U	500 U	500 U	1000 U	500 U	500 U	500 U	500 U	**4150**
MW-201	05/21/05		25 U	3500	25 U	25 U	58	25 U	50 U	25 U	26	25 U	25 U	**3584**
MW-201	01/12/06		1 U	230	1 U	1.2	23	1 U	2 U	1 U	8.8	14	1 U	**277**
MW-201	06/28/06		10 U	550	10 U	10 U	16	10 U	20 U	10 U	32	14	10 U	**612**
MW-201	01/05/07		1 U	80	1 U	1 U	5.1	1 U	2 U	1 U	20	2.8	1 U	**108**
MW-201	10/08/07		1 U	20	1 U	2	2	1 U	2 U	6	7	9	1	**47**
MW-201	05/18/08		1 U	64 E	1 U	2	11	1 U	2 U	1 U	7	10	8	**102**
MW-201	05/18/08	Dilution	4 U	55 D	4 U	4 U	9 D	4 U	8 U	4 U	6 D	9 D	6 D	**85**
MW-201	11/29/08	Fld Dupe	10 U	1580	10 U	10 U	5.5 J	10 U	3.1 J	10 U	12.5	7.1 J	5.6 J	**1614**
MW-201	11/29/08	Dilution	2 J	1460	10 U	10 U	7.1 J	10 U	4.4 J	10 U	14.2	7.7 J	6.2 J	**1502**
MW-201	06/10/09	Dilution	2 J	1200	10 U	10 U	16	10 U	10 U	10 U	10	7.7 J	10 U	**1236**
MW-201	06/10/09	Fld Dupe	10 U	1200	10 U	10 U	9.8 J	10 U	10 U	10 U	7.4 J	5.7 J	10 U	**1223**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-201	11/29/09	Dilution	10 U	480	10 U	10 U	6.4 J	10 U	10 U	10 U	37	10 U	10	**533**
MW-201	11/29/09	Fld Dupe	10 U	500	10 U	10 U	5.7 J	10 U	10 U	10 U	36	10 U	9.3 J	**551**
MW-201	06/29/10		1 U	12	1 U	1 U	5	1 U	1 U	0.53 J	4.4	1.1	0.91 J	**24**
MW-201	11/28/10		1 U	2.7	1 U	0.43 J	0.75 J	1 U	1 U	0.93 J	3.4	1.2	1 U	**9**
MW-201	06/03/11		1 U	2.2	1 U	1 U	0.69 J	1 U	1 U	1.3	3.4	0.85 J	1 U	**8**
MW-201	06/03/11	Fld Dupe	1 U	2.2	1 U	1 U	0.63 J	1 U	0.26 J	1.2	3.4	0.87 J	1 U	**9**
MW-201	12/29/11		1 U	3.7	1 U	1 U	3.3	1 U	5 U	1.7	2.4	0.73 J	1 U	**12**
MW-201	12/29/11	Fld Dupe	1 U	3.6	1 U	1 U	3.3	1 U	5 U	1.8	2.4	0.77 J	1 U	**12**
MW-201	06/27/12		1 U	8	1 U	1 U	0.75 J	1 U	5 U	1.9	5.8	0.44 J	1 U	**17**
MW-201	11/25/12		1 U	5	1 U	1 U	1	1 U	5 U	0.85 J	15	0.31 J	1 U	**22**
MW-202	05/20/99		1 U	1 U	1 U	1 U	0.81	1 U	2 U	4.6	2	2.1	1 U	**10**
MW-202	10/28/99		1 U	1 U	1 U	0.18 J	0.68 J	1 U	2 U	5	2.2	2.1	1 U	**10**
MW-202	02/16/00		1 U	1 U	1 U	1 U	1 U	1 U	2 U	3.6	0.77 J	0.5 J	1 U	**5**
MW-202	04/18/00		0.25 J	1 U	1 U	1 U	1 U	1 U	2 JB	3.1	0.65 J	0.55 J	1 U	**7**
MW-202	07/27/00		0.48	1 U	1 U	1 U	1 U	1 U	2 U	3.5	0.72	0.75	1 U	**5**
MW-202	11/13/00		1 U	1 U	1 U	1 U	1 U	1 U	2 U	14	0.11	0.19	1 U	**14**
MW-202	04/12/01		1 U	1 U	1 U	1 U	1 U	1 U	2 U	13	0.08	0.11	1 U	**13**
MW-202	10/29/01		1 U	1 U	1 U	1 U	1 U	1 U	2 U	12	0.06	1 U	1 U	**12**
MW-202	04/30/02		1 U	1 U	1 U	1 U	1 U	1 U	2 U	10	1 U	0.12	1 U	**10**
MW-202	10/17/02		1 U	1 U	1 U	1 U	1 U	1 U	0.5	12	1 U	1 U	1 U	**13**
MW-202	04/24/03		1 U	1 U	1 U	1 U	1 U	1 U	2 U	2.82	1 U	0.8 J	1 U	**4**
MW-202	12/30/03		1 U	1 U	1 U	0.54 J	1 U	1 U	1 U	2.78	1 U	1.11	1 U	**4**
MW-202	04/28/04		1 U	1 U	1 U	1 U	1 U	1 U	2 U	2.3	1 U	0.68	1 U	**3**
MW-202	05/21/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1.8	1 U	1 U	1 U	**2**
MW-202	10/21/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-202	06/28/06		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1.5	1 U	1 U	1 U	**2**
MW-202	01/05/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	14	1 U	1 U	1 U	**14**
MW-202	10/08/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1	1	0.3	1 U	**2**
MW-202	05/19/08		1 U	1 U	1 U	1 U	1 U	1 U	2 U	4	1 U	1 U	1 U	**4**
MW-202	11/29/08		0.3 J	0.95 J	1 U	1 U	1 U	1 U	1 U	1.26	1.15	0.65 J	1 U	**4**
MW-202	06/11/09		1 U	0.46 J	1 U	1 U	1 U	1 U	1 U	1.2	1	0.6 J	1 U	**3**
MW-202	11/29/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1.2	1 U	1 U	1 U	**1**
MW-202	06/29/10		1 U	0.7 J	1 U	1 U	1 U	1 U	1 U	1.6	1.3	0.79 J	1 U	**4**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-202	11/28/10		1 U	1 U	1 U	1 U	1 U	1 U	1 U	2.1	0.67 J	1 U	1 U	**3**
MW-202	06/03/11		1 U	0.35 J	1 U	1 U	1 U	1 U	0.26 J	1.5	0.45 J	0.39 J	1 U	**3**
MW-202	12/29/11		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1.2	0.22 J	0.28 J	1 U	**2**
MW-202	06/27/12		1 U	0.46 J	1 U	1 U	1 U	1 U	5 U	1.4	0.94 J	1 U	1 U	**3**
MW-202	11/30/12		1 U	0.45 J	1 U	1 U	1 U	1 U	5 U	2.1	1	0.3 J	1 U	**4**
MW-203	05/20/99		1 U	1 U	1 U	1 U	0.67	1 U	2 U	14	0.92	1.2	1 U	**17**
MW-203	10/28/99		0.08 J	0.28 J	1 U	0.42 J	1.5	0.06 J	2 U	15	2.7	2.6	1 U	**23**
MW-203	02/15/00		1 U	1 U	1 U	1 U	0.13 J	1 U	2 U	8.6	0.26 J	0.16 J	1 U	**9**
MW-203	04/18/00		1 U	1 U	1 U	1 U	0.07 J	1 U	2 U	11	0.14 J	0.17 J	1 U	**11**
MW-203	07/27/00		1 U	1 U	1 U	1 U	1 U	1 U	2 U	13	0.2	0.24	1 U	**13**
MW-203	11/13/00		0.82	1 U	1 U	1 U	1 U	1 U	2 U	3.5	0.66	0.81	1 U	**6**
MW-203	04/12/01		1.8	1 U	1 U	1 U	1 U	1 U	2 U	3.2	0.81	0.76	1 U	**7**
MW-203	10/29/01		4.3	0.19	1 U	1 U	1 U	1 U	2 U	3.1	0.76	0.84	1 U	**9**
MW-203	04/30/02		4.1	0.12	1 U	1 U	1 U	1 U	2 U	3	0.69	0.63	1 U	**9**
MW-203	10/17/02		1	1 U	1 U	1 U	1 U	1 U	0.5	3	1 U	0.7	1 U	**5**
MW-203	04/24/03		1 U	1 U	1 U	1 U	1 U	1 U	2 U	10.2	1 U	1 U	1 U	**10**
MW-203	12/30/03		1 U	1 U	1 U	1 U	1 U	1 U	1 U	8.43	1 U	1 U	1 U	**8**
MW-203	04/28/04		1 U	1 U	1 U	1 U	1 U	1 U	2 U	8.79	1 U	1 U	1 U	**9**
MW-203	05/21/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	9.6	1 U	1 U	1 U	**10**
MW-203	10/21/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-203	06/28/06		1 U	1 U	1 U	1 U	1 U	1 U	2 U	17	1 U	1 U	1 U	**17**
MW-203	01/05/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1.7	1 U	1 U	1 U	**2**
MW-203	10/08/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	4	1 U	1 U	1 U	**4**
MW-203	05/18/08	Fld Dupe	1 U	1 U	1 U	1 U	1 U	1 U	2 U	1	1	1 U	1 U	**2**
MW-203	05/18/08		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1	1	1 U	1 U	**2**
MW-203	11/29/08		0.15 J	0.45 J	1 U	1 U	1 U	1 U	1 U	3.11	0.19 J	0.33 J	1 U	**4**
MW-203	06/11/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	4.4	1 U	1 U	1 U	**4**
MW-203	11/29/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	5.4	1 U	1 U	1 U	**5**
MW-203	06/29/10		1 U	1 U	1 U	1 U	1 U	1 U	0.32 J	8.9	1 U	1 U	1 U	**9**
MW-203	11/28/10		1 U	1 U	1 U	1 U	1 U	1 U	1 U	7.3	1 U	1 U	1 U	**7**
MW-203	06/03/11		1 U	1 U	1 U	1 U	1 U	1 U	0.27 J	5.1	1 U	1 U	1 U	**5**
MW-203	12/29/11		1 U	1 U	1 U	1 U	1 U	1 U	5 U	5.1	1 U	0.19 J	1 U	**5**
MW-203	06/28/12		1 U	1 U	1 U	1 U	1 U	1 U	5 U	10	1 U	0.41 J	1 U	**10**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-203	11/30/12		1 U	0.19 J	1 U	1 U	1 U	1 U	5 U	11	0.36 J	0.34 J	1 U	**12**
MW-204	04/23/99		20 U	20 U	20 U	6.2	56	20 U	40 U	20 U	4.7	230	20 U	**297**
MW-204	10/26/99		10 U	5.2 J	4.5 J	8.6 J	51	0.55 J	20 U	2.4 J	5.4 J	230	1.1 J	**309**
MW-204	01/31/00		0.67 J	5 J	5.3 J	8.2 J	41	10 U	2 J	2.4 J	4.2 J	200	0.85 J	**270**
MW-204	04/24/00		0.92 J	4.9 J	5.7 J	9.2 J	44	10 U	20 JB	2 J	4 J	190	1.2 J	**282**
MW-204	07/25/00		1.1	4.4	5.7	6.9	38	10 U	20 U	1.3	3.4	120	10 U	**181**
MW-204	11/08/00		10 U	6.5	6.8	11	37	10 U	20 U	2.4	4	170	10 U	**238**
MW-204	04/12/01		10 U	5	6	11	27	10 U	20 U	2.4	4.5	160	10 U	**216**
MW-204	10/16/01		10 U	5.4	10 U	13	23	10 U	20 U	2.8	4.9	140	10 U	**189**
MW-204	04/17/02		0.77	6.9	10	18	20	10 U	20 U	2.9	6	140	0.041 J	**205**
MW-204	10/03/02		20 U	14	20 U	140	23	20 U	40 U	20 U	20 U	170	1 U	**347**
MW-204	04/22/03		0.59 J	8.21	9.93	28.4 E	28.6 E	0.61 J	2 U	3.9	9.93	192 E	0.76 J	**283**
MW-204	04/22/03	Dilution	10 U	7.58 J	9.49 J	23.9	26.8	10 U	20 U	10 U	9.28 J	165	10 U	**242**
MW-204	12/28/03		0.58 J	8.14	9.41	26.3 E	28.8 E	1 U	1 U	3.83	11.3	163 E	0.8 J	**252**
MW-204	12/28/03	Dilution	10 U	7.65 JD	8.32 JD	21.8 D	23.7 D	10 U	10 U	10 U	9.1 JD	151 D	10 U	**222**
MW-204	04/28/04		10 U	6.41	8.07	21	20.7	10 U	20 U	10 U	8.96	124	10 U	**189**
MW-204	05/21/05		1 U	6	5.9	22	13	1 U	2 U	2.8	10	96	1 U	**156**
MW-204	10/19/05		1 U	6.2	5.7	20	15	1 U	2 U	2.3	9.1	97	1 U	**155**
MW-204	05/06/06		1 U	5.7	4.4	21	13	1 U	2 U	2.9	10	100	1 U	**157**
MW-204	01/03/07		1 U	6	3.5	22	15	1 U	2 U	3.2	10	100	1 U	**160**
MW-204	10/07/07		0.5	6	3	19	15	0.5	2 U	3	10	85	0.4 J	**142**
MW-204	10/07/07	Fld Dupe	0.5 J	5	3	18	15	0.4 J	2 U	3	9	82 D	1 U	**136**
MW-204	05/18/08		4 U	6	4 U	20	20	4 U	8 U	4 U	9	91	4 U	**146**
MW-204	11/29/08		0.65 J	4.9	2.07	13.6	14.4	0.29 J	1 U	2.64	7.61	74	0.32 J	**120**
MW-204	06/11/09		0.67 J	4.3	1.4	11	14	0.4 J	1 U	2.6	7.2	73	0.31 J	**115**
MW-204	11/25/09		0.65 J	5.8	1.8	14	20	1 U	1 U	2.6	6.2	71	0.56 J	**123**
MW-204	06/29/10		1 U	5.2	1.3	12	18	1 U	1 U	2	4.3	61	1 U	**104**
MW-204	11/25/10		0.54 J	5.3	1.5	11	24	1 U	1 U	2.5	6.4	66	1 U	**117**
MW-204	06/02/11		0.5 J	5.9	1.3	11	26	0.4 J	1 U	2.1	5.9	60	0.25 J	**113**
MW-204	12/29/11		0.55 J	5.3	1.3	10	26	0.52 J	5 U	2	5.6	51	1 U	**102**
MW-204	06/27/12		0.63 J	5.5	1.2	7.1	30	1.3	5 U	1.7	5.8	54	1 U	**107**
MW-204	11/25/12		0.45 J	6	1.2	12	33	0.64 J	5 U	1.8	7.3	51	1 U	**113**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-205A	04/22/99		0.88	23	4.4	100	49	5 U	10 U	3.9	570	69	5 U	**820**
MW-205A	10/21/99		1.1 J	23 J	25 U	110	57	25 U	50 U	3.4 J	460	68	25 U	**723**
MW-205A	02/07/00		25 U	22 J	3.5 J	110	56	25 U	50 U	3.6 J	450	68	25 U	**713**
MW-205A	04/18/00		50 U	23 J	50 U	140	61	50 U	100 JB	50 U	540	80	50 U	**944**
MW-205A	07/25/00		20 U	19	3.5	92	50	20 U	40 U	20 U	350	47	20 U	**562**
MW-205A	11/07/00		25 U	27	25 U	120	56	25 U	50 U	25 U	410	66	25 U	**679**
MW-205A	04/09/01		20 U	23	20 U	130	56	20 U	40 U	4.3	430	68	20 U	**711**
MW-205A	10/16/01		1.1	18	20 U	87	44	20 U	40 U	2.1	240	49	20 U	**441**
MW-205A	04/16/02		1.1	17	20 U	79	43	20 U	40 U	6.7	270	47	20 U	**464**
MW-205A	10/07/02		50 U	50 U	50 U	690	53	50 U	84	110	310	49	1 U	**1296**
MW-205A	04/22/03		0.78 J	21	2.39	122 E	51.2 E	1 U	2 U	7.15	397 E	72.8 E	1 U	**674**
MW-205A	04/22/03	Dilution	25 U	19.8 J	25 U	111	46.6	25 U	50 U	25 U	322	64.3	25 U	**564**
MW-205A	12/22/03		0.69 J	19.7	1.48	95.6 E	52.7 E	1 U	1 U	11.3	308 E	64.3 E	1 U	**554**
MW-205A	12/22/03	Dilution	20 U	15.4 JD	20 U	71.9 D	38.5 D	20 U	20 U	20 U	237 D	47.1 D	20 U	**410**
MW-205A	04/28/04		20 U	15.8	20 U	68.7	39.9	20 U	40 U	20 U	229	43.9	20 U	**397**
MW-205A	05/21/05		1 U	15	1 U	51	43	1 U	2 U	11	130	36	1 U	**286**
MW-205A	10/19/05		1 U	13	1 U	35	38	1 U	2 U	11	89	32	1 U	**218**
MW-205A	05/06/06		1 U	14	1 U	29	37	1 U	2 U	18	81	32	1 U	**211**
MW-205A	11/21/06		1 U	13	1 U	49	47	1 U	2 U	17	160	51	1 U	**337**
MW-205A	10/06/07		0.5	12	0.4	31	39	1 U	2 U	16	75	34	1 U	**208**
MW-205A	05/18/08		4 U	13	4 U	27	48	4 U	8 U	20	73	35	4 U	**216**
MW-205A	11/28/08		0.49 J	11.9	0.29 J	21.3	41.5	1 U	1 U	20.2	59.5	30.8	1 U	**186**
MW-205A	06/09/09		0.45 J	10	0.27 J	19	36	1 U	1 U	19	60	30	1 U	**175**
MW-205A	11/25/09		0.48 J	11	1 U	19	32	1 U	1 U	20	46	27	1 U	**155**
MW-205A	06/24/10		0.35 J	11	1 U	16	25	1 U	1 U	22	41	23	1 U	**138**
MW-205A	11/25/10		0.38 J	13	1 U	16	18	1 U	1 U	23	41	24	1 U	**135**
MW-205A	06/02/11		0.34 J	15	1 U	15	13	1 U	1 U	23	36	22	1 U	**124**
MW-205A	01/08/12		0.31 J	20	1 U	14	7.4	1 U	5 U	24	31	16	1 U	**113**
MW-205A	06/28/12		0.4 J	21	1 U	13	5.7	1 U	5 U	24	30	16	1 U	**110**
MW-205A	12/02/12		0.26 J	20	1 U	11	4.6	1 U	5 U	24	27	15	1 U	**102**
MW-205B	04/22/99		0.73	23	3.4	74	47	5 U	10 U	3.5	310	57	5 U	**519**
MW-205B	10/21/99		25 U	23 J	25 U	82	54	25 U	50 U	3.4 J	340	58	25 U	**560**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-205B	02/07/00		25 U	24 J	25 U	86	57	25 U	50 U	3.8 J	360	60	25 U	**591**
MW-205B	04/18/00		20 U	26	20 U	90	59	20 U	40 JB	3.8 J	370	65	20 U	**654**
MW-205B	07/25/00		20 U	23	20 U	70	52	20 U	40 U	20 U	270	44	20 U	**459**
MW-205B	11/07/00		20 U	31	2.9	79	55	20 U	40 U	3.6	270	53	20 U	**495**
MW-205B	04/09/01		20 U	31	20 U	110	68	20 U	40 U	4.5	330	67	20 U	**611**
MW-205B	10/16/01		20 U	21	20 U	73	50	20 U	40 U	5.1	250	45	20 U	**444**
MW-205B	04/16/02		0.82	22	10 U	59	53	1.4	0.7	5.8	220	48	10 U	**411**
MW-205B	10/07/02		50 U	50 U	50 U	470	65	50 U	90	110	310	49	1 U	**1094**
MW-205B	04/22/03		0.75 J	24.2	1.79	92.4 E	59.6 E	1 U	2 U	11.4	303 E	63.8 E	1 U	**557**
MW-205B	04/22/03	Dilution	20 U	23.7	20 U	93.1	57.3	20 U	40 U	10 J	262	60.4	20 U	**507**
MW-205B	12/22/03		0.7 J	21.6	1.36	70.5 E	53.8 E	0.55 J	1 U	13	239 E	52.1 E	1 U	**453**
MW-205B	12/22/03	Dilution	20 U	18.7 JD	20 U	64.9 D	47.1 D	20 U	20 U	10.5 JD	201 D	44.6 D	20 U	**387**
MW-205B	04/28/04		20 U	22.4	20 U	75.5	54.4	20 U	40 U	11.4	233	49.3	20 U	**446**
MW-205B	05/21/05		1 U	17	1 U	43	47	1 U	2 U	13	110	34	1 U	**264**
MW-205B	10/19/05		1 U	17	1 U	32	43	1 U	2 U	14	89	31	1 U	**226**
MW-205B	05/06/06		1 U	18	1 U	26	52	1 U	2 U	23	59	31	1 U	**209**
MW-205B	11/21/06		1 U	18	1 U	39	71	1 U	2 U	23	95	44	1 U	**290**
MW-205B	10/06/07		0.4	15	0.4	30	52	1 U	2 U	18	66	31	1 U	**213**
MW-205B	05/18/08		4 U	16	4 U	30	63	4 U	8 U	22	69	34	4 U	**234**
MW-205B	11/28/08		0.49 J	15	0.38 J	19.9	43.1	1 U	1 U	12.8	79.4	24.6	1 U	**196**
MW-205B	06/09/09		0.49 J	15	0.25 J	21	44	1 U	1 U	18	63	29	1 U	**191**
MW-205B	11/25/09		0.55 J	14	1 U	21	37	1 U	1 U	21	47	27	1 U	**168**
MW-205B	06/24/10		0.38 J	14	0.16 J	17	29	1 U	1 U	22	43	23	1 U	**149**
MW-205B	11/25/10		0.41 J	15	1 U	17	23	1 U	1 U	23	42	24	1 U	**144**
MW-205B	06/02/11		0.38 J	17	1 U	18	21	1 U	1 U	23	39	22	1 U	**140**
MW-205B	01/08/12		0.32 J	20	1 U	14	11	1 U	5 U	23	31	16	1 U	**115**
MW-205B	06/28/12		0.43 J	21	1 U	13	8.2	1 U	5 U	23	30	15	1 U	**111**
MW-205B	12/02/12		0.32 J	20	1 U	10	6	1 U	5 U	16	25	12	1 U	**89**
MW-206A	04/23/99		0.64	8.5	0.75	22	23	2 U	4 U	9.3	100	37	2 U	**201**
MW-206A	10/20/99		10 U	9.8 J	10 U	21	21	10 U	20 U	6.6 J	87	33	10 U	**178**
MW-206A	02/07/00		0.55 J	10	5 U	14	20	5 U	10 U	7	79	25	5 U	**156**
MW-206A	04/18/00		0.55 J	9.6	5 U	12	20	0.36 J	10 JB	5.2	62	22	5 U	**142**
MW-206A	07/25/00		0.72	9.4	5 U	14	21	5 U	10 U	3.1	66	16	5 U	**130**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-206A	11/07/00		5 U	12	5 U	5.9	13	5 U	10 U	0.84	46	7.6	5 U	**85**
MW-206A	04/09/01		0.66	9.7	5 U	13	20	5 U	10 U	4.5	55	22	5 U	**125**
MW-206A	10/16/01		0.49	8.8	2 U	9.9	18	2 U	0.34	3.5	39	18	2 U	**98**
MW-206A	04/16/02		0.39	7.1	2 U	7.1	15	0.39	4 U	3.4	31	16	2 U	**80**
MW-206A	10/08/02		5 U	11	5 U	57	23	5 U	10 U	3	35	18	1 U	**147**
MW-206A	04/21/03		0.87 J	11.8	1 U	11.7	30.3 E	1.05	2 U	3.48	31.1 E	18.1	1 U	**108**
MW-206A	04/21/03	Dilution	2 U	11	2 U	11.1	28.4	2 U	4 U	3.17	26.9	17	2 U	**98**
MW-206A	12/22/03	Dilution	2 U	12.4 D	2 U	11.4 D	33.6 D	1.11 JD	2 U	3.36 D	29.8 D	16.5 D	2 U	**108**
MW-206A	12/22/03		1.04	14.5	1 U	13.9	38.4 E	1.4	1 U	3.99	35.8 E	19	1 U	**128**
MW-206A	04/28/04		1.28	10.7	2 U	11.1	31.6	2 U	4 U	3.65	27.4	15.1	2 U	**101**
MW-206A	05/21/05		1.1	5.6	1 U	6.7	16	1 U	2 U	2.9	17	11	1 U	**60**
MW-206A	10/19/05		1 U	8.1	1 U	8.8	23	1 U	2 U	3.1	19	11	1 U	**73**
MW-206A	05/06/06		1 U	9.2	1 U	9.1	25	1 U	2 U	3.8	23	13	1 U	**83**
MW-206A	11/27/06		1.1	9	1 U	8.2	14	1 U	2 U	4.2	22	14	1 U	**73**
MW-206A	10/06/07		0.6	5	1 U	5	6	1 U	2 U	3	14	9	1 U	**43**
MW-206A	05/18/08		1 U	6	1 U	8	7	1 U	2 U	4	18	11	1 U	**54**
MW-206A	11/28/08		0.28 J	13	0.19 J	7.54	9.43	0.21 J	1 U	1.95	17.9	7.85	1.59	**60**
MW-206A	06/10/09		0.41 J	11	1 U	7.5	7.3	1 U	1 U	2.8	23	9.9	0.97 J	**63**
MW-206A	04/01/10		0.27 J	7.6	1 U	6.8	4.2	1 U	1 U	3.7	18	10	1 U	**51**
MW-206A	06/25/10		0.28 J	8.3	1 U	7.1	4.2	1 U	1 U	3.8	18	9.3	1 U	**51**
MW-206A	11/29/10		0.16 J	13	1 U	4.4	4.5	1 U	1 U	1.5	9.7	4.3	3.6	**41**
MW-206A	06/02/11		0.27 J	12	1 U	6.8	3.8	1 U	0.27 J	3.4	17	9.6	0.55 J	**54**
MW-206A	12/22/11		0.93 J	75	2.2	76	100	1 U	5 U	7.3	52	44	0.92 J	**358**
MW-206A	06/26/12		0.6 J	7.8	1 U	3.7	1.8	1 U	5 U	4.4	11	6.9	1 U	**36**
MW-206A	11/23/12		0.42 J	12	1 U	3.8	2	1 U	5 U	5.5	12	6.2	1 U	**42**
MW-206B	04/23/99		10 U	5.1	10 U	2.5	59	10 U	20 U	13	4.6	150	10 U	**234**
MW-206B	10/20/99		10 U	9.1 J	10 U	4.9 J	54	10 U	1.3 J	9.6 J	8.4 J	160	10 U	**247**
MW-206B	02/17/00		10 U	13	10 U	8.8 J	36	10 U	20 U	5.8 J	16	150	10 U	**230**
MW-206B	04/18/00		0.62 J	14	10 U	9 J	40	0.28 J	20 JB	5.6 J	16	150	10 U	**256**
MW-206B	07/25/00		0.6	12	5 U	6	36	5 U	10 U	0.98	11	86	5 U	**153**
MW-206B	11/07/00		5 U	17	5 U	8.4	34	5 U	10 U	3.3	14	120	5 U	**197**
MW-206B	04/09/01		0.51	14	5 U	9.1	33	5 U	10 U	2.5	16	110	5 U	**185**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-206B	10/16/01		0.62	14	5 U	11	26	5 U	10 U	1.7	20	80	5 U	**153**
MW-206B	04/16/02		0.69	12	5 U	10	23	5 U	10 U	1.5	20	70	5 U	**137**
MW-206B	10/08/02		5 U	22	5 U	76	31	5 U	4	5 U	35	100	1 U	**268**
MW-206B	04/22/03		0.83 J	16.2	0.7 J	16.8	22.1	1 U	2 U	1.35	32.5 E	75.7 E	1 U	**166**
MW-206B	04/22/03	Dilution	5 U	15.1	5 U	15.7	20.5	5 U	10 U	5 U	27.2	68.7	5 U	**147**
MW-206B	12/22/03		0.88 J	17.3	0.71 J	18.2	21.5	1 U	1 U	1.34	34 E	68.8 E	1 U	**163**
MW-206B	12/22/03	Dilution	4 U	14.8 D	4 U	14 D	17.4 D	4 U	4 U	4 U	26.5 D	54.5 D	4 U	**127**
MW-206B	04/28/04		4 U	16	4 U	14.2	19.5	4 U	8 U	4 U	26.3	59.2	4 U	**135**
MW-206B	05/21/05		1 U	16	1 U	13	13	1 U	2 U	1 U	22	33	1 U	**97**
MW-206B	10/19/05		1 U	16	1 U	12	13	1 U	2 U	1 U	22	35	1 U	**98**
MW-206B	05/06/06		1 U	24	1 U	17	15	1 U	2 U	1 U	24	32	1 U	**112**
MW-206B	11/27/06		1 U	47	1.4	31	21	1 U	2 U	1.2	44	45	1 U	**191**
MW-206B	11/27/06	Fld Dupe	1 U	7.1	1 U	5	18	1 U	2 U	1 U	1 U	71	1 U	**101**
MW-206B	10/06/07		0.8	50	1	39	32	1 U	2 U	1	39	28	0.5 J	**191**
MW-206B	05/18/08		4 U	56	4 U	46	50	4 U	8 U	4 U	44	48	4 U	**244**
MW-206B	11/28/08		0.92 J	57.7	1.74	40.9	45.8	0.2 J	1 U	1.71	39.9	35.6	0.72 J	**225**
MW-206B	06/10/09		1	79	2.3	63	70	0.33 J	1 U	3.3	57	37	0.86 J	**314**
MW-206B	04/01/10		0.97 J	77	2.3	77	76	0.57 J	1 U	4.4	58	38	1.2	**335**
MW-206B	06/25/10		1	84	2.4	77	90	0.39 J	1 U	4.9	64	37	1.1	**362**
MW-206B	11/29/10		0.92 J	78	2.3	71	72	0.53 J	1 U	5.5	55	34	1.1	**320**
MW-206B	06/02/11		1.1	91	2.7	83	98	0.39 J	0.27 J	7.2	61	44	1.1	**390**
MW-206B	12/22/11		0.93 J	72	2.2	75	100	1 U	5 U	7.3	50	43	0.96 J	**351**
MW-206B	06/26/12		1	69	2.4	80	130	0.44 J	5 U	10	58	46	0.86 J	**398**
MW-206B	11/23/12		0.86 J	55	2.1	74	130	0.4 J	5 U	14	55	41	0.8 J	**373**
MW-206C	04/23/99		1 U	1 U	1 U	0.31	2.7	1 U	2 U	0.41	1.5	4.1	1 U	**9**
MW-206C	10/20/99		1 U	0.18 J	1 U	0.15 J	2.3	1 U	2 U	1 U	0.26 J	4.3	1 U	**7**
MW-206C	02/07/00		1 U	1 U	1 U	1 U	3.5	1 U	2 U	1 U	1 U	5.3	1 U	**9**
MW-206C	04/18/00		1 U	1 U	1 U	1 U	4	1 U	2 JB	1 U	1 U	6	1 U	**12**
MW-206C	07/25/00		1 U	1 U	1 U	1.3	4.8	1 U	2 U	1 U	1 U	3.5	1 U	**10**
MW-206C	11/07/00		1 U	0.14	1 U	0.12	2.3	1 U	2 U	1 U	0.29	3.4	1 U	**6**
MW-206C	11/07/00	Fld Dupe	1 U	0.14 J	1 U	0.12 J	2.3	1 U	2 U	1 U	0.28 J	3.3	1 U	**6**
MW-206C	04/09/01		1 U	0.36	1 U	0.28	4.3	1 U	2 U	0.25	0.7	6.6	1 U	**12**
MW-206C	04/09/01	Fld Dupe	1 U	0.33 J	1 U	0.26 J	4.2	1 U	2 U	0.26 J	0.48 J	6.3	1 U	**12**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	–
			–											
MW-206C	10/16/01		1 U	0.24	1 U	0.11	5.9	1 U	2 U	0.2	0.18	7.6	1 U	**14**
MW-206C	04/16/02		1 U	1 U	1 U	0.17	6.9	1 U	2 U	0.06	1 U	14	1 U	**21**
MW-206C	10/08/02		5 U	5 U	5 U	5 U	15	5 U	4	5 U	5 U	30	1 U	**49**
MW-206C	04/22/03		1 U	0.86 J	1 U	0.55 J	14.4	1 U	2 U	1 U	1 U	43 E	1 U	**59**
MW-206C	04/22/03	Dilution	2.5 U	2.5 U	2.5 U	2.5 U	13.2	2.5 U	5 U	2.5 U	2.5 U	39.1	2.5 U	**52**
MW-206C	12/22/03		1 U	1.37	1 U	1.68	16.6	0.61 J	1 U	1 U	1 U	53 E	1 U	**73**
MW-206C	12/22/03	Dilution	4 U	4 U	4 U	4 U	14 D	4 U	4 U	4 U	4 U	44.7 D	4 U	**59**
MW-206C	04/28/04		2 U	1.21	2 U	2 U	14.9	2 U	4 U	2 U	2 U	37.7	2 U	**54**
MW-206C	05/21/05		1 U	1.5	1 U	1.1	9.2	1 U	2 U	1 U	1 U	34	1 U	**46**
MW-206C	10/19/05		1 U	3.8	1 U	2.6	15	1 U	0.1	1 U	1 U	47	1 U	**69**
MW-206C	05/06/06		1 U	5	1 U	3.5	14	1 U	2 U	1 U	1 U	52	1 U	**75**
MW-206C	11/27/06		1 U	6.5	1 U	4.4	17	1 U	2 U	1 U	1 U	85	1 U	**113**
MW-206C	10/06/07		1 U	5	1 U	4	11	1 U	2 U	0.4	1 U	44	1 U	**64**
MW-206C	05/18/08		2 U	5	2 U	4	12	2 U	4 U	2 U	2 U	38	2 U	**59**
MW-206C	11/28/08		1 U	3.11	1 U	2.01	5.23	1 U	1 U	1 U	1 U	19.4	1 U	**30**
MW-206C	06/10/09		1 U	2.7	1 U	1.8	4.8	1 U	1 U	1 U	1 U	16	1 U	**25**
MW-206C	04/01/10		1 U	3.4	1 U	2.7	4.8	1 U	1 U	1 U	1 U	16	1 U	**27**
MW-206C	06/25/10		1 U	5.2	1 U	3.6	6.5	1 U	1 U	1 U	1 U	20	1 U	**35**
MW-206C	11/29/10		1 U	3.9	1 U	3.1	5.1	1 U	1 U	1 U	1 U	16	1 U	**28**
MW-206C	06/02/11		1 U	6	1 U	3.9	6.9	1 U	0.26 J	1 U	1 U	22	1 U	**39**
MW-206C	12/22/11		1 U	6.3	1 U	4.4	7.5	1 U	5 U	0.3 J	1 U	24	1 U	**43**
MW-206C	06/26/12		1 U	5.8	1 U	3.8	6.1	1 U	5 U	1 U	1 U	19	1 U	**35**
MW-206C	11/23/12		1 U	7.1	1 U	5.1	7.1	1 U	5 U	0.24 J	1 U	19	1 U	**39**
MW-207	04/23/99		0.39	0.76	2 U	2 U	1.6	2 U	4 U	2.6	2.7	26	2 U	**34**
MW-207	10/27/99		0.59 J	1.3	1 U	0.74 J	5.1	0.06 J	2 U	3.9	5.9	25	1 U	**43**
MW-207	02/17/00		0.54 J	1.1	1 U	0.22 J	1.2	1 U	2 U	2.8	2	22	1 U	**30**
MW-207	04/18/00		0.62 J	1.2	1 U	0.1 J	1.2	0.1 J	2 JB	2.7	2	20	1 U	**30**
MW-207	07/25/00		0.63	1.3	1 U	1 U	1.4	0.16	2 U	2.1	2	17	1 U	**25**
MW-207	11/08/00		0.71	2.1	1 U	0.24	1.4	1 U	2 U	2.3	1.9	16	1 U	**25**
MW-207	04/10/01		0.6	1.5	1 U	1 U	3.2	0.44	2 U	0.51	1.5	11	1 U	**19**
MW-207	10/16/01		0.44	5.3	1 U	0.13	3.4	0.33	2 U	1	4.2	22	1 U	**37**
MW-207	04/17/02		0.36	6.2	2 U	0.26	3.7	0.39	4 U	1.4	5.7	25	1 U	**43**
MW-207	10/08/02		1 U	8	1 U	6	5	1 U	0.8	0.9	5	21	1 U	**47**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-207	04/22/03		0.54 J	7.42	1 U	1.8	5.09	1 U	2 U	2.5	8.37	29.3 E	1 U	**55**
MW-207	04/22/03	Dilution	2 U	7.05	2 U	2.13	4.88	2 U	4 U	2.3	7.6	27.8	2 U	**52**
MW-207	12/28/03		0.53 J	6.12	1 U	2.64	4.5	1 U	1 U	2.58	8.64	29.4 E	1 U	**54**
MW-207	12/28/03	Dilution	2 U	5.68 D	2 U	2.18 D	3.78 D	2 U	2 U	2.21 D	7.19 D	25.8 E	2 U	**47**
MW-207	04/28/04		2 U	5.87	2 U	1.85	4.26	2 U	4 U	2.67	8.24	28.1	2 U	**51**
MW-207	05/21/05		1 U	4.3	1 U	1.7	3	1 U	2 U	2.1	5.4	18	1 U	**35**
MW-207	05/21/05	Fld Dupe	1 U	4.4	1 U	1.6	3	1 U	2 U	2	5.3	18	1 U	**34**
MW-207	10/19/05		1 U	4.5	1 U	1 U	2.7	1 U	2 U	1.3	5.7	17	1 U	**31**
MW-207	05/06/06		1 U	5.2	1 U	1.8	3.3	1 U	2 U	2	6.7	19	1 U	**38**
MW-207	11/27/06		1 U	5.7	1 U	1.1	3.1	1 U	2 U	2.6	9.3	24	1 U	**46**
MW-207	10/07/07		0.4	4	1 U	0.7	3	1 U	1 U	2	7	15	1 U	**32**
MW-207	05/18/08		1 U	4	1 U	2	3	1 U	2 U	2	7	15	1 U	**33**
MW-207	11/29/08		0.36 J	2.97	1 U	1 U	1.89	0.27 J	1 U	1.98	5.58	10.8	1 U	**24**
MW-207	06/10/09		0.31 J	2.4	1 U	0.65 J	1.8	1 U	1 U	2.1	4.6	9.9	1 U	**22**
MW-207	11/25/09		1 U	1.6	1 U	0.6 J	1.2	1 U	1 U	2.2	3.5	7.4	1 U	**17**
MW-207	06/24/10		0.18 J	1.3	1 U	0.52 J	1	1 U	1 U	1.9	2.8	5.6	1 U	**13**
MW-207	11/25/10		0.22 J	1.3	1 U	0.72 J	1.3	1 U	1 U	2.2	3	6	1 U	**15**
MW-207	06/02/11		1 U	1.5	1 U	0.6 J	1.2	1 U	0.3 J	1.6	2.8	5.2	1 U	**13**
MW-207	12/29/11		0.19 J	1.5	1 U	0.57 J	1.4	1 U	5 U	1.7	2.6	4.4	1 U	**12**
MW-207	06/26/12		0.27 J	1.4	1 U	0.4 J	1.2	1 U	5 U	1.3	2.2	3.9	1 U	**11**
MW-207	11/30/12		0.22 J	1.4	1 U	0.53 J	1.2	1 U	5 U	1.4	2.3	4	1 U	**11**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Results reported in micrograms per liter (µg/l)

Highlighted results equal or exceed the Maximum Contaminant Level (MCL), where applicable

CFM	Chloroform
1,1-DCA	1,1-Dichloroethane
1,2-DCA	1,2-Dichloroethane
1,1-DCE	1,1-Dichloroethene
c1,2-DCE	cis- 1,2-Dichloroethene
t1,2-DCE	trans-1,2-Dichloroethene
MC	Methylene Chloride
PCE	Tetrachloroethene
1,1,1-TCA	1,1,1-Trichloroethane
TCE	Trichloroethene
VC	Vinyl Chloride
Total VOCs	Sum of Total Volatile Organic Compound Concentrations

B	Concentration is less than the reporting limit but greater than the instrument detection limit.
D	Reported concentration is based on an analysis requiring a secondary detection limit.
E	The associated value exceeds the calibration range.
J	The reported concentration is estimated.
U	Analyte was not detected at or above the reporting limit.

Sample Type reported as undiluted, investigative sample unless stated otherwise

Fld Dupe Field Duplicate

Table 3: Southeast Rockford NPL Site
Ground Water Elevations

Station Identification	Measurement Date	Water Level (ft TOC)	Groundwater Elevation (ft amsl)	Total Depth (ft TOC)	Comments
MW-16	11/24/12	27.17	700.87	62.36	Limited access - IEPA Lock
MW-47	11/25/12	43.50	692.16	54.49	
MW-101A	11/24/12	46.33	719.29	90.35	
MW-101B	11/24/12	47.37	719.25	153.74	
MW-101C	11/30/12	47.13	719.35	174.89	Field Duplicate (FD-2) collected
MW-101D	11/24/12	48.75	716.21	212.72	
MW-102A	11/30/12	19.50	768.93	37.69	
MW-102B	11/30/12	37.25	751.36	100.50	
MW-102C	11/30/12	40.31	749.56	187.42	
MW-113A	11/24/12	58.17	708.37	104.50	
MW-113B	11/24/12	58.63	708.02	155.26	
MW-114A	11/24/12	30.43	696.46	97.48	
MW-114B	11/24/12	31.92	695.50	222.58	Field Duplicate (FD-1) collected; Limited access - IEPA Lock
MW-117B	11/25/12	7.70	688.56	89.50	
MW-117C	11/25/12	6.70	689.41	158.31	1 bolt hole stripped
MW-117D	11/25/12	6.21	689.89	200.20	
MW-119	11/25/12	27.89	691.08	62.41	
MW-121	11/25/12	24.58	692.40	67.55	
MW-124	11/25/12	37.33	693.97	102.76	
MW-130	11/24/12	26.22	701.73	38.17	
MW-133A	11/24/12	37.35	742.83	37.85	dry - no sample collected
MW-133B	11/24/12	30.82	749.51	61.49	
MW-133C	11/24/12	26.21	754.08	98.49	
MW-136	11/24/12	38.58	796.19	44.33	
MW-200	11/24/12	52.30	707.86	89.93	
MW-201	11/25/12	31.92	697.11	50.15	
MW-202	11/30/12	31.35	698.27	50.01	
MW-203	11/30/12	36.89	692.20	49.35	
MW-204	11/25/12	28.97	688.24	88.96	
MW-205A	12/02/12	4.85	688.48	110.27	limited access - bailed
MW-205B	12/02/12	4.73	688.49	150.05	limited access - bailed
MW-206A	11/23/12	6.81	686.89	90.24	
MW-206B	11/23/12	4.73	688.53	129.94	
MW-206C	11/23/12	5.00	688.06	251.31	
MW-207	11/30/12	36.47	687.70	90.81	

ft amsl Feet above mean sea level
ft TOC Feet from Top of Casing

APPENDIX A

Ground Water Monitoring
Laboratory Data Sheets and
Data Validation Summary

Data Quality Control Criteria Review Summary

SDG Number: 1212036 **Project Number:** 1016-2

Site: SE Rockford, 28th Event

Contractor Lab: TriMatrix (Grand Rapids, MI)

Validator: Brian LaFlamme **Validation Date:** 01/16/13

Sample Matrix: Water **Sample Date:** 11/30/12 – 12/02/12

Analytical Methods: EPA SW-846 Method 8260B

Sample Designations:

MW-101C	**MW-202**	**MW-205A**	**FD-2 (field duplicate of MW-101C)**
MW-102A	**MW-102C**	**MW-205B**	
MW-102B	**MW-203**	**MW-207**	

The analytical data were reviewed in accordance with the analytical methods, SW-846 validation guidelines, and the Environmental Protections Agency (EPA) Contract Laboratory Program (CLP) National Functional Guidelines. The review included comparing quality control (QC) values provided on the laboratory QC forms to method QC criteria. Review of the raw data was not performed.

Quality Control Summary

QC Review Item	VOA
Completeness	X
Case Narrative	X
Chain of Custody (COC) Forms	X
Sample Preservation	X
Holding Times	X
Laboratory Blank Results	X
System Monitoring Compounds (Surrogate) Results	X
Matrix Spike/Matrix Duplicate (MS/MSD) Results	X
Laboratory Control Sample (LCS) Results	X
Method Specific QC Results *	1
System Performance	X
Field QC Results #	2
Other	3

X Acceptable, no qualification necessary NR Not required
See validation summary comment NA Not applicable
*) The reviewer has indicated in the comments, if necessary, the method specific QC results included in the data package that were reviewed.
#) Field QC may include field duplicates, trip blanks, rinse blanks, field blanks, and equipment blank samples as required by project specific criteria.

Data for the above samples are:

- ☒ Acceptable for use
- ☐ Acceptable for use as qualified
- ☐ Unacceptable for use

Is action required by the Project Manager?

Yes ☐ No ☒

Data Validation Summary Comments:

1. **Method Specific QC Criteria** – The corresponding CCV in the analytical batch had a recovery below the lower control limit of the method for 1,2-Dibromo-3-chloropropane. Therefore, positive results in any associated samples are considered estimated; non-detectable results are not qualified.

   The corresponding CCV in the analytical batch had a recovery exceeding the upper control limit of the method for carbon disulfide. Therefore, positive results in any associated samples are considered estimated; non-detectable results are not qualified.

   Because neither of these compounds are chemicals of concern, and there were no positive results, qualification is not necessary.

2. **Field Quality Control Samples** – The relative percent difference (RPD) is not necessarily calculated if both the primary and duplicate results are not five times greater than the reporting limit. However, the RPD between the investigative and duplicate samples was generally less than 8%. Qualification is not necessary.

3. **Other**

Two containers had labels different from the COC. The samples labeled as MW-102A and MW-102B on the COC form had MW-101A and MW-101B written on the bottles. The laboratory-receiving group correctly logged these in per the sample IDs listed on the COC form. There were no MW-101A or MW-101B samples listed on the COC form where there needed to be concerned about bottles being switched. .

OVERALL ASSESSMENT OF DATA

Based on the review of the quality control criteria, the method appeared to be in control. Therefore, the data are acceptable for use.

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1212036**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW101C**	Sampled:	11/30/12 09:08
Lab Sample ID:	**1212036-01**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	12/04/12 09:30
Unit:	ug/L	Prepared:	12/10/201: By: BAG
Dilution Factor:	2.5	Analyzed:	12/10/12 By: DLV
QC Batch:	1215198	Analytical Batch:	2L11013

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	**6.5J**	50	2.7
71-43-2	Benzene	2.5U	2.5	0.28
74-97-5	Bromochloromethane	2.5U	2.5	0.74
75-27-4	Bromodichloromethane	2.5U	2.5	0.32
75-25-2	Bromoform	2.5U	2.5	0.64
74-83-9	Bromomethane	2.5U	2.5	0.54
*75-15-0	Carbon Disulfide	12U	12	0.58
56-23-5	Carbon Tetrachloride	2.5U	2.5	0.66
108-90-7	Chlorobenzene	2.5U	2.5	0.42
75-00-3	Chloroethane	2.5U	2.5	0.36
67-66-3	Chloroform	**1.3J**	2.5	0.24
74-87-3	Chloromethane	2.5U	2.5	0.72
*96-12-8	1,2-Dibromo-3-chloropropane	2.5U	2.5	0.32
124-48-1	Dibromochloromethane	2.5U	2.5	0.38
106-93-4	1,2-Dibromoethane	2.5U	2.5	0.38
95-50-1	1,2-Dichlorobenzene	2.5U	2.5	0.59
541-73-1	1,3-Dichlorobenzene	2.5U	2.5	0.60
106-46-7	1,4-Dichlorobenzene	2.5U	2.5	0.62
75-34-3	1,1-Dichloroethane	**99**	2.5	0.46
107-06-2	1,2-Dichloroethane	2.5U	2.5	0.53
75-35-4	1,1-Dichloroethene	**20**	2.5	0.52
156-59-2	cis-1,2-Dichloroethene	**40**	2.5	0.30
156-60-5	trans-1,2-Dichloroethene	**3.6**	2.5	0.50
78-87-5	1,2-Dichloropropane	2.5U	2.5	0.69
10061-01-5	cis-1,3-Dichloropropene	2.5U	2.5	0.48
10061-02-6	trans-1,3-Dichloropropene	2.5U	2.5	0.47
100-41-4	Ethylbenzene	2.5U	2.5	0.52
591-78-6	2-Hexanone	12U	12	1.2
75-09-2	Methylene Chloride	12U	12	0.61
78-93-3	2-Butanone (MEK)	12U	12	1.6
108-10-1	4-Methyl-2-pentanone (MIBK)	12U	12	0.99

VALIDATED

Continued on next page

*See Statement of Data Qualifications

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1212036**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW101C**	Sampled:	11/30/12 09:08
Lab Sample ID:	**1212036-01**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	12/04/12 09:30
Unit:	ug/L	Prepared:	12/10/2012 By: BAG
Dilution Factor:	2.5	Analyzed:	12/10/12 By: DLV
QC Batch:	1215198	Analytical Batch:	2L11013

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	2.5U	2.5	0.51
79-34-5	1,1,2,2-Tetrachloroethane	2.5U	2.5	0.64
127-18-4	Tetrachloroethene	**18**	2.5	0.56
108-88-3	Toluene	2.5U	2.5	0.46
71-55-6	1,1,1-Trichloroethane	**360**	2.5	0.34
79-00-5	1,1,2-Trichloroethane	**0.90J**	2.5	0.51
79-01-6	Trichloroethene	**20**	2.5	0.53
75-01-4	Vinyl Chloride	2.5U	2.5	0.52
1330-20-7	Xylene (Total)	7.5U	7.5	0.98

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*103*	*85-118*
1,2-Dichloroethane-d4	*104*	*87-122*
Toluene-d8	*99*	*85-113*
4-Bromofluorobenzene	*100*	*82-110*

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1212036**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**FD2** MW-101C Field dupe	Sampled:	11/30/12 09:11
Lab Sample ID:	**1212036-02**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	12/04/12 09:30
Unit:	ug/L	Prepared:	12/10/2012 By: BAG
Dilution Factor:	5	Analyzed:	12/10/12 By: DLV
QC Batch:	1215198	Analytical Batch:	2L11013

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	**6.9J**	100	5.4
71-43-2	Benzene	5.0U	5.0	0.57
74-97-5	Bromochloromethane	5.0U	5.0	1.5
75-27-4	Bromodichloromethane	5.0U	5.0	0.64
75-25-2	Bromoform	5.0U	5.0	1.3
74-83-9	Bromomethane	5.0U	5.0	1.1
*75-15-0	Carbon Disulfide	25U	25	1.2
56-23-5	Carbon Tetrachloride	5.0U	5.0	1.3
108-90-7	Chlorobenzene	5.0U	5.0	0.84
75-00-3	Chloroethane	5.0U	5.0	0.72
67-66-3	Chloroform	**1.4J**	5.0	0.49
74-87-3	Chloromethane	5.0U	5.0	1.4
*96-12-8	1,2-Dibromo-3-chloropropane	5.0U	5.0	0.64
124-48-1	Dibromochloromethane	5.0U	5.0	0.76
106-93-4	1,2-Dibromoethane	5.0U	5.0	0.76
95-50-1	1,2-Dichlorobenzene	5.0U	5.0	1.2
541-73-1	1,3-Dichlorobenzene	5.0U	5.0	1.2
106-46-7	1,4-Dichlorobenzene	5.0U	5.0	1.2
75-34-3	1,1-Dichloroethane	**99**	5.0	0.92
107-06-2	1,2-Dichloroethane	5.0U	5.0	1.1
75-35-4	1,1-Dichloroethene	**20**	5.0	1.0
156-59-2	cis-1,2-Dichloroethene	**40**	5.0	0.60
156-60-5	trans-1,2-Dichloroethene	**3.6J**	5.0	1.0
78-87-5	1,2-Dichloropropane	5.0U	5.0	1.4
10061-01-5	cis-1,3-Dichloropropene	5.0U	5.0	0.95
10061-02-6	trans-1,3-Dichloropropene	5.0U	5.0	0.94
100-41-4	Ethylbenzene	5.0U	5.0	1.0
591-78-6	2-Hexanone	25U	25	2.5
75-09-2	Methylene Chloride	25U	25	1.2
78-93-3	2-Butanone (MEK)	25U	25	3.2
108-10-1	4-Methyl-2-pentanone (MIBK)	25U	25	2.0

Continued on next page

*See Statement of Data Qualifications

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1212036**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**FD2**	Sampled:	11/30/12 09:11
Lab Sample ID:	**1212036-02**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	12/04/12 09:30
Unit:	ug/L	Prepared:	12/10/2012 By: BAG
Dilution Factor:	5	Analyzed:	12/10/12 By: DLV
QC Batch:	1215198	Analytical Batch:	2L11013

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	5.0U	5.0	1.0
79-34-5	1,1,2,2-Tetrachloroethane	5.0U	5.0	1.3
127-18-4	Tetrachloroethene	**18**	5.0	1.1
108-88-3	Toluene	5.0U	5.0	0.92
71-55-6	1,1,1-Trichloroethane	**360**	5.0	0.69
79-00-5	1,1,2-Trichloroethane	5.0U	5.0	1.0
79-01-6	Trichloroethene	**20**	5.0	1.1
75-01-4	Vinyl Chloride	5.0U	5.0	1.0
1330-20-7	Xylene (Total)	15U	15	2.0

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*103*	*85-118*
1,2-Dichloroethane-d4	*103*	*87-122*
Toluene-d8	*99*	*85-113*
4-Bromofluorobenzene	*98*	*82-110*

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1212036**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW102A**	Sampled:	11/30/12 10:03
Lab Sample ID:	**1212036-03**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	12/04/12 09:30
Unit:	ug/L	Prepared:	12/10/2012 By: BAG
Dilution Factor:	1	Analyzed:	12/10/12 By: DLV
QC Batch:	1215198	Analytical Batch:	2L11013

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.1
71-43-2	Benzene	1.0U	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	**0.33J**	1.0	0.14
67-66-3	Chloroform	1.0U	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
*96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	**82**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.21
75-35-4	1,1-Dichloroethene	**1.6**	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	**160**	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	**5.7**	1.0	0.20
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

Continued on next page

*See Statement of Data Qualifications

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ◆ Grand Rapids, MI 49512 ◆ 616.975.4500 ◆ Fax 616.942.7663 ◆ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1212036**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW102A**	Sampled:	11/30/12 10:03
Lab Sample ID:	**1212036-03**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	12/04/12 09:30
Unit:	ug/L	Prepared:	12/10/2012 By: BAG
Dilution Factor:	1	Analyzed:	12/10/12 By: DLV
QC Batch:	1215198	Analytical Batch:	2L11013

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	1.0U	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	**59**	1.0	0.14
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.20
79-01-6	Trichloroethene	**14**	1.0	0.21
75-01-4	Vinyl Chloride	1.0U	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*101*	*85-118*
1,2-Dichloroethane-d4	*102*	*87-122*
Toluene-d8	*99*	*85-113*
4-Bromofluorobenzene	*97*	*82-110*

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1212036**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW102B**	Sampled:	11/30/12 10:42
Lab Sample ID:	**1212036-04**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	12/04/12 09:30
Unit:	ug/L	Prepared:	12/10/201: By: BAG
Dilution Factor:	1	Analyzed:	12/10/12 By: DLV
QC Batch:	1215198	Analytical Batch:	2L11013

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	**1.2J**	20	1.1
71-43-2	Benzene	1.0U	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	**0.65J**	1.0	0.14
67-66-3	Chloroform	1.0U	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
*96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	**2.8**	1.0	0.18
107-06-2	1,2-Dichloroethane	**0.52J**	1.0	0.21
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	**4.6**	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.20
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

Continued on next page

*See Statement of Data Qualifications

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7457 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1212036**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW102B**	Sampled:	11/30/12 10:42
Lab Sample ID:	**1212036-04**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	12/04/12 09:30
Unit:	ug/L	Prepared:	12/10/2012 By: BAG
Dilution Factor:	1	Analyzed:	12/10/12 By: DLV
QC Batch:	1215198	Analytical Batch:	2L11013

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	1.0U	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	1.0U	1.0	0.14
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.20
79-01-6	Trichloroethene	1.0U	1.0	0.21
75-01-4	Vinyl Chloride	**0.43J**	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*102*	*85-118*
1,2-Dichloroethane-d4	*103*	*87-122*
Toluene-d8	*99*	*85-113*
4-Bromofluorobenzene	*99*	*82-110*

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1212036**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW102C**	Sampled:	11/30/12 11:26
Lab Sample ID:	**1212036-05**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	12/04/12 09:30
Unit:	ug/L	Prepared:	12/10/2012 By: BAG
Dilution Factor:	2	Analyzed:	12/10/12 By: DLV
QC Batch:	1215198	Analytical Batch:	2L11013

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	**5.0J**	40	2.2
71-43-2	Benzene	2.0U	2.0	0.23
74-97-5	Bromochloromethane	2.0U	2.0	0.59
75-27-4	Bromodichloromethane	2.0U	2.0	0.26
75-25-2	Bromoform	2.0U	2.0	0.51
74-83-9	Bromomethane	2.0U	2.0	0.43
*75-15-0	Carbon Disulfide	10U	10	0.46
56-23-5	Carbon Tetrachloride	2.0U	2.0	0.53
108-90-7	Chlorobenzene	2.0U	2.0	0.33
75-00-3	Chloroethane	2.0U	2.0	0.29
67-66-3	Chloroform	**0.36J**	2.0	0.20
74-87-3	Chloromethane	2.0U	2.0	0.58
*96-12-8	1,2-Dibromo-3-chloropropane	2.0U	2.0	0.26
124-48-1	Dibromochloromethane	2.0U	2.0	0.30
106-93-4	1,2-Dibromoethane	2.0U	2.0	0.30
95-50-1	1,2-Dichlorobenzene	2.0U	2.0	0.47
541-73-1	1,3-Dichlorobenzene	2.0U	2.0	0.48
106-46-7	1,4-Dichlorobenzene	2.0U	2.0	0.50
75-34-3	1,1-Dichloroethane	**64**	2.0	0.37
107-06-2	1,2-Dichloroethane	**0.54J**	2.0	0.43
75-35-4	1,1-Dichloroethene	**15**	2.0	0.42
156-59-2	cis-1,2-Dichloroethene	**200**	2.0	0.24
156-60-5	trans-1,2-Dichloroethene	**2.0**	2.0	0.40
78-87-5	1,2-Dichloropropane	2.0U	2.0	0.55
10061-01-5	cis-1,3-Dichloropropene	2.0U	2.0	0.38
10061-02-6	trans-1,3-Dichloropropene	2.0U	2.0	0.37
100-41-4	Ethylbenzene	2.0U	2.0	0.41
591-78-6	2-Hexanone	10U	10	0.99
75-09-2	Methylene Chloride	10U	10	0.49
78-93-3	2-Butanone (MEK)	10U	10	1.3
108-10-1	4-Methyl-2-pentanone (MIBK)	10U	10	0.79

Continued on next page

*See Statement of Data Qualifications

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1212036**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW102C**	Sampled:	11/30/12 11:26
Lab Sample ID:	**1212036-05**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	12/04/12 09:30
Unit:	ug/L	Prepared:	12/10/2012 By: BAG
Dilution Factor:	2	Analyzed:	12/10/12 By: DLV
QC Batch:	1215198	Analytical Batch:	2L11013

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	2.0U	2.0	0.41
79-34-5	1,1,2,2-Tetrachloroethane	2.0U	2.0	0.51
127-18-4	Tetrachloroethene	**4.2**	2.0	0.45
108-88-3	Toluene	2.0U	2.0	0.37
71-55-6	1,1,1-Trichloroethane	**41**	2.0	0.28
79-00-5	1,1,2-Trichloroethane	2.0U	2.0	0.41
79-01-6	Trichloroethene	**15**	2.0	0.42
75-01-4	Vinyl Chloride	2.0U	2.0	0.42
1330-20-7	Xylene (Total)	6.0U	6.0	0.79

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*103*	*85-118*
1,2-Dichloroethane-d4	*103*	*87-122*
Toluene-d8	*99*	*85-113*
4-Bromofluorobenzene	*99*	*82-110*

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1212036**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW202**	Sampled:	11/30/12 12:55
Lab Sample ID:	**1212036-07**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	12/04/12 09:30
Unit:	ug/L	Prepared:	12/10/201: By: BAG
Dilution Factor:	1	Analyzed:	12/10/12 By: DLV
QC Batch:	1215198	Analytical Batch:	2L11013

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	**1.2J**	20	1.1
71-43-2	Benzene	1.0U	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	1.0U	1.0	0.14
67-66-3	Chloroform	1.0U	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
*96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	**0.45J**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.21
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	1.0U	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.20
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

Continued on next page

*See Statement of Data Qualifications

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1212036**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW202**	Sampled:	11/30/12 12:55
Lab Sample ID:	**1212036-07**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	12/04/12 09:30
Unit:	ug/L	Prepared:	12/10/201: By: BAG
Dilution Factor:	1	Analyzed:	12/10/12 By: DLV
QC Batch:	1215198	Analytical Batch:	2L11013

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	**2.1**	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	**1.0**	1.0	0.14
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.20
79-01-6	Trichloroethene	**0.30J**	1.0	0.21
75-01-4	Vinyl Chloride	1.0U	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*101*	*85-118*
1,2-Dichloroethane-d4	*104*	*87-122*
Toluene-d8	*100*	*85-113*
4-Bromofluorobenzene	*97*	*82-110*

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1212036**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW203**	Sampled:	11/30/12 12:15
Lab Sample ID:	**1212036-06**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	12/04/12 09:30
Unit:	ug/L	Prepared:	12/10/201: By: BAG
Dilution Factor:	1	Analyzed:	12/10/12 By: DLV
QC Batch:	1215198	Analytical Batch:	2L11013

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	**1.8J**	20	1.1
71-43-2	Benzene	1.0U	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	1.0U	1.0	0.14
67-66-3	Chloroform	1.0U	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
*96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	**0.19J**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.21
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	1.0U	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.20
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

Continued on next page

*See Statement of Data Qualifications

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5550 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1212036**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW203**	Sampled:	11/30/12 12:15
Lab Sample ID:	**1212036-06**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	12/04/12 09:30
Unit:	ug/L	Prepared:	12/10/2012 By: BAG
Dilution Factor:	1	Analyzed:	12/10/12 By: DLV
QC Batch:	1215198	Analytical Batch:	2L11013

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	**11**	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	**0.36J**	1.0	0.14
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.20
79-01-6	Trichloroethene	**0.34J**	1.0	0.21
75-01-4	Vinyl Chloride	1.0U	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*100*	*85-118*
1,2-Dichloroethane-d4	*103*	*87-122*
Toluene-d8	*100*	*85-113*
4-Bromofluorobenzene	*97*	*82-110*

VALIDATED

Reviewed By [signature]

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1212036**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW205A**	Sampled:	12/02/12 09:12
Lab Sample ID:	**1212036-10**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	12/04/12 09:30
Unit:	ug/L	Prepared:	12/10/2012 By: BAG
Dilution Factor:	1	Analyzed:	12/10/12 By: DLV
QC Batch:	1215198	Analytical Batch:	2L11013

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.1
71-43-2	Benzene	1.0U	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	1.0U	1.0	0.14
67-66-3	Chloroform	**0.26J**	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
*96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	**20**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.21
75-35-4	1,1-Dichloroethene	**11**	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	**4.6**	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.20
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

Continued on next page

*See Statement of Data Qualifications

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1212036**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW205A**	Sampled:	12/02/12 09:12
Lab Sample ID:	**1212036-10**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	12/04/12 09:30
Unit:	ug/L	Prepared:	12/10/2012 By: BAG
Dilution Factor:	1	Analyzed:	12/10/12 By: DLV
QC Batch:	1215198	Analytical Batch:	2L11013

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	**24**	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	**27**	1.0	0.14
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.20
79-01-6	Trichloroethene	**15**	1.0	0.21
75-01-4	Vinyl Chloride	1.0U	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*103*	*85-118*
1,2-Dichloroethane-d4	*104*	*87-122*
Toluene-d8	*100*	*85-113*
4-Bromofluorobenzene	*100*	*82-110*

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5550 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1212036**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW205B**	Sampled:	12/02/12 08:25
Lab Sample ID:	**1212036-09**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	12/04/12 09:30
Unit:	ug/L	Prepared:	12/10/201: By: BAG
Dilution Factor:	1	Analyzed:	12/10/12 By: DLV
QC Batch:	1215198	Analytical Batch:	2L11013

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	**1.5J**	20	1.1
71-43-2	Benzene	1.0U	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	1.0U	1.0	0.14
67-66-3	Chloroform	**0.32J**	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
*96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	**20**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.21
75-35-4	1,1-Dichloroethene	**10**	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	**6.0**	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.20
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

Continued on next page

*See Statement of Data Qualifications

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7451 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1212036**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW205B**	Sampled:	12/02/12 08:25
Lab Sample ID:	**1212036-09**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	12/04/12 09:30
Unit:	ug/L	Prepared:	12/10/2012 By: BAG
Dilution Factor:	1	Analyzed:	12/10/12 By: DLV
QC Batch:	1215198	Analytical Batch:	2L11013

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	**16**	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	**25**	1.0	0.14
79-00-5	1,1,2-Trichloroethane	**0.30J**	1.0	0.20
79-01-6	Trichloroethene	**12**	1.0	0.21
75-01-4	Vinyl Chloride	1.0U	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*103*	*85-118*
1,2-Dichloroethane-d4	*103*	*87-122*
Toluene-d8	*100*	*85-113*
4-Bromofluorobenzene	*99*	*82-110*

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1212036**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW207**	Sampled:	11/30/12 13:41
Lab Sample ID:	**1212036-08**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	12/04/12 09:30
Unit:	ug/L	Prepared:	12/10/2012 By: BAG
Dilution Factor:	1	Analyzed:	12/10/12 By: DLV
QC Batch:	1215198	Analytical Batch:	2L11013

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.1
71-43-2	Benzene	1.0U	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	1.0U	1.0	0.14
67-66-3	Chloroform	**0.22J**	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
*96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	**1.4**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.21
75-35-4	1,1-Dichloroethene	**0.53J**	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	**1.2**	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.20
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

Continued on next page

*See Statement of Data Qualifications

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1212036**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW207**	Sampled:	11/30/12 13:41
Lab Sample ID:	**1212036-08**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	12/04/12 09:30
Unit:	ug/L	Prepared:	12/10/2012 By: BAG
Dilution Factor:	1	Analyzed:	12/10/12 By: DLV
QC Batch:	1215198	Analytical Batch:	2L11013

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	**1.4**	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	**2.3**	1.0	0.14
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.20
79-01-6	Trichloroethene	**4.0**	1.0	0.21
75-01-4	Vinyl Chloride	1.0U	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*102*	*85-118*
1,2-Dichloroethane-d4	*104*	*87-122*
Toluene-d8	*101*	*85-113*
4-Bromofluorobenzene	*98*	*82-110*

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

5560 Corporate Exchange Court SE
Grand Rapids, MI 49512
Phone (616) 975-4500 Fax (616) 942-7463
www.trimatrixlabs.com

Chain of Custody Record

COC No. 142907

Pg 1 of 1

For Lab Use Only
Cart
VOA Rack/Tray 136, 451 Blue LL 12/4/12
Receipt Log No. 41910
Project Chemist
Work Order No. 1212036

Client Name: Nationwide Env. Svcs
Address: 14818 N. 6th Ave STE A
City, State, Zip: Golden CO 80401
Phone/Fax: 303 232 2134
Email: R. LaFlamme

Project Name: SE Rock
Client Project No. (P.O. No.)
Invoice To: ☐ Client ☐ Other (comments)
Contact/Report To:

Analyses Requested: VOC, Aug 8260, GRO

Preservatives: A NONE pH~7; B HNO_3 pH<2; C H_2SO_4 pH<2; D 1+1 HCl pH<2; E NaOH pH>12; F $ZnAc/NaOH$ pH>9; G MeOH; H Other (note below)

Container Type (corresponds to Container Packing List)

Schedule	Matrix Code	Sample Number	Field Sample ID	Cooler ID	Sample Date	Sample Time	Matrix	Number of Containers Submitted	Total	Sample Comments
		01	MW 101C		11/30	908	GW	3	3	
		02	FD2		11/30	911	GW	3	3	
		03	MW102A		11/30	1003	GW	3	3	
		04	MW102B		11/30	1042	GW	3	3	
		05	MW102C		11/30	1126	GW	3	3	
		06	MW 203		11/30	1215	GW	3	3	
		07	MW 202		11/30	1255	GW	3	3	
		08	MW 207		11/30	1341	GW	3	3	
		09	MW 205B		12/2	825	GW	3	3	
		10	MW 205A		12/2	912	GW	3	3	

Sampled By (print): Patrick Regan
Sampler's Signature:
Company:

How Shipped? Hand ___ Carrier: Fedex
Tracking No. 1941 9831 3780

Relinquished By: Date 12/3/12 Time 1930
1. Received By: Date: Time:
2. Relinquished By: Date: Time:
2. Received By: Date: Time:
3. Relinquished By: Date: Time:
3. Received For Lab By: Date 12/4/12 Time 0930

Comments: All samples kept in secure location at 4°C

WHITE COPY - REPORT YELLOW COPY - LABORATORY PINK COPY - FIELD

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

TRIMATRIX LABORATORIES

Data Quality Control Criteria Review Summary

SDG Number: 1211459 **Project Number:** 1016-2

Site: SE Rockford, 28th Event

Contractor Lab: TriMatrix (Grand Rapids, MI)

Validator: Brian LaFlamme **Validation Date:** 01/16/13

Sample Matrix: Water **Sample Date:** 11/23/12 – 11/25/12

Analytical Methods: EPA SW-846 Method 8260B

Sample Designations:

MW-16	**MW-113A**	**MW-119**	**MW-136**	**MW-206C**
MW-47	**MW-113B**	**MW-121**	**MW-200**	
MW-101A	**MW-114A**	**MW-124**	**MW-201**	
MW-101B	**MW-114B**	**MW-130**	**MW-204**	**Trip Blank TM1982**
MW-101D	**MW-117B**	**MW-133B**	**MW-206A**	
MW-117C	**MW-117D**	**MW-133C**	**MW-206B**	**FD-1 (field duplicate of MW-114B)**

The analytical data were reviewed in accordance with the analytical methods, SW-846 validation guidelines, and the Environmental Protections Agency (EPA) Contract Laboratory Program (CLP) National Functional Guidelines. The review included comparing quality control (QC) values provided on the laboratory QC forms to method QC criteria. Review of the raw data was not performed.

Quality Control Summary

QC Review Item	VOA
Completeness	X
Case Narrative	X
Chain of Custody (COC) Forms	X
Sample Preservation	X
Holding Times	X
Laboratory Blank Results	1
System Monitoring Compounds (Surrogate) Results	X
Matrix Spike/Matrix Duplicate (MS/MSD) Results	X
Laboratory Control Sample (LCS) Results	2
Method Specific QC Results *	3
System Performance	X
Field QC Results #	4
Other	X

X Acceptable, no qualification necessary NR Not required
See validation summary comment NA Not applicable
*) The reviewer has indicated in the comments, if necessary, the method specific QC results included in the data package that were reviewed.
#) Field QC may include field duplicates, trip blanks, rinse blanks, field blanks, and equipment blank samples as required by project specific criteria.

Data for the above samples are:

- ☐ Acceptable for use
- ☒ Acceptable for use as qualified
- ☐ Unacceptable for use

Is action required by the Project Manager?

Yes ☐ No ☒

Data Validation Summary Comments:

1. **Laboratory Blank Results**
   Acetone was detected in the laboratory method blank in QC batch 1214857 at 3.9 J µg/l. There were no positive detections of acetone in the investigative samples. Therefore, no qualification is necessary.

   Acetone and carbon disulfide were detected in the laboratory method blank in QC batch 1215059 at 11 J µg/l and 0.31 J µg/l, respectively. Because the samples were diluted at 10 times the, the positive detections of acetone in samples MW-101A and MW-133B become 110U µg/l and 120U µg/l, respectively. There were no positive detections of carbon disulfide in the investigative samples. Therefore, no qualification is necessary.

2. **Laboratory Control Sample (LCS) Results**
   The LCS recovery for acetone and carbon disulfide exceeded the upper control limit in the QC batch 1214857. There were no positive detections of acetone or carbon disulfide in the investigative samples. Therefore, no qualification is necessary.

3. **Method Specific QC Criteria** – The corresponding CCV in the analytical batch had a recovery below the lower control limit of the method for 1,2-dibromo-3-chloropropane. Therefore, positive results in any associated samples are considered estimated; non-detectable results are not qualified.

   The corresponding CCV in the analytical batch had a recovery exceeding the upper control limit of the method for acetone, carbon disulfide, and 1,2-dibromo-3-chloropropane. Therefore, positive results in any associated samples are considered estimated; non-detectable results are not qualified.

   Because neither of these compounds are chemicals of concern, and there were either no positive results or positive results have already been qualified, further qualification is not necessary.

4. **Field Quality Control Samples** – The relative percent difference (RPD) is not necessarily calculated if both the primary and duplicate results are not five times greater than the reporting limit. However, the RPD between the investigative and duplicate samples was approximately 5%. An RPD of approximately 15% resulted from comparing positive results less than 1.0 µg/l. Qualification is not necessary.

OVERALL ASSESSMENT OF DATA

Based on the review of the quality control criteria, the method appeared to be in control. Therefore, the data are acceptable for use.

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW16**	Sampled:	11/24/12 12:15
Lab Sample ID:	**1211459-07**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214846	Analytical Batch:	2K30034

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.1
71-43-2	Benzene	1.0U	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	1.0U	1.0	0.14
67-66-3	Chloroform	**0.90J**	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	**68**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.21
75-35-4	1,1-Dichloroethene	**13**	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	**22**	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	**2.4**	1.0	0.20
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

Continued on next page

*See Statement of Data Qualifications

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW16**	Sampled:	11/24/12 12:15
Lab Sample ID:	**1211459-07**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214846	Analytical Batch:	2K30034

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	**10**	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	**110**	1.0	0.14
79-00-5	1,1,2-Trichloroethane	**0.51J**	1.0	0.20
79-01-6	Trichloroethene	**35**	1.0	0.21
75-01-4	Vinyl Chloride	1.0U	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*101*	*85-118*
1,2-Dichloroethane-d4	*107*	*87-122*
Toluene-d8	*98*	*85-113*
4-Bromofluorobenzene	*102*	*82-110*

VALIDATED

Reviewed By _____

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5550 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW47**	Sampled:	11/25/12 10:21
Lab Sample ID:	**1211459-20**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/30/12 By: BAG
QC Batch:	1214857	Analytical Batch:	2K30046

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
*67-64-1	Acetone	20U	20	1.1
71-43-2	Benzene	1.0U	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	1.0U	1.0	0.14
67-66-3	Chloroform	1.0U	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	1.0U	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.21
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	1.0U	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.20
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

Continued on next page

*See Statement of Data Qualifications

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW47**	Sampled:	11/25/12 10:21
Lab Sample ID:	**1211459-20**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/30/12 By: BAG
QC Batch:	1214857	Analytical Batch:	2K30046

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	1.0U	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	1.0U	1.0	0.14
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.20
79-01-6	Trichloroethene	1.0U	1.0	0.21
75-01-4	Vinyl Chloride	1.0U	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*101*	*85-118*
1,2-Dichloroethane-d4	*108*	*87-122*
Toluene-d8	*101*	*85-113*
4-Bromofluorobenzene	*104*	*82-110*

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW101A**	Sampled:	11/24/12 16:00
Lab Sample ID:	**1211459-16**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	12/5/2012 By: BAG
Dilution Factor:	10	Analyzed:	12/05/12 By: DLV
QC Batch:	1215059	Analytical Batch:	2L06032

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
*67-64-1	Acetone	~~110J~~ 110U	200	11
71-43-2	Benzene	10U	10	1.1
74-97-5	Bromochloromethane	10U	10	3.0
75-27-4	Bromodichloromethane	10U	10	1.3
75-25-2	Bromoform	10U	10	2.6
74-83-9	Bromomethane	10U	10	2.1
*75-15-0	Carbon Disulfide	50U	50	2.3
56-23-5	Carbon Tetrachloride	**3.5J**	10	2.6
108-90-7	Chlorobenzene	10U	10	1.7
75-00-3	Chloroethane	10U	10	1.4
67-66-3	Chloroform	**3.4J**	10	0.98
74-87-3	Chloromethane	10U	10	2.9
*96-12-8	1,2-Dibromo-3-chloropropane	10U	10	1.3
124-48-1	Dibromochloromethane	10U	10	1.5
106-93-4	1,2-Dibromoethane	10U	10	1.5
95-50-1	1,2-Dichlorobenzene	10U	10	2.4
541-73-1	1,3-Dichlorobenzene	10U	10	2.4
106-46-7	1,4-Dichlorobenzene	10U	10	2.5
75-34-3	1,1-Dichloroethane	**240**	10	1.8
107-06-2	1,2-Dichloroethane	10U	10	2.1
75-35-4	1,1-Dichloroethene	**39**	10	2.1
156-59-2	cis-1,2-Dichloroethene	**1200**	10	1.2
156-60-5	trans-1,2-Dichloroethene	**57**	10	2.0
78-87-5	1,2-Dichloropropane	10U	10	2.8
10061-01-5	cis-1,3-Dichloropropene	10U	10	1.9
10061-02-6	trans-1,3-Dichloropropene	10U	10	1.9
100-41-4	Ethylbenzene	10U	10	2.1
591-78-6	2-Hexanone	50U	50	4.9
75-09-2	Methylene Chloride	50U	50	2.4
78-93-3	2-Butanone (MEK)	50U	50	6.3
108-10-1	4-Methyl-2-pentanone (MIBK)	50U	50	4.0

Continued on next page

*See Statement of Data Qualifications

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW101A**	Sampled:	11/24/12 16:00
Lab Sample ID:	**1211459-16**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	12/5/2012 By: BAG
Dilution Factor:	10	Analyzed:	12/05/12 By: DLV
QC Batch:	1215059	Analytical Batch:	2L06032

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	10U	10	2.0
79-34-5	1,1,2,2-Tetrachloroethane	10U	10	2.6
127-18-4	Tetrachloroethene	**55**	10	2.3
108-88-3	Toluene	10U	10	1.8
71-55-6	1,1,1-Trichloroethane	**500**	10	1.4
79-00-5	1,1,2-Trichloroethane	10U	10	2.0
79-01-6	Trichloroethene	**160**	10	2.1
75-01-4	Vinyl Chloride	10U	10	2.1
1330-20-7	Xylene (Total)	30U	30	3.9

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*99*	*85-118*
1,2-Dichloroethane-d4	*99*	*87-122*
Toluene-d8	*97*	*85-113*
4-Bromofluorobenzene	*98*	*82-110*

VALIDATED

Reviewed By _____

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5550 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW101B**	Sampled:	11/24/12 15:35
Lab Sample ID:	**1211459-15**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	12/4/2012 By: BAG
Dilution Factor:	2.5	Analyzed:	12/04/12 By: BAG
QC Batch:	1214987	Analytical Batch:	2L05005

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	50U	50	2.7
71-43-2	Benzene	2.5U	2.5	0.28
74-97-5	Bromochloromethane	2.5U	2.5	0.74
75-27-4	Bromodichloromethane	2.5U	2.5	0.32
75-25-2	Bromoform	2.5U	2.5	0.64
74-83-9	Bromomethane	2.5U	2.5	0.54
75-15-0	Carbon Disulfide	12U	12	0.58
56-23-5	Carbon Tetrachloride	2.5U	2.5	0.66
108-90-7	Chlorobenzene	2.5U	2.5	0.42
75-00-3	Chloroethane	2.5U	2.5	0.36
67-66-3	Chloroform	**1.4J**	2.5	0.24
74-87-3	Chloromethane	2.5U	2.5	0.72
*96-12-8	1,2-Dibromo-3-chloropropane	2.5U	2.5	0.32
124-48-1	Dibromochloromethane	2.5U	2.5	0.38
106-93-4	1,2-Dibromoethane	2.5U	2.5	0.38
95-50-1	1,2-Dichlorobenzene	2.5U	2.5	0.59
541-73-1	1,3-Dichlorobenzene	2.5U	2.5	0.60
106-46-7	1,4-Dichlorobenzene	2.5U	2.5	0.62
75-34-3	1,1-Dichloroethane	**120**	2.5	0.46
107-06-2	1,2-Dichloroethane	2.5U	2.5	0.53
75-35-4	1,1-Dichloroethene	**26**	2.5	0.52
156-59-2	cis-1,2-Dichloroethene	**33**	2.5	0.30
156-60-5	trans-1,2-Dichloroethene	**4.1**	2.5	0.50
78-87-5	1,2-Dichloropropane	2.5U	2.5	0.69
10061-01-5	cis-1,3-Dichloropropene	2.5U	2.5	0.48
10061-02-6	trans-1,3-Dichloropropene	2.5U	2.5	0.47
100-41-4	Ethylbenzene	2.5U	2.5	0.52
591-78-6	2-Hexanone	12U	12	1.2
75-09-2	Methylene Chloride	**0.88J**	12	0.61
78-93-3	2-Butanone (MEK)	12U	12	1.6
108-10-1	4-Methyl-2-pentanone (MIBK)	12U	12	0.99

Continued on next page

*See Statement of Data Qualifications

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW101B**	Sampled:	11/24/12 15:35
Lab Sample ID:	**1211459-15**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	12/4/2012 By: BAG
Dilution Factor:	2.5	Analyzed:	12/04/12 By: BAG
QC Batch:	1214987	Analytical Batch:	2L05005

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	2.5U	2.5	0.51
79-34-5	1,1,2,2-Tetrachloroethane	2.5U	2.5	0.64
127-18-4	Tetrachloroethene	**25**	2.5	0.56
108-88-3	Toluene	2.5U	2.5	0.46
71-55-6	1,1,1-Trichloroethane	**430**	2.5	0.34
79-00-5	1,1,2-Trichloroethane	**1.0J**	2.5	0.51
79-01-6	Trichloroethene	**26**	2.5	0.53
75-01-4	Vinyl Chloride	2.5U	2.5	0.52
1330-20-7	Xylene (Total)	7.5U	7.5	0.98

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*104*	*85-118*
1,2-Dichloroethane-d4	*106*	*87-122*
Toluene-d8	*97*	*85-113*
4-Bromofluorobenzene	*96*	*82-110*

VALIDATED

Reviewed By _____

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7453 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW101D**	Sampled:	11/24/12 16:22
Lab Sample ID:	**1211459-17**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214857	Analytical Batch:	2K30046

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
*67-64-1	Acetone	20U	20	1.1
71-43-2	Benzene	1.0U	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	1.0U	1.0	0.14
67-66-3	Chloroform	**1.0**	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	**42**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.21
75-35-4	1,1-Dichloroethene	**13**	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	**27**	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	**1.6**	1.0	0.20
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

VALIDATED

Continued on next page

*See Statement of Data Qualifications

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7460 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW101D**	Sampled:	11/24/12 16:22
Lab Sample ID:	**1211459-17**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214857	Analytical Batch:	2K30046

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	**11**	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	**140**	1.0	0.14
79-00-5	1,1,2-Trichloroethane	**0.37J**	1.0	0.20
79-01-6	Trichloroethene	**16**	1.0	0.21
75-01-4	Vinyl Chloride	1.0U	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*103*	*85-118*
1,2-Dichloroethane-d4	*111*	*87-122*
Toluene-d8	*101*	*85-113*
4-Bromofluorobenzene	*105*	*82-110*

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5550 Corporate Exchange Court SE ♦ Grand Rapids MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW113A**	Sampled:	11/24/12 14:49
Lab Sample ID:	**1211459-13**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214846	Analytical Batch:	2K30034

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.1
71-43-2	Benzene	1.0U	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	1.0U	1.0	0.14
67-66-3	Chloroform	**1.2**	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	**110**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.21
75-35-4	1,1-Dichloroethene	**14**	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	**43**	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	**4.4**	1.0	0.20
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

Continued on next page

*See Statement of Data Qualifications

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW113A**	Sampled:	11/24/12 14:49
Lab Sample ID:	**1211459-13**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214846	Analytical Batch:	2K30034

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	**13**	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	**140**	1.0	0.14
79-00-5	1,1,2-Trichloroethane	**0.70J**	1.0	0.20
79-01-6	Trichloroethene	**45**	1.0	0.21
75-01-4	Vinyl Chloride	1.0U	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*103*	*85-118*
1,2-Dichloroethane-d4	*109*	*87-122*
Toluene-d8	*100*	*85-113*
4-Bromofluorobenzene	*104*	*82-110*

VALIDATED

Reviewed By _____

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW113B**	Sampled:	11/24/12 14:17
Lab Sample ID:	**1211459-12**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214846	Analytical Batch:	2K30034

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.1
71-43-2	Benzene	1.0U	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	1.0U	1.0	0.14
67-66-3	Chloroform	**0.34J**	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	**59**	1.0	0.18
107-06-2	1,2-Dichloroethane	**0.46J**	1.0	0.21
75-35-4	1,1-Dichloroethene	**14**	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	**78**	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	**1.8**	1.0	0.20
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

Continued on next page

*See Statement of Data Qualifications

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5860 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW113B**	Sampled:	11/24/12 14:17
Lab Sample ID:	**1211459-12**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214846	Analytical Batch:	2K30034

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	**3.7**	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	**18**	1.0	0.14
79-00-5	1,1,2-Trichloroethane	**0.34J**	1.0	0.20
79-01-6	Trichloroethene	**26**	1.0	0.21
75-01-4	Vinyl Chloride	**7.5**	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*100*	*85-118*
1,2-Dichloroethane-d4	*107*	*87-122*
Toluene-d8	*98*	*85-113*
4-Bromofluorobenzene	*103*	*82-110*

VALIDATED

Reviewed By _____

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.
5550 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7453 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW114A**	Sampled:	11/24/12 13:24
Lab Sample ID:	**1211459-10**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/201: By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214846	Analytical Batch:	2K30034

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.1
71-43-2	Benzene	1.0U	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	1.0U	1.0	0.14
67-66-3	Chloroform	1.0U	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	**2.9**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.21
75-35-4	1,1-Dichloroethene	**1.6**	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	**2.4**	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	**0.22J**	1.0	0.20
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

Continued on next page

*See Statement of Data Qualifications

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW114A**	Sampled:	11/24/12 13:24
Lab Sample ID:	**1211459-10**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214846	Analytical Batch:	2K30034

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	1.0U	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	**27**	1.0	0.14
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.20
79-01-6	Trichloroethene	**1.8**	1.0	0.21
75-01-4	Vinyl Chloride	1.0U	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*101*	*85-118*
1,2-Dichloroethane-d4	*108*	*87-122*
Toluene-d8	*99*	*85-113*
4-Bromofluorobenzene	*103*	*82-110*

VALIDATED

Reviewed By _____

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5550 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW114B**	Sampled:	11/24/12 12:58
Lab Sample ID:	**1211459-08**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214846	Analytical Batch:	2K30034

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.1
71-43-2	Benzene	1.0U	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	1.0U	1.0	0.14
67-66-3	Chloroform	1.0U	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	**1.3**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.21
75-35-4	1,1-Dichloroethene	**0.44J**	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	**1.9**	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.20
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

VALIDATED

Continued on next page

*See Statement of Data Qualifications

Reviewed By _____

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW114B**	Sampled:	11/24/12 12:58
Lab Sample ID:	**1211459-08**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214846	Analytical Batch:	2K30034

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	1.0U	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	1.0U	1.0	0.14
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.20
79-01-6	Trichloroethene	**6.1**	1.0	0.21
75-01-4	Vinyl Chloride	1.0U	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*98*	*85-118*
1,2-Dichloroethane-d4	*107*	*87-122*
Toluene-d8	*99*	*85-113*
4-Bromofluorobenzene	*103*	*82-110*

VALIDATED

Reviewed By _____

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**FD1** MW-114B Field dupe	Sampled:	11/24/12 13:00
Lab Sample ID:	**1211459-09**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214846	Analytical Batch:	2K30034

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.1
71-43-2	Benzene	1.0U	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	1.0U	1.0	0.14
67-66-3	Chloroform	1.0U	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	**1.3**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.21
75-35-4	1,1-Dichloroethene	**0.38J**	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	**1.8**	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.20
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

Continued on next page

*See Statement of Data Qualifications

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**FD1**	Sampled:	11/24/12 13:00
Lab Sample ID:	**1211459-09**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214846	Analytical Batch:	2K30034

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	1.0U	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	1.0U	1.0	0.14
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.20
79-01-6	Trichloroethene	**5.8**	1.0	0.21
75-01-4	Vinyl Chloride	1.0U	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*98*	*85-118*
1,2-Dichloroethane-d4	*107*	*87-122*
Toluene-d8	*99*	*85-113*
4-Bromofluorobenzene	*102*	*82-110*

VALIDATED

Reviewed By _____

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW117B**	Sampled:	11/25/12 13:22
Lab Sample ID:	**1211459-24**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/30/12 By: BAG
QC Batch:	1214857	Analytical Batch:	2K30046

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
*67-64-1	Acetone	20U	20	1.1
71-43-2	Benzene	1.0U	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	1.0U	1.0	0.14
67-66-3	Chloroform	**0.35J**	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	**10**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.21
75-35-4	1,1-Dichloroethene	**3.0**	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	**1.1**	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.20
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

VALIDATED

Continued on next page

*See Statement of Data Qualifications

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW117B**	Sampled:	11/25/12 13:22
Lab Sample ID:	**1211459-24**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/30/12 By: BAG
QC Batch:	1214857	Analytical Batch:	2K30046

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	**5.7**	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	**10**	1.0	0.14
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.20
79-01-6	Trichloroethene	**6.0**	1.0	0.21
75-01-4	Vinyl Chloride	1.0U	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*101*	*85-118*
1,2-Dichloroethane-d4	*110*	*87-122*
Toluene-d8	*102*	*85-113*
4-Bromofluorobenzene	*105*	*82-110*

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW117C**	Sampled:	11/25/12 13:47
Lab Sample ID:	**1211459-25**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/30/12 By: BAG
QC Batch:	1214857	Analytical Batch:	2K30046

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
*67-64-1	Acetone	20U	20	1.1
71-43-2	Benzene	1.0U	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	1.0U	1.0	0.14
67-66-3	Chloroform	**0.35J**	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	**29**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.21
75-35-4	1,1-Dichloroethene	**17**	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	**7.4**	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.20
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

VALIDATED

Continued on next page

*See Statement of Data Qualifications

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW117C**	Sampled:	11/25/12 13:47
Lab Sample ID:	**1211459-25**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/30/12 By: BAG
QC Batch:	1214857	Analytical Batch:	2K30046

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	**22**	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	**36**	1.0	0.14
79-00-5	1,1,2-Trichloroethane	**0.42J**	1.0	0.20
79-01-6	Trichloroethene	**14**	1.0	0.21
75-01-4	Vinyl Chloride	1.0U	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*101*	*85-118*
1,2-Dichloroethane-d4	*109*	*87-122*
Toluene-d8	*101*	*85-113*
4-Bromofluorobenzene	*105*	*82-110*

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW117D**	Sampled:	11/25/12 14:18
Lab Sample ID:	**1211459-26**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/30/12 By: BAG
QC Batch:	1214857	Analytical Batch:	2K30046

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
*67-64-1	Acetone	20U	20	1.1
71-43-2	Benzene	1.0U	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	1.0U	1.0	0.14
67-66-3	Chloroform	**0.32J**	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	**48**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.21
75-35-4	1,1-Dichloroethene	**12**	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	**3.0**	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.20
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

VALIDATED

Continued on next page

*See Statement of Data Qualifications

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5580 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW117D**	Sampled:	11/25/12 14:18
Lab Sample ID:	**1211459-26**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/30/12 By: BAG
QC Batch:	1214857	Analytical Batch:	2K30046

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	**19**	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	**34**	1.0	0.14
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.20
79-01-6	Trichloroethene	**11**	1.0	0.21
75-01-4	Vinyl Chloride	1.0U	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*102*	*85-118*
1,2-Dichloroethane-d4	*111*	*87-122*
Toluene-d8	*101*	*85-113*
4-Bromofluorobenzene	*105*	*82-110*

VALIDATED

Reviewed By: [signature]

Date: 1-10-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW119**	Sampled:	11/25/12 10:53
Lab Sample ID:	**1211459-21**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/30/12 By: BAG
QC Batch:	1214857	Analytical Batch:	2K30046

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
*67-64-1	Acetone	20U	20	1.1
71-43-2	Benzene	1.0U	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	1.0U	1.0	0.14
67-66-3	Chloroform	**0.13J**	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	**0.99J**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.21
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	**0.80J**	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.20
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

VALIDATED

Continued on next page

*See Statement of Data Qualifications

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW119**	Sampled:	11/25/12 10:53
Lab Sample ID:	**1211459-21**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/30/12 By: BAG
QC Batch:	1214857	Analytical Batch:	2K30046

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	1.0U	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	**1.2**	1.0	0.14
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.20
79-01-6	Trichloroethene	**0.32J**	1.0	0.21
75-01-4	Vinyl Chloride	1.0U	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*99*	*85-118*
1,2-Dichloroethane-d4	*109*	*87-122*
Toluene-d8	*101*	*85-113*
4-Bromofluorobenzene	*105*	*82-110*

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7483 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW121**	Sampled:	11/25/12 09:49
Lab Sample ID:	**1211459-19**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/201: By: BAG
Dilution Factor:	1	Analyzed:	11/30/12 By: BAG
QC Batch:	1214857	Analytical Batch:	2K30046

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
*67-64-1	Acetone	20U	20	1.1
71-43-2	Benzene	1.0U	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	1.0U	1.0	0.14
67-66-3	Chloroform	**0.76J**	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	**23**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.21
75-35-4	1,1-Dichloroethene	**3.0**	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	**5.3**	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	**0.74J**	1.0	0.20
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

Continued on next page

*See Statement of Data Qualifications

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

3560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW121**	Sampled:	11/25/12 09:49
Lab Sample ID:	**1211459-19**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/30/12 By: BAG
QC Batch:	1214857	Analytical Batch:	2K30046

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	**1.5**	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	**12**	1.0	0.14
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.20
79-01-6	Trichloroethene	**18**	1.0	0.21
75-01-4	Vinyl Chloride	1.0U	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*102*	*85-118*
1,2-Dichloroethane-d4	*110*	*87-122*
Toluene-d8	*101*	*85-113*
4-Bromofluorobenzene	*104*	*82-110*

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5590 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.1500 ♦ Fax 616.942.7483 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW124**	Sampled:	11/25/12 11:31
Lab Sample ID:	**1211459-22**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	12/4/2012 By: BAG
Dilution Factor:	2	Analyzed:	12/04/12 By: BAG
QC Batch:	1214987	Analytical Batch:	2L05005

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	40U	40	2.2
71-43-2	Benzene	2.0U	2.0	0.23
74-97-5	Bromochloromethane	2.0U	2.0	0.59
75-27-4	Bromodichloromethane	2.0U	2.0	0.26
75-25-2	Bromoform	2.0U	2.0	0.51
74-83-9	Bromomethane	2.0U	2.0	0.43
75-15-0	Carbon Disulfide	10U	10	0.46
56-23-5	Carbon Tetrachloride	2.0U	2.0	0.53
108-90-7	Chlorobenzene	2.0U	2.0	0.33
75-00-3	Chloroethane	**5.9**	2.0	0.29
67-66-3	Chloroform	2.0U	2.0	0.20
74-87-3	Chloromethane	2.0U	2.0	0.58
*96-12-8	1,2-Dibromo-3-chloropropane	2.0U	2.0	0.26
124-48-1	Dibromochloromethane	2.0U	2.0	0.30
106-93-4	1,2-Dibromoethane	2.0U	2.0	0.30
95-50-1	1,2-Dichlorobenzene	2.0U	2.0	0.47
541-73-1	1,3-Dichlorobenzene	2.0U	2.0	0.48
106-46-7	1,4-Dichlorobenzene	2.0U	2.0	0.50
75-34-3	1,1-Dichloroethane	**330**	2.0	0.37
107-06-2	1,2-Dichloroethane	2.0U	2.0	0.43
75-35-4	1,1-Dichloroethene	**9.6**	2.0	0.42
156-59-2	cis-1,2-Dichloroethene	**70**	2.0	0.24
156-60-5	trans-1,2-Dichloroethene	**0.90J**	2.0	0.40
78-87-5	1,2-Dichloropropane	2.0U	2.0	0.55
10061-01-5	cis-1,3-Dichloropropene	2.0U	2.0	0.38
10061-02-6	trans-1,3-Dichloropropene	2.0U	2.0	0.37
100-41-4	Ethylbenzene	2.0U	2.0	0.41
591-78-6	2-Hexanone	10U	10	0.99
75-09-2	Methylene Chloride	**1.0J**	10	0.49
78-93-3	2-Butanone (MEK)	10U	10	1.3
108-10-1	4-Methyl-2-pentanone (MIBK)	10U	10	0.79

Continued on next page

*See Statement of Data Qualifications

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW124**	Sampled:	11/25/12 11:31
Lab Sample ID:	**1211459-22**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	12/4/2012 By: BAG
Dilution Factor:	2	Analyzed:	12/04/12 By: BAG
QC Batch:	1214987	Analytical Batch:	2L05005

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	2.0U	2.0	0.41
79-34-5	1,1,2,2-Tetrachloroethane	2.0U	2.0	0.51
127-18-4	Tetrachloroethene	**5.2**	2.0	0.45
108-88-3	Toluene	2.0U	2.0	0.37
71-55-6	1,1,1-Trichloroethane	**50**	2.0	0.28
79-00-5	1,1,2-Trichloroethane	2.0U	2.0	0.41
79-01-6	Trichloroethene	**4.3**	2.0	0.42
75-01-4	Vinyl Chloride	**30**	2.0	0.42
1330-20-7	Xylene (Total)	6.0U	6.0	0.79

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*101*	*85-118*
1,2-Dichloroethane-d4	*105*	*87-122*
Toluene-d8	*97*	*85-113*
4-Bromofluorobenzene	*96*	*82-110*

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5550 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW130**	Sampled:	11/24/12 13:49
Lab Sample ID:	**1211459-11**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214846	Analytical Batch:	2K30034

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.1
71-43-2	Benzene	1.0U	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	1.0U	1.0	0.14
67-66-3	Chloroform	1.0U	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	**7.5**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.21
75-35-4	1,1-Dichloroethene	**1.7**	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	**2.5**	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.20
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

Continued on next page

*See Statement of Data Qualifications

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW130**	Sampled:	11/24/12 13:49
Lab Sample ID:	**1211459-11**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214846	Analytical Batch:	2K30034

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	**0.64J**	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	**47**	1.0	0.14
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.20
79-01-6	Trichloroethene	**1.9**	1.0	0.21
75-01-4	Vinyl Chloride	1.0U	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*101*	*85-118*
1,2-Dichloroethane-d4	*107*	*87-122*
Toluene-d8	*100*	*85-113*
4-Bromofluorobenzene	*103*	*82-110*

VALIDATED

Reviewed By _____

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7460 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW133B**	Sampled:	11/24/12 10:56
Lab Sample ID:	**1211459-05**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	12/5/2012 By: BAG
Dilution Factor:	10	Analyzed:	12/05/12 By: DLV
QC Batch:	1215059	Analytical Batch:	2L06032

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
*67-64-1	Acetone	~~120J~~ 120U	200	11
71-43-2	Benzene	10U	10	1.1
74-97-5	Bromochloromethane	10U	10	3.0
75-27-4	Bromodichloromethane	10U	10	1.3
75-25-2	Bromoform	10U	10	2.6
74-83-9	Bromomethane	10U	10	2.1
*75-15-0	Carbon Disulfide	**2.6J**	50	2.3
56-23-5	Carbon Tetrachloride	10U	10	2.6
108-90-7	Chlorobenzene	10U	10	1.7
75-00-3	Chloroethane	10U	10	1.4
67-66-3	Chloroform	**6.0J**	10	0.98
74-87-3	Chloromethane	10U	10	2.9
*96-12-8	1,2-Dibromo-3-chloropropane	10U	10	1.3
124-48-1	Dibromochloromethane	10U	10	1.5
106-93-4	1,2-Dibromoethane	10U	10	1.5
95-50-1	1,2-Dichlorobenzene	10U	10	2.4
541-73-1	1,3-Dichlorobenzene	10U	10	2.4
106-46-7	1,4-Dichlorobenzene	10U	10	2.5
75-34-3	1,1-Dichloroethane	**160**	10	1.8
107-06-2	1,2-Dichloroethane	**3.3J**	10	2.1
75-35-4	1,1-Dichloroethene	**49**	10	2.1
156-59-2	cis-1,2-Dichloroethene	**1300**	10	1.2
156-60-5	trans-1,2-Dichloroethene	**49**	10	2.0
78-87-5	1,2-Dichloropropane	10U	10	2.8
10061-01-5	cis-1,3-Dichloropropene	10U	10	1.9
10061-02-6	trans-1,3-Dichloropropene	10U	10	1.9
100-41-4	Ethylbenzene	10U	10	2.1
591-78-6	2-Hexanone	50U	50	4.9
75-09-2	Methylene Chloride	50U	50	2.4
78-93-3	2-Butanone (MEK)	50U	50	6.3
108-10-1	4-Methyl-2-pentanone (MIBK)	50U	50	4.0

Continued on next page

*See Statement of Data Qualifications

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7450 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW133B**	Sampled:	11/24/12 10:56
Lab Sample ID:	**1211459-05**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	12/5/2012 By: BAG
Dilution Factor:	10	Analyzed:	12/05/12 By: DLV
QC Batch:	1215059	Analytical Batch:	2L06032

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	10U	10	2.0
79-34-5	1,1,2,2-Tetrachloroethane	10U	10	2.6
127-18-4	Tetrachloroethene	**64**	10	2.3
108-88-3	Toluene	10U	10	1.8
71-55-6	1,1,1-Trichloroethane	**420**	10	1.4
79-00-5	1,1,2-Trichloroethane	**3.0J**	10	2.0
79-01-6	Trichloroethene	**96**	10	2.1
75-01-4	Vinyl Chloride	10U	10	2.1
1330-20-7	Xylene (Total)	30U	30	3.9

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*101*	*85-118*
1,2-Dichloroethane-d4	*99*	*87-122*
Toluene-d8	*99*	*85-113*
4-Bromofluorobenzene	*96*	*82-110*

VALIDATED

Reviewed By _____

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7453 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW133C**	Sampled:	11/24/12 11:28
Lab Sample ID:	**1211459-06**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214846	Analytical Batch:	2K30034

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.1
71-43-2	Benzene	1.0U	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	**0.36J**	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	1.0U	1.0	0.14
67-66-3	Chloroform	**5.3**	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	**49**	1.0	0.18
107-06-2	1,2-Dichloroethane	**1.6**	1.0	0.21
75-35-4	1,1-Dichloroethene	**41**	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	**130**	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	**1.5**	1.0	0.20
78-87-5	1,2-Dichloropropane	**0.29J**	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

Continued on next page

*See Statement of Data Qualifications

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax: 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW133C**	Sampled:	11/24/12 11:28
Lab Sample ID:	**1211459-06**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214846	Analytical Batch:	2K30034

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	**6.6**	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	**140**	1.0	0.14
79-00-5	1,1,2-Trichloroethane	**1.0**	1.0	0.20
79-01-6	Trichloroethene	**75**	1.0	0.21
75-01-4	Vinyl Chloride	1.0U	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*101*	*85-118*
1,2-Dichloroethane-d4	*106*	*87-122*
Toluene-d8	*98*	*85-113*
4-Bromofluorobenzene	*103*	*82-110*

VALIDATED

Reviewed By _____

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5550 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW136**	Sampled:	11/24/12 10:18
Lab Sample ID:	**1211459-04**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214846	Analytical Batch:	2K30034

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.1
71-43-2	Benzene	1.0U	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	1.0U	1.0	0.14
67-66-3	Chloroform	**0.50J**	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	1.0U	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.21
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	1.0U	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.20
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

Continued on next page

*See Statement of Data Qualifications

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW136**	Sampled:	11/24/12 10:18
Lab Sample ID:	**1211459-04**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214846	Analytical Batch:	2K30034

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	1.0U	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	1.0U	1.0	0.14
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.20
79-01-6	Trichloroethene	1.0U	1.0	0.21
75-01-4	Vinyl Chloride	1.0U	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*100*	*85-118*
1,2-Dichloroethane-d4	*107*	*87-122*
Toluene-d8	*99*	*85-113*
4-Bromofluorobenzene	*103*	*82-110*

VALIDATED

Reviewed By _____

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW200**	Sampled:	11/24/12 15:16
Lab Sample ID:	**1211459-14**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/201: By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214857	Analytical Batch:	2K30046

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
*67-64-1	Acetone	20U	20	1.1
71-43-2	Benzene	1.0U	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	1.0U	1.0	0.14
67-66-3	Chloroform	1.0U	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	1.0U	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.21
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	1.0U	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.20
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

VALIDATED

Continued on next page

*See Statement of Data Qualifications

Reviewed By _____

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW200**	Sampled:	11/24/12 15:16
Lab Sample ID:	**1211459-14**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214857	Analytical Batch:	2K30046

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	1.0U	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	1.0U	1.0	0.14
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.20
79-01-6	Trichloroethene	1.0U	1.0	0.21
75-01-4	Vinyl Chloride	1.0U	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*100*	*85-118*
1,2-Dichloroethane-d4	*110*	*87-122*
Toluene-d8	*101*	*85-113*
4-Bromofluorobenzene	*104*	*82-110*

VALIDATED

Reviewed By _____

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5550 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW201**	Sampled:	11/25/12 12:43
Lab Sample ID:	**1211459-23**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/30/12 By: BAG
QC Batch:	1214857	Analytical Batch:	2K30046

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
*67-64-1	Acetone	20U	20	1.1
71-43-2	Benzene	1.0U	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	1.0U	1.0	0.14
67-66-3	Chloroform	1.0U	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	**5.0**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.21
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	**1.0**	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.20
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

Continued on next page

*See Statement of Data Qualifications

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5550 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW201**	Sampled:	11/25/12 12:43
Lab Sample ID:	**1211459-23**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/201: By: BAG
Dilution Factor:	1	Analyzed:	11/30/12 By: BAG
QC Batch:	1214857	Analytical Batch:	2K30046

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	**0.85J**	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	**15**	1.0	0.14
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.20
79-01-6	Trichloroethene	**0.31J**	1.0	0.21
75-01-4	Vinyl Chloride	1.0U	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*102*	*85-118*
1,2-Dichloroethane-d4	*110*	*87-122*
Toluene-d8	*101*	*85-113*
4-Bromofluorobenzene	*105*	*82-110*

VALIDATED

Reviewed By _____

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7453 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW204**	Sampled:	11/25/12 09:16
Lab Sample ID:	**1211459-18**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/30/12 By: BAG
QC Batch:	1214857	Analytical Batch:	2K30046

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
*67-64-1	Acetone	20U	20	1.1
71-43-2	Benzene	1.0U	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	1.0U	1.0	0.14
67-66-3	Chloroform	**0.45J**	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	**6.0**	1.0	0.18
107-06-2	1,2-Dichloroethane	**1.2**	1.0	0.21
75-35-4	1,1-Dichloroethene	**12**	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	**33**	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	**0.64J**	1.0	0.20
78-87-5	1,2-Dichloropropane	**0.48J**	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

Continued on next page

*See Statement of Data Qualifications

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW204**	Sampled:	11/25/12 09:16
Lab Sample ID:	**1211459-18**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/30/12 By: BAG
QC Batch:	1214857	Analytical Batch:	2K30046

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	**1.8**	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	**7.3**	1.0	0.14
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.20
79-01-6	Trichloroethene	**51**	1.0	0.21
75-01-4	Vinyl Chloride	1.0U	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*103*	*85-118*
1,2-Dichloroethane-d4	*110*	*87-122*
Toluene-d8	*100*	*85-113*
4-Bromofluorobenzene	*104*	*82-110*

VALIDATED

Reviewed By _____

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW206A**	Sampled:	11/23/12 15:55
Lab Sample ID:	**1211459-03**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214846	Analytical Batch:	2K30034

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.1
71-43-2	Benzene	1.0U	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	1.0U	1.0	0.14
67-66-3	Chloroform	**0.42J**	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	**12**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.21
75-35-4	1,1-Dichloroethene	**3.8**	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	**2.0**	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.20
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

Continued on next page

*See Statement of Data Qualifications

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5550 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW206A _**	Sampled:	11/23/12 15:55
Lab Sample ID:	**1211459-03**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214846	Analytical Batch:	2K30034

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	**5.5**	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	**12**	1.0	0.14
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.20
79-01-6	Trichloroethene	**6.2**	1.0	0.21
75-01-4	Vinyl Chloride	1.0U	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*100*	*85-118*
1,2-Dichloroethane-d4	*106*	*87-122*
Toluene-d8	*99*	*85-113*
4-Bromofluorobenzene	*103*	*82-110*

VALIDATED

Reviewed By _____

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client-Sample ID:	**MW206B**	Sampled:	11/23/12 15:20
Lab Sample ID:	**1211459-02**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214846	Analytical Batch:	2K30034

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.1
71-43-2	Benzene	**0.18J**	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	1.0U	1.0	0.14
67-66-3	Chloroform	**0.86J**	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	**55**	1.0	0.18
107-06-2	1,2-Dichloroethane	**2.1**	1.0	0.21
75-35-4	1,1-Dichloroethene	**74**	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	**130**	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	**0.40J**	1.0	0.20
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

Continued on next page

*See Statement of Data Qualifications

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW206B**	Sampled:	11/23/12 15:20
Lab Sample ID:	**1211459-02**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214846	Analytical Batch:	2K30034

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	**14**	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	**55**	1.0	0.14
79-00-5	1,1,2-Trichloroethane	**4.8**	1.0	0.20
79-01-6	Trichloroethene	**41**	1.0	0.21
75-01-4	Vinyl Chloride	**0.80J**	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*101*	*85-118*
1,2-Dichloroethane-d4	*105*	*87-122*
Toluene-d8	*98*	*85-113*
4-Bromofluorobenzene	*103*	*82-110*

VALIDATED

Reviewed By _____

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW206C**	Sampled:	11/23/12 14:52
Lab Sample ID:	**1211459-01**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214846	Analytical Batch:	2K30034

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.1
71-43-2	Benzene	1.0U	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	1.0U	1.0	0.14
67-66-3	Chloroform	1.0U	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	**7.1**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.21
75-35-4	1,1-Dichloroethene	**5.1**	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	**7.1**	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.20
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

VALIDATED

Continued on next page

*See Statement of Data Qualifications

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW206C**	Sampled:	11/23/12 14:52
Lab Sample ID:	**1211459-01**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214846	Analytical Batch:	2K30034

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	**0.24J**	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	1.0U	1.0	0.14
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.20
79-01-6	Trichloroethene	**19**	1.0	0.21
75-01-4	Vinyl Chloride	1.0U	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*99*	*85-118*
1,2-Dichloroethane-d4	*106*	*87-122*
Toluene-d8	*99*	*85-113*
4-Bromofluorobenzene	*102*	*82-110*

VALIDATED

Reviewed By _____

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5550 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**Trip Blank TM1982**	Sampled:	11/25/12 00:00
Lab Sample ID:	**1211459-27**	Sampled By:	TML
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214857	Analytical Batch:	2K30046

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
*67-64-1	Acetone	20U	20	1.1
71-43-2	Benzene	1.0U	1.0	0.11
74-97-5	Bromochloromethane	1.0U	1.0	0.30
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.26
74-83-9	Bromomethane	1.0U	1.0	0.21
*75-15-0	Carbon Disulfide	5.0U	5.0	0.23
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.26
108-90-7	Chlorobenzene	1.0U	1.0	0.17
75-00-3	Chloroethane	1.0U	1.0	0.14
67-66-3	Chloroform	1.0U	1.0	0.098
74-87-3	Chloromethane	1.0U	1.0	0.29
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.13
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.15
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.24
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.24
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.25
75-34-3	1,1-Dichloroethane	1.0U	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.21
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.21
156-59-2	cis-1,2-Dichloroethene	1.0U	1.0	0.12
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.20
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.28
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.19
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.21
591-78-6	2-Hexanone	5.0U	5.0	0.49
75-09-2	Methylene Chloride	5.0U	5.0	0.24
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.63
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.40

Continued on next page

*See Statement of Data Qualifications

VALIDATED

Reviewed By

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5550 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1211459**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**Trip Blank TM1982**	Sampled:	11/25/12 00:00
Lab Sample ID:	**1211459-27**	Sampled By:	TML
Matrix:	Water	Received:	11/27/12 08:30
Unit:	ug/L	Prepared:	11/29/2012 By: BAG
Dilution Factor:	1	Analyzed:	11/29/12 By: BAG
QC Batch:	1214857	Analytical Batch:	2K30046

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.20
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.26
127-18-4	Tetrachloroethene	1.0U	1.0	0.23
108-88-3	Toluene	1.0U	1.0	0.18
71-55-6	1,1,1-Trichloroethane	1.0U	1.0	0.14
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.20
79-01-6	Trichloroethene	1.0U	1.0	0.21
75-01-4	Vinyl Chloride	1.0U	1.0	0.21
1330-20-7	Xylene (Total)	3.0U	3.0	0.39

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*100*	*85-118*
1,2-Dichloroethane-d4	*110*	*87-122*
Toluene-d8	*101*	*85-113*
4-Bromofluorobenzene	*104*	*82-110*

VALIDATED

Reviewed By _____

Date 1-16-13

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

5560 Corporate Exchange Court SE
Grand Rapids, MI 49512
Phone (616) 975-4500 Fax (616) 942-7463
www.trimatrixlabs.com

Chain of Custody Record

COC No. 142905

Pg. 1 of 3

Analyses Requested

For Lab Use Only

Cart

VOA Rack/Tray: BOX/634B.

Receipt Log No.: 29-10.

Project Chemist:

Work Order No.: 1211459

Client Name: Nationwide Env Svcs

Address: 14818 N 6th Ave Ste SA

City, State Zip: GOLDEN CO 80401

Phone/Fax: 3032322134

Email:

Project Name: SERock

Client Project No. / P.O. No.:

Invoice To: ☐ Client ☐ Other (comments)

Contact/Report To: BLAFLAMME

D

VOC per Contact

Container Type (corresponds to Container Packing List): 1

PRESERVATIVES
A NONE pH>7
B HNO3 pH<2
C H2SO4 pH<2
D 1+1 HCl pH<2
E NaOH pH>12
F ZnAc/NaOH pH>9
G MeOH
H Other (note below)

Schedule	Matrix Code	Sample Number	Field Sample ID	Cooler ID	Sample Date	Sample Time	Matrix	Number of Containers Submitted	Total	Sample Comments
		01	MW206C	1982	11/23	1452	x GW 3		3	
		02	MW206B		11/23	1520	x GW 3		3	
		03	MW206A		11/23	1555	x GW 3		3	
		04	MW136		11/24	1018	x GW 3		3	
		05	MW133B		11/24	1056	x GW 3		3	
		06	MW133C		11/24	1128	x GW 3		3	
		07	MW16		11/24	1215	x GW 3		3	
		08	MW114B		11/24	1258	x GW 3		3	
		09	FD1		11/24	1300	x GW 3		3	
		10	MW114A		11/24	1324	x GW 3		3	

Sampled By (print): Patrick Egan

Sampler's Signature: [signature]

Company: AEE

How Shipped? Hand ___ Carrier: Fedex

Tracking No.: 7941 5159 1840

Comments: All Samples Kept in Secure Location @ 4°C

1. Relinquished By: [signature] Date: 11/26/12 Time: 1900

2. Relinquished By: Date: Time:

3. Relinquished By: Date: Time:

1. Received By: Date: Time:

2. Received By: Date: Time:

3. Received For Lab By: [signature] Date: 11/27/12 Time: 0830

WHITE COPY - REPORT YELLOW COPY - LABORATORY PINK COPY - FIELD

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

TRIMATRIX LABORATORIES

TRIMATRIX LABORATORIES

5560 Corporate Exchange Court SE
Grand Rapids, MI 49512
Phone (616) 975-4500 Fax (616) 942-7463
www.trimatrixlabs.com

Chain of Custody Record

COC No. 142909

Pg. 2 of 3

Analyses Requested

For Lab Use Only	
Cert.	
VOA Rack/Tray	
Receipt Log No.	29-10
Project Chemist	
Work Order No.	1211459

Client Name: NATIONWIDE ENV SVCS
Address: 14818 N 6TH AVE STE 5A
City, State Zip: GOLDEN CO 80401
Phone/Fax:
Email: 3032322134

Project Name: SE ROCK
Client Project No. / P.O. No.
Invoice To: ☐ Client ☐ Other (comments)
Contact/Report To: BLAFLAMME

VOC D PER CONTRACT

Container Type (corresponds to Container Packing List)

PRESERVATIVES
A NONE pH~7
B HNO_3 pH<2
C H_2SO_4 pH<2
D 1+1 HCl pH<2
E NaOH pH>12
F ZnAc/NaOH pH>9
G MeOH
H Other (note below)

Schedule	Matrix Code	Sample Number	Field Sample ID	Cooler ID	Sample Date	Sample Time	Matrix	Number of Containers Submitted	Sample Comments
		11	MW 130	1982	11/24	1349	X GW	2	2
		12	MW 113B		11/24	1417	X GW	3	3
		13	MW 113A		11/24	1449	X GW	3	3
		14	MW 200		11/24	1516	X GW	3	3
		15	MW 101B		11/24	1535	X GW	3	3
		16	MW 101A		11/24	1600	X GW	3	3
		17	MW 101D		11/24	1622	X GW	3	3
		18	MW 204		11/25	916	X GW	3	3
		19	MW 121		11/25	949	X GW	3	3
		20	MW 47		11/25	1021	X GW	3	3

Sampled By (print): PATRICK EGAN
Sampler's Signature: [signature]
Company: AEE

How Shipped? Hand ___ Carrier Fedex
Tracking No. 7941 5159 1840

Comments: All Samples Kept in Secure location @ 4°C

1. Relinquished By: [signature] Date 11/26/12 Time 1900
2. Relinquished By: Date Time
3. Relinquished By: Date Time
1. Received By: Date Time
2. Received By: Date Time
3. Received For Lab By: [signature] Date 11/27/12 Time 0830

WHITE COPY - REPORT YELLOW COPY - LABORATORY PINK COPY - FIELD

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

TRIMATRIX LABORATORIES

5560 Corporate Exchange Court SE
Grand Rapids, MI 49512
Phone (616) 975-4500 Fax (616) 942-7463
www.trimatrixlabs.com

Chain of Custody Record

COC No. 142906

Pg. 3 of 3

Analyses Requested

For Lab Use Only		
Cart		
VOA Rack/Tray	Client Name: NATIONWIDE ENV SVCS	Project Name: SE ROCK
Receipt Log No.: 29-10	Address: 14818 N 6TH AVE STE 5A	Client Project No. / P.O. No.:
Project Chemist:	City, State Zip: GOLDEN CO	Invoice To: ☐ Client ☐ Other (comments)
Work Order No.: 1211459	Phone/Fax: Email: 3032322134	Contact/Report To: BLAFLAMME

VOC D Per Contract

Container Type (corresponds to Container Packing List)

PRESERVATIVES
A NONE pH>7
B HNO_3 pH<2
C H_2SO_4 pH<2
D 1+1 HCl pH<2
E NaOH pH>12
F ZnAc/NaOH pH>9
G MeOH
H Other (note below)

Schedule	Matrix Code	Sample Number	Field Sample ID	Color ID	Sample Date	Sample Time	Comp	Grab	Matrix	Number of Containers Submitted	Test	Sample Comments
		21	MW 119	1982	11/25	1053		x	GW	3	3	
		22	MW 124		11/25	1131		x	GW	3	3	
		23	MW 201		11/25	1243		x	GW	3	3	
		24	MW 117B		11/25	1322		x	GW	3	3	
		25	MW 117C		11/25	1347		x	GW	3	3	
		26	MW 117D		11/25	1418		x	GW	3	3	
		27	TRIP BLANK		—	—				1	1	

Sampled By (print): PATRICK EGAN
Sampler's Signature: [signature]
Company: AEE

How Shipped? Hand Carrier: Fedex
Tracking No.: 7941 5159 1840

Comments: All Samples Kept in Secure location @ 4°C

1. Relinquished By: [signature] Date: 11/26/12 Time: 1900
2. Relinquished By: Date: Time:
3. Relinquished By: Date: Time:

1. Received By: Date: Time:
2. Received By: Date: Time:
3. Received For Lab By: [signature] Date: 11/27/12 Time: 0830

WHITE COPY - REPORT YELLOW COPY - LABORATORY PINK COPY - FIELD

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

APPENDIX B
Ground Water Monitoring
Field Data Sheets

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	60	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW16**
Casing Stickup (Ft.)	2.36	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	24-Nov-12
Total Well Depth (Ft.) TOC	62.36	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	27.17	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	35.19	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2012		

FIELD PURGE MONITORING

Time HHMMSS	pH Units	DO mg/l	Temp øC	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
							0	27.17	Static
11:53	7.65	4.86	11.34	-45	1.198		500		Start Time
11:57	7.66	4.82	11.34	-40	1.198		500	27.22	redish brown
12:01	7.68	4.82	11.34	-38	1.197		500		clear
12:04	7.68	4.82	11.34	-35	1.195		500		clear
12:09	7.68	4.82	11.34	-33	1.195		500		clear
12:12	7.68	4.82	11.34	-32	1.195		500	27.22	clear
12:15	7.68	4.82	11.34	-33	1.195	15	500		sample
MINUTES							**TOTAL LITERS**		
22.0	0.00	0.00%	0.00%	0.00	0.00%		**11.00**		

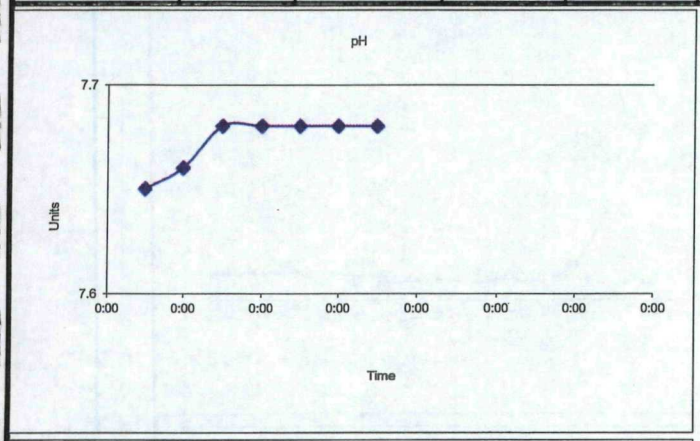

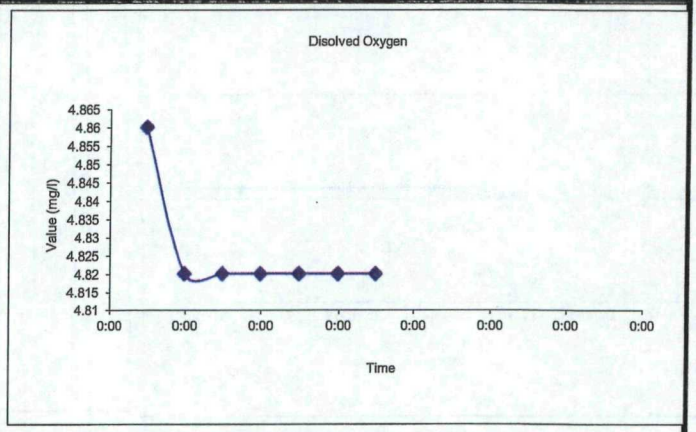

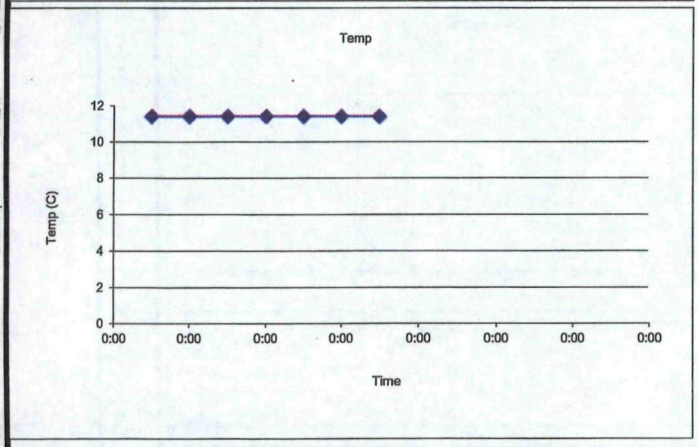

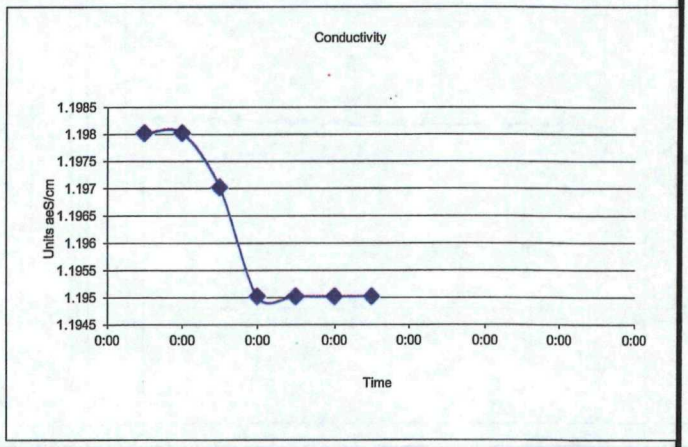

Remarks: (well condition, maintenance, etc...)

Limited access - IEPA Lock

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	52	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 47**
Casing Stickup (Ft.)	-0.63	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	25-Nov-12
Total Well Depth (Ft.) TOC	54.49	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	43.5	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	10.99	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2012		

FIELD PURGE MONITORING

Time HHMMSS	pH Units	DO mg/l	Temp øC	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
							0	43.50	Start Time
10:05	7.61	6.36	10.91	4	1.081		400	43.68	brown
10:08	7.6	6.15	10.92	6	1.089		400		brown
10:11	7.61	6.13	10.92	11	1.088		400	43.68	clear
10:14	7.61	6.13	10.92	15	1.091		400		clear
10:18	7.61	6.14	10.93	13	1.091		400		clear
10:21	7.61	6.14	10.93	15	1.092	36	400	43.68	sample
MINUTES							**TOTAL LITERS**		
16.0	0.00	0.16%	0.00%	0.00	0.00%		**6.40**		

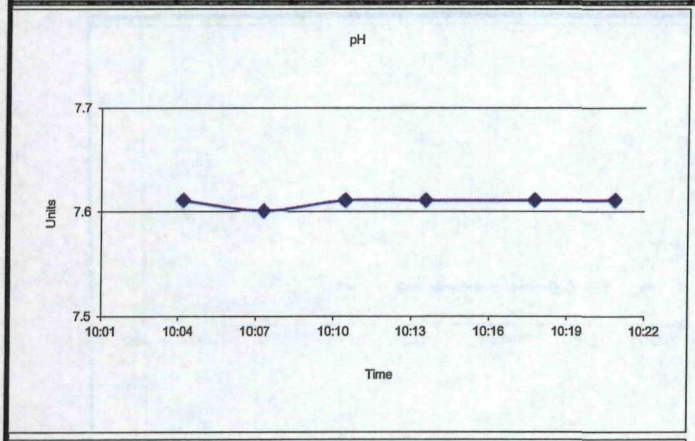

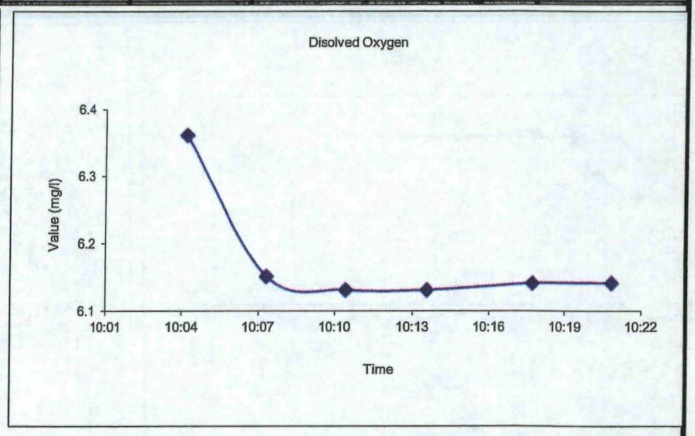

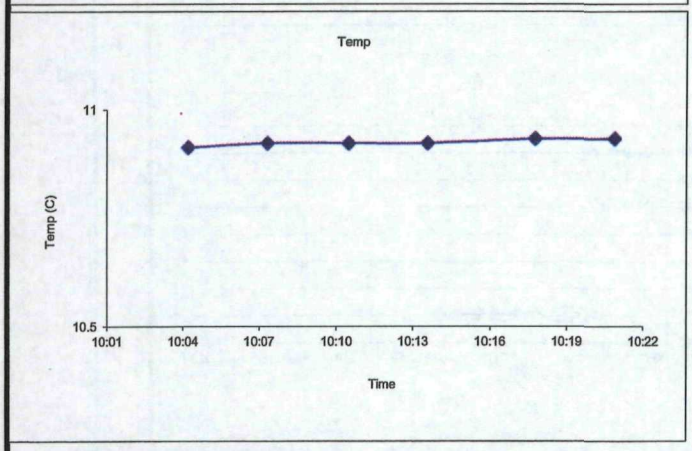

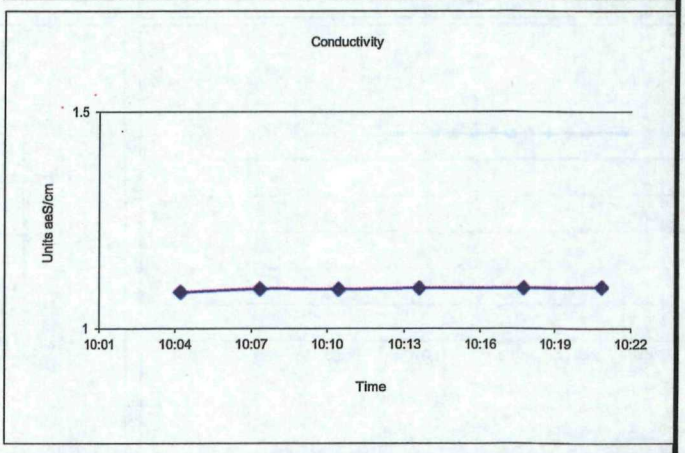

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	88	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 101A**
Casing Stickup (Ft.)	1.45	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	24-Nov-12
Total Well Depth (Ft.) TOC	90.35	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	46.33	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	44.02	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2012		

PURGE MONITORING

Time HHMMSS	pH Units	DO mg/l	Temp øC	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
							0	46.33	Static
15:45	7.51	3.24	10.53	-44	0.948		500		Start Time
15:48	7.52	3.28	10.53	-43	0.943		500	46.39	clear
15:51	7.52	3.29	10.53	-40	0.946		500		clear
15:54	7.52	3.29	10.51	-38	0.946		500		clear
15:57	7.53	3.3	10.52	-38	0.947		500	46.39	clear
16:00	7.53	3.29	10.51	-38	0.947	18	500		sample
MINUTES							**TOTAL LITERS**		
15.0	0.01	0.00%	0.00%	0.00	0.00%		**7.50**		

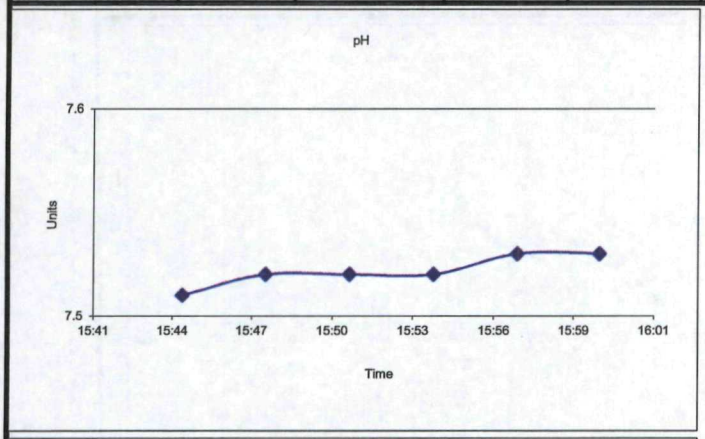

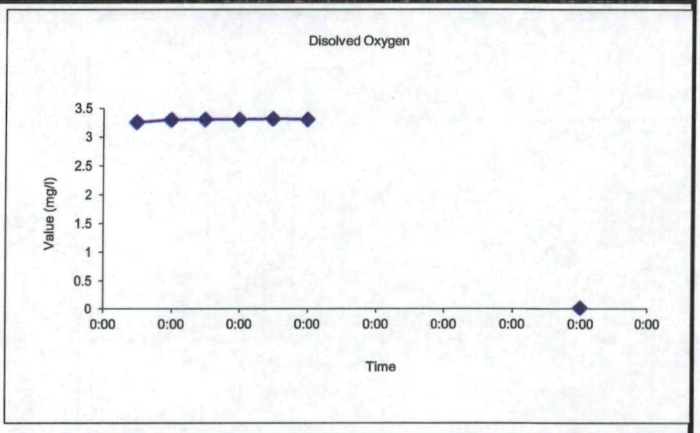

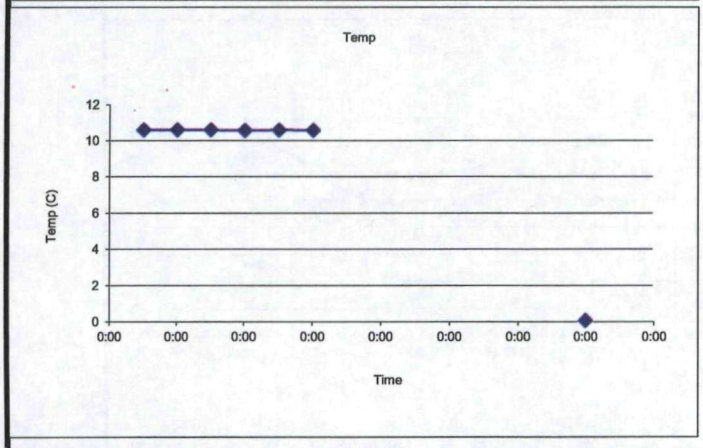

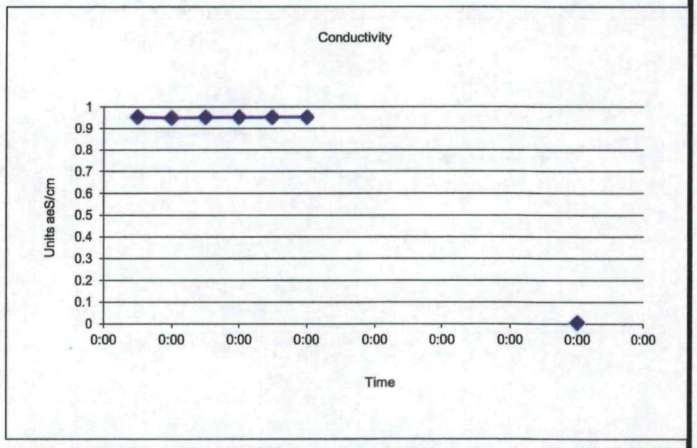

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	151	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 101B**
Casing Stickup (Ft.)	2.16	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	24-Nov-12
Total Well Depth (Ft.) TOC	153.74	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	47.37	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	106.37	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2012		

PURGE MONITORING

Time HHMMSS	pH Units	DO mg/l	Temp øC	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
							0	47.37	Static
15:20	7.33	3.86	10.49	15	0.881		470		Start Time
15:23	7.34	3.88	10.48	18	0.883		500	47.40	clear
15:26	7.33	3.89	10.48	20	0.883		500		clear
15:29	7.34	3.89	10.47	26	0.883		500		clear
15:32	7.34	3.89	10.49	26	0.884		500	47.40	clear
15:35	7.35	3.91	10.49	27	0.884	11	500		sample
MINUTES							**TOTAL LITERS**		
15.0	0.01	0.51%	0.00%	1.00	0.00%		**7.50**		

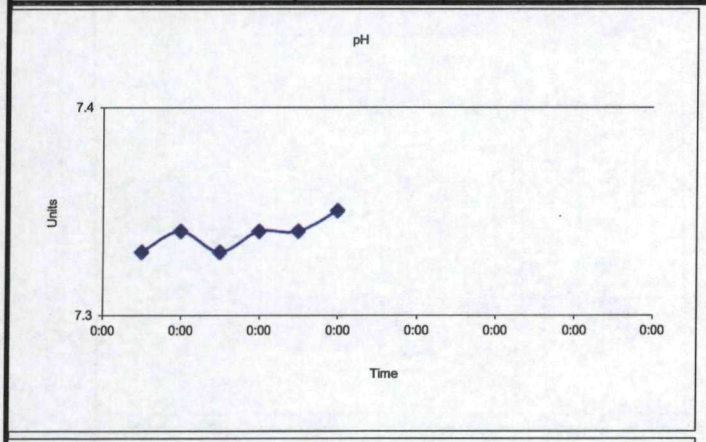

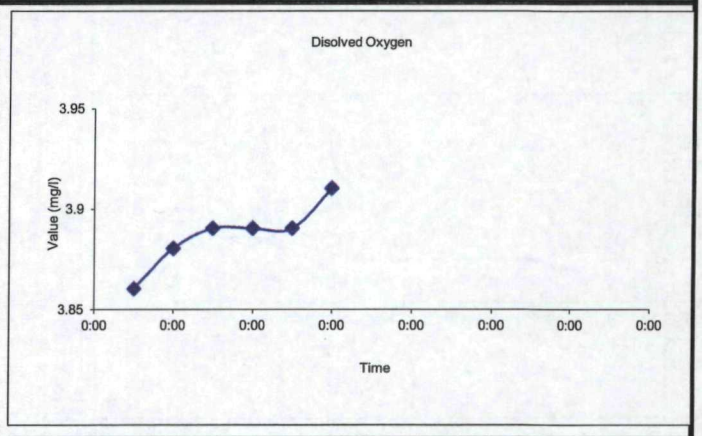

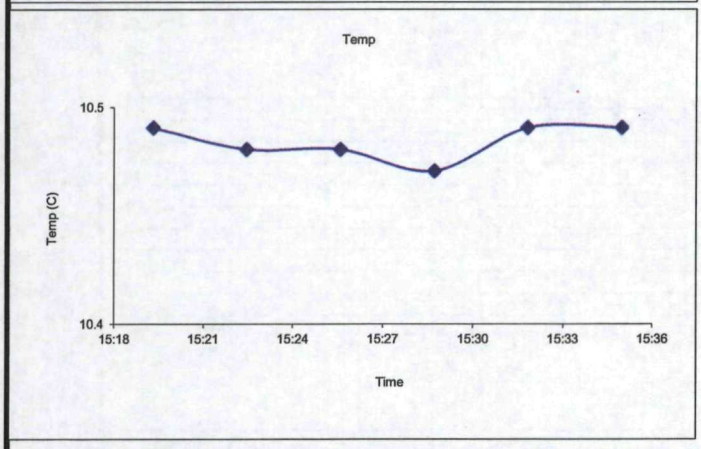

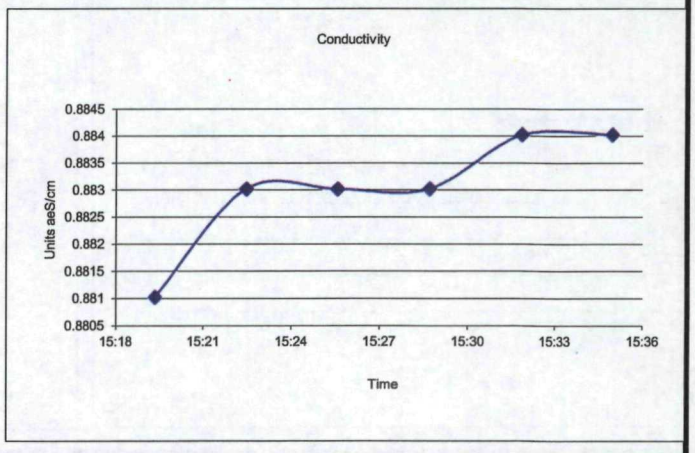

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	172	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 101C**
Casing Stickup (Ft.)	1.12	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	30-Nov-12
Total Well Depth (Ft.) TOC	174.89	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	47.13	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	127.76	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2012		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	mS/cm	FTU	mL/min	(Ft.) TOC	
							0	47.13	Static
8:49	7.39	2.86	10.51	18	0.902		450	47.15	Start Time
8:53	7.4	2.88	10.51	19	0.902		450		clear
8:58	7.41	2.89	10.51	22	0.903		450		clear
9:02	7.41	2.89	10.52	25	0.903		450	47.15	clear
9:05	7.41	2.9	10.52	26	0.903		450		clear
9:08	7.41	2.9	10.52	26	0.903	8	450	47.15	sample
									**Field Dup2 collected
MINUTES							**TOTAL LITERS**		
19.0	0.00	0.34%	0.00%	1.00	0.00%		**8.55**		

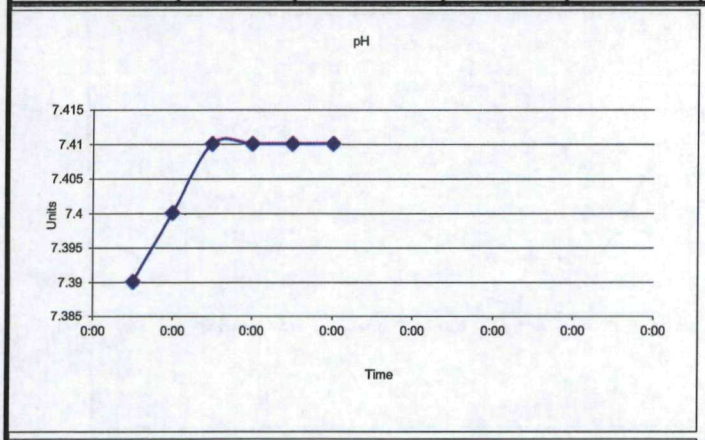

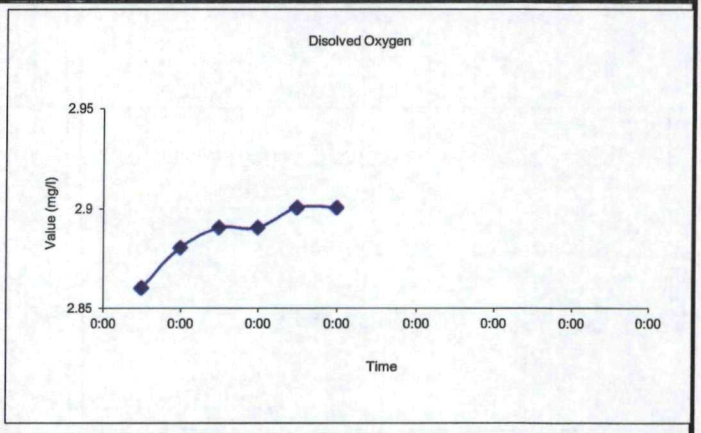

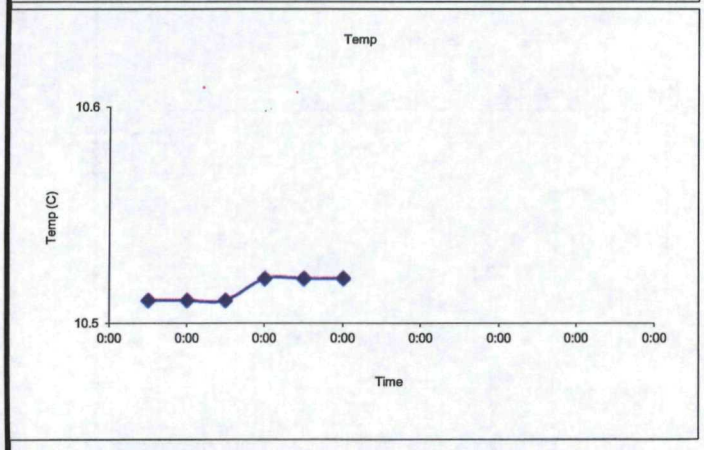

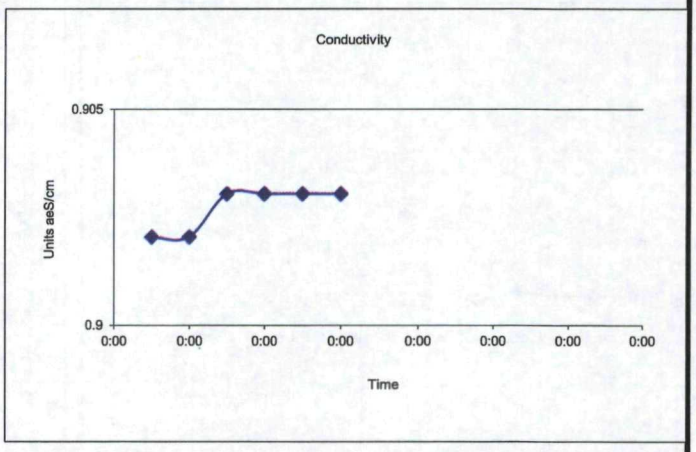

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	172	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 101D**
Casing Stickup (Ft.)	0.89	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	24-Nov-12
Total Well Depth (Ft.) TOC	212.72	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	48.75	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	163.97	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2012		

PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	mS/cm	FTU	mL/min	(Ft.) TOC	
							0	48.75	Static
16:10	7.44	2.01	10.56	-15	1.002		500		Start Time
16:13	7.43	1.95	10.56	-11	1.003		500		cloudy
16:16	7.43	1.94	10.56	-10	1.003		500	48.80	clear
16:19	7.43	1.94	10.57	-10	1.002		500		clear
16:22	7.43	1.94	10.55	-5	1.001	10	500	48.80	sample
MINUTES							**TOTAL LITERS**		
12.0	0.00	0.00%	0.00%	5.00	0.00%		**6.00**		

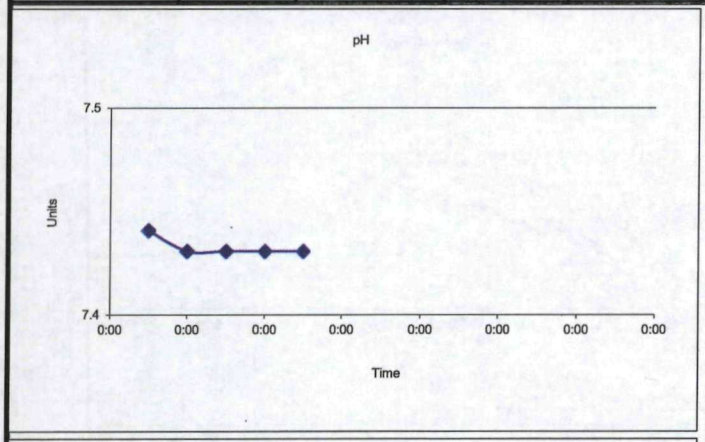

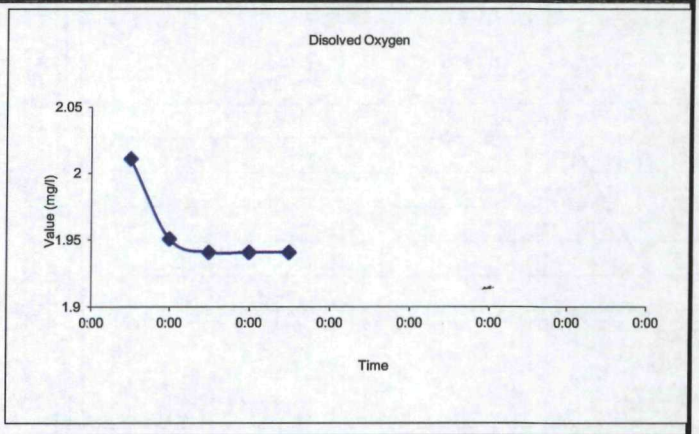

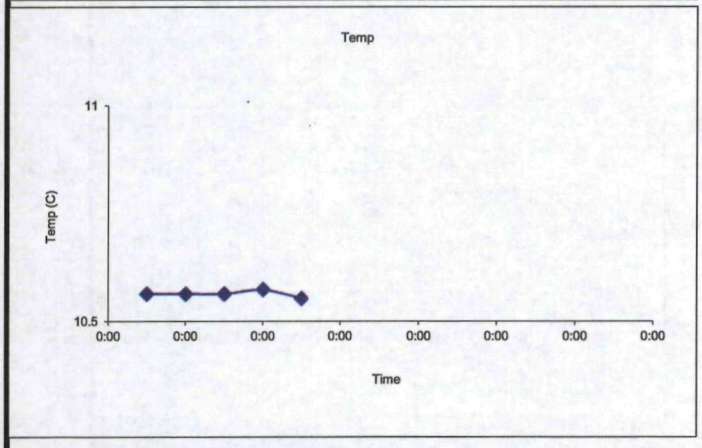

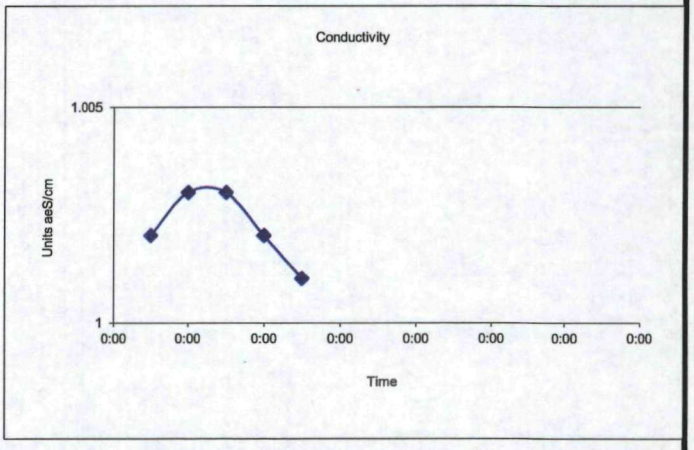

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	35	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 102A**
Casing Stickup (Ft.)	-0.47	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	30-Nov-12
Total Well Depth (Ft.) TOC	37.69	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	19.5	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	18.19	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2012		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	mS/cm	FTU	mL/min	(Ft.) TOC	
							0	19.50	Static
9:43	7.29	2.12	11.76	-46	2.81		500		Start Time
9:47	7.28	2.1	11.76	-42	2.80		500		brown cloudy
9:52	7.29	2.11	11.76	-42	2.79		500	19.58	brown cloudy
9:55	7.3	2.11	11.75	-40	2.79		500		clear
10:00	7.3	2.11	11.76	-38	2.78		500		clear
10:03	7.3	2.11	11.76	-38	2.78	31	500	19.58	sample
MINUTES							**TOTAL LITERS**		
20.0	0.00	0.00%	0.00%	2.00	0.00%		**10.00**		

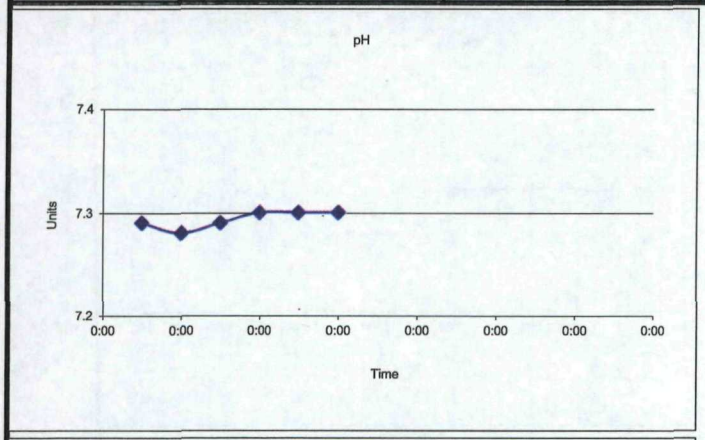

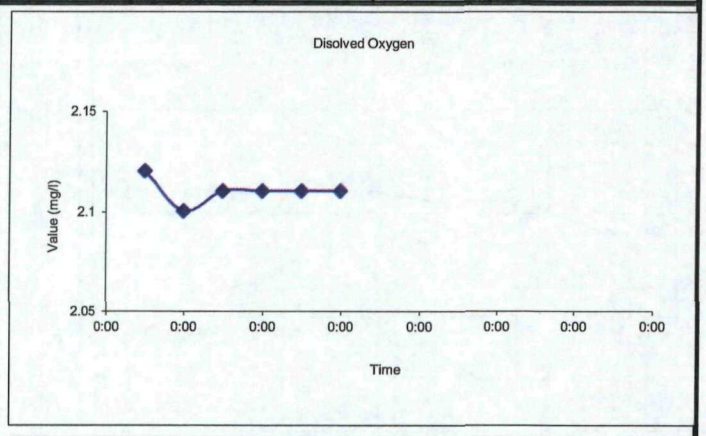

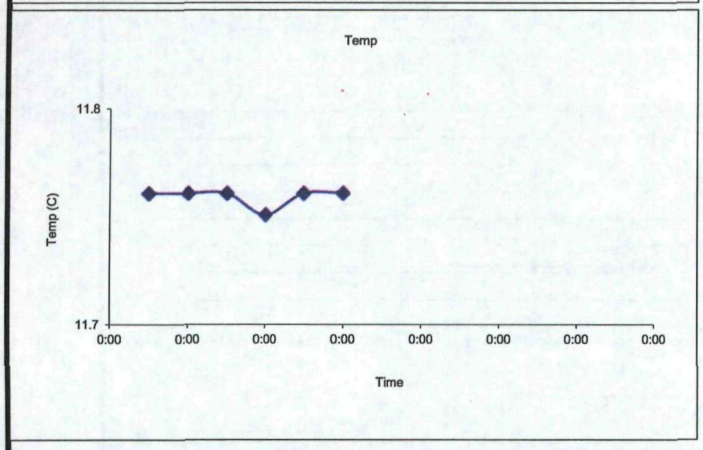

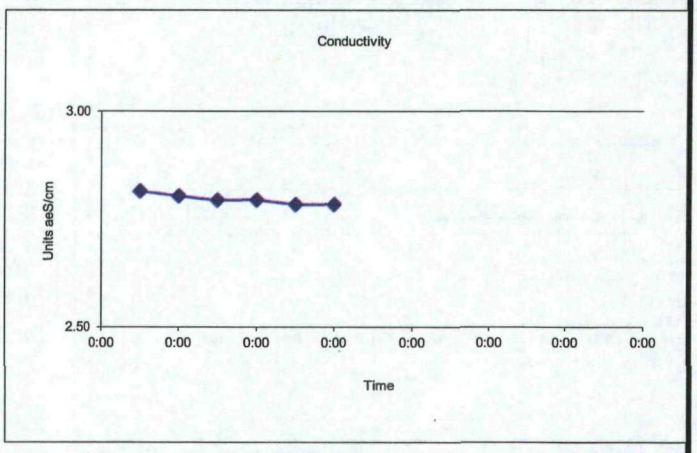

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	98	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 102B**
Casing Stickup (Ft.)	-0.68	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	30-Nov-12
Total Well Depth (Ft.) TOC	100.5	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	37.25	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	63.25	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2012		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	mS/cm	FTU	mL/min	(Ft.) TOC	
							0	37.25	Static
10:25	7.38	2.46	11.86	-42	1.08		460	37.33	Start Time
10:29	7.41	1.86	11.86	-46	1.06		460		redish brown color
10:32	7.41	1.85	11.86	-48	1.10		460	37.33	redish brown color
10:35	7.42	1.85	11.85	-52	1.10		460		cloudy
10:38	7.42	1.83	11.86	-53	1.10		460		clear
10:42	7.42	1.83	11.86	-53	1.09	19	460	37.33	sample
MINUTES						**TOTAL LITERS**			
17.0	0.00	-1.09%	0.00%	-1.00	0.00%		**7.82**		

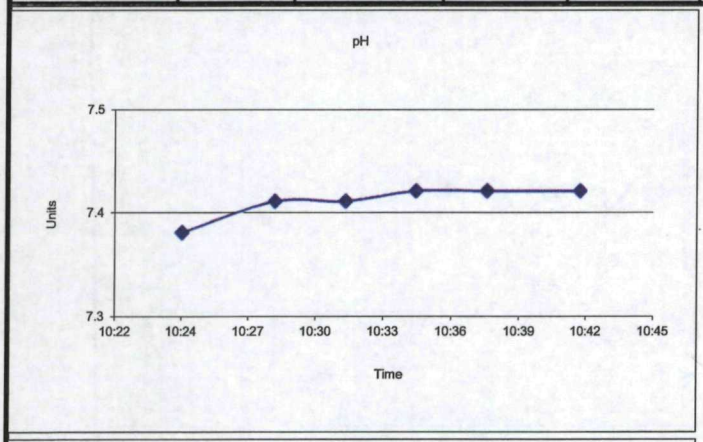

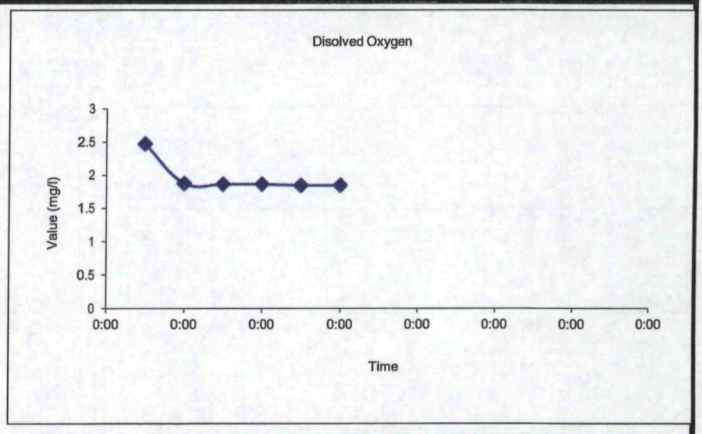

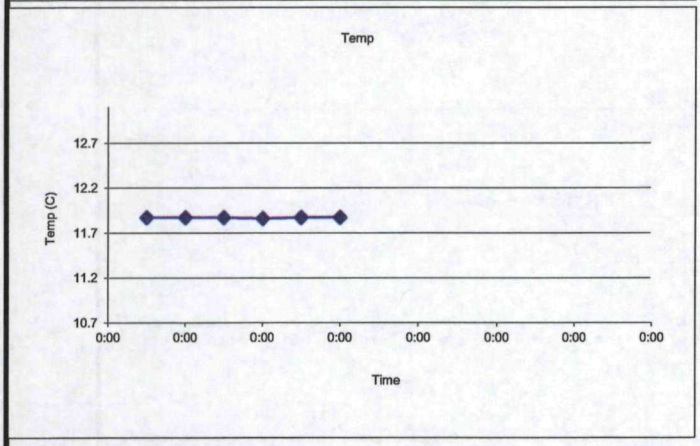

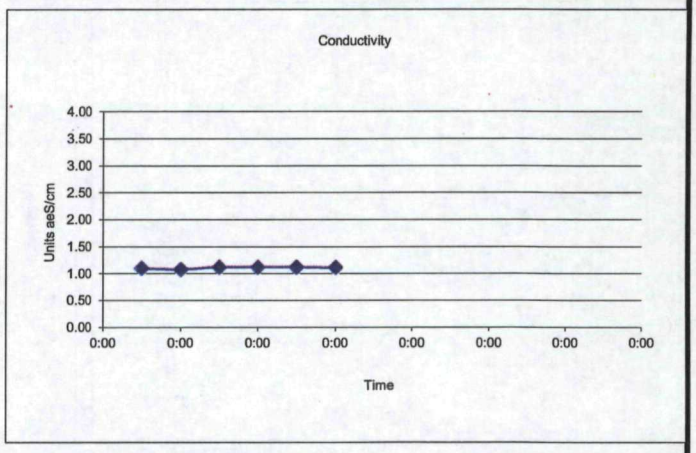

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	185	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 102C**
Casing Stickup (Ft.)	-0.43	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	30-Nov-12
Total Well Depth (Ft.) TOC	187.42	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	40.31	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	147.11	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2012		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	mS/cm	FTU	mL/min	(Ft.) TOC	
							0	40.31	Static
11:03	7.51	1.29	11.87	-81	1.760		425	40.43	Start Time
11:07	7.51	1.29	11.87	-84	0.762		425		clear
11:10	7.5	1.31	11.87	-84	0.781		425		clear
11:14	7.5	1.31	11.85	-86	0.781		425	40.43	clear
11:17	7.5	1.31	11.85	-86	0.780		425		clear
11:22	7.5	1.31	11.85	-88	0.780		425		clear
11:26	7.5	1.32	11.85	-88	0.780	86	425	40.43	sample
MINUTES							**TOTAL LITERS**		
23.0	0.00	0.76%	0.00%	-2.00	0.00%		**9.78**		

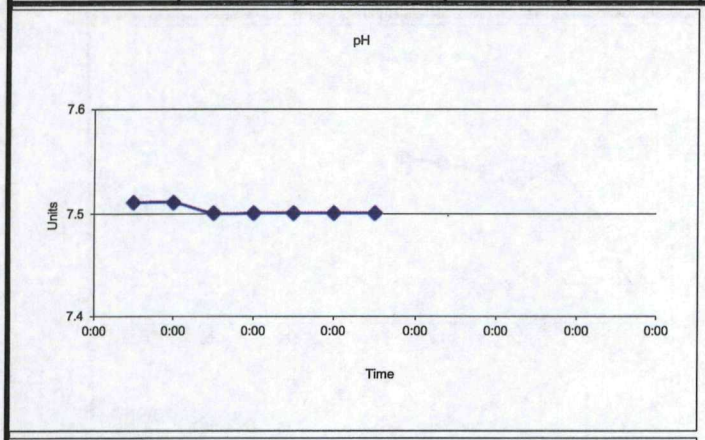

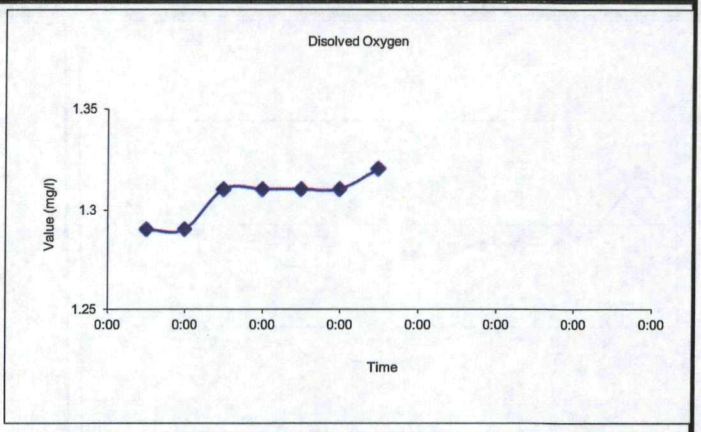

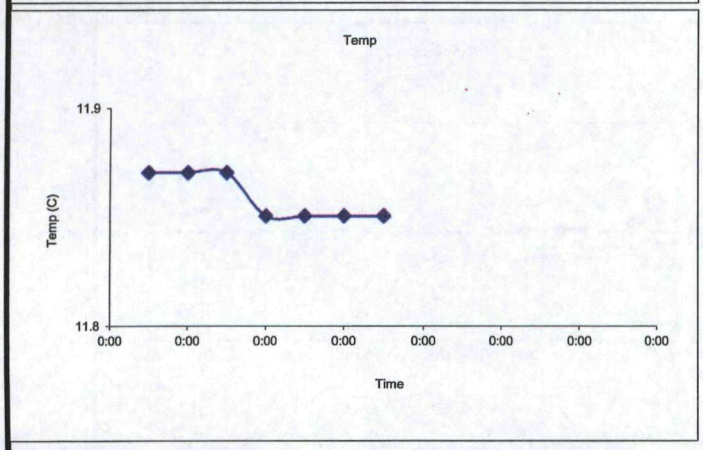

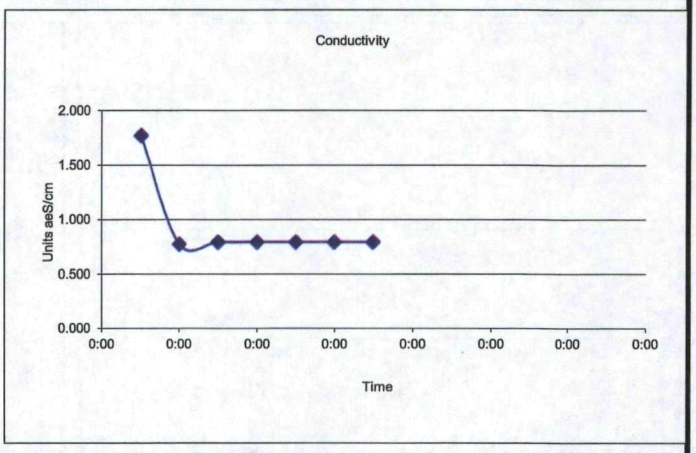

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	102	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 113A**
Casing Stickup (Ft.)	-1.06	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	24-Nov-12
Total Well Depth (Ft.) TOC	104.5	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	58.17	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	46.33	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2012		

FIELD PURGE MONITORING

Time HHMMSS	pH Units	DO mg/l	Temp øC	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
							0	58.17	Static
14:31	7.75	1.5	11.43	10	1.056		500	58.17	Start Time
14:34	7.7	1.61	11.4	13	1.051		500		brown & cloudy
14:37	7.68	1.68	11.4	16	1.051		500		cloudy
14:40	7.68	1.66	11.4	18	1.049		500	58.17	cloudy
14:43	7.68	1.68	11.4	18	1.049		500		cloudy
14:46	7.67	1.69	11.41	20	1.049		500		cloudy
14:49	7.67	1.7	11.4	19	1.049	188	500	58.17	sample
MINUTES							**TOTAL LITERS**		
18.0	-0.01	1.18%	0.00%	1.00	0.00%		**9.00**		

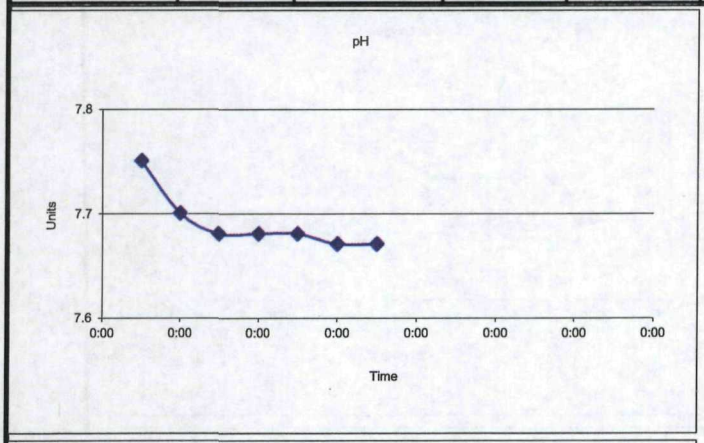

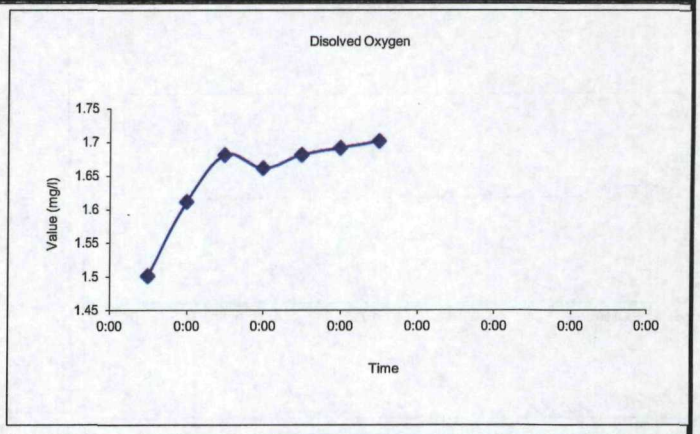

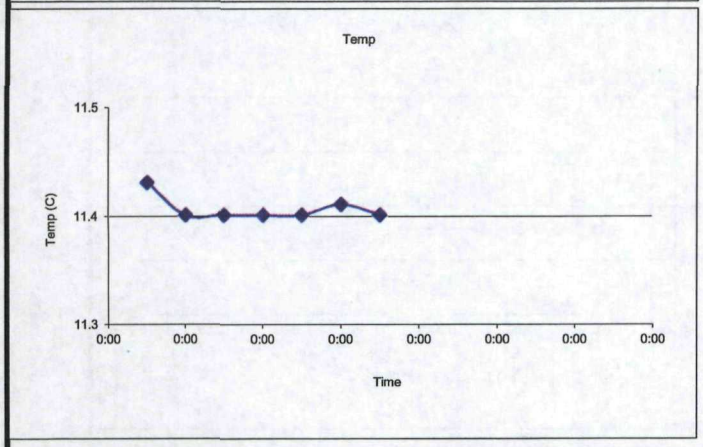

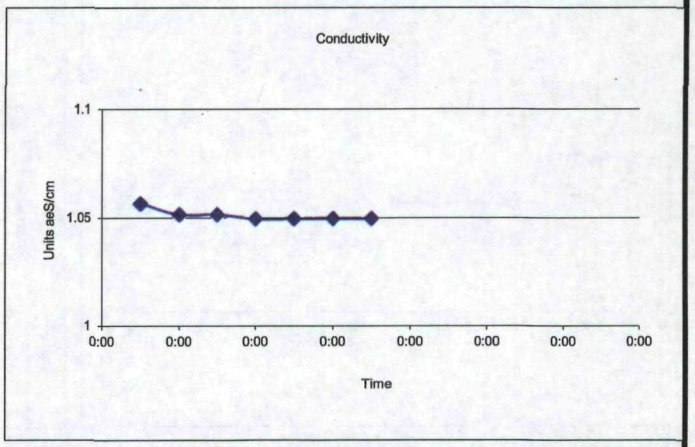

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	153	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 113B**
Casing Stickup (Ft.)	-0.43	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	24-Nov-12
Total Well Depth (Ft.) TOC	155.26	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	58.63	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	96.63	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2012		

FIELD PURGE MONITORING

Time HHMMSS	pH Units	DO mg/l	Temp øC	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
							0	58.63	Static
14:01	7.81	0.98	11.12	-68	0.922		500	58.69	Start Time
14:05	7.7	1.17	11.15	-83	0.924		500		cloudy white
14:08	7.71	1.24	11.15	-85	0.924		500		cloudy
14:11	7.71	1.24	11.15	-85	0.924		500	58.69	clear
14:14	7.71	1.24	11.15	-84	0.925		500		clear
14:17	7.72	1.24	11.17	-86	0.925	105	500	58.69	sample
MINUTES							**TOTAL LITERS**		
16.0	0.01	0.00%	0.00%	-1.00	0.00%		**8.00**		

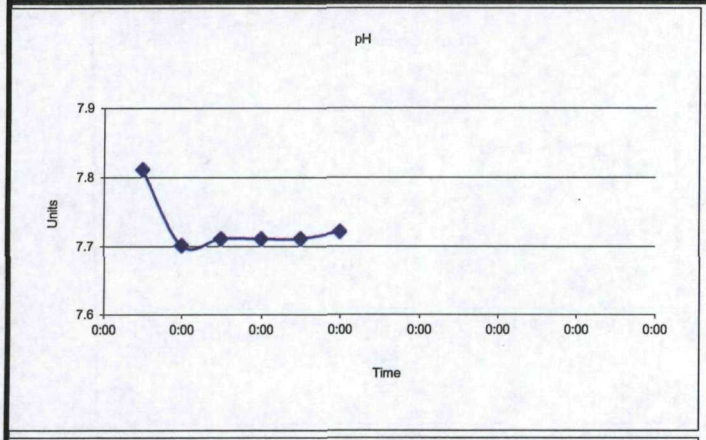

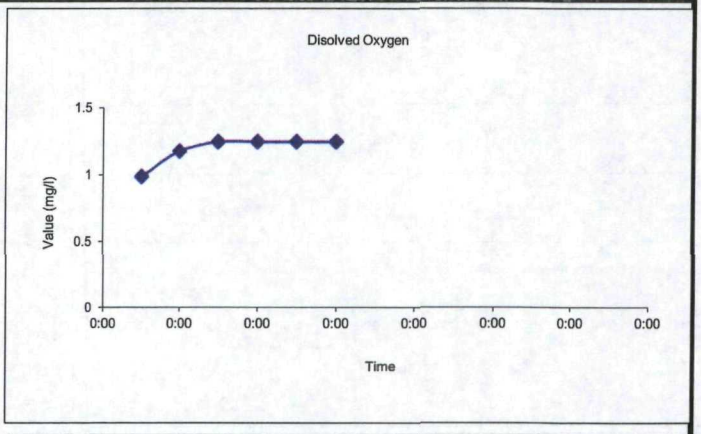

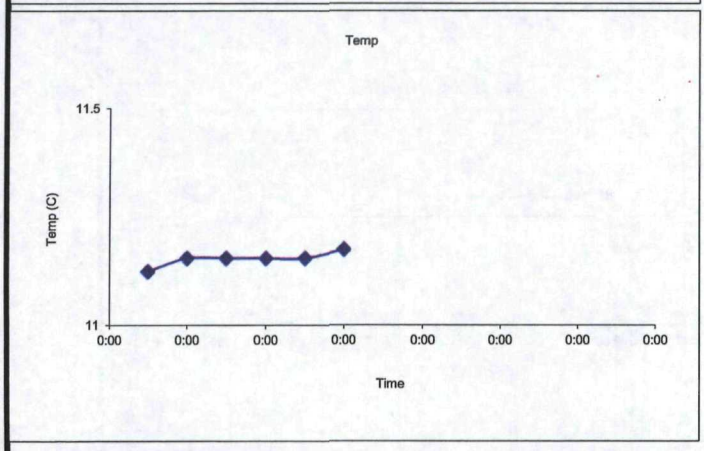

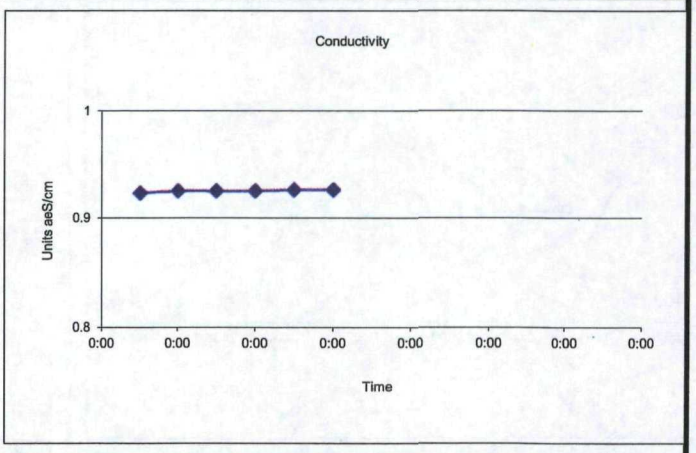

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	95	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 114A**
Casing Stickup (Ft.)	2.45	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	24-Nov-12
Total Well Depth (Ft.) TOC	97.48	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	30.43	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	67.05	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2012		

FIELD PURGE MONITORING

Time HHMMSS	pH Units	DO mg/l	Temp øC	ORP mV	SpCond mS/cm	TURB NTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
								30.43	Static
13:11	7.9	2	10.88	-61	1.115		490		Start Time
13:15	7.78	2.18	10.85	-55	1.216		490	30.43	clear
13:18	7.76	2.19	10.85	-56	1.217		490		clear
13:21	7.76	2.19	10.85	-56	1.217		490	30.43	clear
13:24	7.76	2.19	10.85	-56	1.215	16	490		clear
MINUTES						**TOTAL LITERS**			
13.0	0.00	0.00%	0.00%	0.00	0.00%		**6.37**		

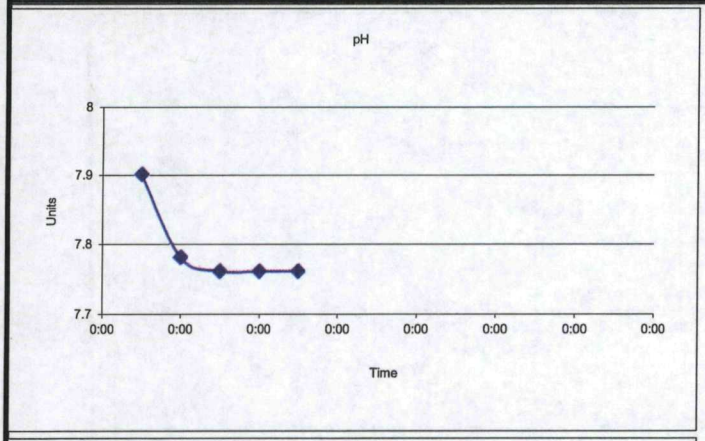

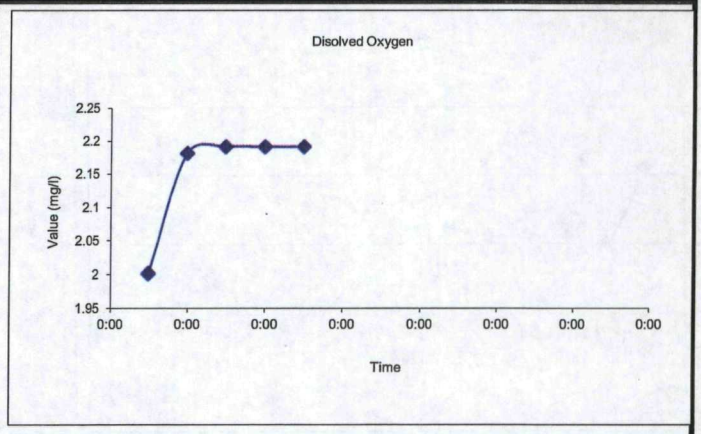

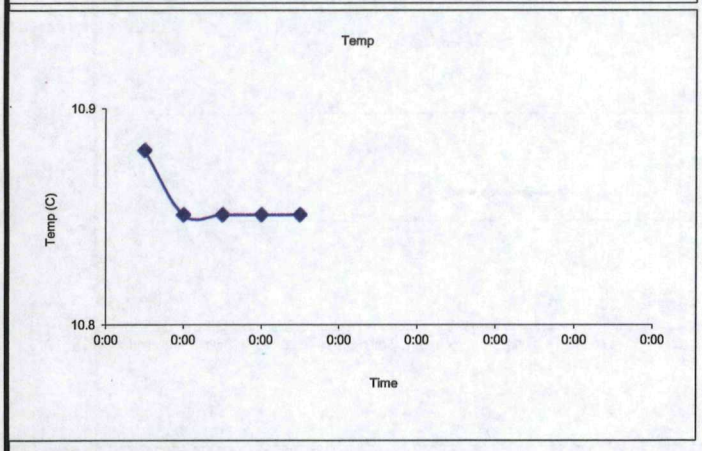

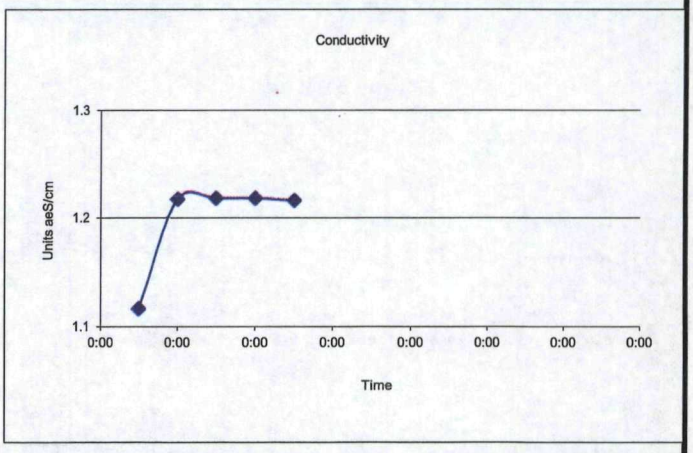

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	220	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 114B**
Casing Stickup (Ft.)	2.35	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	11/24//12
Total Well Depth (Ft.) TOC	222.58	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	31.92	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	190.66	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2012		

FIELD PURGE MONITORING

Time HHMMSS	pH Units	DO mg/l	Temp øC	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
							0	31.92	Static
12:38	7.72	0.55	10.98	-144	0.931		500	31.92	Start Time
12:42	7.89	0.54	10.99	-156	0.93		500		clear
12:46	7.92	0.51	10.99	-159	0.931		500		clear
12:50	7.92	0.49	10.99	-161	0.93		500	31.92	clear
12:53	7.92	0.49	10.99	-161	0.93		500		clear
12:58	7.91	0.48	10.99	-160	0.93	9	500	31.92	sample collected
									*Field Dup1 collected
MINUTES							**TOTAL LITERS**		
20.0	-0.01	-2.08%	0.00%	1.00	0.00%		**10.00**		

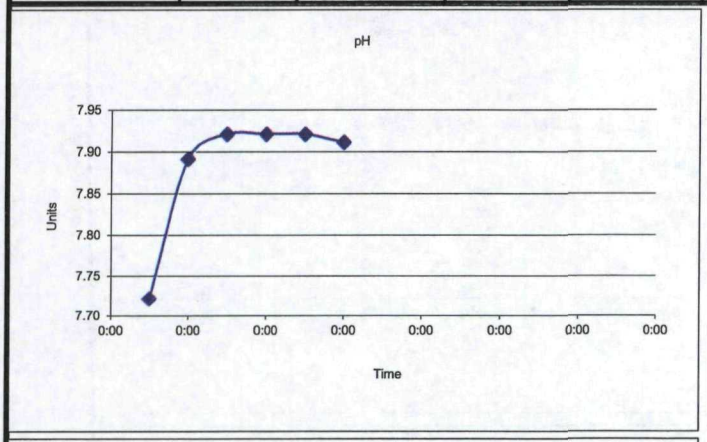

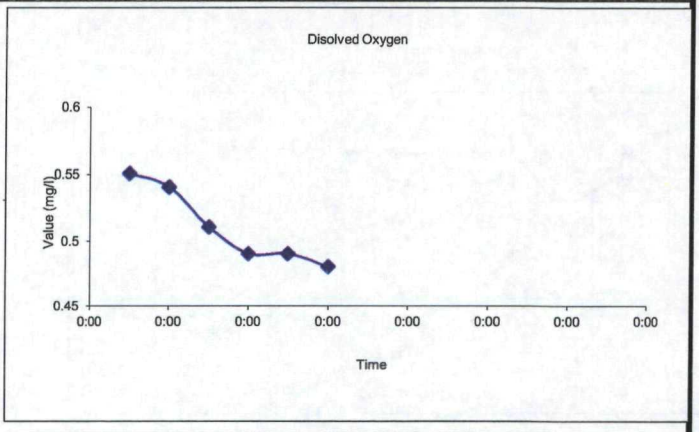

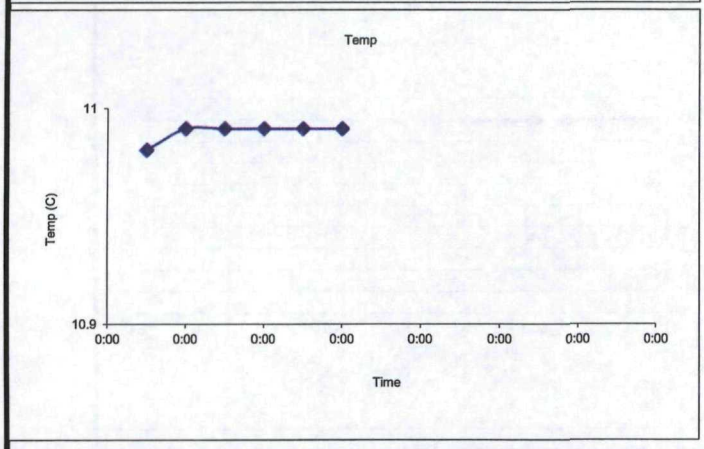

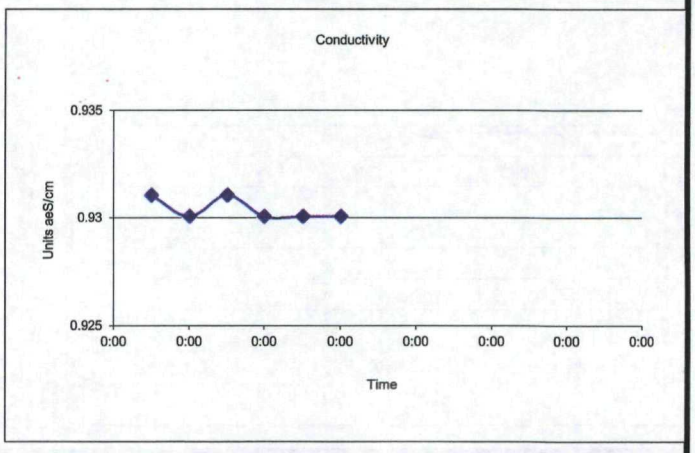

Remarks: (well condition, maintenance, etc...)

Limited access IEPA lock

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	87	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 117B**
Casing Stickup (Ft.)	-0.45	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	25-Nov-12
Total Well Depth (Ft.) TOC	89.5	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	7.7	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	81.8	**Field Analysis Equip**	YSI 556 MPS	**Sampling Period**	Fall 2012		–

FIELD PURGE MONITORING

Time HHMMSS	pH Units	DO mg/l	Temp øC	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
							0	7.70	Static
13:00	7.57	1.33	11.46	64	0.891		500	7.70	Start Time
13:03	7.55	1.35	11.46	53	0.89		500		clear
13:07	7.55	1.35	11.43	44	0.889		500		clear
13:10	7.57	1.38	11.45	44	0.887		500		clear
13:15	7.57	1.38	11.43	40	0.886		500	7.70	clear
13:19	7.57	1.38	11.43	40	0.886		500		clear
13:22	7.57	1.39	11.43	41	0.886	52	500	7.70	sample
MINUTES							**TOTAL LITERS**		
22.0	0.00	0.72%	0.00%	1.00	0.00%		**11.00**		

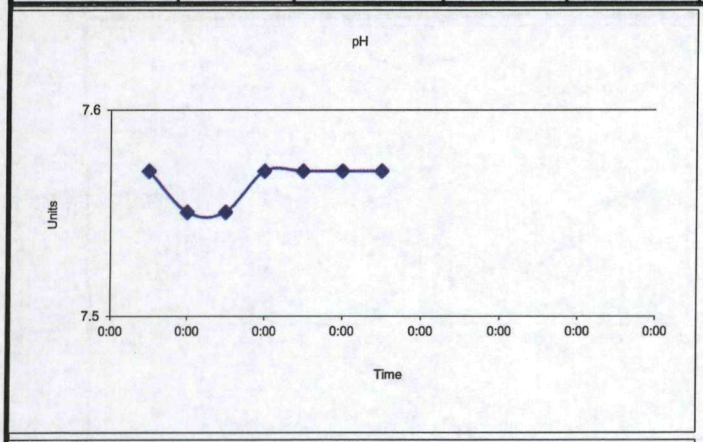

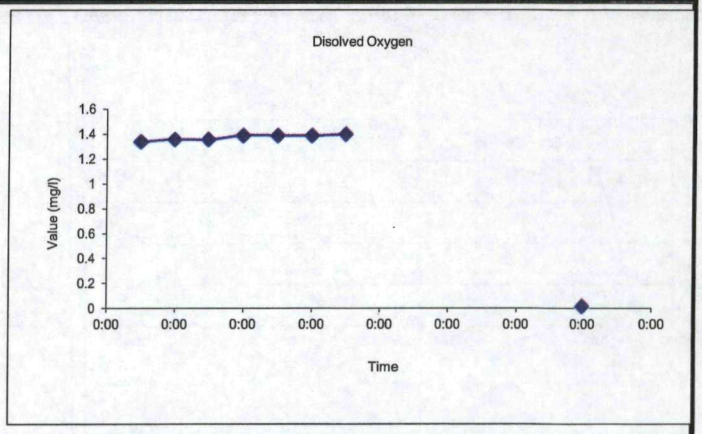

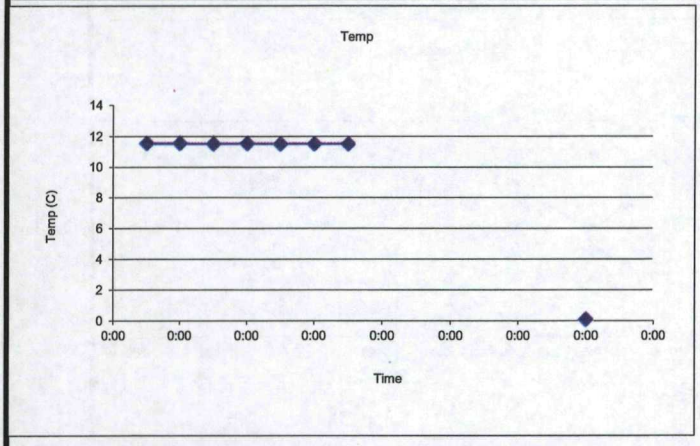

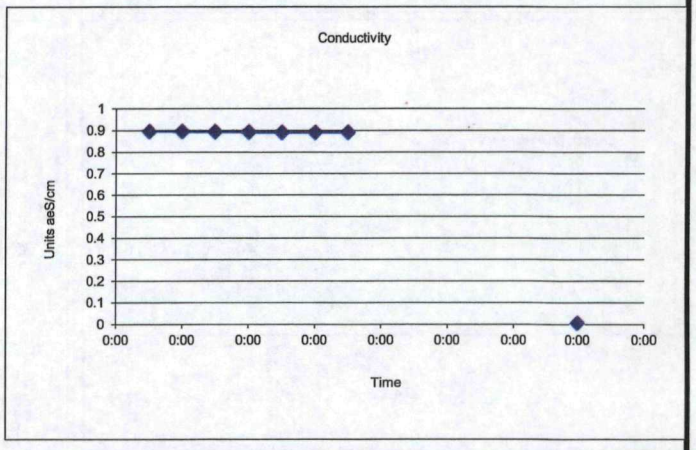

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	156	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 117C**
Casing Stickup (Ft.)	-0.63	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	25-Nov-12
Total Well Depth (Ft.) TOC	158.31	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	6.7	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	151.61	**Field Analysis Equip**	YSI556 MPS	**Sampling Period**	Fall 2012		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	mS/cm	FTU	mL/min	(Ft.) TOC	
							0	6.70	Static
13:30	7.43	1.2	11.46	-56	0.861		500	6.70	Start Time
13:33	7.43	1.22	11.45	-66	0.863		500		clear
13:37	7.44	1.21	11.43	-67	0.862		500	6.70	clear
13:41	7.43	1.21	11.43	-68	0.862		500		clear
13:44	7.43	1.21	11.43	-69	0.862		500	6.70	clear
13:47	7.43	1.2	11.43	-72	0.862	6	500		sample
MINUTES							**TOTAL LITERS**		
17.0	0.00	-0.83%	0.00%	-4.00	0.00%		**8.50**		

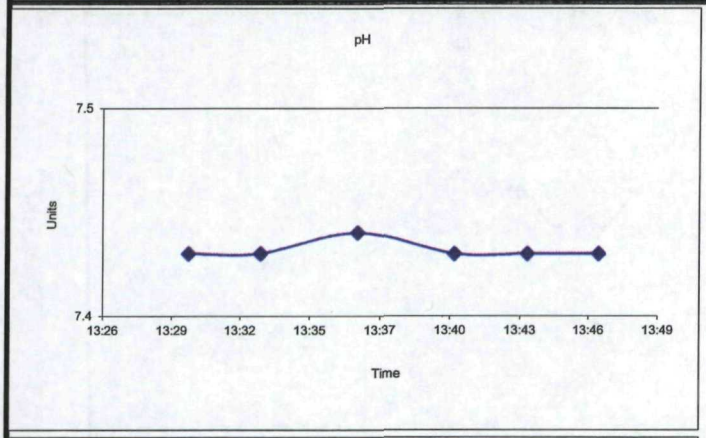

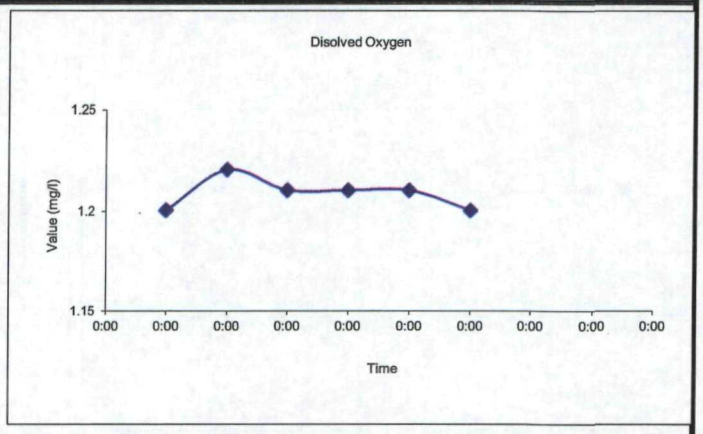

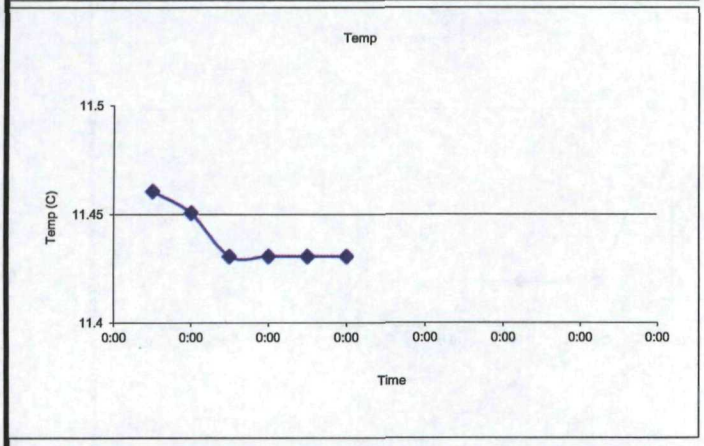

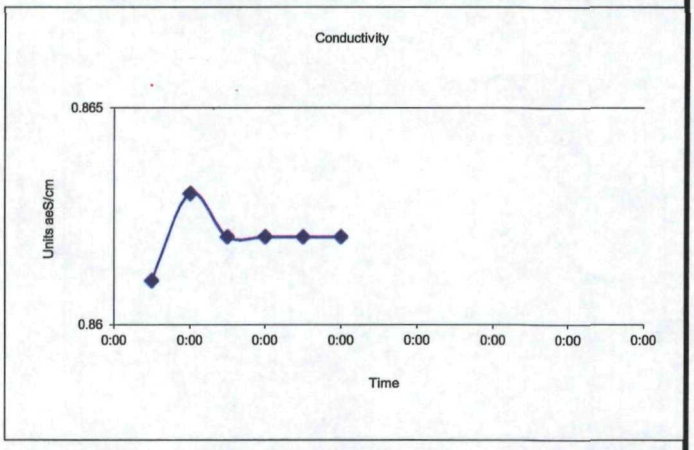

Remarks: (well condition, maintenance, etc...)

1 bolt hole stripped

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	198	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 117D**
Casing Stickup (Ft.)	-0.3	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	25-Nov-12
Total Well Depth (Ft.) TOC	200.2	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	6.21	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	193.99	**Field Analysis Equip**	YSI556 MPS	**Sampling Period**	Fall 2012		–

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	mS/cm	FTU	mL/min	(Ft.) TOC	
							0	6.21	Static
14:05	7.51	0.63	11.86	-90	1.098		500	6.21	Start Time
14:08	7.56	0.62	11.86	-95	1.096		500		clear
14:12	7.56	0.62	11.87	-93	1.096		500		clear
14:15	7.56	0.63	11.87	-94	1.096		500		clear
14:18	7.56	0.63	11.87	-94	1.096	10	500	6.21	sample
MINUTES							**TOTAL LITERS**		
13.0	0.00	1.59%	0.00%	-1.00	0.00%		**6.50**		

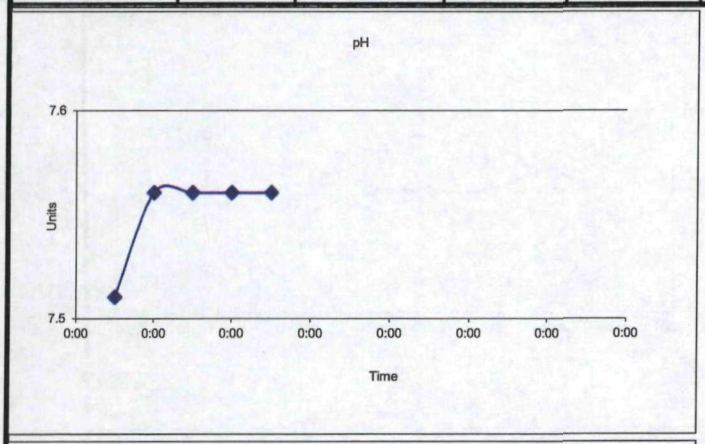

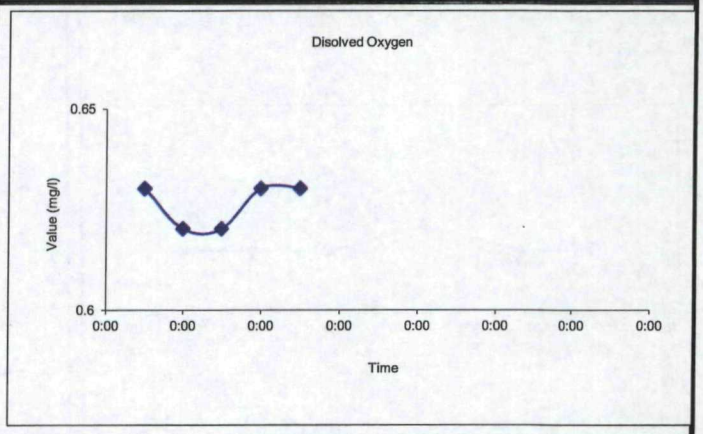

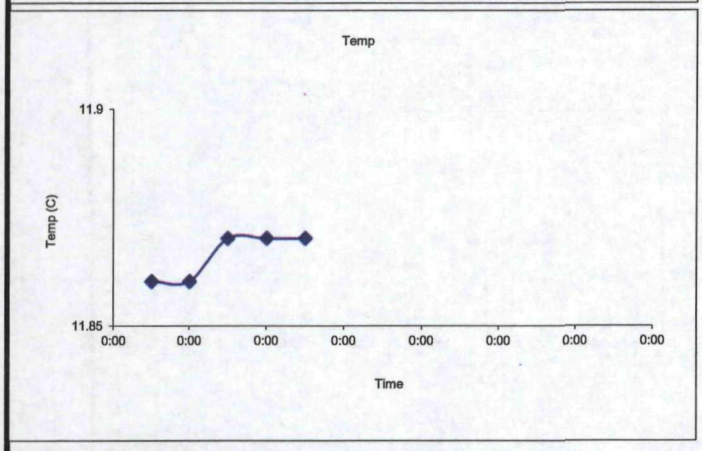

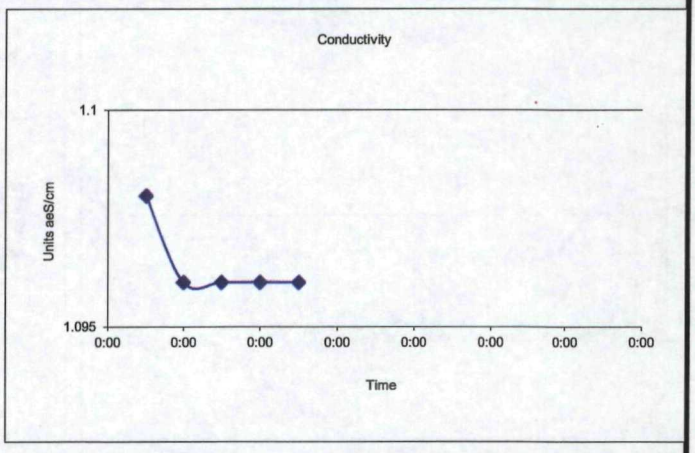

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	60	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 119**
Casing Stickup (Ft.)	3.25	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	25-Nov-12
Total Well Depth (Ft.) TOC	62.41	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	27.89	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	34.52	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2012		

FIELD PURGE MONITORING

Time HHMMSS	pH Units	DO mg/l	Temp øC	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
							0	27.89	Static
10:36	7.56	4.23	11.22	23	1.21		425	27.93	Start Time
10:40	7.52	4.31	11.28	25	1.211		425		clear
10:43	7.52	4.3	11.28	26	1.213		425		clear
10:46	7.53	4.31	11.28	28	1.213		425	27.93	clear
10:50	7.53	4.33	11.27	28	1.213		425		clear
10:53	7.53	4.33	11.27	27	1.213	9	425		sample
MINUTES							**TOTAL LITERS**		
17.0	0.00	0.46%	0.00%	-1.00	0.00%		**7.23**		

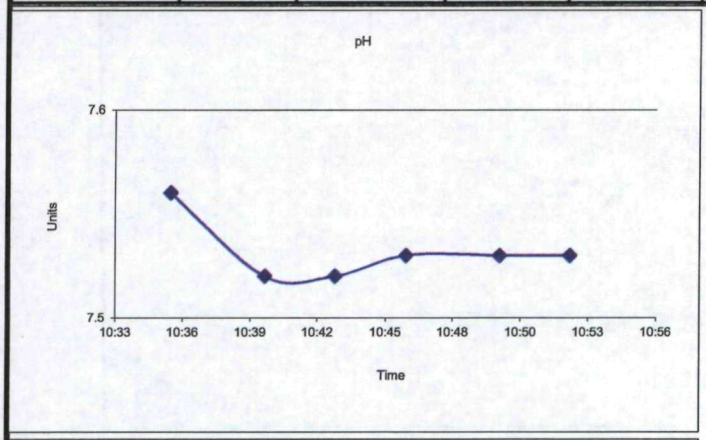

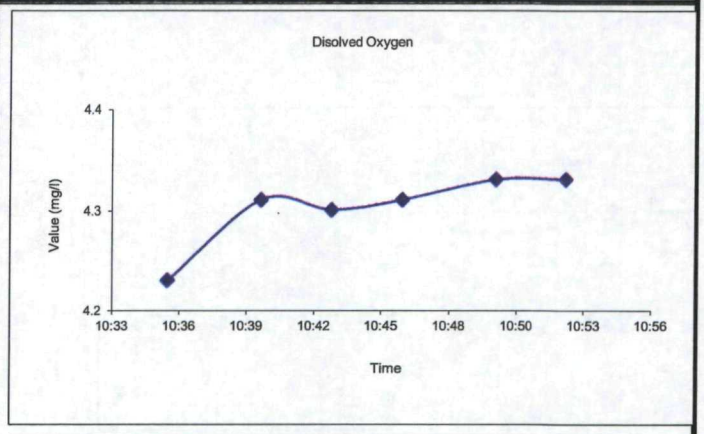

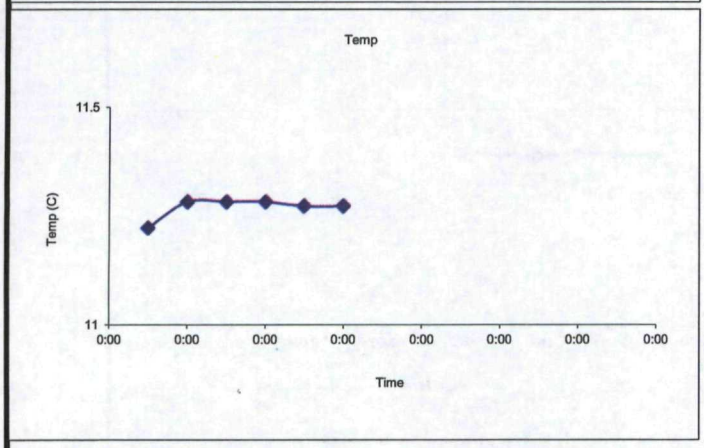

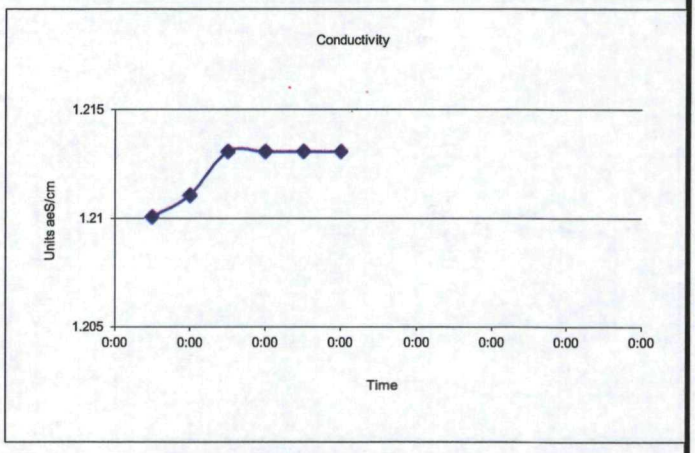

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	65	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 121**
Casing Stickup (Ft.)	2.53	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	25-Nov-12
Total Well Depth (Ft.) TOC	67.55	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	24.58	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	42.97	**Field Analysis Equip**	YSI556 MSP	**Sampling Period**	Fall 2012		–

FIELD PURGE MONITORING

Time HHMMSS	pH Units	DO mg/l	Temp øC	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
							0	24.58	Start Time
9:34	7.51	3.05	11.22	33	1.178		350	24.64	cloudy
9:37	7.5	3.11	11.21	34	1.179		350		clear
9:40	7.49	3.13	11.21	41	1.179		350		clear
9:43	7.48	3.13	11.21	37	1.178		350		clear
9:46	7.48	3.15	11.21	37	1.179		350	24.68	clear
9:49	7.48	3.15	11.20	38	1.179	49	350		sample
MINUTES							**TOTAL LITERS**		
15.0	0.00	0.63%	0.00%	1.00	0.00%		**5.25**		

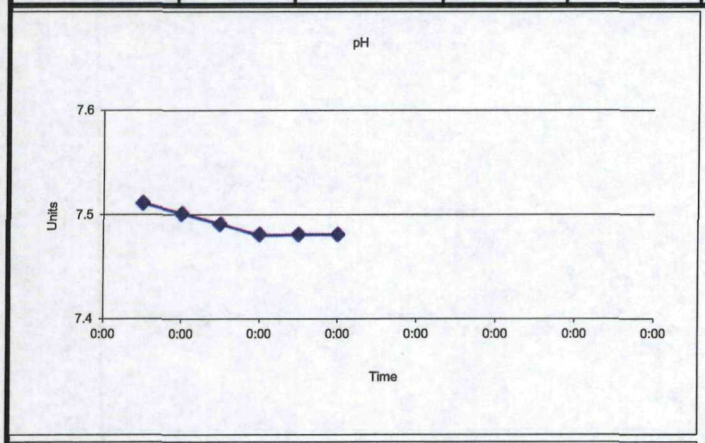

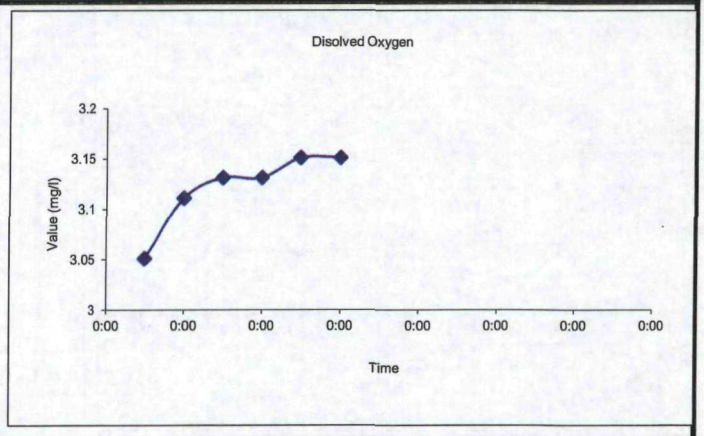

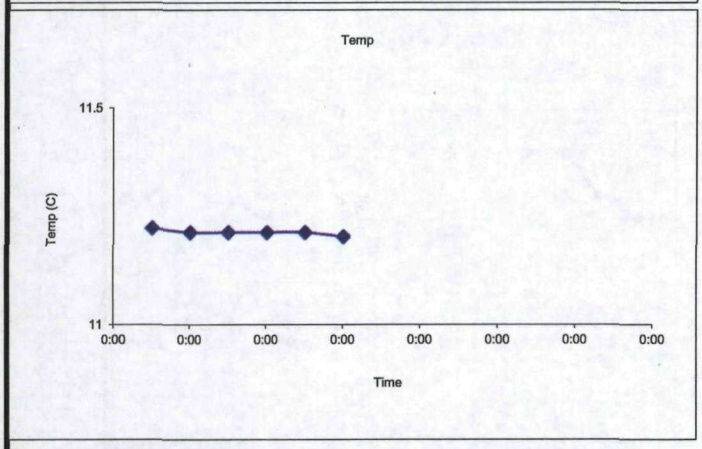

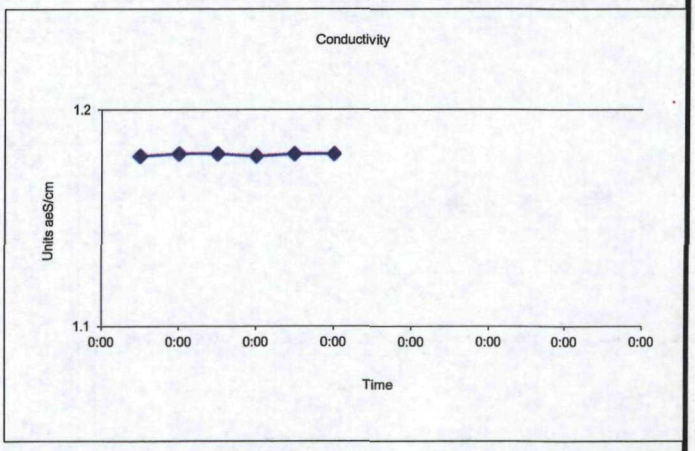

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	100	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 124**
Casing Stickup (Ft.)	2.17	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	25-Nov-12
Total Well Depth (Ft.) TOC	102.76	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	37.33	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	65.43	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2012		–

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	mS/cm	FTU	mL/min	(Ft.) TOC	
							0	37.33	Start Time
11:14	7.62	1.03	11.05	-60	1.105		430	37.51	cloudy
11:17	7.6	1.11	11.13	-66	1.104		430		cloudy
11:20	7.6	1.1	11.13	-69	1.104		430		clear
11:24	7.61	1.12	11.14	-74	1.103		430		clear
11:27	7.61	1.12	11.14	-80	1.103		430	37.51	clear
11:31	7.61	1.12	11.13	-80	1.103	8	430		clear
MINUTES						**TOTAL LITERS**			
17.0	0.00	0.00%	0.00%	-6.00	0.00%		**7.31**		

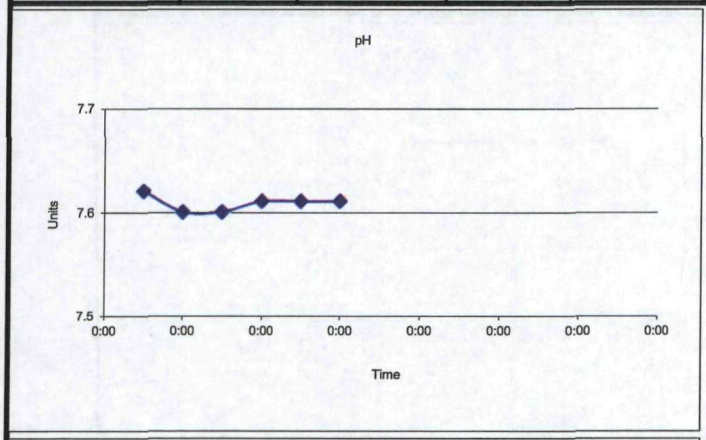

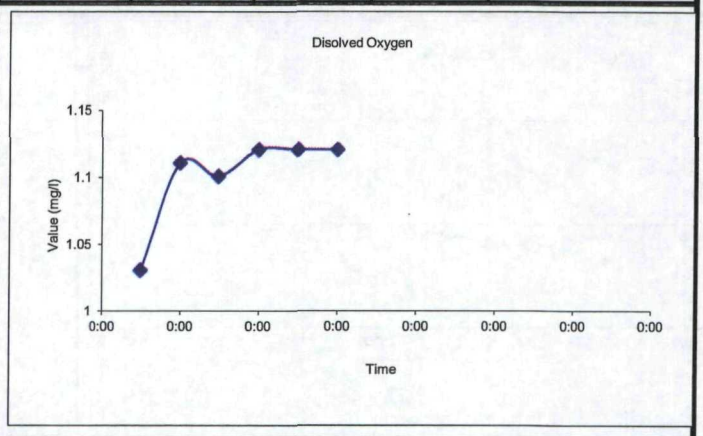

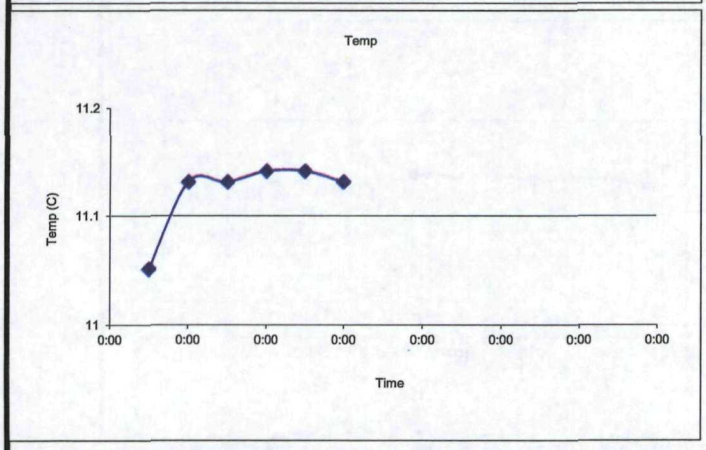

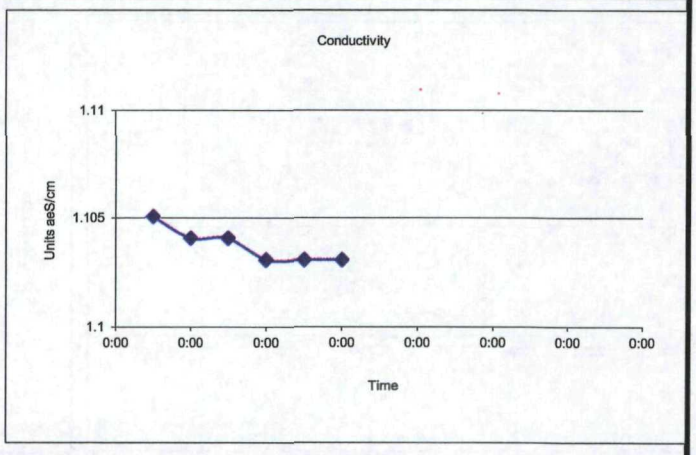

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	36	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 130**
Casing Stickup (Ft.)	-0.3	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	24-Nov-12
Total Well Depth (Ft.) TOC	38.17	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	26.22	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	11.95	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2012		

FIELD PURGE MONITORING

Time HHMMSS	pH Units	DO mg/l	Temp øC	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
							0	26.22	Start Time
13:27	7.5	2.04	11.04	-11	1.284		440	26.33	cloudy
13:31	7.49	2.65	11.02	-5	1.286		440		slightly cloudy
13:35	7.48	2.66	11.00	7	1.286		440		clear
13:38	7.48	2.67	10.98	9	1.286		440	26.33	clear
13:42	7.48	2.68	10.96	10	1.287		440		clear
13:46	7.49	2.68	10.96	15	1.287		440		clear
13:49	7.49	2.69	10.96	15	1.287	20	440	26.33	sample
MINUTES							**TOTAL LITERS**		
22.0	0.01	0.37%	0.00%	5.00	0.00%		**9.68**		

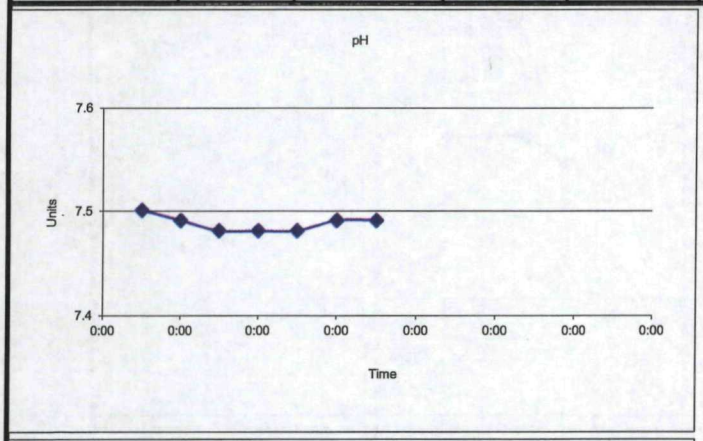

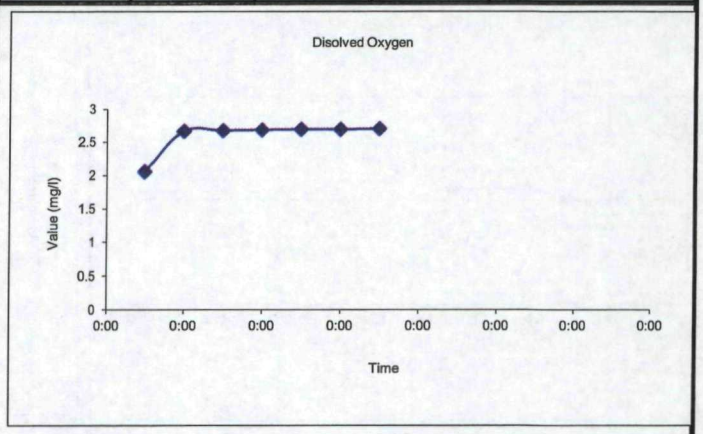

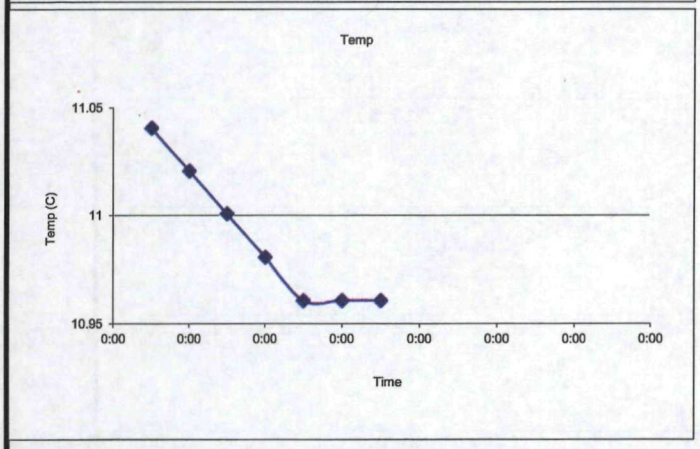

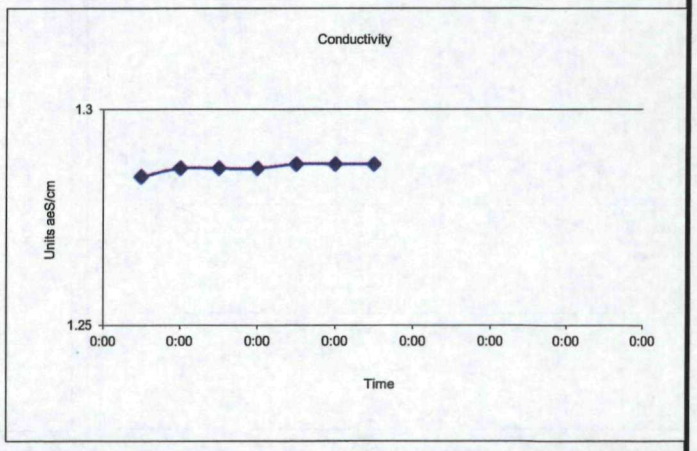

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	35	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 133A**
Casing Stickup (Ft.)	2.3	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	24-Nov-12
Total Well Depth (Ft.) TOC	37.85	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	37.35	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	0.5	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2012		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	mS/cm	FTU	mL/min	(Ft.) TOC	
							0	37.35	Static
									No Sample - Well Dry
MINUTES						**TOTAL LITERS**			
0.0	0.00	0.00%	0.00%	0.00	0.00%		**0.00**		

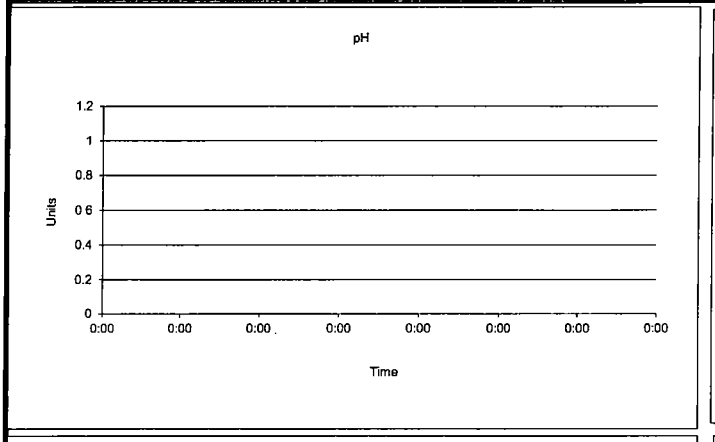

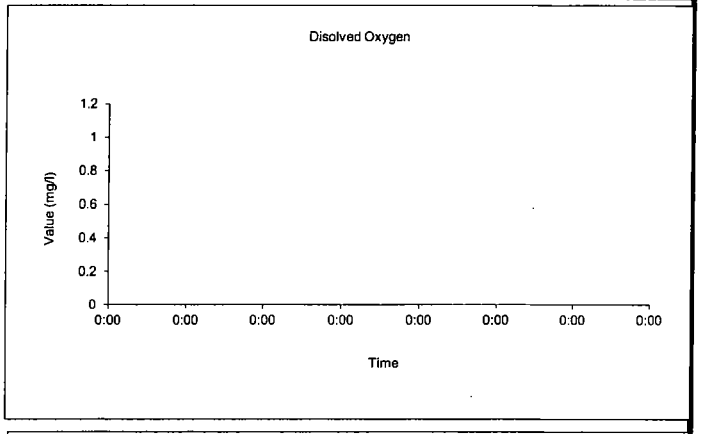

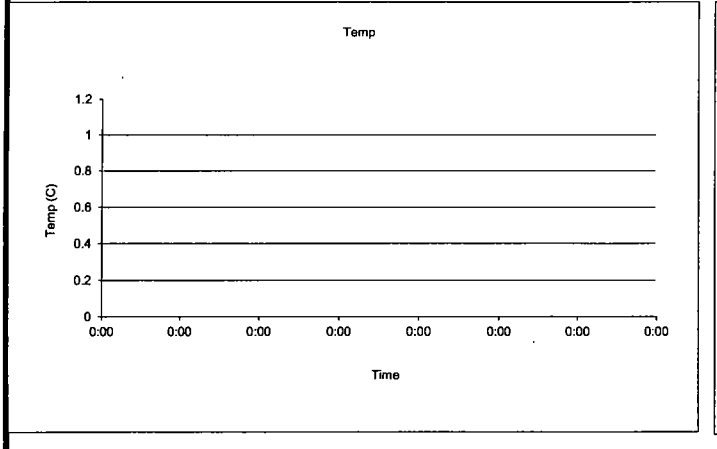

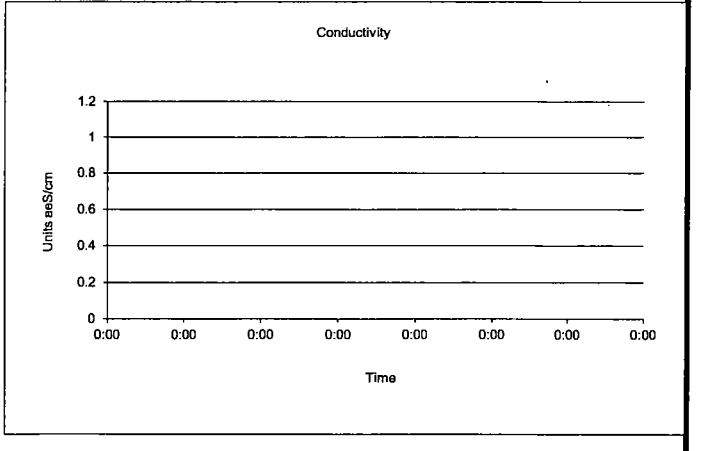

Remarks: (well condition, maintenance, etc...)

WELL DRY

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	59	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 133B**
Casing Stickup (Ft.)	2.51	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	24-Nov-12
Total Well Depth (Ft.) TOC	61.49	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	30.82	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	30.67	**Field Analysis Equip**	YAI 556 MSP	**Sampling Period**	Fall 2012		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	mS/cm	NTU	mL/min	(Ft.) TOC	
							0	30.82	Static
10:36	7.55	3.87	10.89	22	1.001		475	30.91	Start Time
10:39	7.48	3.8	10.88	5	1.005		475		slightly cloudy
10:42	7.48	3.79	10.88	0	1.102		475	30.92	clear
10:45	7.48	3.79	10.89	-1	1.105		475		clear
10:48	7.47	3.79	10.89	-8	1.108		475		clear
10:52	7.48	3.78	10.89	-10	1.108		475	30.92	clear
10:56	7.48	3.78	10.89	-11	1.108	63	475		clear
MINUTES							**TOTAL LITERS**		
20.0	0.01	-0.26%	0.00%	-3.00	0.00%		**9.50**		

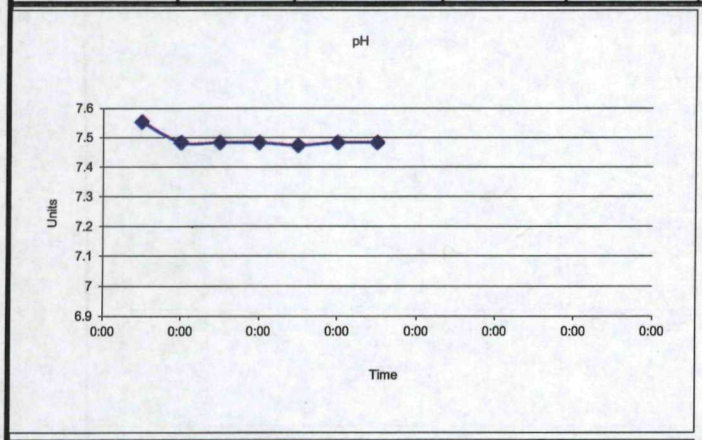

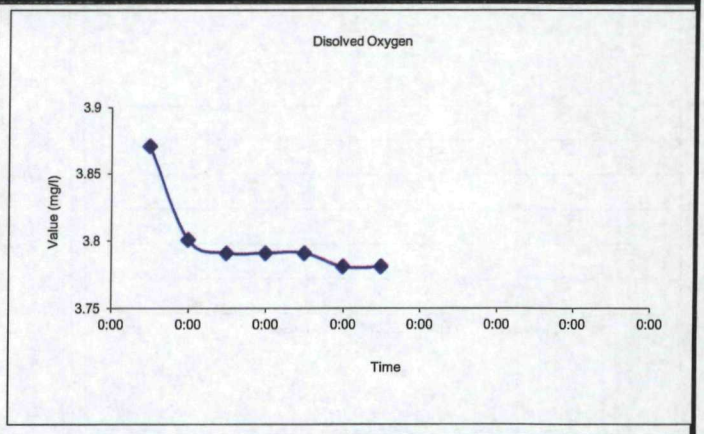

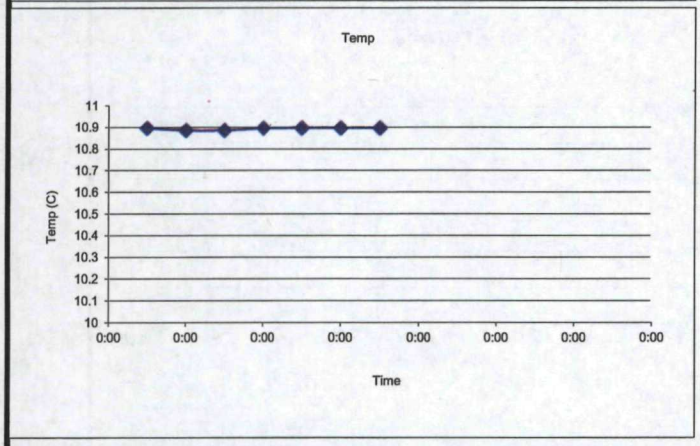

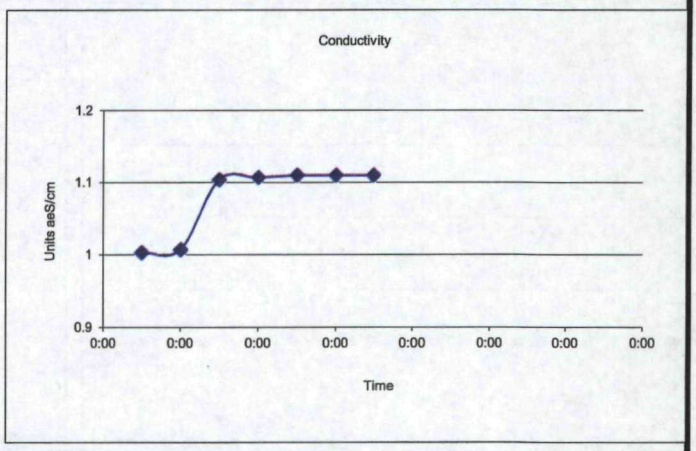

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	96	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 133C**
Casing Stickup (Ft.)	2.37	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	24-Nov-12
Total Well Depth (Ft.) TOC	98.49	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	26.21	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	72.28	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2012		

FIELD PURGE MONITORING

Time HHMMSS	pH Units	DO mg/l	Temp øC	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
							0	26.21	Static
11:11	7.44	2.15	10.78	-96	0.787		500		Start Time
11:16	7.46	2.89	10.78	-46	0.782		500	26.28	clear
11:21	7.46	2.89	10.78	-45	0.78		500		clear
11:25	7.46	2.88	10.80	-45	0.779		500		clear
11:28	7.46	2.88	10.80	-43	0.779	19	500	26.28	clear
MINUTES							**TOTAL LITERS**		
17.0	0.00	-0.35%	0.00%	2.00	0.00%		**8.50**		

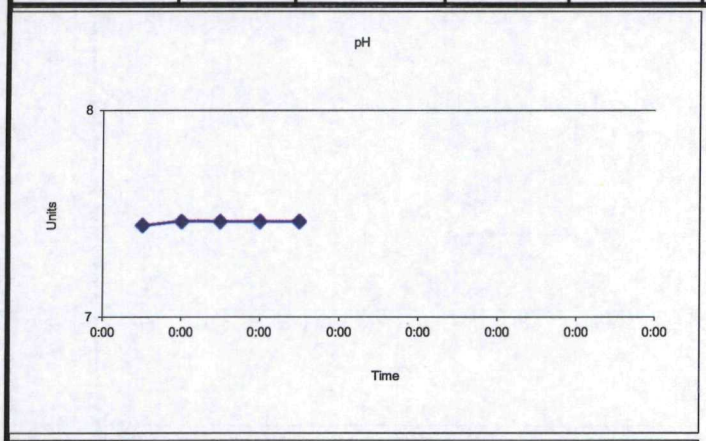

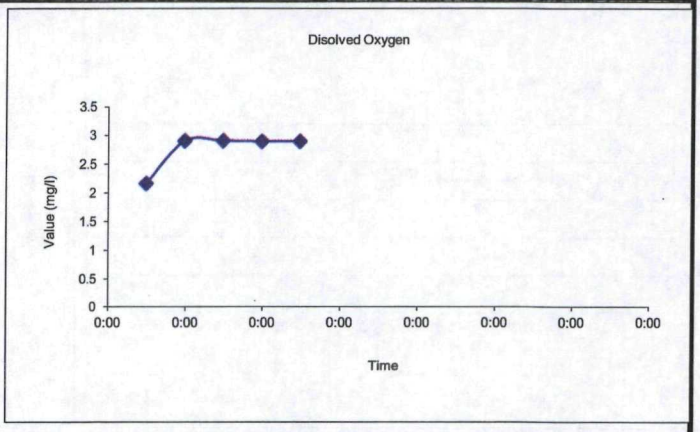

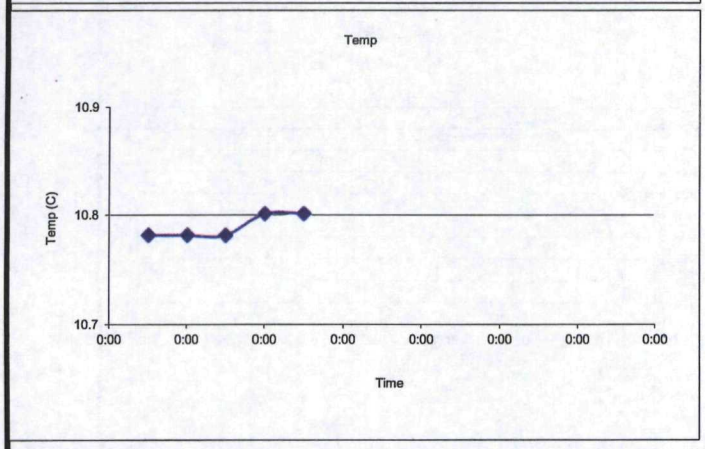

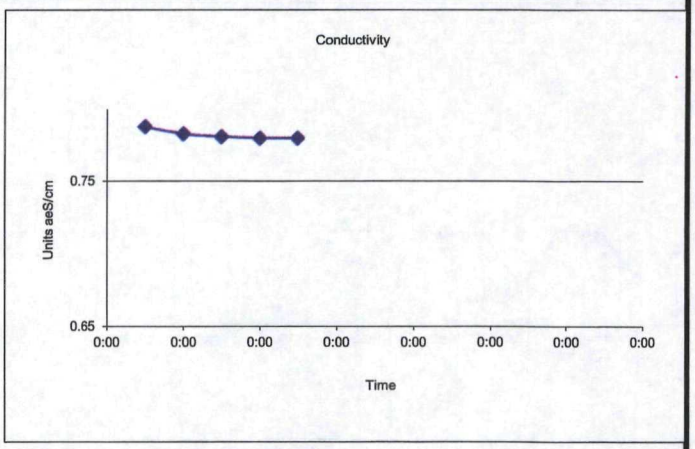

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	42	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 136**
Casing Stickup (Ft.)	-0.42	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	24-Nov-12
Total Well Depth (Ft.) TOC	44.33	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	38.58	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	5.75	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2012		

FIELD PURGE MONITORING

Time HHMMSS	pH Units	DO mg/l	Temp øC	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
							0	38.58	Static
10:03	7.09	8.75	11.92	22	1.181		250		Start Time
10:06	7.11	3.91	11.94	-5	1.211		250	38.60	slightly cloudy
10:08	7.15	3.78	11.94	-8	1.218		250		slightly cloudy
10:11	7.15	3.77	11.92	-4	1.218		250		slightly cloudy
10:15	7.15	3.77	11.94	1	1.218		250	38.61	slightly cloudy
10:18	7.15	3.76	11.94	4	1.218	95	250		slightly cloudy
MINUTES							**TOTAL LITERS**		
15.0	0.00	-0.27%	0.00%	8.00	0.00%		**3.75**		

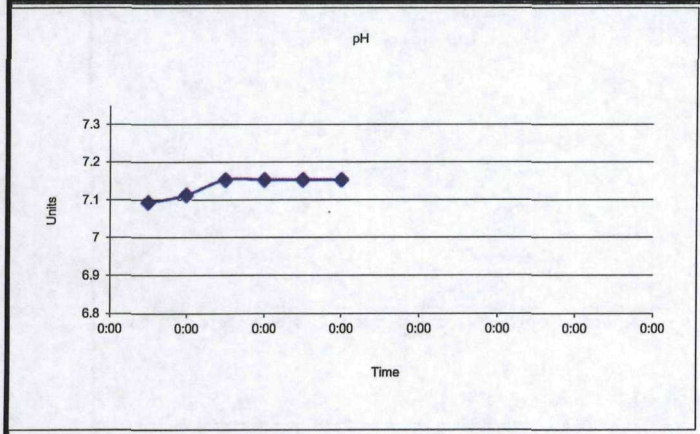

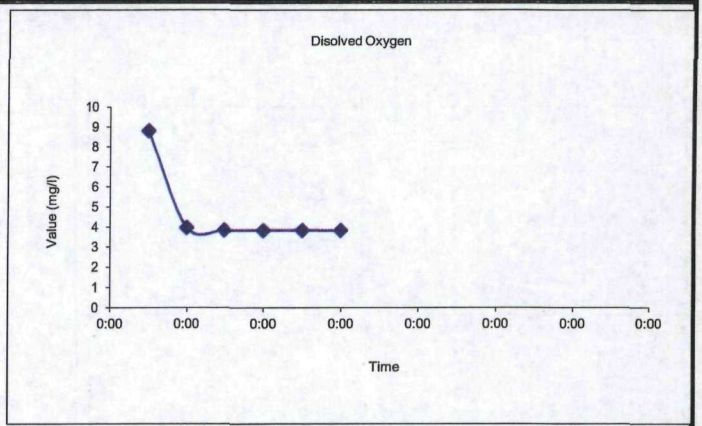

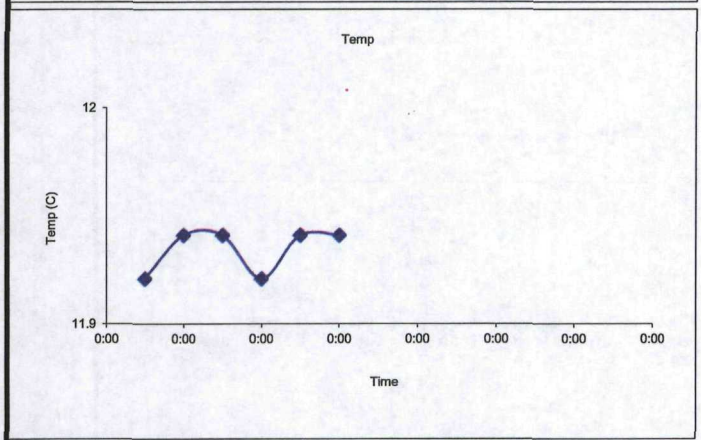

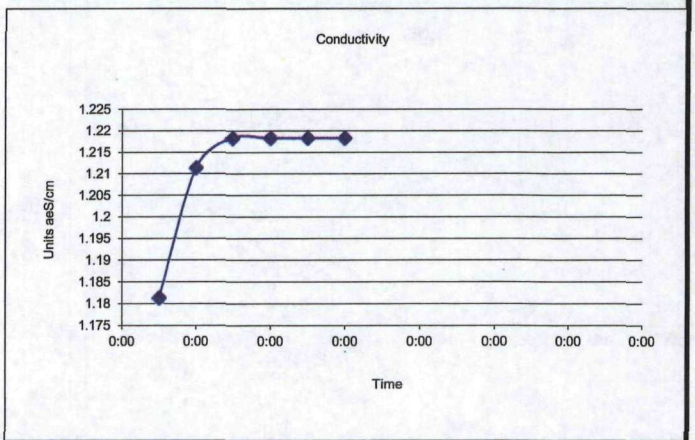

Remarks: (well condition, maintenance, etc...)

Low producing well - pumped at low flow rate.

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	87	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 200**
Casing Stickup (Ft.)	1.15	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	24-Nov-12
Total Well Depth (Ft.) TOC	89.93	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	52.3	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	37.63	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2012		

FIELD PURGE MONITORING

Time HHMMSS	pH Units	DO mg/l	Temp øC	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
							0	52.30	Static
15:01	7.48	4.77	11.89	22	1.005		410	52.41	Start Time
15:04	7.5	4.92	11.89	25	1		410		cloudy
15:07	7.51	5.11	11.85	30	1.006		410	52.41	slightly cloudy
15:10	7.5	5.13	11.85	35	1.008		410		slightly cloudy
15:13	7.5	5.14	11.85	36	1.008		410		slightly cloudy
15:16	7.5	5.14	11.85	38	1.008	55	410	52.48	sample
MINUTES							**TOTAL LITERS**		
15.0	0.00	0.19%	0.00%	3.00	0.00%		**6.15**		

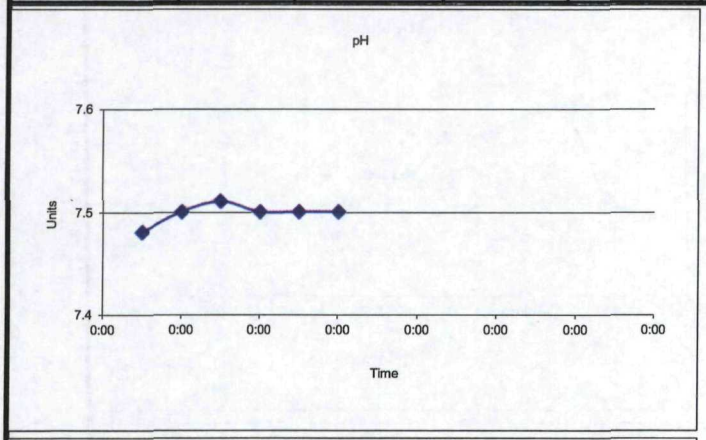

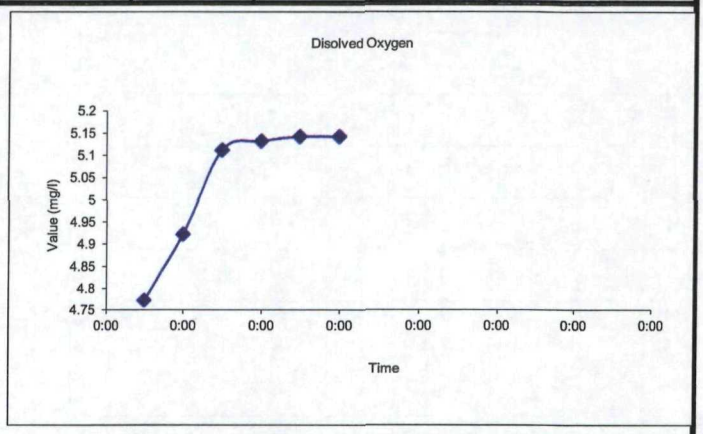

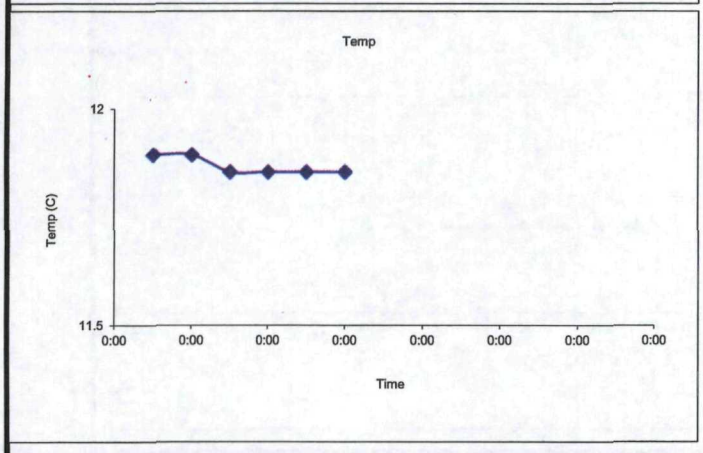

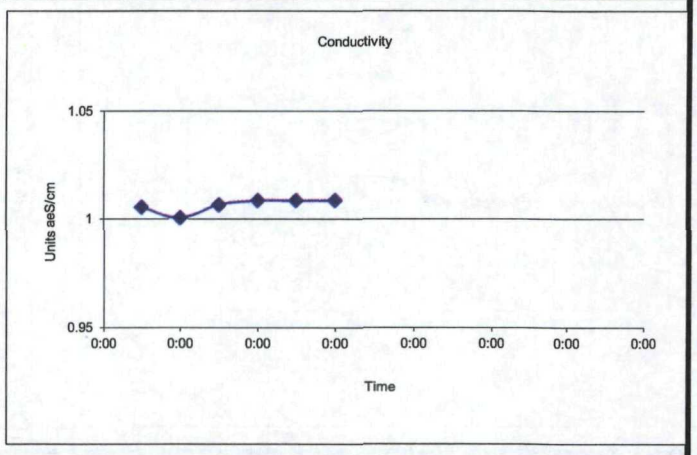

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	48	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 201**
Casing Stickup (Ft.)	-0.32	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	25-Nov-12
Total Well Depth (Ft.) TOC	50.15	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	31.92	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	18.23	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2012		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	mS/cm	FTU	mL/min	(Ft.) TOC	
							0	31.92	Start Time
12:16	7.97	7.44	12.23	64	1.196		350	32.01	cloudy
12:20	7.76	7.449	12.26	68	1.195		350		clear
12:24	7.73	7.49	12.26	77	1.194		350		clear
12:27	7.71	7.49	12.25	79	1.194		350	32.01	clear
12:32	7.71	7.48	12.25	82	1.194		350		clear
12:35	7.7	7.48	12.25	88	1.194		350		clear
12:39	7.7	7.46	12.26	85	1.195		350	32.01	clear
12:43	7.7	7.46	12.26	86	1.195	30	350		clear
MINUTES							**TOTAL LITERS**		
27.0	0.00	-0.27%	0.00%	-2.00	0.00%		**9.45**		

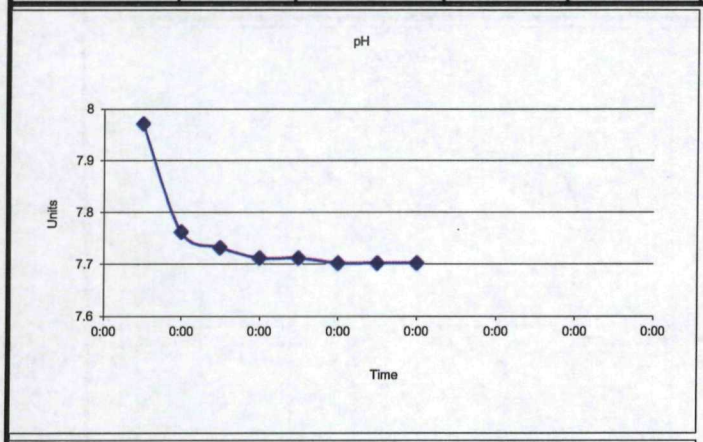

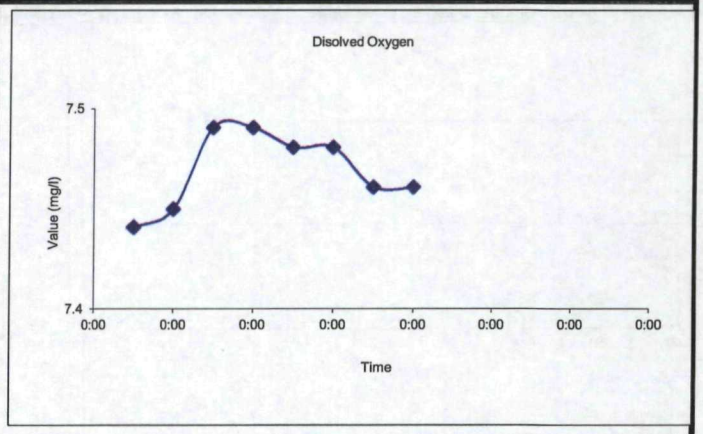

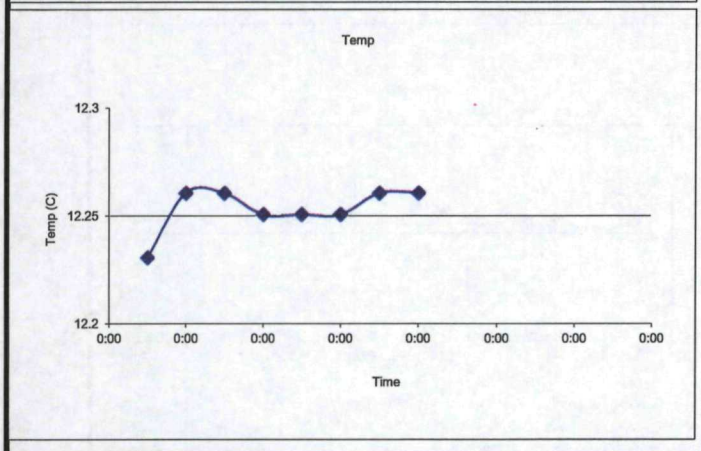

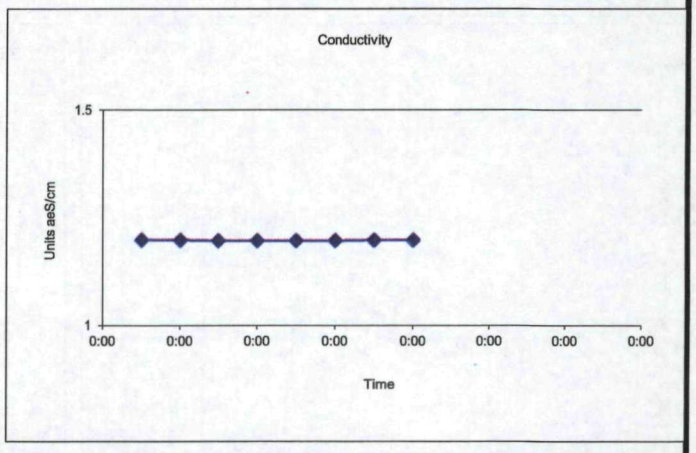

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	48	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 202**
Casing Stickup (Ft.)	-0.32	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	30-Nov-12
Total Well Depth (Ft.) TOC	50.01	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	31.35	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	18.66	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2012		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	mS/cm	FTU	mL/min	(Ft.) TOC	
							0	31.35	Start Time
12:35	7.64	4.3	12.83	33	1.246		340	31.50	cloudy
12:39	7.65	4.02	12.86	36	1.246		340		clear
12:42	7.63	4.03	12.86	38	1.248		340		clear
12:45	7.62	4.03	12.86	43	1.248		340		clear
12:48	7.62	4.03	12.85	44	1.248		340	31.49	clear
12:51	7.62	4.04	12.84	46	1.249		340		clear
12:55	7.62	4.04	12.84	48	1.249	94	340	31.49	sample
MINUTES							**TOTAL LITERS**		
20.0	0.00	0.25%	0.00%	4.00	0.00%		**6.80**		

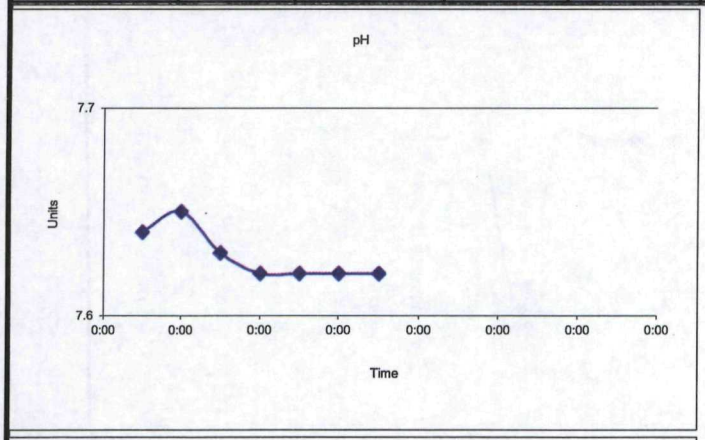

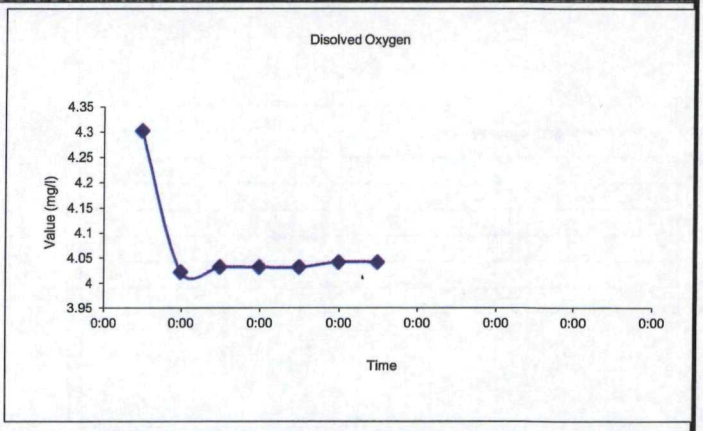

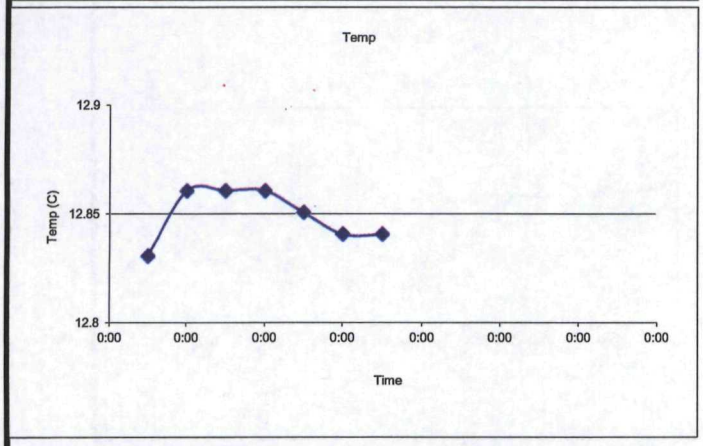

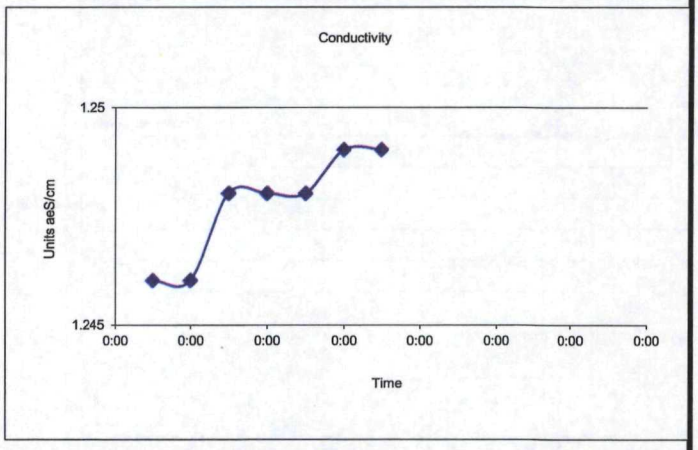

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	47	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 203**
Casing Stickup (Ft.)	-0.58	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	30-Nov-12
Total Well Depth (Ft.) TOC	49.35	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	36.89	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	12.46	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2012		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	mS/cm	FTU	mL/min	(Ft.) TOC	
							0	36.89	Start Time
11:57	7.51	1.52	11.86	31	0.923		400	36.96	cloudy
12:00	7.49	1.53	11.86	30	0.922		400		cloudy
12:04	7.48	1.55	11.88	35	0.921		400		clear
12:08	7.48	1..54	11.88	34	0.918		400	36.96	clear
12:11	7.48	1.54	11.88	36	0.918		400		clear
12:15	7.48	1.54	11.88	36	0.918	15	400	36.96	sample
MINUTES						**TOTAL LITERS**			
18.0	0.00	0.00%	0.00%	2.00	0.00%		**7.20**		

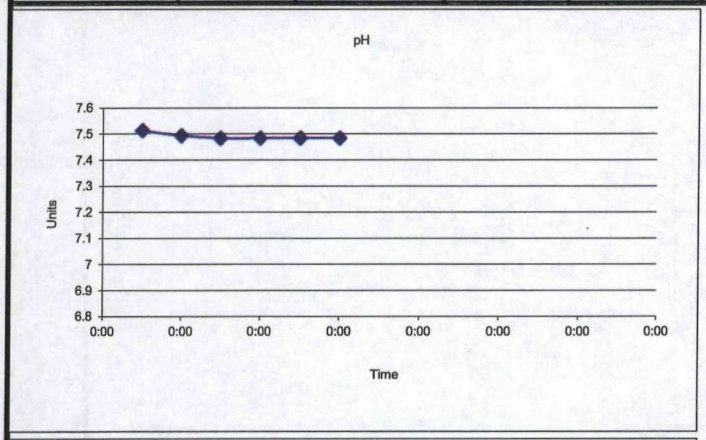

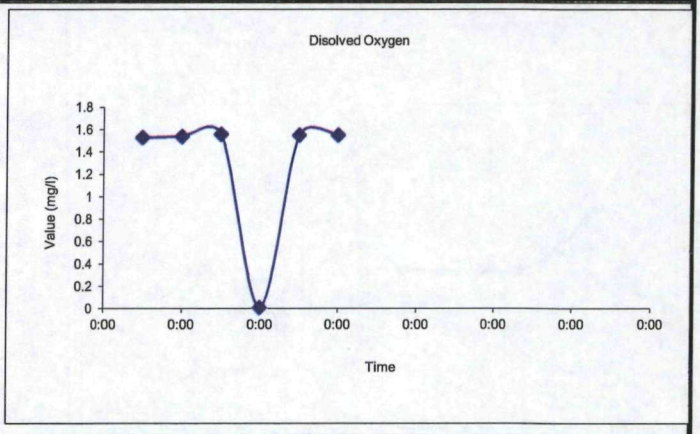

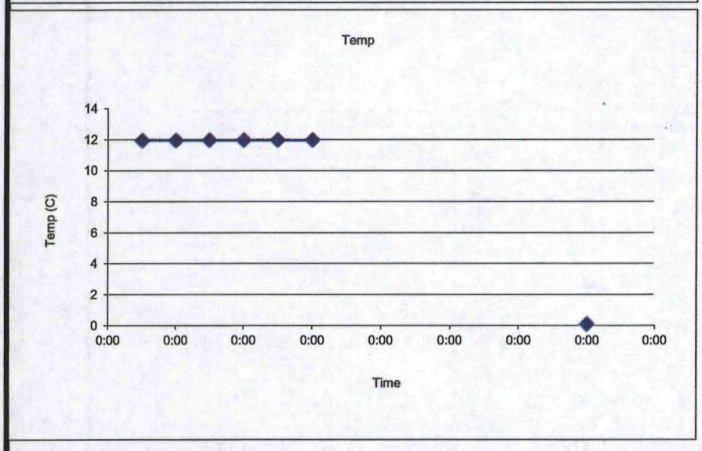

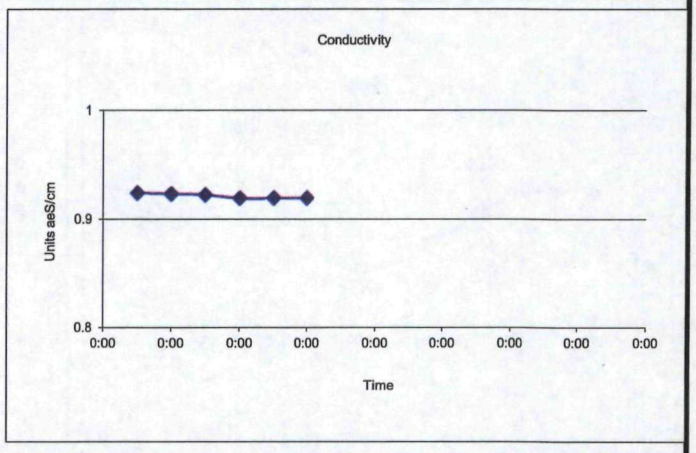

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	86	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 204**
Casing Stickup (Ft.)	-0.39	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	25-Nov-12
Total Well Depth (Ft.) TOC	88.96	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	28.97	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	59.99	**Field Analysis Equip**	YSI 556 MPS	**Sampling Period**	Fall 2012		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	mS/cm	FTU	mL/min	(Ft.) TOC	
							0	28.97	Static
8:54	7.49	0.89	11.15	65	0.944		430	29.00	slightly cloudy
8:57	7.46	0.9	11.12	66	0.943		430		slightly cloudy
9:00	7.46	0.91	11.11	72	0.943		430		slightly cloudy
9:03	7.45	0.91	11.11	75	0.943		430	29.10	slightly cloudy
9:07	7.45	0.92	11.10	74	0.942		430		slightly cloudy
9:10	7.45	0.92	11.11	75	0.942		430		slightly cloudy
9:13	7.45	0.93	11.10	75	0.942		430	29.10	clear
9:16	7.45	0.92	11.10	74	0.942	84	430		sample
MINUTES						**TOTAL LITERS**			
22.0	0.00	0.00%	0.00%	-1.00	0.00%		**9.46**		

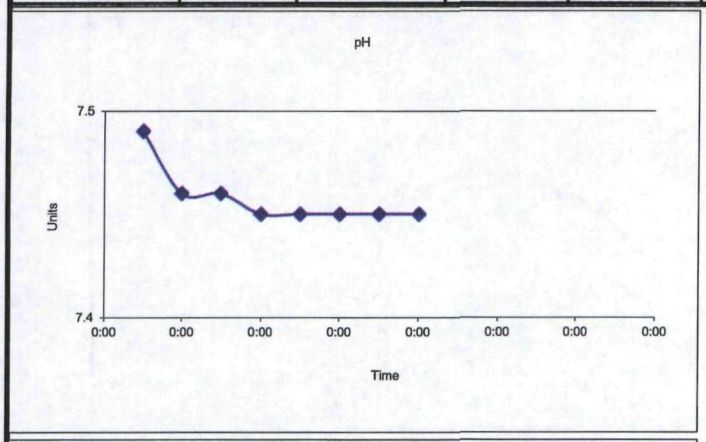

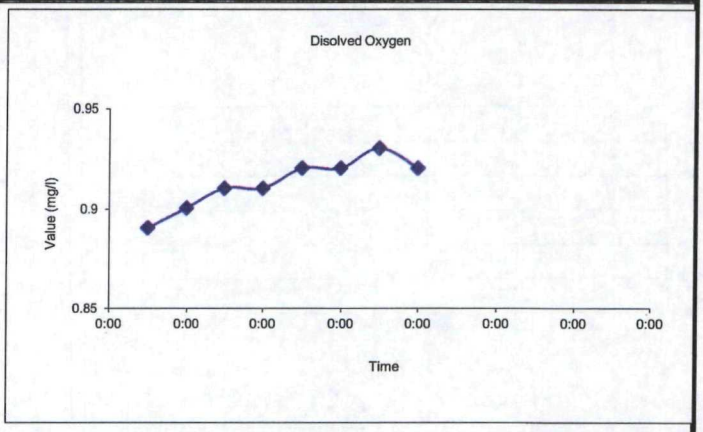

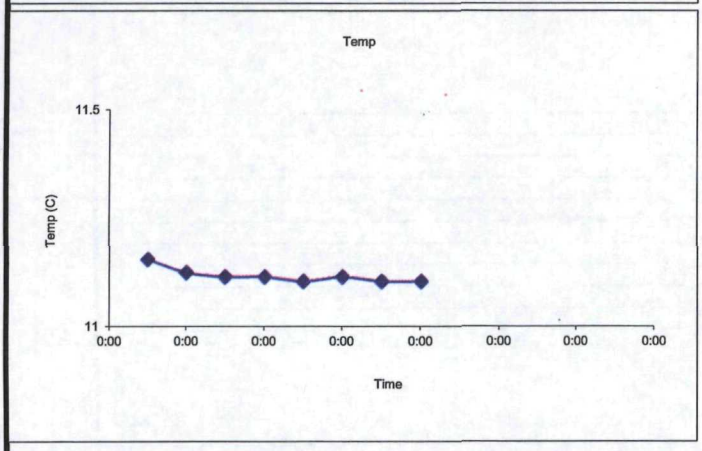

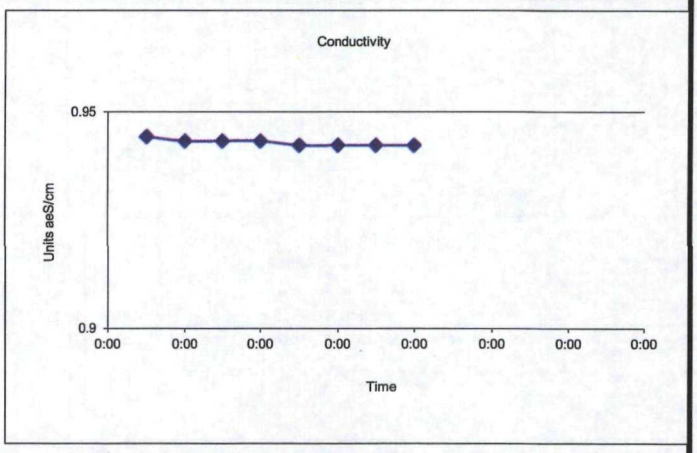

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	108	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 205A**
Casing Stickup (Ft.)	-0.34	**Purge Method**	Bailing	**Container**	40 mL VOA Vial	Sample Date	2-Dec-12
Total Well Depth (Ft.) TOC	110.27	**Purge Equip**	SS Bailer	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	4.85	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	105.42	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2012		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	mS/cm	FTU	mL/min	(Ft.) TOC	
							0	4.85	Static
8:58	7.39	4.33	12.33	15	1.006				clear
9:03	7.41	4.35	12.30	-2	1.006				clear
9:08	7.41	4.36	12.30	-10	1.008				clear
9:12	7.41	4.35	12.30	-9	1.008	4		4.85	sample
MINUTES							**TOTAL LITERS**		
14.0	0.00	0.00%	0.00%	-7.00	0.00%		**0.00**		

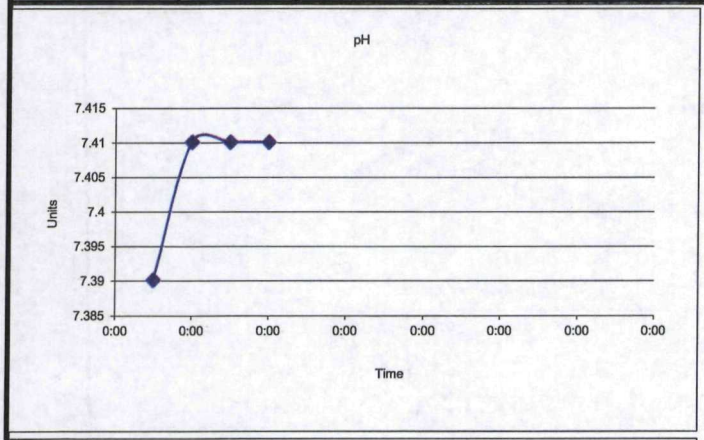

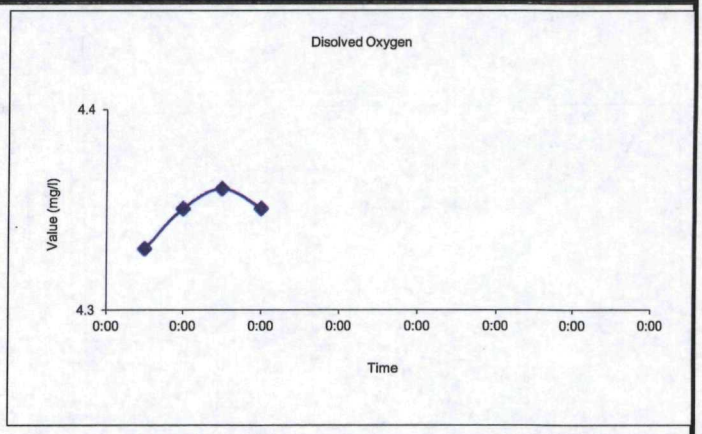

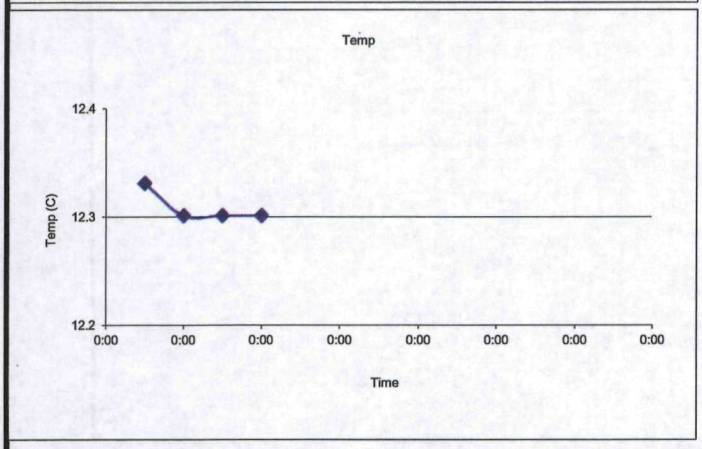

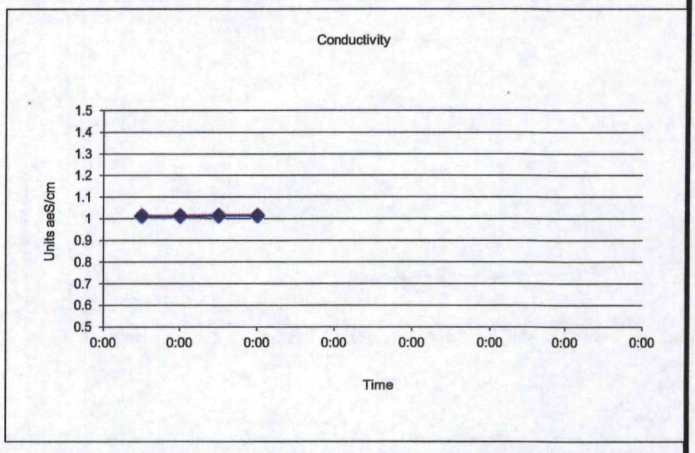

Remarks: (well condition, maintenance, etc...)

limited access - bailed well

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	148	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 205B**
Casing Stickup (Ft.)	-0.48	**Purge Method**	Bailing	**Container**	40 mL VOA Vial	Sample Date	2-Dec-12
Total Well Depth (Ft.) TOC	150.05	**Purge Equip**	ss bailer	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	4.73	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	145.32	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2012		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	mS/cm	FTU	mL/min	(Ft.) TOC	
							0	4.73	Static
8:12	7.13	1.3	12.65	20	1.032				Start Time
8:16	7.36	1.32	12.68	22	1.034				clear
8:21	7.38	1.35	12.68	25	1.033				clear
8:25	7.38	1.34	12.65	30	1.03	5		4.73	clear
MINUTES							**TOTAL LITERS**		
13.0	0.02	1.49%	0.00%	8.00	0.00%		**0.00**		

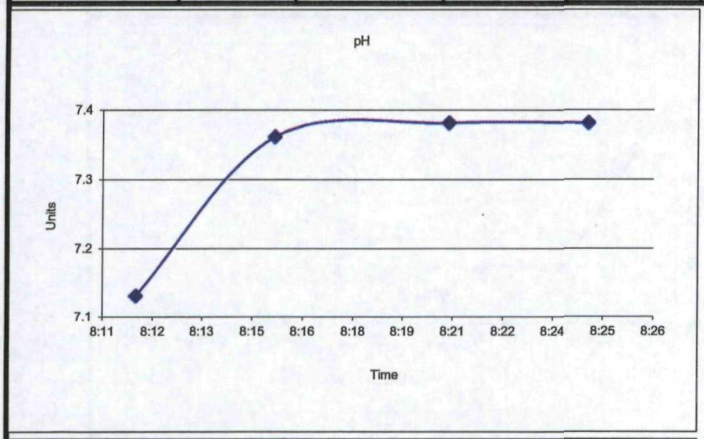

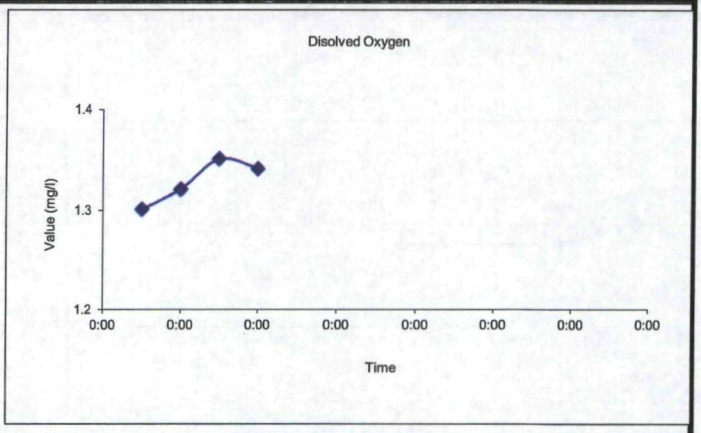

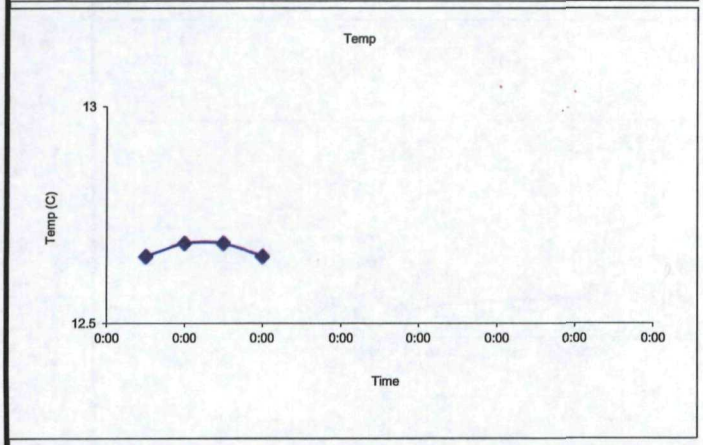

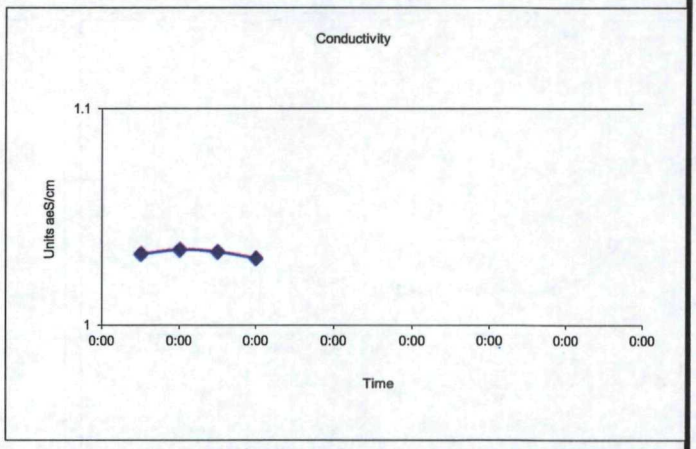

Remarks: (well condition, maintenance, etc...)

limited access - bailed well

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	88	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 206A**
Casing Stickup (Ft.)	-0.36	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	23-Nov-12
Total Well Depth (Ft.) TOC	90.24	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	6.81	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	83.43	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2012		

FIELD PURGE MONITORING

Time HHMMSS	pH Units	DO mg/l	Temp øC	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
							0	6.81	Static
15:33	7.5	1.12	11.15	-72	0.943		450		Start Time
15:37	7.49	1.1	11.13	-48	0.911		450		clear
15:41	7.48	1.08	11.12	-45	0.909		450		clear
15:44	7.48	1.08	11.12	-35	0.908		450	6.80	clear
15:48	7.48	1.08	11.12	-33	0.908		450		clear
15:52	7.48	1.07	11.12	-32	0.907		450	6.80	clear
15:55	7.48	1.07	11.12	-35	0.906	65	450		clear
MINUTES							**TOTAL LITERS**		
22.0	0.00	-0.93%	0.00%	-2.00	0.00%		**9.90**		

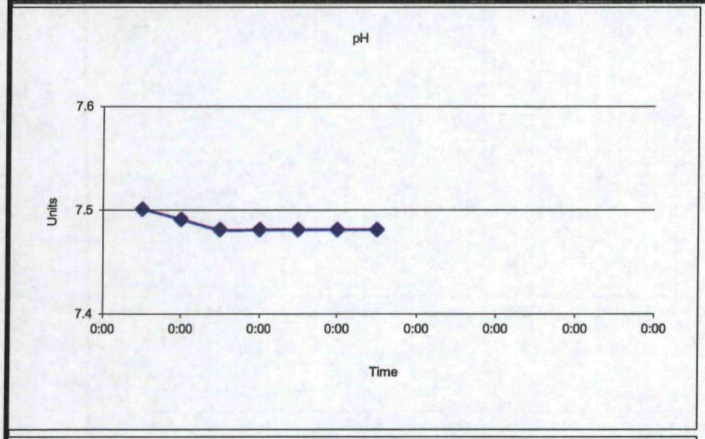

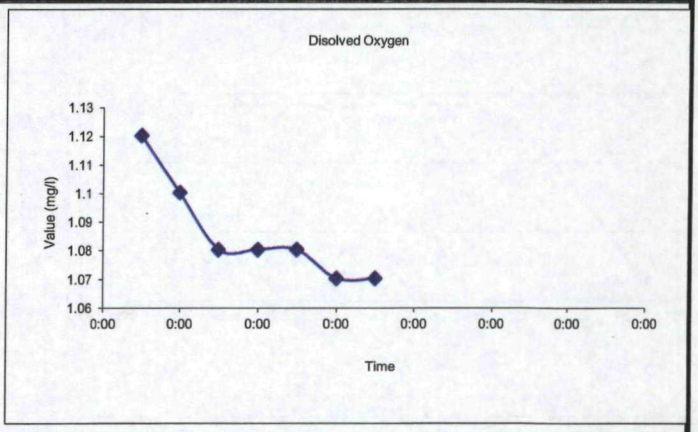

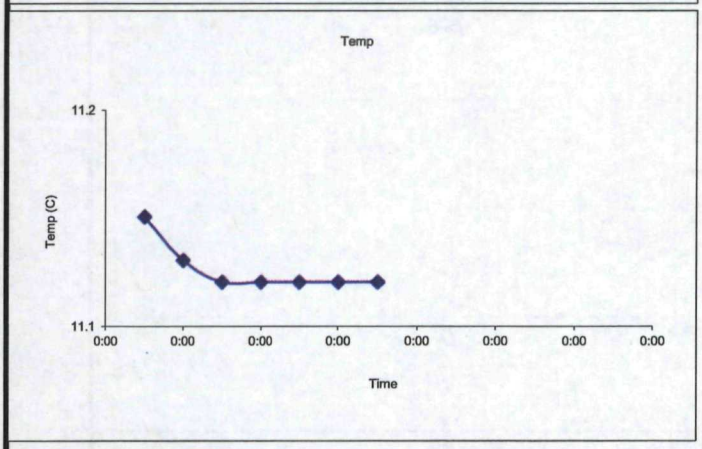

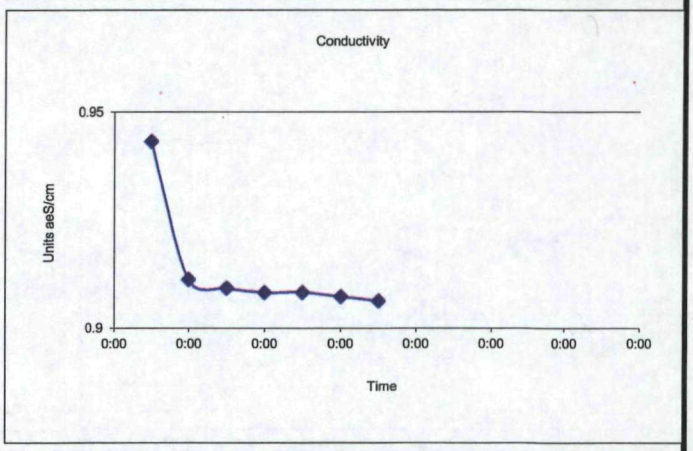

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	127	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 206B**
Casing Stickup (Ft.)	-0.45	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	23-Nov-12
Total Well Depth (Ft.) TOC	129.94	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	4.73	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	125.21	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2012		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	mS/cm	FTU	mL/min	(Ft.) TOC	
							0	4.73	Static
14:57	7.71	0.92	11.67	-89	0.869		500		Start Time
15:00	7.7	0.76	11.27	-88	0.888		500		clear
15:02	7.71	0.71	11.27	-91	0.892		500		clear
15:05	7.7	0.7	11.25	-91	0.892		500	4.73	clear
15:09	7.7	0.68	11.25	-93	0.892		500		clear
15:13	7.69	0.68	11.25	-93	0.891		500	4.73	clear
15:17	7.68	0.66	11.25	-94	0.891		500		clear
15:20	7.68	0.66	11.25	-94	0.890	3	500	4.73	clear
MINUTES						**TOTAL LITERS**			
23.0	-0.01	-3.03%	0.00%	-1.00	0.00%		**11.50**		

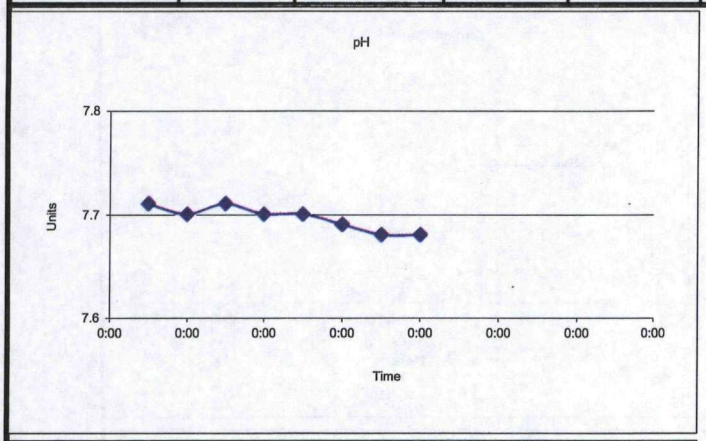

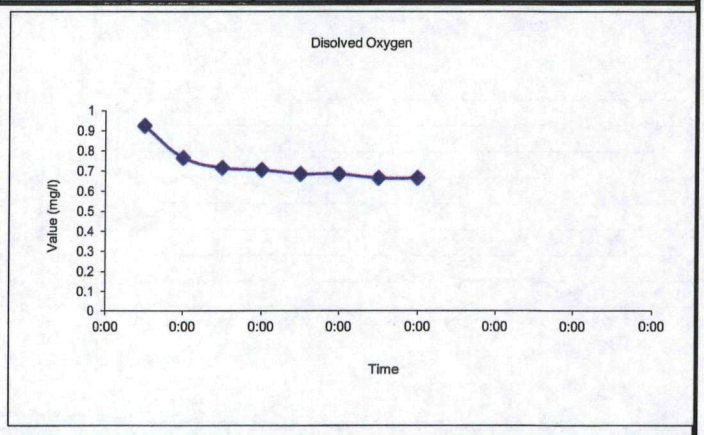

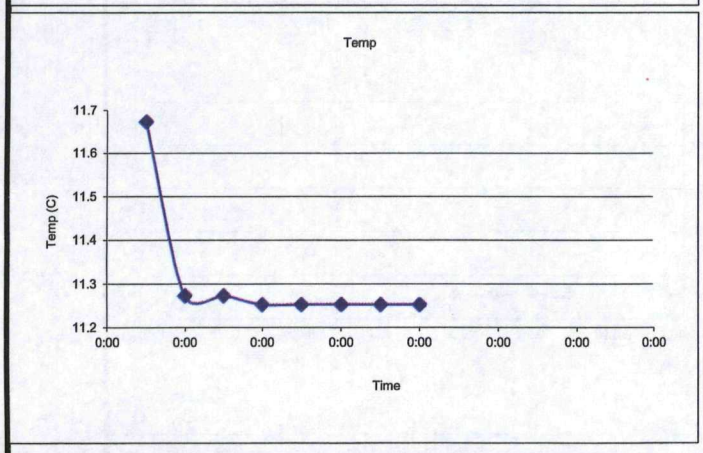

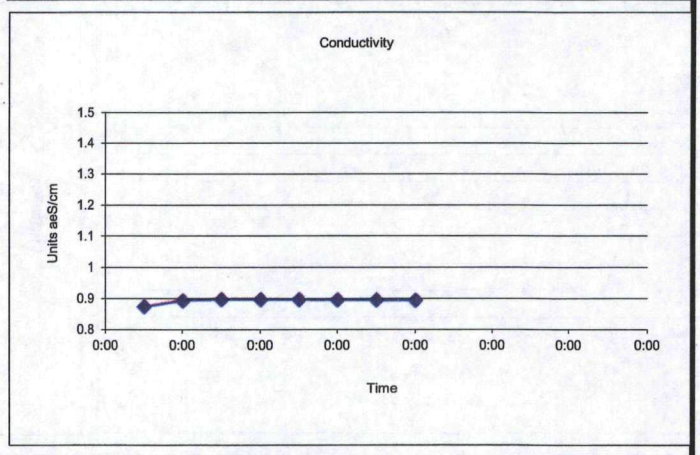

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	249	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 206C**
Casing Stickup (Ft.)	-0.55	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	23-Nov-12
Total Well Depth (Ft.) TOC	251.31	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	5.00	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	246.31	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2012		–

FIELD PURGE MONITORING

Time HHMMSS	pH Units	DO mg/l	Temp øC	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
							0	5.00	Static
14:35	7.74	0.88	11.78	-86	0.744		500		clear
14:38	7.65	0.78	11.75	-90	0.728		500		clear
14:41	7.61	0.69	11.75	-92	0.706		500	5.00	clear
14:44	7.62	0.68	11.75	-93	0.706		500		clear
14:48	7.62	0.68	11.75	-93	0.705		500		clear
14:52	7.62	0.68	11.75	-95	0.705	8	500	5.00	clear
MINUTES							**TOTAL LITERS**		
17.0	0.00	0.00%	0.00%	-2.00	0.00%		**8.50**		

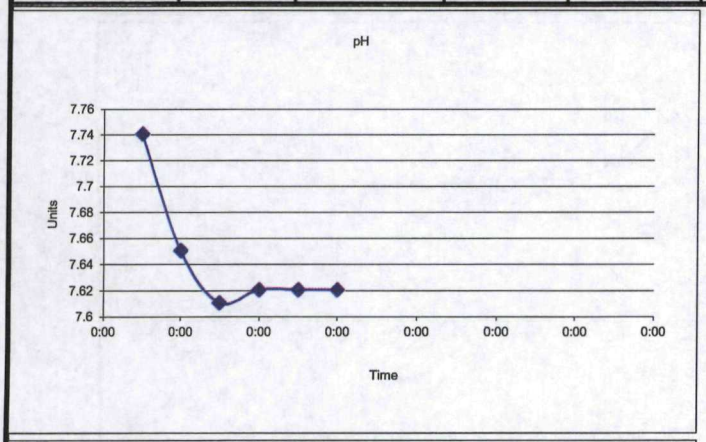

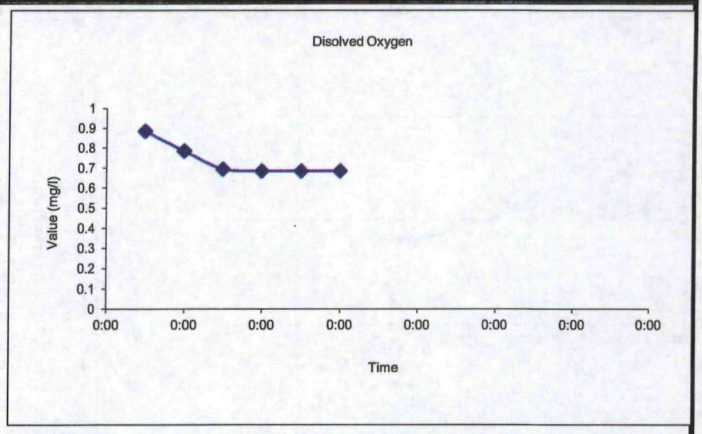

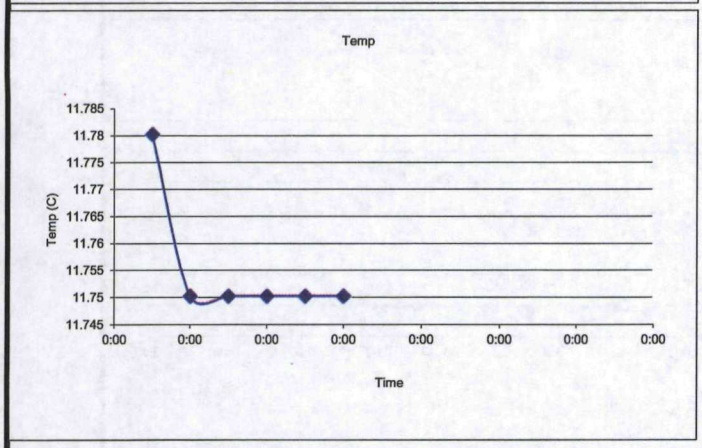

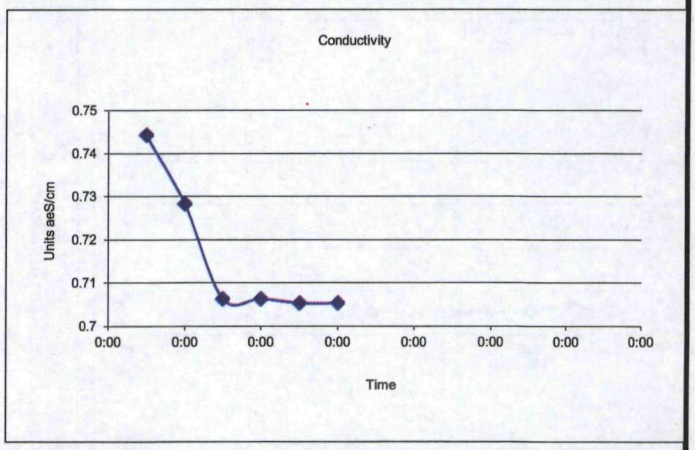

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	88	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 207**
Casing Stickup (Ft.)	-0.3	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	30-Nov-12
Total Well Depth (Ft.) TOC	90.81	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	36.47	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	54.34	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2012		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	mS/cm	FTU	mL/min	(Ft.) TOC	
							0	36.47	Static
13:21	7.62	5.25	11.97	22	1.091		490	36.61	redish brown cloudy
13:25	7.6	5.26	11.97	20	1.099		490		redish brown cloudy
13:30	7.61	5.26	11.96	16	1.132		490		slightly cloudy
13:34	7.61	5.26	11.96	10	1.13		490	36.62	slightly cloudy
13:37	7.62	5.27	11.96	12	1.131		490		clear
13:41	7.62	5.27	11.96	12	1.131	195	490	36.62	sample
MINUTES							**TOTAL LITERS**		
20.0	0.01	0.19%	0.00%	2.00	0.00%		**9.80**		

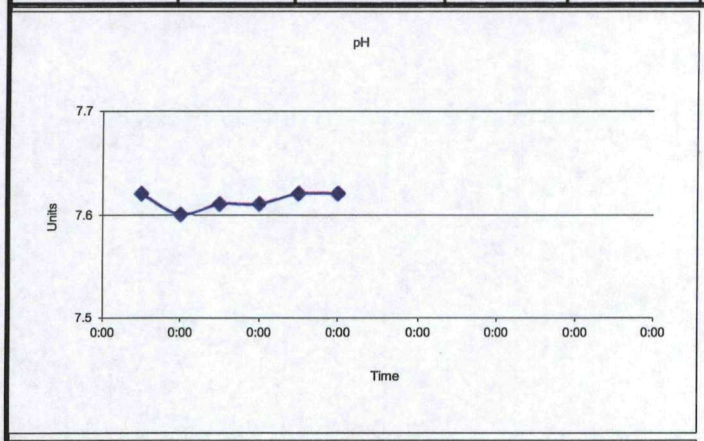

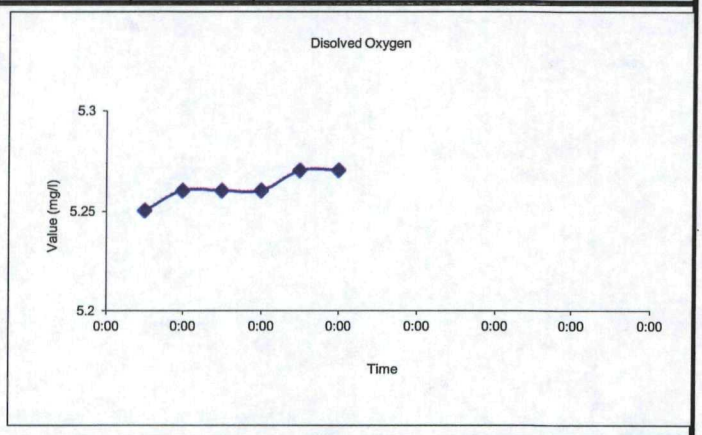

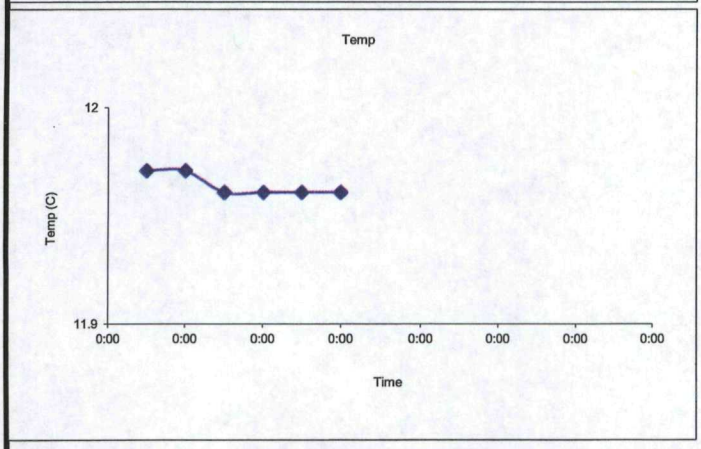

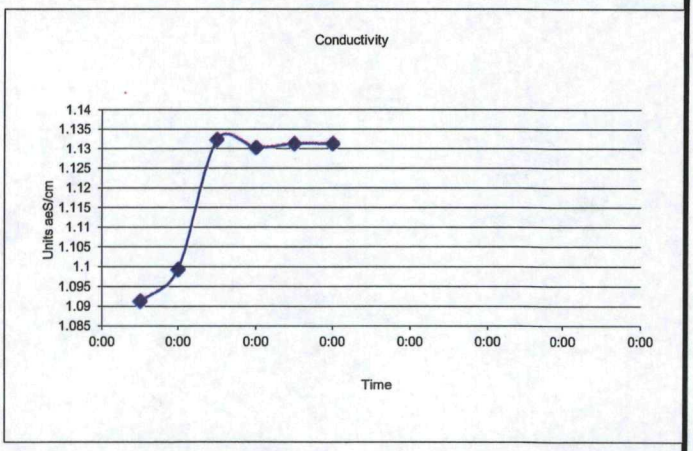

Remarks: (well condition, maintenance, etc...)
