W-1

E & E Drilling and Testing Co., Inc.

FIELD LOG OF BORING AND WELL INSTALLATION

PROJECT NUMBER AND NAME: TDD#R-10-8410-14 Resource Recovery Corp.	BORING/WELL No.: EE-1
PROJECT MANAGER: Andrew Hafferty	SURFACE ELEVATION: DEPTH OF HOLE: 88'
LOGGED BY: Randall S. Holtz	
BORING DIAMETER: 4" WELL DIAMETER: 2"	CASING MATERIAL: Stainless Steel
BORING METHOD: Hollow Stem Augers	FIELD CHEMIST: N/A
HAMMER WT. (lbs): N/A	DRILLER: Boyles Brothers
DROP (inches): N/A	START TIME: 7:20 PST COMPLETION TIME: 9:30 PST DATE: 8/2/85 DATE: 8/2/85

SAMPLING RECORD

SAMPLE NUMBER	SAMPLE INTERVAL	TYPE OF ANALYSIS			
		OVA	HNu	pH	Cond.
	No readings recorded				

MATERIALS RECORD

DESCRIPTION	QUANTITY
TOTAL BORING (FT)	88'
TOTAL CORING (FT)	N/A
NUMBER OF SPLIT SPOON SAMPLES	N/A
TOTAL CASING (FT)	69'
TOTAL SCREEN (FT)	22'
NUMBER OF CAPS AND/OR PLUGS	1
SAND-L.F. No.	27'
BENTONITE-L.F. No.	48'
CEMENT-L.F. No.	13'
SECURITY CAP (Y OR N)	Y
WELL DEVELOPMENT (Y OR N)	Y

LOCATION DIAGRAM:

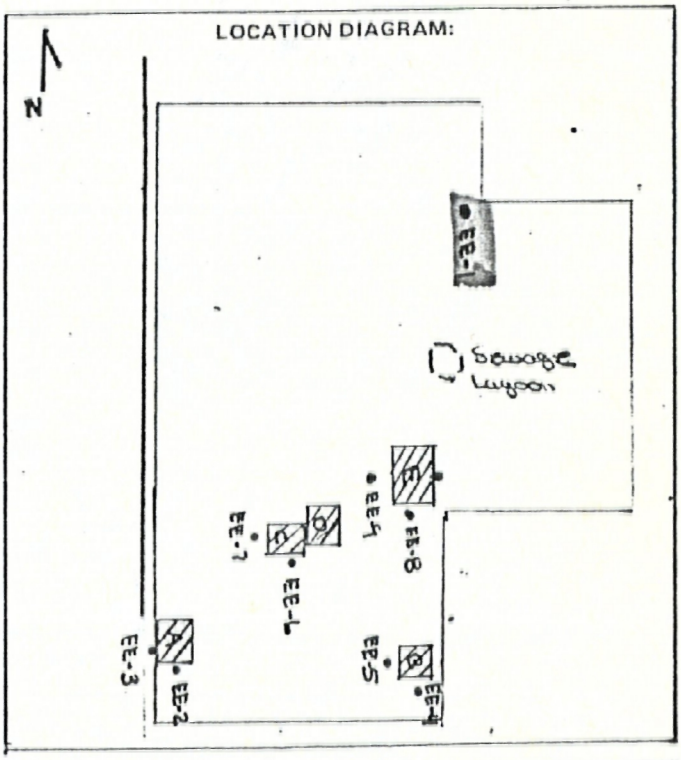

*All times are in Pacific Standard Time

USEPA SF
1452438
