US EPA RECORDS CENTER REGION 5
460820

NATIONWIDE ENVIRONMENTAL SERVICES, INC.

6th Avenue West Business Park
14818 W 6th Ave. Suite 5A
Golden, CO 80401

July 8, 2011

Mr. Tim Drexler
Remedial Project Manager
U.S. Environmental Protection Agency
77 West Jackson Boulevard, HSRM-6J
Chicago, IL 60604

Mr. Doyle W. Wilson
Illinois Environmental Protection Agency
1021 North Grand Avenue East
P.O. Box 19276
Springfield, IL 62794-9276

RE: Southeast Rockford Ground Water NPL Site
Ground Water Monitoring Report-November 2010 Monitoring Event

Gentlemen:

Nationwide Environmental Services, Inc. (NES) is submitting the revised semi-annual monitoring report presenting the analytical data and data interpretation summary for the ground water quality monitoring samples collected at the Southeast Rockford Ground Water NPL Site (the Site) during the November 2010 semi-annual monitoring event. The report was revised to incorporate comments received from USEPA upon review of the original report submittal.

The locations of the monitoring wells comprising the Site ground water monitoring network are shown in Figure 1. The analytical results are summarized in Table 1 and present concentrations for the chemicals of concern (COC) identified in Section VI of the Site Record of Decision (ROD) and for vinyl chloride (VC) reported above the MCL of 2 micrograms per liter (µg/l). The historical analytical results for samples collected from the Site ground water monitoring network, by monitoring well location, are presented in Table 2.

A series of graphs depicting historical total VOC concentrations for select wells are also enclosed. The validated laboratory data sheets and data quality summaries are provided in Appendix A. The field sampling sheets for the current monitoring event are contained in Appendix B.

The general trends occurring at each monitoring location, based on total VOC concentrations are presented below. In brief, evaluation of the historical data for total VOCs indicates the following:

- Total VOC concentrations have generally decreased across the Site since inception of the long-term monitoring program in March 1999. Noted exceptions to this trend or total VOC concentrations differing markedly from historical results or from previous events occur at certain monitoring locations located proximate to, or down-gradient of, identified source areas as presented below.

- **Source Areas 4, 9, 10, & 11**

  - Total VOC concentrations reported at ground water monitoring location MW-113A have been decreasing overall during the past five monitoring events (November 2008 to November 2010). Total VOC concentrations for monitoring well MW-113B have

increased since inception of the semi-annual monitoring program in 1999, but have generally been stable for the past several years (2008 to present).

- Total VOC concentrations reported at ground water monitoring location MW-114A decreased since inception of the groundwater monitoring program in 1999, but have increased during the last three monitoring events. VOC concentrations at monitoring well location MW-114B have generally been stable at current levels since inception of the groundwater monitoring program in 1999, under the O&M phase of the Site remedy.

- Total VOC concentrations reported at ground water monitoring location MW-130 decreased to concentrations previously reported at this location. The decrease in total VOC concentrations from the previous monitoring event is primarily due to the decrease in the concentration of 1,1,1-trichloroethane (1,1,1-TCA). Overall the trend in this well is decreasing. This monitoring well is located down-gradient of Source Area 4 and future analytical results obtained at this location will be reviewed for any noticeable trend that may be occurring.

- Total VOC concentrations and in particular concentrations of 1,1-DCA reported at monitoring location MW-201 have been decreasing for the past three monitoring events (November 2009 to November 2010). Total VOC concentrations at MW-202 have generally been stable at low levels for the past several monitoring events (October 2007 to November 2010).

- **Source Area 7**

  - The total VOC concentrations reported at ground water monitoring location MW-101A increased since the previous event but are within historical results. The increase is primarily due to an increase in concentrations of cis-1,2-dichloroethene (cis-1,2-DCE), 1,1,1-TCA, and trichloroethene (TCE).

  - The total VOC concentrations reported at ground water monitoring location MW-102A have generally increased over the period November 2006 to November 2010. Total VOC concentrations at monitoring location MW-102B have generally been stable at low levels since inception of the monitoring program in 1999.

  - Review of the analytical data obtained for monitoring location MW-102C over the term of the O&M monitoring program reveals that total VOC concentrations have fluctuated between 20 and 1200 µg/l. The total VOC concentrations have differed markedly from historical results during the last three monitoring events. Analytical results from future monitoring events at this location will be monitored for any noticeable trend in total VOC concentrations.

  - The total VOC concentrations reported at ground water monitoring locations MW-133B have fluctuated during the Site O&M monitoring program period, and continue to remain elevated with respect to previous reported concentrations. Analytical results from future monitoring events at this location will be monitored for continuing trends in total VOC concentrations.

  - The total VOC concentrations reported at ground water monitoring locations MW-133C have an increasing trend, with fluctuations. Analytical results from future monitoring

events at this cluster location will be monitored for any noticeable trend in total VOC concentrations.

- **Rock River**

  - Total VOC concentrations reported at monitoring locations proximate to the Rock River remain generally constant or are decreasing, with the exception of monitoring well MW-119. Analytical results from future monitoring events at this location will be monitored for continuing trends in total VOC concentrations.

  - Analytical results reported for ground water monitoring location MW-206B have been increasing since 2006 with the exception of a decrease in total VOC concentration for the current reporting period.

- The total VOC concentrations reported at the ground water locations proximate to Areas 4 & 7 appear to indicate either a pulsing of VOCs into the system from a fluctuating water table or a continued release of VOCs in these areas.

- The ratios of parent VOC compound concentrations to associated breakdown product concentrations indicate biodegradation, comprising one component of natural attenuation, is occurring at the Site however, degradation products beyond DCE and DCA have generally not been observed.

NES continues to coordinate efforts with IEPA to share ground water data obtained from common monitoring well locations at the Site. However, NES is aware that IEPA sample collection from Site monitoring locations last occurred in 2008. Therefore, no comparative data is presented in this report.

Please contact me at telephone 303-232-2134 if you have any questions regarding the information provided or require any additional information.

Sincerely,

William B. Dotterrer
William B. Dotterrer,
Sr. Project Manager

cc: Nadine Miller, City of Rockford

Enclosures

Figure 1: Southeast Rockford NPL Site Ground Water Monitoring Network and Source Location

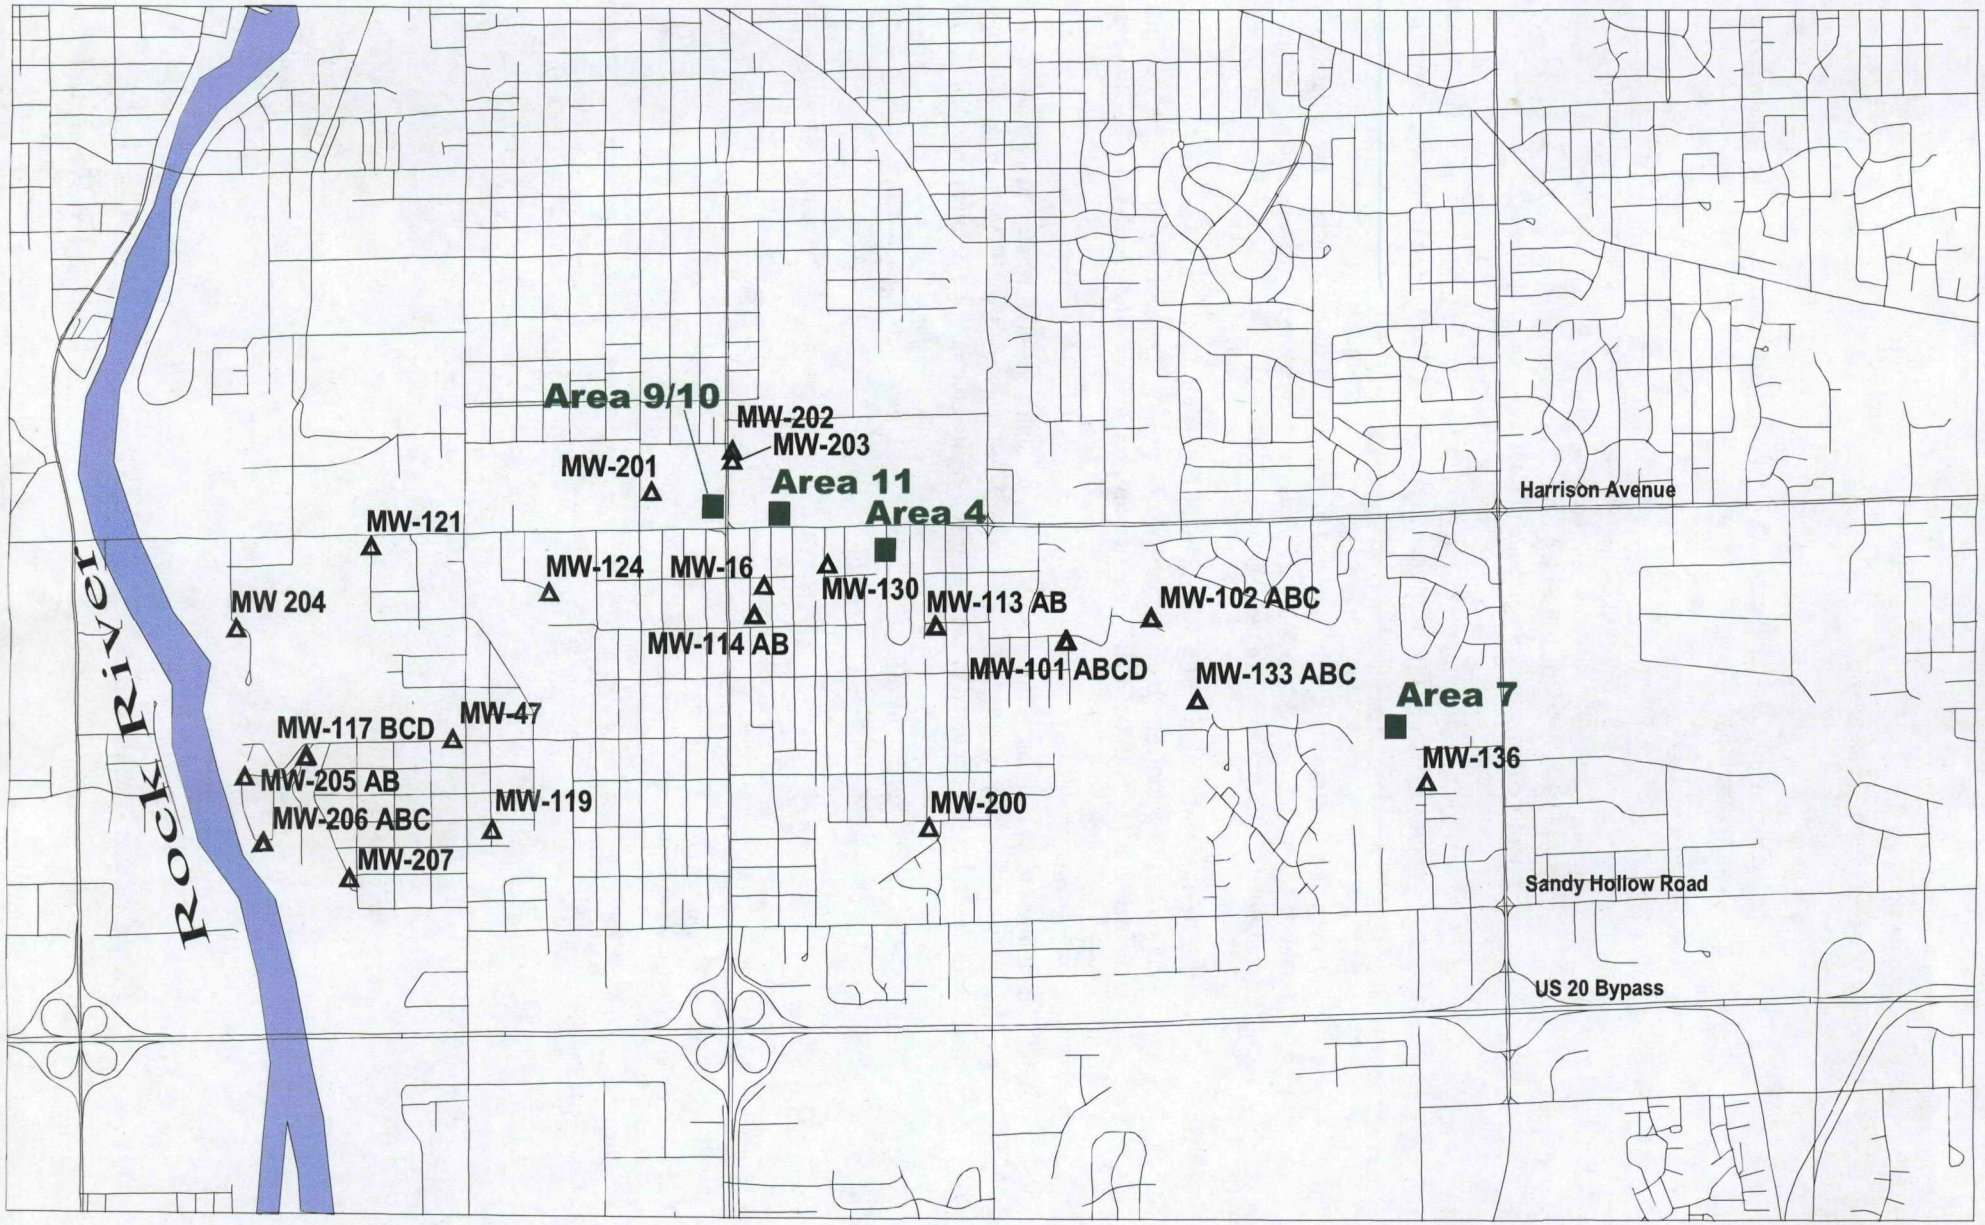

Table 1: Southeast Rockford NPL Site
Summary of Groundwater Analytical Results
Sampling Event #24

Compound	MCL	MW-16 11/27/10	MW-47 11/29/10	MW-101A 11/26/10	MW-101B 11/26/10	MW-101C 11/26/10	MW-101D 11/26/10	MW-102A 11/26/10	MW-102B 11/26/10
Chloroform	N/A	1.4J	1.0U	3.2J	10.0U	1.9J	1.4J	2.0U	1.0U
1,1-Dichloroethane	N/A	78	0.27J	280	130	98	51	99	2.9
1,2-Dichloroethane	5	2.0U	1.0U	10.0U	10.0U	1.8J	1.0J	2.0U	0.67J
1,1-Dichloroethene	7	**24**	1.0U	**68**	**36**	**24**	**18**	3	1.0U
cis-1,2-Dichloroethene	70	45	1.0U	**1100**	**850**	**640**	**320**	**200**	5
trans-1,2-Dichloroethene	100	1.6J	1.0U	18	10.0U	5.0U	0.62J	5.3	1.0U
Methylene Chloride	5	2.0U	1.0U	10.0U	10.0U	5.0U	2.5U	2.0U	1.0U
Tetrachloroethene	5	**10**	1.0U	**36**	**32**	**20**	**17**	2.0U	1.0U
1,1,1-Trichloroethane	200	180	0.3J	**550**	**430**	**310**	160	90	1.0U
Trichloroethene	5	**60**	1.0U	**230**	**77**	**48**	**38**	**20**	1.0U
Vinyl chloride	2	2.0U	1.0U	10.0U	10.0U	5.0U	2.5U	2.0U	1.0U

Compound	MCL	MW-102C 11/27/10	MW-113A 11/28/10	MW-113B 11/28/10	MW-114A 11/27/10	MW-114B 11/27/10	MW-117B 11/24/10	MW-117C 11/24/10	MW-117D 11/24/10
Chloroform	N/A	10.0U	0.95J	2.0U	1.0U	1.0U	0.31J	0.38J	0.34J
1,1-Dichloroethane	N/A	170	85	67	2.8	1.8	11	22	30
1,2-Dichloroethane	5	3.2J	0.7J	0.8J	1.0U	1.0U	1.0U	1.0U	1.0U
1,1-Dichloroethene	7	**51**	**17**	**19**	**8.5**	1	**8.1**	**22**	**16**
cis-1;2-Dichloroethene	70	**720**	**250**	**160**	2.1	2.3	4.6	34	5.6
trans-1,2-Dichloroethene	100	10.0U	11	3	1.0U	1.0U	1.0U	1.0U	1.0U
Methylene Chloride	5	10.0U	2.5U	2.0U	1.0U	1.0U	1.0U	1.0U	1.0U
Tetrachloroethene	5	**21**	**12**	4.2	1.0U	1.0U	**8.4**	**27**	**29**
1,1,1-Trichloroethane	200	110	110	26	65	1.0U	31	53	45
Trichloroethene	5	**68**	**67**	**37**	4.7	**7.8**	**19**	**21**	**17**
Vinyl chloride	2	10.0U	2.5U	**8.8**	1.0U	1.0U	1.0U	1.0U	1.0U

Table 1: Southeast Rockford NPL Site
Summary of Groundwater Analytical Results
Sampling Event #24

Compound	MCL	MW-119 11/26/10	MW-121 11/25/10	MW-124 11/27/10	MW-130 11/27/10	MW-133A 11/27/10	MW-133B 11/27/10	MW-133C 11/27/10	MW-136 11/28/10
Chloroform	N/A	0.46J	0.6J	5.0U	5.0U	1.0U	20U	6.1	0.82J
1,1-Dichloroethane	N/A	1.1	4.6	490	29	0.21J	240	47	1.0U
1,2-Dichloroethane	5	1.0U	1.0U	5.0U	5.0U	1.0U	20U	1.8	1.0U
1,1-Dichloroethene	7	1.0U	2.5	**25**	**8.4**	1.0U	**120**	**46**	1.0U
cis-1,2-Dichloroethene	70	1.1	4.3	**280**	8.3	0.91J	**1900**	**130**	1.0U
trans-1,2-Dichloroethene	100	1.0U	1.0U	5.0U	5.0U	1.0U	11J	0.3J	1.0U
Methylene Chloride	5	1.0U	1.0U	5.0U	5.0U	1.0U	20U	1.0U	1.0U
Tetrachloroethene	5	1.0U	2.1	**14**	5.0U	1.0U	**110**	**10**	1.0U
1,1,1-Trichloroethane	200	1.7	3.4	95	**430**	0.86J	**790**	180	1.0U
Trichloroethene	5	0.42J	**22**	**9.2**	3.6J	1.0U	**180**	**94**	1.0U
Vinyl chloride	2	1.0U	1.0U	**30**	5.0U	1.0U	20U	1.0U	1.0U

Compound	MCL	MW-200 11/28/10	MW-201 11/28/10	MW-202 11/28/10	MW-203 11/28/10	MW-204 11/25/10	MW-205A 11/25/10	MW-205B 11/25/10	MW-206A 11/29/10
Chloroform	N/A	1.0U	1.0U	1.0U	1.0U	0.54J	0.38J	0.41J	0.16J
1,1-Dichloroethane	N/A	1.0U	2.7	1.0U	1.0U	5.3	13	15	13
1,2-Dichloroethane	5	1.0U	1.0U	1.0U	1.0U	1.5	1.0U	1.0U	1.0U
1,1-Dichloroethene	7	1.0U	0.43J	1.0U	1.0U	**11**	**16**	**17**	4.4
cis-1,2-Dichloroethene	70	1.0U	0.75J	1.0U	1.0U	24	18	23	4.5
trans-1,2-Dichloroethene	100	1.0U	1.0U	1.0U	1.0U	1.0U	1.0U	1.0U	1.0U
Methylene Chloride	5	1.0U	1.0U	1.0U	1.0U	1.0U	1.0U	1.0U	1.0U
Tetrachloroethene	5	1.0U	0.93J	2.1	**7.3**	2.5	**23**	**23**	1.5
1,1,1-Trichloroethane	200	1.0U	3.4	0.67J	1.0U	6.4	41	42	9.7
Trichloroethene	5	1.0U	1.2	1.0U	1.0U	**66**	**24**	**24**	4.3
Vinyl chloride	2	1.0U	1.0U	1.0U	1.0U	1.0U	1.0U	1.0U	**3.6**

Table 1: Southeast Rockford NPL Site
Summary of Groundwater Analytical Results
Sampling Event #24

Compound	MCL	MW-206B 11/29/10	MW-206C 11/29/10	MW-207 11/25/10	MW-102A (d) 11/26/10	MW-133A (d) 11/27/10
Chloroform	N/A	0.92J	1.0U	0.22J	2.0U	1.0U
1,1-Dichloroethane	N/A	78	3.9	1.3	95	1.0U
1,2-Dichloroethane	5	2.3	1.0U	1.0U	2.0U	1.0U
1,1-Dichloroethene	7	**71**	3.1	0.72J	2.7	1.0U
cis-1,2-Dichloroethene	70	**72**	5.1	1.3	**200**	0.79J
trans-1,2-Dichloroethene	100	0.53J	1.0U	1.0U	4.9	1.0U
Methylene Chloride	5	1.0U	1.0U	1.0U	2.0U	1.0U
Tetrachloroethene	5	**5.5**	1.0U	2.2	2.0U	1.0U
1,1,1-Trichloroethane	200	55	1.0U	3	87	0.82J
Trichloroethene	5	**34**	**16**	**6**	**19**	1.0U
Vinyl chloride	2	1.1	1.0U	1.0U	2.0U	1.0U

(d) Field duplicate

All units in micrograms per liter (µg/l) or parts per billion (ppb)

Bold value and outlined cell denotes analytical result > than MCL

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-16	06/01/99		3	76	1.2	24	140	1.8	2 U	5.4	170	64
MW-16	10/26/99		2.3 J	73	10 U	23	130	2.5 J	20 U	5.2 J	170	65
MW-16	01/31/00		2.3 J	75	10 U	2.2 J	120	16	20 U	5.9 J	170	68
MW-16	04/24/00		2.5 J	79	5 U	2 J	130 E	16	10 JB	5.7	170 E	65
MW-16	04/24/00	Dilution	50 DJB	75 D	50 U	50 U	130 D	17 DJ	100 DJB	5.3 DJ	160 D	62 D
MW-16	07/27/00		2.7	75	10 U	3.8	130	12	20 U	5.2	160	58
MW-16	11/13/00		2.2	87	10 U	20	150	2.8	20 U	5	140	55
MW-16	04/12/01		2.3	74	10 U	3.1	150	14	20 U	5.8	180	64
MW-16	10/31/01		2.5	88	10 U	10 U	160	22	20 U	7.1	210	72
MW-16	04/25/02		2.3	70	10 U	15	170	6.7	20 U	6.6	150	62
MW-16	10/15/02		20 U	130	20 U	98	240	22	40 U	20 U	240	91
MW-16	04/23/03		2.51	95.6 E	1.08	24.2	244 E	15.7	2 U	9.74	237 E	97.6 E
MW-16	04/23/03	Dilution	20 U	75.6	20 U	24.6	200	20 U	40 U	20 U	172	75.3
MW-16	12/26/03		2.48	93.9 E	1 U	32.2 E	209 E	13.9	1 U	9.45	208 E	77.8 E
MW-16	12/26/03	Dilution	10 U	93.9 D	10 U	31.7 D	247 D	10 U	10 U	9.14 JD	221 D	92.7 D
MW-16	12/26/03	Fld Dupe	10 U	96.3 E	10 U	34.5 E	227 D	10 U	10 U	7.88 JD	182 D	72.5 D
MW-16	04/28/04		20 U	100	20 U	30.1	254	20 U	40 U	20 U	202	77.3
MW-16	05/21/05		1.8	91	1 U	28	230	5.6	2 U	6.5	160	65
MW-16	10/20/05		1.8	91	1 U	28	230	5.6	2 U	6.5	160	65
MW-16	05/08/06		2	94	1 U	27	290	7.3	2 U	9.1	170	78
MW-16	01/04/07		5	94	5 U	24	280	5	10 U	5.3	160	63
MW-16	10/08/07		2	100	1	28	260	14	2 U	8	140	61
MW-16	05/17/08		20 U	130	20 U	39	320	20 U	40 U	20 U	170	78
MW-16	12/18/08	Dilution	1.3 J	100	1 J	2 U	240	35	0.7 J	4.6	120	56
MW-16	06/20/09	Dilution	1.6 J	110	2 U	2 U	39	6.8	2 U	5.5	170	42
MW-16	11/28/09	Dilution	1.6 J	110	2 U	7.9	56	6.9	0.88 J	6.1	180	55
MW-16	06/25/10		1.4	93	0.21 J	21	51	3.8	1 U	8.7	200	58
MW-16	11/27/10	Dilution	1.4 J	78	2 U	24	45	1.6 J	2 U	10	180	60

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-47	06/01/99		1 U	1.1	1 U	0.49	1.3	1 U	2 U	0.53	3.5	2.8
MW-47	10/27/99		1 U	1.1	1 U	0.87 J	4.5	0.05 J	2 U	2.2	6.5	5.7
MW-47	02/17/00		1 U	0.32 J	1 U	0.1 J	0.18 J	1 U	2 U	0.27 J	1	0.58 J
MW-47	04/18/00		1 U	0.53 J	1 U	0.18 J	0.36 J	1 U	2 U	0.27 J	1	0.66 J
MW-47	07/27/00		1 U	0.61	1 U	0.13	0.38	1 U	2 U	0.64	1.2	0.82
MW-47	11/08/00		0.17	0.55	1 U	0.1	0.25	1 U	2 U	0.45	0.58	0.37
MW-47	04/10/01		0.28	0.57	1 U	1	0.31	1 U	2 U	0.48	1.1	0.56
MW-47	10/31/01		0.92	0.21	1 U	1 U	1 U	1 U	2 U	0.38	0.34	0.25
MW-47	04/30/02		1.3	0.13	1 U	1 U	0.13	1 U	2 U	0.33	0.23	0.27
MW-47	10/17/02		1	1 U	1 U	1 U	1 U	1 U	0.6	1 U	1 U	1 U
MW-47	04/22/03		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	0.67 J	1 U
MW-47	12/28/03		1 U	1 U	1 U	0.51 J	1 U	1 U	1 U	0.77 J	0.59 J	1 U
MW-47	04/28/04		1 U	0.54	1 U	1 U	1 U	1 U	2 U	1 U	0.91	0.58
MW-47	05/21/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1.4	1 U
MW-47	06/28/06		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-47	01/05/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-47	10/08/07		1 U	2	1 U	0.9	2	1 U	2 U	0.6	3	1
MW-47	05/17/08		1 U	1	1 U	1 U	1	1 U	2 U	1 U	4	1
MW-47	11/29/08		1 U	1.6	1 U	1 U	0.93 J	1 U	1 U	0.62 J	2.91	1.17
MW-47	11/29/08	Fld Dupe	0.15 J	1.58	1 U	0.34 J	0.96 J	1 U	1 U	0.61 J	2.89	1.15
MW-47	06/20/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U
MW-47	11/28/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U
MW-47	06/24/10		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U
MW-47	11/29/10		1 U	0.27 J	1 U	1 U	1 U	1 U	1 U	1 U	0.3 J	1 U

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-101A	04/20/99		7.3	230	3.4	63	540	9.3	2 U	16	580	200
MW-101A	10/25/99		5.6 J	240	50 U	64	620	7 J	100 U	14 J	610	220
MW-101A	01/27/00		6.2 J	270	50 U	61	690	40 J	100 U	15 J	740	270
MW-101A	04/25/00		7 JB	240	50 U	65	720	7.8 J	100 JB	50 U	690	220
MW-101A	07/26/00		6.1	210	20 U	51	730	10	40 U	4.4	620	140
MW-101A	11/16/00		6.3	310	50 U	77	830	8.3	100 U	15	740	250
MW-101A	04/13/01		5.6	240	50 U	81	780	8.6	100 U	14	830	270
MW-101A	10/30/01		6.3	300	50 U	79	990	12	100 U	15	1000	300
MW-101A	04/22/02		6.8	250	50 U	82	1000	11	100 U	18	890	280
MW-101A	10/10/02		100 U	370	100 U	440	1200	100 U	200 U	64	1200	340
MW-101A	04/23/03		6.28	320 E	1 U	125 E	1080 E	19.4	2 U	26.8 E	919 E	427 E
MW-101A	04/23/03	Dilution	100 U	266	100 U	81.8 J	1110	100 U	200 U	100 U	909	309
MW-101A	12/26/03		8.18	313 E	3.83	128 E	1080 E	21.8	1 U	51.7 E	796 E	344 E
MW-101A	12/26/03	Dilution	100 U	268 D	100 U	101 D	1260 D	100 U	100 U	100 U	950 D	278 D
MW-101A	04/28/04		100 U	265	100 U	98.1	1230	100 U	200 U	56.4	1040	302
MW-101A	05/21/05		10 U	260	10 U	89	1100	13	20 U	80	850	250
MW-101A	01/12/06		4.5	220	5 U	37	990	44	10 U	61	800	220
MW-101A	05/08/06		4.4	25 U	1 U	76	1100	17	2 U	93	970	270
MW-101A	01/04/07		10 U	180	10 U	48	840	21	20 U	56	820	190
MW-101A	10/07/07		4	220	2	38	790	72	2 U	67	590	200
MW-101A	05/17/08		50 U	260	50 U	100	1000	50 U	100	64	740	240
MW-101A	11/28/08	Dilution	4.1 J	233	2.15 J	57.5	908	38.4	1.8 J	56.2	691	214
MW-101A	06/10/09	Dilution	4.3 J	230	2 J	50	870	30	5 U	56	550	190
MW-101A	11/27/09	Dilution	5.2 J	280	10 U	70	990	36	10 U	47	550	220
MW-101A	06/28/10	Dilution	2 U	54	2 U	15	210	6	2 U	6.8	90	38
MW-101A	06/28/10	Fld Dupe	2 U	51	2 U	14	200	5.3	2 U	6.3	86	37
MW-101A	11/26/10	Dilution	3.2 J	280	10 U	68	1100	18	10 U	36	550	230

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-101B	04/20/99		3.6	150	10 U	36	520	10 U	20 U	45	690	140
MW-101B	10/25/99		3.6 J	140	25 U	38	430	3.2 J	50 U	47	580	150
MW-101B	01/27/00		50 U	140	50 U	33 J	490	50 U	100 U	42 J	570	150
MW-101B	04/25/00		4.5 J	150	50 U	37 J	510	5.2 J	100 JB	33 J	590	140
MW-101B	07/26/00		4.4	150	20 U	41	700	4	40 U	39	750	140
MW-101B	11/16/00		3.3	170	25 U	35	550	3.9	50 U	18	450	120
MW-101B	04/13/01		50 U	140	50 U	42	570	50 U	100 U	39	620	160
MW-101B	10/30/01		3.5	150	25 U	33	580	4	50 U	21	440	140
MW-101B	04/22/02		4.4	140	50 U	37	630	4.4	3.3	48	580	140
MW-101B	10/10/02		50 U	230	50 U	290	850	50 U	100 U	80	840	180
MW-101B	04/23/03		3.62	202 E	1 U	66 E	891 E	11.7	2 U	67.1 E	753 E	206 E
MW-101B	04/23/03	Dilution	50 U	162	50 U	45 J	795	50 U	100 U	50.7	656	160
MW-101B	12/26/03		4.11	222 E	1 U	70.1 E	893 E	13	1 U	68 E	671 E	180 E
MW-101B	12/26/03	Dilution	100 U	188 D	100 U	100 U	963 D	100 U	100 U	100 U	696 D	148 D
MW-101B	04/28/04		50 U	226	50 U	59.4	1140	50 U	100 U	61.8	843	174
MW-101B	05/21/05		10 U	200	10 U	50	920	10 U	20 U	47	610	130
MW-101B	01/12/06		5 U	200	5 U	42	890	6.3	10 U	41	570	120
MW-101B	05/08/06		10 U	230	10 U	52	1100	10 U	20 U	50	660	130
MW-101B	01/04/07		10 U	210	10 U	46	950	10 U	20 U	46	620	120
MW-101B	10/07/07		2	200	2	47	790	12	2 U	44	460	110
MW-101B	05/17/08		50 U	240	50 U	64	960	50 U	100	52	560	130
MW-101B	11/28/08	Dilution	2.4 J	181	1.75 J	36.2	760	7.45	1.35 J	41.1	438	96.3
MW-101B	06/10/09	Dilution	3.1 J	160	1.8 J	31	750	7.1	5 U	36	390	81
MW-101B	11/27/09	Dilution	2.6 J	170	5 U	37	840	8.4	5 U	37	400	81
MW-101B	06/28/10	Dilution	10 U	130	10 U	35	790	9 J	10 U	32	320	70
MW-101B	11/26/10	Dilution	10 U	130	10 U	36	850	10 U	10 U	32	430	77

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-101C	04/20/99		3.5	140	10 U	34	550	10 U	20 U	45	740	140
MW-101C	10/25/99		3 J	110	25 U	31	380	2.5 J	50 U	42	480	130
MW-101C	01/27/00		20 U	110	20 U	28	370	2.8 J	40 U	42	460	120
MW-101C	04/25/00		3.9 J	120	50 U	28 J	420	3.5 J	100 JB	31 J	450	100
MW-101C	07/26/00		3.6	110	20 U	25	390	2.7	40 U	21	390	82
MW-101C	11/13/00		2.6	130	25 U	24	420	2.7	50 U	34	370	100
MW-101C	04/12/01		2.5	100	25 U	27	420	3	50 U	37	450	110
MW-101C	10/30/01		2.9	120	25 U	21	510	11	50 U	32	470	110
MW-101C	04/22/02		3.2	120	25 U	31	570	4.2	50 U	41	490	120
MW-101C	10/10/02		50 U	200	50 U	200	660	50 U	28	150	650	130
MW-101C	04/23/03		3	157 E	1 U	44.3 E	750 E	12.1	2 U	42 E	602 E	152 E
MW-101C	04/23/03	Dilution	50 U	125	50 U	35.8 J	626	50 U	100 U	36.7 J	489	121
MW-101C	12/30/03		3.64	193 E	1 U	57.2 E	782 E	32.5 E	1 U	63.2 E	644 E	175 E
MW-101C	12/30/03	Dilution	50 U	141 D	50 U	42.4 JD	775 D	50 U	50 U	44.7 JD	628 D	142 D
MW-101C	11/26/08	Dilution	2.45 J	157	2.05 J	33.8	682	6.8	1.5 J	27.9	398	86.4
MW-101C	06/10/09	Dilution	2.6 J	120	5 U	22	550	5.8	5 U	24	270	56
MW-101C	11/27/09	Dilution	2.4 J	120	5 U	28	620	5.5	5 U	25	290	63
MW-101C	06/28/10	Dilution	5 U	85	5 U	23	570	5.4	5 U	19	220	44
MW-101C	11/26/10	Dilution	1.9 J	98	1.8 J	24	640	5 U	5 U	20	310	48

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-101D	04/21/99		2.6	80	5 U	24	230	5 U	10 U	23	300	80
MW-101D	01/27/00		1.6 J	42	10 U	14	130	1.5 J	20	18	180	54
MW-101D	04/25/00		2.4 JB	70	20 U	23	250	1.9 J	40 JB	23	270	81
MW-101D	07/26/00		2.5	60	1.2	14	180	1.1	20 U	2.9	180	33
MW-101D	11/16/00		2.2	76	1.3	17	210	1.3	20 U	3.8	180	46
MW-101D	04/13/01		2.2	66	10 U	21	250	1.9	20 U	18	250	73
MW-101D	10/30/01		2.3	70	20 U	22	260	2	40 U	26	300	80
MW-101D	04/30/02		2.5	66	20 U	22	260	2	40 U	20	240	67
MW-101D	10/10/02		20 U	100	20 U	94	280	20 U	40 U	20 U	300	58
MW-101D	04/23/03		2.17	72.1 E	1 U	28.2 E	323 E	5.34	2 U	24.8	297 E	82.6 E
MW-101D	04/23/03	Dilution	20 U	64.7	20 U	23.9	291	20 U	40 U	23	254	73.7
MW-101D	04/23/03	Fld Dupe	50 U	127	50 U	35.6 J	744 E	50 U	2 U	40.7 E	500	151 E
MW-101D	12/28/03		1.87	47 E	0.88 J	19.8	184 E	8.27	1 U	19.2	202 E	58.3 E
MW-101D	12/28/03	Dilution	10 U	41.8 D	10 U	17.6 D	179 D	10 U	10 U	16 D	168 D	51.6 D
MW-101D	04/28/04		25 U	68	25 U	22.2	323	25 U	50 U	20.7	249	62.3
MW-101D	05/21/05		2	74	1 U	28	330	1 U	2 U	22	230	61
MW-101D	01/12/06		2 U	53	2 U	5	85	2 U	4 U	14	190	20
MW-101D	06/23/06		10 U	77	10 U	24	410	10 U	20 U	20	220	56
MW-101D	01/04/07		5	56	5 U	16	200	5 U	10 U	15	180	46
MW-101D	10/07/07		10 U	55	10 U	22	240	10 U	10 U	18	180	50
MW-101D	05/17/08		10 U	98	10 U	35	420 E	10 U	18 J	26	250 E	70
MW-101D	05/17/08	Dilution	25 U	81 D	25 U	28 D	380 D	25 U	50 U	25 U	220 D	60 D
MW-101D	11/28/08	Dilution	1.46 J	41.6	0.58 J	15	199	1.94 J	0.62 J	16.4	137	39.3
MW-101D	06/10/09	Dilution	1.8 J	68	0.86 J	19	340	3.6	2 U	20	180	47
MW-101D	11/27/09	Dilution	1.5 J	64	2.5 U	18	290	4.1	2.5 U	16	150	39
MW-101D	06/28/10	Dilution	2.5 U	44	2.5 U	16	270	3.1	2.5 U	13	110	32
MW-101D	11/26/10	Dilution	1.4 J	51	1 J	18	320	0.62 J	2.5 U	17	160	38

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-102A	05/20/99		1 U	43	0.25	1.2	54	1.8	2 U	0.6	51	6.3
MW-102A	10/25/99		0.15 J	43	5 U	2.5 J	61	1.7 J	10 U	3.1 J	57	15
MW-102A	02/16/00		5 U	64	5 U	2.8 J	90	3 J	10 U	5 U	97	14
MW-102A	04/25/00		5 U	43	5 U	1.5 J	49	1.4 J	10 JB	5 U	57	7.6
MW-102A	04/25/00	Fld Dupe	0.14 J	43	5 U	1.4 J	49	1.3 J	10 JB	5 U	57	7.7
MW-102A	07/26/00		10 U	71	10 U	2.7	95	2.5	20 U	10 U	100	16
MW-102A	11/16/00		5 U	91	5 U	2.8	110	2.7	10 U	5 U	88	14
MW-102A	04/10/01		10 U	91	10 U	4.2	140	4.4	20 U	10 U	120	22
MW-102A	10/17/01		10 U	77	10 U	2.3	110	4.1	20 U	10 U	88	16
MW-102A	04/30/02		5 U	47	5 U	1.6	65	1.9	10 U	5 U	62	11
MW-102A	10/10/02		20 U	130	20 U	20 U	160	20 U	40 U	20 U	140	26
MW-102A	04/25/03		1 U	101 E	1 U	4.17	153 E	5.08	2 U	1 U	123 E	25.7 E
MW-102A	04/25/03	Dilution	10 U	92.9	10 U	10 U	137	10 U	20 U	10 U	102	22.2
MW-102A	12/26/03		1 U	108 E	1 U	4.14	145 E	5.89	1 U	1 U	111 E	20.1
MW-102A	12/26/03	Dilution	10 U	118 D	10 U	10 U	156 D	5.56 JD	10 U	10 U	114 D	22.4 D
MW-102A	04/28/04		2 U	39	2 U	2 U	34.2	1.45	4 U	2 U	37.3	6.93
MW-102A	05/02/05		1 U	19	1 U	1 U	16	0.84	2 U	1 U	19	3.5
MW-102A	11/02/05		1 U	71	1 U	1.9	110	5.1	2 U	1 U	57	11
MW-102A	06/22/06		1 U	39	1 U	0.98	54	1.9	2 U	1 U	31	6.6
MW-102A	11/16/06		1 U	73	1 U	1.8	120	3.3	2 U	1 U	100	15
MW-102A	10/08/07		10 U	64	10 U	4	150	5	9	10 U	95	20
MW-102A	05/19/08		10 U	68	10 U	10 U	150	10 U	20	10 U	93	18
MW-102A	11/26/08		0.18 J	58.1	0.32 J	2.81	137	4.14	1 U	1 U	82.6	17.6
MW-102A	06/11/09		0.19 J	66	0.26 J	2.6	150	4.1	1 U	1 U	82	16
MW-102A	11/27/09		1 U	96	1 U	3.5	190	5.3	1 U	1 U	89	18
MW-102A	06/28/10	Dilution	2 U	80	2 U	2.7	170	5.3	2 U	2 U	62	15
MW-102A	11/26/10	Dilution	2 U	99	2 U	3	200	5.3	2 U	2 U	90	20
MW-102A	11/26/10	Fld Dupe	2 U	95	2 U	2.7	200	4.9	2 U	2 U	87	19

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-102B	05/20/99		1 U	0.99	0 63	0.32	2.1	1 U	2 U	1.1	1 4	2.1
MW-102B	10/25/99		1 U	0.93 J	0.66 J	0.4 J	2.7	1 U	2 U	2	5.1	3.7
MW-102B	02/16/00		1 U	0.32 J	0.47 J	1 U	0.28 J	1 U	2 U	1 U	1 U	1 U
MW-102B	04/25/00		1 U	0.36 J	0 49 J	1 U	0.48 J	1 U	2 U	1 U	0.2 J	0.09 J
MW-102B	07/26/00		1 U	0.62	0.54	1 U	0 54	1 U	2 U	1 U	1 U	1 U
MW-102B	11/16/00		1 U	0.76	1 U	1 U	0 62	1 U	2 U	1 U	1 U	1 U
MW-102B	04/10/01		1 U	0.71	0.61	1 U	0.71	1 U	2 U	1 U	1 U	1 U
MW-102B	10/17/01		1 U	0.83	1 U	1 U	1.2	1 U	2 U	1 U	1 U	1 U
MW-102B	04/30/02		1 U	1	0.58	1 U	1.4	0.13	2 U	1 U	1 U	1 U
MW-102B	10/10/02		1 U	2	1 U	1 U	2	1 U	0.6	1 U	1 U	1 U
MW-102B	04/25/03		1 U	1.35	1 U	1 U	2.27	1 U	2 U	1 U	1 U	1 U
MW-102B	12/26/03		1 U	1.64	0.64 J	1 U	2.9	1 U	1 U	1 U	1 U	1 U
MW-102B	04/28/04		1 U	1.73	0.62	1 U	3.2	1 U	2 U	1 U	1 U	1 U
MW-102B	05/02/05		1 U	1.6	0 48	1 U	2.4	1 U	2 U	1 U	1 U	1 U
MW-102B	11/02/05		1 U	1.9	1 U	1 U	3.5	1 U	2 U	1 U	1 U	1 U
MW-102B	06/22/06		1 U	2.3	1 U	1 U	4 3	1 U	2 U	1 U	1 U	1 U
MW-102B	11/16/06		1 U	3	1 U	1 U	5	1 U	2 U	1 U	1 U	1 U
MW-102B	10/08/07		1 U	3	0 5	1 U	4	1 U	2 U	1 U	1 U	1 U
MW-102B	05/19/08		1 U	4	1 U	1 U	6	1 U	2 U	1 U	1 U	1 U
MW-102B	11/26/08		1 U	2 8	0.66 J	1 U	5.11	0.28 J	1 U	1 U	1 U	1 U
MW-102B	06/11/09		1 U	3.2	0.65 J	1 U	5	1 U	1 U	1 U	1 U	1 U
MW-102B	11/27/09		1 U	3.5	0.56 J	1 U	5.6	1 U	1 U	1 U	1 U	1 U
MW-102B	06/28/10		1 U	3	0.69 J	1 U	4.4	1 U	1 U	1 U	1 U	1 U
MW-102B	11/26/10		1 U	2 9	0.67 J	1 U	5	1 U	1 U	1 U	1 U	1 U

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-102C	05/20/99		2.5	180	4	59	390	10 U	20 U	33	170	140
MW-102C	10/25/99		3 J	210	25 U	78	460	25 U	50 U	46	250	170
MW-102C	02/16/00		0.66 J	32	0.91 J	12	61 E	0.57 J	0.38 J	5.9	60 E	26
MW-102C	02/16/00	Dilution	0.52 DJ	24 D	5 U	9 D	44 D	5 U	10 U	4.4 DJ	44 D	20 D
MW-102C	04/25/00		0.91 J	44	5 U	5.2	65	0.96 J	10 JB	0.67 J	60	10
MW-102C	07/26/00		0.64	29	0.8	4.5	39	0.41	4 U	0.99	44	8.2
MW-102C	11/16/00		0.32	19	2 U	4.5	28	0.26	4 U	1.1	23	8.3
MW-102C	04/10/01		0.94	48	5 U	2.6	39	5 U	10 U	0.8	90	5.4
MW-102C	10/17/01		0.6	29	4 U	8.9	53	0.39	8 U	3.5	46	17
MW-102C	04/30/02		2.1	110	2.4	40	240	3.3	20 U	19	170	78
MW-102C	10/10/02		5 U	56	5 U	54	87	5 U	10 U	4 J	69	20
MW-102C	04/25/03		1.16	83.3 E	1.57	33 E	200 E	4	2 U	16.3	143 E	64.8 E
MW-102C	04/25/03	Dilution	10 U	48.4	10 U	18.6	112	10 U	20 U	7.94 J	73.2	34.9
MW-102C	12/26/03		0.6 J	40.4 E	0.76 J	9.18	69 E	1.04	1 U	1.6	60.2 E	16.3
MW-102C	12/26/03	Dilution	4 U	42.6 D	4 U	9.85 D	79.1 D	4 U	4 U	4 U	59 D	16.2 D
MW-102C	04/28/04		25 U	105	25 U	38.2	278	25 U	50 U	20.9	136	70.4
MW-102C	05/02/05		0.74	69	1.2	0.62	22	1 U	2 U	1.1	110	1.5
MW-102C	11/02/05		1 U	3.4	1 U	1.3	7.4	1 U	2 U	1 U	6.4	2.9
MW-102C	06/22/06		1 U	23	1 U	8.4	49	1 U	2 U	4.9	19	15
MW-102C	11/16/06		1 U	69	1.3	10	120	0.97 J	2 U	4	70	23
MW-102C	10/08/07		0.4	60	1	22	170	2	2 U	10	35	34
MW-102C	05/19/08		10 U	66	10 U	26	210	10 U	21	12	74	37
MW-102C	11/26/08		0.21 J	18.9	0.33 J	5.75	56.6	0.79 J	1 U	2.66	18.4	9.54
MW-102C	06/11/09		0.31 J	36	0.57 J	6.1	99	0.74 J	1 U	0.94 J	23	8.9
MW-102C	11/27/09	Dilution	10 U	210	10 U	59	760	6.7 J	10 U	22	94	74
MW-102C	06/28/10	Dilution	5 U	160	5 U	53	740	6.8	5 U	18	89	65
MW-102C	11/26/10	Dilution	10 U	170	3.2 J	51	720	10 U	10 U	21	110	68

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-113A	05/03/99		0.9	34	0.4	10	52	1.2	2 U	1.9	59	24
MW-113A	11/10/99		2.3 J	100	10 U	27	160	2.4 J	20	3.2 J	160	69
MW-113A	02/15/00		2.1 J	91	10 U	16	160	5.7 J	20 U	2.9 J	160	71
MW-113A	04/24/00		2.1 JB	92	10 U	5.1 J	160	13	20 JB	2.4 J	160	61
MW-113A	07/27/00		2.3	86	10 U	4	110	7.5	20 U	10 U	130	22
MW-113A	11/16/00		2.3	130	10 U	9.4	200	12	20 U	2.1	170	62
MW-113A	04/12/01		2.4	10	10 U	210	210	15	20 U	3.7	200	81
MW-113A	10/31/01		2.8	110	10 U	3	240	22	20 U	3.3	200	75
MW-113A	04/29/02		2.5	100	10 U	1.5	200	23	20 U	4.5	200	70
MW-113A	10/18/02		20 U	190	20 U	240	430	20 U	40 U	20 U	370	140
MW-113A	04/23/03		2.84	139 E	1 U	27.6 E	371 E	18.2	2 U	8.11	306 E	126 E
MW-113A	04/23/03	Dilution	25 U	121	25 U	33.9	325	25 U	50 U	25 U	245	101
MW-113A	12/28/03		2.93	140 E	1.38	38.3 E	345 E	10.4	1 U	9.72	309 E	124 E
MW-113A	12/28/03	Dilution	20 U	109 D	20 U	31.4 D	318 D	20 U	20 U	20 U	232 D	92.9 D
MW-113A	04/28/04		25 U	123	25 U	32.4	360	25 U	50 U	25 U	239	89.1
MW-113A	05/21/05		5 U	140	5 U	45	410	5.7	10 U	8.1	260	100
MW-113A	10/20/05		2.6	110	1 U	22	330	17	2 U	8	210	82
MW-113A	05/08/06		2.3	110	1 U	32	470	9.1	20 U	10	270	93
MW-113A	01/04/07		10 U	110	10 U	27	430	10 U	20 U	10	210	10
MW-113A	10/08/07		2	150	1	46	480	15	2 U	10	260	110
MW-113A	05/17/08		20 U	160	20 U	54	510 E	20 U	41	20 U	280	130
MW-113A	05/17/08	Dilution	40 U	140 D	40 U	48 D	470 D	40 U	80 U	40 U	250 D	110 D
MW-113A	11/29/08	Dilution	2.2 J	135	1.5 J	7.25	369	40.6	1.7 J	10.5	210	98.6
MW-113A	06/11/09	Dilution	2.6 J	110	5 U	21	370	15	5 U	10	180	85
MW-113A	11/28/09	Dilution	1.5 J	110	2.5 U	1.7 J	290	44	2.5 U	12	170	84
MW-113A	06/29/10	Dilution	1.1 J	88	1 J	3.3	240	30	0.85 J	12	130	76
MW-113A	11/28/10	Dilution	0.95 J	85	0.7 J	17	250	11	2.5 U	12	110	67

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-113B	04/29/99		0.54	33	0.56	12	38	0.65	2 U	1.8	17	19
MW-113B	10/27/99		0.45 J	33	5 U	8.4	39	0.55 J	10 U	1.3 J	13	20
MW-113B	02/15/00		0.65 J	48	5 U	11	62	0.83 J	10 U	1.4 J	27	30
MW-113B	04/24/00		0.61 JB	43	5 U	11	56	0.98 J	10 JB	1.2 J	21	26
MW-113B	07/27/00		0.71	38	0.6	9.4	49	0.91	10 U	0.89	17	20
MW-113B	11/16/00		0.63	55	5 U	11	62	1.3	10 U	1.4	22	27
MW-113B	04/12/01		0.56	40	5 U	8.9	53	1	10 U	5 U	17	20
MW-113B	10/31/01		0.64	50	5 U	12	67	1.1	10 U	5 U	24	29
MW-113B	04/29/02		0.6	39	5 U	9.8	60	0.97	10 U	1.3	19	23
MW-113B	10/18/02		10 U	84	10 U	88	120	10 U	5	10 U	39	42
MW-113B	04/23/03		1.05	77.3 E	1 U	23.3	143 E	6.06	2 U	3.77	65.8 E	55.8 E
MW-113B	04/23/03	Dilution	10 U	58.6	10 U	17.4	115	10 U	20 U	10 U	45.6	41.9
MW-113B	12/28/03		0.97 J	71.3 E	1 U	21.4	134 E	4.01	1 U	3.72	53.4 E	52.1 E
MW-113B	12/28/03	Dilution	10 U	65.1 D	10 U	19.1 D	129 D	10 U	10 U	10 U	43.1 D	45.9 D
MW-113B	04/28/04		10 U	70	10 U	19.8	143	10 U	20 U	10 U	44.9	42.7
MW-113B	05/21/05		1 U	64	1 U	19	140	1.8	2 U	2.9	39	39
MW-113B	10/20/05		1 U	78	1 U	22	170	1.9	2 U	3.8	45	47
MW-113B	05/08/06		1 U	64	1 U	21	140	1.9	2 U	3.6	33	37
MW-113B	01/04/07		1 U	61	1 U	20	120	1.7	2 U	3	30	38
MW-113B	10/08/07		0.5	56	0.6	17	120	2	2 U	3	21	30
MW-113B	05/17/08		10 U	66	10 U	19	140	10 U	19 J	10 U	25	34
MW-113B	11/29/08		0.71 J	71.3	0.92 J	20.4	169	2.15	1 U	3.49	28.8	41.5
MW-113B	06/11/09		0.73 J	71	0.87 J	19	180	2.2	1 U	3.6	29	42
MW-113B	11/28/09		0.69 J	77	0.76 J	22	190	2.5	1 U	3.9	31	41
MW-113B	06/29/10	Dilution	2 U	63	2 U	19	150	2.7	2 U	3	19	33
MW-113B	11/28/10	Dilution	2 U	67	0.8 J	19	160	3	2 U	4.2	26	37

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-114A	04/28/99		5 U	6.7	5 U	46	14	5 U	10 U	1.9 J	250	34
MW-114A	10/26/99		0.34 J	7.1 J	25 U	48	11 J	25 U	50 U	25 U	290	47
MW-114A	01/31/00		10 U	5 J	10 U	34	6.6 J	10 U	1.5 J	10 U	220	33
MW-114A	04/24/00		10 U	4.2 J	10 U	26	5.6 J	10 U	20 JB	10 U	160	24
MW-114A	07/27/00		10 U	3.9	10 U	24	5.4	10 U	20 U	10 U	140	22
MW-114A	11/13/00		10 U	4.2	10 U	20	4.7	10 U	20 U	10 U	120	19
MW-114A	04/12/01		5 U	2.7	5 U	18	3.9	5 U	10 U	5 U	120	20
MW-114A	10/31/01		5 U	2.5	5 U	15	3.6	5 U	10 U	5 U	100	18
MW-114A	04/25/02		5 U	3.1	5 U	16	4.1	5 U	10 U	5 U	100	22
MW-114A	10/15/02		10 U	10 U	10 U	140	7	10 U	20 U	10 U	170	38
MW-114A	04/23/03		1 U	3.28	1 U	13.4	4.09	1 U	2 U	1 U	94.6 E	23.5
MW-114A	04/23/03	Dilution	10 U	10 U	10 U	12.9	10 U	10 U	20 U	10 U	80.2	20.8
MW-114A	12/26/03		1 U	2.86	1 U	9.96	3.62	1 U	1 U	1 U	73.9 E	16.3
MW-114A	12/26/03	Dilution	4 U	2.86 JD	4 U	10.3 D	3.6 JD	4 U	4 U	4 U	70.1 D	15.9 D
MW-114A	04/28/04		5 U	3.69	5 U	12	4.25	5 U	10 U	5 U	79.9	20.8
MW-114A	05/21/05		1 U	2.5	1 U	5.7	3.3	1 U	2 U	1 U	28	7.9
MW-114A	10/20/05		1 U	2.6	1 U	7.2	2.9	1 U	2 U	1 U	39	9.8
MW-114A	05/06/06		1 U	3.4	1 U	9.4	3.7	1 U	2 U	1 U	44	12
MW-114A	01/04/07		1 U	3.5	1 U	11	3.3	1 U	2 U	1 U	51	9.6
MW-114A	10/08/07		1 U	2	1 U	7	2	1 U	2 U	2 U	34	5
MW-114A	05/17/08		2 U	2	2 U	5	3	2 U	3 J	2 U	28	4
MW-114A	11/29/08		1 U	0.28 J	1 U	1 U	1 U	1 U	1 U	1 U	1.09	1 U
MW-114A	06/11/09		0.16 J	1 U	1 U	1 U	1 U	1 U	1 U	1 U	0.9 J	1 U
MW-114A	11/28/09		0.46 J	1.9	1 U	3.9	1.3	1 U	1 U	1 U	36	2.7
MW-114A	06/25/10		1 U	3.2	1 U	6.6	2.2	1 U	1 U	1 U	70	4.4
MW-114A	11/27/10		1 U	2.8	1 U	8.5	2.1	1 U	1 U	1 U	65	4.7

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-114B	04/28/99		1 U	0.89	1 U	0.6	3.3	1 U	2 U	1	4	6.2
MW-114B	10/26/99		1 U	1	1 U	0.46 J	3.3	1 U	2 U	0.66 J	1.2	8.2
MW-114B	01/31/00		1 U	0.81 J	1 U	0.18 J	2.3	1 U	2 U	1 U	1 U	5.7
MW-114B	04/24/00		1 U	0.68 J	1 U	0.11 J	1.7	1 U	2 JB	1 U	0.05 J	1.8
MW-114B	07/27/00		1 U	1	1 U	0.26	3	1 U	2 U	1 U	1 U	7.9
MW-114B	11/13/00		1 U	1.2	1 U	0.13	2.4	1 U	2 U	1 U	1 U	3.5
MW-114B	04/12/01		1 U	0.98	1 U	0.26	2.9	1 U	2 U	1 U	1 U	8.2
MW-114B	10/31/01		1 U	0.96	1 U	0.13	2.2	1 U	2 U	1 U	1 U	4.8
MW-114B	04/25/02		1 U	1.1	1 U	0.29	3	0.04	2 U	1 U	1 U	7.2
MW-114B	10/15/02		1 U	2	3	1	3	1 U	0.6	1 U	1 U	9
MW-114B	04/23/03		1 U	1.15	1 U	1 U	2.84	1 U	2 U	1 U	1 U	8.8
MW-114B	12/26/03		1 U	1.25	1 U	1.07	2.98	1 U	1 U	1 U	1 U	8.91
MW-114B	04/28/04		1 U	1.21	1 U	1 U	2.87	1 U	2 U	1 U	1 U	8.82
MW-114B	05/21/05		1 U	1.5	1 U	1 U	2.3	1 U	2 U	1 U	1 U	7.6
MW-114B	10/20/05		1 U	1.6	1 U	1 U	2.3	1 U	2 U	1 U	1 U	8.8
MW-114B	05/06/06		1 U	1 U	1 U	1 U	2.1	1 U	2 U	1 U	1 U	8.7
MW-114B	01/04/07		1 U	1.4	1 U	1 U	1.8	1 U	2 U	1 U	1 U	6.7
MW-114B	10/08/07		1 U	2	1 U	0.5	2	1 U	2 U	1 U	1 U	6
MW-114B	05/17/08		1 U	2	1 U	1 U	2	1 U	2 U	1 U	1 U	9
MW-114B	12/18/08		1 U	1.6	1 U	0.67 J	2	1 U	1 U	1 U	1 U	6.8
MW-114B	06/20/09		1 U	1.8	1 U	0.67 J	2.2	1 U	1 U	1 U	1 U	6.5
MW-114B	11/28/09		1 U	2.2	1 U	1	2	1 U	1 U	1 U	1 U	6.7
MW-114B	11/28/09	Fld Dupe	1 U	2.4	1 U	0.93 J	1.9	1 U	1 U	1 U	1 U	6.8
MW-114B	06/25/10		1 U	2.1	1 U	0.84 J	2	1 U	1 U	1 U	1 U	6.3
MW-114B	06/25/10	Fld Dupe	1 U	2	1 U	0.81 J	1.9	1 U	1 U	1 U	1 U	6.3
MW-114B	11/27/10		1 U	1.8	1 U	1	2.3	1 U	1 U	1 U	1 U	7.8

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-117B	04/22/99		0.72	7.3	0.54	14	16	1 U	2 U	3.1	83	21
MW-117B	10/18/99		0.58 J	7.7	5 U	14	17	5 U	10	1.3 J	68	17
MW-117B	01/26/00		0.36 J	8	5 U	9.5	18	5 U	10	1.9 J	59	22
MW-117B	04/17/00		0.39 J	8.1	0.42 J	11	19	2 U	4 JB	1.6 J	49	19
MW-117B	07/24/00		0.49	6.6	2 U	9.6	15	2 U	4 U	1.7	42	17
MW-117B	11/07/00		0.42	10	2 U	11	18	2 U	4 U	1.7	37	19
MW-117B	04/09/01		0.37	5.8	2 U	7.3	13	0.25	4 U	1.8	28	17
MW-117B	10/15/01		0.35	7.1	2 U	7.5	16	2 U	4 U	1.3	23	16
MW-117B	04/16/02		0.3	5.9	0.22	7.3	15	0.2	2 U	1.7	22	16
MW-117B	10/07/02		5 U	8	5 U	54	20	5 U	10 U	3	25	16
MW-117B	04/22/03		1 U	7.55	1 U	10.4	20.1	0.61 J	2 U	2.31	23.1	18.4
MW-117B	12/22/03		0.99 J	5.96	1 U	9.38	18.7	0.53 J	1 U	2.25	21.8	16.9
MW-117B	04/28/04		0.73	3.77	1 U	4.76	11.5	1 U	2 U	2	13.5	11.5
MW-117B	05/21/05		1 U	4.5	1 U	5.7	13	1 U	2 U	1.6	11	9.4
MW-117B	10/19/05		1 U	4.7	1 U	5.6	14	1 U	2 U	1.8	12	9.3
MW-117B	06/28/06		1 U	21	1 U	23	70	1 U	2 U	24	56	23
MW-117B	11/21/06		1 U	3.6	1 U	4	11	1 U	2 U	2.1	12	11
MW-117B	10/06/07		0.4	6	1 U	8	8	1 U	2 U	2	16	12
MW-117B	05/17/08		1 U	8	1 U	11	11	1 U	2 U	3	25 E	16
MW-117B	05/17/08	Dilution	2 U	7 D	2 U	10 D	9 D	2 U	4 U	3 D	22 D	14 D
MW-117B	11/28/08		0.38 J	7.91	1 U	8.73	8.11	1 U	1 U	4.99	24	15.8
MW-117B	06/09/09		0.49 J	11	1 U	12	7.9	1 U	1 U	4.5	31	17
MW-117B	11/24/09		0.42 J	8.5	1 U	9	5.1	1 U	1 U	5.3	24	15
MW-117B	06/24/10		0.32 J	12	1 U	12	6	1 U	1 U	6.5	37	17
MW-117B	11/24/10		0.31 J	11	1 U	8.1	4.6	1 U	1 U	8.4	31	19

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-117C	04/22/99		0.77	54	2.3	44	69	2 U	4 U	6	75	36
MW-117C	10/18/99		5 U	60	5 U	53	82	5 U	10 U	7.5	94	40
MW-117C	02/16/00		0.82 J	61	5 U	53	94	0.5 J	0.8 J	9.7	93	41
MW-117C	04/18/00		0.79 J	54	2.2 J	49	94	0.6 J	10 JB	10	91	39
MW-117C	07/24/00		1	55	2.4	48	99	1.1	10 U	8.7	89	38
MW-117C	11/07/00		0.79	69	2.4	50	100	5 U	10 U	8.8	78	34
MW-117C	04/09/01		0.84	57	2.3	59	120	0.82	10 U	12	99	42
MW-117C	10/15/01		0.81	48	5 U	45	110	0.44	10 U	11	74	32
MW-117C	04/16/02		0.75	41	1.6	469	120	0.74	0.3	16	82	34
MW-117C	10/07/02		20 U	59	20 U	330	150	20 U	32	22	110	42
MW-117C	04/22/03		0.85 J	43.6 E	1.35	63.6 E	134 E	1.71	2 U	27.1 E	113 E	48 E
MW-117C	04/22/03	Dilution	10 U	40	10 U	58.2	123	10 U	20 U	23.1	93	44.3
MW-117C	12/22/03		0.82 J	39.6 E	1.01	55.8 E	126 E	2.07	1 U	27.5 E	104 E	46.4 E
MW-117C	12/22/03	Dilution	10 U	33.1 D	10 U	43.3 D	107 D	10 U	10 U	19.9 D	78.2 D	34.8 D
MW-117C	04/28/04		10 U	30.5	10 U	37	97.3	10 U	20 U	20.3	66.4	30.1
MW-117C	05/21/05		1 U	28	1 U	34	91	1 U	2 U	22	59	27
MW-117C	10/19/05		1 U	25	1 U	29	84	1 U	2 U	20	54	26
MW-117C	05/06/06		1 U	25	1 U	26	91	1 U	2 U	21	50	26
MW-117C	11/21/06		1 U	41	1 U	46	140	1 U	2 U	36	100	44
MW-117C	10/06/07		0.5	24	0.3	30	88	0.9	2 U	24	60	26
MW-117C	05/17/08		5 U	28	5 U	33	99	5 U	10	30	72	30
MW-117C	11/28/08		0.55 J	24.1	0.26 J	25.6	85.9	0.31 J	1 U	26.5	57.1	23.1
MW-117C	06/09/09		0.51 J	24	0.23 J	25	70	0.33 J	1 U	26	58	23
MW-117C	11/24/09		0.48 J	23	1 U	24	57	1 U	1 U	26	51	21
MW-117C	06/24/10		0.42 J	24	1 U	23	40	0.24 J	1 U	28	51	20
MW-117C	11/24/10		0.38 J	22	1 U	22	34	1 U	1 U	27	53	21

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-117D	04/22/99		0.74	46	2	50	110	2 U	4 U	17	110	38
MW-117D	10/18/99		10 U	39	10 U	44	110	10 U	1.5 J	17	97	35
MW-117D	02/17/00		0.8 J	34	1.4 J	41	100	5 U	10 U	19	91	35
MW-117D	04/18/00		0.63 J	29	1.1 J	35	90	5 U	10 JB	17	82	32
MW-117D	07/24/00		0.85	27	1.2	36	81	5 U	10 U	16	80	35
MW-117D	11/07/00		0.6	37	1	33	87	5 U	10 U	16	71	30
MW-117D	04/09/01		0.65	29	5 U	37	88	0.39	10 U	13	80	31
MW-117D	10/16/01		0.53	23	5 U	25	75	5 U	10 U	17	57	23
MW-117D	04/16/02		0.61	21	5 U	24	72	5 U	10 U	18	58	23
MW-117D	10/07/02		10 U	36	10 U	180	100	10 U	18	24	87	29
MW-117D	04/22/03		0.64 J	29.8 E	0.7 J	43.1 E	95.8 E	1 U	2 U	6.41	78.7 E	32.4 E
MW-117D	04/22/03	Dilution	5 U	28.3	5 U	36.7	83.1	5 U	10 U	4.62 J	64.5	26
MW-117D	12/22/03		0.61 J	28.1 E	1 U	30.4 E	102 E	1 U	1 U	30.1 E	84.2 E	31.2 E
MW-117D	12/22/03	Dilution	5 U	29 D	5 U	32.8 D	110 D	5 U	5 U	29.6 D	85.1 D	31.2 D
MW-117D	04/28/04		5 U	28.6	5 U	37.7	105	5 U	10 U	17.4	75.5	33.2
MW-117D	05/21/05		1 U	20	1 U	24	84	1 U	2 U	21	60	24
MW-117D	10/19/05		1 U	24	1 U	21	73	1 U	2 U	24	58	22
MW-117D	05/06/06		1 U	23	1 U	17	67	1 U	2 U	22	52	20
MW-117D	11/21/06		1 U	27	1 U	22	76	2.1	2 U	31	89	32
MW-117D	10/06/07		0.4	22	0.3	22	71	1	2 U	15	62	29
MW-117D	05/17/08		5 U	24	5 U	24	31	5 U	12	30	62	23
MW-117D	11/28/08		0.46 J	23.3	1 U	19.5	23.5	0.27 J	1 U	28.6	58	19.4
MW-117D	06/09/09		0.49 J	25	1 U	18	13	1 U	1 U	30	55	20
MW-117D	11/24/09		0.49 J	29	1 U	19	11	1 U	1 U	28	49	18
MW-117D	06/24/10		0.33 J	28	1 U	16	5.3	0.18 J	1 U	29	46	15
MW-117D	11/24/10		0.34 J	30	1 U	16	5.6	1 U	1 U	29	45	17

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-119	05/03/99		1 U	1 U	1 U	1 U	0.36	1 U	2 U	0.63	1.8	1
MW-119	10/27/99		0.26 J	0.35 J	1 U	0.28 J	1.3	1 U	2 U	1.4	2.5	2
MW-119	01/26/00		0.19 J	0.21 J	1 U	1 U	1 U	1 U	2 U	0.18 J	0.75 J	0.2 J
MW-119	04/17/00		0.16 J	0.23 J	1 U	1 U	1 U	1 U	2 JB	0.19 J	0.79 J	0.2 J
MW-119	07/25/00		0.12	0.26	1 U	1 U	1 U	1 U	2 U	0.22	0.88	0.21
MW-119	11/08/00		1 U	0.27	1 U	1 U	1 U	1 U	2 U	0.18	0.72	0.18
MW-119	04/10/01		1 U	0.26	1 U	1 U	1 U	1 U	2 U	0.17	0.85	0.19
MW-119	10/16/01		0.1	0.29	1 U	1 U	1 U	1 U	2 U	0.15	0.71	0.16
MW-119	04/30/02		0.1	0.31	1 U	1 U	1 U	1 U	2 U	0.18	0.95	0.17
MW-119	10/17/02		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-119	04/22/03		1.07	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1	1 U
MW-119	12/30/03		7.22	0.67 J	1 U	0.54 J	0.59 J	1 U	1 U	1 U	0.72 J	1 U
MW-119	04/28/04		1.67	0.51	1 U	1 U	1 U	1 U	2 U	1 U	0.62	1 U
MW-119	05/21/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1.3	1 U
MW-119	10/20/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1.3	1 U
MW-119	05/06/06		1 U	1.2	1 U	1 U	1 U	1 U	2 U	1 U	1.1	1 U
MW-119	01/04/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-119	10/08/07		1 U	1	1 U	1 U	0.4	1 U	2 U	1 U	1	1 U
MW-119	05/18/08		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1	1 U
MW-119	11/29/08		0.3 J	0.98 J	1 U	1 U	0.54 J	1 U	1 U	1 U	1.29	0.27 J
MW-119	06/10/09		0.64 J	1	1 U	1 U	0.66 J	1 U	1 U	1 U	1.2	0.29 J
MW-119	11/29/09		0.45 J	1.4	1 U	1 U	0.61 J	1 U	1 U	1 U	1.2	1 U
MW-119	06/29/10		1 U	0.92 J	1 U	1 U	1.2	1 U	1 U	1 U	1.1	1 U
MW-119	11/27/10		0.46 J	1.1	1 U	1 U	1.1	1 U	1 U	1 U	1.7	0.42 J

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-121	04/28/99		5 U	3.4	5 U	6	7.2	5 U	10 U	2.7	3.8	26
MW-121	10/26/99		0.67 J	3.8	0.78 J	8	8.4	0.15 J	2 U	3.4	5.5	33 E
MW-121	10/26/99	Dilution	2 U	3.2 D	0.67 DJ	6.6 D	6.8 D	0.1 DJ	4 U	2.9 D	4.4 D	29 D
MW-121	01/31/00		0.65 J	2.9	2 U	5.5	6.3	0.2 J	0.41 J	2.5	3.4	23
MW-121	04/18/00		0.55 J	2.8	0.72 J	3	5.6	0.22 J	2 JB	0.64 J	2.8	11
MW-121	07/25/00		0.68	3.5	0.82	4.4	6.8	0.39	2 U	1.8	4.3	20
MW-121	11/08/00		0.77	4.6	0.89	8	7	0.22	2 U	2.6	5.1	22
MW-121	04/10/01		0.78	3.7	0.82	2	6.7	0.68	2 U	2.3	5.5	22
MW-121	10/16/01		0.82	3.8	0.81	3.6	6.5	0.42	2 U	2.4	5.9	19
MW-121	04/17/02		0.75	3.8	0.07	3	6.1	0.58	2 U	2.6	6.9	20
MW-121	10/17/02		5 U	5	5 U	42	7	5 U	2 U	3	9	24
MW-121	04/22/03		0.65 J	4.3	0.55 J	7.28	5.74	1 U	2 U	2.85	7.18	22.6
MW-121	12/28/03		1 U	4.76	1 U	5.11	4.61	1 U	1 U	2.74	5.79	20.3
MW-121	04/28/04		0.52	4.37	1 U	4.58	4.79	1 U	2 U	2.43	5.84	18.8
MW-121	05/21/05		1 U	2.2	1 U	3.9	5.2	1 U	2 U	1.9	5.1	18
MW-121	10/20/05		1 U	2.9	1 U	3.9	5.9	1 U	2 U	2.1	5.7	20
MW-121	05/06/06		1 U	2.5	1 U	3.3	5.3	1 U	2 U	2.3	4.8	22
MW-121	01/03/07		1 U	1.4	1 U	1.7	3	1 U	2 U	1.9	3.9	20
MW-121	10/07/07		0.7	2	1 U	2	6	0.4	2 U	2	5	22
MW-121	05/18/08		1 U	2	1 U	2	7	1 U	2 U	2	6	26 E
MW-121	05/18/08	Dilution	2 U	2 D	2 U	3 D	6 D	2 U	3 DJ	2 D	5 D	25 D
MW-121	11/29/08		0.56 J	1.36	1 U	1 U	3.42	0.55 J	1 U	1.84	2.67	14.4
MW-121	06/11/09		0.65 J	1.9	1 U	1 U	4.8	0.76 J	1 U	2.3	4	23
MW-121	11/25/09		0.63 J	2.1	1 U	1.8	4.3	1 U	1 U	2	3.1	20
MW-121	06/29/10		1 U	2.9	1 U	1.7	3.7	1 U	1 U	1.5	2	16
MW-121	11/25/10		0.6 J	4.6	1 U	2.5	4.3	1 U	1 U	2.1	3.4	22

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-124	04/28/99		10 U	75	10 U	97	1200	10 U	20 U	47	540	36
MW-124	10/27/99		50 U	50	50 U	41 J	560	50 U	8.2 J	28 J	280	28 J
MW-124	01/31/00		25 U	95	25 U	36	540	25 U	50 U	12 J	190	20 J
MW-124	04/24/00		0.72 J	92	25 U	24 J	440	3.9 J	50 JB	3.8 J	100	14 J
MW-124	07/25/00		20 U	89	20 U	20	330	20 U	40 U	20 U	79	10
MW-124	11/13/00		20 U	110	20 U	20	300	20 U	40 U	2.7	75	12
MW-124	04/12/01		20 U	47	20 U	35	240	2.1	40 U	30	230	24
MW-124	10/29/01		10 U	98	10 U	19	190	1.4	20 U	6.2	110	16
MW-124	04/17/02		20 U	64	20 U	35	370	12	40 U	30	210	26
MW-124	10/17/02		20 U	92	20 U	230	360	20 U	40 U	35	290	33
MW-124	04/25/03		1 U	83.4 E	1.32	30 E	226 E	8.35	2 U	13.8	136 E	20.9
MW-124	04/25/03	Dilution	10 U	71.4	10 U	26.4	213	10 U	20 U	13.5	119	18.9
MW-124	12/28/03		1 U	109 E	1.34	22.8	174 E	6.96	1 U	11.2	116 E	19.2
MW-124	12/28/03	Dilution	10 U	83.2 D	10 U	20.1 D	176 D	10 U	10 U	10.6 D	94.7 D	15.6 D
MW-124	04/28/04		40 U	197	40 U	43.6	389	40 U	80 U	34.6	185	26.7
MW-124	05/21/05		5 U	340	5 U	37	420	5 U	10 U	8.4	120	18
MW-124	10/20/05		1 U	250	1 U	25	260	1.5	2 U	6.6	76	15
MW-124	05/06/06		1 U	320	1.2	29	370	1.5	2 U	15	120	18
MW-124	01/04/07		10 U	370	10 U	15	250	10 U	20 U	10 U	110	10
MW-124	10/07/07		1 U	620	0.7	28	300	4	2 U	8	100	12
MW-124	05/18/08		40 U	870	40 U	42	320	40 U	80 U	40 U	190	40 U
MW-124	11/29/08	Dilution	5 U	415	5 U	16.1	144	1.4 J	1.45 J	11.8	90	10.4
MW-124	06/10/09	Dilution	1 J	500	5 U	18	150	5 U	5 U	14	100	10
MW-124	11/29/09	Dilution	5 U	510	5 U	22	170	5 U	5 U	16	98	9.4
MW-124	06/29/10	Dilution	5 U	500	5 U	20	220	5 U	1.9 J	14	82	8.6
MW-124	11/27/10	Dilution	5 U	490	5 U	25	280	5 U	5 U	14	95	9.2

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-130	04/28/99		0.19	19	1 U	11	24	1 U	2 U	5.3	670	17
MW-130	10/28/99		25 U	10 J	25 U	4.9 J	7.8 J	25 U	50 U	25 U	370	8.2 J
MW-130	02/16/00		25 U	11 J	25 U	3.6 J	7.5 J	25 U	50 U	25 U	460	8.5 J
MW-130	04/24/00		50 JB	12 J	50 U	3.1 J	7.7 J	50 U	100 JB	50 U	510	8.3 J
MW-130	07/27/00		20 U	13	20 U	3.3	7.7	20 U	40 U	20 U	670	8.5
MW-130	11/14/00		25 U	12	25 U	4.3	7.2	25 U	50 U	25 U	390	7
MW-130	04/12/01		20 U	10	20 U	20 U	5.7	20 U	40 U	20 U	440	6.2
MW-130	10/30/01		50 U	14	50	50 U	50 U	50 U	100 U	50 U	660	50 U
MW-130	04/30/02		25 U	11	25 U	1.6	5.7	25 U	50 U	0.97	360	5.4
MW-130	10/17/02		50 U	50 U	50 U	54	50 U	50 U	43	50 U	840	50 U
MW-130	04/25/03		0.1 J	13	1 U	5.33	7.5	0.48 J	2 U	1.37	424 E	5.94
MW-130	04/25/03	Dilution	20 U	11.6 J	20 U	20 U	20 U	20 U	40 U	20 U	322	20 U
MW-130	04/25/03	Fld Dupe	0.11 J	13.2	20 U	5.68	7.84	0.43 J	2 U	20 U	341	20 U
MW-130	12/28/03		1 U	12.1	1 U	5.65	8.09	1 U	1 U	1.11	320 E	5.46
MW-130	12/28/03	Dilution	20 U	10.3 JD	20 U	20 U	20 U	20 U	20 U	20 U	263 D	20 U
MW-130	04/28/04		10 U	11	10 U	10 U	10.6	10 U	20 U	10 U	157	10 U
MW-130	05/21/05		1 U	14	1 U	4	11	1 U	2 U	1 U	210	3.5
MW-130	10/20/05		1 U	16	1 U	4.2	14	1 U	2 U	1 U	210	3.6
MW-130	05/08/06		1 U	16	1 U	4.1	14	1 U	2 U	1 U	140	3.6
MW-130	01/04/07		1 U	20	1 U	4.6	18	1 U	2 U	1 U	160	4.3
MW-130	10/07/07		1 U	17	1 U	5	21	0.6	2 U	0.6	170	4
MW-130	05/17/08		10 U	22	10 U	10 U	25	10 U	20 U	10 U	200	10 U
MW-130	11/29/08	Dilution	2 U	21.9	2 U	4.18	21	0.4 J	0.56 J	0.56 J	198	4.26
MW-130	06/11/09	Dilution	0.48 J	26	2 U	4.3	20	2 U	2 U	0.9 J	300	4.3
MW-130	11/29/09	Dilution	2 U	31	2 U	5.5	12	2 U	2 U	2 U	320	3.3
MW-130	06/29/10	Dilution	10 U	70	10 U	15	17	10 U	2.9 J	10 U	1100	7.6 J
MW-130	11/27/10	Dilution	5 U	29	5 U	8.4	8.3	5 U	5 U	5 U	430	3.6 J

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-133A	04/26/99		1 U	1 U	1 U	1 U	0.27	1 U	2 U	0.37	0.95	1.1
MW-133A	10/26/99		0.03 J	0.52 J	1 U	0.66 J	1 8	1 U	2 U	1	4.6	4.8
MW-133A	02/15/00		1 U	0.08 J	1 U	1 U	0.16 J	1 U	2 U	1 U	0.38 J	1 U
MW-133A	04/25/00		1 U	1 U	1 U	1 U	1 U	1 U	2 JB	1 U	0.35 J	1 U
MW-133A	07/27/00		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-133A	11/16/00		1 U	1 U	1 U	1 U	0.49	1 U	2 U	1 U	0.81	0.11
MW-133A	04/10/01		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-133A	10/31/01		1 U	0.41	1 U	0 1	1.2	1 U	2 U	1 U	1	0.19
MW-133A	04/29/02		1 U	1 U	1 U	1 U	0.04	1 U	2 U	1 U	0.06	1 U
MW-133A	10/16/02		1 U	1	1 U	1 U	4	1 U	0.6	1 U	3	1 U
MW-133A	04/25/03		1 U	2.96	1 U	1.05	11.7	1 U	2 U	1 U	5 2	0 98 J
MW-133A	12/30/03		1 U	1.92	1 U	0.53 J	6.34	1 U	1 U	1 U	2 51	1 U
MW-133A	04/28/04		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-133A	05/02/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-133A	11/02/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-133A	06/22/06		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-133A	11/16/06		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-133A	10/07/07		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U
MW-133A	05/17/08		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-133A	11/26/08		1 U	1 U	1 U	1 U	0.26 J	1 U	1 U	1 U	0.32 J	1 U
MW-133A	06/20/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U
MW-133A	06/20/09	Fld Dupe	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U
MW-133A	11/28/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U
MW-133A	06/25/10		1 U	1 U	1 U	1 U	0.23 J	1 U	1 U	1 U	0.26 J	1 U
MW-133A	11/27/10		1 U	0.21 J	1 U	1 U	0 91 J	1 U	1 U	1 U	0.86 J	1 U
MW-133A	11/27/10	Fld Dupe	1 U	1 U	1 U	1 U	0.79 J	1 U	1 U	1 U	0.82 J	1 U

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-133B	04/26/99		10	200	4.6	110	780	7	4 U	110	840	270
MW-133B	10/26/99		7.9 J	170	50 U	67	810	7.1 J	6.8 J	77	630	190
MW-133B	02/15/00		9.3 J	180	50 U	100	840	50 U	100 U	120	730	250
MW-133B	04/25/00		12 J	170	50 U	78	600	50 U	100 JB	76	620	190
MW-133B	07/27/00		12	160	4.1	88	670	10	40 U	94	760	220
MW-133B	11/16/00		11	200	25 U	88	530	9.5	50 U	94	570	230
MW-133B	04/10/01		13	200	50 U	46	660	43	100 U	140	830	300
MW-133B	10/31/01		12	180	50 U	7	510	49	100 U	110	700	250
MW-133B	04/29/02		9.1	150	3.7	25 U	460	54	50 U	99	570	170
MW-133B	10/16/02		50 U	250	50 U	650	820	50 U	31	140	800	290
MW-133B	04/25/03		10.7	183 E	3.97	110 E	728 E	24.5	2 U	151 E	699 E	325 E
MW-133B	04/25/03	Dilution	40 U	158	40 U	40.4	571	41.4	80 U	112	617	237
MW-133B	12/30/03		9.91	162 E	1 U	93 E	562 E	16.3	1 U	122 E	510 E	250 E
MW-133B	12/30/03	Dilution	50 U	151 D	50 U	81.6 D	623 D	50 U	50 U	109 D	577 D	240 D
MW-133B	04/28/04		10 U	161	10 U	106	803	10 U	20 U	111	622	216
MW-133B	05/02/05		5.6	120	5 U	70	630	17	10 U	81	460	160
MW-133B	11/02/05		8.2	180	5 U	98	930	28	10 U	110	620	220
MW-133B	06/22/06		10 U	110	10 U	54	720	11	20 U	68	430	120
MW-133B	11/16/06		10 U	160	10 U	10 U	740	78	50 U	85	10 U	170
MW-133B	10/07/07		6	160	3	84	930	38	2 U	110	600	200
MW-133B	05/17/08		40 U	130	40 U	60	900	40 U	80 U	59	440	110
MW-133B	11/26/08		8 J	308	5.4 J	12	1860	193	3.2 J	126	955	208
MW-133B	06/20/09	Dilution	7.3 J	230	4.3 J	19	1400	140	10 U	110	710	170
MW-133B	11/28/09	Dilution	7.8 J	280	20 U	100	2000	84	20 U	110	820	190
MW-133B	06/25/10	Dilution	5.4 J	230	4 J	81	1700	47	20 U	96	680	150
MW-133B	11/27/10	Dilution	20 U	240	20 U	120	1900	11 J	20 U	110	790	180

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-133C	04/26/99		8.5	57	2.8	47	100	5 U	10 U	28	200	110
MW-133C	10/26/99		7.2 J	49	10 U	40	91	1.1 J	20 U	22	170	93
MW-133C	02/15/00		5.4	31	2.3 J	23	32	0.42 J	10 U	2.5 J	110	55
MW-133C	04/25/00		4.7 JB	28	10 U	21	28	0.34 J	20 JB	1.2 J	100	48
MW-133C	07/27/00		4.9	28	2.2	18	30	5 U	10 U	0.82	91	34
MW-133C	11/16/00		5.2	35	2.2	22	31	5 U	10 U	1.2	95	47
MW-133C	04/10/01		6.2	36	10 U	28	36	10 U	20 U	1.6	130	62
MW-133C	10/31/01		5.1	31	5 U	14	31	5 U	10 U	5 U	100	31
MW-133C	04/29/02		5.4	33	1.8	26	45	0.73	0.49	4.5	120	58
MW-133C	10/16/02		6	49	10 U	150	51	10 U	6	10 U	140	66
MW-133C	04/25/03		5.34	33.5 E	1.86	29.9 E	42.1 E	1.04	2 U	2.41	137 E	72.2 E
MW-133C	04/25/03	Dilution	5.04 J	31.6	10 U	26.5	39.2	10 U	20 U	10 U	113	60.7
MW-133C	12/30/03		6.43	40.7 E	2.01	36.8 E	55.5 E	0.8 J	1 U	3.02	166 E	83 E
MW-133C	12/30/03	Dilution	5.64 JD	143 D	10 U	32.5 D	49.5 D	10 U	10 U	10 U	136 D	74.4 D
MW-133C	04/28/04		5.42	34.7	10 U	29.2	47.2	10 U	20 U	10 U	124	63.7
MW-133C	05/02/05		5.7	37	1.8	31	53	0.59	2 U	2.6	130	63
MW-133C	11/02/05		6.5	46	5 U	43	70	5 U	10 U	5 U	150	75
MW-133C	06/22/06		7.3	44	1 U	42	71	1.3	2 U	4.3	150	78
MW-133C	11/16/06		7.7	61	1.9	23	86	3.5	2 U	5.1	220	110
MW-133C	10/07/07		7	50	2	51	88	2	2 U	5	170	88
MW-133C	05/17/08		8 U	60	8 U	62	120	8 U	16 U	8 U	200 E	100
MW-133C	05/17/08	Dilution	10 U	57 D	10 U	58 D	110 D	10 U	20 U	10 U	180 D	94 D
MW-133C	05/17/08	Fld Dupe	7	60 D	20 U	65 D	110 D	20 U	20 DJ	20 U	200 E	100 E
MW-133C	11/26/08		7.82	53.6	1.92	24.6	96.9	6.93	0.23 J	6.06	182	94.8
MW-133C	06/20/09		7.4	59	2	36	110	9.7	1 U	6	190	100
MW-133C	11/28/09		7.1	58	1.8	53	110	1.2	1 U	6.2	170	94
MW-133C	06/25/10		6.9	54	1.8	50	130	1.3	1 U	8.6	180	89
MW-133C	11/27/10		6.1	47	1.8	46	130	0.3 J	1 U	10	180	94

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-136	04/29/99		0.37	0.35	1 U	0 88	3.5	1 U	2 U	1.7	8	3.8
MW-136	10/28/99		1.5	0.34 J	1 U	0.37 J	1.1	0.03 J	2 U	1.4	16	2.4
MW-136	02/15/00		0.74 J	1 U	1 U	1 U	1 U	1 U	2 U	1 U	0.28 J	1 U
MW-136	04/25/00		0.57 JB	1 U	1 U	1 U	1 U	1 U	2 JB	1 U	0.31 J	1 U
MW-136	07/27/00		0.48	1 U	1 U	1 U	1 U	1 U	2 U	1 U	0 3	1 U
MW-136	11/17/00		0.5	1 U	1 U	1 U	1 U	1 U	2 U	1 U	0.29	1 U
MW-136	04/10/01		0.45	1 U	1 U	1 U	1 U	1 U	2 U	1 U	0.3	1 U
MW-136	10/31/01		0.45	1 U	1 U	1 U	1 U	1 U	2 U	1 U	0.3	1 U
MW-136	04/29/02		0.45	1 U	1 U	1 U	1 U	1 U	2 U	0.53	0.3	1 U
MW-136	10/18/02		0.6	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-136	04/23/03		0.8 J	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-136	04/28/04		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-136	06/23/06		1.1	1 U	1 U	1 U	1 U	1 U	1 8	1 U	1 U	1 U
MW-136	01/05/07		2.5	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-136	10/07/07		1 U	1 U	1 U	1 U	1 U	1 U	0.7	1 U	1 U	1 U
MW-136	05/18/08		2	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-136	11/29/08		4.5	1 U	1 U	1 U	0.2 J	1 U	1 U	1 U	1 U	1 U
MW-136	06/11/09		3.1	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U
MW-136	11/28/09		1.5	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U
MW-136	06/29/10		0.84 J	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U
MW-136	11/28/10		0.82 J	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-200	04/26/99		1 U	1 U	1 U	0 34	0.66	1 U	2 U	0.61	2.2	2.2
MW-200	10/27/99		1 U	1 U	1 U	0.26 J	1.2	1 U	2 U	1.1	1.9	1.8
MW-200	02/15/00		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-200	04/25/00		1 U	1 U	1 U	1 U	1 U	1 U	2 JB	1 U	0.07 J	1 U
MW-200	07/27/00		1 U	1 U	1 U	1 U	0.1	1 U	2 U	1 U	1 U	1 U
MW-200	11/14/00		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-200	04/10/01		1 U	1 U	1 U	1 U	0.17	1 U	2 U	1 U	1 U	1 U
MW-200	10/29/01		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	0.12
MW-200	04/22/02		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-200	10/18/02		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-200	04/25/03		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-200	12/30/03		1 U	1 U	1 U	0.89 J	1 U	1 U	1 U	1 U	1 U	1 U
MW-200	04/28/04		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-200	05/21/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1.9	1 U
MW-200	01/12/06		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-200	05/08/06		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-200	01/04/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-200	10/08/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-200	05/18/08		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-200	11/29/08		1 U	1 U	1 U	1 U	0.69 J	1 U	1 U	1 U	0.21 J	0.17 J
MW-200	06/11/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U
MW-200	11/28/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U
MW-200	06/29/10		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U
MW-200	11/28/10		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-201	02/16/00		5 U	48	5 U	1.1 J	85	5 U	10 U	5 U	4.5 J	8.3
MW-201	04/18/00		10 U	120	10 U	1.9 J	87	0.78 J	20 JB	10 U	4.9 J	15
MW-201	04/18/00	Fld Dupe	0.29 J	130	10 U	2.3 J	93	0.74 J	20 JB	10 U	5.8 J	12
MW-201	07/25/00		20 U	330	20 U	6.8	220	20 U	40 U	20 U	110	4.5
MW-201	11/13/00		20 U	340	20 U	5.2	180	20 U	40 U	20 U	39	4.9
MW-201	04/12/01		5 U	43	5 U	1.6	60	0.64	10 U	5 U	12	19
MW-201	10/29/01		10 U	150	10 U	3.6	120	10 U	20 U	10 U	55	25
MW-201	04/30/02		5	5500	250 U	130	2600	250 U	500 U	250 U	1700	13
MW-201	10/03/02		500 U	7100	500 U	480	2200	500 U	1000 U	500 U	970	500 U
MW-201	04/25/03		0.05 J	1410 E	1 U	52.8 E	989 E	20.3	2 U	0.29 J	452 E	28.9 E
MW-201	04/25/03	Dilution	500 U	6350	500 U	500 U	863	500 U	1000 U	500 U	294 J	500 U
MW-201	12/30/03		1 U	1580 E	1 U	15	123 E	1 U	1 U	1 U	175 E	2.99
MW-201	12/30/03	Dilution	400 U	6480 D	400 U	400 U	400 U	400 U	400 U	400 U	400 U	400 U
MW-201	12/30/03	Fld Dupe	1 U	1430 E	400 U	400 U	400 U	1 U	400 U	400 U	145 E	400 U
MW-201	04/28/04		500 U	4150	500 U	500 U	500 U	500 U	1000 U	500 U	500 U	500 U
MW-201	05/21/05		25 U	3500	25 U	25 U	58	25 U	50 U	25 U	26	25 U
MW-201	01/12/06		1 U	230	1 U	1.2	23	1 U	2 U	1 U	8.8	14
MW-201	06/28/06		10 U	550	10 U	10 U	16	10 U	20 U	10 U	32	14
MW-201	01/05/07		1 U	80	1 U	1 U	5.1	1 U	2 U	1 U	20	2.8
MW-201	10/08/07		1 U	20	1 U	2	2	1 U	2 U	6	7	9
MW-201	05/18/08		1 U	64 E	1 U	2	11	1 U	2 U	1 U	7	10
MW-201	05/18/08	Dilution	4 U	55 D	4 U	4 U	9 D	4 U	8 U	4 U	6 D	9 D
MW-201	11/29/08	Dilution	2 J	1460	10 U	10 U	7.1 J	10 U	4.4 J	10 U	14.2	7.7 J
MW-201	11/29/08	Fld Dupe	10 U	1580	10 U	10 U	5.5 J	10 U	3.1 J	10 U	12.5	7.1 J
MW-201	06/10/09	Dilution	2 J	1200	10 U	10 U	16	10 U	10 U	10 U	10	7.7 J
MW-201	06/10/09	Fld Dupe	10 U	1200	10 U	10 U	9.8 J	10 U	10 U	10 U	7.4 J	5.7 J
MW-201	11/29/09	Dilution	10 U	480	10 U	10 U	6.4 J	10 U	10 U	10 U	37	10 U
MW-201	11/29/09	Fld Dupe	10 U	500	10 U	10 U	5.7 J	10 U	10 U	10 U	36	10 U
MW-201	06/29/10		1 U	12	1 U	1 U	5	1 U	1 U	0.53 J	4.4	1.1
MW-201	11/28/10		1 U	2.7	1 U	0.43 J	0.75 J	1 U	1 U	0.93 J	3.4	1.2

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-202	05/20/99		1 U	1 U	1 U	1 U	0.81	1 U	2 U	4.6	2	2.1
MW-202	10/28/99		1 U	1 U	1 U	0.18 J	0.68 J	1 U	2 U	5	2.2	2.1
MW-202	02/16/00		1 U	1 U	1 U	1 U	1 U	1 U	2 U	3.6	0.77 J	0.5 J
MW-202	04/18/00		0.25 J	1 U	1 U	1 U	1 U	1 U	2 JB	3.1	0.65 J	0.55 J
MW-202	07/27/00		0.48	1 U	1 U	1 U	1 U	1 U	2 U	3.5	0.72	0.75
MW-202	11/13/00		1 U	1 U	1 U	1 U	1 U	1 U	2 U	14	0.11	0.19
MW-202	04/12/01		1 U	1 U	1 U	1 U	1 U	1 U	2 U	13	0.08	0.11
MW-202	10/29/01		1 U	1 U	1 U	1 U	1 U	1 U	2 U	12	0.06	1 U
MW-202	04/30/02		1 U	1 U	1 U	1 U	1 U	1 U	2 U	10	1 U	0.12
MW-202	10/17/02		1 U	1 U	1 U	1 U	1 U	1 U	0.5	12	1 U	1 U
MW-202	04/24/03		1 U	1 U	1 U	1 U	1 U	1 U	2 U	2.82	1 U	0.8 J
MW-202	12/30/03		1 U	1 U	1 U	0.54 J	1 U	1 U	1 U	2.78	1 U	1.11
MW-202	04/28/04		1 U	1 U	1 U	1 U	1 U	1 U	2 U	2.3	1 U	0.68
MW-202	05/21/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1.8	1 U	1 U
MW-202	10/21/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-202	06/28/06		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1.5	1 U	1 U
MW-202	01/05/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	14	1 U	1 U
MW-202	10/08/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1	1	0.3
MW-202	05/19/08		1 U	1 U	1 U	1 U	1 U	1 U	2 U	4	1 U	1 U
MW-202	11/29/08		0.3 J	0.95 J	1 U	1 U	1 U	1 U	1 U	1.26	1.15	0.65 J
MW-202	06/11/09		1 U	0.46 J	1 U	1 U	1 U	1 U	1 U	1.2	1	0.6 J
MW-202	11/29/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1.2	1 U	1 U
MW-202	06/29/10		1 U	0.7 J	1 U	1 U	1 U	1 U	1 U	1.6	1.3	0.79 J
MW-202	11/28/10		1 U	1 U	1 U	1 U	1 U	1 U	1 U	2.1	0.67 J	1 U

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-203	05/20/99		1 U	1 U	1 U	1 U	0.67	1 U	2 U	14	0.92	1.2
MW-203	10/28/99		0.08 J	0.28 J	1 U	0.42 J	1.5	0.06 J	2 U	15	2.7	2.6
MW-203	02/15/00		1 U	1 U	1 U	1 U	0.13 J	1 U	2 U	8.6	0.26 J	0.16 J
MW-203	04/18/00		1 U	1 U	1 U	1 U	0.07 J	1 U	2 U	11	0.14 J	0.17 J
MW-203	07/27/00		1 U	1 U	1 U	1 U	1 U	1 U	2 U	13	0.2	0.24
MW-203	11/13/00		0.82	1 U	1 U	1 U	1 U	1 U	2 U	3.5	0.66	0.81
MW-203	04/12/01		1.8	1 U	1 U	1 U	1 U	1 U	2 U	3.2	0.81	0.76
MW-203	10/29/01		4.3	0.19	1 U	1 U	1 U	1 U	2 U	3.1	0.76	0.84
MW-203	04/30/02		4.1	0.12	1 U	1 U	1 U	1 U	2 U	3	0.69	0.63
MW-203	10/17/02		1	1 U	1 U	1 U	1 U	1 U	0.5	3	1 U	0.7
MW-203	04/24/03		1 U	1 U	1 U	1 U	1 U	1 U	2 U	10.2	1 U	1 U
MW-203	12/30/03		1 U	1 U	1 U	1 U	1 U	1 U	1 U	8.43	1 U	1 U
MW-203	04/28/04		1 U	1 U	1 U	1 U	1 U	1 U	2 U	8.79	1 U	1 U
MW-203	05/21/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	9.6	1 U	1 U
MW-203	10/21/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U
MW-203	06/28/06		1 U	1 U	1 U	1 U	1 U	1 U	2 U	17	1 U	1 U
MW-203	01/05/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1.7	1 U	1 U
MW-203	10/08/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	4	1 U	1 U
MW-203	05/18/08		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1	1	1 U
MW-203	05/18/08	Fld Dupe	1 U	1 U	1 U	1 U	1 U	1 U	2 U	1	1	1 U
MW-203	11/29/08		0.15 J	0.45 J	1 U	1 U	1 U	1 U	1 U	3.11	0.19 J	0.33 J
MW-203	06/11/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	4.4	1 U	1 U
MW-203	11/29/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	5.4	1 U	1 U
MW-203	06/29/10		1 U	1 U	1 U	1 U	1 U	1 U	0.32 J	8.9	1 U	1 U
MW-203	11/28/10		1 U	1 U	1 U	1 U	1 U	1 U	1 U	7.3	1 U	1 U

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-204	04/23/99		20 U	20 U	20 U	6.2	56	20 U	40 U	20 U	4.7	230
MW-204	10/26/99		10 U	5.2 J	4.5 J	8.6 J	51	0.55 J	20 U	2.4 J	5.4 J	230
MW-204	01/31/00		0.67 J	5 J	5.3 J	8.2 J	41	10 U	2 J	2.4 J	4.2 J	200
MW-204	04/24/00		0.92 J	4.9 J	5.7 J	9.2 J	44	10 U	20 JB	2 J	4 J	190
MW-204	07/25/00		1.1	4.4	5.7	6.9	38	10 U	20 U	1.3	3.4	120
MW-204	11/08/00		10 U	6.5	6.8	11	37	10 U	20 U	2.4	4	170
MW-204	04/12/01		10 U	5	6	11	27	10 U	20 U	2.4	4.5	160
MW-204	10/16/01		10 U	5.4	10 U	13	23	10 U	20 U	2.8	4.9	140
MW-204	04/17/02		0.77	6.9	10	18	20	10 U	20 U	2.9	6	140
MW-204	10/03/02		20 U	14	20 U	140	23	20 U	40 U	20 U	20 U	170
MW-204	04/22/03		0.59 J	8.21	9.93	28.4 E	28.6 E	0.61 J	2 U	3.9	9.93	192 E
MW-204	04/22/03	Dilution	10 U	7.58 J	9.49 J	23.9	26.8	10 U	20 U	10 U	9.28 J	165
MW-204	12/28/03		0.58 J	8.14	9.41	26.3 E	28.8 E	1 U	1 U	3.83	11.3	163 E
MW-204	12/28/03	Dilution	10 U	7.65 JD	8.32 JD	21.8 D	23.7 D	10 U	10 U	10 U	9.1 JD	151 D
MW-204	04/28/04		10 U	6.41	8.07	21	20.7	10 U	20 U	10 U	8.96	124
MW-204	05/21/05		1 U	6	5.9	22	13	1 U	2 U	2.8	10	96
MW-204	10/19/05		1 U	6.2	5.7	20	15	1 U	2 U	2.3	9.1	97
MW-204	05/06/06		1 U	5.7	4.4	21	13	1 U	2 U	2.9	10	100
MW-204	01/03/07		1 U	6	3.5	22	15	1 U	2 U	3.2	10	100
MW-204	10/07/07		0.5	6	3	19	15	0.5	2 U	3	10	85
MW-204	05/18/08		4 U	6	4 U	20	20	4 U	8 U	4 U	9	91
MW-204	11/29/08		0.65 J	4.9	2.07	13.6	14.4	0.29 J	1 U	2.64	7.61	74
MW-204	06/11/09		0.67 J	4.3	1.4	11	14	0.4 J	1 U	2.6	7.2	73
MW-204	11/25/09		0.65 J	5.8	1.8	14	20	1 U	1 U	2.6	6.2	71
MW-204	06/29/10		1 U	5.2	1.3	12	18	1 U	1 U	2	4.3	61
MW-204	11/25/10		0.54 J	5.3	1.5	11	24	1 U	1 U	2.5	6.4	66

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-205A	04/22/99		0.88	23	4.4	100	49	5 U	10 U	3.9	570	69
MW-205A	10/21/99		1.1 J	23 J	25 U	110	57	25 U	50 U	3.4 J	460	68
MW-205A	02/07/00		25 U	22 J	3.5 J	110	56	25 U	50 U	3.6 J	450	68
MW-205A	04/18/00		50 U	23 J	50 U	140	61	50 U	100 JB	50 U	540	80
MW-205A	07/25/00		20 U	19	3.5	92	50	20 U	40 U	20 U	350	47
MW-205A	11/07/00		25 U	27	25 U	120	56	25 U	50 U	25 U	410	66
MW-205A	04/09/01		20 U	23	20 U	130	56	20 U	40 U	4.3	430	68
MW-205A	10/16/01		1.1	18	20 U	87	44	20 U	40 U	2.1	240	49
MW-205A	04/16/02		1.1	17	20 U	79	43	20 U	40 U	6.7	270	47
MW-205A	10/07/02		50 U	50 U	50 U	690	53	50 U	84	110	310	49
MW-205A	04/22/03		0.78 J	21	2.39	122 E	51.2 E	1 U	2 U	7.15	397 E	72.8 E
MW-205A	04/22/03	Dilution	25 U	19.8 J	25 U	111	46.6	25 U	50 U	25 U	322	64.3
MW-205A	12/22/03		0.69 J	19.7	1.48	95.6 E	52.7 E	1 U	1 U	11.3	308 E	64.3 E
MW-205A	12/22/03	Dilution	20 U	15.4 JD	20 U	71.9 D	38.5 D	20 U	20 U	20 U	237 D	47.1 D
MW-205A	04/28/04		20 U	15.8	20 U	68.7	39.9	20 U	40 U	20 U	229	43.9
MW-205A	05/21/05		1 U	15	1 U	51	43	1 U	2 U	11	130	36
MW-205A	10/19/05		1 U	13	1 U	35	38	1 U	2 U	11	89	32
MW-205A	05/06/06		1 U	14	1 U	29	37	1 U	2 U	18	81	32
MW-205A	11/21/06		1 U	13	1 U	49	47	1 U	2 U	17	160	51
MW-205A	10/06/07		0.5	12	0.4	31	39	1 U	2 U	16	75	34
MW-205A	05/18/08		4 U	13	4 U	27	48	4 U	8 U	20	73	35
MW-205A	11/28/08		0.49 J	11.9	0.29 J	21.3	41.5	1 U	1 U	20.2	59.5	30.8
MW-205A	06/09/09		0.45 J	10	0.27 J	19	36	1 U	1 U	19	60	30
MW-205A	11/25/09		0.48 J	11	1 U	19	32	1 U	1 U	20	46	27
MW-205A	06/24/10		0.35 J	11	1 U	16	25	1 U	1 U	22	41	23
MW-205A	11/25/10		0.38 J	13	1 U	16	18	1 U	1 U	23	41	24

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-205B	04/22/99		0.73	23	3.4	74	47	5 U	10 U	3.5	310	57
MW-205B	10/21/99		25 U	23 J	25 U	82	54	25 U	50 U	3.4 J	340	58
MW-205B	02/07/00		25 U	24 J	25 U	86	57	25 U	50 U	3.8 J	360	60
MW-205B	04/18/00		20 U	26	20 U	90	59	20 U	40 JB	3.8 J	370	65
MW-205B	07/25/00		20 U	23	20 U	70	52	20 U	40 U	20 U	270	44
MW-205B	11/07/00		20 U	31	2.9	79	55	20 U	40 U	3.6	270	53
MW-205B	04/09/01		20 U	31	20 U	110	68	20 U	40 U	4.5	330	67
MW-205B	10/16/01		20 U	21	20 U	73	50	20 U	40 U	5.1	250	45
MW-205B	04/16/02		0.82	22	10 U	59	53	1.4	0.7	5.8	220	48
MW-205B	10/07/02		50 U	50 U	50 U	470	65	50 U	90	110	310	49
MW-205B	04/22/03		0.75 J	24.2	1.79	92.4 E	59.6 E	1 U	2 U	11.4	303 E	63.8 E
MW-205B	04/22/03	Dilution	20 U	23.7	20 U	93.1	57.3	20 U	40 U	10 J	262	60.4
MW-205B	12/22/03		0.7 J	21.6	1.36	70.5 E	53.8 E	0.55 J	1 U	13	239 E	52.1 E
MW-205B	12/22/03	Dilution	20 U	18.7 JD	20 U	64.9 D	47.1 D	20 U	20 U	10.5 JD	201 D	44.6 D
MW-205B	04/28/04		20 U	22.4	20 U	75.5	54.4	20 U	40 U	11.4	233	49.3
MW-205B	05/21/05		1 U	17	1 U	43	47	1 U	2 U	13	110	34
MW-205B	10/19/05		1 U	17	1 U	32	43	1 U	2 U	14	89	31
MW-205B	05/06/06		1 U	18	1 U	26	52	1 U	2 U	23	59	31
MW-205B	11/21/06		1 U	18	1 U	39	71	1 U	2 U	23	95	44
MW-205B	10/06/07		0.4	15	0.4	30	52	1 U	2 U	18	66	31
MW-205B	05/18/08		4 U	16	4 U	30	63	4 U	8 U	22	69	34
MW-205B	11/28/08		0.49 J	15	0.38 J	19.9	43.1	1 U	1 U	12.8	79.4	24.6
MW-205B	06/09/09		0.49 J	15	0.25 J	21	44	1 U	1 U	18	63	29
MW-205B	11/25/09		0.55 J	14	1 U	21	37	1 U	1 U	21	47	27
MW-205B	06/24/10		0.38 J	14	0.16 J	17	29	1 U	1 U	22	43	23
MW-205B	11/25/10		0.41 J	15	1 U	17	23	1 U	1 U	23	42	24

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-206A	04/23/99		0.64	8.5	0.75	22	23	2 U	4 U	9.3	100	37
MW-206A	10/20/99		10 U	9.8 J	10 U	21	21	10 U	20 U	6.6 J	87	33
MW-206A	02/07/00		0.55 J	10	5 U	14	20	5 U	10 U	7	79	25
MW-206A	04/18/00		0.55 J	9.6	5 U	12	20	0.36 J	10 JB	5.2	62	22
MW-206A	07/25/00		0.72	9.4	5 U	14	21	5 U	10 U	3.1	66	16
MW-206A	11/07/00		5 U	12	5 U	5.9	13	5 U	10 U	0.84	46	7.6
MW-206A	04/09/01		0.66	9.7	5 U	13	20	5 U	10 U	4.5	55	22
MW-206A	10/16/01		0.49	8.8	2 U	9.9	18	2 U	0.34	3.5	39	18
MW-206A	04/16/02		0.39	7.1	2 U	7.1	15	0.39	4 U	3.4	31	16
MW-206A	10/08/02		5 U	11	5 U	57	23	5 U	10 U	3	35	18
MW-206A	04/21/03		0.87 J	11.8	1 U	11.7	30.3 E	1.05	2 U	3.48	31.1 E	18.1
MW-206A	04/21/03	Dilution	2 U	11	2 U	11.1	28.4	2 U	4 U	3.17	26.9	17
MW-206A	12/22/03		1.04	14.5	1 U	13.9	38.4 E	1.4	1 U	3.99	35.8 E	19
MW-206A	12/22/03	Dilution	2 U	12.4 D	2 U	11.4 D	33.6 D	1.11 JD	2 U	3.36 D	29.8 D	16.5 D
MW-206A	04/28/04		1.28	10.7	2 U	11.1	31.6	2 U	4 U	3.65	27.4	15.1
MW-206A	05/21/05		1.1	5.6	1 U	6.7	16	1 U	2 U	2.9	17	11
MW-206A	10/19/05		1 U	8.1	1 U	8.8	23	1 U	2 U	3.1	19	11
MW-206A	05/06/06		1 U	9.2	1 U	9.1	25	1 U	2 U	3.8	23	13
MW-206A	11/27/06		1.1	9	1 U	8.2	14	1 U	2 U	4.2	22	14
MW-206A	10/06/07		0.6	5	1 U	5	6	1 U	2 U	3	14	9
MW-206A	05/18/08		1 U	6	1 U	8	7	1 U	2 U	4	18	11
MW-206A	11/28/08		0.28 J	13	0.19 J	7.54	9.43	0.21 J	1 U	1.95	17.9	7.85
MW-206A	06/10/09		0.41 J	11	1 U	7.5	7.3	1 U	1 U	2.8	23	9.9
MW-206A	04/01/10		0.27 J	7.6	1 U	6.8	4.2	1 U	1 U	3.7	18	10
MW-206A	06/25/10		0.28 J	8.3	1 U	7.1	4.2	1 U	1 U	3.8	18	9.3
MW-206A	11/29/10		0.16 J	13	1 U	4.4	4.5	1 U	1 U	1.5	9.7	4.3

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-206B	04/23/99		10 U	5.1	10 U	2.5	59	10 U	20 U	13	4.6	150
MW-206B	10/20/99		10 U	9.1 J	10 U	4.9 J	54	10 U	1.3 J	9.6 J	8.4 J	160
MW-206B	02/17/00		10 U	13	10 U	8.8 J	36	10 U	20 U	5.8 J	16	150
MW-206B	04/18/00		0.62 J	14	10 U	9 J	40	0.28 J	20 JB	5.6 J	16	150
MW-206B	07/25/00		0.6	12	5 U	6	36	5 U	10 U	0.98	11	86
MW-206B	11/07/00		5 U	17	5 U	8.4	34	5 U	10 U	3.3	14	120
MW-206B	04/09/01		0.51	14	5 U	9.1	33	5 U	10 U	2.5	16	110
MW-206B	10/16/01		0.62	14	5 U	11	26	5 U	10 U	1.7	20	80
MW-206B	04/16/02		0.69	12	5 U	10	23	5 U	10 U	1.5	20	70
MW-206B	10/08/02		5 U	22	5 U	76	31	5 U	4	5 U	35	100
MW-206B	04/22/03		0.83 J	16.2	0.7 J	16.8	22.1	1 U	2 U	1.35	32.5 E	75.7 E
MW-206B	04/22/03	Dilution	5 U	15.1	5 U	15.7	20.5	5 U	10 U	5 U	27.2	68.7
MW-206B	12/22/03		0.88 J	17.3	0.71 J	18.2	21.5	1 U	1 U	1.34	34 E	68.8 E
MW-206B	12/22/03	Dilution	4 U	14.8 D	4 U	14 D	17.4 D	4 U	4 U	4 U	26.5 D	54.5 D
MW-206B	04/28/04		4 U	16	4 U	14.2	19.5	4 U	8 U	4 U	26.3	59.2
MW-206B	05/21/05		1 U	16	1 U	13	13	1 U	2 U	1 U	22	33
MW-206B	10/19/05		1 U	16	1 U	12	13	1 U	2 U	1 U	22	35
MW-206B	05/06/06		1 U	24	1 U	17	15	1 U	2 U	1 U	24	32
MW-206B	11/27/06		1 U	47	1.4	31	21	1 U	2 U	1.2	44	45
MW-206B	10/06/07		0.8	50	1	39	32	1 U	2 U	1	39	28
MW-206B	05/18/08		4 U	56	4 U	46	50	4 U	8 U	4 U	44	48
MW-206B	11/28/08		0.92 J	57.7	1.74	40.9	45.8	0.2 J	1 U	1.71	39.9	35.6
MW-206B	06/10/09		1	79	2.3	63	70	0.33 J	1 U	3.3	57	37
MW-206B	04/01/10		0.97 J	77	2.3	77	76	0.57 J	1 U	4.4	58	38
MW-206B	06/25/10		1	84	2.4	77	90	0.39 J	1 U	4.9	64	37
MW-206B	11/29/10		0.92 J	78	2.3	71	72	0.53 J	1 U	5.5	55	34

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-206C	04/23/99		1 U	1 U	1 U	0.31	2.7	1 U	2 U	0.41	1.5	4.1
MW-206C	10/20/99		1 U	0.18 J	1 U	0.15 J	2.3	1 U	2 U	1 U	0.26 J	4.3
MW-206C	02/07/00		1 U	1 U	1 U	1 U	3.5	1 U	2 U	1 U	1 U	5.3
MW-206C	04/18/00		1 U	1 U	1 U	1 U	4	1 U	2 JB	1 U	1 U	6
MW-206C	07/25/00		1 U	1 U	1 U	1.3	4.8	1 U	2 U	1 U	1 U	3.5
MW-206C	11/07/00		1 U	0.14	1 U	0.12	2.3	1 U	2 U	1 U	0.29	3.4
MW-206C	04/09/01		1 U	0.36	1 U	0.28	4.3	1 U	2 U	0.25	0.7	6.6
MW-206C	10/16/01		1 U	0.24	1 U	0.11	5.9	1 U	2 U	0.2	0.18	7.6
MW-206C	04/16/02		1 U	1 U	1 U	0.17	6.9	1 U	2 U	0.06	1 U	14
MW-206C	10/08/02		5 U	5 U	5 U	5 U	15	5 U	4	5 U	5 U	30
MW-206C	04/22/03		1 U	0.86 J	1 U	0.55 J	14.4	1 U	2 U	1 U	1 U	43 E
MW-206C	04/22/03	Dilution	2.5 U	2.5 U	2.5 U	2.5 U	13.2	2.5 U	5 U	2.5 U	2.5 U	39.1
MW-206C	12/22/03		1 U	1.37	1 U	1.68	16.6	0.61 J	1 U	1 U	1 U	53 E
MW-206C	12/22/03	Dilution	4 U	4 U	4 U	4 U	14 D	4 U	4 U	4 U	4 U	44.7 D
MW-206C	04/28/04		2 U	1.21	2 U	2 U	14.9	2 U	4 U	2 U	2 U	37.7
MW-206C	05/21/05		1 U	1.5	1 U	1.1	9.2	1 U	2 U	1 U	1 U	34
MW-206C	10/19/05		1 U	3.8	1 U	2.6	15	1 U	0.1	1 U	1 U	47
MW-206C	05/06/06		1 U	5	1 U	3.5	14	1 U	2 U	1 U	1 U	52
MW-206C	11/27/06		1 U	6.5	1 U	4.4	17	1 U	2 U	1 U	1 U	85
MW-206C	10/06/07		1 U	5	1 U	4	11	1 U	2 U	0.4	1 U	44
MW-206C	05/18/08		2 U	5	2 U	4	12	2 U	4 U	2 U	2 U	38
MW-206C	11/28/08		1 U	3.11	1 U	2.01	5.23	1 U	1 U	1 U	1 U	19.4
MW-206C	06/10/09		1 U	2.7	1 U	1.8	4.8	1 U	1 U	1 U	1 U	16
MW-206C	04/01/10		1 U	3.4	1 U	2.7	4.8	1 U	1 U	1 U	1 U	16
MW-206C	06/25/10		1 U	5.2	1 U	3.6	6.5	1 U	1 U	1 U	1 U	20
MW-206C	11/29/10		1 U	3.9	1 U	3.1	5.1	1 U	1 U	1 U	1 U	16

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE
		MCL	NA	NA	5	7	70	100	5	5	200	5
MW-207	04/23/99		0.39	0.76	2 U	2 U	1.6	2 U	4 U	2.6	2.7	26
MW-207	10/27/99		0.59 J	1.3	1 U	0.74 J	5.1	0.06 J	2 U	3.9	5.9	25
MW-207	02/17/00		0.54 J	1.1	1 U	0.22 J	1.2	1 U	2 U	2.8	2	22
MW-207	04/18/00		0.62 J	1.2	1 U	0.1 J	1.2	0.1 J	2 JB	2.7	2	20
MW-207	07/25/00		0.63	1.3	1 U	1 U	1.4	0.16	2 U	2.1	2	17
MW-207	11/08/00		0.71	2.1	1 U	0.24	1.4	1 U	2 U	2.3	1.9	16
MW-207	04/10/01		0.6	1.5	1 U	1 U	3.2	0.44	2 U	0.51	1.5	11
MW-207	10/16/01		0.44	5.3	1 U	0.13	3.4	0.33	2 U	1	4.2	22
MW-207	04/17/02		0.36	6.2	2 U	0.26	3.7	0.39	4 U	1.4	5.7	25
MW-207	10/08/02		1 U	8	1 U	6	5	1 U	0.8	0.9	5	21
MW-207	04/22/03		0.54 J	7.42	1 U	1.8	5.09	1 U	2 U	2.5	8.37	29.3 E
MW-207	04/22/03	Dilution	2 U	7.05	2 U	2.13	4.88	2 U	4 U	2.3	7.6	27.8
MW-207	12/28/03		0.53 J	6.12	1 U	2.64	4.5	1 U	1 U	2.58	8.64	29.4 E
MW-207	12/28/03	Dilution	2 U	5.68 D	2 U	2.18 D	3.78 D	2 U	2 U	2.21 D	7.19 D	25.8 D
MW-207	04/28/04		2 U	5.87	2 U	1.85	4.26	2 U	4 U	2.67	8.24	28.1
MW-207	05/21/05		1 U	4.3	1 U	1.7	3	1 U	2 U	2.1	5.4	18
MW-207	10/19/05		1 U	4.5	1 U	1 U	2.7	1 U	2 U	1.3	5.7	17
MW-207	05/06/06		1 U	5.2	1 U	1.8	3.3	1 U	2 U	2	6.7	19
MW-207	11/27/06		1 U	5.7	1 U	1.1	3.1	1 U	2 U	2.6	9.3	24
MW-207	10/07/07		0.4	4	1 U	0.7	3	1 U	1 U	2	7	15
MW-207	05/18/08		1 U	4	1 U	2	3	1 U	2 U	2	7	15
MW-207	11/29/08		0.36 J	2.97	1 U	1 U	1.89	0.27 J	1 U	1.98	5.58	10.8
MW-207	06/10/09		0.31 J	2.4	1 U	0.65 J	1.8	1 U	1 U	2.1	4.6	9.9
MW-207	11/25/09		1 U	1.6	1 U	0.6 J	1.2	1 U	1 U	2.2	3.5	7.4
MW-207	06/24/10		0.18 J	1.3	1 U	0.52 J	1	1 U	1 U	1.9	2.8	5.6
MW-207	11/25/10		0.22 J	1.3	1 U	0.72 J	1.3	1 U	1 U	2.2	3	6

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Results reported in micrograms per liter (µg/l)

Highlighted results equal or exceed the Maximum Contaminant Level (MCL)

CFM	Chloroform
1,1-DCA	1,1-Dichloroethane
1,2-DCA	1,2-Dichloroethane
1,1-DCE	1,1-Dichloroethene
c1,2-DCE	cis- 1,2-Dichloroethene
t1,2-DCE	trans-1,2-Dichloroethene
MC	Methylene Chloride
PCE	Tetrachloroethene
1,1,1-TCA	1,1,1-Trichloroethane
TCE	Trichloroethene

B	Concentration is less than the reporting limit but greater than the instrument detection limit.
D	Reported concentration is based on an analysis requiring a secondary detection limit.
E	The associated value exceeds the calibration range.
J	The reported concentration is estimated.
U	Analyte was not detected at or above the reporting limit.

Fld Dupe	Field Duplicate
Fld Dupe Dln	Field Duplicate Dilution

Southeast Rockford Superfund Site
Monitoring Wells Near Area 7

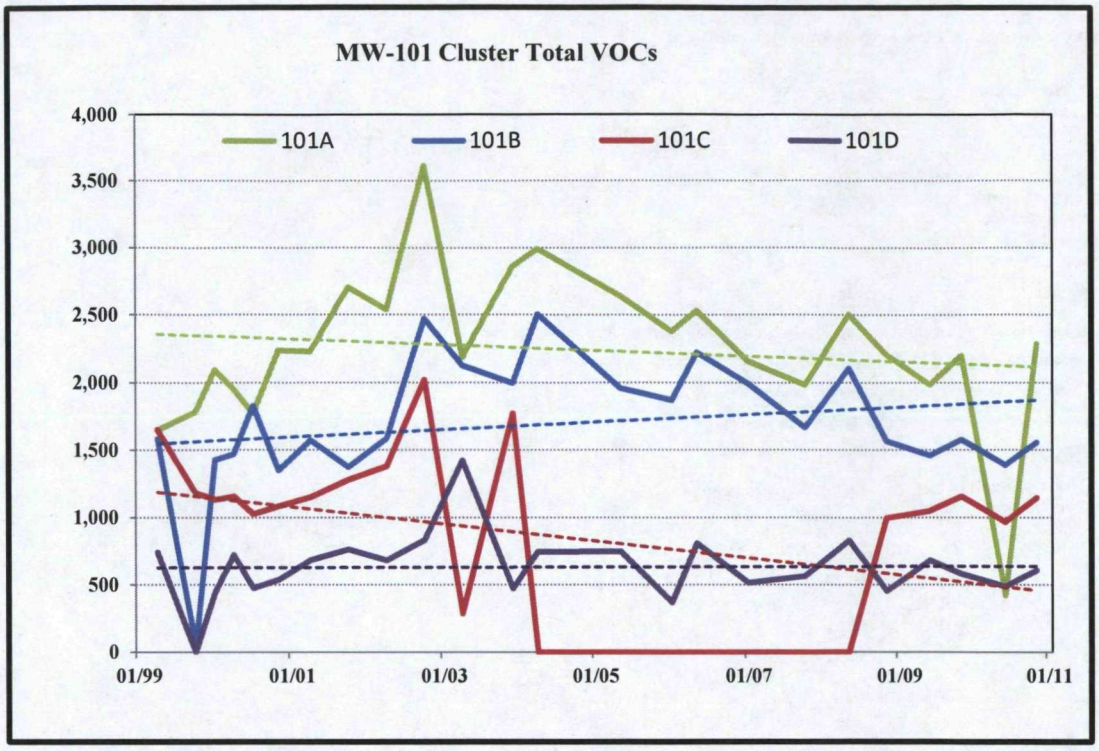

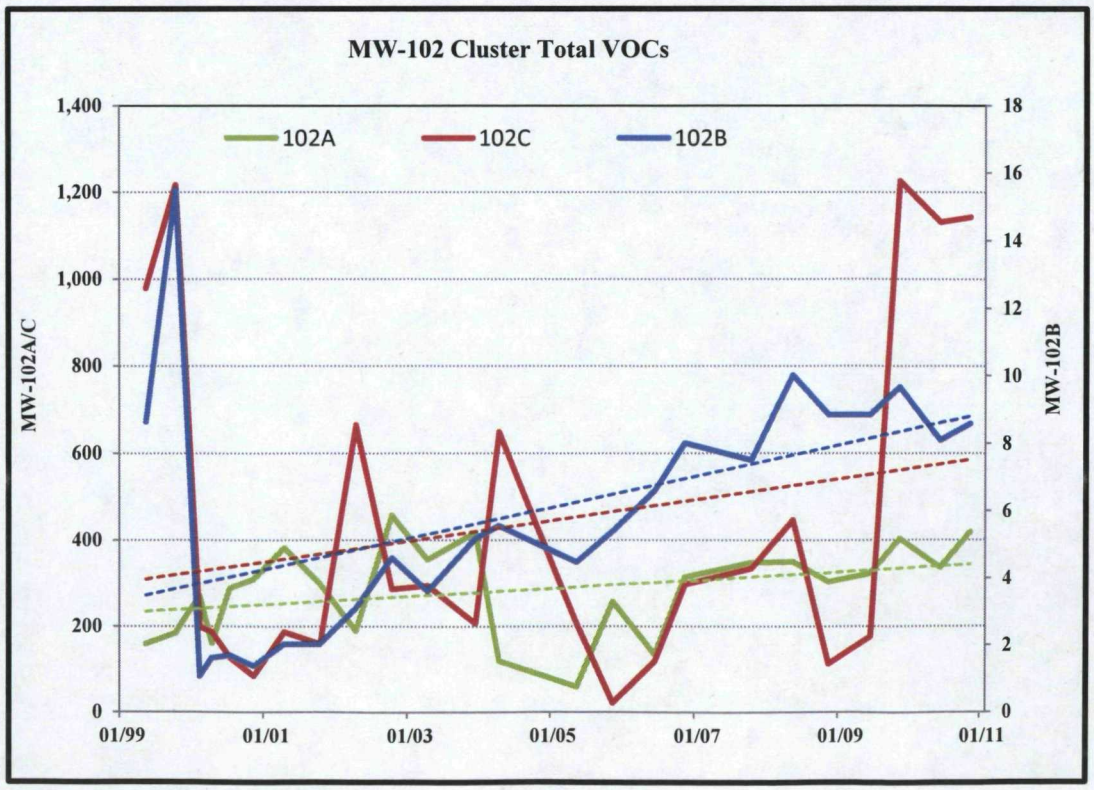

Y-axis = Total VOCs in parts per billion; X- axis = Sampling Date

Southeast Rockford Superfund Site
Monitoring Wells Near Area 7

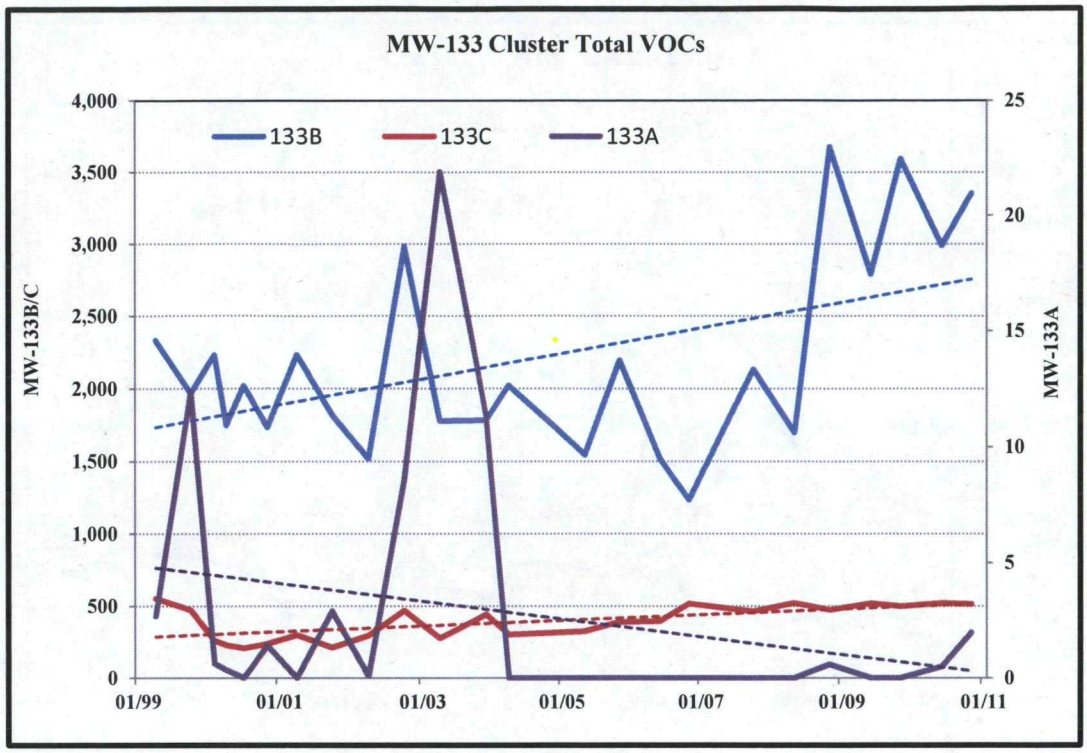

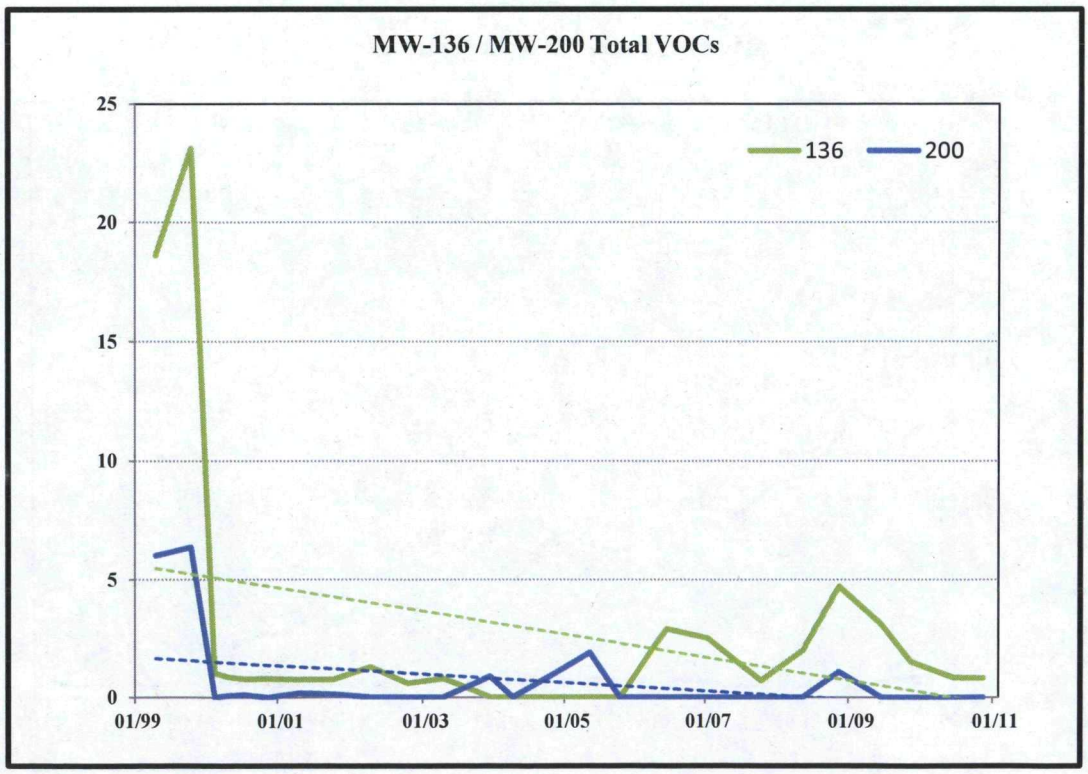

Y-axis = Total VOCs in parts per billion; X- axis = Sampling Date

Southeast Rockford Superfund Site
Monitoring Wells Near Areas 4, 9/10, 11

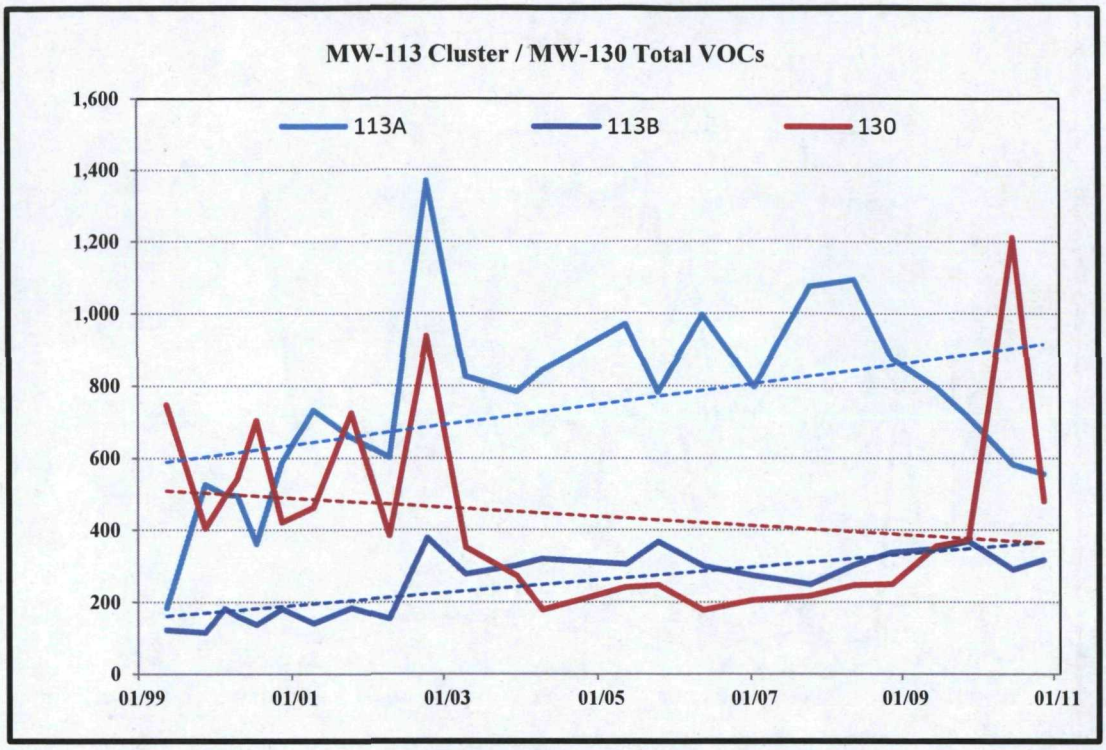

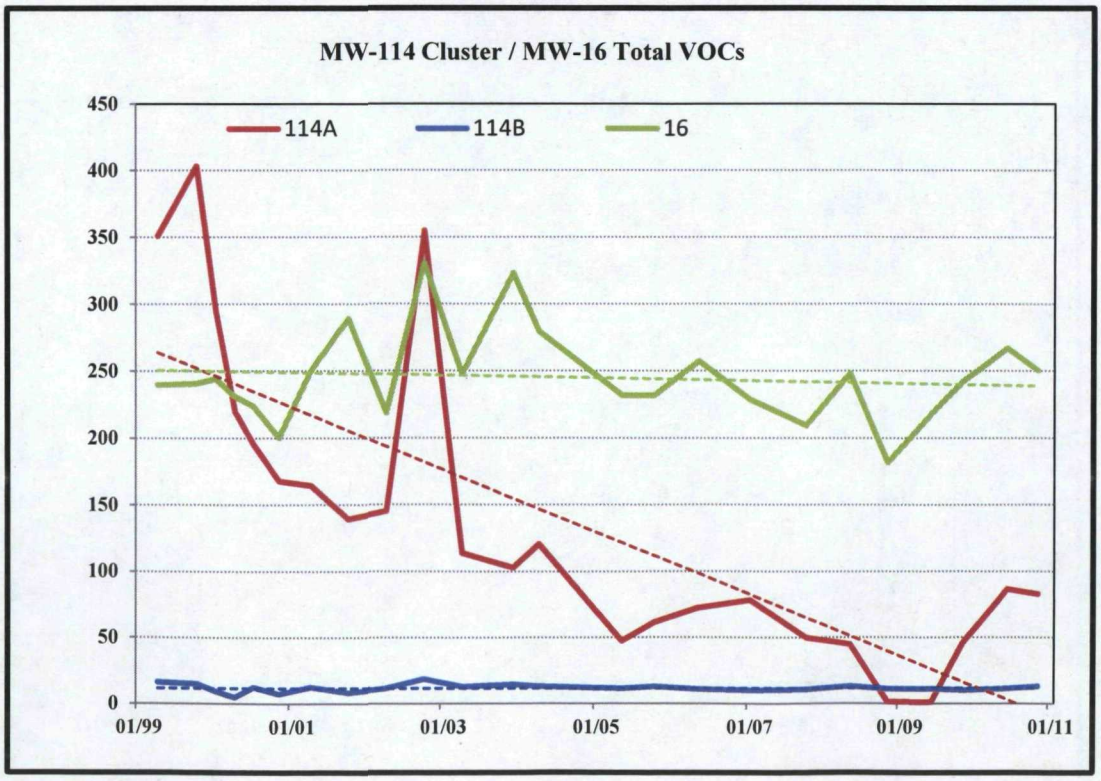

Y-axis = Total VOCs in parts per billion; X- axis = Sampling Date

Southeast Rockford Superfund Site
Monitoring Wells Near Areas 4, 9/10, 11

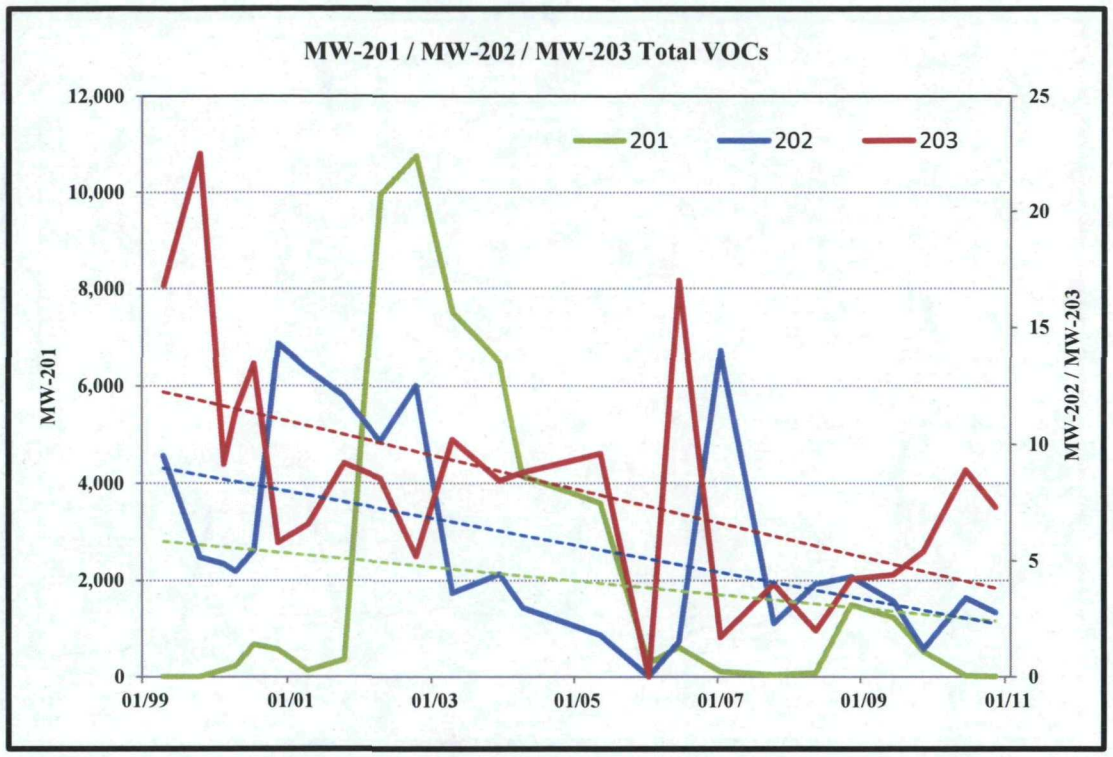

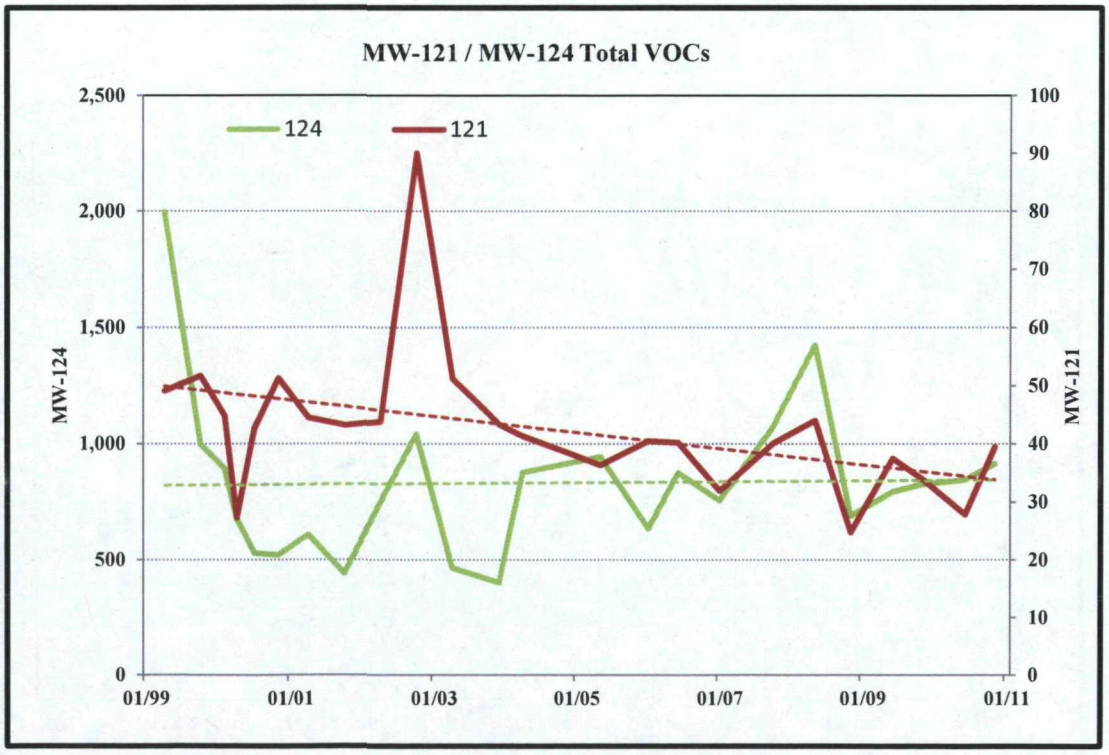

Y-axis = Total VOCs in parts per billion; X- axis = Sampling Date

Southeast Rockford Superfund Site
Monitoring Wells Near Rock River

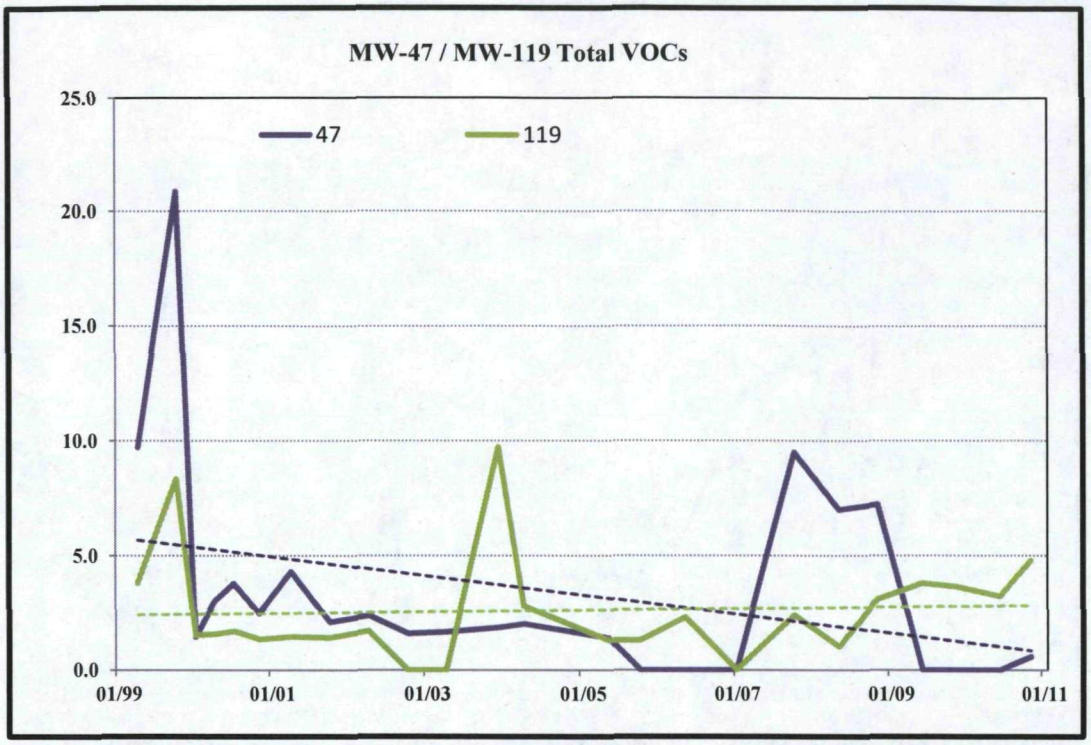

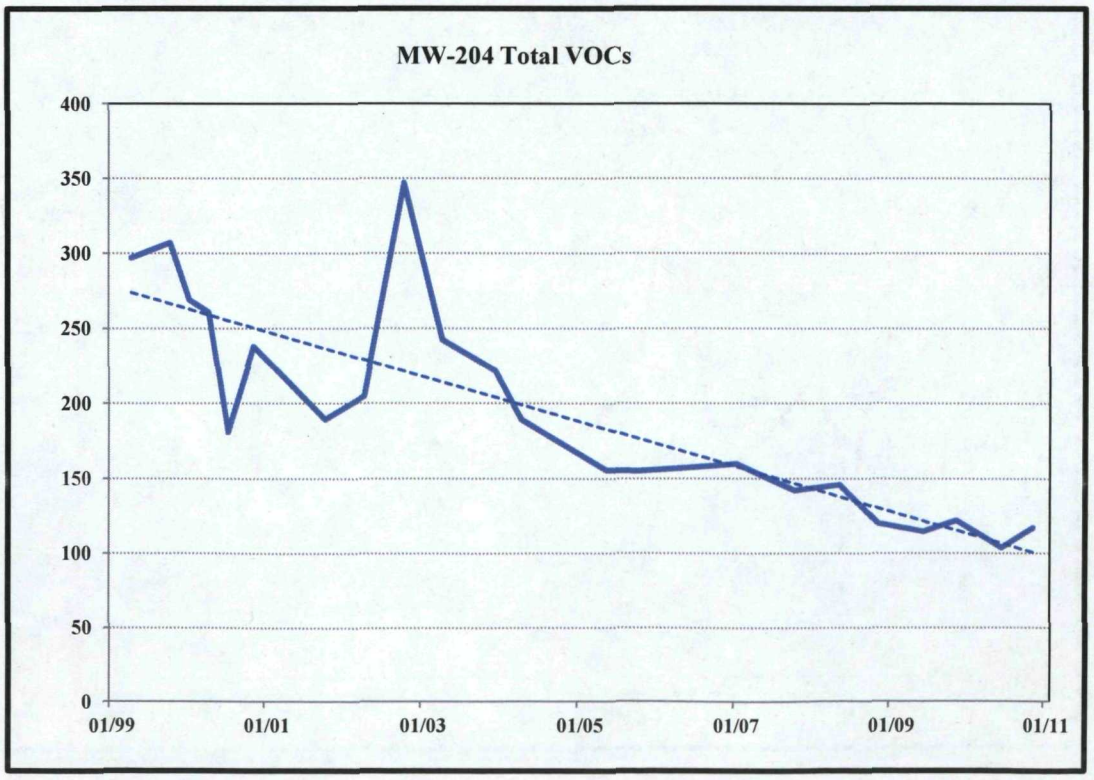

Y-axis = Total VOCs in parts per billion; X- axis = Sampling Date

Southeast Rockford Superfund Site
Monitoring Wells Near Rock River

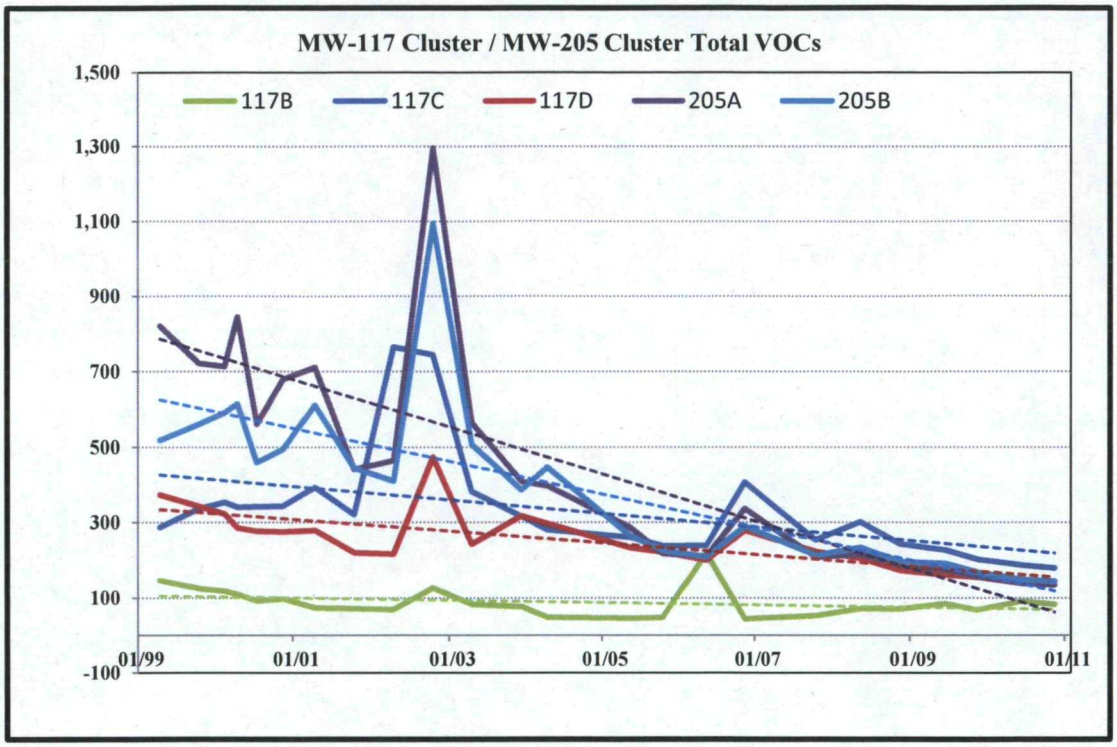

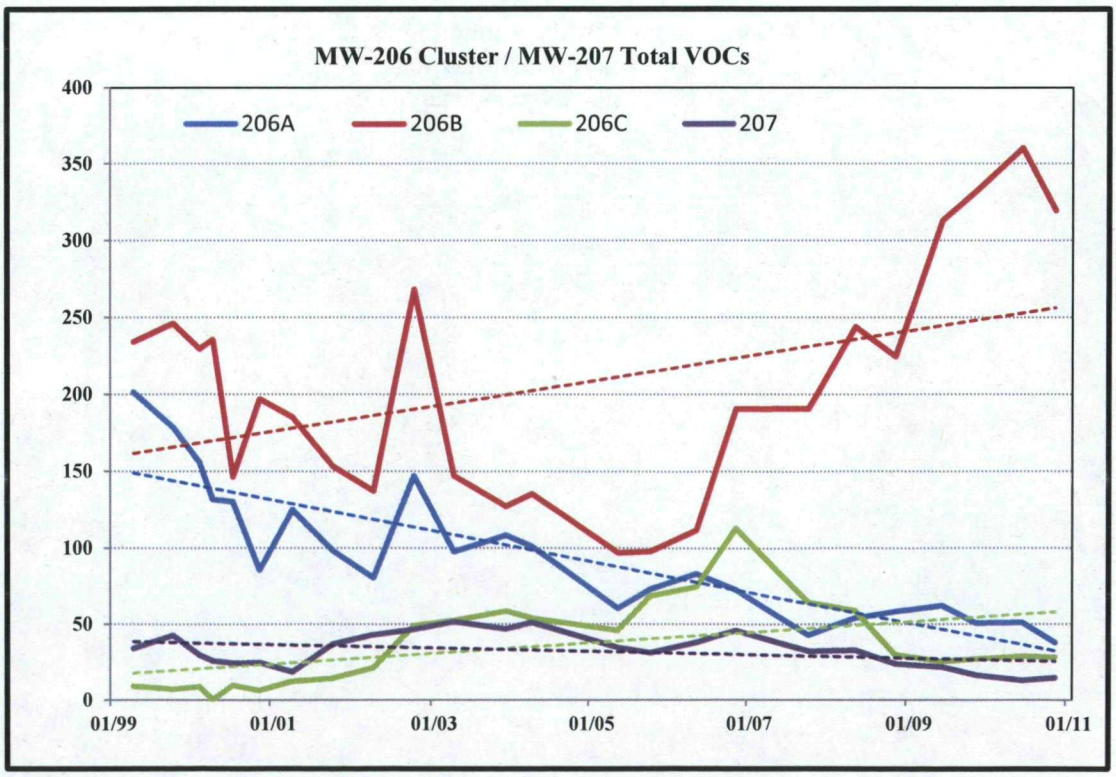

Y-axis = Total VOCs in parts per billion; X- axis = Sampling Date

APPENDIX A
Ground Water Monitoring
Laboratory Data Sheets and
Data Validation Summary

Data Quality Control Criteria Review Summary

SDG Number: 1011494 **Project Number:** 1016-2
Site: SE Rockford, 24th Event
Contractor Lab: TriMatrix (Grand Rapids, MI)
Validator: Brian LaFlamme **Validation Date:** 01/14/11
Sample Matrix: Water **Sample Date:** 11/24/10 – 11/29/10
Analytical Methods: EPA SW-846 Method 8260B
Sample Designations:

MW-16	**MW-102C**	**MW-119**	**MW-200**	**MW-206B**
MW-47	**MW-113A**	**MW-121**	**MW-201**	**MW-206C**
MW-101A	**MW-113B**	**MW-124**	**MW-202**	**MW-207**
MW-101B	**MW-114A**	**MW-130**	**MW-203**	**FD-1 (field duplicate of MW-102A)**
MW-101C	**MW-114B**	**MW-133A**	**MW-204**	**FD-1 (field duplicate of MW-133A)**
MW-101D	**MW-117B**	**MW-133B**	**MW-205A**	**Trip Blank**
MW-102A	**MW-117C**	**MW-133C**	**MW-205B**	
MW-102B	**MW-117D**	**MW-136**	**MW-206A**	

The analytical data were reviewed in accordance with the analytical methods, SW-846 validation guidelines, and the Environmental Protections Agency (EPA) Contract Laboratory Program (CLP) National Functional Guidelines. The review included comparing quality control (QC) values provided on the laboratory QC forms to method QC criteria. Review of the raw data was not performed.

Quality Control Summary

QC Review Item	VOA
Completeness	X
Case Narrative	X
Chain of Custody (COC) Forms	X
Sample Preservation	X
Holding Times	X
Laboratory Blank Results	1
System Monitoring Compounds (Surrogate) Results	X
Matrix Spike/Matrix Duplicate (MS/MSD) Results	2
Laboratory Control Sample (LCS) Results	3
Method Specific QC Results *	NA
System Performance	X
Field QC Results #	4
Other	X

X Acceptable, no qualification necessary NR Not required
See validation summary comment NA Not applicable
*) The reviewer has indicated in the comments, if necessary, the method specific QC results included in the data package that were reviewed.
#) Field QC may include field duplicates, trip blanks, rinse blanks, field blanks, and equipment blank samples as required by project specific criteria.

Data for the above samples are:

- [x] Acceptable for use
- [ ] Acceptable for use as qualified
- [ ] Unacceptable for use

Is action required by the Project Manager?

Yes ☐ No ☒

Data Validation Summary Comments:

1. Acetone was detected in the method blank at 2.3J µg/l for QC batch 1013276. Acetone was detected in the sample collected from MW-136 2.7 µg/l. This detection has been qualified as 5U.

   1,4-Dichlorobenzene was detected in the method blank 0.23J µg/l for QC batch 1013277. 1,4-Dichlorobenzene was not detected in any investigative samples. Therefore, no qualification is necessary.

2. Recoveries in either the MS or MSD did not meet QC criteria as follows:

QC Batch	Analyte	QC Samples	Spike % Recovery	Control Limits
1013275	Carbon Tetrachloride	MS	130	83-126
	Dibromochloromethane	MS	115	74-110
	Dibromochloromethane	MSD	120	74-110
1013276	Carbon Tetrachloride	MS	130	83-126
	Dibromochloromethane	MS	120	74-110
	Dibromochloromethane	MSD	114	74-110

   The LCS recoveries for these samples were within control limits. The only detection in an investigative sample was MW-133C at 0.63J µg/l. No qualification is necessary.

3. Recoveries in the LCS did not meet QC criteria as follows:

QC Batch	Analyte	Spike % Recovery	Control Limits
1013275	1,1,2,2-Tetrachloroethane	80	81-127

   There were no detections in the investigative samples. Therefore, no qualification is necessary.

4. Results of field duplicates follows:

Sample	Analyte	Investigative Sample (µg/l)	Duplicate Sample (µg/l)
MW-102A/FD1	Chloroform	2.0U	2.0U
	1,1-Dichloroethane	99	95
	1,2-Dichloroethane	2.0U	2.0U
	1,1-Dichloroethene	3.0	2.7
	cis-1,2-Dichloroethene	200	200
	trans-1,2-Dichloroethene	5.3	4.9
	Methylene Chloride	2.0U	2.0U
	Tetrachloroethene	2.0U	2.0U
	1,1,1-Trichloroethane	90	87
	Trichloroethene	20	19
MW-133A/FD2	Chloroform	1.0U	1.0U
	1,1-Dichloroethane	0.21J	1.0U
	1,2-Dichloroethane	1.0U	1.0U
	1,1-Dichloroethene	1.0U	1.0U
	cis-1,2-Dichloroethene	0.91J	0.79J

Sample	Analyte	Investigative Sample (µg/l)	Duplicate Sample (µg/l)
MW-133A/FD2	trans-1,2-Dichloroethene	1.0U	1.0U
	Methylene Chloride	1.0U	1.0U
	Tetrachloroethene	1.0U	1.0U
	1,1,1-Trichloroethane	0.86J	0.82J
	Trichloroethene	1.0U	1.0U

As shown, the investigative and duplicate sample results are in good agreement with each other. Therefore, the samples collected during this quarter are deemed representative of Site conditions at the time of sample collection.

Analytes were not reported in the trip blank (Trip Blank).

OVERALL ASSESSMENT OF DATA

Based on the review of the quality control criteria, the method appeared to be in control. Therefore, the data are acceptable for use.

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW16**	Sampled:	11/27/10 15:00
Lab Sample ID:	**1011494-23**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/03/10 By: JDM
Dilution Factor:	2	Analyzed:	12/03/10 By: JDM
QC Batch:	1013276	Analytical Batch:	0L04003

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	10U	10	3.6
71-43-2	Benzene	2.0U	2.0	0.25
74-97-5	Bromochloromethane	2.0U	2.0	0.23
75-27-4	Bromodichloromethane	2.0U	2.0	0.28
75-25-2	Bromoform	2.0U	2.0	0.23
74-83-9	Bromomethane	2.0U	2.0	0.23
75-15-0	Carbon Disulfide	10U	10	1.2
56-23-5	Carbon Tetrachloride	2.0U	2.0	0.42
108-90-7	Chlorobenzene	2.0U	2.0	0.13
75-00-3	Chloroethane	2.0U	2.0	0.36
67-66-3	Chloroform	**1.4J**	2.0	0.15
74-87-3	Chloromethane	2.0U	2.0	0.21
96-12-8	1,2-Dibromo-3-chloropropane	2.0U	2.0	0.83
124-48-1	Dibromochloromethane	2.0U	2.0	0.30
106-93-4	1,2-Dibromoethane	2.0U	2.0	0.19
95-50-1	1,2-Dichlorobenzene	2.0U	2.0	0.55
541-73-1	1,3-Dichlorobenzene	2.0U	2.0	0.43
106-46-7	1,4-Dichlorobenzene	2.0U	2.0	0.42
75-34-3	1,1-Dichloroethane	**78**	2.0	0.35
107-06-2	1,2-Dichloroethane	2.0U	2.0	0.30
75-35-4	1,1-Dichloroethene	**24**	2.0	0.34
156-59-2	cis-1,2-Dichloroethene	**45**	2.0	0.39
156-60-5	trans-1,2-Dichloroethene	**1.6J**	2.0	0.20
78-87-5	1,2-Dichloropropane	2.0U	2.0	0.38
10061-01-5	cis-1,3-Dichloropropene	2.0U	2.0	0.29
10061-02-6	trans-1,3-Dichloropropene	2.0U	2.0	0.37
100-41-4	Ethylbenzene	2.0U	2.0	0.088
591-78-6	2-Hexanone	10U	10	2.7
75-09-2	Methylene Chloride	2.0U	2.0	0.38
78-93-3	2-Butanone (MEK)	10U	10	3.0
108-10-1	4-Methyl-2-pentanone (MIBK)	10U	10	1.7

Continued on next page

VALIDATED

Reviewed By _____

Date 1/14/11

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW16**	Sampled:	11/27/10 15:00
Lab Sample ID:	**1011494-23**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/03/10 By: JDM
Dilution Factor:	2	Analyzed:	12/03/10 By: JDM
QC Batch:	1013276	Analytical Batch:	0L04003

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	2.0U	2.0	0.21
79-34-5	1,1,2,2-Tetrachloroethane	2.0U	2.0	0.43
127-18-4	Tetrachloroethene	**10**	2.0	0.49
108-88-3	Toluene	2.0U	2.0	0.16
71-55-6	1,1,1-Trichloroethane	**180**	2.0	0.27
79-00-5	1,1,2-Trichloroethane	2.0U	2.0	0.27
79-01-6	Trichloroethene	**60**	2.0	0.17
75-01-4	Vinyl Chloride	2.0U	2.0	0.11
1330-20-7	Xylene (Total)	6.0U	6.0	0.81

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	106	*88-115*
1,2-Dichloroethane-d4	101	*81-116*
Toluene-d8	99	*87-113*
4-Bromofluorobenzene	92	*78-116*

VALIDATED

Reviewed By [illegible]

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.942.5500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW47**	Sampled:	11/29/10 15:36
Lab Sample ID:	**1011494-37**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/04/10 By: JDM
Dilution Factor:	1	Analyzed:	12/05/10 By: JDM
QC Batch:	1013277	Analytical Batch:	0L04004

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	5.0U	5.0	1.8
71-43-2	Benzene	1.0U	1.0	0.13
74-97-5	Bromochloromethane	1.0U	1.0	0.11
75-27-4	Bromodichloromethane	1.0U	1.0	0.14
75-25-2	Bromoform	1.0U	1.0	0.12
74-83-9	Bromomethane	1.0U	1.0	0.11
75-15-0	Carbon Disulfide	5.0U	5.0	0.60
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.21
108-90-7	Chlorobenzene	1.0U	1.0	0.065
75-00-3	Chloroethane	1.0U	1.0	0.18
67-66-3	Chloroform	1.0U	1.0	0.077
74-87-3	Chloromethane	1.0U	1.0	0.10
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.41
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.096
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.27
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.21
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.21
75-34-3	1,1-Dichloroethane	**0.27J**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.15
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.17
156-59-2	cis-1,2-Dichloroethene	1.0U	1.0	0.19
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.10
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.19
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.15
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.044
591-78-6	2-Hexanone	5.0U	5.0	1.3
75-09-2	Methylene Chloride	1.0U	1.0	0.19
78-93-3	2-Butanone (MEK)	5.0U	5.0	1.5
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.87

VALIDATED

Continued on next page

Reviewed By _____

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7453 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW47**	Sampled:	11/29/10 15:36
Lab Sample ID:	**1011494-37**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/04/10 By: JDM
Dilution Factor:	1	Analyzed:	12/05/10 By: JDM
QC Batch:	1013277	Analytical Batch:	0L04004

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.22
127-18-4	Tetrachloroethene	1.0U	1.0	0.24
108-88-3	Toluene	1.0U	1.0	0.081
71-55-6	1,1,1-Trichloroethane	**0.30J**	1.0	0.13
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.13
79-01-6	Trichloroethene	1.0U	1.0	0.084
75-01-4	Vinyl Chloride	1.0U	1.0	0.054
1330-20-7	Xylene (Total)	3.0U	3.0	0.40

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	99	*88-115*
1,2-Dichloroethane-d4	98	*81-116*
Toluene-d8	96	*87-113*
4-Bromofluorobenzene	94	*78-116*

VALIDATED

Reviewed By _____

Date 1/14/11

This report shall not be reproduced except in full without written approval of Trimatrix Laboratories, Inc.
Individual sample results relate only to the samples tested.

3560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7314 ♦ www.trimatrixlab.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW101A**	Sampled:	11/26/10 14:20
Lab Sample ID:	**1011494-15**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/03/10 By: JDM
Dilution Factor:	10	Analyzed:	12/03/10 By: JDM
QC Batch:	1013276	Analytical Batch:	0L04003

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	50U	50	18
71-43-2	Benzene	10U	10	1.3
74-97-5	Bromochloromethane	10U	10	1.1
75-27-4	Bromodichloromethane	10U	10	1.4
75-25-2	Bromoform	10U	10	1.2
74-83-9	Bromomethane	10U	10	1.1
75-15-0	Carbon Disulfide	50U	50	6.0
56-23-5	Carbon Tetrachloride	10U	10	2.1
108-90-7	Chlorobenzene	10U	10	0.65
75-00-3	Chloroethane	10U	10	1.8
67-66-3	Chloroform	**3.2J**	10	0.77
74-87-3	Chloromethane	10U	10	1.0
96-12-8	1,2-Dibromo-3-chloropropane	10U	10	4.1
124-48-1	Dibromochloromethane	10U	10	1.5
106-93-4	1,2-Dibromoethane	10U	10	0.96
95-50-1	1,2-Dichlorobenzene	10U	10	2.7
541-73-1	1,3-Dichlorobenzene	10U	10	2.1
106-46-7	1,4-Dichlorobenzene	10U	10	2.1
75-34-3	1,1-Dichloroethane	**280**	10	1.8
107-06-2	1,2-Dichloroethane	10U	10	1.5
75-35-4	1,1-Dichloroethene	**68**	10	1.7
156-59-2	cis-1,2-Dichloroethene	**1100**	10	1.9
156-60-5	trans-1,2-Dichloroethene	**18**	10	1.0
78-87-5	1,2-Dichloropropane	10U	10	1.9
10061-01-5	cis-1,3-Dichloropropene	10U	10	1.5
10061-02-6	trans-1,3-Dichloropropene	10U	10	1.9
100-41-4	Ethylbenzene	10U	10	0.44
591-78-6	2-Hexanone	50U	50	13
75-09-2	Methylene Chloride	10U	10	1.9
78-93-3	2-Butanone (MEK)	50U	50	15
108-10-1	4-Methyl-2-pentanone (MIBK)	50U	50	8.7

VALIDATED

Continued on next page

Reviewed By _____

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5563 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7461 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW101A**	Sampled:	11/26/10 14:20
Lab Sample ID:	**1011494-15**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/03/10 By: JDM
Dilution Factor:	10	Analyzed:	12/03/10 By: JDM
QC Batch:	1013276	Analytical Batch:	0L04003

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	10U	10	1.1
79-34-5	1,1,2,2-Tetrachloroethane	10U	10	2.2
127-18-4	Tetrachloroethene	**36**	10	2.4
108-88-3	Toluene	10U	10	0.81
71-55-6	1,1,1-Trichloroethane	**550**	10	1.3
79-00-5	1,1,2-Trichloroethane	10U	10	1.3
79-01-6	Trichloroethene	**230**	10	0.84
75-01-4	Vinyl Chloride	10U	10	0.54
1330-20-7	Xylene (Total)	30U	30	4.0

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	109	*88-115*
1,2-Dichloroethane-d4	103	*81-116*
Toluene-d8	101	*87-113*
4-Bromofluorobenzene	90	*78-116*

VALIDATED

Reviewed By _____

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.
[illegible] Corporate [illegible] Court SE ♦ Grand Rapids, MI 49[illegible] ♦ [illegible] ♦ [illegible] ♦ [illegible]

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW101B**	Sampled:	11/26/10 13:49
Lab Sample ID:	**1011494-14**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	10	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	50U	50	18
71-43-2	Benzene	10U	10	1.3
74-97-5	Bromochloromethane	10U	10	1.1
75-27-4	Bromodichloromethane	10U	10	1.4
75-25-2	Bromoform	10U	10	1.2
74-83-9	Bromomethane	10U	10	1.1
75-15-0	Carbon Disulfide	50U	50	6.0
*56-23-5	Carbon Tetrachloride	10U	10	2.1
108-90-7	Chlorobenzene	10U	10	0.65
75-00-3	Chloroethane	10U	10	1.8
67-66-3	Chloroform	10U	10	0.77
74-87-3	Chloromethane	10U	10	1.0
96-12-8	1,2-Dibromo-3-chloropropane	10U	10	4.1
*124-48-1	Dibromochloromethane	10U	10	1.5
106-93-4	1,2-Dibromoethane	10U	10	0.96
95-50-1	1,2-Dichlorobenzene	10U	10	2.7
541-73-1	1,3-Dichlorobenzene	10U	10	2.1
106-46-7	1,4-Dichlorobenzene	10U	10	2.1
75-34-3	1,1-Dichloroethane	**130**	10	1.8
107-06-2	1,2-Dichloroethane	10U	10	1.5
75-35-4	1,1-Dichloroethene	**36**	10	1.7
156-59-2	cis-1,2-Dichloroethene	**850**	10	1.9
156-60-5	trans-1,2-Dichloroethene	10U	10	1.0
78-87-5	1,2-Dichloropropane	10U	10	1.9
10061-01-5	cis-1,3-Dichloropropene	10U	10	1.5
10061-02-6	trans-1,3-Dichloropropene	10U	10	1.9
100-41-4	Ethylbenzene	10U	10	0.44
591-78-6	2-Hexanone	50U	50	13
75-09-2	Methylene Chloride	10U	10	1.9
78-93-3	2-Butanone (MEK)	50U	50	15
108-10-1	4-Methyl-2-pentanone (MIBK)	50U	50	8.7

VALIDATED

Continued on next page

*See Statement of Data Qualifications

Reviewed By [signature]

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of TRIMATRIX Laboratories, Inc.
In accordance with results relate only to the sample tested.
5500 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.5300 ♦ Fax 616.942.7363 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW101B**	Sampled:	11/26/10 13:49
Lab Sample ID:	**1011494-14**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	10	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	10U	10	1.1
*79-34-5	1,1,2,2-Tetrachloroethane	10U	10	2.2
127-18-4	Tetrachloroethene	**32**	10	2.4
108-88-3	Toluene	10U	10	0.81
71-55-6	1,1,1-Trichloroethane	**430**	10	1.3
79-00-5	1,1,2-Trichloroethane	10U	10	1.3
79-01-6	Trichloroethene	**77**	10	0.84
75-01-4	Vinyl Chloride	10U	10	0.54
1330-20-7	Xylene (Total)	30U	30	4.0

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	107	*88-115*
1,2-Dichloroethane-d4	101	*81-116*
Toluene-d8	100	*87-113*
4-Bromofluorobenzene	91	*78-116*

VALIDATED

*See Statement of Data Qualifications

Reviewed By

Date 1/19/11

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW101C**	Sampled:	11/26/10 13:18
Lab Sample ID:	**1011494-13**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	5	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	25U	25	9.0
71-43-2	Benzene	5.0U	5.0	0.64
74-97-5	Bromochloromethane	5.0U	5.0	0.57
75-27-4	Bromodichloromethane	5.0U	5.0	0.70
75-25-2	Bromoform	5.0U	5.0	0.58
74-83-9	Bromomethane	5.0U	5.0	0.56
75-15-0	Carbon Disulfide	25U	25	3.0
56-23-5	Carbon Tetrachloride	5.0U	5.0	1.1
108-90-7	Chlorobenzene	5.0U	5.0	0.33
75-00-3	Chloroethane	5.0U	5.0	0.89
67-66-3	Chloroform	**1.9J**	5.0	0.38
74-87-3	Chloromethane	5.0U	5.0	0.52
96-12-8	1,2-Dibromo-3-chloropropane	5.0U	5.0	2.1
124-48-1	Dibromochloromethane	5.0U	5.0	0.76
106-93-4	1,2-Dibromoethane	5.0U	5.0	0.48
95-50-1	1,2-Dichlorobenzene	5.0U	5.0	1.4
541-73-1	1,3-Dichlorobenzene	5.0U	5.0	1.1
106-46-7	1,4-Dichlorobenzene	5.0U	5.0	1.1
75-34-3	1,1-Dichloroethane	**98**	5.0	0.88
107-06-2	1,2-Dichloroethane	**1.8J**	5.0	0.75
75-35-4	1,1-Dichloroethene	**24**	5.0	0.86
156-59-2	cis-1,2-Dichloroethene	**640**	5.0	0.96
156-60-5	trans-1,2-Dichloroethene	5.0U	5.0	0.51
78-87-5	1,2-Dichloropropane	5.0U	5.0	0.96
10061-01-5	cis-1,3-Dichloropropene	5.0U	5.0	0.74
10061-02-6	trans-1,3-Dichloropropene	5.0U	5.0	0.93
100-41-4	Ethylbenzene	5.0U	5.0	0.22
591-78-6	2-Hexanone	25U	25	6.6
75-09-2	Methylene Chloride	5.0U	5.0	0.94
78-93-3	2-Butanone (MEK)	25U	25	7.6
108-10-1	4-Methyl-2-pentanone (MIBK)	25U	25	4.3

Continued on next page

VALIDATED

Reviewed By

Date 1/14/11

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW101C**	Sampled:	11/26/10 13:18
Lab Sample ID:	**1011494-13**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	5	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	5.0U	5.0	0.54
*79-34-5	1,1,2,2-Tetrachloroethane	5.0U	5.0	1.1
127-18-4	Tetrachloroethene	**20**	5.0	1.2
108-88-3	Toluene	5.0U	5.0	0.40
71-55-6	1,1,1-Trichloroethane	**310**	5.0	0.66
79-00-5	1,1,2-Trichloroethane	5.0U	5.0	0.66
79-01-6	Trichloroethene	**48**	5.0	0.42
75-01-4	Vinyl Chloride	5.0U	5.0	0.27
1330-20-7	Xylene (Total)	15U	15	2.0

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	110	*88-115*
1,2-Dichloroethane-d4	102	*81-116*
Toluene-d8	100	*87-113*
4-Bromofluorobenzene	92	*78-116*

VALIDATED

*See Statement of Data Qualifications

Reviewed By _____

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5960 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.1500 ♦ Fax 616.[illegible] ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW101D**	Sampled:	11/26/10 15:03
Lab Sample ID:	**1011494-16**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	2.5	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	12U	12	4.5
71-43-2	Benzene	2.5U	2.5	0.32
74-97-5	Bromochloromethane	2.5U	2.5	0.28
75-27-4	Bromodichloromethane	2.5U	2.5	0.35
75-25-2	Bromoform	2.5U	2.5	0.29
74-83-9	Bromomethane	2.5U	2.5	0.28
75-15-0	Carbon Disulfide	12U	12	1.5
56-23-5	Carbon Tetrachloride	2.5U	2.5	0.53
108-90-7	Chlorobenzene	2.5U	2.5	0.16
75-00-3	Chloroethane	2.5U	2.5	0.44
67-66-3	Chloroform	**1.4J**	2.5	0.19
74-87-3	Chloromethane	2.5U	2.5	0.26
96-12-8	1,2-Dibromo-3-chloropropane	2.5U	2.5	1.0
124-48-1	Dibromochloromethane	2.5U	2.5	0.38
106-93-4	1,2-Dibromoethane	2.5U	2.5	0.24
95-50-1	1,2-Dichlorobenzene	2.5U	2.5	0.68
541-73-1	1,3-Dichlorobenzene	2.5U	2.5	0.54
106-46-7	1,4-Dichlorobenzene	2.5U	2.5	0.53
75-34-3	1,1-Dichloroethane	**51**	2.5	0.44
107-06-2	1,2-Dichloroethane	**1.0J**	2.5	0.38
75-35-4	1,1-Dichloroethene	**18**	2.5	0.43
156-59-2	cis-1,2-Dichloroethene	**320**	2.5	0.48
156-60-5	trans-1,2-Dichloroethene	**0.62J**	2.5	0.26
78-87-5	1,2-Dichloropropane	2.5U	2.5	0.48
10061-01-5	cis-1,3-Dichloropropene	2.5U	2.5	0.37
10061-02-6	trans-1,3-Dichloropropene	2.5U	2.5	0.46
100-41-4	Ethylbenzene	2.5U	2.5	0.11
591-78-6	2-Hexanone	12U	12	3.3
75-09-2	Methylene Chloride	2.5U	2.5	0.47
78-93-3	2-Butanone (MEK)	12U	12	3.8
108-10-1	4-Methyl-2-pentanone (MIBK)	12U	12	2.2

Continued on next page

VALIDATED

Reviewed By

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Indefinite samples results relate only to the sample tested.

5500 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7461 ♦ www.trimatrix.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW101D**	Sampled:	11/26/10 15:03
Lab Sample ID:	**1011494-16**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	2.5	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	2.5U	2.5	0.27
*79-34-5	1,1,2,2-Tetrachloroethane	2.5U	2.5	0.54
127-18-4	Tetrachloroethene	**17**	2.5	0.61
108-88-3	Toluene	2.5U	2.5	0.20
71-55-6	1,1,1-Trichloroethane	**160**	2.5	0.33
79-00-5	1,1,2-Trichloroethane	2.5U	2.5	0.33
79-01-6	Trichloroethene	**38**	2.5	0.21
75-01-4	Vinyl Chloride	2.5U	2.5	0.13
1330-20-7	Xylene (Total)	7.5U	7.5	1.0

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	102	*88-115*
1,2-Dichloroethane-d4	99	*81-116*
Toluene-d8	98	*87-113*
4-Bromofluorobenzene	91	*78-116*

VALIDATED

*See Statement of Data Qualifications

Reviewed By _____

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.975.7462 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW102A**	Sampled:	11/26/10 11:10
Lab Sample ID:	**1011494-09**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	2	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	10U	10	3.6
71-43-2	Benzene	2.0U	2.0	0.25
74-97-5	Bromochloromethane	2.0U	2.0	0.23
75-27-4	Bromodichloromethane	2.0U	2.0	0.28
75-25-2	Bromoform	2.0U	2.0	0.23
74-83-9	Bromomethane	2.0U	2.0	0.23
75-15-0	Carbon Disulfide	10U	10	1.2
56-23-5	Carbon Tetrachloride	2.0U	2.0	0.42
108-90-7	Chlorobenzene	2.0U	2.0	0.13
75-00-3	Chloroethane	2.0U	2.0	0.36
67-66-3	Chloroform	2.0U	2.0	0.15
74-87-3	Chloromethane	2.0U	2.0	0.21
96-12-8	1,2-Dibromo-3-chloropropane	2.0U	2.0	0.83
124-48-1	Dibromochloromethane	2.0U	2.0	0.30
106-93-4	1,2-Dibromoethane	2.0U	2.0	0.19
95-50-1	1,2-Dichlorobenzene	2.0U	2.0	0.55
541-73-1	1,3-Dichlorobenzene	2.0U	2.0	0.43
106-46-7	1,4-Dichlorobenzene	2.0U	2.0	0.42
75-34-3	1,1-Dichloroethane	**99**	2.0	0.35
107-06-2	1,2-Dichloroethane	2.0U	2.0	0.30
75-35-4	1,1-Dichloroethene	**3.0**	2.0	0.34
156-59-2	cis-1,2-Dichloroethene	**200**	2.0	0.39
156-60-5	trans-1,2-Dichloroethene	**5.3**	2.0	0.20
78-87-5	1,2-Dichloropropane	2.0U	2.0	0.38
10061-01-5	cis-1,3-Dichloropropene	2.0U	2.0	0.29
10061-02-6	trans-1,3-Dichloropropene	2.0U	2.0	0.37
100-41-4	Ethylbenzene	2.0U	2.0	0.088
591-78-6	2-Hexanone	10U	10	2.7
75-09-2	Methylene Chloride	2.0U	2.0	0.38
78-93-3	2-Butanone (MEK)	10U	10	3.0
108-10-1	4-Methyl-2-pentanone (MIBK)	10U	10	1.7

Continued on next page

VALIDATED

Reviewed By _____

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.947.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW102A**	Sampled:	11/26/10 11:10
Lab Sample ID:	**1011494-09**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	2	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	2.0U	2.0	0.21
*79-34-5	1,1,2,2-Tetrachloroethane	2.0U	2.0	0.43
127-18-4	Tetrachloroethene	2.0U	2.0	0.49
108-88-3	Toluene	2.0U	2.0	0.16
71-55-6	1,1,1-Trichloroethane	**90**	2.0	0.27
79-00-5	1,1,2-Trichloroethane	2.0U	2.0	0.27
79-01-6	Trichloroethene	**20**	2.0	0.17
75-01-4	Vinyl Chloride	2.0U	2.0	0.11
1330-20-7	Xylene (Total)	6.0U	6.0	0.81

Surrogates:	*% Recovery*	*Control Limits*
Dibromofluoromethane	108	*88-115*
1,2-Dichloroethane-d4	103	*81-116*
Toluene-d8	102	*87-113*
4-Bromofluorobenzene	91	*78-116*

VALIDATED

*See Statement of Data Qualifications

Reviewed By _____

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual service results apply only to the sample tested.

5960 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7461 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**FD-1** MW-102A field dupe	Sampled:	11/26/10 11:12
Lab Sample ID:	**1011494-10**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	2	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	10U	10	3.6
71-43-2	Benzene	2.0U	2.0	0.25
74-97-5	Bromochloromethane	2.0U	2.0	0.23
75-27-4	Bromodichloromethane	2.0U	2.0	0.28
75-25-2	Bromoform	2.0U	2.0	0.23
74-83-9	Bromomethane	2.0U	2.0	0.23
75-15-0	Carbon Disulfide	10U	10	1.2
56-23-5	Carbon Tetrachloride	2.0U	2.0	0.42
108-90-7	Chlorobenzene	2.0U	2.0	0.13
75-00-3	Chloroethane	2.0U	2.0	0.36
67-66-3	Chloroform	2.0U	2.0	0.15
74-87-3	Chloromethane	2.0U	2.0	0.21
96-12-8	1,2-Dibromo-3-chloropropane	2.0U	2.0	0.83
124-48-1	Dibromochloromethane	2.0U	2.0	0.30
106-93-4	1,2-Dibromoethane	2.0U	2.0	0.19
95-50-1	1,2-Dichlorobenzene	2.0U	2.0	0.55
541-73-1	1,3-Dichlorobenzene	2.0U	2.0	0.43
106-46-7	1,4-Dichlorobenzene	2.0U	2.0	0.42
75-34-3	1,1-Dichloroethane	**95**	2.0	0.35
107-06-2	1,2-Dichloroethane	2.0U	2.0	0.30
75-35-4	1,1-Dichloroethene	**2.7**	2.0	0.34
156-59-2	cis-1,2-Dichloroethene	**200**	2.0	0.39
156-60-5	trans-1,2-Dichloroethene	**4.9**	2.0	0.20
78-87-5	1,2-Dichloropropane	2.0U	2.0	0.38
10061-01-5	cis-1,3-Dichloropropene	2.0U	2.0	0.29
10061-02-6	trans-1,3-Dichloropropene	2.0U	2.0	0.37
100-41-4	Ethylbenzene	2.0U	2.0	0.088
591-78-6	2-Hexanone	10U	10	2.7
75-09-2	Methylene Chloride	2.0U	2.0	0.38
78-93-3	2-Butanone (MEK)	10U	10	3.0
108-10-1	4-Methyl-2-pentanone (MIBK)	10U	10	1.7

Continued on next page

VALIDATED

Reviewed By _____

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5500 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7363 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**FD-1** MW-102A Field dup	Sampled:	11/26/10 11:12
Lab Sample ID:	**1011494-10**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	2	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	2.0U	2.0	0.21
*79-34-5	1,1,2,2-Tetrachloroethane	2.0U	2.0	0.43
127-18-4	Tetrachloroethene	2.0U	2.0	0.49
108-88-3	Toluene	2.0U	2.0	0.16
71-55-6	1,1,1-Trichloroethane	**87**	2.0	0.27
79-00-5	1,1,2-Trichloroethane	2.0U	2.0	0.27
79-01-6	Trichloroethene	**19**	2.0	0.17
75-01-4	Vinyl Chloride	2.0U	2.0	0.11
1330-20-7	Xylene (Total)	6.0U	6.0	0.81

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	106	*88-115*
1,2-Dichloroethane-d4	102	*81-116*
Toluene-d8	99	*87-113*
4-Bromofluorobenzene	90	*78-116*

VALIDATED

*See Statement of Data Qualifications

Reviewed By _____

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
In which sample results relate only to the sample tested.

5500 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7163 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW102B**	Sampled:	11/26/10 11:59
Lab Sample ID:	**1011494-11**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	5.0U	5.0	1.8
71-43-2	Benzene	1.0U	1.0	0.13
74-97-5	Bromochloromethane	1.0U	1.0	0.11
75-27-4	Bromodichloromethane	1.0U	1.0	0.14
75-25-2	Bromoform	1.0U	1.0	0.12
74-83-9	Bromomethane	1.0U	1.0	0.11
75-15-0	Carbon Disulfide	5.0U	5.0	0.60
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.21
108-90-7	Chlorobenzene	1.0U	1.0	0.065
75-00-3	Chloroethane	1.0U	1.0	0.18
67-66-3	Chloroform	1.0U	1.0	0.077
74-87-3	Chloromethane	1.0U	1.0	0.10
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.41
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.096
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.27
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.21
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.21
75-34-3	1,1-Dichloroethane	**2.9**	1.0	0.18
107-06-2	1,2-Dichloroethane	**0.67J**	1.0	0.15
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.17
156-59-2	cis-1,2-Dichloroethene	**5.0**	1.0	0.19
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.10
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.19
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.15
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.044
591-78-6	2-Hexanone	5.0U	5.0	1.3
75-09-2	Methylene Chloride	1.0U	1.0	0.19
78-93-3	2-Butanone (MEK)	5.0U	5.0	1.5
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.87

VALIDATED

Continued on next page

Reviewed By [signature]

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

[illegible] Corporate Exchange Court SE ♦ Grand Rapids, MI [illegible] ♦ 616.975.4500 ♦ Fax [illegible] ♦ www.trimatrixlab.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW102B**	Sampled:	11/26/10 11:59
Lab Sample ID:	**1011494-11**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
*79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.22
127-18-4	Tetrachloroethene	1.0U	1.0	0.24
108-88-3	Toluene	1.0U	1.0	0.081
71-55-6	1,1,1-Trichloroethane	1.0U	1.0	0.13
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.13
79-01-6	Trichloroethene	1.0U	1.0	0.084
75-01-4	Vinyl Chloride	1.0U	1.0	0.054
1330-20-7	Xylene (Total)	3.0U	3.0	0.40

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	107	*88-115*
1,2-Dichloroethane-d4	104	*81-116*
Toluene-d8	100	*87-113*
4-Bromofluorobenzene	90	*78-116*

VALIDATED

Reviewed By _____

Date 1/14/11

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written permission of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

3601 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW102C**	Sampled:	11/26/10 12:30
Lab Sample ID:	**1011494-12**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	10	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	50U	50	18
71-43-2	Benzene	10U	10	1.3
74-97-5	Bromochloromethane	10U	10	1.1
75-27-4	Bromodichloromethane	10U	10	1.4
75-25-2	Bromoform	10U	10	1.2
74-83-9	Bromomethane	10U	10	1.1
75-15-0	Carbon Disulfide	50U	50	6.0
56-23-5	Carbon Tetrachloride	10U	10	2.1
108-90-7	Chlorobenzene	10U	10	0.65
75-00-3	Chloroethane	10U	10	1.8
67-66-3	Chloroform	10U	10	0.77
74-87-3	Chloromethane	10U	10	1.0
96-12-8	1,2-Dibromo-3-chloropropane	10U	10	4.1
124-48-1	Dibromochloromethane	10U	10	1.5
106-93-4	1,2-Dibromoethane	10U	10	0.96
95-50-1	1,2-Dichlorobenzene	10U	10	2.7
541-73-1	1,3-Dichlorobenzene	10U	10	2.1
106-46-7	1,4-Dichlorobenzene	10U	10	2.1
75-34-3	1,1-Dichloroethane	**170**	10	1.8
107-06-2	1,2-Dichloroethane	**3.2J**	10	1.5
75-35-4	1,1-Dichloroethene	**51**	10	1.7
156-59-2	cis-1,2-Dichloroethene	**720**	10	1.9
156-60-5	trans-1,2-Dichloroethene	10U	10	1.0
78-87-5	1,2-Dichloropropane	10U	10	1.9
10061-01-5	cis-1,3-Dichloropropene	10U	10	1.5
10061-02-6	trans-1,3-Dichloropropene	10U	10	1.9
100-41-4	Ethylbenzene	10U	10	0.44
591-78-6	2-Hexanone	50U	50	13
75-09-2	Methylene Chloride	10U	10	1.9
78-93-3	2-Butanone (MEK)	50U	50	15
108-10-1	4-Methyl-2-pentanone (MIBK)	50U	50	8.7

Continued on next page

VALIDATED

Reviewed By [signature]

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results apply to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW102C**	Sampled:	11/26/10 12:30
Lab Sample ID:	**1011494-12**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	10	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	10U	10	1.1
*79-34-5	1,1,2,2-Tetrachloroethane	10U	10	2.2
127-18-4	Tetrachloroethene	**21**	10	2.4
108-88-3	Toluene	10U	10	0.81
71-55-6	1,1,1-Trichloroethane	**110**	10	1.3
79-00-5	1,1,2-Trichloroethane	10U	10	1.3
79-01-6	Trichloroethene	**68**	10	0.84
75-01-4	Vinyl Chloride	10U	10	0.54
1330-20-7	Xylene (Total)	30U	30	4.0

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	107	*88-115*
1,2-Dichloroethane-d4	101	*81-116*
Toluene-d8	100	*87-113*
4-Bromofluorobenzene	91	*78-116*

VALIDATED

Reviewed By [signature]

Date 1/14/11

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
It divulges sample results relevant only to the sample tested.

3560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.947.7465 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW113A**	Sampled:	11/28/10 14:48
Lab Sample ID:	**1011494-33**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/04/10 By: JDM
Dilution Factor:	2.5	Analyzed:	12/05/10 By: JDM
QC Batch:	1013277	Analytical Batch:	0L04004

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	12U	12	4.5
71-43-2	Benzene	2.5U	2.5	0.32
74-97-5	Bromochloromethane	2.5U	2.5	0.28
75-27-4	Bromodichloromethane	2.5U	2.5	0.35
75-25-2	Bromoform	2.5U	2.5	0.29
74-83-9	Bromomethane	2.5U	2.5	0.28
75-15-0	Carbon Disulfide	12U	12	1.5
56-23-5	Carbon Tetrachloride	2.5U	2.5	0.53
108-90-7	Chlorobenzene	2.5U	2.5	0.16
75-00-3	Chloroethane	2.5U	2.5	0.44
67-66-3	Chloroform	**0.95J**	2.5	0.19
74-87-3	Chloromethane	2.5U	2.5	0.26
96-12-8	1,2-Dibromo-3-chloropropane	2.5U	2.5	1.0
124-48-1	Dibromochloromethane	2.5U	2.5	0.38
106-93-4	1,2-Dibromoethane	2.5U	2.5	0.24
95-50-1	1,2-Dichlorobenzene	2.5U	2.5	0.68
541-73-1	1,3-Dichlorobenzene	2.5U	2.5	0.54
106-46-7	1,4-Dichlorobenzene	2.5U	2.5	0.53
75-34-3	1,1-Dichloroethane	**85**	2.5	0.44
107-06-2	1,2-Dichloroethane	**0.70J**	2.5	0.38
75-35-4	1,1-Dichloroethene	**17**	2.5	0.43
156-59-2	cis-1,2-Dichloroethene	**250**	2.5	0.48
156-60-5	trans-1,2-Dichloroethene	**11**	2.5	0.26
78-87-5	1,2-Dichloropropane	2.5U	2.5	0.48
10061-01-5	cis-1,3-Dichloropropene	2.5U	2.5	0.37
10061-02-6	trans-1,3-Dichloropropene	2.5U	2.5	0.46
100-41-4	Ethylbenzene	2.5U	2.5	0.11
591-78-6	2-Hexanone	12U	12	3.3
75-09-2	Methylene Chloride	2.5U	2.5	0.47
78-93-3	2-Butanone (MEK)	12U	12	3.8
108-10-1	4-Methyl-2-pentanone (MIBK)	12U	12	2.2

Continued on next page

VALIDATED

Reviewed By [signature]

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7485 ♦ www.trimatrix-labs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW113A**	Sampled:	11/28/10 14:48
Lab Sample ID:	**1011494-33**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/04/10 By: JDM
Dilution Factor:	2.5	Analyzed:	12/05/10 By: JDM
QC Batch:	1013277	Analytical Batch:	0L04004

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	2.5U	2.5	0.27
79-34-5	1,1,2,2-Tetrachloroethane	2.5U	2.5	0.54
127-18-4	Tetrachloroethene	**12**	2.5	0.61
108-88-3	Toluene	2.5U	2.5	0.20
71-55-6	1,1,1-Trichloroethane	**110**	2.5	0.33
79-00-5	1,1,2-Trichloroethane	2.5U	2.5	0.33
79-01-6	Trichloroethene	**67**	2.5	0.21
75-01-4	Vinyl Chloride	2.5U	2.5	0.13
1330-20-7	Xylene (Total)	7.5U	7.5	1.0

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	102	*88-115*
1,2-Dichloroethane-d4	101	*81-116*
Toluene-d8	97	*87-113*
4-Bromofluorobenzene	93	*78-116*

VALIDATED

Reviewed By _____

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

3560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax: 616.975.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW113B**	Sampled:	11/28/10 14:02
Lab Sample ID:	**1011494-32**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/04/10 By: JDM
Dilution Factor:	2	Analyzed:	12/05/10 By: JDM
QC Batch:	1013277	Analytical Batch:	0L04004

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	10U	10	3.6
71-43-2	Benzene	2.0U	2.0	0.25
74-97-5	Bromochloromethane	2.0U	2.0	0.23
75-27-4	Bromodichloromethane	2.0U	2.0	0.28
75-25-2	Bromoform	2.0U	2.0	0.23
74-83-9	Bromomethane	2.0U	2.0	0.23
75-15-0	Carbon Disulfide	10U	10	1.2
56-23-5	Carbon Tetrachloride	2.0U	2.0	0.42
108-90-7	Chlorobenzene	2.0U	2.0	0.13
75-00-3	Chloroethane	2.0U	2.0	0.36
67-66-3	Chloroform	2.0U	2.0	0.15
74-87-3	Chloromethane	2.0U	2.0	0.21
96-12-8	1,2-Dibromo-3-chloropropane	2.0U	2.0	0.83
124-48-1	Dibromochloromethane	2.0U	2.0	0.30
106-93-4	1,2-Dibromoethane	2.0U	2.0	0.19
95-50-1	1,2-Dichlorobenzene	2.0U	2.0	0.55
541-73-1	1,3-Dichlorobenzene	2.0U	2.0	0.43
106-46-7	1,4-Dichlorobenzene	2.0U	2.0	0.42
75-34-3	1,1-Dichloroethane	**67**	2.0	0.35
107-06-2	1,2-Dichloroethane	**0.80J**	2.0	0.30
75-35-4	1,1-Dichloroethene	**19**	2.0	0.34
156-59-2	cis-1,2-Dichloroethene	**160**	2.0	0.39
156-60-5	trans-1,2-Dichloroethene	**3.0**	2.0	0.20
78-87-5	1,2-Dichloropropane	2.0U	2.0	0.38
10061-01-5	cis-1,3-Dichloropropene	2.0U	2.0	0.29
10061-02-6	trans-1,3-Dichloropropene	2.0U	2.0	0.37
100-41-4	Ethylbenzene	2.0U	2.0	0.088
591-78-6	2-Hexanone	10U	10	2.7
75-09-2	Methylene Chloride	2.0U	2.0	0.38
78-93-3	2-Butanone (MEK)	10U	10	3.0
108-10-1	4-Methyl-2-pentanone (MIBK)	10U	10	1.7

Continued on next page.

VALIDATED

Reviewed By _____

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5500 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.975.4534 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW113B**	Sampled:	11/28/10 14:02
Lab Sample ID:	**1011494-32**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/04/10 By: JDM
Dilution Factor:	2	Analyzed:	12/05/10 By: JDM
QC Batch:	1013277	Analytical Batch:	0L04004

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	2.0U	2.0	0.21
79-34-5	1,1,2,2-Tetrachloroethane	2.0U	2.0	0.43
127-18-4	Tetrachloroethene	**4.2**	2.0	0.49
108-88-3	Toluene	2.0U	2.0	0.16
71-55-6	1,1,1-Trichloroethane	**26**	2.0	0.27
79-00-5	1,1,2-Trichloroethane	2.0U	2.0	0.27
79-01-6	Trichloroethene	**37**	2.0	0.17
75-01-4	Vinyl Chloride	**8.8**	2.0	0.11
1330-20-7	Xylene (Total)	6.0U	6.0	0.81

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	101	*88-115*
1,2-Dichloroethane-d4	98	*81-116*
Toluene-d8	95	*87-113*
4-Bromofluorobenzene	88	*78-116*

VALIDATED

Reviewed By [illegible]

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

[illegible] Corporate Exchange Court SE • Grand Rapids MI 49512 • 616.975.4500 • Fax 616.957.7462 • www.trimatrixlab.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW114A**	Sampled:	11/27/10 15:58
Lab Sample ID:	**1011494-25**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/03/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013276	Analytical Batch:	0L04003

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	5.0U	5.0	1.8
71-43-2	Benzene	1.0U	1.0	0.13
74-97-5	Bromochloromethane	1.0U	1.0	0.11
75-27-4	Bromodichloromethane	1.0U	1.0	0.14
75-25-2	Bromoform	1.0U	1.0	0.12
74-83-9	Bromomethane	1.0U	1.0	0.11
75-15-0	Carbon Disulfide	5.0U	5.0	0.60
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.21
108-90-7	Chlorobenzene	1.0U	1.0	0.065
75-00-3	Chloroethane	1.0U	1.0	0.18
67-66-3	Chloroform	1.0U	1.0	0.077
74-87-3	Chloromethane	1.0U	1.0	0.10
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.41
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.096
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.27
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.21
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.21
75-34-3	1,1-Dichloroethane	**2.8**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.15
75-35-4	1,1-Dichloroethene	**8.5**	1.0	0.17
156-59-2	cis-1,2-Dichloroethene	**2.1**	1.0	0.19
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.10
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.19
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.15
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.044
591-78-6	2-Hexanone	5.0U	5.0	1.3
75-09-2	Methylene Chloride	1.0U	1.0	0.19
78-93-3	2-Butanone (MEK)	5.0U	5.0	1.5
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.87

VALIDATED

Continued on next page

Reviewed By _____

Date 1/14/11

"This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc. Individual single results apply to the sample tested.

3960 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7453 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW114A**	Sampled:	11/27/10 15:58
Lab Sample ID:	**1011494-25**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/03/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013276	Analytical Batch:	0L04003

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.22
127-18-4	Tetrachloroethene	1.0U	1.0	0.24
108-88-3	Toluene	1.0U	1.0	0.081
71-55-6	1,1,1-Trichloroethane	**65**	1.0	0.13
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.13
79-01-6	Trichloroethene	**4.7**	1.0	0.084
75-01-4	Vinyl Chloride	1.0U	1.0	0.054
1330-20-7	Xylene (Total)	3.0U	3.0	0.40

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	109	*88-115*
1,2-Dichloroethane-d4	105	*81-116*
Toluene-d8	102	*87-113*
4-Bromofluorobenzene	90	*78-116*

VALIDATED

Reviewed By _____

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

3560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7163 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW114B**	Sampled:	11/27/10 15:25
Lab Sample ID:	**1011494-24**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/03/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013276	Analytical Batch:	0L04003

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	5.0U	5.0	1.8
71-43-2	Benzene	1.0U	1.0	0.13
74-97-5	Bromochloromethane	1.0U	1.0	0.11
75-27-4	Bromodichloromethane	1.0U	1.0	0.14
75-25-2	Bromoform	1.0U	1.0	0.12
74-83-9	Bromomethane	1.0U	1.0	0.11
75-15-0	Carbon Disulfide	5.0U	5.0	0.60
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.21
108-90-7	Chlorobenzene	1.0U	1.0	0.065
75-00-3	Chloroethane	1.0U	1.0	0.18
67-66-3	Chloroform	1.0U	1.0	0.077
74-87-3	Chloromethane	1.0U	1.0	0.10
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.41
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.096
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.27
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.21
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.21
75-34-3	1,1-Dichloroethane	**1.8**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.15
75-35-4	1,1-Dichloroethene	**1.0**	1.0	0.17
156-59-2	cis-1,2-Dichloroethene	**2.3**	1.0	0.19
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.10
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.19
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.15
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.044
591-78-6	2-Hexanone	5.0U	5.0	1.3
75-09-2	Methylene Chloride	1.0U	1.0	0.19
78-93-3	2-Butanone (MEK)	5.0U	5.0	1.5
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.87

Continued on next page

VALIDATED

Reviewed By _____

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.940.7462 ♦ www.trimatrix-labs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW114B**	Sampled:	11/27/10 15:25
Lab Sample ID:	**1011494-24**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/03/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013276	Analytical Batch:	0L04003

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.22
127-18-4	Tetrachloroethene	1.0U	1.0	0.24
108-88-3	Toluene	1.0U	1.0	0.081
71-55-6	1,1,1-Trichloroethane	1.0U	1.0	0.13
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.13
79-01-6	Trichloroethene	**7.8**	1.0	0.084
75-01-4	Vinyl Chloride	1.0U	1.0	0.054
1330-20-7	Xylene (Total)	3.0U	3.0	0.40

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	107	*88-115*
1,2-Dichloroethane-d4	102	*81-116*
Toluene-d8	102	*87-113*
4-Bromofluorobenzene	91	*78-116*

VALIDATED

Reviewed By _____

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW117B**	Sampled:	11/24/10 11:24
Lab Sample ID:	**1011494-01**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/03/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013276	Analytical Batch:	0L04003

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	5.0U	5.0	1.8
71-43-2	Benzene	1.0U	1.0	0.13
74-97-5	Bromochloromethane	1.0U	1.0	0.11
75-27-4	Bromodichloromethane	1.0U	1.0	0.14
75-25-2	Bromoform	1.0U	1.0	0.12
74-83-9	Bromomethane	1.0U	1.0	0.11
75-15-0	Carbon Disulfide	5.0U	5.0	0.60
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.21
108-90-7	Chlorobenzene	1.0U	1.0	0.065
75-00-3	Chloroethane	1.0U	1.0	0.18
67-66-3	Chloroform	**0.31J**	1.0	0.077
74-87-3	Chloromethane	1.0U	1.0	0.10
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.41
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.096
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.27
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.21
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.21
75-34-3	1,1-Dichloroethane	**11**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.15
75-35-4	1,1-Dichloroethene	**8.1**	1.0	0.17
156-59-2	cis-1,2-Dichloroethene	**4.6**	1.0	0.19
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.10
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.19
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.15
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.044
591-78-6	2-Hexanone	5.0U	5.0	1.3
75-09-2	Methylene Chloride	1.0U	1.0	0.19
78-93-3	2-Butanone (MEK)	5.0U	5.0	1.5
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.87

Continued on next page

VALIDATED

Reviewed By

Date 1/4/11

This report shall not be reproduced, except in full, without written approval of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW117B**	Sampled:	11/24/10 11:24
Lab Sample ID:	**1011494-01**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/03/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013276	Analytical Batch:	0L04003

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.22
127-18-4	Tetrachloroethene	**8.4**	1.0	0.24
108-88-3	Toluene	1.0U	1.0	0.081
71-55-6	1,1,1-Trichloroethane	**31**	1.0	0.13
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.13
79-01-6	Trichloroethene	**19**	1.0	0.084
75-01-4	Vinyl Chloride	1.0U	1.0	0.054
1330-20-7	*Xylene (Total)*	*3.0U*	*3.0*	*0.40*

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	108	*88-115*
1,2-Dichloroethane-d4	103	*81-116*
Toluene-d8	101	*87-113*
4-Bromofluorobenzene	92	*78-116*

VALIDATED

Reviewed By _____

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW117C**	Sampled:	11/24/10 12:12
Lab Sample ID:	**1011494-02**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/03/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013276	Analytical Batch:	0L04003

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	5.0U	5.0	1.8
71-43-2	Benzene	1.0U	1.0	0.13
74-97-5	Bromochloromethane	1.0U	1.0	0.11
75-27-4	Bromodichloromethane	1.0U	1.0	0.14
75-25-2	Bromoform	1.0U	1.0	0.12
74-83-9	Bromomethane	1.0U	1.0	0.11
75-15-0	Carbon Disulfide	5.0U	5.0	0.60
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.21
108-90-7	Chlorobenzene	1.0U	1.0	0.065
75-00-3	Chloroethane	1.0U	1.0	0.18
67-66-3	Chloroform	**0.38J**	1.0	0.077
74-87-3	Chloromethane	1.0U	1.0	0.10
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.41
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.096
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.27
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.21
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.21
75-34-3	1,1-Dichloroethane	**22**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.15
75-35-4	1,1-Dichloroethene	**22**	1.0	0.17
156-59-2	cis-1,2-Dichloroethene	**34**	1.0	0.19
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.10
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.19
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.15
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.044
591-78-6	2-Hexanone	5.0U	5.0	1.3
75-09-2	Methylene Chloride	1.0U	1.0	0.19
78-93-3	2-Butanone (MEK)	5.0U	5.0	1.5
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.87

Continued on next page

VALIDATED

Reviewed By

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5960 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7462 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW117C**	Sampled:	11/24/10 12:12
Lab Sample ID:	**1011494-02**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/03/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013276	Analytical Batch:	0L04003

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.22
127-18-4	Tetrachloroethene	**27**	1.0	0.24
108-88-3	Toluene	1.0U	1.0	0.081
71-55-6	1,1,1-Trichloroethane	**53**	1.0	0.13
79-00-5	1,1,2-Trichloroethane	**0.77J**	1.0	0.13
79-01-6	Trichloroethene	**21**	1.0	0.084
75-01-4	Vinyl Chloride	1.0U	1.0	0.054
1330-20-7	Xylene (Total)	3.0U	3.0	0.40

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	107	*88-115*
1,2-Dichloroethane-d4	100	*81-116*
Toluene-d8	100	*87-113*
4-Bromofluorobenzene	92	*78-116*

VALIDATED

Reviewed By _____

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlab.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW117D**	Sampled:	11/24/10 13:00
Lab Sample ID:	**1011494-03**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	**2.1J**	5.0	1.8
71-43-2	Benzene	1.0U	1.0	0.13
74-97-5	Bromochloromethane	1.0U	1.0	0.11
75-27-4	Bromodichloromethane	1.0U	1.0	0.14
75-25-2	Bromoform	1.0U	1.0	0.12
74-83-9	Bromomethane	1.0U	1.0	0.11
75-15-0	Carbon Disulfide	5.0U	5.0	0.60
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.21
108-90-7	Chlorobenzene	1.0U	1.0	0.065
75-00-3	Chloroethane	1.0U	1.0	0.18
67-66-3	Chloroform	**0.34J**	1.0	0.077
74-87-3	Chloromethane	1.0U	1.0	0.10
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.41
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.096
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.27
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.21
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.21
75-34-3	1,1-Dichloroethane	**30**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.15
75-35-4	1,1-Dichloroethene	**16**	1.0	0.17
156-59-2	cis-1,2-Dichloroethene	**5.6**	1.0	0.19
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.10
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.19
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.15
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.044
591-78-6	2-Hexanone	5.0U	5.0	1.3
75-09-2	Methylene Chloride	1.0U	1.0	0.19
78-93-3	2-Butanone (MEK)	5.0U	5.0	1.5
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.87

Continued on next page

VALIDATED

Reviewed By _____

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5500 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.1500 ♦ Fax 616.942.7455 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW117D**	Sampled:	11/24/10 13:00
Lab Sample ID:	**1011494-03**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
*79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.22
127-18-4	Tetrachloroethene	**29**	1.0	0.24
108-88-3	Toluene	1.0U	1.0	0.081
71-55-6	1,1,1-Trichloroethane	**45**	1.0	0.13
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.13
79-01-6	Trichloroethene	**17**	1.0	0.084
75-01-4	Vinyl Chloride	1.0U	1.0	0.054
1330-20-7	Xylene (Total)	3.0U	3.0	0.40

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	106	*88-115*
1,2-Dichloroethane-d4	99	*81-116*
Toluene-d8	99	*87-113*
4-Bromofluorobenzene	93	*78-116*

VALIDATED

*See Statement of Data Qualifications

Reviewed By

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Results of sample results relate only to the sample tested.

5960 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW119**	Sampled:	11/27/10 10:46
Lab Sample ID:	**1011494-18**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	5.0U	5.0	1.8
71-43-2	Benzene	1.0U	1.0	0.13
74-97-5	Bromochloromethane	1.0U	1.0	0.11
75-27-4	Bromodichloromethane	1.0U	1.0	0.14
75-25-2	Bromoform	1.0U	1.0	0.12
74-83-9	Bromomethane	1.0U	1.0	0.11
75-15-0	Carbon Disulfide	5.0U	5.0	0.60
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.21
108-90-7	Chlorobenzene	1.0U	1.0	0.065
75-00-3	Chloroethane	1.0U	1.0	0.18
67-66-3	Chloroform	**0.46J**	1.0	0.077
74-87-3	Chloromethane	1.0U	1.0	0.10
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.41
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.096
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.27
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.21
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.21
75-34-3	1,1-Dichloroethane	**1.1**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.15
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.17
156-59-2	cis-1,2-Dichloroethene	**1.1**	1.0	0.19
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.10
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.19
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.15
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.044
591-78-6	2-Hexanone	5.0U	5.0	1.3
75-09-2	Methylene Chloride	1.0U	1.0	0.19
78-93-3	2-Butanone (MEK)	5.0U	5.0	1.5
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.87

Continued on next page

VALIDATED

Reviewed By _____

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results are for only those samples tested.

5500 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.940.7463 ♦ www.trimatrixlab.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW119**	Sampled:	11/27/10 10:46
Lab Sample ID:	**1011494-18**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
*79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.22
127-18-4	Tetrachloroethene	1.0U	1.0	0.24
108-88-3	Toluene	1.0U	1.0	0.081
71-55-6	1,1,1-Trichloroethane	**1.7**	1.0	0.13
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.13
79-01-6	Trichloroethene	**0.42J**	1.0	0.084
75-01-4	Vinyl Chloride	1.0U	1.0	0.054
1330-20-7	Xylene (Total)	3.0U	3.0	0.40

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	108	*88-115*
1,2-Dichloroethane-d4	103	*81-116*
Toluene-d8	100	*87-113*
4-Bromofluorobenzene	90	*78-116*

VALIDATED

*See Statement of Data Qualifications

Reviewed By

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5500 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.975.4653 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW121**	Sampled:	11/25/10 10:05
Lab Sample ID:	**1011494-05**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	5.0U	5.0	1.8
71-43-2	Benzene	1.0U	1.0	0.13
74-97-5	Bromochloromethane	1.0U	1.0	0.11
75-27-4	Bromodichloromethane	1.0U	1.0	0.14
75-25-2	Bromoform	1.0U	1.0	0.12
74-83-9	Bromomethane	1.0U	1.0	0.11
75-15-0	Carbon Disulfide	5.0U	5.0	0.60
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.21
108-90-7	Chlorobenzene	1.0U	1.0	0.065
75-00-3	Chloroethane	1.0U	1.0	0.18
67-66-3	Chloroform	**0.60J**	1.0	0.077
74-87-3	Chloromethane	1.0U	1.0	0.10
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.41
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.096
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.27
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.21
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.21
75-34-3	1,1-Dichloroethane	**4.6**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.15
75-35-4	1,1-Dichloroethene	**2.5**	1.0	0.17
156-59-2	cis-1,2-Dichloroethene	**4.3**	1.0	0.19
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.10
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.19
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.15
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.044
591-78-6	2-Hexanone	5.0U	5.0	1.3
75-09-2	Methylene Chloride	1.0U	1.0	0.19
78-93-3	2-Butanone (MEK)	5.0U	5.0	1.5
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.87

Continued on next page

VALIDATED

Reviewed By _____

Date 1/24/11

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the samples tested.

Neal Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW121**	Sampled:	11/25/10 10:05
Lab Sample ID:	**1011494-05**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
*79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.22
127-18-4	Tetrachloroethene	**2.1**	1.0	0.24
108-88-3	Toluene	1.0U	1.0	0.081
71-55-6	1,1,1-Trichloroethane	**3.4**	1.0	0.13
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.13
79-01-6	Trichloroethene	**22**	1.0	0.084
75-01-4	Vinyl Chloride	1.0U	1.0	0.054
1330-20-7	Xylene (Total)	3.0U	3.0	0.40

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	106	*88-115*
1,2-Dichloroethane-d4	103	*81-116*
Toluene-d8	101	*87-113*
4-Bromofluorobenzene	90	*78-116*

VALIDATED

*See Statement of Data Qualifications

Reviewed By [signature]

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5500 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ FAX 616.942.2463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW124**	Sampled:	11/27/10 11:38
Lab Sample ID:	**1011494-17**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	5	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	**11J**	25	9.0
71-43-2	Benzene	5.0U	5.0	0.64
74-97-5	Bromochloromethane	5.0U	5.0	0.57
75-27-4	Bromodichloromethane	5.0U	5.0	0.70
75-25-2	Bromoform	5.0U	5.0	0.58
74-83-9	Bromomethane	5.0U	5.0	0.56
75-15-0	Carbon Disulfide	25U	25	3.0
56-23-5	Carbon Tetrachloride	5.0U	5.0	1.1
108-90-7	Chlorobenzene	5.0U	5.0	0.33
75-00-3	Chloroethane	5.0U	5.0	0.89
67-66-3	Chloroform	5.0U	5.0	0.38
74-87-3	Chloromethane	5.0U	5.0	0.52
96-12-8	1,2-Dibromo-3-chloropropane	5.0U	5.0	2.1
124-48-1	Dibromochloromethane	5.0U	5.0	0.76
106-93-4	1,2-Dibromoethane	5.0U	5.0	0.48
95-50-1	1,2-Dichlorobenzene	5.0U	5.0	1.4
541-73-1	1,3-Dichlorobenzene	5.0U	5.0	1.1
106-46-7	1,4-Dichlorobenzene	5.0U	5.0	1.1
75-34-3	1,1-Dichloroethane	**490**	5.0	0.88
107-06-2	1,2-Dichloroethane	5.0U	5.0	0.75
75-35-4	1,1-Dichloroethene	**25**	5.0	0.86
156-59-2	cis-1,2-Dichloroethene	**280**	5.0	0.96
156-60-5	trans-1,2-Dichloroethene	5.0U	5.0	0.51
78-87-5	1,2-Dichloropropane	5.0U	5.0	0.96
10061-01-5	cis-1,3-Dichloropropene	5.0U	5.0	0.74
10061-02-6	trans-1,3-Dichloropropene	5.0U	5.0	0.93
100-41-4	Ethylbenzene	5.0U	5.0	0.22
591-78-6	2-Hexanone	25U	25	6.6
75-09-2	Methylene Chloride	5.0U	5.0	0.94
78-93-3	2-Butanone (MEK)	25U	25	7.6
108-10-1	4-Methyl-2-pentanone (MIBK)	25U	25	4.3

VALIDATED

Continued on next page

Reviewed By _____

Date 1/14/11

5500 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ Phone 616.975.4500 ♦ Fax 616.442.7467 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW124**	Sampled:	11/27/10 11:38
Lab Sample ID:	**1011494-17**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	5	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	5.0U	5.0	0.54
*79-34-5	1,1,2,2-Tetrachloroethane	5.0U	5.0	1.1
127-18-4	Tetrachloroethene	**14**	5.0	1.2
108-88-3	Toluene	5.0U	5.0	0.40
71-55-6	1,1,1-Trichloroethane	**95**	5.0	0.66
79-00-5	1,1,2-Trichloroethane	5.0U	5.0	0.66
79-01-6	Trichloroethene	**9.2**	5.0	0.42
75-01-4	Vinyl Chloride	**30**	5.0	0.27
1330-20-7	Xylene (Total)	15U	15	2.0

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	108	*88-115*
1,2-Dichloroethane-d4	104	*81-116*
Toluene-d8	100	*87-113*
4-Bromofluorobenzene	91	*78-116*

VALIDATED

*See Statement of Data Qualifications

Reviewed By _____

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7163 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW130**	Sampled:	11/27/10 16:56
Lab Sample ID:	**1011494-26**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/04/10 By: JDM
Dilution Factor:	5	Analyzed:	12/05/10 By: JDM
QC Batch:	1013277	Analytical Batch:	0L04004

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	25U	25	9.0
71-43-2	Benzene	5.0U	5.0	0.64
74-97-5	Bromochloromethane	5.0U	5.0	0.57
75-27-4	Bromodichloromethane	5.0U	5.0	0.70
75-25-2	Bromoform	5.0U	5.0	0.58
74-83-9	Bromomethane	5.0U	5.0	0.56
75-15-0	Carbon Disulfide	25U	25	3.0
56-23-5	Carbon Tetrachloride	5.0U	5.0	1.1
108-90-7	Chlorobenzene	5.0U	5.0	0.33
75-00-3	Chloroethane	5.0U	5.0	0.89
67-66-3	Chloroform	5.0U	5.0	0.38
74-87-3	Chloromethane	5.0U	5.0	0.52
96-12-8	1,2-Dibromo-3-chloropropane	5.0U	5.0	2.1
124-48-1	Dibromochloromethane	5.0U	5.0	0.76
106-93-4	1,2-Dibromoethane	5.0U	5.0	0.48
95-50-1	1,2-Dichlorobenzene	5.0U	5.0	1.4
541-73-1	1,3-Dichlorobenzene	5.0U	5.0	1.1
106-46-7	1,4-Dichlorobenzene	5.0U	5.0	1.1
75-34-3	1,1-Dichloroethane	**29**	5.0	0.88
107-06-2	1,2-Dichloroethane	5.0U	5.0	0.75
75-35-4	1,1-Dichloroethene	**8.4**	5.0	0.86
156-59-2	cis-1,2-Dichloroethene	**8.3**	5.0	0.96
156-60-5	trans-1,2-Dichloroethene	5.0U	5.0	0.51
78-87-5	1,2-Dichloropropane	5.0U	5.0	0.96
10061-01-5	cis-1,3-Dichloropropene	5.0U	5.0	0.74
10061-02-6	trans-1,3-Dichloropropene	5.0U	5.0	0.93
100-41-4	Ethylbenzene	5.0U	5.0	0.22
591-78-6	2-Hexanone	25U	25	6.6
75-09-2	Methylene Chloride	5.0U	5.0	0.94
78-93-3	2-Butanone (MEK)	25U	25	7.6
108-10-1	4-Methyl-2-pentanone (MIBK)	25U	25	4.3

Continued on next page

VALIDATED

Reviewed By

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.5500 ♦ Fax 616.942.7407 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW130**	Sampled:	11/27/10 16:56
Lab Sample ID:	**1011494-26**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/04/10 By: JDM
Dilution Factor:	5	Analyzed:	12/05/10 By: JDM
QC Batch:	1013277	Analytical Batch:	0L04004

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	5.0U	5.0	0.54
79-34-5	1,1,2,2-Tetrachloroethane	5.0U	5.0	1.1
127-18-4	Tetrachloroethene	5.0U	5.0	1.2
108-88-3	Toluene	5.0U	5.0	0.40
71-55-6	1,1,1-Trichloroethane	**430**	5.0	0.66
79-00-5	1,1,2-Trichloroethane	5.0U	5.0	0.66
79-01-6	Trichloroethene	**3.6J**	5.0	0.42
75-01-4	Vinyl Chloride	5.0U	5.0	0.27
1330-20-7	Xylene (Total)	15U	15	2.0

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	102	*88-115*
1,2-Dichloroethane-d4	98	*81-116*
Toluene-d8	95	*87-113*
4-Bromofluorobenzene	89	*78-116*

VALIDATED

Reviewed By _____

Date 1/14/11

This report may not be reproduced, except in full, without written approval of Trimatrix Laboratories.
Individual sample results relate only to the sample tested.

1560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.1500 ♦ Fax 616.942.7168 ♦ www.trimatrixlab.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW133A**	Sampled:	11/27/10 12:56
Lab Sample ID:	**1011494-19**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	5.0U	5.0	1.8
71-43-2	Benzene	1.0U	1.0	0.13
74-97-5	Bromochloromethane	1.0U	1.0	0.11
75-27-4	Bromodichloromethane	1.0U	1.0	0.14
75-25-2	Bromoform	1.0U	1.0	0.12
74-83-9	Bromomethane	1.0U	1.0	0.11
75-15-0	Carbon Disulfide	5.0U	5.0	0.60
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.21
108-90-7	Chlorobenzene	1.0U	1.0	0.065
75-00-3	Chloroethane	1.0U	1.0	0.18
67-66-3	Chloroform	1.0U	1.0	0.077
74-87-3	Chloromethane	1.0U	1.0	0.10
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.41
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.096
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.27
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.21
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.21
75-34-3	1,1-Dichloroethane	**0.21J**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.15
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.17
156-59-2	cis-1,2-Dichloroethene	**0.91J**	1.0	0.19
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.10
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.19
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.15
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.044
591-78-6	2-Hexanone	5.0U	5.0	1.3
75-09-2	Methylene Chloride	1.0U	1.0	0.19
78-93-3	2-Butanone (MEK)	5.0U	5.0	1.5
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.87

Continued on next page

VALIDATED

Reviewed By [illegible]

Date 1/14/11

This report shall not be reproduced except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the samples tested.

5563 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.1500 ♦ Fax 616.942.7[illegible] ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW133A**	Sampled:	11/27/10 12:56
Lab Sample ID:	**1011494-19**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
*79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.22
127-18-4	Tetrachloroethene	1.0U	1.0	0.24
108-88-3	Toluene	1.0U	1.0	0.081
71-55-6	1,1,1-Trichloroethane	**0.86J**	1.0	0.13
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.13
79-01-6	Trichloroethene	1.0U	1.0	0.084
75-01-4	Vinyl Chloride	1.0U	1.0	0.054
1330-20-7	Xylene (Total)	3.0U	3.0	0.40

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	106	*88-115*
1,2-Dichloroethane-d4	99	*81-116*
Toluene-d8	100	*87-113*
4-Bromofluorobenzene	91	*78-116*

VALIDATED

*See Statement of Data Qualifications

Reviewed By _____

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**FD-2** MW-133A Field dup	Sampled:	11/27/10 13:00
Lab Sample ID:	**1011494-20**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	5.0U	5.0	1.8
71-43-2	Benzene	1.0U	1.0	0.13
74-97-5	Bromochloromethane	1.0U	1.0	0.11
75-27-4	Bromodichloromethane	1.0U	1.0	0.14
75-25-2	Bromoform	1.0U	1.0	0.12
74-83-9	Bromomethane	1.0U	1.0	0.11
75-15-0	Carbon Disulfide	5.0U	5.0	0.60
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.21
108-90-7	Chlorobenzene	1.0U	1.0	0.065
75-00-3	Chloroethane	1.0U	1.0	0.18
67-66-3	Chloroform	1.0U	1.0	0.077
74-87-3	Chloromethane	1.0U	1.0	0.10
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.41
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.096
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.27
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.21
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.21
75-34-3	1,1-Dichloroethane	1.0U	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.15
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.17
156-59-2	cis-1,2-Dichloroethene	**0.79J**	1.0	0.19
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.10
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.19
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.15
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.044
591-78-6	2-Hexanone	5.0U	5.0	1.3
75-09-2	Methylene Chloride	1.0U	1.0	0.19
78-93-3	2-Butanone (MEK)	5.0U	5.0	1.5
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.87

Continued on next page

VALIDATED

Reviewed By [illegible]

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7461 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**FD-2** MW-133A Field dup	Sampled:	11/27/10 13:00
Lab Sample ID:	**1011494-20**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
*79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.22
127-18-4	Tetrachloroethene	1.0U	1.0	0.24
108-88-3	Toluene	1.0U	1.0	0.081
71-55-6	1,1,1-Trichloroethane	**0.82J**	1.0	0.13
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.13
79-01-6	Trichloroethene	1.0U	1.0	0.084
75-01-4	Vinyl Chloride	1.0U	1.0	0.054
1330-20-7	Xylene (Total)	3.0U	3.0	0.40

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	105	*88-115*
1,2-Dichloroethane-d4	102	*81-116*
Toluene-d8	100	*87-113*
4-Bromofluorobenzene	92	*78-116*

VALIDATED

*See Statement of Data Qualifications

Reviewed By [signature]

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.
5500 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7163 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW133B**	Sampled:	11/27/10 13:39
Lab Sample ID:	**1011494-21**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/03/10 By: JDM
Dilution Factor:	20	Analyzed:	12/03/10 By: JDM
QC Batch:	1013276	Analytical Batch:	0L04003

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	100U	100	36
71-43-2	Benzene	20U	20	2.5
74-97-5	Bromochloromethane	20U	20	2.3
75-27-4	Bromodichloromethane	20U	20	2.8
75-25-2	Bromoform	20U	20	2.3
74-83-9	Bromomethane	20U	20	2.3
75-15-0	Carbon Disulfide	100U	100	12
56-23-5	Carbon Tetrachloride	20U	20	4.2
108-90-7	Chlorobenzene	20U	20	1.3
75-00-3	Chloroethane	20U	20	3.6
67-66-3	Chloroform	20U	20	1.5
74-87-3	Chloromethane	20U	20	2.1
96-12-8	1,2-Dibromo-3-chloropropane	20U	20	8.3
124-48-1	Dibromochloromethane	20U	20	3.0
106-93-4	1,2-Dibromoethane	20U	20	1.9
95-50-1	1,2-Dichlorobenzene	20U	20	5.5
541-73-1	1,3-Dichlorobenzene	20U	20	4.3
106-46-7	1,4-Dichlorobenzene	20U	20	4.2
75-34-3	1,1-Dichloroethane	**240**	20	3.5
107-06-2	1,2-Dichloroethane	20U	20	3.0
75-35-4	1,1-Dichloroethene	**120**	20	3.4
156-59-2	cis-1,2-Dichloroethene	**1900**	20	3.9
156-60-5	trans-1,2-Dichloroethene	**11J**	20	2.0
78-87-5	1,2-Dichloropropane	20U	20	3.8
10061-01-5	cis-1,3-Dichloropropene	20U	20	2.9
10061-02-6	trans-1,3-Dichloropropene	20U	20	3.7
100-41-4	Ethylbenzene	20U	20	0.88
591-78-6	2-Hexanone	100U	100	27
75-09-2	Methylene Chloride	20U	20	3.8
78-93-3	2-Butanone (MEK)	100U	100	30
108-10-1	4-Methyl-2-pentanone (MIBK)	100U	100	17

Continued on next page

VALIDATED

Reviewed By [signature]

Date 1/14/11

[illegible] report shall not be reproduced except in full, without written authorization [illegible] Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7162 ♦ www.trimatrixlab.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW133B**	Sampled:	11/27/10 13:39
Lab Sample ID:	**1011494-21**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/03/10 By: JDM
Dilution Factor:	20	Analyzed:	12/03/10 By: JDM
QC Batch:	1013276	Analytical Batch:	0L04003

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	20U	20	2.1
79-34-5	1,1,2,2-Tetrachloroethane	20U	20	4.3
127-18-4	Tetrachloroethene	**110**	20	4.9
108-88-3	Toluene	20U	20	1.6
71-55-6	1,1,1-Trichloroethane	**790**	20	2.7
79-00-5	1,1,2-Trichloroethane	20U	20	2.7
79-01-6	Trichloroethene	**180**	20	1.7
75-01-4	Vinyl Chloride	20U	20	1.1
1330-20-7	Xylene (Total)	60U	60	8.1

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	107	*88-115*
1,2-Dichloroethane-d4	102	*81-116*
Toluene-d8	99	*87-113*
4-Bromofluorobenzene	91	*78-116*

VALIDATED

Reviewed By _____

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
In-situ dual sample results relate only to the sample tested.

5500 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax [illegible] ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW133C**	Sampled:	11/27/10 14:12
Lab Sample ID:	**1011494-22**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/03/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013276	Analytical Batch:	0L04003

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	5.0U	5.0	1.8
71-43-2	Benzene	1.0U	1.0	0.13
74-97-5	Bromochloromethane	1.0U	1.0	0.11
75-27-4	Bromodichloromethane	1.0U	1.0	0.14
75-25-2	Bromoform	1.0U	1.0	0.12
74-83-9	Bromomethane	1.0U	1.0	0.11
75-15-0	Carbon Disulfide	5.0U	5.0	0.60
56-23-5	Carbon Tetrachloride	**0.63J**	1.0	0.21
108-90-7	Chlorobenzene	1.0U	1.0	0.065
75-00-3	Chloroethane	1.0U	1.0	0.18
67-66-3	Chloroform	**6.1**	1.0	0.077
74-87-3	Chloromethane	1.0U	1.0	0.10
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.41
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.096
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.27
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.21
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.21
75-34-3	1,1-Dichloroethane	**47**	1.0	0.18
107-06-2	1,2-Dichloroethane	**1.8**	1.0	0.15
75-35-4	1,1-Dichloroethene	**46**	1.0	0.17
156-59-2	cis-1,2-Dichloroethene	**130**	1.0	0.19
156-60-5	trans-1,2-Dichloroethene	**0.30J**	1.0	0.10
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.19
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.15
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.044
591-78-6	2-Hexanone	5.0U	5.0	1.3
75-09-2	Methylene Chloride	1.0U	1.0	0.19
78-93-3	2-Butanone (MEK)	5.0U	5.0	1.5
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.87

VALIDATED

Continued on next page

Reviewed By _____

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5500 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.1567 ♦ www.trimatrixlab.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW133C**	Sampled:	11/27/10 14:12
Lab Sample ID:	**1011494-22**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/03/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013276	Analytical Batch:	0L04003

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.22
127-18-4	Tetrachloroethene	**10**	1.0	0.24
108-88-3	Toluene	1.0U	1.0	0.081
71-55-6	1,1,1-Trichloroethane	**180**	1.0	0.13
79-00-5	1,1,2-Trichloroethane	**0.95J**	1.0	0.13
79-01-6	Trichloroethene	**94**	1.0	0.084
75-01-4	Vinyl Chloride	1.0U	1.0	0.054
1330-20-7	Xylene (Total)	3.0U	3.0	0.40

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	109	*88-115*
1,2-Dichloroethane-d4	104	*81-116*
Toluene-d8	101	*87-113*
4-Bromofluorobenzene	93	*78-116*

VALIDATED

Reviewed By

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7453 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW136**	Sampled:	11/28/10 12:46
Lab Sample ID:	**1011494-30**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/03/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013276	Analytical Batch:	0L04003

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
*67-64-1	Acetone	2.5U	5.0	1.8
71-43-2	Benzene	1.0U	1.0	0.13
74-97-5	Bromochloromethane	1.0U	1.0	0.11
75-27-4	Bromodichloromethane	1.0U	1.0	0.14
75-25-2	Bromoform	1.0U	1.0	0.12
74-83-9	Bromomethane	1.0U	1.0	0.11
75-15-0	Carbon Disulfide	5.0U	5.0	0.60
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.21
108-90-7	Chlorobenzene	1.0U	1.0	0.065
75-00-3	Chloroethane	1.0U	1.0	0.18
67-66-3	Chloroform	**0.82J**	1.0	0.077
74-87-3	Chloromethane	1.0U	1.0	0.10
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.41
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.096
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.27
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.21
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.21
75-34-3	1,1-Dichloroethane	1.0U	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.15
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.17
156-59-2	cis-1,2-Dichloroethene	1.0U	1.0	0.19
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.10
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.19
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.15
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.044
591-78-6	2-Hexanone	5.0U	5.0	1.3
75-09-2	Methylene Chloride	1.0U	1.0	0.19
78-93-3	2-Butanone (MEK)	5.0U	5.0	1.5
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.87

Continued on next page

*See Statement of Data Qualifications

VALIDATED

Reviewed By [illegible]

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7451 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW136**	Sampled:	11/28/10 12:46
Lab Sample ID:	**1011494-30**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/03/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013276	Analytical Batch:	0L04003

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.22
127-18-4	Tetrachloroethene	1.0U	1.0	0.24
108-88-3	Toluene	1.0U	1.0	0.081
71-55-6	1,1,1-Trichloroethane	1.0U	1.0	0.13
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.13
79-01-6	Trichloroethene	1.0U	1.0	0.084
75-01-4	Vinyl Chloride	1.0U	1.0	0.054
1330-20-7	Xylene (Total)	3.0U	3.0	0.40

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	105	*88-115*
1,2-Dichloroethane-d4	104	*81-116*
Toluene-d8	101	*87-113*
4-Bromofluorobenzene	91	*78-116*

VALIDATED

Reviewed By [signature]

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Test and sample results relate only to the sample tested.
CSA Corporate Exchange Court, SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.941.7462 ♦ www.trimatrix.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW200**	Sampled:	11/28/10 13:26
Lab Sample ID:	**1011494-31**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/03/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013276	Analytical Batch:	0L04003

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	5.0U	5.0	1.8
71-43-2	Benzene	1.0U	1.0	0.13
74-97-5	Bromochloromethane	1.0U	1.0	0.11
75-27-4	Bromodichloromethane	1.0U	1.0	0.14
75-25-2	Bromoform	1.0U	1.0	0.12
74-83-9	Bromomethane	1.0U	1.0	0.11
75-15-0	Carbon Disulfide	5.0U	5.0	0.60
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.21
108-90-7	Chlorobenzene	1.0U	1.0	0.065
75-00-3	Chloroethane	1.0U	1.0	0.18
67-66-3	Chloroform	1.0U	1.0	0.077
74-87-3	Chloromethane	1.0U	1.0	0.10
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.41
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.096
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.27
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.21
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.21
75-34-3	1,1-Dichloroethane	1.0U	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.15
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.17
156-59-2	cis-1,2-Dichloroethene	1.0U	1.0	0.19
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.10
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.19
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.15
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.044
591-78-6	2-Hexanone	5.0U	5.0	1.3
75-09-2	Methylene Chloride	1.0U	1.0	0.19
78-93-3	2-Butanone (MEK)	5.0U	5.0	1.5
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.87

VALIDATED

Continued on next page

Reviewed By [signature]

Date 1/14/11

[illegible]
[illegible]
7560 Corporate Exchange [illegible] SE ♦ Grand Rapids, MI 49512 ♦ [illegible] ♦ [illegible] ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW200**	Sampled:	11/28/10 13:26
Lab Sample ID:	**1011494-31**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/03/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013276	Analytical Batch:	0L04003

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.22
127-18-4	Tetrachloroethene	1.0U	1.0	0.24
108-88-3	Toluene	1.0U	1.0	0.081
71-55-6	1,1,1-Trichloroethane	1.0U	1.0	0.13
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.13
79-01-6	Trichloroethene	1.0U	1.0	0.084
75-01-4	Vinyl Chloride	1.0U	1.0	0.054
1330-20-7	Xylene (Total)	3.0U	3.0	0.40

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	106	*88-115*
1,2-Dichloroethane-d4	103	*81-116*
Toluene-d8	102	*87-113*
4-Bromofluorobenzene	91	*78-116*

VALIDATED

Reviewed By _____

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616 975-4500 ♦ Fax 616 957 7461 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW201**	Sampled:	11/28/10 11:52
Lab Sample ID:	**1011494-29**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/04/10 By: JDM
Dilution Factor:	1	Analyzed:	12/05/10 By: JDM
QC Batch:	1013277	Analytical Batch:	0L04004

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	5.0U	5.0	1.8
71-43-2	Benzene	1.0U	1.0	0.13
74-97-5	Bromochloromethane	1.0U	1.0	0.11
75-27-4	Bromodichloromethane	1.0U	1.0	0.14
75-25-2	Bromoform	1.0U	1.0	0.12
74-83-9	Bromomethane	1.0U	1.0	0.11
75-15-0	Carbon Disulfide	5.0U	5.0	0.60
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.21
108-90-7	Chlorobenzene	1.0U	1.0	0.065
75-00-3	Chloroethane	1.0U	1.0	0.18
67-66-3	Chloroform	1.0U	1.0	0.077
74-87-3	Chloromethane	1.0U	1.0	0.10
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.41
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.096
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.27
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.21
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.21
75-34-3	1,1-Dichloroethane	**2.7**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.15
75-35-4	1,1-Dichloroethene	**0.43J**	1.0	0.17
156-59-2	cis-1,2-Dichloroethene	**0.75J**	1.0	0.19
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.10
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.19
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.15
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.044
591-78-6	2-Hexanone	5.0U	5.0	1.3
75-09-2	Methylene Chloride	1.0U	1.0	0.19
78-93-3	2-Butanone (MEK)	5.0U	5.0	1.5
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.87

Continued on next page

VALIDATED

Reviewed By

Date 1/14/11

This report shall not be reproduced except in full, without written authorization of Trimatrix Laboratories, Inc.
Results of sample analysis relate only to the sample tested.

5500 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616 975 4500 ♦ Fax 616 981 7857 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW201**	Sampled:	11/28/10 11:52
Lab Sample ID:	**1011494-29**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/04/10 By: JDM
Dilution Factor:	1	Analyzed:	12/05/10 By: JDM
QC Batch:	1013277	Analytical Batch:	0L04004

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.22
127-18-4	Tetrachloroethene	**0.93J**	1.0	0.24
108-88-3	Toluene	1.0U	1.0	0.081
71-55-6	1,1,1-Trichloroethane	**3.4**	1.0	0.13
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.13
79-01-6	Trichloroethene	**1.2**	1.0	0.084
75-01-4	Vinyl Chloride	1.0U	1.0	0.054
1330-20-7	Xylene (Total)	3.0U	3.0	0.40

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	102	*88-115*
1,2-Dichloroethane-d4	104	*81-116*
Toluene-d8	98	*87-113*
4-Bromofluorobenzene	89	*78-116*

VALIDATED

Reviewed By _____

Date 1/14/11

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW202**	Sampled:	11/28/10 11:10
Lab Sample ID:	**1011494-28**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/03/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013276	Analytical Batch:	0L04003

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	5.0U	5.0	1.8
71-43-2	Benzene	1.0U	1.0	0.13
74-97-5	Bromochloromethane	1.0U	1.0	0.11
75-27-4	Bromodichloromethane	1.0U	1.0	0.14
75-25-2	Bromoform	1.0U	1.0	0.12
74-83-9	Bromomethane	1.0U	1.0	0.11
75-15-0	Carbon Disulfide	5.0U	5.0	0.60
*56-23-5	Carbon Tetrachloride	1.0U	1.0	0.21
108-90-7	Chlorobenzene	1.0U	1.0	0.065
75-00-3	Chloroethane	1.0U	1.0	0.18
67-66-3	Chloroform	1.0U	1.0	0.077
74-87-3	Chloromethane	1.0U	1.0	0.10
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.41
*124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.096
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.27
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.21
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.21
75-34-3	1,1-Dichloroethane	1.0U	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.15
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.17
156-59-2	cis-1,2-Dichloroethene	1.0U	1.0	0.19
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.10
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.19
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.15
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.044
591-78-6	2-Hexanone	5.0U	5.0	1.3
75-09-2	Methylene Chloride	1.0U	1.0	0.19
78-93-3	2-Butanone (MEK)	5.0U	5.0	1.5
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.87

Continued on next page

VALIDATED

*See Statement of Data Qualifications

Reviewed By

Date: 1/14/11

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW202**	Sampled:	11/28/10 11:10
Lab Sample ID:	**1011494-28**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/03/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013276	Analytical Batch:	0L04003

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.22
127-18-4	Tetrachloroethene	**2.1**	1.0	0.24
108-88-3	Toluene	1.0U	1.0	0.081
71-55-6	1,1,1-Trichloroethane	**0.67J**	1.0	0.13
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.13
79-01-6	Trichloroethene	1.0U	1.0	0.084
75-01-4	Vinyl Chloride	1.0U	1.0	0.054
1330-20-7	Xylene (Total)	3.0U	3.0	0.40

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	106	*88-115*
1,2-Dichloroethane-d4	105	*81-116*
Toluene-d8	100	*87-113*
4-Bromofluorobenzene	90	*78-116*

VALIDATED

Reviewed By _____

Date 1/14/11

[illegible]

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW203**	Sampled:	11/28/10 10:29
Lab Sample ID:	**1011494-27**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/03/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013276	Analytical Batch:	0L04003

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	5.0U	5.0	1.8
71-43-2	Benzene	1.0U	1.0	0.13
74-97-5	Bromochloromethane	1.0U	1.0	0.11
75-27-4	Bromodichloromethane	1.0U	1.0	0.14
75-25-2	Bromoform	1.0U	1.0	0.12
74-83-9	Bromomethane	1.0U	1.0	0.11
75-15-0	Carbon Disulfide	5.0U	5.0	0.60
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.21
108-90-7	Chlorobenzene	1.0U	1.0	0.065
75-00-3	Chloroethane	1.0U	1.0	0.18
67-66-3	Chloroform	1.0U	1.0	0.077
74-87-3	Chloromethane	1.0U	1.0	0.10
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.41
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.096
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.27
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.21
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.21
75-34-3	1,1-Dichloroethane	1.0U	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.15
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.17
156-59-2	cis-1,2-Dichloroethene	1.0U	1.0	0.19
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.10
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.19
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.15
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.044
591-78-6	2-Hexanone	5.0U	5.0	1.3
75-09-2	Methylene Chloride	1.0U	1.0	0.19
78-93-3	2-Butanone (MEK)	5.0U	5.0	1.5
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.87

VALIDATED

Continued on next page

Reviewed By [signature]

Date 1/14/11

[illegible] except in full, without written [illegible] Inc.
[illegible] sample results relate only to the sample [illegible]
[illegible] Corporate Exchange Court [illegible] ♦ [illegible] Rapids, MI 49512 ♦ [illegible] ♦ Fax [illegible] ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW203**	Sampled:	11/28/10 10:29
Lab Sample ID:	**1011494-27**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/03/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013276	Analytical Batch:	0L04003

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.22
127-18-4	Tetrachloroethene	**7.3**	1.0	0.24
108-88-3	Toluene	1.0U	1.0	0.081
71-55-6	1,1,1-Trichloroethane	1.0U	1.0	0.13
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.13
79-01-6	Trichloroethene	1.0U	1.0	0.084
75-01-4	Vinyl Chloride	1.0U	1.0	0.054
1330-20-7	Xylene (Total)	3.0U	3.0	0.40

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	107	*88-115*
1,2-Dichloroethane-d4	104	*81-116*
Toluene-d8	101	*87-113*
4-Bromofluorobenzene	90	*78-116*

VALIDATED

Reviewed By _____

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual grab results relate only to the sample tested.

5500 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7962 • www.trimatrix.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW204**	Sampled:	11/25/10 09:10
Lab Sample ID:	**1011494-04**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	5.0U	5.0	1.8
71-43-2	Benzene	1.0U	1.0	0.13
74-97-5	Bromochloromethane	1.0U	1.0	0.11
75-27-4	Bromodichloromethane	1.0U	1.0	0.14
75-25-2	Bromoform	1.0U	1.0	0.12
74-83-9	Bromomethane	1.0U	1.0	0.11
75-15-0	Carbon Disulfide	5.0U	5.0	0.60
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.21
108-90-7	Chlorobenzene	1.0U	1.0	0.065
75-00-3	Chloroethane	1.0U	1.0	0.18
67-66-3	Chloroform	**0.54J**	1.0	0.077
74-87-3	Chloromethane	1.0U	1.0	0.10
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.41
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.096
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.27
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.21
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.21
75-34-3	1,1-Dichloroethane	**5.3**	1.0	0.18
107-06-2	1,2-Dichloroethane	**1.5**	1.0	0.15
75-35-4	1,1-Dichloroethene	**11**	1.0	0.17
156-59-2	cis-1,2-Dichloroethene	**24**	1.0	0.19
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.10
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.19
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.15
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.044
591-78-6	2-Hexanone	5.0U	5.0	1.3
75-09-2	Methylene Chloride	1.0U	1.0	0.19
78-93-3	2-Butanone (MEK)	5.0U	5.0	1.5
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.87

Continued on next page

VALIDATED

Reviewed By [signature]

Date 1/14/11

[illegible] reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
[illegible] sample results [illegible] sample tested
[illegible] ♦ Grand Rapids, MI 49512 ♦ [illegible] ♦ [illegible] ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW204**	Sampled:	11/25/10 09:10
Lab Sample ID:	**1011494-04**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
*79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.22
127-18-4	Tetrachloroethene	**2.5**	1.0	0.24
108-88-3	Toluene	1.0U	1.0	0.081
71-55-6	1,1,1-Trichloroethane	**6.4**	1.0	0.13
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.13
79-01-6	Trichloroethene	**66**	1.0	0.084
75-01-4	Vinyl Chloride	1.0U	1.0	0.054
1330-20-7	Xylene (Total)	3.0U	3.0	0.40

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	106	*88-115*
1,2-Dichloroethane-d4	101	*81-116*
Toluene-d8	102	*87-113*
4-Bromofluorobenzene	90	*78-116*

VALIDATED

*See Statement of Data Qualifications

Reviewed By _____

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5500 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlab.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW205A**	Sampled:	11/25/10 11:45
Lab Sample ID:	**1011494-07**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	5.0U	5.0	1.8
71-43-2	Benzene	1.0U	1.0	0.13
74-97-5	Bromochloromethane	1.0U	1.0	0.11
75-27-4	Bromodichloromethane	1.0U	1.0	0.14
75-25-2	Bromoform	1.0U	1.0	0.12
74-83-9	Bromomethane	1.0U	1.0	0.11
75-15-0	Carbon Disulfide	5.0U	5.0	0.60
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.21
108-90-7	Chlorobenzene	1.0U	1.0	0.065
75-00-3	Chloroethane	1.0U	1.0	0.18
67-66-3	Chloroform	**0.38J**	1.0	0.077
74-87-3	Chloromethane	1.0U	1.0	0.10
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.41
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.096
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.27
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.21
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.21
75-34-3	1,1-Dichloroethane	**13**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.15
75-35-4	1,1-Dichloroethene	**16**	1.0	0.17
156-59-2	cis-1,2-Dichloroethene	**18**	1.0	0.19
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.10
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.19
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.15
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.044
591-78-6	2-Hexanone	5.0U	5.0	1.3
75-09-2	Methylene Chloride	1.0U	1.0	0.19
78-93-3	2-Butanone (MEK)	5.0U	5.0	1.5
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.87

Continued on next page

VALIDATED

Reviewed By

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Results apply only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.975.4747 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW205A**	Sampled:	11/25/10 11:45
Lab Sample ID:	**1011494-07**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
*79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.22
127-18-4	Tetrachloroethene	**23**	1.0	0.24
108-88-3	Toluene	1.0U	1.0	0.081
71-55-6	1,1,1-Trichloroethane	**41**	1.0	0.13
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.13
79-01-6	Trichloroethene	**24**	1.0	0.084
75-01-4	Vinyl Chloride	1.0U	1.0	0.054
1330-20-7	Xylene (Total)	3.0U	3.0	0.40

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	105	*88-115*
1,2-Dichloroethane-d4	107	*81-116*
Toluene-d8	100	*87-113*
4-Bromofluorobenzene	90	*78-116*

VALIDATED

*See Statement of Data Qualifications

Reviewed By _____

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7865 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW205B**	Sampled:	11/25/10 11:00
Lab Sample ID:	**1011494-06**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	5.0U	5.0	1.8
71-43-2	Benzene	1.0U	1.0	0.13
74-97-5	Bromochloromethane	1.0U	1.0	0.11
75-27-4	Bromodichloromethane	1.0U	1.0	0.14
75-25-2	Bromoform	1.0U	1.0	0.12
74-83-9	Bromomethane	1.0U	1.0	0.11
75-15-0	Carbon Disulfide	5.0U	5.0	0.60
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.21
108-90-7	Chlorobenzene	1.0U	1.0	0.065
75-00-3	Chloroethane	1.0U	1.0	0.18
67-66-3	Chloroform	**0.41J**	1.0	0.077
74-87-3	Chloromethane	1.0U	1.0	0.10
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.41
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.096
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.27
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.21
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.21
75-34-3	1,1-Dichloroethane	**15**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.15
75-35-4	1,1-Dichloroethene	**17**	1.0	0.17
156-59-2	cis-1,2-Dichloroethene	**23**	1.0	0.19
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.10
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.19
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.15
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.044
591-78-6	2-Hexanone	5.0U	5.0	1.3
75-09-2	Methylene Chloride	1.0U	1.0	0.19
78-93-3	2-Butanone (MEK)	5.0U	5.0	1.5
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.87

VALIDATED

Continued on next page

Reviewed By _____

Date 1/14/11

This report shall not be reproduced, except in full, without written approval of Trimatrix Laboratories, Inc. Individual sample results relate only to the sample tested.

560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW205B**	Sampled:	11/25/10 11:00
Lab Sample ID:	**1011494-06**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
*79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.22
127-18-4	Tetrachloroethene	**23**	1.0	0.24
108-88-3	Toluene	1.0U	1.0	0.081
71-55-6	1,1,1-Trichloroethane	**42**	1.0	0.13
79-00-5	1,1,2-Trichloroethane	**0.56J**	1.0	0.13
79-01-6	Trichloroethene	**24**	1.0	0.084
75-01-4	Vinyl Chloride	1.0U	1.0	0.054
1330-20-7	Xylene (Total)	3.0U	3.0	0.40

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	107	*88-115*
1,2-Dichloroethane-d4	101	*81-116*
Toluene-d8	99	*87-113*
4-Bromofluorobenzene	88	*78-116*

VALIDATED

*See Statement of Data Qualifications

Reviewed By

Date 1/14/11

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW206A**	Sampled:	11/29/10 14:36
Lab Sample ID:	**1011494-36**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/04/10 By: JDM
Dilution Factor:	1	Analyzed:	12/05/10 By: JDM
QC Batch:	1013277	Analytical Batch:	0L04004

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	5.0U	5.0	1.8
71-43-2	Benzene	1.0U	1.0	0.13
74-97-5	Bromochloromethane	1.0U	1.0	0.11
75-27-4	Bromodichloromethane	1.0U	1.0	0.14
75-25-2	Bromoform	1.0U	1.0	0.12
74-83-9	Bromomethane	1.0U	1.0	0.11
75-15-0	Carbon Disulfide	5.0U	5.0	0.60
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.21
108-90-7	Chlorobenzene	1.0U	1.0	0.065
75-00-3	Chloroethane	1.0U	1.0	0.18
67-66-3	Chloroform	**0.16J**	1.0	0.077
74-87-3	Chloromethane	1.0U	1.0	0.10
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.41
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.096
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.27
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.21
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.21
75-34-3	1,1-Dichloroethane	**13**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.15
75-35-4	1,1-Dichloroethene	**4.4**	1.0	0.17
156-59-2	cis-1,2-Dichloroethene	**4.5**	1.0	0.19
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.10
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.19
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.15
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.044
591-78-6	2-Hexanone	5.0U	5.0	1.3
75-09-2	Methylene Chloride	1.0U	1.0	0.19
78-93-3	2-Butanone (MEK)	5.0U	5.0	1.5
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.87

Continued on next page

VALIDATED

Reviewed By

Date 1/14/11

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW206A**	Sampled:	11/29/10 14:36
Lab Sample ID:	**1011494-36**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/04/10 By: JDM
Dilution Factor:	1	Analyzed:	12/05/10 By: JDM
QC Batch:	1013277	Analytical Batch:	0L04004

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.22
127-18-4	Tetrachloroethene	**1.5**	1.0	0.24
108-88-3	Toluene	1.0U	1.0	0.081
71-55-6	1,1,1-Trichloroethane	**9.7**	1.0	0.13
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.13
79-01-6	Trichloroethene	**4.3**	1.0	0.084
75-01-4	Vinyl Chloride	**3.6**	1.0	0.054
1330-20-7	Xylene (Total)	3.0U	3.0	0.40

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	104	*88-115*
1,2-Dichloroethane-d4	99	*81-116*
Toluene-d8	96	*87-113*
4-Bromofluorobenzene	91	*78-116*

VALIDATED

Reviewed By _____

Date 1/14/11

This report may not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results pertain only to the sample tested.

5960 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.1500 ♦ Fax 616.942.7165 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW206B**	Sampled:	11/29/10 13:39
Lab Sample ID:	**1011494-34**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/04/10 By: JDM
Dilution Factor:	1	Analyzed:	12/05/10 By: JDM
QC Batch:	1013277	Analytical Batch:	0L04004

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	5.0U	5.0	1.8
71-43-2	Benzene	**0.21J**	1.0	0.13
74-97-5	Bromochloromethane	1.0U	1.0	0.11
75-27-4	Bromodichloromethane	1.0U	1.0	0.14
75-25-2	Bromoform	1.0U	1.0	0.12
74-83-9	Bromomethane	1.0U	1.0	0.11
75-15-0	Carbon Disulfide	5.0U	5.0	0.60
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.21
108-90-7	Chlorobenzene	1.0U	1.0	0.065
75-00-3	Chloroethane	1.0U	1.0	0.18
67-66-3	Chloroform	**0.92J**	1.0	0.077
74-87-3	Chloromethane	1.0U	1.0	0.10
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.41
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.096
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.27
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.21
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.21
75-34-3	1,1-Dichloroethane	**78**	1.0	0.18
107-06-2	1,2-Dichloroethane	**2.3**	1.0	0.15
75-35-4	1,1-Dichloroethene	**71**	1.0	0.17
156-59-2	cis-1,2-Dichloroethene	**72**	1.0	0.19
156-60-5	trans-1,2-Dichloroethene	**0.53J**	1.0	0.10
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.19
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.15
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.044
591-78-6	2-Hexanone	5.0U	5.0	1.3
75-09-2	Methylene Chloride	1.0U	1.0	0.19
78-93-3	2-Butanone (MEK)	5.0U	5.0	1.5
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.87

Continued on next page

VALIDATED

Reviewed By [signature]

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7461 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW206B**	Sampled:	11/29/10 13:39
Lab Sample ID:	**1011494-34**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/04/10 By: JDM
Dilution Factor:	1	Analyzed:	12/05/10 By: JDM
QC Batch:	1013277	Analytical Batch:	0L04004

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.22
127-18-4	Tetrachloroethene	**5.5**	1.0	0.24
108-88-3	Toluene	1.0U	1.0	0.081
71-55-6	1,1,1-Trichloroethane	**55**	1.0	0.13
79-00-5	1,1,2-Trichloroethane	**5.6**	1.0	0.13
79-01-6	Trichloroethene	**34**	1.0	0.084
75-01-4	Vinyl Chloride	**1.1**	1.0	0.054
1330-20-7	Xylene (Total)	3.0U	3.0	0.40

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	103	*88-115*
1,2-Dichloroethane-d4	97	*81-116*
Toluene-d8	97	*87-113*
4-Bromofluorobenzene	91	*78-116*

VALIDATED

Reviewed By _____

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7403 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW206C**	Sampled:	11/29/10 14:12
Lab Sample ID:	**1011494-35**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/04/10 By: JDM
Dilution Factor:	1	Analyzed:	12/05/10 By: JDM
QC Batch:	1013277	Analytical Batch:	0L04004

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	5.0U	5.0	1.8
71-43-2	Benzene	1.0U	1.0	0.13
74-97-5	Bromochloromethane	1.0U	1.0	0.11
75-27-4	Bromodichloromethane	1.0U	1.0	0.14
75-25-2	Bromoform	1.0U	1.0	0.12
74-83-9	Bromomethane	1.0U	1.0	0.11
75-15-0	Carbon Disulfide	5.0U	5.0	0.60
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.21
108-90-7	Chlorobenzene	1.0U	1.0	0.065
75-00-3	Chloroethane	1.0U	1.0	0.18
67-66-3	Chloroform	1.0U	1.0	0.077
74-87-3	Chloromethane	1.0U	1.0	0.10
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.41
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.096
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.27
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.21
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.21
75-34-3	1,1-Dichloroethane	**3.9**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.15
75-35-4	1,1-Dichloroethene	**3.1**	1.0	0.17
156-59-2	cis-1,2-Dichloroethene	**5.1**	1.0	0.19
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.10
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.19
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.15
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.044
591-78-6	2-Hexanone	5.0U	5.0	1.3
75-09-2	Methylene Chloride	1.0U	1.0	0.19
78-93-3	2-Butanone (MEK)	5.0U	5.0	1.5
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.87

Continued on next page

VALIDATED

Reviewed By

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

4560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW206C**	Sampled:	11/29/10 14:12
Lab Sample ID:	**1011494-35**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/04/10 By: JDM
Dilution Factor:	1	Analyzed:	12/05/10 By: JDM
QC Batch:	1013277	Analytical Batch:	0L04004

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.22
127-18-4	Tetrachloroethene	1.0U	1.0	0.24
108-88-3	Toluene	1.0U	1.0	0.081
71-55-6	1,1,1-Trichloroethane	1.0U	1.0	0.13
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.13
79-01-6	Trichloroethene	**16**	1.0	0.084
75-01-4	Vinyl Chloride	1.0U	1.0	0.054
1330-20-7	Xylene (Total)	3.0U	3.0	0.40

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	101	*88-115*
1,2-Dichloroethane-d4	99	*81-116*
Toluene-d8	97	*87-113*
4-Bromofluorobenzene	90	*78-116*

VALIDATED

Reviewed By [signature]

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7463 ♦ www.trimatrix.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW207**	Sampled:	11/25/10 12:30
Lab Sample ID::	**1011494-08**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	5.0U	5.0	1.8
71-43-2	Benzene	1.0U	1.0	0.13
74-97-5	Bromochloromethane	1.0U	1.0	0.11
75-27-4	Bromodichloromethane	1.0U	1.0	0.14
75-25-2	Bromoform	1.0U	1.0	0.12
74-83-9	Bromomethane	1.0U	1.0	0.11
75-15-0	Carbon Disulfide	5.0U	5.0	0.60
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.21
108-90-7	Chlorobenzene	1.0U	1.0	0.065
75-00-3	Chloroethane	1.0U	1.0	0.18
67-66-3	Chloroform	**0.22J**	1.0	0.077
74-87-3	Chloromethane	1.0U	1.0	0.10
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.41
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.096
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.27
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.21
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.21
75-34-3	1,1-Dichloroethane	**1.3**	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.15
75-35-4	1,1-Dichloroethene	**0.72J**	1.0	0.17
156-59-2	cis-1,2-Dichloroethene	**1.3**	1.0	0.19
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.10
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.19
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.15
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.044
591-78-6	2-Hexanone	5.0U	5.0	1.3
75-09-2	Methylene Chloride	1.0U	1.0	0.19
78-93-3	2-Butanone (MEK)	5.0U	5.0	1.5
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.87

Continued on next page

VALIDATED

Reviewed By _____

Date 1/14/11

5560 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.5000 ♦ Fax 616.942.7463 ♦ www.trimatrixlab.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW207**	Sampled:	11/25/10 12:30
Lab Sample ID:	**1011494-08**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/02/10 By: JDM
Dilution Factor:	1	Analyzed:	12/03/10 By: JDM
QC Batch:	1013275	Analytical Batch:	0L04002

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
*79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.22
127-18-4	Tetrachloroethene	**2.2**	1.0	0.24
108-88-3	Toluene	1.0U	1.0	0.081
71-55-6	1,1,1-Trichloroethane	**3.0**	1.0	0.13
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.13
79-01-6	Trichloroethene	**6.0**	1.0	0.084
75-01-4	Vinyl Chloride	1.0U	1.0	0.054
1330-20-7	Xylene (Total)	3.0U	3.0	0.40

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	106	*88-115*
1,2-Dichloroethane-d4	102	*81-116*
Toluene-d8	100	*87-113*
4-Bromofluorobenzene	92	*78-116*

VALIDATED

*See Statement of Data Qualifications

Reviewed By _____

Date 1/14/11

The report shall not be reproduced, except in full, without written approval of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5500 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.942.7563 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**Trip Blank**	Sampled:	11/29/10 00:00
Lab Sample ID:	**1011494-38**	Sampled By:	TML
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/04/10 By: JDM
Dilution Factor:	1	Analyzed:	12/05/10 By: JDM
QC Batch:	1013277	Analytical Batch:	0L04004

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	**3.6J**	5.0	1.8
71-43-2	Benzene	1.0U	1.0	0.13
74-97-5	Bromochloromethane	1.0U	1.0	0.11
75-27-4	Bromodichloromethane	1.0U	1.0	0.14
75-25-2	Bromoform	1.0U	1.0	0.12
74-83-9	Bromomethane	1.0U	1.0	0.11
75-15-0	Carbon Disulfide	5.0U	5.0	0.60
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.21
108-90-7	Chlorobenzene	1.0U	1.0	0.065
75-00-3	Chloroethane	1.0U	1.0	0.18
67-66-3	Chloroform	1.0U	1.0	0.077
74-87-3	Chloromethane	1.0U	1.0	0.10
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.41
124-48-1	Dibromochloromethane	1.0U	1.0	0.15
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.096
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.27
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.21
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.21
75-34-3	1,1-Dichloroethane	1.0U	1.0	0.18
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.15
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.17
156-59-2	cis-1,2-Dichloroethene	1.0U	1.0	0.19
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.10
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.19
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.15
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.19
100-41-4	Ethylbenzene	1.0U	1.0	0.044
591-78-6	2-Hexanone	5.0U	5.0	1.3
75-09-2	Methylene Chloride	1.0U	1.0	0.19
78-93-3	2-Butanone (MEK)	5.0U	5.0	1.5
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.87

Continued on next page

VALIDATED

Reviewed By B. F.

Date 1/14/11

This report shall not be reproduced, except in full, without written approval of Trimatrix Laboratories, Inc.
Individual results relate solely to the sample tested.

5500 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.5300 ♦ Fax 616.942.7463 ♦ www.trimatrixlab.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1011494**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**Trip Blank**	Sampled:	11/29/10 00:00
Lab Sample ID:	**1011494-38**	Sampled By:	TML
Matrix:	Water	Received:	11/30/10 08:45
Unit:	ug/L	Prepared:	12/04/10 By: JDM
Dilution Factor:	1	Analyzed:	12/05/10 By: JDM
QC Batch:	1013277	Analytical Batch:	0L04004

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.22
127-18-4	Tetrachloroethene	1.0U	1.0	0.24
108-88-3	Toluene	1.0U	1.0	0.081
71-55-6	1,1,1-Trichloroethane	1.0U	1.0	0.13
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.13
79-01-6	Trichloroethene	1.0U	1.0	0.084
75-01-4	Vinyl Chloride	1.0U	1.0	0.054
1330-20-7	Xylene (Total)	3.0U	3.0	0.40

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	99	*88-115*
1,2-Dichloroethane-d4	100	*81-116*
Toluene-d8	95	*87-113*
4-Bromofluorobenzene	91	*78-116*

VALIDATED

Reviewed By B. F.

Date 1/14/11

This report shall not be reproduced, except in full, without written authorization of Trimatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5500 Corporate Exchange Court SE ♦ Grand Rapids, MI 49512 ♦ 616.975.4500 ♦ Fax 616.949.2163 ♦ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

5560 Corporate Exchange Court SE
Grand Rapids, MI 49512
Phone (616) 975-4500 Fax (616) 942-7463
www.trimatrixlabs.com

Chain of Custody Record

COC No. 136408

Pg. 1 of 4

For Lab Use Only
Cooler: —
VOA Rec'd Trip: Box
Receipt Log No.: 398
Project Code:
Work Order No.: 101494

Client Name: Nationwide Env Svcs
Address: 14818 6th Ave SE SA
City/State/Zip: Golden Co 80401
Phone: 303 232 2134
Email: blaflamme@nationwideenv.com

Project Name: SE Rock - Fall 2010
Client Project No. / P.O. No.:
Invoice To: ☐ Client ☐ Other (comments)
Contact Report To: Dotterer/Laflamme

Analyses Requested: VOC per 8260

PRESERVATIVES
A NONE pH~7
B HNO3 pH<2
C H2SO4 pH<2
D 1+1 HCl pH<2
E NaOH pH>12
F 2%AcNaOH pH>9
G MeOH
H Other (note below)

Container Type (correspond to Container Packing List)

Selected	Matrix	Sample Number	Field Sample ID	Cooler ID	Sample Date	Sample Time	Matrix	Number of Containers Submitted	Sample Comments
		01	MW 117B	N/A	11/24	1124	x GW	3	
		02	MW 117C		11/24	1212	x GW	3	
		03	MW 117D		11/24	1300	x GW	3	
		04	MW 204		11/25	910	x GW	3	
		05	MW 121		11/25	1005	x GW	3	
		06	MW 205B		11/25	1100	x GW	3	
		07	MW 205A		11/25	1145	x GW	3	
		08	MW 207		11/25	1230	x GW	3	
		09	MW 102A		11/26	1110	x GW	3	
		10	FD-1		11/26	1112	x GW	3	

Sampled By (print): Patrick Egan
Signature: [signature]
Company: AEE

How Shipped? Hand ___ Carrier Fedex
Tracking No. 7964 9644 9851
1. Relinquished By: [signature] Date 11/29/10 Time 1930
1. Received By: Date Time
2. Relinquished By: Date Time
2. Received By: Date Time
3. Relinquished By: Date Time
3. Received By: [signature] Date 11/30/10 Time 0815

Comments:
* All Samples kept in secure location at ≤4°C.

WHITE COPY - REPORT YELLOW COPY - LABORATORY PINK COPY - FIELD

TRIMATRIX LABORATORIES
5560 Corporate Exchange Court SE
Grand Rapids, MI 49512
Phone (616) 975-4500 Fax (616) 942-7463
www.trimatrixlabs.com

Chain of Custody Record

COC No 136409

Pg 2 of 4

For Lab Use Only
Cart
VOA Rack/Tray: Box
Reaction Log No: 398
Project Chemist
Work Order No: 101494

Client Name: Nationwide Env Svcs
Address: 14818 6th Ave Ste 5A
City, State, Zip: Golden CO 80401
Phone/Fax: 303 232 2434
Email

Project Name: SE Rock - Fall 2010
Client Project No. / P.O. No.
Invoice To: ☐ Client ☐ Other (comments)
Contact/Report To: Dotterer/LaFlamme

Analyses Requested: VOC per List

Container Type (consistent with Container Packing List)

PRESERVATIVES
A NONE pH>7
B HNO_3 pH<2
C H_2SO_4 pH<2
D 1+1 HCl pH<2
E NaOH pH>12
F ZnAc/NaOH pH>9
G MeOH
H Other (note below)

Sample Number	Field Sample ID	Copy ID	Sample Date	Sample Time	Matrix	Number of Containers Submitted	Sample Comments
11	MW 102B	N/A	11/26	1159	GW	3	
12	MW 102C		11/26	1230	GW	3	
13	MW 101C		11/26	1318	GW	3	
14	MW 101B		11/26	1349	GW	3	
15	MW 101A		11/26	1420	GW	3	
16	MW 101D		11/26	1503	GW	3	
17	MW 124		11/27	1138	GW	3	
18	MW 119		11/27	1046	GW	3	
19	MW 133A		11/27	1256	GW	3	
20	FD-2		11/27	1300	GW	3	

Sampled By (print): Patrick Egan
Sampler's Signature:
Company: AEE

How Shipped? Hand Carrier: Fedex
Tracking No. 7964 9644 9851
Date 11/29/10 Time 1930

Comments: All Samples kept in Secure Location at ≤ 4°C

Relinquished By: Date: Time:
Received By: Date: Time:
Relinquished By: Date: Time:
Received By: Date: Time:
Relinquished By: Date: Time:
Received By: Date: Time: 11/30/10 0815

WHITE COPY - REPORT YELLOW COPY - LABORATORY PINK COPY - FIELD

TRIMATRIX LABORATORIES

5560 Corporate Exchange Court SE
Grand Rapids, MI 49512
Phone (616) 975-4500 Fax (616) 942-7463
www.trimatrixlabs.com

Chain of Custody Record

COC No. 136410

Pg. 3 of 4

For Lab Use Only

Cart

VOA Rack/Tray: BOX

Receipt Log No.: 398

Project Chemist:

Work Order No.: 1011494

Client Name: Nationwide Env. Svcs

Address: 14818 6th Ave STE 5A

City/State Zip: Golden CO 80401

Phone/Fax: 303 232 2134

Email:

Project No.: SE Rock - Fall 2010

Client Project No. / P.O. No.:

Invoice to: ☐ Client ☐ Other (comments)

Contact Report to: Dotterer/LaFlamme

Analyses Requested: VOC per List

Container Type (corresponds to Container Packing List): 1

PRESERVATIVES
A NONE pH>7
B HNO_3 pH<2
C H_2SO_4 pH<2
D 1:1 HCl pH<2
E NaOH pH>12
F ZnAc/NaOH pH>9
G MeOH
H Other (note below)

Schedule	Sample Number	Field Sample ID	Cooler ID	Sample Date	Sample Time	Matrix	Number of Containers Submitted	Type	Sample Comments
	21	MW 133B	NA	11/27	1339	x GW 3		3	
	22	MW 133C		11/27	1412	x GW 3		3	
	23	MW 16		11/27	1500	x GW 3		3	
	24	MW 114B		11/27	1525	x GW 3		3	
	25	MW 114A		11/27	1558	x GW 3		3	
	26	MW 130		11/27	1656	x GW 3		3	
	27	MW 203		11/28	1029	x GW 3		3	
	28	MW 202		11/28	1110	x GW 3		3	
	29	MW 201		11/28	1152	x GW 3		3	
	30	MW 136		11/28	1246	x GW 3		3	

Sampled By (print): Patrick Egan

Sampler's Signature: [signature]

Company: AEE

How Shipped? Hand Carrier: Fedex

Tracking No.: 7964 9644 9851

Comments: *all Samples Kept in Secure Location at ≤4°C

1. Relinquished By: [signature] Date: 11/29/10 Time: 1930

2. Relinquished By: Date: Time:

3. Relinquished By: Date: Time:

1. Received By: Date: Time:

2. Received By: Date: Time:

3. Received By: [signature] Date: 11/30/10 Time: 0815

WHITE COPY - REPORT YELLOW COPY - LABORATORY PINK COPY - FIELD

TRIMATRIX LABORATORIES

5500 Corporate Exchange Court SE
Grand Rapids, MI 49512
Phone (616) 975-4500 Fax (616) 942-7463
www.trimatrixlabs.com

Chain of Custody Record

COC No. 136411

Pg. 4 of 4

For Lab Use Only
Cart
VOA Fan/Tray: BOX
Receipt Log No.: 398
Project Chemist:
Work Order No.: 1011494

Client Name: Nationwide Env Svcs
Address: 14818 6th Ave STE 5A
City/State/Zip: Golden CO 80401
Phone/Fax: 303 232 2134
Email:

P.O. Name: SE Rock - Fall 2010
Client Project No. / P.O. No.:
Invoice To: ☐ Client ☐ Other (comments)
Contact/Report To: Dotterrer/LaFlamme

Analyses Requested: D VOC per List

PRESERVATIVES
A NONE pH>7
B HNO_3 pH<2
C H_2SO_4 pH<2
D 1+1 HCl pH<2
E NaOH pH<12
F ZnAc/NaOH pH<9
G MeOH
H Other (note below)

Container Type (corresponds to Container Packing List): 1

Schedule	Matrix Code	Sample Number	Field Sample ID	Cooler ID	Sample Date	Sample Time	Matrix	Number of Containers Submitted	Total	Sample Comments
		31	MW 200	NA	11/28	1326	x GW 3		3	
		32	MW 113B		11/28	1402	x GW 3		3	
		33	MW 113A		11/28	1448	x GW 3		3	
		34	MW 206B		11/29	1339	x GW 3		3	
		35	MW 206C		11/29	1412	x GW 3		3	
		36	MW 206A		11/29	1436	x GW 3		3	
		37	MW 47		11/29	1536	x GW 3		3	
		38	Trip Blank							

Sampled By (print): Patrick Egan
Sampler's Signature: [signature]
Company: AEE

How Shipped? Hand Carrier: Fedex
Tracking No.: 7964 9644 9851
1. Received By: [signature] Date: 11/29/10 Time: 1930
1. Received By: Date: Time:
2. Relinquished By: Date: Time:
2. Received By: Date: Time:
3. Relinquished By: Date: Time:
3. Received By: [signature] Date: 11/30/10 Time: 0845

Comments

WHITE COPY - REPORT YELLOW COPY - LABORATORY PINK COPY - FIELD

APPENDIX B
Ground Water Monitoring
Field Data Sheets

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	60	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW16**
Casing Stickup (Ft.)	2.36	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	27-Nov-10
Total Well Depth (Ft.) TOC	62.36	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	22.86	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	39.5	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	æS/cm	FTU	mL/min	(Ft.) TOC	
							0	22.86	Static
14:41	7.08	5.54	12.65	-21	1.363		500		Start Time
14:42	7.09	5.53	12.53	-20	1.368		500		redish brown
14:43	7.09	5.58	12.51	-20	1.369		500	22.92	clear
14:44	7.18	9.47	11.35	-19	1.392		500		clear
14:45	7.12	6.19	12.4	-17	1.365		500		clear
14:46	7.11	5.8	12.47	-19	1.368		500	22.92	clear
14:47	7.1	5.86	12.51	-19	1.37		500		clear
14:48	7.1	5.86	12.52	-19	1.371		500		clear
14:49	7.11	5.94	12.52	-19	1.37		500		clear
14:50	7.11	5.96	12.54	-18	1.369		500		clear
14:51	7.11	5.95	12.54	-18	1.371		500		clear
14:52	7.11	5.92	12.53	-18	1.371		500	22.94	clear
14:53	7.11	5.86	12.54	-17	1.372	23	500		clear
MINUTES							**TOTAL LITERS**		
12.0	0.00	-1.51%	0.00%	1.00	0.07%		**6.00**		

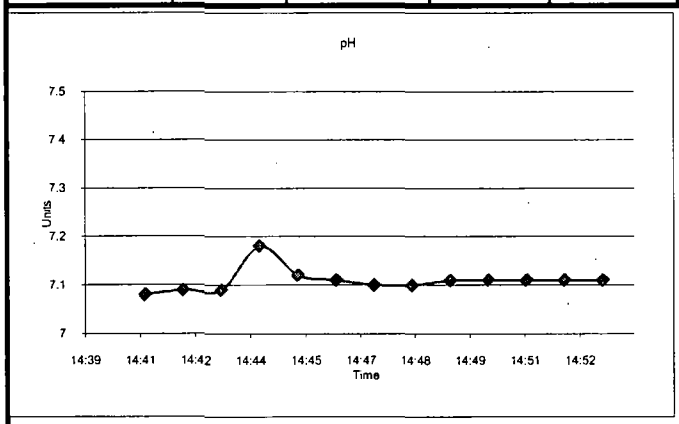

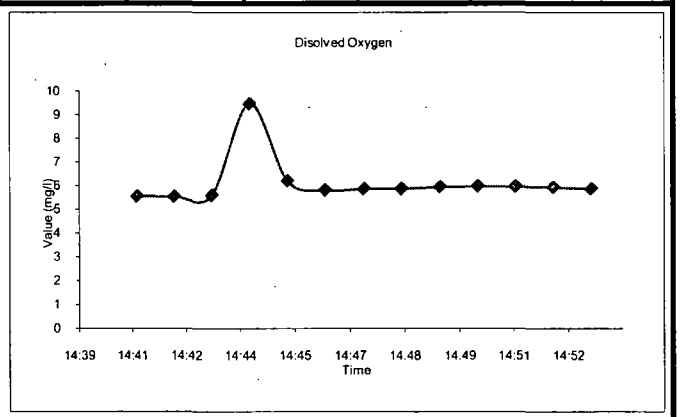

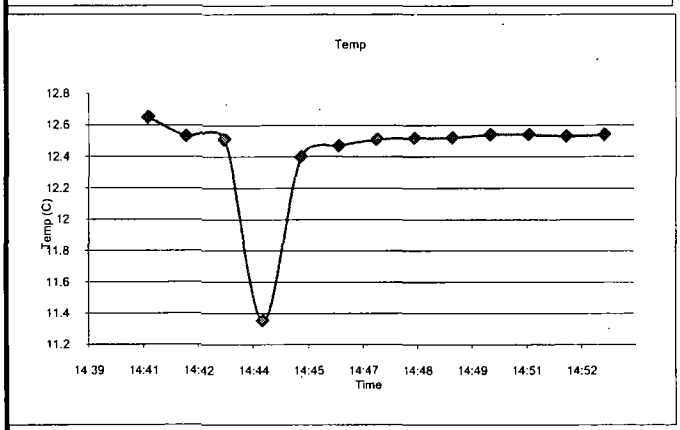

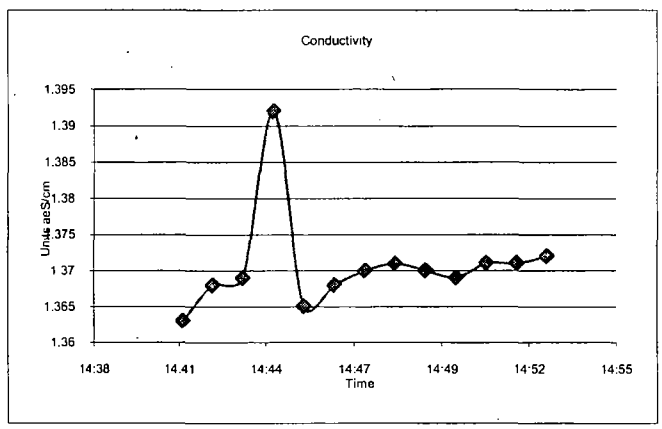

Remarks: (well condition, maintenance, etc...)

Limited access - IEPA Lock

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	52	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 47**
Casing Stickup (Ft.)	-0.63	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	29-Nov-10
Total Well Depth (Ft.) TOC	54.49	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	40.85	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	13.64	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	æS/cm	FTU	mL/min	(Ft.) TOC	
							0	40.85	Static
15:20	7.36	10.08	12.31	-10	1.464		310		Start Time
15:21	7.41	10.11	12.28	-10	1.466		310		brown
15:22	7.38	10.16	12.3	-9	1.467		310		brown
15:23	7.38	10.3	12.31	-9	1.467		310	40.91	brown
15:24	7.39	10.2	12.31	-8	1.469		310		clear
15:25	7.38	10.02	12.32	-8	1.471		310		clear
15:26	7.41	10.09	12.3	-8	1.473		310		clear
15:27	7.42	10.38	12.31	-7	1.474		310	40.91	clear
15:28	7.43	10.18	12.32	-7	1.475	33	310		clear
MINUTES							**TOTAL LITERS**		
8.0	0.02	0.89%	0.16%	1.00	0.14%		**2.48**		

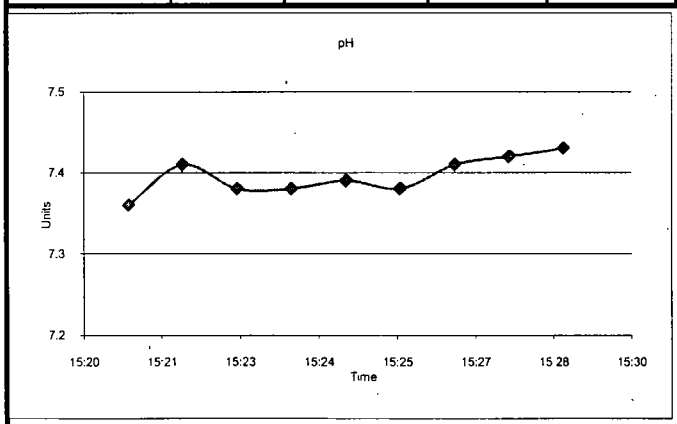

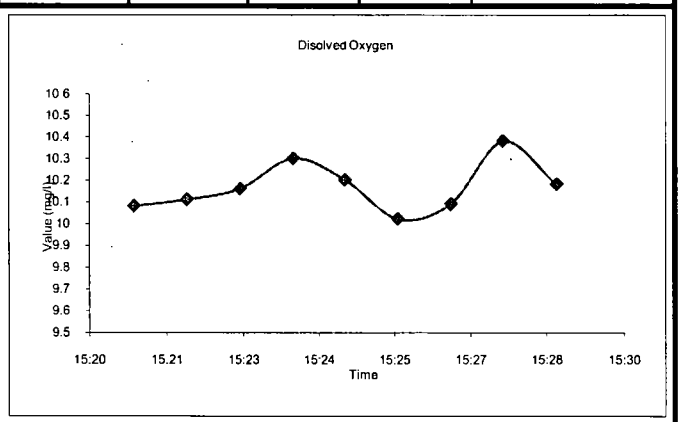

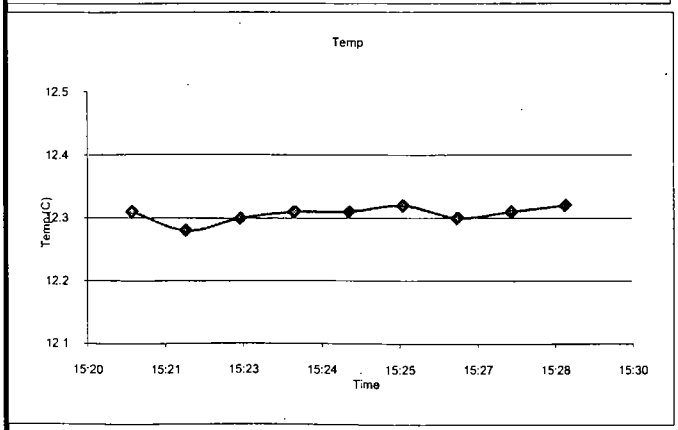

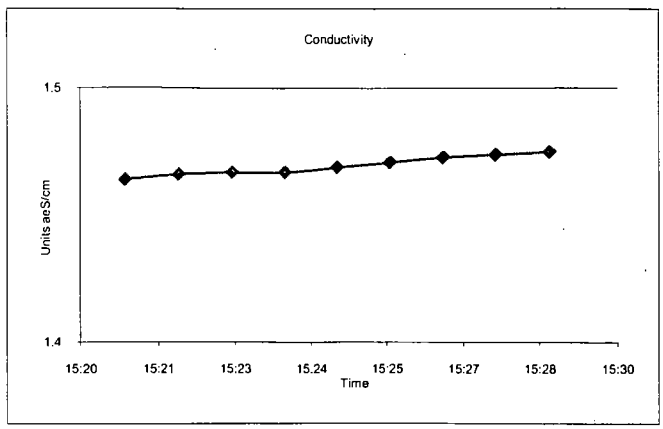

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	88	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 101A**
Casing Stickup (Ft.)	1.45	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	26-Nov-10
Total Well Depth (Ft.) TOC	90.35	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	39.39	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	50.96	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	æS/cm	FTU	mL/min	(Ft.) TOC	
							0	39.39	Static
14:13	7.02	0.88	10.6	-164	0.851		480		Start Time
14:14	7.02	0.92	10.6	-158	0.852		480		clear
14:15	7.02	0.91	10.57	-154	0.852		480		clear
14:16	7.02	0.82	10.58	-145	0.852		480		clear
14:17	7.02	0.72	10.57	-145	0.851		480		clear
14:18	7.02	0.85	10.56	-26	0.85		480		clear
14:19	7.02	0.76	10.55	-94	0.84		480	39.4	clear
14:20	7.02	0.71	10.49	-129	0.847		480		clear
14:21	7.02	0.6	10.4	-134	0.85		480		clear
14:22	7.02	0.51	10.41	-145	0.85		480		clear
14:23	7.02	0.5	10.47	-151	0.85		480		clear
14:24	7.02	0.51	10.41	-158	0.851		480	39.4	clear
14:25	7.02	0.49	10.45	-164	0.85		480		clear
14:26	7.02	0.49	10.45	-161	0.851	24	480		clear
MINUTES							**TOTAL LITERS**		
13.0	0.00	-3.92%	0.38%	-3.00	0.00%		**6.24**		

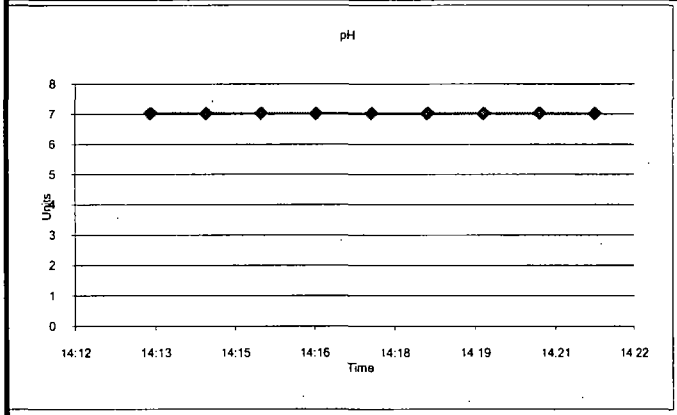

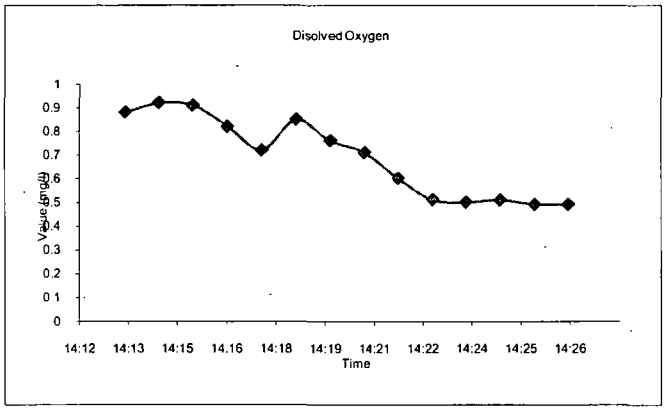

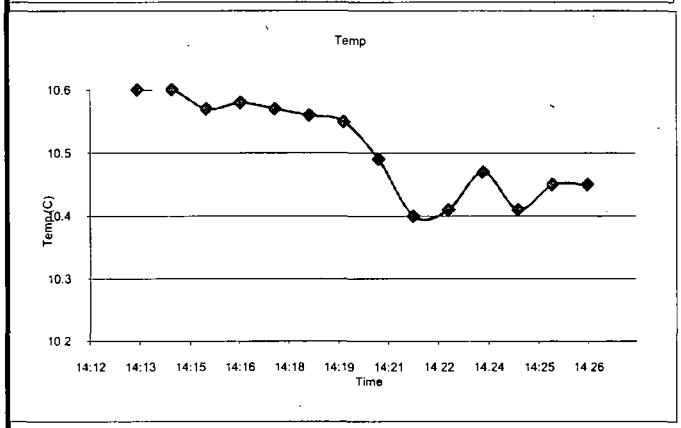

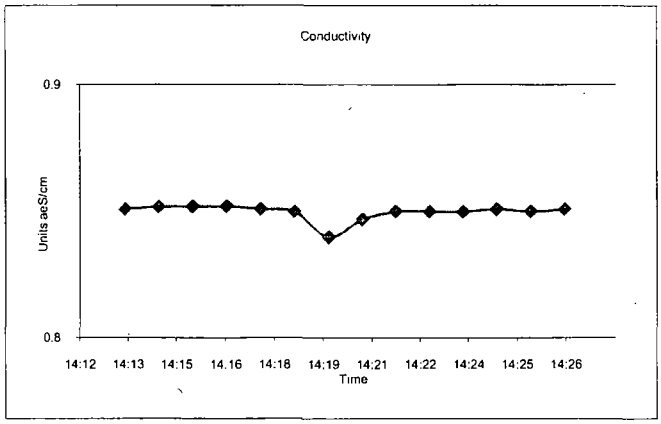

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	151	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 101B**
Casing Stickup (Ft.)	2.16	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	26-Nov-10
Total Well Depth (Ft.) TOC	153.74	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	40.48	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	113.26	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	æS/cm	FTU	mL/min	(Ft.) TOC	
							0	40.48	Static
13:35	7.18	0.44	10.52	-103	0.794		500		Start Time
13:36	7.2	0.43	10.54	-101	0.794		500		clear
13:37	7.21	0.53	10.55	-104	0.794		500		clear
13:38	7.21	0.61	10.54	-102	0.794		500		clear
13:39	7.21	0.71	10.56	-103	0.794		500	40.446	clear
13:40	7.2	0.76	10.55	-103	0.794		500		clear
13:41	7.21	0.84	10.57	-103	0.794		500		clear
13:42	7.21	0.91	10.56	-100	0.794		500		clear
13:43	7.21	0.98	10.56	-99	0.794		500		clear
13:44	7.21	1.06	10.61	-91	0.793		500	40.8	clear
13:45	7.21	1.1	10.59	-93	0.793		500		clear
13:46	7.21	1.15	10.6	-90	0.793		500		clear
13:47	7.21	1.2	10.59	-90	0.793	73.5	500		clear
MINUTES							**TOTAL LITERS**		
12.0	0.00	9.09%	0.00%	3.00	0.00%		**6.00**		

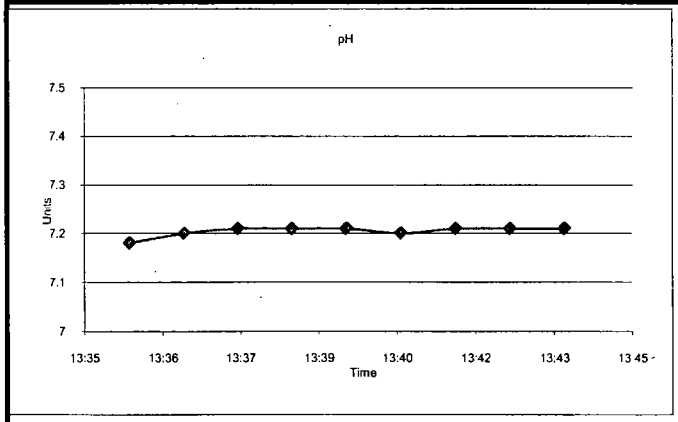

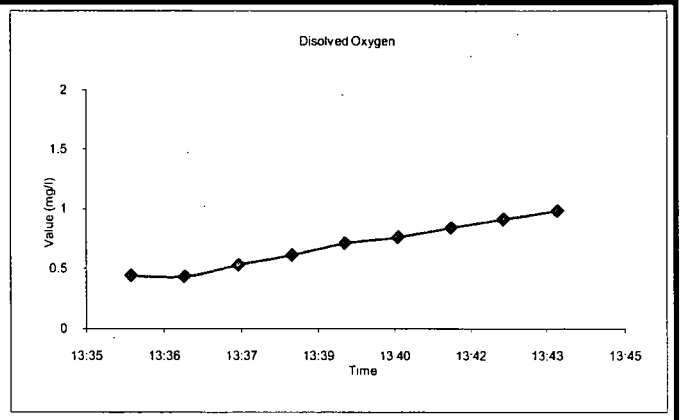

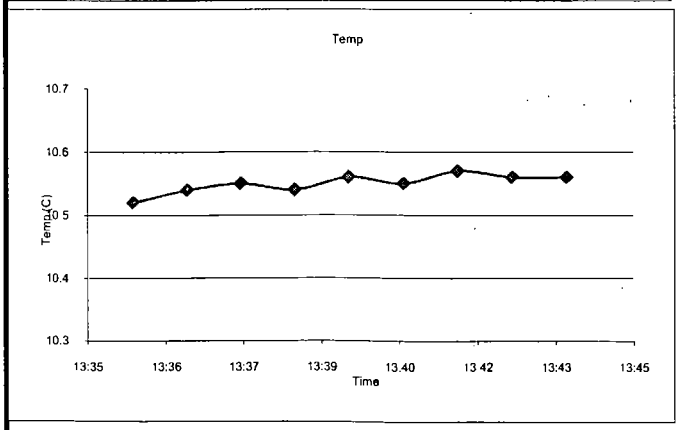

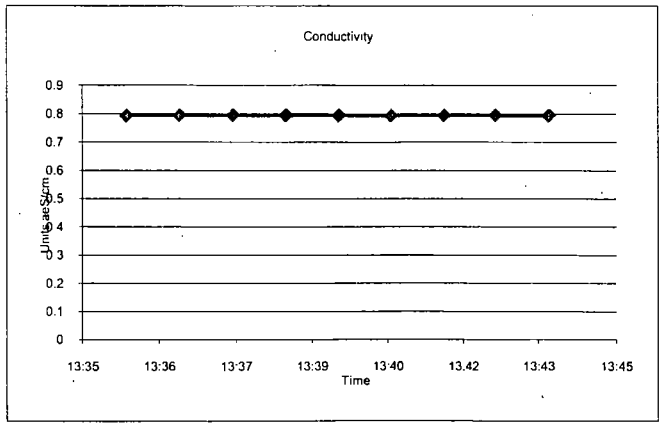

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	172	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 101C**
Casing Stickup (Ft.)	1.12	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	26-Nov-10
Total Well Depth (Ft.) TOC	174.89	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	40.2	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	134.69	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	æS/cm	FTU	mL/min	(Ft.) TOC	
							0	40.2	Static
13:02	7.29	2.52	10.74	-143	0.793		500		Start Time
13:03	7.3	2.5	10.77	-136	0.793		500		clear
13:04	8.03	2.49	10.75	-130	0.793		500		clear
13:05	7.85	2.47	10.72	-127	0.793		500		clear
13:06	7.64	2.5	10.72	-124	0.793		500		clear
13:07	8.46	2.52	10.7	-122	0.793		500	40.2	clear
13:08	9.93	2.49	10.71	-146	0.793		500		clear
13:09	8.6	2.47	10.71	-136	0.793		500		clear
13:10	8.05	2.53	10.68	-131	0.793		500		clear
13:11	7.78	2.53	10.7	-128	0.793		500		clear
13:12	7.61	2.53	10.71	-126	0.792		500		clear
13:13	7.52	2.57	10.71	-126	0.792		500	40.2	clear
13:14	7.46	2.56	10.68	-125	0.792	56	500		clear
MINUTES						**TOTAL LITERS**			
12.0	-0.15	1.19%	-0.28%	1.00	0.00%		**6.00**		

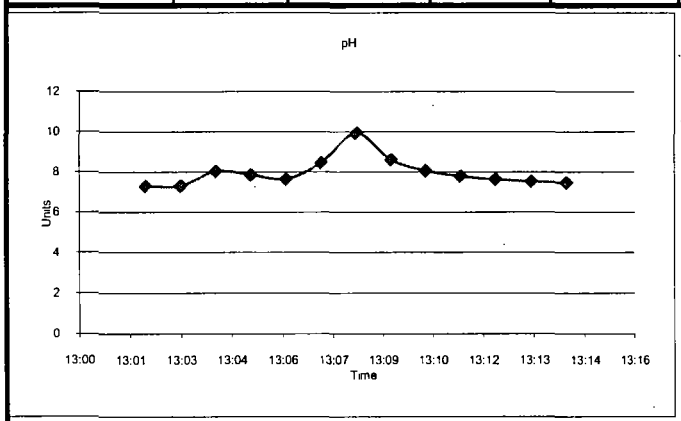

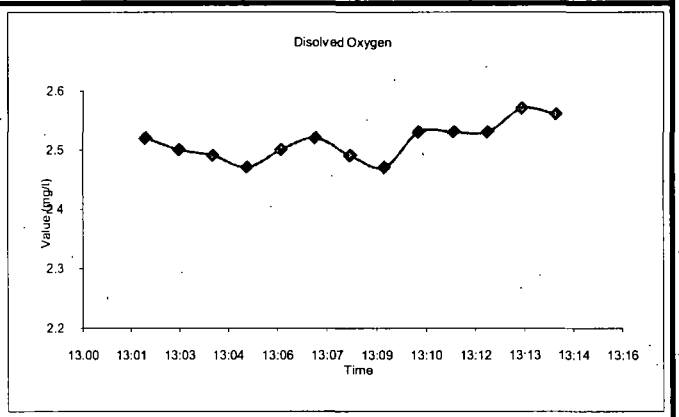

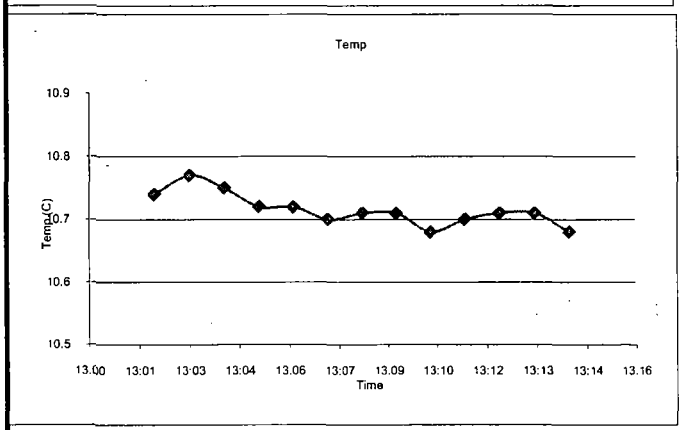

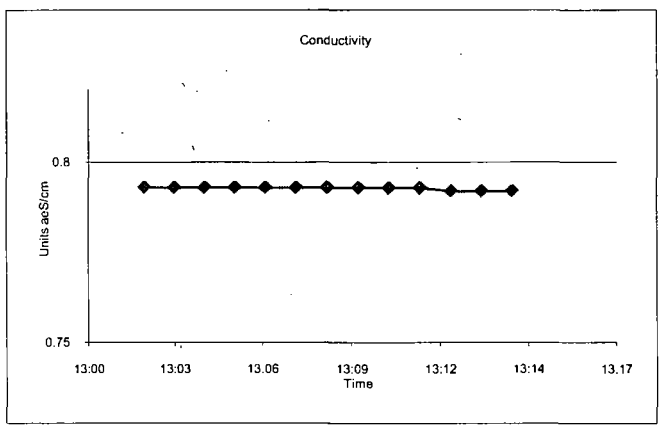

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	172	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 101D**
Casing Stickup (Ft.)	0.89	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	26-Nov-10
Total Well Depth (Ft.) TOC	212.72	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	42.5	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	170.22	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	æS/cm	FTU	mL/min	(Ft.) TOC	
							0	42.5	Static
14:38	6.92	1.32	10.75	-92	0.768		500		Start Time
14:39	6.87	0.89	10.85	-94	0.858		500		cloudy
14:40	6.81	0.62	10.85	-94	0.899		500		clear
14:41	6.81	0.44	10.85	-93	0.919		500	42.5	clear
14:42	6.8	0.42	10.82	-100	0.924		500		clear
14:43	6.8	0.59	10.83	-96	0.929		500		clear
14:44	6.8	1.17	10.76	-99	0.927		500		clear
14:45	6.8	1.83	10.78	-99	0.924		500		clear
14:46	6.8	2.49	10.79	-99	0.921		500		clear
14:47	6.8	3.01	10.82	-97	0.92		500		clear
14:48	6.8	3.18	10.83	-97	0.918		500	42.5	clear
14:49	6.8	3.2	10.85	-99	0.923		500		clear
14:50	6.8	3.19	10.83	-103	0.927	13	500		clear
MINUTES							**TOTAL LITERS**		
12.0	0.00	0.31%	0.00%	-6.00	0.98%		**6.00**		

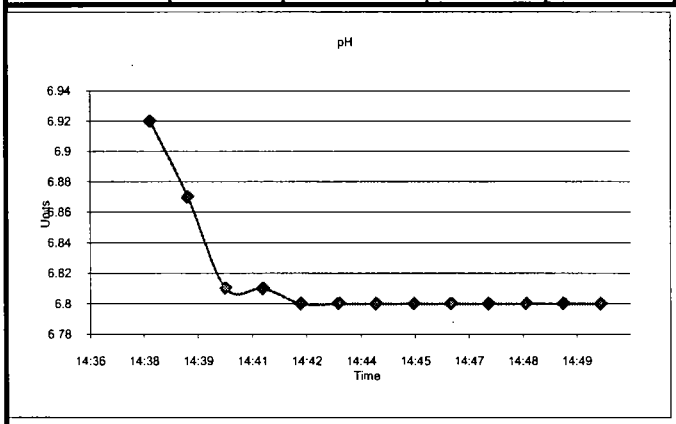

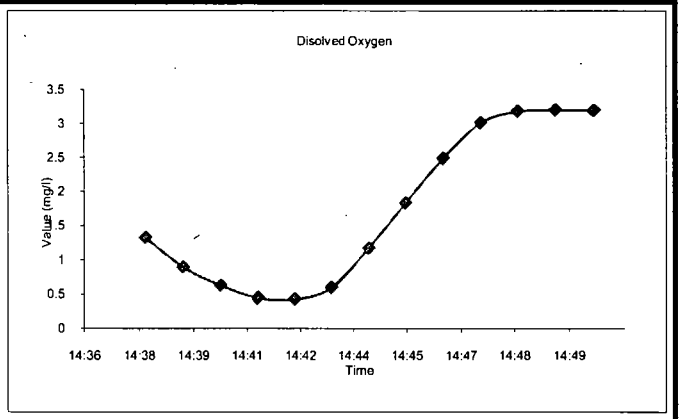

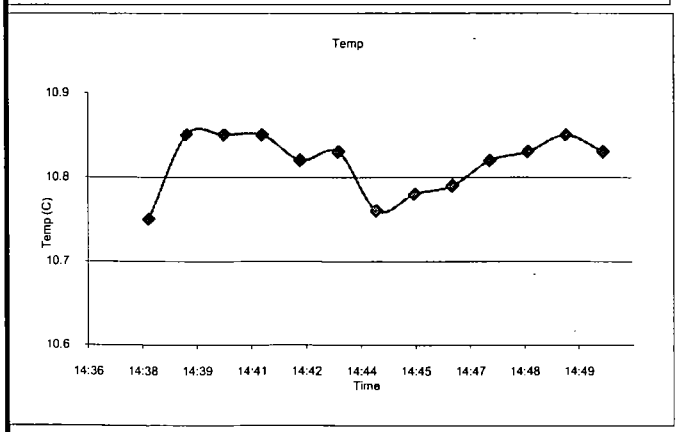

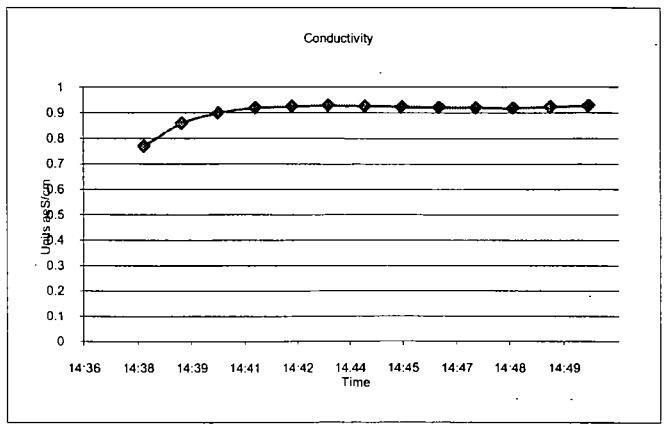

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	35	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 102A**
Casing Stickup (Ft.)	-0.47	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	26-Nov-10
Total Well Depth (Ft.) TOC	37.69	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	17.42	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	20.27	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time HHMMSS	pH Units	DO mg/l	Temp øC	ORP mV	SpCond æS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
							0	17.42	Static
10:53	9.86	6.09	13.24	-84	2.591		500		Start Time
10:54	9.87	5.88	13.24	-85	2.577		500		brown cloudy
10:55	9.92	5.53	13.27	-87	2.564		500		brown cloudy
10:56	10.2	5.35	13.28	-90	2.551		500		cloudy
10:57	10.21	5.17	13.28	-92	2.54		500	17.53	cloudy
10:58	10.27	4.78	13.25	-94	2.529		500		clear
10:59	10.34	4.58	13.26	-95	2.517		500		clear
11:00	10.39	4.57	13.25	-97	2.507		500		clear
11:01	10.45	4.48	13.23	-99	2.496		500		clear
11:02	10.53	4.41	13.22	-104	2.487		500	17.53	clear
11:03	10.61	4.27	13.23	-106	2.476		500		clear
11:04	10.68	4.15	13.23	-108	2.465		500		clear
11:05	10.65	3.99	13.25	-110	2.456	22	500		clear
MINUTES						**TOTAL LITERS**			
12.0	0.04	-6.56%	0.15%	-4.00	-0.81%		**6.00**		

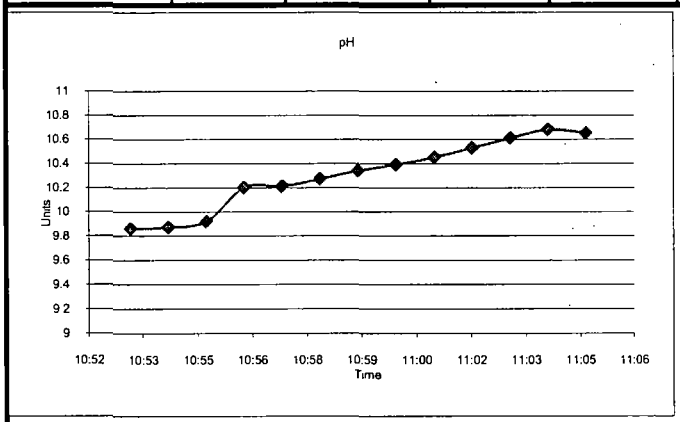

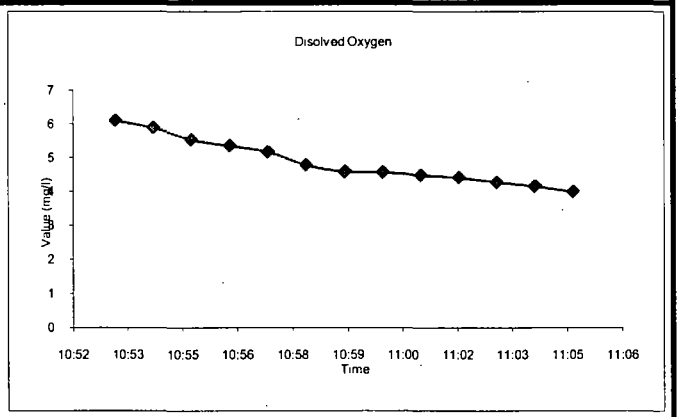

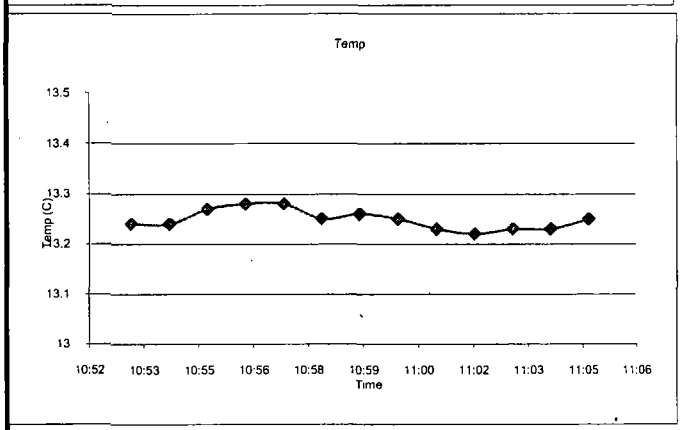

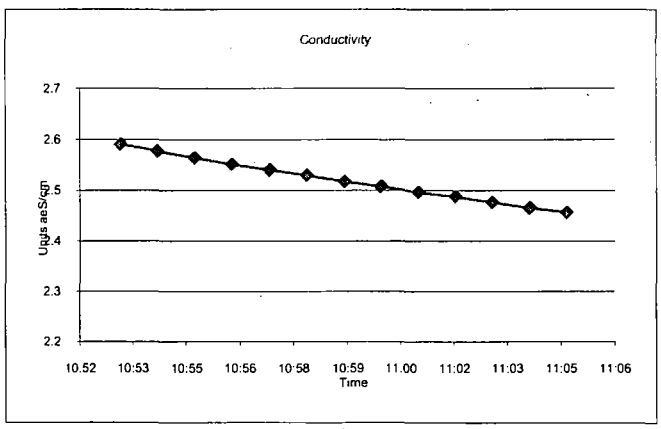

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	98	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 102B**
Casing Stickup (Ft.)	-0.68	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	26-Nov-10
Total Well Depth (Ft.) TOC	100.5	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	32.33	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	68.17	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	æS/cm	FTU	mL/min	(Ft.) TOC	
							0	32.33	Static
11:43	5.4	0.37	10.86	-99	0.75		410		Start Time
11:44	5.39	0.34	10.87	-102	0.751		410		redish brown color
11:45	5.38	0.32	10.86	-104	0.75		410		redish brown color
11:46	5.37	0.31	10.85	-105	0.75		410		cloudy
11:47	5.33	0.31	10.86	-107	0.749		410	32.31	cloudy
11:48	5.29	0.33	10.83	-108	0.748		410		clear
11:49	5.34	0.31	10.85	-110	0.747		410		clear
11:50	5.11	0.32	10.85	-108	0.747		410		sample collection
11:51	5.03	0.32	10.86	-109	0.746		410	32.31	
11:52	4.99	0.34	10.86	-110	0.745		410		
11:53	4.93	0.35	10.84	-111	0.744		410		
11:54	4.95	0.41	10.85	-111	0.744		410		
11:55	4.9	0.43	10.82	-116	0.744	23	410	32.31	
MINUTES						**TOTAL LITERS**			
12.0	-0.03	22.86%	-0.18%	-5.00	0.00%		**4.92**		

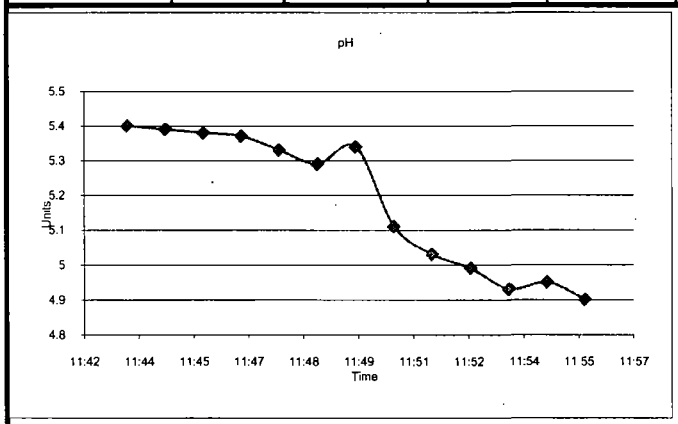

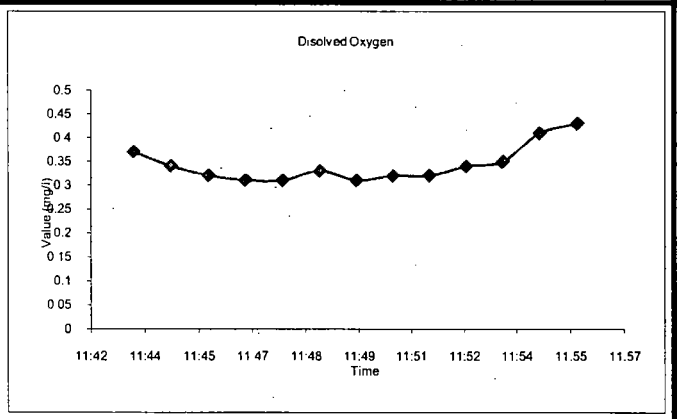

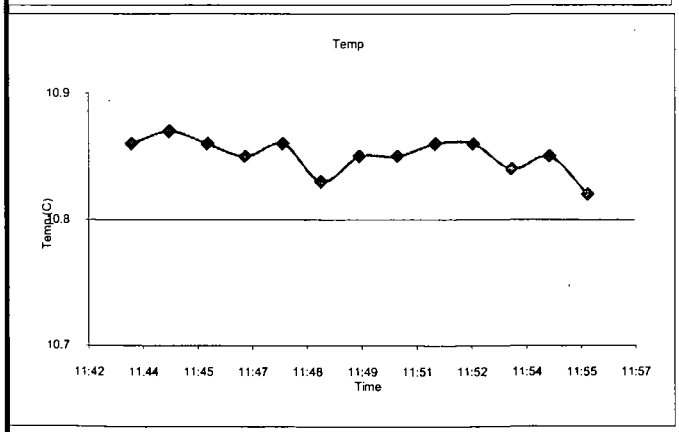

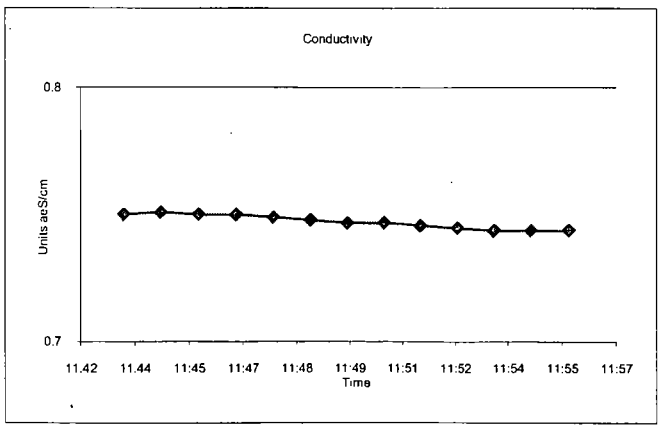

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	185	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 102C**
Casing Stickup (Ft.)	-0.43	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	26-Nov-10
Total Well Depth (Ft.) TOC	187.42	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	33.7	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	153.72	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time HHMMSS	pH Units	DO mg/l	Temp øC	ORP mV	SpCond æS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
							0	33.7	Static
12:21	7.02	0.41	10.2	-104	0.565		500		Start Time
12:22	9.07	0.36	10.44	-122	0.56		500		clear
12:23	9.39	0.36	10.26	-126	0.572		500		clear
12:24	9.41	0.3	10.07	-128	0.582		500		clear
12:25	9.37	0.3	10.34	-129	0.595		500	33.85	clear
12:26	9.4	0.34	10.34	-130	0.616		500		clear
12:27	9.38	0.34	10.39	-131	0.631		500		clear
12:28	9.33	0.33	10.33	-131	0.642		500		clear
12:29	9.33	0.33	10.23	-133	0.648		500	33.85	clear
12:30	9.38	0.36	10.3	-131	0.653		500		clear
12:31	9.35	0.39	10.33	-132	0.66	65	500		clear
MINUTES						**TOTAL LITERS**			
10.0	0.02	18.18%	0.98%	1.00	1.85%		**5.00**		

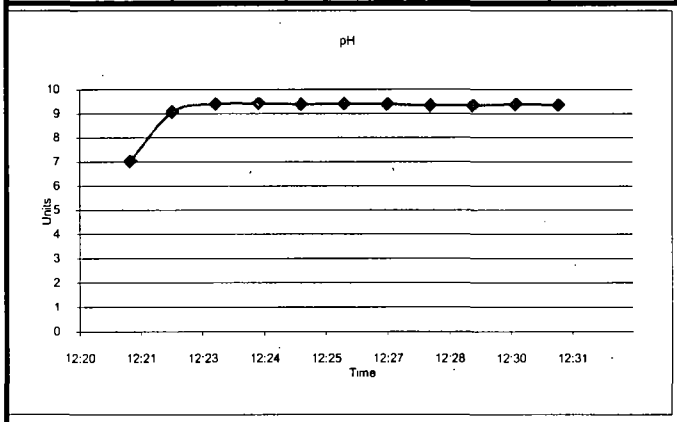

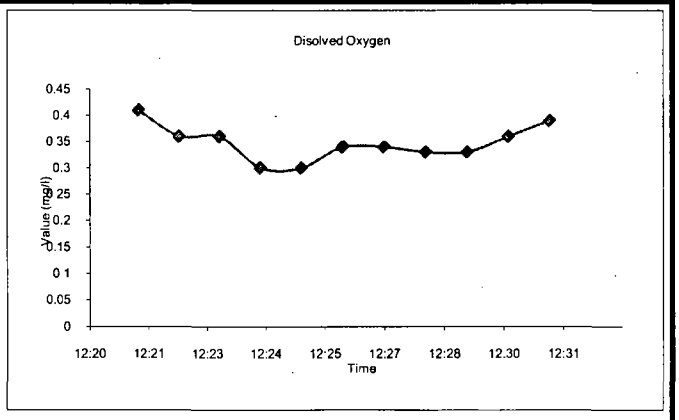

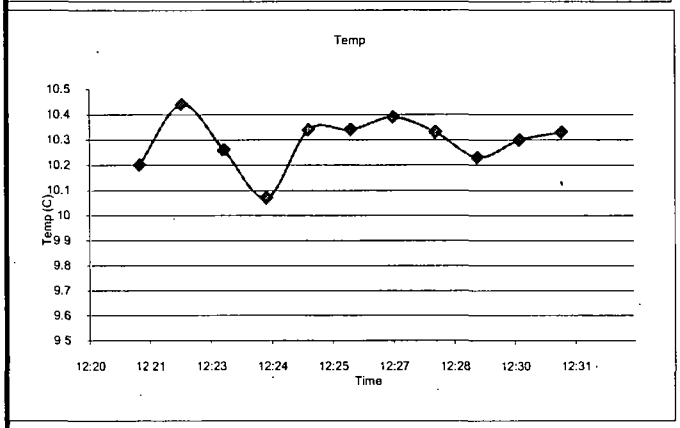

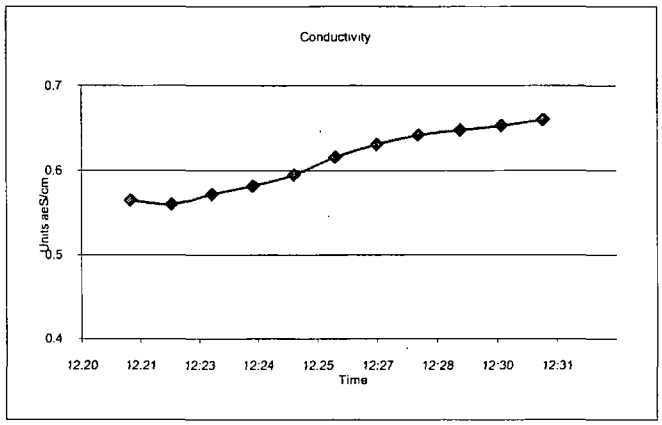

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	102	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 113A**
Casing Stickup (Ft.)	-1.06	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	28-Nov-10
Total Well Depth (Ft.) TOC	104.5	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	52.3	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	52.2	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	æS/cm	FTU	mL/min	(Ft.) TOC	
							0	52.3	Static
14:32	7.15	12.29	11.55	-6	1.24		500		Start Time
14:33	7.1	2.73	11.61	-10	1.24		500		brown & cloudy
14:34	7.1	2.42	11.62	-12	1.24		500	52.41	cloudy
14:35	7.09	2.42	11.62	-13	1.24		500		cloudy
14:36	7.09	2.41	11.63	-13	1.24		500		cloudy
14:37	7.09	2.42	11.64	-13	1.24		500		cloudy
14:38	7.09	2.41	11.64	-13	1.241		500	52.41	cloudy
14:39	7.09	2.42	11.64	-14	1.241		500		cloudy
14:40	7.09	2.43	11.64	-14	1.241		500		cloudy
14:41	7.09	2.43	11.63	-14	1.241		500		cloudy
14:42	7.1	2.45	11.64	-14	1.241		500		cloudy
14:43	7.09	2.41	11.62	-14	1.242		500	52.41	cloudy
14:44	7.1	2.43	11.62	-14	1.243		500		cloudy
14:45	7.08	2.41	11.61	-13	1.243	211	500		cloudy
MINUTES							**TOTAL LITERS**		
13.0	-0.01	0.00%	-0.09%	1.00	0.08%		**6.50**		

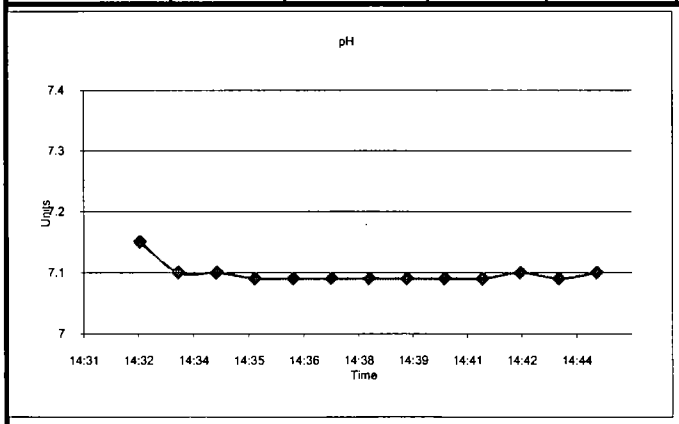

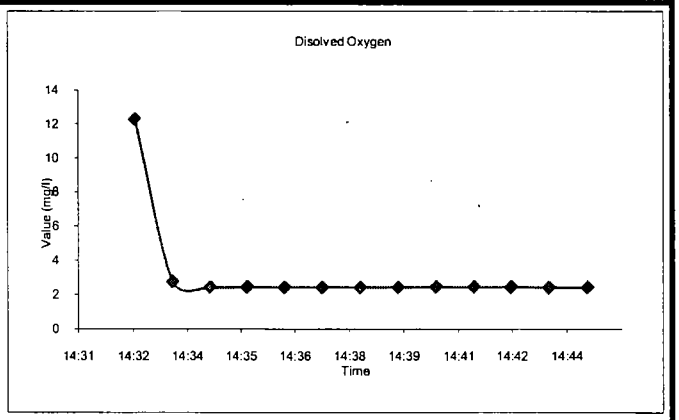

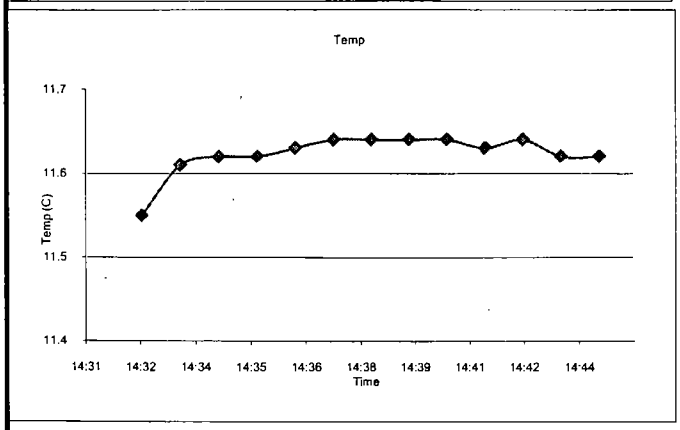

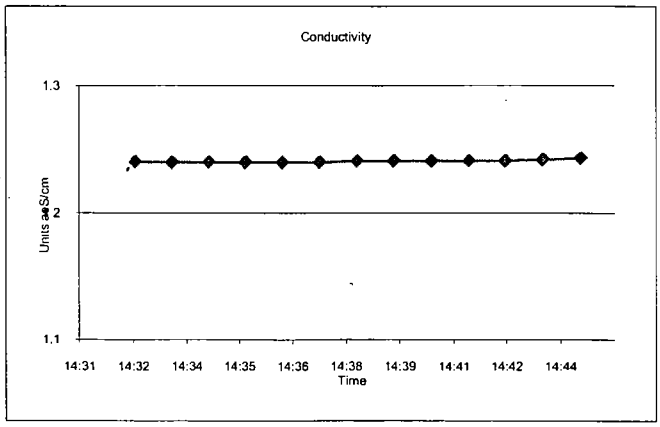

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	153	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 113B**
Casing Stickup (Ft.)	-0.43	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	28-Nov-10
Total Well Depth (Ft.) TOC	155.26	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	53.12	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	102.14	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time HHMMSS	pH Units	DO mg/l	Temp øC	ORP mV	SpCond æS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
							0	53.12	Static
13:46	7.22	0.33	11.57	-102	0.888		500		Start Time
13:47	7.21	0.23	11.56	-106	0.9		500		cloudy white
13:48	7.21	0.28	11.56	-108	0.91		500	53.27	cloudy
13:49	7.21	0.3	11.56	-108	0.915		500		cloudy
13:50	7.21	0.26	11.56	-110	0.918		500		cloudy
13:51	7.21	0.24	11.56	-110	0.919		500		cloudy
13:52	7.21	0.26	11.56	-111	0.919		500	53.28	cloudy
13:53	7.21	0.27	11.56	-111	0.919		500		cloudy
13:54	7.22	0.27	11.56	-111	0.918		500		slightly cloudy
13:55	7.22	0.29	11.58	-111	0.917		500		slightly cloudy
13:56	7.22	0.26	11.57	-110	0.916		500		slightly cloudy
13:57	7.22	0.27	11.56	-110	0.916		500		slightly cloudy
13:58	7.22	0.31	11.56	-110	0.915	42	500	53.28	slightly cloudy
MINUTES						**TOTAL LITERS**			
12.0	0.00	19.23%	-0.09%	0.00	-0.11%		**6.00**		

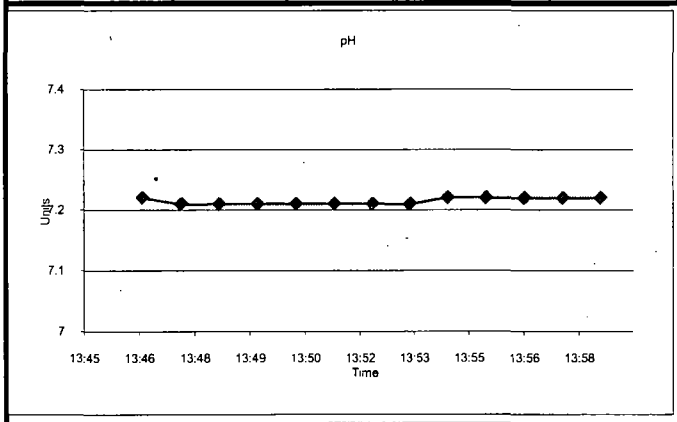

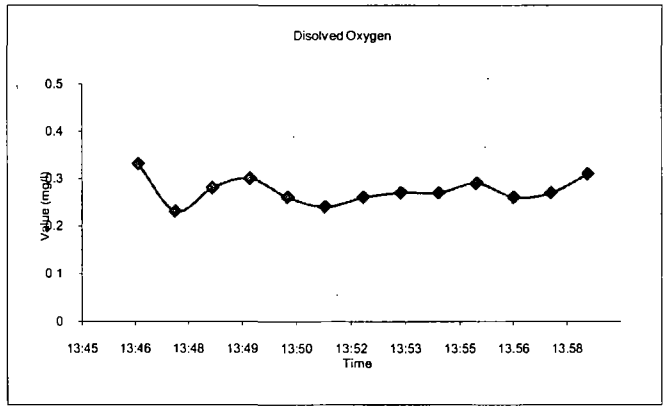

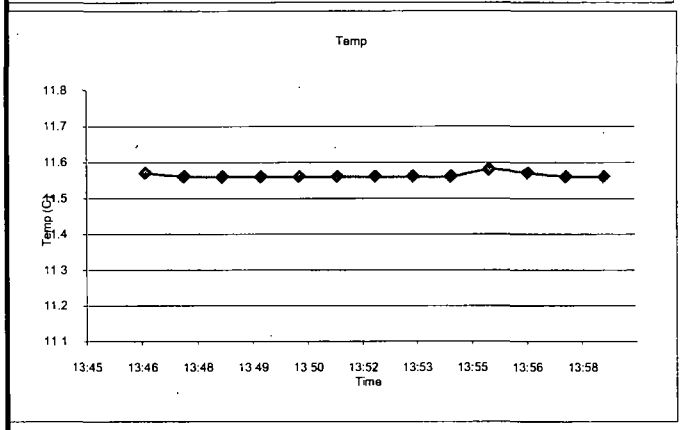

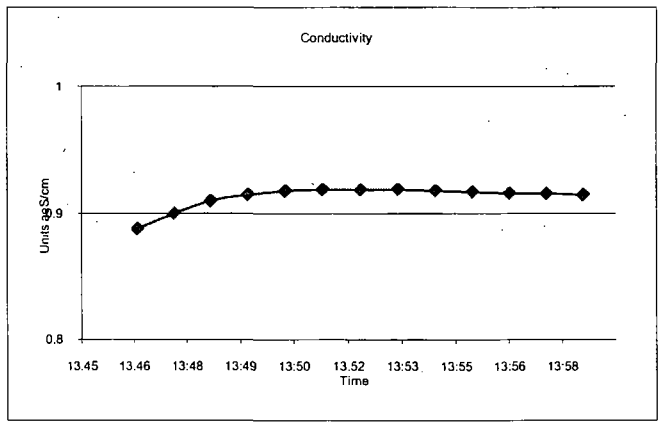

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	95	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 114A**
Casing Stickup (Ft.)	2.45	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	27-Nov-10
Total Well Depth (Ft.) TOC	97.48	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	26.775	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	70.705	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	PSIG	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	æS/cm		mL/min	(Ft.) TOC	
						0	0	26.775	Static
15:44	7.34	8.59	12.33	-29	1.644	46	340		Start Time
15:45	7.34	8.49	12.33	-28	1.642	46	340		clear
15:46	7.34	8.47	12.29	-28	1.64	46	340	26.5	clear
15:47	7.33	8.22	12.27	-27	1.636	46	340	26.5	clear
15:48	7.32	8.24	12.21	-27	1.633	46	340		clear
15:49	7.32	8.12	12.18	-28	1.625	46	340		sample collection
15:50	7.31	8.03	12.21	-28	1.618				
15:52	7.32	8.03	12.19	-27	1.591				
15:53	7.31	8.22	12.15	-29	1.588				
15:54	7.29	7.99	12.21	-32	1.583				
15:55	7.27	7.82	12.22	-34	1.577				
15:56	7.27	7.68	12.25	-35	1.568				
15:57	7.27	7.72	12.24	-35	1.56				
MINUTES						**TOTAL LITERS**			
5.0	-0.01	-1.22%	-0.73%	-1.00	-0.67%		**1.70**		

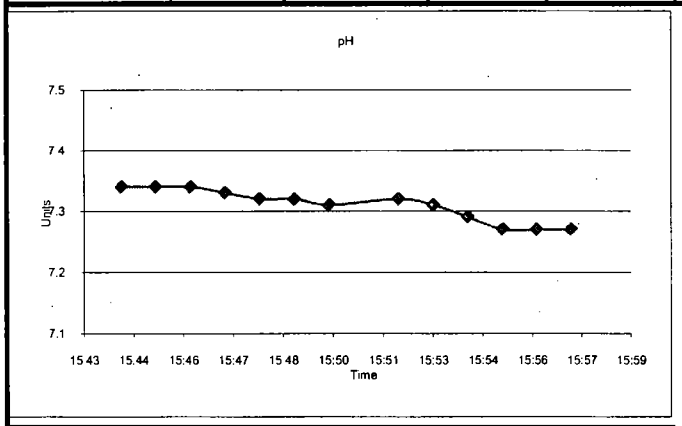

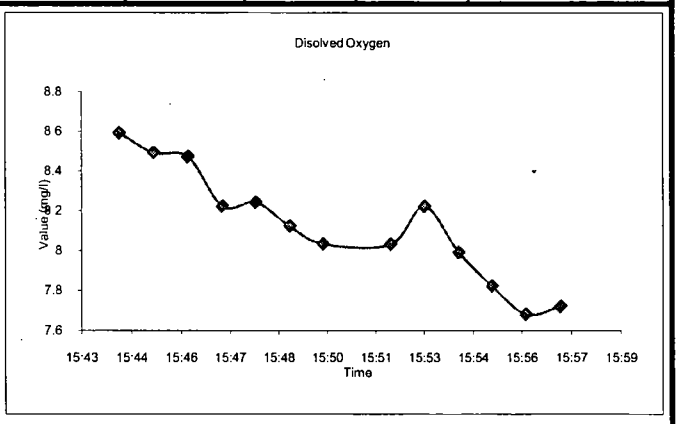

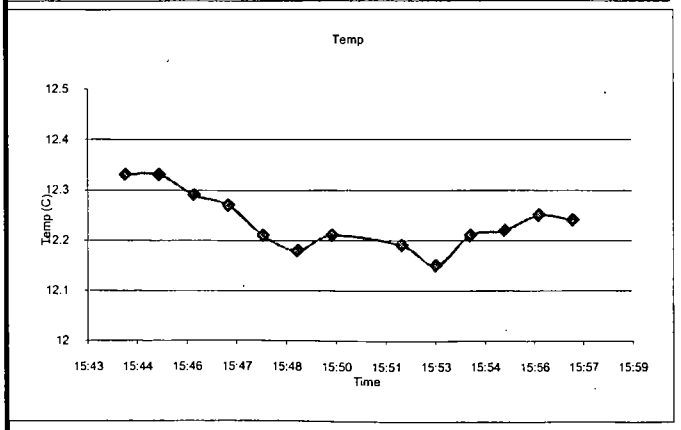

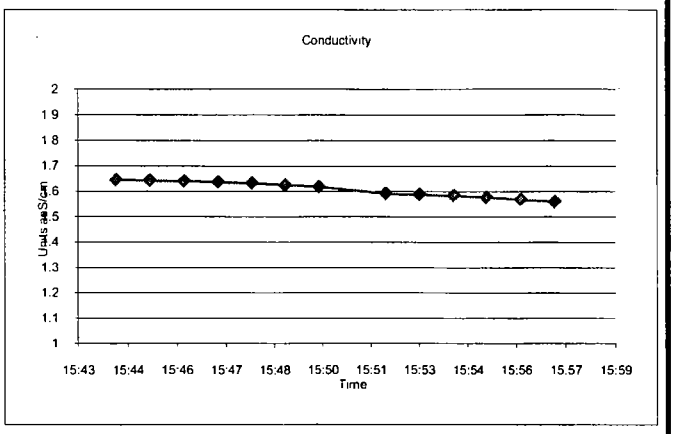

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	220	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 114B**
Casing Stickup (Ft.)	2.35	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	27-Nov-10
Total Well Depth (Ft.) TOC	222.58	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	28.63	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	193.95	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time HHMMSS	pH Units	DO mg/l	Temp øC	ORP mV	SpCond æS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
							0	28.63	Static
15:13	8.51	0.24	12.37	-167	0.96		500		Start Time
15:14	8.42	0.27	12.48	-169	0.957		500		clear
15:15	8.32	0.23	12.39	-169	0.963		500	28.68	clear
15:16	8.28	0.24	12.45	-171	0.966		500		clear
15:17	8.16	0.21	12.51	-170	0.972	--	500		clear
15:18	8.05	0.23	12.46	-170	0.981		500		clear
15:19	7.96	0.24	12.39	-169	0.99		500	28.71	clear
15:20	7.89	0.21	12.38	-168	0.995		500		clear
15:21	7.83	0.22	12.36	-167	0.999		500		clear
15:22	7.79	0.21	12.36	-165	1.004		500	28.7	clear
15:23	7.74	0.21	12.34	-164	1.008		500		clear
15:24	7.79	0.21	12.32	-161	1.003	6	500		clear
MINUTES							**TOTAL LITERS**		
11.0	0.00	0.00%	-0.32%	4.00	-0.10%		**5.50**		

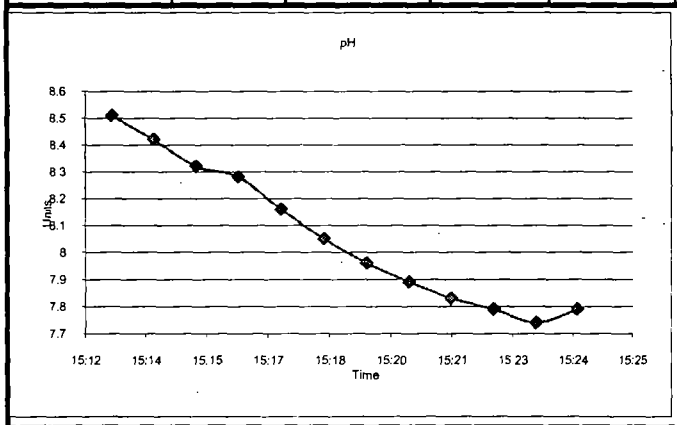

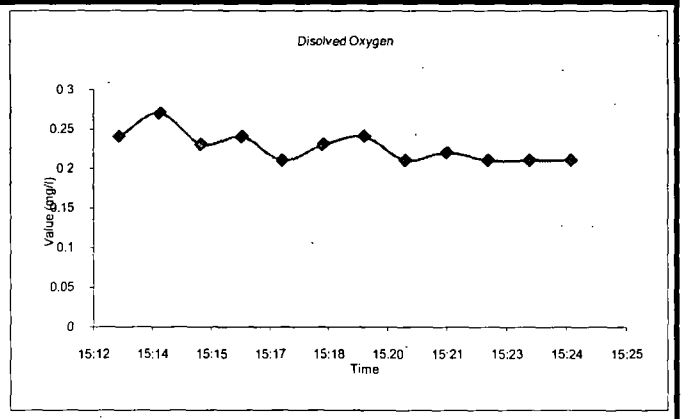

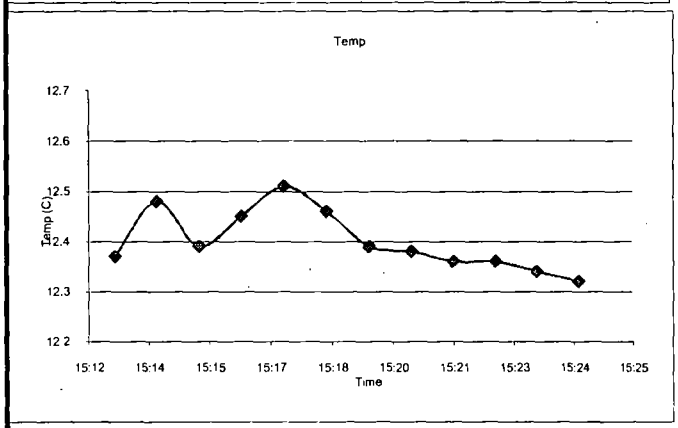

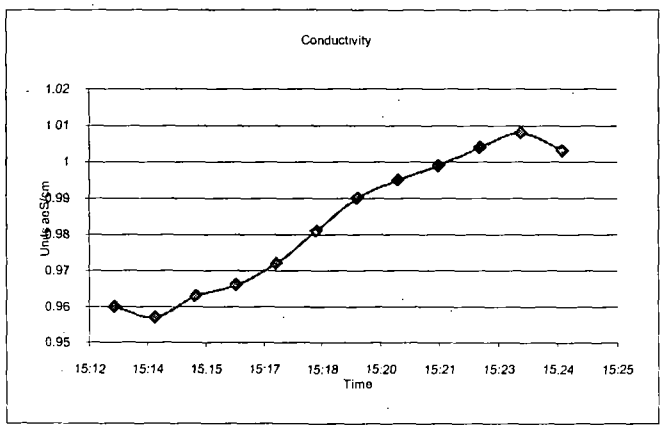

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	87	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 117B**
Casing Stickup (Ft.)	-0.45	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	24-Nov-10
Total Well Depth (Ft.) TOC	89.5	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	4.18	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	85.32	**Field Analysis Equip**	YSI 556 MPS	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time HHMMSS	pH Units	DO mg/l	Temp øC	ORP mV	SpCond æS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
							0	4.18	Static
11:10	7.14	0.64	12.58	5	0.935		500		Start Time
11:11	7.14	0.83	12.55	5	0.936		500		clear
11:12	7.15	0.58	12.56	5	0.936		500	4.2	clear
11:13	7.15	0.59	12.51	6	0.936		500		clear
11:14	7.15	0.6	12.5	6	0.936		500		clear
11:15	7.15	0.6	12.52	7	0.936		500		clear
11:16	7.14	0.6	12.53	7	0.936		500		clear
11:17	7.15	0.61	12.53	7	0.936		500		clear
11:18	7.14	0.59	12.54	8	0.935		500		clear
11:19	7.14	0.61	12.55	8	0.935		500	4.19	clear
11:20	7.15	0.61	12.53	8	0.936		500		clear
11:21	7.16	0.59	12.53	8	0.936		500		clear
11:22	7.15	0.59	12.55	9	0.936		500		clear
11:23	7.15	0.57	12.55	9	0.935	8	500	4.19	sample collection
MINUTES						**TOTAL LITERS**			
13.0	-0.01	-3.39%	0.16%	1.00	-0.11%		**6.50**		

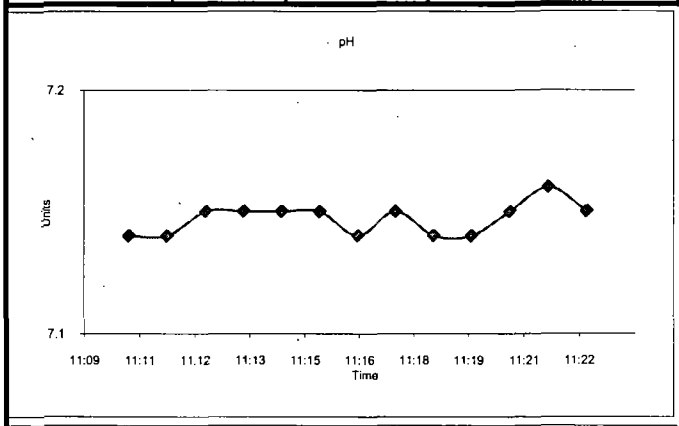

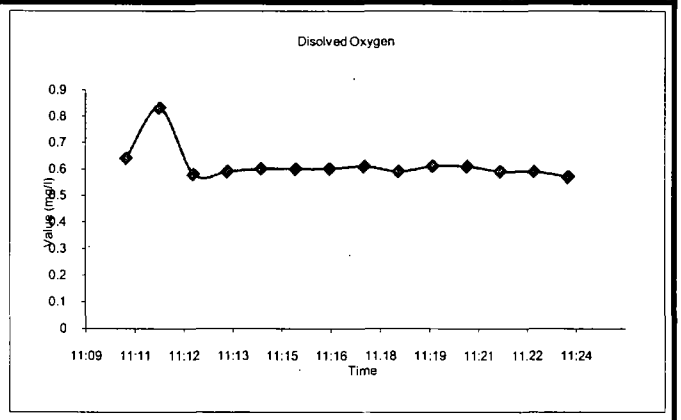

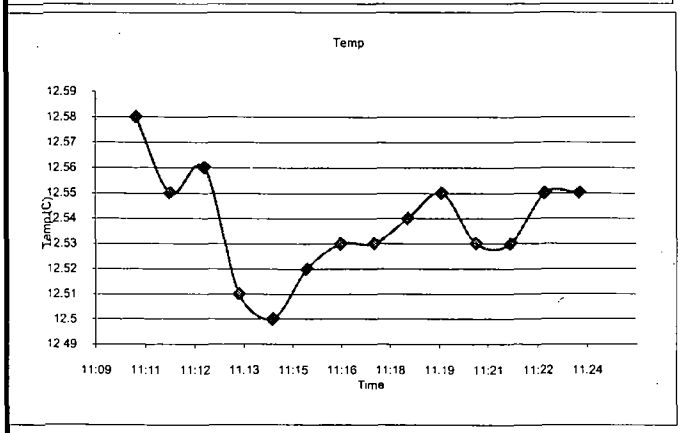

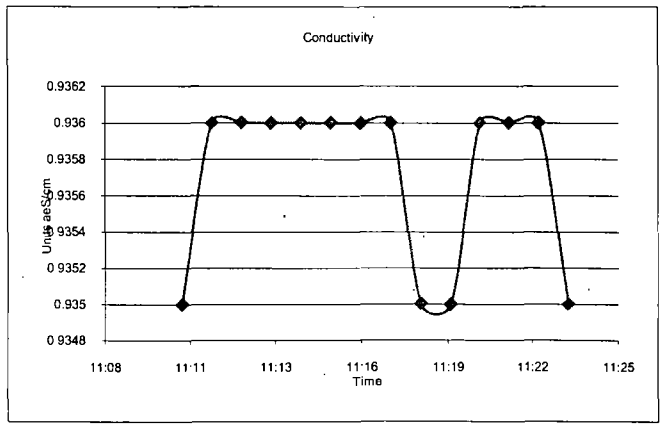

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	156	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 117C**
Casing Stickup (Ft.)	-0.63	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	24-Nov-10
Total Well Depth (Ft.) TOC	158.31	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	2.81	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	155.5	**Field Analysis Equip**	YSI556 MPS	**Sampling Period**	Fall2010		

FIELD PURGE MONITORING

Time HHMMSS	pH Units	DO mg/l	Temp øC	ORP mV	SpCond æS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
							0	2.81	Static
11:54	7.03	0.37	12.74	29	0.91		500		Start Time
11:55	7.04	0.39	12.77	29	0.91		500		clear
11:56	7.04	0.41	12.72	29	0.911		500	2.81	clear
11:57	7.04	0.43	12.72	29	0.912		500		clear
11:58	7.04	0.38	12.73	29	0.912		500		clear
11:59	7.04	0.41	12.73	28	0.913		500		clear
12:00	7.04	0.4	12.71	28	0.912		500	2.81	clear
12:01	7.05	0.39	12.69	28	0.912		500		clear
12:02	7.05	0.41	12.7	28	0.913		500		clear
12:03	7.05	0.43	12.73	28	0.913		500		clear
12:04	7.04	0.43	12.75	28	0.913		500		clear
12:05	7.04	0.42	12.73	28	0.913		500		clear
12:06	7.04	0.41	12.7	27	0.913	12	500	2.81	clear
MINUTES						**TOTAL LITERS**			
12.0	0.00	-4.65%	-0.39%	-1.00	0.00%		**6.00**		

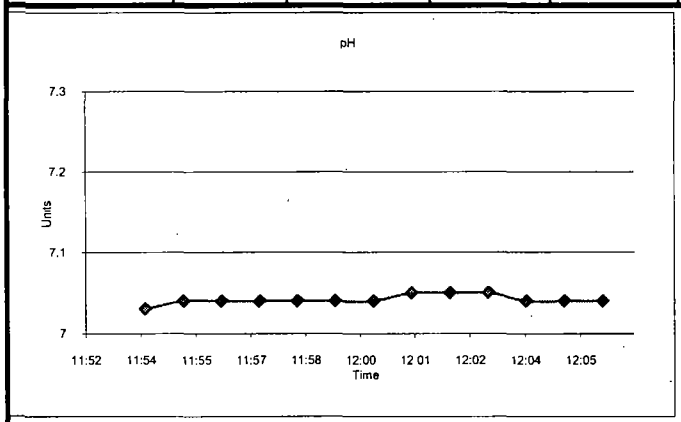

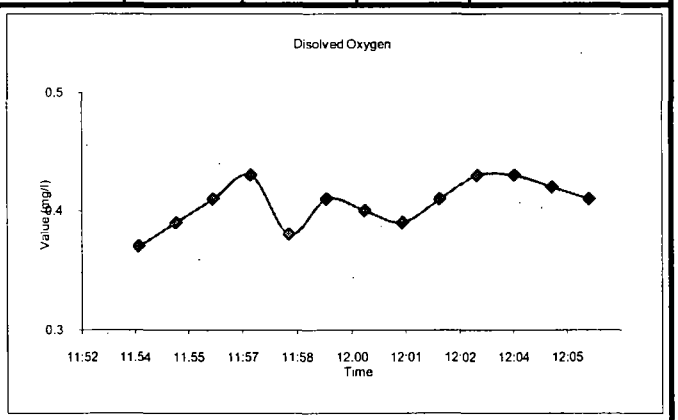

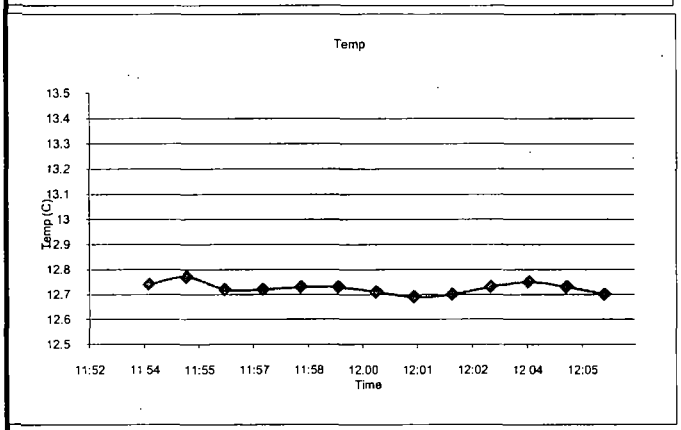

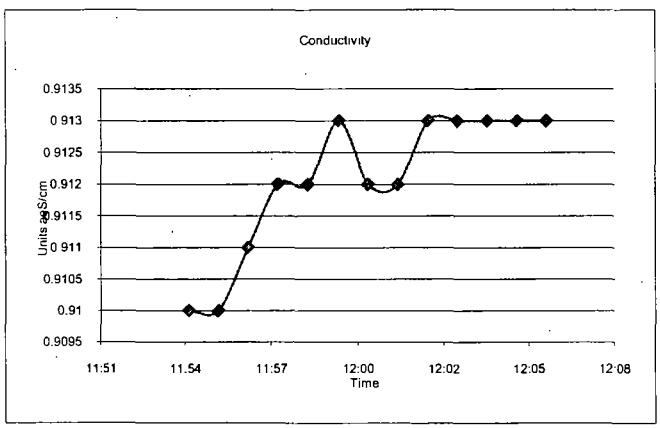

Remarks: (well condition, maintenance, etc...)

1 bolt hole stripped

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	198	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 117D**
Casing Stickup (Ft.)	-0.3	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	11/24/100
Total Well Depth (Ft.) TOC	200.2	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	2.51	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	197.69	**Field Analysis Equip**	YSI556 MPS	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	æS/cm	FTU	mL/min	(Ft.) TOC	
							0	2.51	Static
12:41	7.03	0.25	12.77	36	0.979		500		Start Time
12:42	7.03	0.24	12.76	35	0.979		500		clear
12:43	7.04	0.24	12.76	35	0.979		500	2.52	clear
12:44	7.04	0.24	12.76	35	0.978		500		clear
12:45	7.04	0.24	12.75	34	0.979		500		clear
12:46	7.04	0.23	12.75	34	0.979		500		clear
12:47	7.04	0.23	12.76	34	0.978		500		clear
12:48	7.04	0.24	12.76	33	0.978		500		clear
12:49	6.94	0.21	12.75	34	0.979		500		clear
12:50	7.02	0.22	12.75	34	0.979		500	2.52	clear
12:51	7.04	0.24	12.74	34	0.978		500		clear
12:52	7.04	0.23	12.75	33	0.979		500		clear
12:53	7.01	0.23	12.74	33	0.979	7	500		clear
MINUTES							**TOTAL LITERS**		
12.0	-0.03	-4.17%	0.00%	-1.00	0.10%		**6.00**		

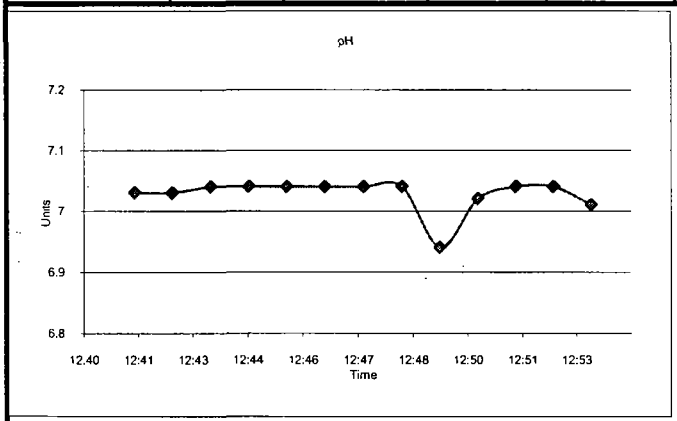

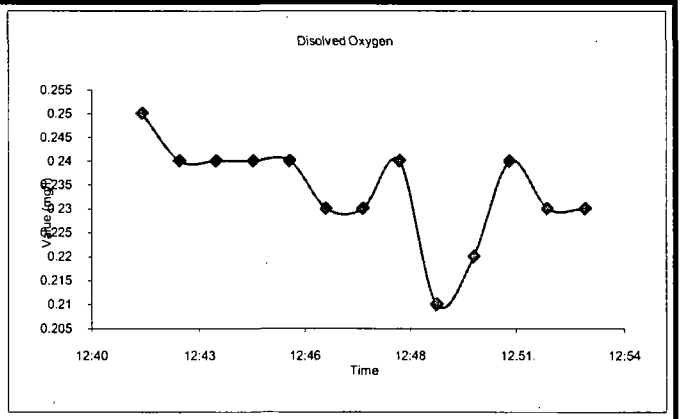

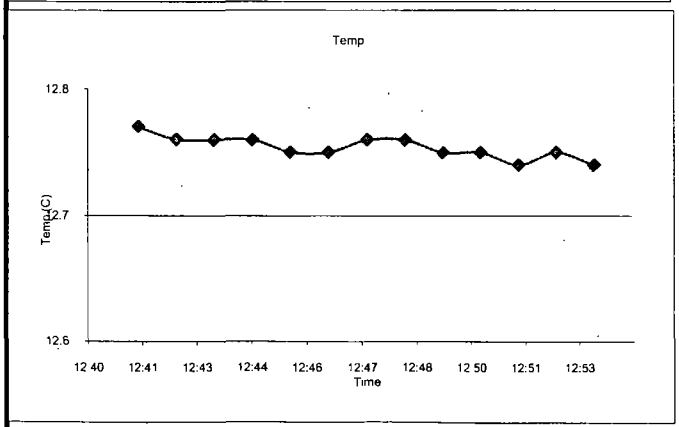

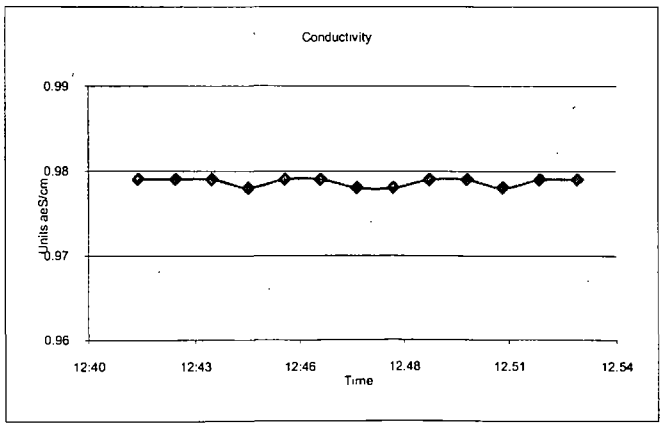

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	60	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 119**
Casing Stickup (Ft.)	3.25	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	27-Nov-10
Total Well Depth (Ft.) TOC	62.41	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	25.59	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	36.82	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time HHMMSS	pH Units	DO mg/l	Temp øC	ORP mV	SpCond æS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
							0	25.59	Static
10:38	7.9	33.6	12.21	95	1.015		480		Start Time
10:40	7.12	5.28	11.89	82	1.277		480		clear
10:41	7.12	5.05	11.9	82	1.277		480	25.52	clear
10:42	7.11	4.9	11.82	82	1.276		480		clear
10:43	7.11	5.14	11.9	83	1.276		480		clear
10:44	7.11	5.26	11.91	82	1.277		480		clear
10:45	7.1	5.32	11.87	83	1.278		480		clear
10:46	7.11	5.02	11.89	82	1.277		480		clear
10:47	7.12	5.25	11.91	82	1.277		480	25.52	clear
10:48	7.12	5	11.91	82	1.276		480		clear
10:49	7.11	4.96	11.82	82	1.277		480		clear
10:50	7.11	5.13	11.9	82	1.277	49	480		clear
MINUTES							**TOTAL LITERS**		
11.6	-0.01	2.60%	-0.08%	0.00	0.08%		**5.59**		

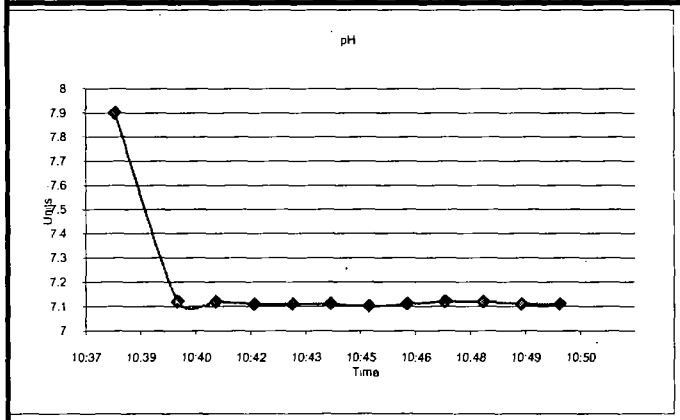

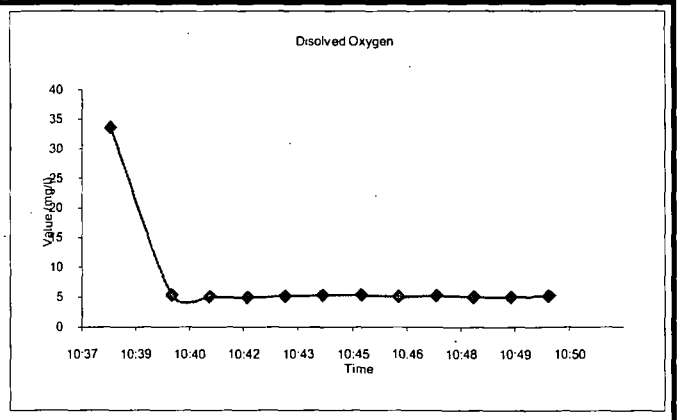

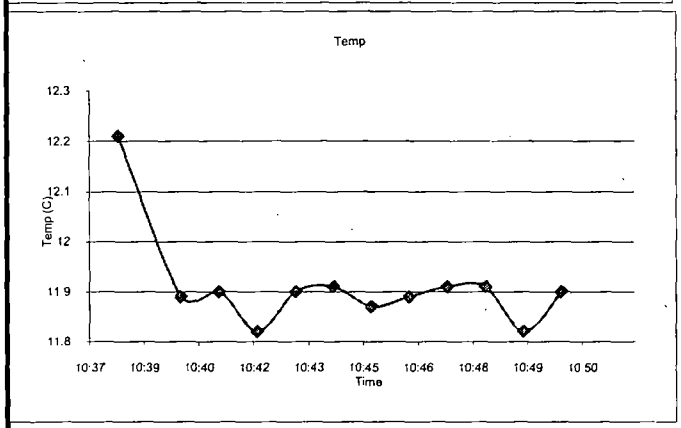

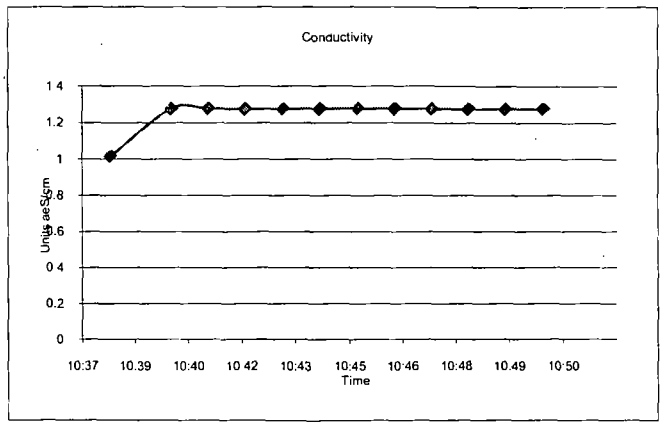

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	65	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 121**
Casing Stickup (Ft.)	2.53	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	25-Nov-10
Total Well Depth (Ft.) TOC	67.55	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	21.81	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	45.74	**Field Analysis Equip**	YSI556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	æS/cm	FTU	mL/min	(Ft.) TOC	
							0	21.81	Static
9:52	7.24	3.63	12.73	2	1.092		500		Start Time
9:53	7.24	3.7	12.67	2	1.093		500		redish brown
9:54	7.25	3.69	12.72	3	1.092		500	21.8	redish brown
9:55	7.25	3.67	12.69	3	1.092	-	500		clear - slightly brown
9:56	7.25	3.64	12.66	3	1.093		500		clear - slightly brown
9:57	7.25	3.62	12.65	4	1.093		500		clear
9:58	7.31	3.69	12.65	3	1.094		500		clear
9:59	7.27	3.64	12.65	3	1.093		500		clear
10:00	7.27	3.65	12.63	4	1.094		500		clear
10:01	7.27	3.71	12.63	4	1.093		500		clear
10:02	7.27	3.63	12.68	5	1.092		500		clear
10:03	7.27	3.65	12.63	5	1.094		500		clear
10:04	7.27	3.64	12.68	5	1.093		500	21.8	clear
10:05	7.28	3.69	12.68	5	1.093	15	500		clear
MINUTES							**TOTAL LITERS**		
13.0	0.01	1.10%	0.40%	0.00	-0.09%		**6.50**		

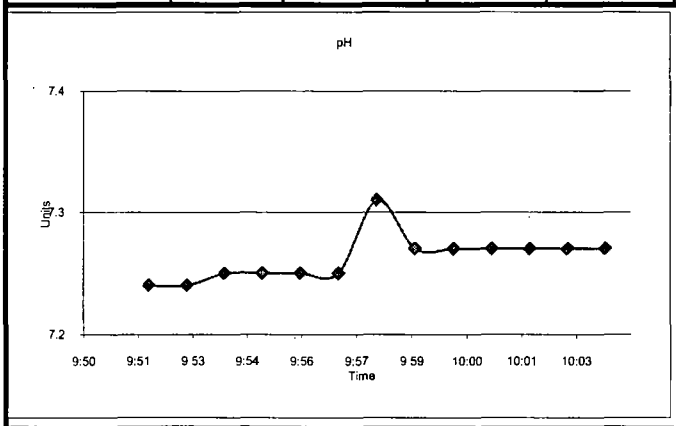

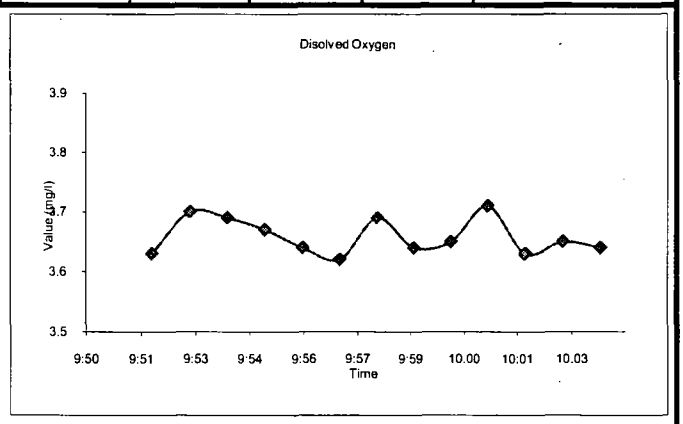

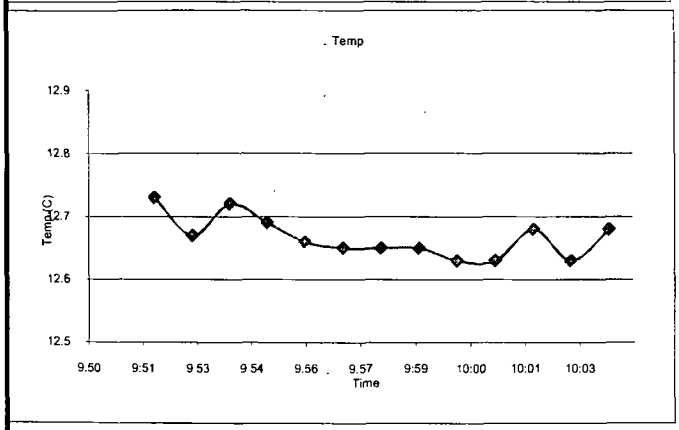

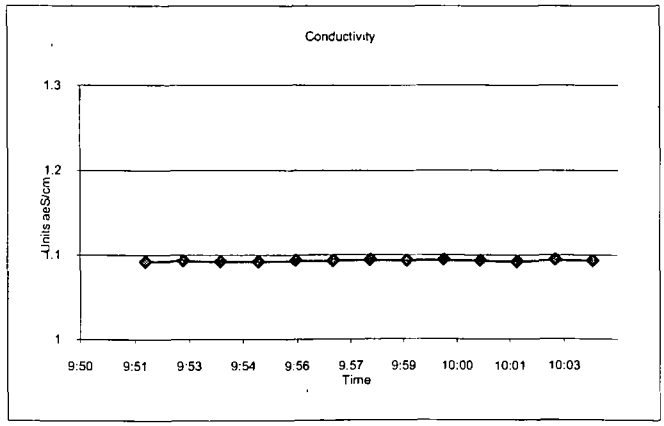

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	100	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 124**
Casing Stickup (Ft.)	2.17	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	27-Nov-10
Total Well Depth (Ft.) TOC	102.76	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	34.22	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	68.54	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	æS/cm	FTU	mL/min	(Ft.) TOC	
							0	34.22	Static
11:22	7.23	0.49	12.41	-104	1.229		390		Start Time
11:23	7.21	0.49	12.51	-100	1.23		390		yellow cloudy
11:24	7.19	0.49	12.53	-95	1.235		390	34.25	yellow cloudy
11:25	7.15	0.49	12.48	-91	1.243		390		cloudy
11:26	7.13	0.51	12.48	-88	1.248		390		cloudy
11:27	7.14	0.52	12.42	-86	1.256		390		cloudy
11:28	7.11	0.5	12.45	-84	1.258		390	34.28	cloudy
11:29	7.11	0.51	12.38	-82	1.268		390		cloudy
11:30	7.11	0.53	12.46	-81	1.268		390		cloudy
11:31	7.11	0.52	12.47	-79	1.273		390		clear
11:32	6.98	0.52	12.49	-68	1.277		390		clear
11:33	6.99	0.52	12.4	-68	1.287		390	34.28	clear
11:34	6.99	0.52	12.5	-73	1.291	71	390		clear
MINUTES						**TOTAL LITERS**			
12.0	0.01	0.00%	0.08%	-5.00	1.10%		**4.68**		

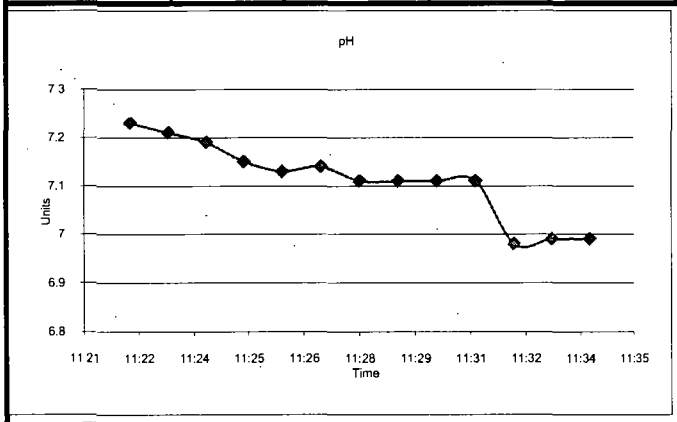

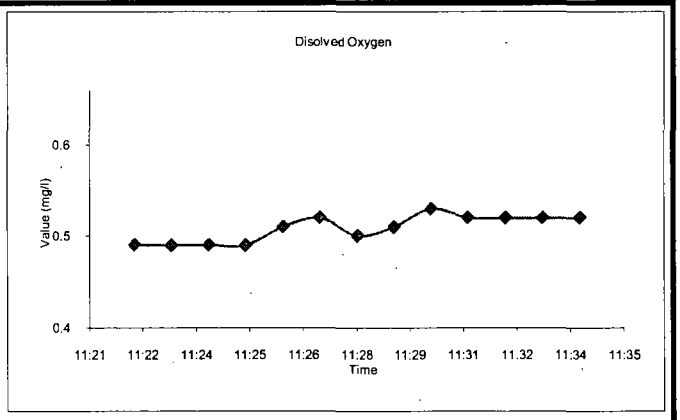

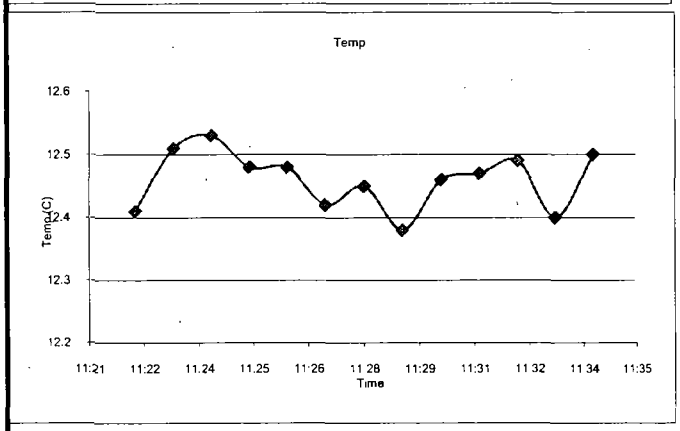

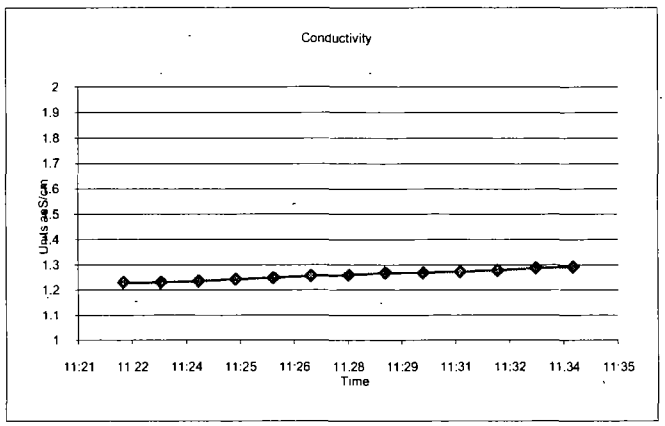

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	36	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 130**
Casing Stickup (Ft.)	-0.3	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	27-Nov-10
Total Well Depth (Ft.) TOC	38.17	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	21.58	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	16.59	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	æS/cm	FTU	mL/min	(Ft.) TOC	
							0	21.58	Static
16:20	6.75	2.24	12.35	-41	1.395		460		Start Time
16:21	6.78	2.73	12.39	-38	1.392		460		brown cloudy
16:22	6.78	2.98	12.42	-37	1.392		460	21.63	slightly brown
16:23	6.8	3.13	12.42	-36	1.392		460		clear
16:24	6.81	3.2	12.41	-35	1.392		460		clear
16:25	6.82	3.37	12.4	-34	1.392		460		clear
16:26	6.83	3.59	12.41	-33	1.392		460	21.63	clear
16:27	6.84	3.67	12.43	-32	1.392		460		clear
16:28	6.84	3.58	12.39	-31	1.394		460		clear
16:29	6.85	3.69	12.41	-31	1.393		460	21.63	clear
16:30	6.86	3.59	12.43	-30	1.392	14	460		clear
MINUTES						**TOTAL LITERS**			
10.0	0.02	0.28%	0.32%	1.00	-0.14%		**4.60**		

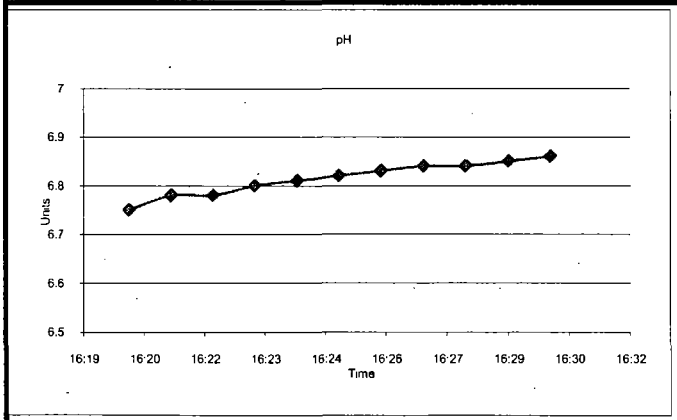

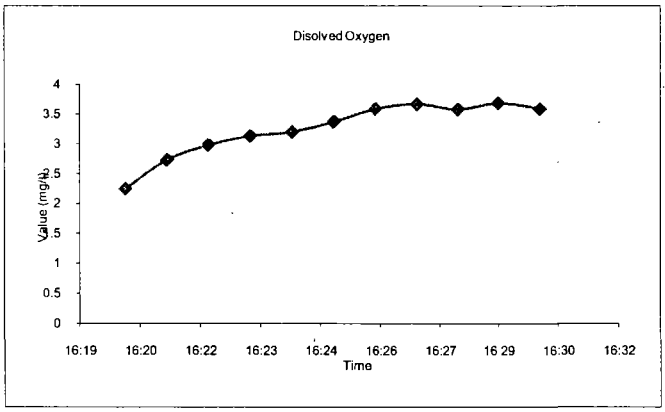

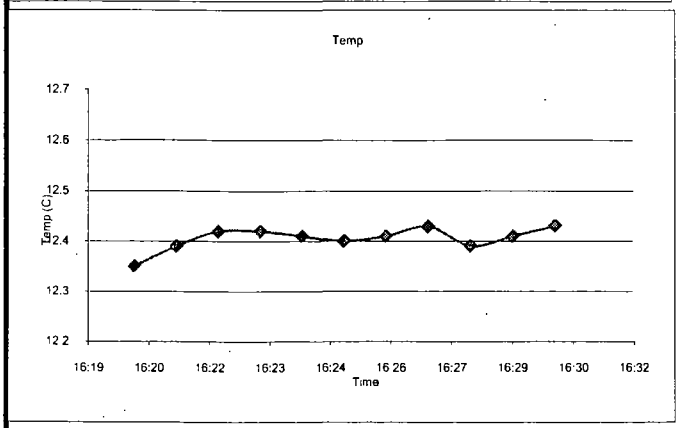

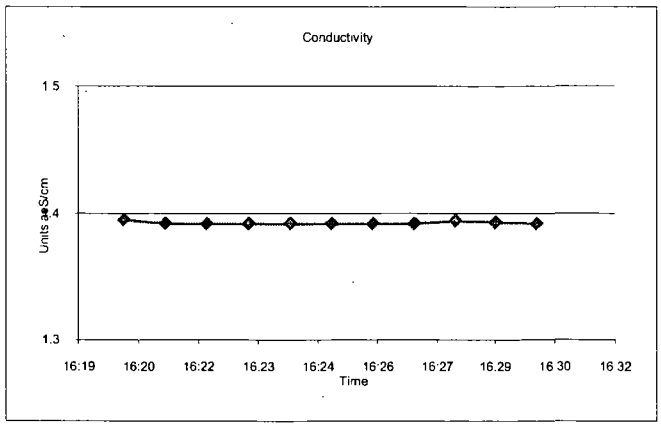

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	35	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 133A**
Casing Stickup (Ft.)	2.3	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	27-Nov-10
Total Well Depth (Ft.) TOC	37.85	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	26.83	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	11.02	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	æS/cm	FTU	mL/min	(Ft.) TOC	
							0	26.83	Static
12:43	7.21	12.35	11.13	-26	0.602		470		Start Time
12:44	7.21	12.54	11.13	-26	0.601		470		brown cloudy
12:45	7.21	12.74	11.13	-26	0.6		470	26.85	cloudy
12:46	7.21	12.92	11.13	-25	0.6		470		clear
12:47	7.21	13.05	11.13	-25	0.599		470		clear
12:48	7.21	13.06	11.12	-25	0.599		470		clear
12:49	7.21	13.03	11.13	-24	0.599		470		clear
12:50	7.21	12.96	11.13	-24	0.598		470	26.86	clear
12:51	7.2	12.96	11.12	-23	0.598		470		clear
12:52	7.2	13.01	11.15	-23	0.598		470		clear
12:53	7.21	12.81	11.15	-22	0.598		470		clear
12:54	7.2	12.74	11.14	-22	0.598		470		clear
12:55	7.2	12.77	11.14	-22	0.598	16	470	26.86	clear
MINUTES						**TOTAL LITERS**			
12.0	-0.01	-0.31%	-0.09%	0.00	0.00%		**5.64**		

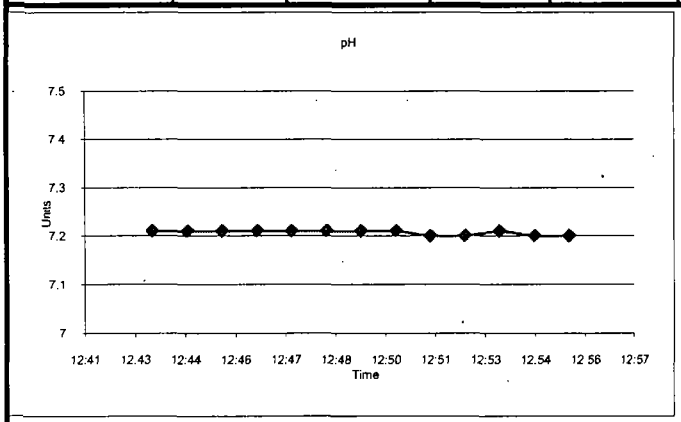

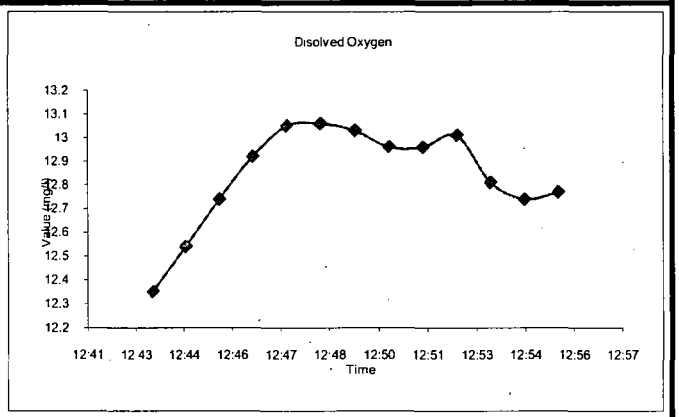

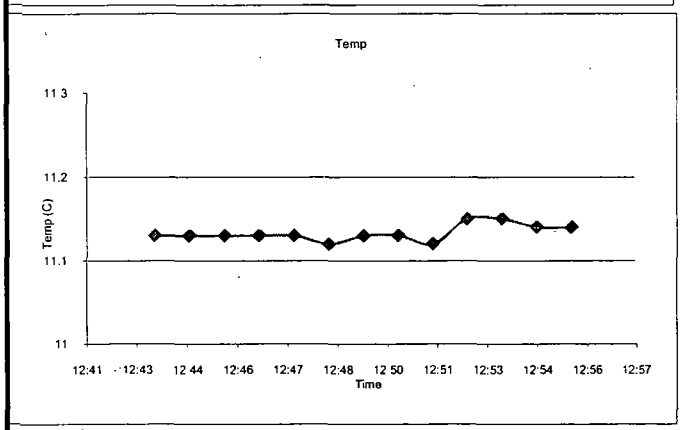

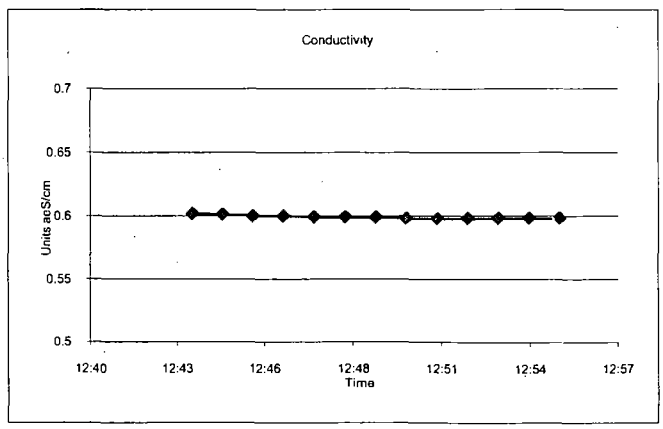

Remarks: (well condition, maintenance, etc...)

Blind field dup collected: labeled FD-2

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	59	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 133B**
Casing Stickup (Ft.)	2.51	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	27-Nov-10
Total Well Depth (Ft.) TOC	61.49	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	25.55	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	35.94	**Field Analysis Equip**	YAI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	æS/cm	NTU	mL/min	(Ft.) TOC	
							0	25.55	Static
13:24	7.06	4.35	10.82	-33	1.12		490		Start Time
13:25	7.06	4.17	10.84	-34	1.12		490		slightly cloudy
13:26	7.06	4.14	10.85	-34	1.12		490	25.59	slightly cloudy
13:27	7.06	3.94	10.92	-34	1.121		490		clear
13:28	7.06	4.26	10.86	-34	1.121		490		clear
13:29	7.06	4.15	10.88	-34	1.12		490		clear
13:30	7.06	4.18	10.89	-34	1.116		490		clear
13:31	7.06	4.17	10.86	-34	1.113		490		clear
13:32	7.06	4.08	10.87	-34	1.113		490	25.59	clear
13:33	7.05	4.03	10.81	-33	1.118		490		clear
13:34	7.06	4	10.8	-34	1.12		490		clear
13:35	7.05	3.85	10.79	-34	1.123		490	25.59	clear
13:36	7.05	3.83	10.76	-34	1.125	35	490		clear
MINUTES							**TOTAL LITERS**		
12.0	-0.01	-4.25%	-0.37%	0.00	0.45%		**5.88**		

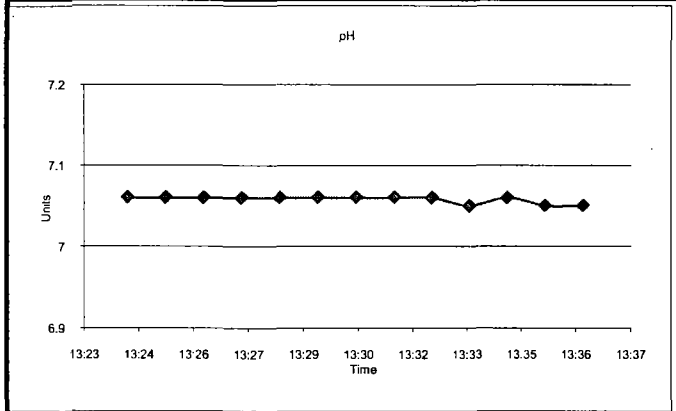

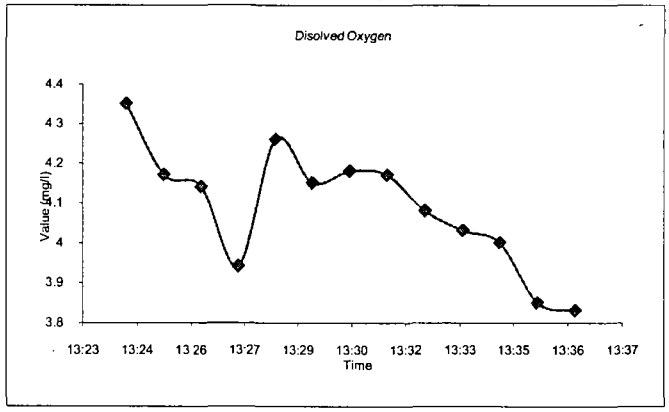

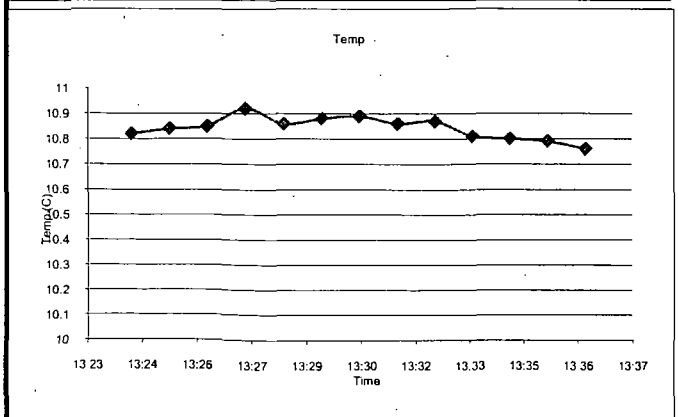

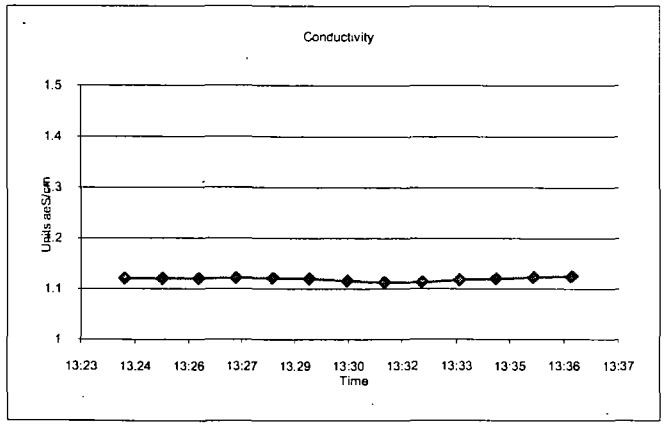

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	96	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 133C**
Casing Stickup (Ft.)	2.37	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	27-Nov-10
Total Well Depth (Ft.) TOC	98.49	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	22.1	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	76.39	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time HHMMSS	pH Units	DO mg/l	Temp øC	ORP mV	SpCond æS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
							0	22.1	Static
13:53	7.22	0.26	10.98	-39	0.728		460		Start Time
13:54	7.22	0.23	10.96	-40	0.727		460		clear
13:55	7.21	0.25	10.96	-40	0.726		460		clear
13:56	7.21	0.3	10.98	-40	0.725		460	22.15	clear
13:57	7.21	0.29	10.98	-40	0.725		460		clear
13:58	7.21	0.29	10.98	-39	0.725		460		clear
13:59	7.21	0.31	10.98	-39	0.726		460		clear
14:00	7.21	0.32	10.99	-39	0.727		460	22.16	clear
14:01	7.21	0.33	10.97	-38	0.728		460		clear
14:02	7.2	0.37	10.98	-38	0.73		460		clear
14:03	7.21	0.43	10.96	-39	0.732		460		clear
14:04	7.21	0.44	10.99	-39	0.733		460		clear
14:05	7.2	0.47	10.98	-39	0.734	5	460	22.17	clear
MINUTES						**TOTAL LITERS**			
12.0	-0.01	9.30%	0.18%	0.00	0.27%		**5.52**		

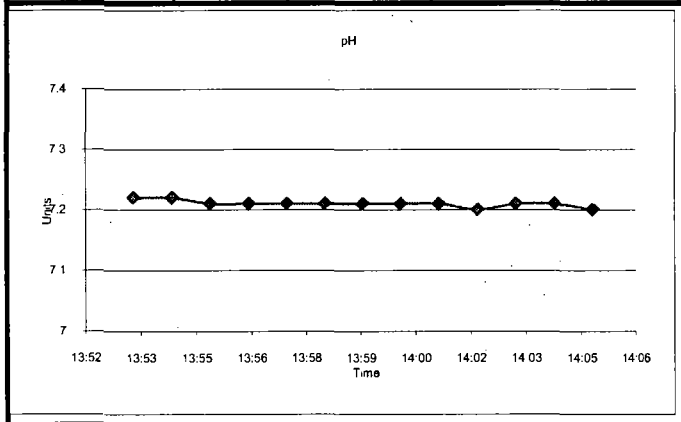

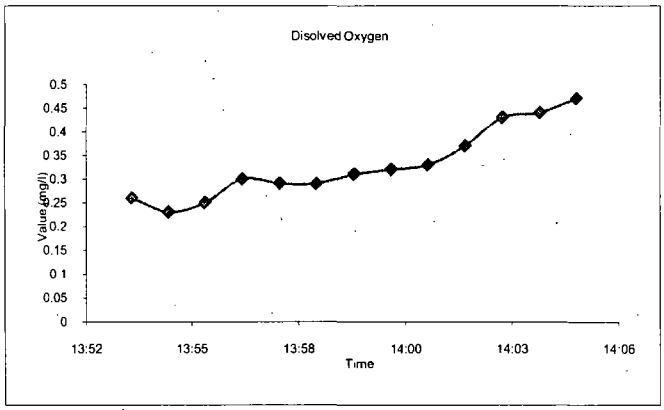

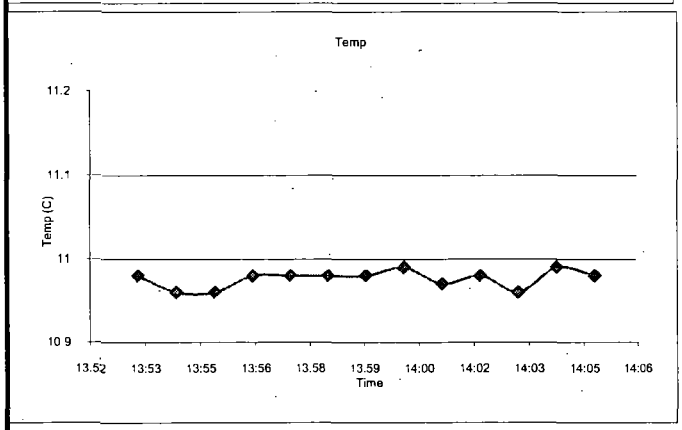

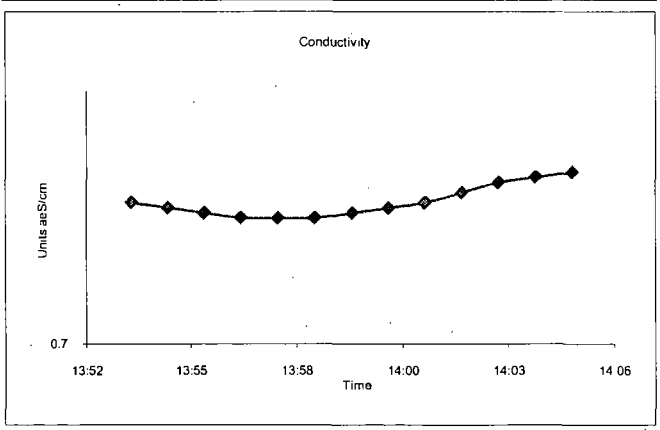

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	42	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 136**
Casing Stickup (Ft.)	-0.42	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	28-Nov-10
Total Well Depth (Ft.) TOC	44.33	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	33	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	11.33	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	æS/cm	FTU	mL/min	(Ft.) TOC	
							0	33	Static
12:19	7.2	4.29	12.57	5	1.364		250		Start Time
12:20	7.16	2.38	12.6	1	1.356		250	33.29	cloudy
12:21	6.97	5.27	12.83	7	0.023		250	33.3	cloudy
12:22	7.23	8.71	12.64	2	1.313		250		cloudy
12:23	7.17	3.09	12.67	1	1.349		250		clear
12:24	7.13	3.09	12.6	0	1.351		250		clear
12:25	7.1	3.48	12.63	0	1.347		250	33.3	clear
12:26	7.09	3.87	12.54	0	1.348		250		clear
12:27	7.06	4.27	12.51	0	1.344		250		clear
12:28	7.05	4.68	12.59	1	1.337		250		clear
12:29	7.03	5.1	12.5	0	1.336		250		clear
12:30	7.01	5.42	12.54	0	1.334		250	33.32	clear
12:31	7	5.5	12.51	0	1.336	16	250		clear
MINUTES						**TOTAL LITERS**			
12.0	-0.03	7.84%	0.08%	0.00	0.00%		**3.00**		

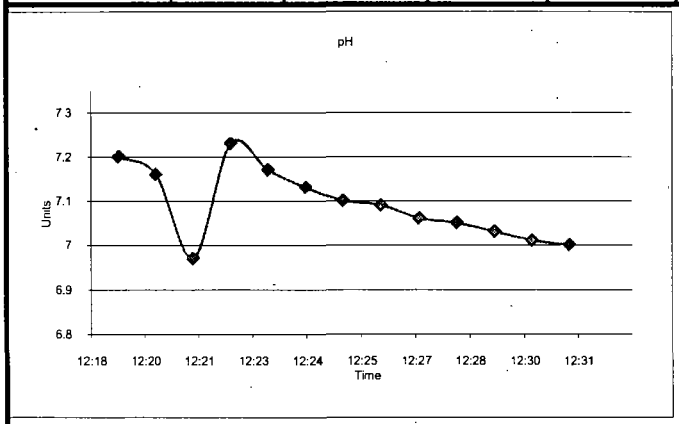

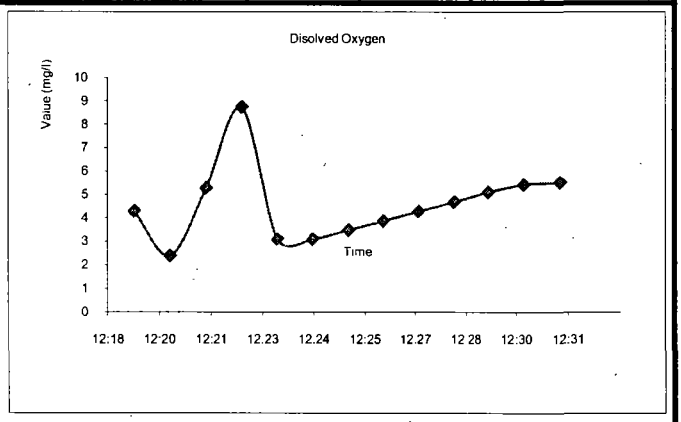

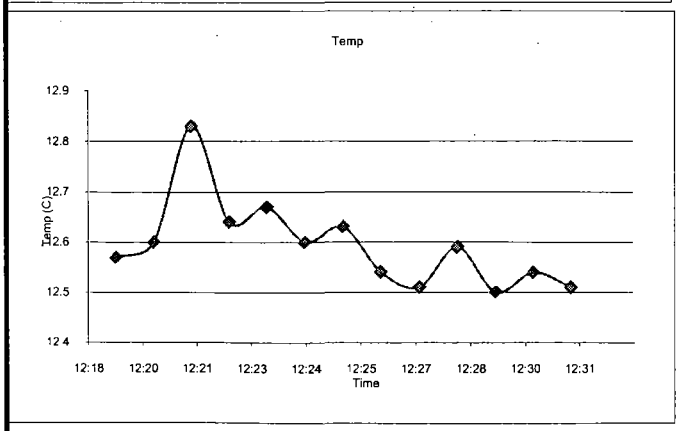

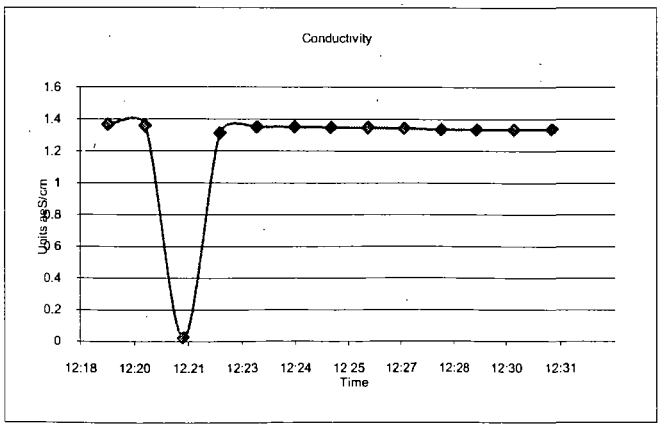

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	87	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 200**
Casing Stickup (Ft.)	1.15	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	28-Nov-11
Total Well Depth (Ft.) TOC	89.93	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	46.55	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	43.38	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	æS/cm	FTU	mL/min	(Ft.) TOC	
							0	46.55	Static
13:12	7.01	6.04	12.08	-11	1.459		410		*Start Time*
13:13	7.01	6.02	12.1	-9	1.446		410		cloudy
13:14	7.02	6	12.06	-9	1.441		410	46.62	cloudy
13:15	7.04	6.14	12.01	-9	1.416		410		cloudy
13:16	7.1	6.06	11.52	-6	1.415		410		cloudy
13:17	7.1	6.11	11.89	-7	1.41		410		slightly cloudy
13:18	7.05	5.99	11.96	-7	1.41		410	46.62	slightly cloudy
13:19	7.04	5.87	12.01	-6	1.406		410		slightly cloudy
13:20	7.04	5.89	11.99	-6	1.404		410		slightly cloudy
13:21	7.05	5.86	12.05	-6	1.398		410		slightly cloudy
13:22	7.04	5.79	12.02	-6	1.396		410		slightly cloudy
13:23	7.04	5.85	12.06	-5	1.393		410	46.63	slightly cloudy
13:24	7.03	5.81	12.05	-5	1.392	85	410		slightly cloudy
MINUTES						**TOTAL LITERS**			
12.0	-0.01	0.35%	0.25%	1.00	-0.29%		**4.92**		

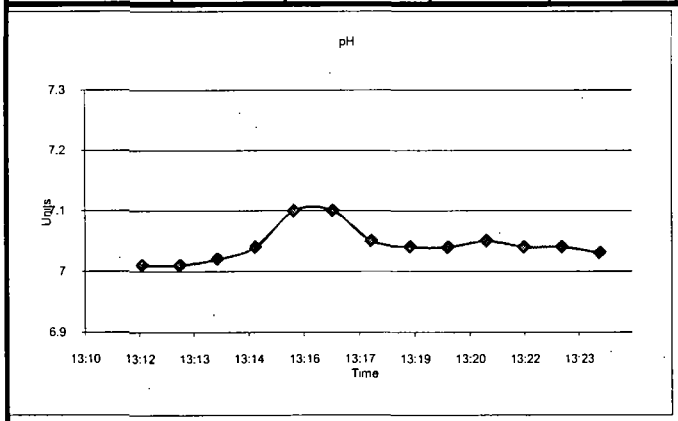

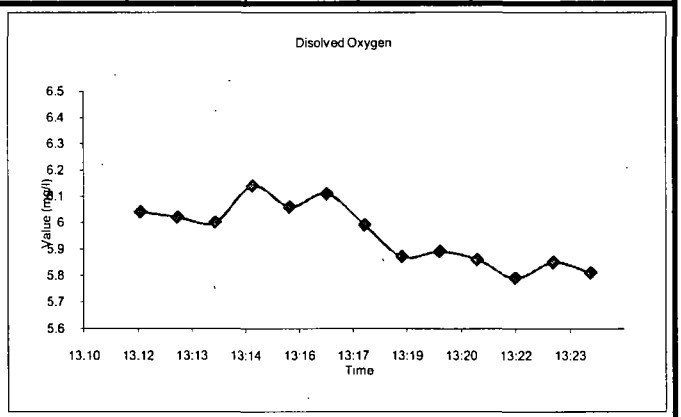

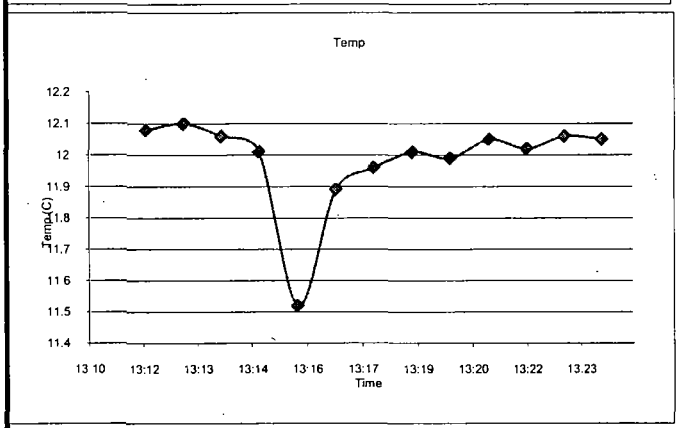

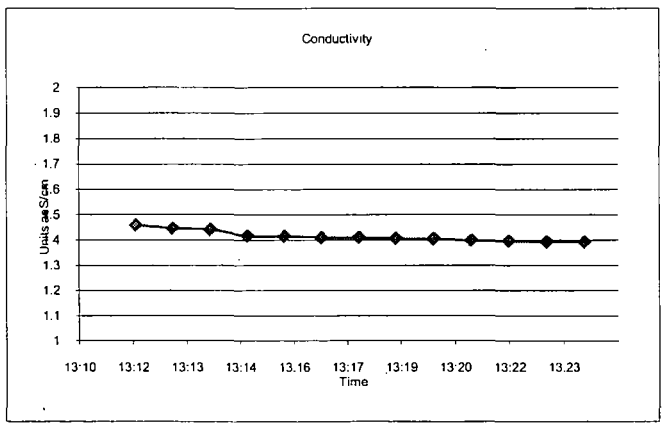

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	48	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 201**
Casing Stickup (Ft.)	-0.32	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	28-Nov-10
Total Well Depth (Ft.) TOC	50.15	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	28.79	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	21.36	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	æS/cm	FTU	mL/min	(Ft.) TOC	
							0	28.79	Static
11:35	7.12	0.25	14.26	-57	1.277		320		Start Time
11:36	7.12	0.27	14.2	-59	1.278		320	28.85	cloudy
11:37	7.13	0.26	14.28	-62	1.274		320		cloudy
11:38	7.13	0.28	14.22	-65	1.277		320		clear
11:39	7.13	0.29	14.22	-66	1.276		320		clear
11:40	7.15	0.3	14.23	-66	1.274		320	28.86	clear
11:41	7.14	0.35	14.15	-68	1.277		320		clear
11:42	7.15	0.39	14.21	-69	1.275		320		clear
11:43	7.15	0.44	14.17	-70	1.275		320		clear
11:44	7.15	0.52	14.17	-71	1.275		320		clear
11:45	7.16	0.6	14.17	-70	1.275		320	28.86	clear
11:46	7.16	0.64	14.2	-70	1.274		320		clear
11:47	7.17	0.64	14.16	-71	1.275	4	320		clear
MINUTES						**TOTAL LITERS**			
12.0	0.01	6.67%	-0.07%	-1.00	0.00%		**3.84**		

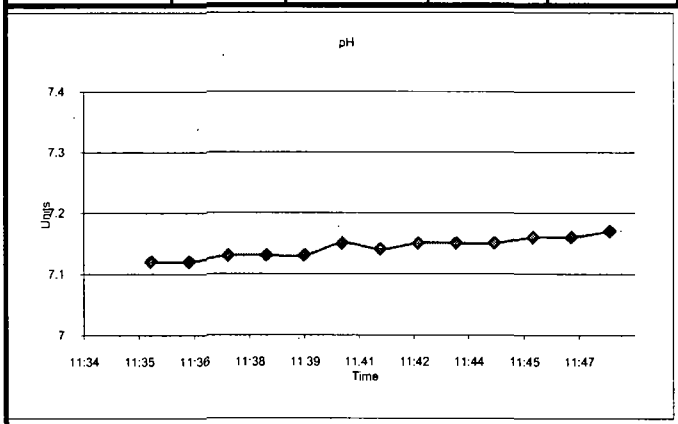

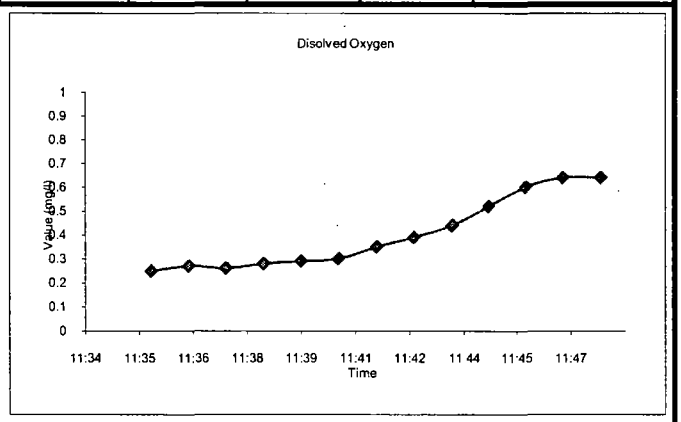

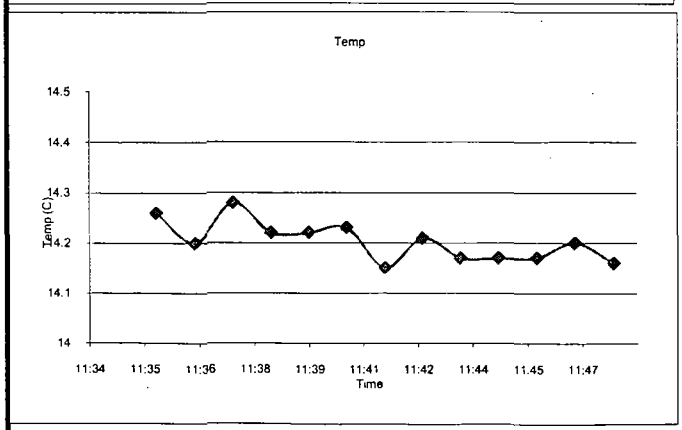

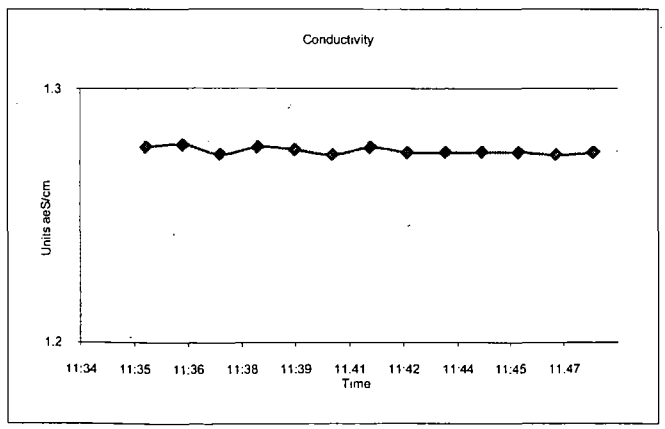

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	48	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 202**
Casing Stickup (Ft.)	-0.32	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	28-Nov-10
Total Well Depth (Ft.) TOC	50.01	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	27.8	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	22.21	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	æS/cm	FTU	mL/min	(Ft.) TOC	
							0	27.8	Static
10:56	6.94	3.9	14.56	-5	1.324		390		Start Time
10:57	7.02	3.99	14.54	-11	1.322		390	27.84	cloudy
10:58	6.95	4.04	14.6	-8	1.32		390		cloudy
10:59	6.95	4.1	14.64	-7	1.32		390		cloudy
11:00	6.94	4.06	14.61	-6	1.321		390		cloudy
11:01	6.96	4.21	14.61	-6	1.319		390	27.85	slightly cloudy
11:02	6.96	4.33	14.63	-6	1.319		390		clear
11:03	6.99	12	14.77	3	0.694		390		clear
11:04	6.99	5.2	14.65	-2	1.32		390		clear
11:05	6.97	4.71	14.69	-3	1.318		390	27.85	clear
11:06	6.96	4.53	14.75	-3	1.319		390		clear
11:07	6.96	4.53	14.68	-2	1.32		390		clear
11:08	6.95	4.64	14.72	-1	1.318	86	390		clear
MINUTES							**TOTAL LITERS**		
12.0	-0.01	2.43%	-0.20%	2.00	-0.08%		**4.68**		

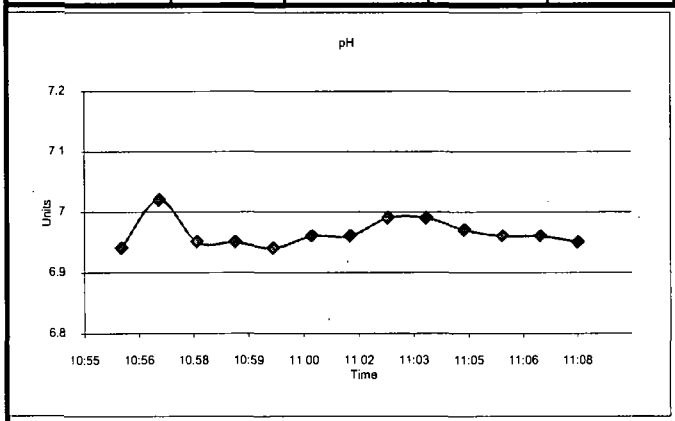

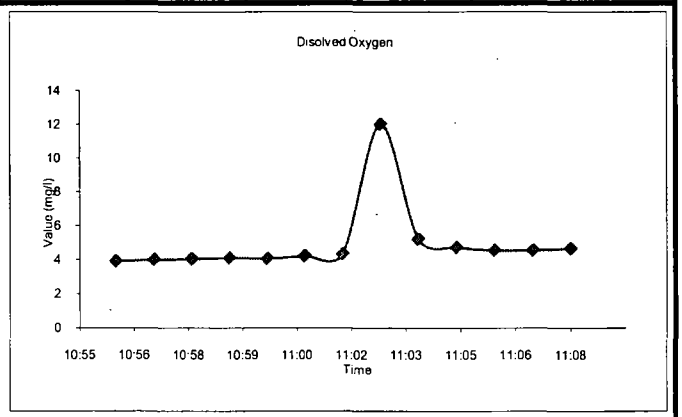

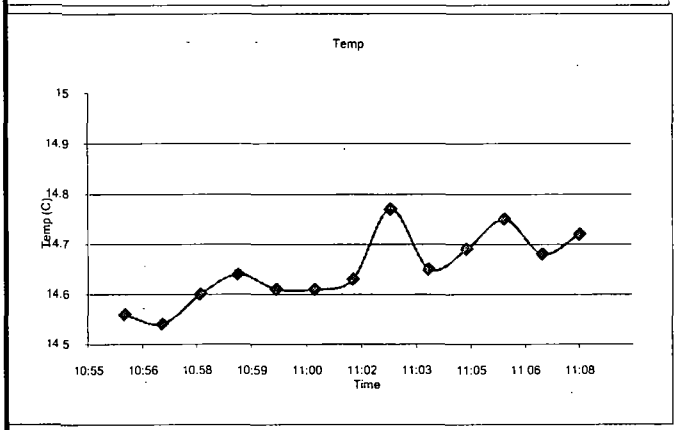

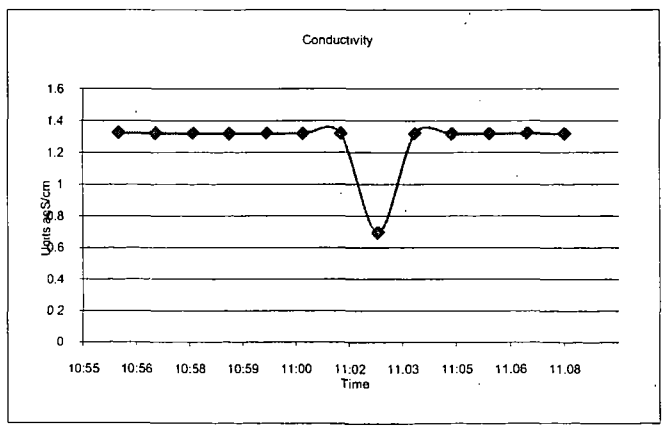

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	47	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 203**
Casing Stickup (Ft.)	-0.58	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	28-Nov-10
Total Well Depth (Ft.) TOC	49.35	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	27.42	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	21.93	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	æS/cm	FTU	mL/min	(Ft.) TOC	
							0	27.42	Static
10:16	6.96	6.49	14.22	33	0.914		415		Start Time
10:17	6.97	6.18	14.21	32	0.91		415	27.49	cloudy
10:18	6.98	5.98	14.2	31	0.908		415		cloudy
10:19	6.98	5.86	14.19	30	0.906		415		cloudy
10:20	6.98	5.8	14.19	29	0.905		415		clear
10:21	6.98	5.77	14.16	29	0.905		415		clear
10:22	6.98	5.72	14.14	28	0.905		415	27.49	clear
10:23	6.99	5.73	14.15	28	0.904		415		clear
10:24	6.99	5.74	14.12	28	0.905		415		clear
10:25	6.99	5.74	14.12	27	0.905		415		clear
10:26	7	5.71	14.12	27	0.903		415		clear
10:27	6.99	5.73	14.11	27	0.902		415	27.5	clear
10:28	7.01	5.74	14.08	25	0.9		415		clear
10:29	7	5.73	14.11	26	0.899	8	415		clear
MINUTES							**TOTAL LITERS**		
13.0	0.01	0.00%	0.00%	-1.00	-0.33%		**5.40**		

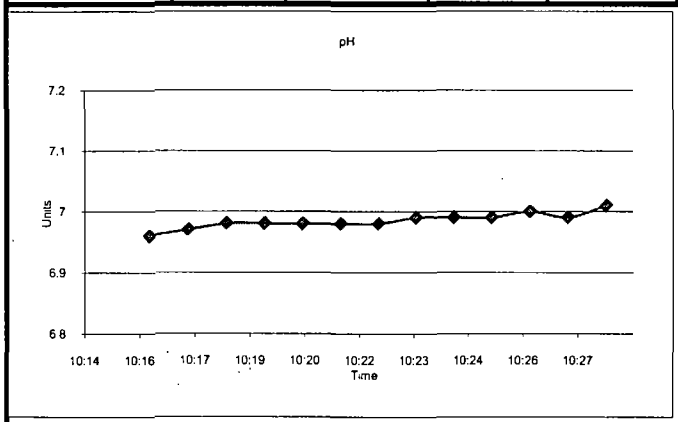

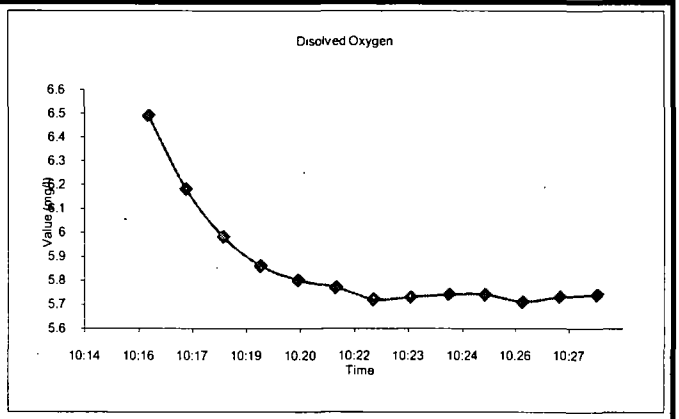

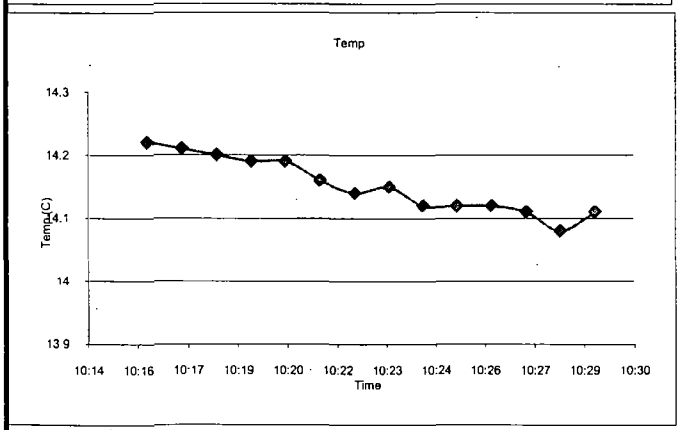

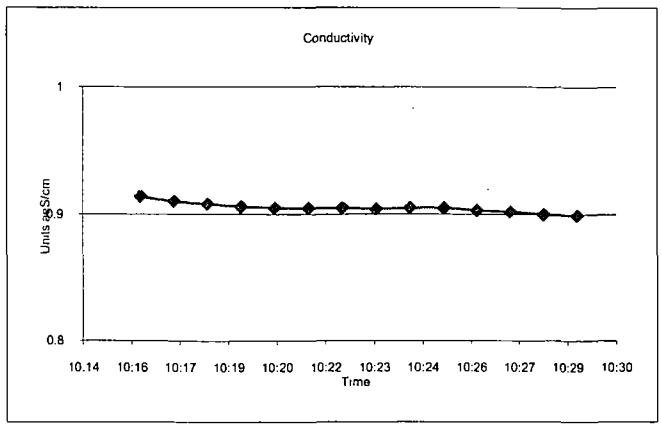

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	86	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 204**
Casing Stickup (Ft.)	-0.39	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	25-Nov-10
Total Well Depth (Ft.) TOC	88.96	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	27.2	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	61.76	**Field Analysis Equip**	YSI 556 MPS	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	æS/cm	FTU	mL/min	(Ft.) TOC	
							0	27.2	Static
8:57	7.36	0.66	13.05	19	0.841		480		Start Time
8:58	7.36	0.59	13.08	16	0.841		480		slightly cloudy
8:59	7.36	0.57	13.12	13	0.841		480		slightly cloudy
9:00	7.36	0.5	13.11	10	0.841		480		slightly cloudy
9:01	7.35	0.48	13.12	7	0.84		480		slightly cloudy
9:02	7.36	0.43	13.09	5	0.841		480	27.2	slightly cloudy
9:03	7.35	0.4	13.08	2	0.841		480		slightly cloudy
9:04	7.35	0.38	13.06	0	0.841		480		slightly cloudy
9:05	7.35	0.37	13.04	-3	0.841		480		slightly cloudy
9:06	7.35	0.32	12.97	-5	0.841		480		slightly cloudy
9:07	7.34	0.37	12.99	-6	0.841		480		slightly cloudy
9:08	7.33	0.35	13.04	-8	0.84		480	27.2	slightly cloudy
9:09	7.34	0.35	13.08	-10	0.84	68	480		slightly cloudy
MINUTES						**TOTAL LITERS**			
12.0	0.00	-5.41%	0.69%	-4.00	-0.12%		**5.76**		

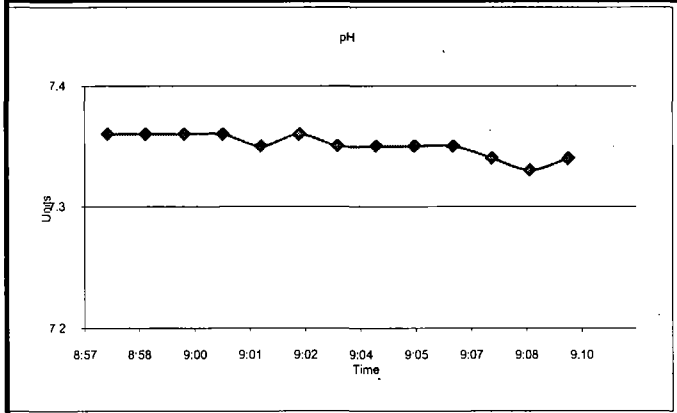

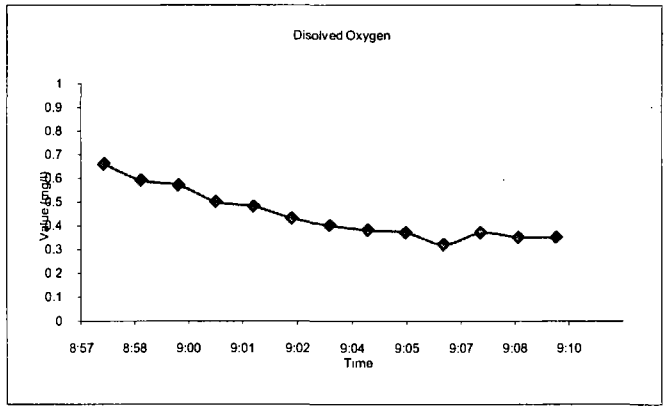

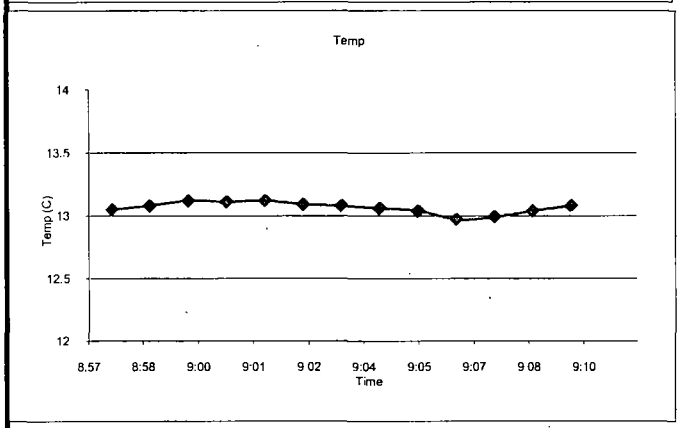

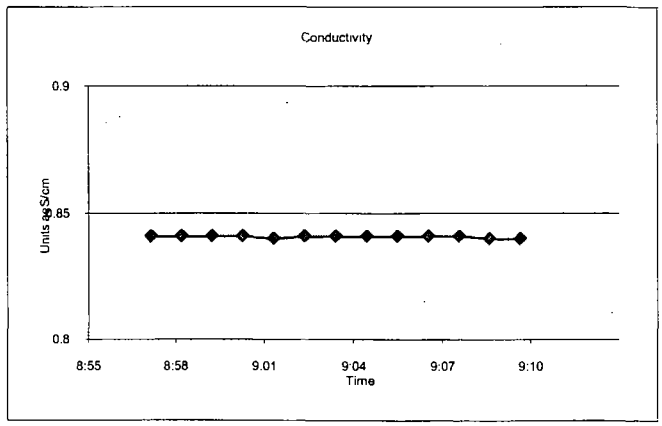

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	108	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 205A**
Casing Stickup (Ft.)	-0.34	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	25-Nov-10
Total Well Depth (Ft.) TOC	110.27	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	2.73	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	107.54	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	æS/cm	FTU	mL/min	(Ft.) TOC	
							0	2.73	Static
11:30	7.29	0.13	12.74	-29	0.962		500		Start Time
11:31	7.29	0.14	12.75	-30	0.961		500		clear
11:32	7.29	0.14	12.81	-31	0.96		500	2.73	clear
11:33	7.29	0.14	12.79	-32	0.961	-	500		clear
11:34	7.29	0.16	12.82	-33	0.96		500		clear
11:35	7.29	0.16	12.75	-34	0.962		500		clear
11:36	7.29	0.19	12.78	-35	0.961		500		clear
11:37	7.29	0.18	12.78	-35	0.961		500		clear
11:38	7.29	0.18	12.76	-36	0.961		500		clear
11:39	7.29	0.21	12.76	-37	0.961		500	2.73	clear
11:40	7.29	0.18	12.73	-37	0.961		500		clear
11:41	7.29	0.18	12.75	-38	0.96		500		clear
11:42	7.29	0.16	12.7	-38	0.961	16	500		clear
MINUTES							**TOTAL LITERS**		
12.0	0.00	-11.11%	-0.24%	-1.00	0.00%		**6.00**		

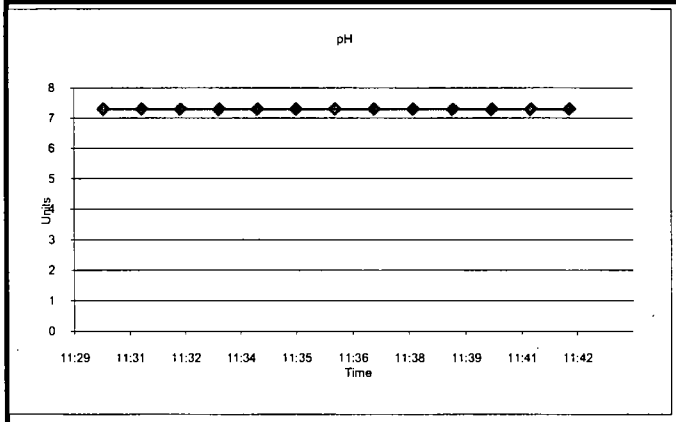

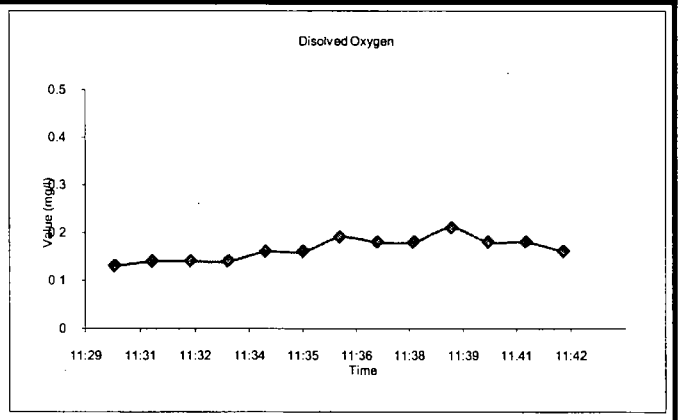

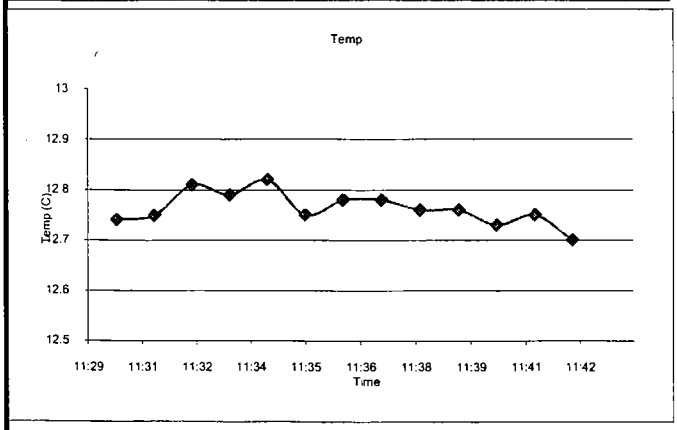

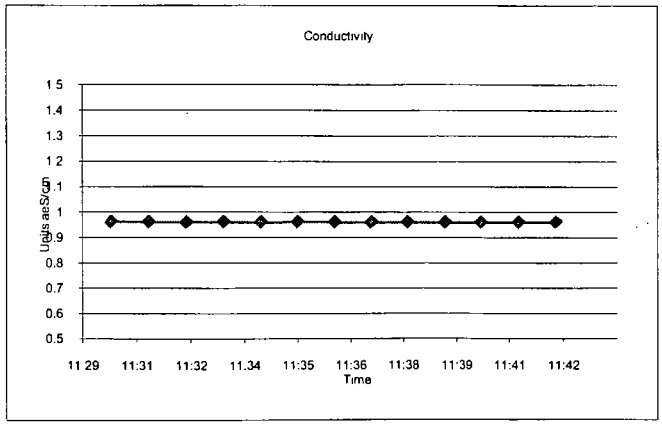

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	148	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 205B**
Casing Stickup (Ft.)	-0.48	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	25-Nov-10
Total Well Depth (Ft.) TOC	150.05	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	2.6	**Field Analysis Method**	*Flow Thru Analysis - 250 mL*	**Preservation**	HCl / Ice	Site Visitors:	*None*
Water Thickness (Ft.)	147.45	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	æS/cm	FTU	mL/min	(Ft.) TOC	
							0	2.6	Static
10:48	7.27	0.2	12.88	-10	0.959		500		Start Time
10:49	7.27	0.17	12.9	-11	0.959		500		clear
10:50	7.28	0.18	12.88	-13	0.959		500	2.59	clear
10:51	7.28	0.15	12.89	-14	0.957		500		clear
10:52	7.28	0.16	12.9	-15	0.957		500		clear
10:53	7.28	0.17	12.89	-16	0.958		500		clear
10:54	7.29	0.15	12.89	-18	0.957		500		clear
10:55	7.29	0.16	12.88	-19	0.958		500		
10:56	7.3	0.16	12.88	-21	0.958		500		
10:57	7.29	0.14	12.9	-21	0.957		500		
10:58	7.3	0.14	12.9	-23	0.957		500		
10:59	7.3	0.16	12.9	-24	0.958		500		
11:00	7.3	0.16	12.93	-25	0.957	11	500	2.6	
MINUTES							**TOTAL LITERS**		
12.0	*0.00*	*14.29%*	*0.23%*	*-2.00*	*0.00%*		**6.00**		

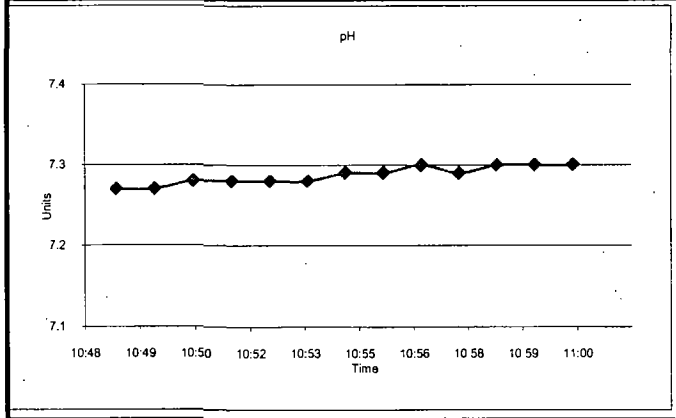

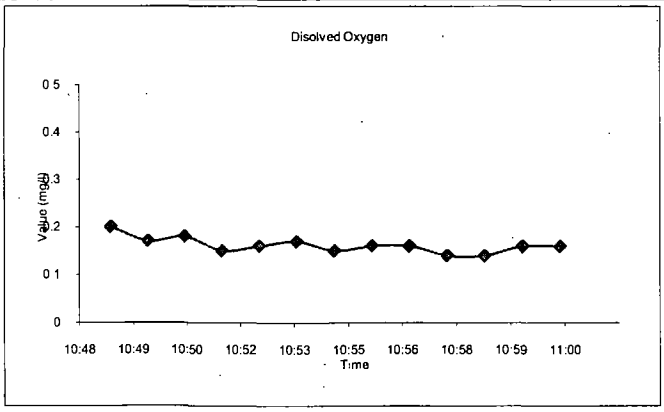

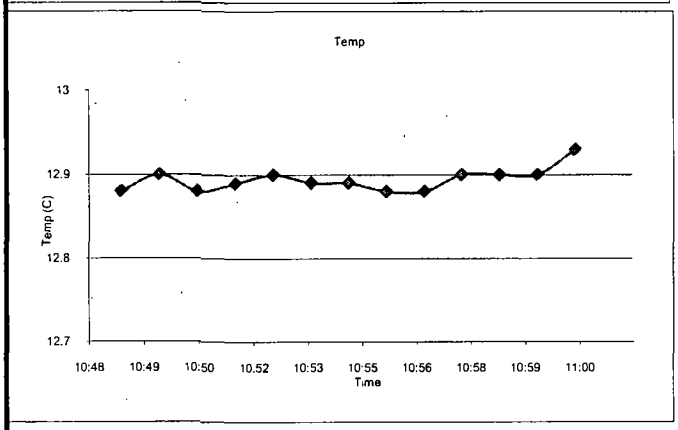

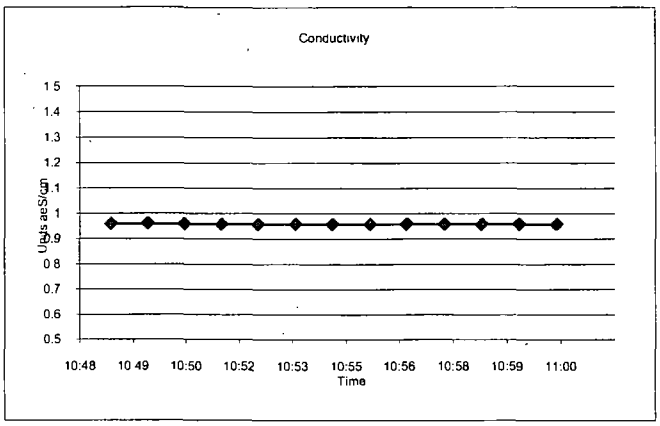

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	88	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 206A**
Casing Stickup (Ft.)	-0.36	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	29-Nov-10
Total Well Depth (Ft.) TOC	90.24	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	5.22	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	85.02	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	æS/cm	FTU	mL/min	(Ft.) TOC	
							0	5.22	Static
14:17	7.11	1.66	13.39	-61	0.744		470		Start Time
14:18	7.15	1.35	13.54	-62	0.849		470	5.22	clear
14:19	7.15	1.02	13.6	-55	0.968		470		clear
14:20	7.14	0.83	13.61	-49	1.01		470		clear
14:21	7.13	0.45	13.57	-52	1.031		470		clear
14:22	7.13	0.36	13.53	-60	1.044		470	5.22	clear
14:23	7.13	0.31	13.53	-73	1.051		470		clear
14:24	7.13	0.29	13.52	-97	1.056		470		clear
14:25	7.12	0.27	13.56	-99	1.059		470		clear
14:26	7.12	0.25	13.57	-102	1.065		470	5.22	clear
14:27	7.12	0.26	13.6	-101	1.07	7	470		clear
MINUTES							**TOTAL LITERS**		
10.0	0.00	-3.70%	0.29%	-2.00	1.04%		**4.70**		

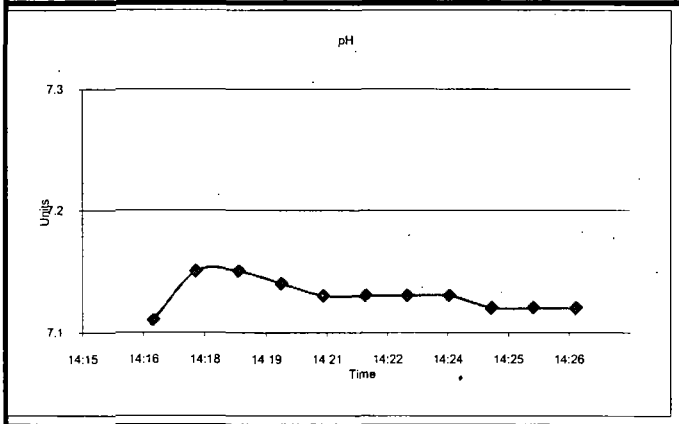

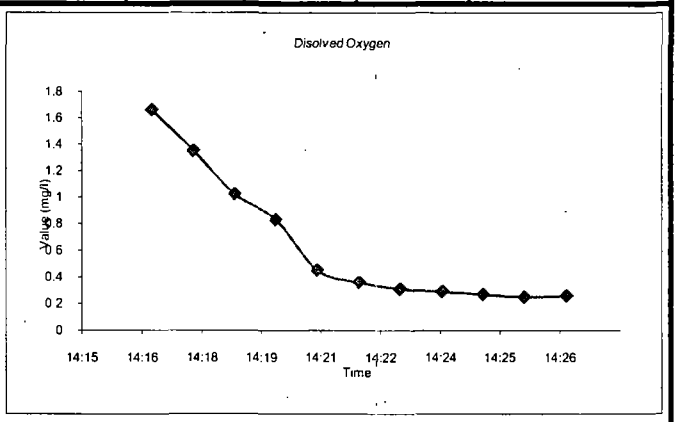

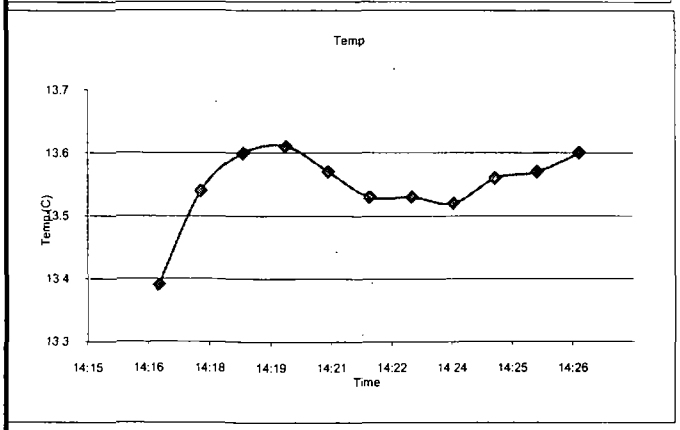

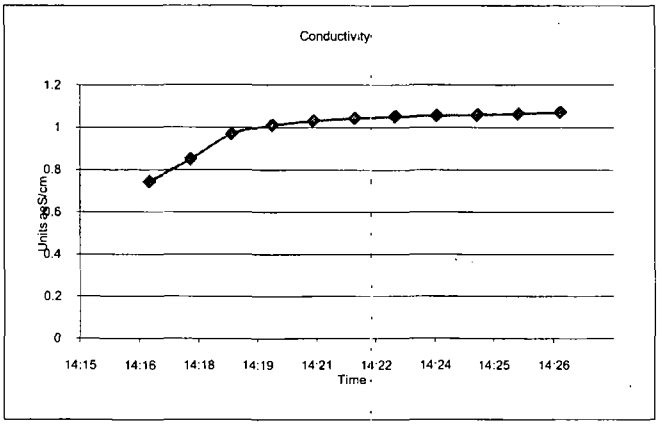

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	127	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 206B**
Casing Stickup (Ft.)	-0.45	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	29-Nov-10
Total Well Depth (Ft.) TOC	129.94	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	2.53	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	127.41	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time HHMMSS	pH Units	DO mg/l	Temp øC	ORP mV	SpCond æS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
							0	2.53	Static
13:47	7.32	4.43	13.46	-9	1.018		500		Start Time
13:48	7.22	1.31	13.45	-15	1.017		500	2.53	clear
13:49	7.21	1.03	13.47	-17	1.014		500		clear
13:50	7.2	0.86	13.48	-19	1.014		500		clear
13:51	7.18	0.75	13.48	-20	1.011		500		clear
13:52	7.17	0.67	13.45	-20	1.011		500		clear
13:53	7.17	0.63	13.45	-20	1.01		500		clear
13:54	7.16	0.56	13.45	-21	1.01		500	2.53	clear
13:55	7.15	0.53	13.45	-21	1.008		500		clear
13:56	7.14	0.49	13.45	-21	1.008		500		clear
13:57	7.15	0.47	13.45	-21	1.006		500		clear
13:58	7.15	0.44	13.44	-21	1.007		500	2.53	clear
13:59	7.14	0.41	13.52	-21	1.005	15	500		clear
MINUTES							**TOTAL LITERS**		
12.0	-0.01	-12.77%	0.52%	0.00	-0.10%		**6.00**		

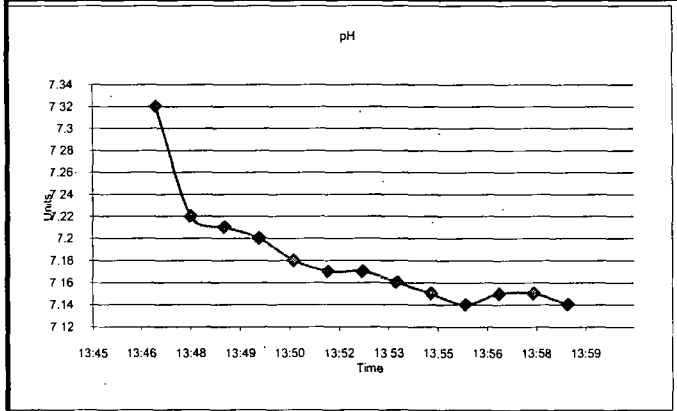

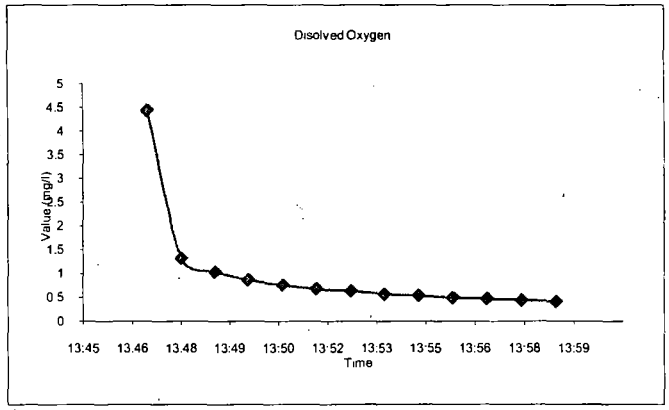

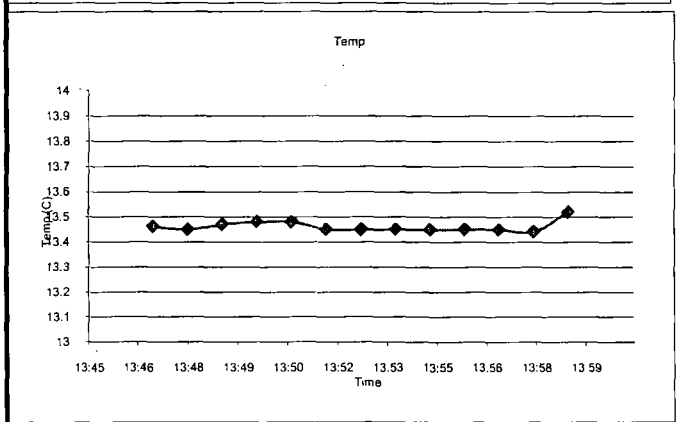

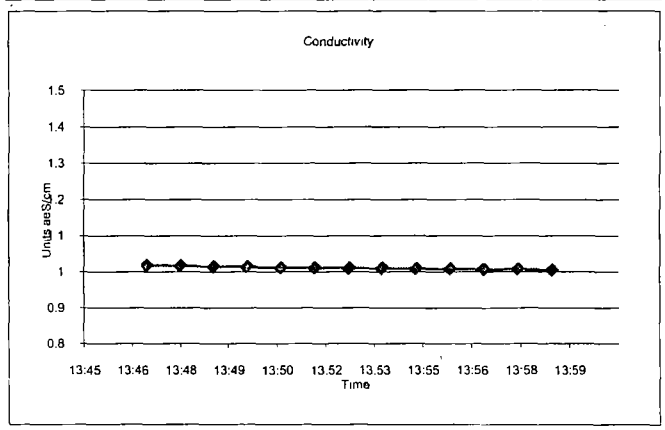

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	249	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 206C**
Casing Stickup (Ft.)	-0.55	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	29-Nov-10
Total Well Depth (Ft.) TOC	251.31	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	2.9	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	248.41	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	æS/cm	FTU	mL/min	(Ft.) TOC	
							0	2.9	Static
14:04	7.13	1.58	13.54	-19	0.81		480		clear
14:05	7.12	2.34	13.3	-17	0.77		480	2.9	clear
14:06	7.11	1.54	13.24	-17	0.758		480		clear
14:07	7.08	1.11	13.24	-21	0.753		480		clear
14:08	7.05	0.79	13.19	-36	0.74		480		clear
14:09	7.03	0.68	13.18	-41	0.724		480	2.9	clear
14:10	7.02	0.69	13.19	-41	0.72		480		clear
14:11	7.02	0.71	13.18	-40	0.722	6	480		clear
MINUTES							**TOTAL LITERS**		
7.0	-0.01	4.41%	0.00%	1.00	-0.28%		**3.36**		

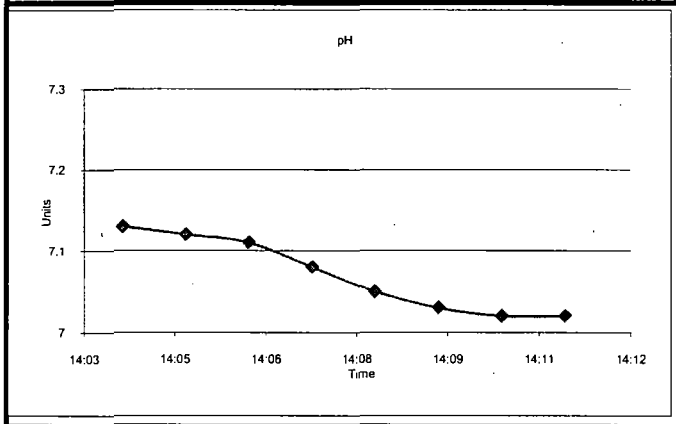

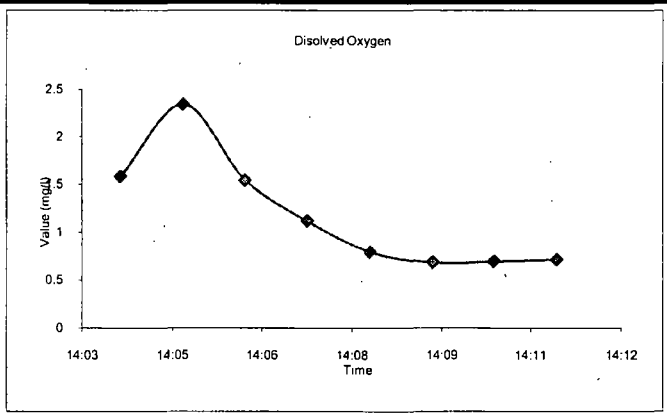

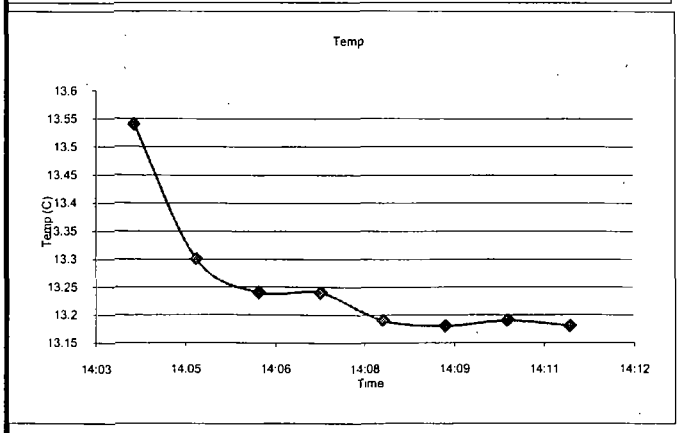

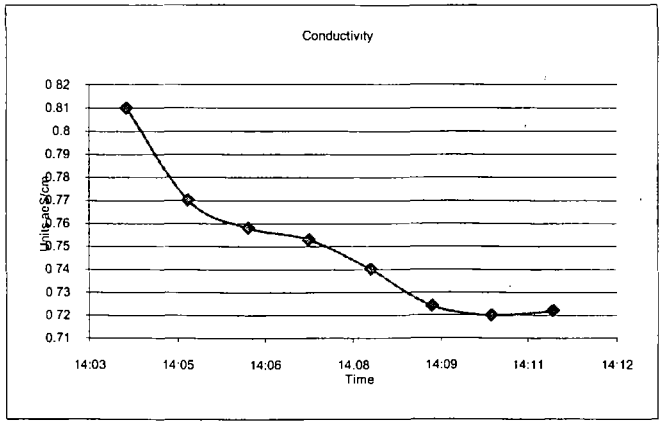

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site
Groundwater Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	88	**Lab Analysis**	VOC per Target Conpound List	Well ID:	**MW 207**
Casing Stickup (Ft.)	-0.3	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	25-Nov-10
Total Well Depth (Ft.) TOC	90.81	**Purge Equip**	QED Air Diaphram	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	34.96	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	55.85	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	Fall 2010		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HHMMSS	Units	mg/l	øC	mV	æS/cm	FTU	mL/min	(Ft.) TOC	
							0	34.96	Static
12:15	7.26	6.68	12.11	10	1.027		500		redish brown cloudy
12:16	7.26	6.53	12.11	11	1.027		500		redish brown cloudy
12:17	7.26	6.47	12.12	11	1.027		500		redish brown cloudy
12:18	7.26	6.41	12.13	12	1.027		500	34.96	cloudy
12:19	7.26	6.26	12.11	12	1.027		500		cloudy
12:20	7.26	6.23	12.1	13	1.028		500		cloudy
12:21	7.26	6.29	12.12	13	1.028		500		cloudy
12:22	7.26	6.28	12.16	13	1.027		500	34.96	cloudy
12:23	7.27	6.44	12.15	14	1.027		500		clear
12:24	7.27	6.5	12.14	14	1.027		500		clear
12:25	7.27	6.46	12.14	14	1.028		500		clear
12:26	7.24	6.57	12.15	15	1.028		500		clear
12:27	7.26	6.6	12.14	15	1.028	87	500		clear
MINUTES						**TOTAL LITERS**			
12.0	-0.01	2.17%	0.00%	1.00	0.00%		**6.00**		

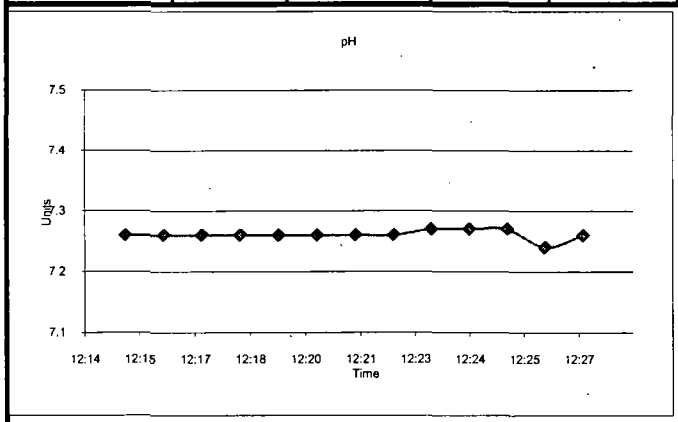

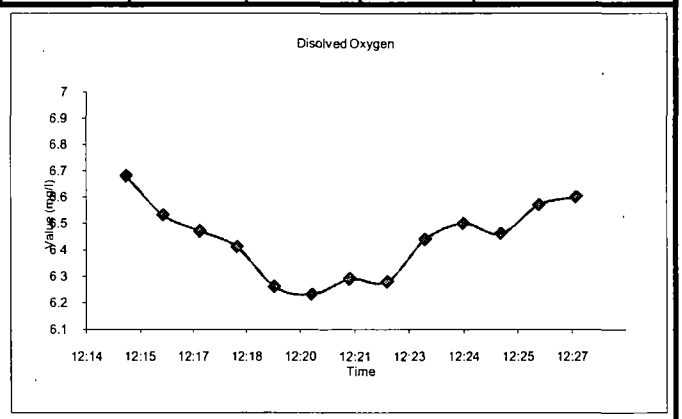

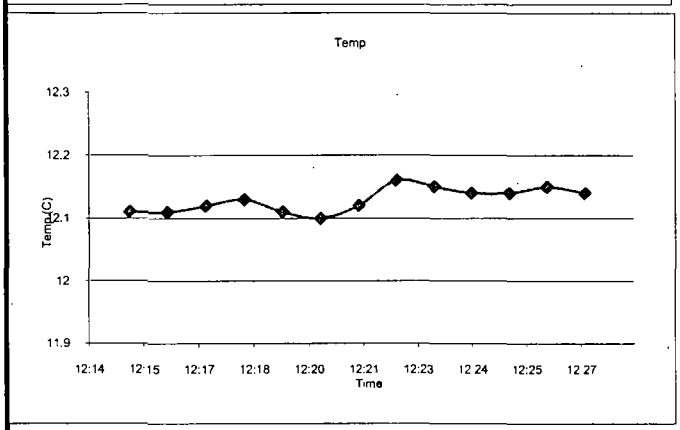

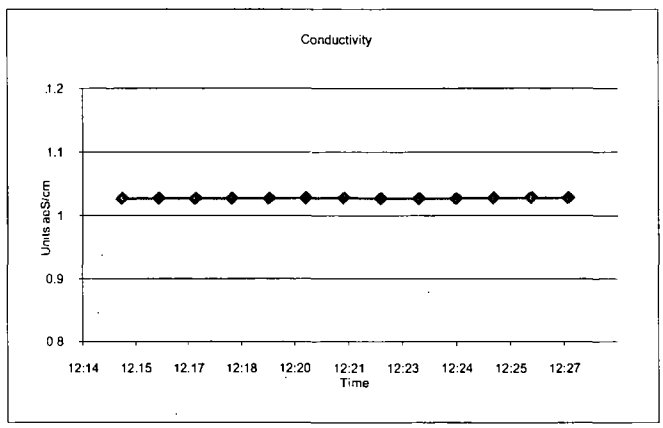

Remarks: (well condition, maintenance, etc...)
