1118537 - R8 SDMS

SUMMARY REPORT
FOR
ASARCO EAST HELENA SMELTER
2008 INTERIM MEASURES WORK PLAN ADDENDUM

BLAST FURNACE FLUE AND MONIER FLUE CLEANING AND DEMOLITION AND DEMOLITION FOOTPRINT EXPOSED AREAS SOIL SAMPLING

Prepared by:

Hydrometrics, Inc.
3020 Bozeman Avenue
Helena, MT 59601

February 2009

TARGET SHEET

EPA REGION VIII

SUPERFUND DOCUMENT MANAGEMENT SYSTEM

DOCUMENT NUMBER: 1118537

SITE NAME: EAST HELENA RCRA CORRECTIVE ACTION

DOCUMENT DATE: 02/19/2009

DOCUMENT NOT SCANNED

Due to one of the following reasons:

- ☐ PHOTOGRAPHS
- ☐ 3-DIMENSIONAL
- ☐ OVERSIZED
- ☑ AUDIO/VISUAL
- ☐ PERMANENTLY BOUND DOCUMENTS
- ☐ POOR LEGIBILITY
- ☐ OTHER
- ☐ NOT AVAILABLE
- ☐ TYPES OF DOCUMENTS NOT TO BE SCANNED
  (Data Packages, Data Validation, Sampling Data, CBI, Chain of Custody)

DOCUMENT DESCRIPTION:

1 CD - BLAST FURNACE FLUE AND MONIER FLUE CLEANING AND DEMOLITION AND DEMOLITION FOOTPRINT EXPOSED AREAS SOIL SAMPLING

Contact the Superfund Records Center to view available document.
(303) 312-6473

ASARCO

RECEIVED
FEB 24 2009
Office of Enforcement
Compliance & Environmental
Justice

Linda Jacobson (3 Copies)
RCRA Project Manager
US EPA Region VIII 8ENF-T
1595 Wynkoop Street
Denver, Colorado 80202-1129

February 20, 2009

SENT BY CERTIFIED MAIL
RETURN RECEIPT REQUESTED

RE: 2008 Interim Measures Work Plan Addendum, Blast Furnace Flue and Monier Flue Cleaning and Demolition and Demolition Footprint Exposed Areas Soil Sampling, Summary Report, Asarco East Helena Facility

Dear Ms. Jacobson:

On May 8, 2008, Asarco submitted the 2008 Interim Measures Work Plan Addendum, Blast Furnace Flue and Monier Flue Cleaning and Demolition and Demolition Footprint Exposed Areas Soil Sampling for the Asarco East Helena Facility. Asarco herewith submits the attached Summary Report that discusses the actions that occurred to fulfill the obligations set forth in the Work Plan Addendum. A copy of the Summary Report is simultaneously being submitted in the enclosed compact diskette. The Summary Report, compact diskettes, and the certification signed by an officer of ASARCO (Asarco) are attached to this letter.

In January 2009, EPA directed Asarco to complete the Summary Report. Over the last few weeks, Asarco's contractor assembled the necessary information to complete the Summary Report at an estimated cost of $3000.00. The Custodial Trust Agreement (Trust) entitles Asarco to receive credit for work performed at the Asarco East Helena site between February 1, 2009 and the effective date of the Trust. Asarco seeks written approval from EPA that preparation of the Summary Report qualifies for the credit.

Sincerely,

Jon Nickel

Jon Nickel

Enclosures

CERTIFICATION
PURSUANT TO U.S. v ASARCO INCORPORATED
(CV-98-3-H-CCL, USDC, D. MONTANA)

I certify under penalty of law that this document, 2008 Interim Measures Work Plan Addendum, Blast Furnace Flue and Monier Flue Cleaning and Demolition and Demolition Footprint Exposed Areas Soil Sampling, Summary Report, Asarco East Helena Facility and all attachment, were prepared under my direct supervision in accordance with a system designed to assure that qualified personnel gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and completes. I am aware that there are significant penalties for submitting false information, including the possibility of fine or imprisonment for knowing violations.

Signature _____
Name: Thomas L. Aldrich
Title: Vice President Environmental Affairs
Date: February 19, 2009

SUMMARY REPORT

FOR

ASARCO EAST HELENA SMELTER

2008 INTERIM MEASURES WORK PLAN ADDENDUM

BLAST FURNACE FLUE AND MONIER FLUE CLEANING AND DEMOLITION AND DEMOLITION FOOTPRINT EXPOSED AREAS SOIL SAMPLING

Prepared by:

Hydrometrics, Inc.
3020 Bozeman Avenue
Helena, MT 59601

February 2009

TABLE OF CONTENTS

LIST OF FIGURES ii
LIST OF APPENDICIES iii
1.0 INTRODUCTION 1-1
2.0 2008 BLAST FURNACE FLUE AND MONIER FLUE CLEANING AND DEMOLITION OVERVIEW 2-1
2.1 PRE-DEMOLITION CLEANING 2-1
2.2 DEMOLITION 2-2
2.2.1 Dust Control 2-2
2.2.2 Isolation Activities Before Demolition of Structures 2-3
2.2.3 Steel Structure Demolition 2-4
2.2.4 Concrete/Masonry Structure Demolition 2-4
2.2.5 Demolition Material Stockpiling 2-5
2.2.6 Debris Transport 2-5
2.2.7 Waste Sampling and Characterization 2-6
2.3 FINAL CLEANING ACTIONS 2-7
3.0 DEMOLITION FOOTPRINT EXPOSED AREAS SOIL SAMPLING 3-1
4.0 PLUG AND ABANDON UNDERGROUND PIPING 4-1
5.0 INTERIM CAPPING 5-1
5.1 MAINTENANCE OF INTERIM CAP 5-1
6.0 REFERENCES 6-1

LIST OF FIGURES

FIGURE 2-1. 2008 POST-DEMOLITION SURVEY OF CONCRETE AND EXPOSED SOILS AREAS 2-9
FIGURE 3-1. CLEANING AND DEMOLITION STRUCTURE FOOTPRINT EXPOSED SOILS SAMPLE AREAS 3-2

FIGURE 3-2. DEMOLITION FOOTPRINT SOIL SAMPLING LOCATION MAP .3-3
FIGURE 4-1. UTILITIES GROUTED IN 2008 4-2
FIGURE 5-1. 2008 DEMOLITION INTERIM CAPS.....5-2

LIST OF APPENDICES

APPENDIX A WASTE SAMPLING AND CHARACTERIZATION SAMPLE RESULTS
APPENDIX B DEMOLITION FOOTPRINT EXPOSED SOIL SAMPLING RESULTS

SUMMARY REPORT FOR ASARCO EAST HELENA SMELTER 2008 INTERIM MEASURES WORK PLAN ADDENDUM

BLAST FURNACE FLUE AND MONIER FLUE CLEANING AND DEMOLITION AND DEMOLITION FOOTPRINT EXPOSED AREAS SOIL SAMPLING

1.0 INTRODUCTION

On May 8, 2008, Asarco submitted the 2008 Interim Measures Work Plan Addendum – Blast Furnace Flue and Monier Flue Cleaning and Demolition and Demolition Foot Print Exposed Areas Soil Sampling (Asarco, 2008a). The 2008 Interim Measures Addendum Work Plan contained specific procedures for addressing the following actions, in accordance with the RCRA Consent Decree.

- Pre-demolition cleaning of the Blast Furnace Flue and Monier Flue,
- Cleaning and demolition of the Blast Furnace Flue and Monier Flue,
- Collection of soil samples from the exposed area footprints associated with the 2008 Interim Measures Work Plan Addendum and 2008 Cleaning and Demolition Project Work Plan,
- Plugging and abandoning of underground utilities, and
- Interim capping of demolition areas.

On May 28, 2008, the United States Environmental Protection Agency (EPA) approved the 2008 Interim Measures Work Plan Addendum. Following Asarco's efforts that provided the required historic recordation and context narrative for the building and structures scheduled for demolition, EPA issued a notice on August 19, 2008 for Asarco to proceed with the

proposed actions. This summary report discusses the 2008 Interim Measures Work Plan Addendum for demolition activities that occurred at the Asarco East Helena Smelter.

2.0 2008 BLAST FURNACE FLUE AND MONIER FLUE CLEANING AND DEMOLITION OVERVIEW

On August 25, 2008, Asarco's Contractor, URS/Cleveland Wrecking Company (URS/CWC), mobilized to commence the pre-cleaning tasks set forth in the approved Interim Measures Work Plan Addendum. Over the next several months, Asarco successfully implemented each component of the Interim Measures Work Plan Addendum. Asarco's contractor concluded the final capping within the demolition area footprints by December 9, 2008, approximately three weeks ahead of schedule. The following sections of this summary report comprehensively discuss the completion of the various work plan components.

2.1 PRE-DEMOLITION CLEANING

The pre-demolition cleaning was conducted to reduce the potential for fugitive dust emissions during demolition activities and included work area preparation, initial dry removal of bulk solids, and moistening of building interiors. Work area preparation consisted of delineating an area that could be both easily contained and considered a cohesive unit with similar levels of contamination. The identified work areas included the Blast Furnace Flue and Monier Flue. Once these work areas were defined, Asarco's subcontractor (IRS Environmental) began removing the bulk solids. The bulk solid removal reduced the gross, dry accumulation of materials (lead, lead dust, lead debris) at accessible areas. This task was accomplished through the use of hand tools, small bobcat skid steers, and a trailer mounted "Hurricane" vacuum system with HEPA filtration. Waste was loaded via an airtight chute into double 6-mil mega bags and hauled within the bags to the CAMU Phase 2 Cell. On September 4, 2008, IRS Environmental began hauling Blast Furnace Flue and Monier Flue dust from pre-demolition cleaning efforts to the CAMU Phase 2 Cell. All pre-demolition cleaning was completed by October 1, 2008.

URS/CWC and IRS Environmental identified vehicle overpasses, flue transitions, and confined areas within the Blast Furnace Flue and Monier Flue that did not appear to be structurally sound and may have presented a health and safety hazard for field personnel.

These areas comprised a small percent of the entire Flue system. Safety concerns prevented the pre-cleaning of these areas and were instead, addressed during the demolition phase.

Upon completion of bulk solids removal from all accessible areas, URS/CWC initiated the pre-wetting and moistening of the interior of the Blast Furnace Flue and Monier Flue structures in preparation for demolition. The pre-wetting and moistening minimized airborne dust generation during above grade structure demolition. This task was accomplished through the use of water hoses and water trucks.

2.2 DEMOLITION

The demolition commenced within the buildings and structures identified in the 2008 Cleaning and Demolition Work Plan (Asarco, 2008b) before moving to the Blast Furnace Flue and Monier Flue. Prior to above grade structure demolition, a site inspection was conducted by Asarco personnel and URS/CWC to confirm that pre-demolition decontamination and cleaning were complete. Non-friable asbestos mastic coated some of the Blast Furnace Flue brick. The manner in which the mastic coated the brick, the non-friable nature of the mastic, and the successful measures implemented to minimize airborne hazards negated the necessity for its removal prior to demolition. The Blast Furnace Flue brick with mastic was handled using the same procedures for other concrete and masonry, as described below.

2.2.1 Dust Control

Asarco's contractor (URS/CWC) implemented the approved dust control plan submitted as part of the 2008 Interim Measures Work Plan Addendum (Asarco, 2008a) to manage dust during cleaning and demolition activities. The general requirements of the plan provided adequate resources to control the emission of visible fugitive nuisance dust. URS/CWC used the following administrative, engineering, and physical controls for dust suppression.

- Moistening of structure surfaces prior to and during demolition,
- Control of fugitive dust with water during demolition,
- Stopping work during high wind conditions (over 15 MPH),
- Quick and efficient structure demolition,
- Control of vehicle and equipment speeds, and
- Restriction of traffic to designated roads/corridors.

Prior to the demolition of structures, the gross accumulation of debris inside structures was removed and the interiors of the Blast Furnace Flue and Monier Flue were moistened. In addition, prior to demolition, the exteriors of all demolished structures were moistened using fire hoses by personnel on man-lifts. Once demolition of a structure commenced, personnel on man lifts continuously sprayed water on the structure and the surrounding air, which controlled fugitive dust emissions. The contractor effectively controlled fugitive dust emissions during demolition activities by knocking buildings into themselves, minimizing drop heights, and demolishing structures quickly and efficiently. Once structures were on the ground, water was continuously sprayed on the debris as the contractor sized, segregated, and loaded material into haul trucks.

During demolition activities, the contractor continuously swept haul roads and corridors surrounding the demolition area. Designated roads and corridors were used to size, load, and haul waste. These designated areas were continuously cleaned through the use of a mechanical sweeper.

2.2.2 Isolation Activities Before Demolition of Structures

Concurrent with pre-demolition cleaning activities, isolation activities were conducted to create a physical separation of the Blast Furnace Flue and Monier Flue from surrounding structures, piping, and items that were to remain in place. This task was accomplished through the use of excavators equipped with shear attachments and laborers using hand tools and cutting equipment. Piping, conduits, and structures that were accessible to an excavator were selectively sheared at marked isolation locations. Certain piping, conduits, and

structures that were not accessible to the excavator were cut free by personnel using hand saws and torch cutting equipment. These materials were staged behind working areas of primary excavators, where additional shears prepared it before being cleaned and loaded into haul trucks. Steel materials were taken to a recycling facility and materials that could not be recycled were hauled to the CAMU Phase 2 Cell.

2.2.3 Steel Structure Demolition

Although few steel structures were available during the demolition of the Blast Furnace Flue and Monier Flue, portions of the flues that connected other structures required steel structure removal. URS/CWC accomplished the steel structure demolition task through the use of track mounted excavators equipped with specialty attachments (shears, breakers, and grapples) to structurally remove, bay by bay, various structural members. Steel columns were removed without damaging the Blast Furnace Flue or Monier Flue. All removed steel material was staged behind working areas of primary excavators, where additional shears prepared it before being cleaned and loaded into haul trucks. All recyclable steel was taken to a recycling facility.

2.2.4 Concrete/Masonry Structure Demolition

Concrete/masonry demolition constituted the majority of the demolition work for the Blast Furnace Flue and Monier Flue. URS/CWC accomplished the concrete/masonry demolition task through the use of several 100,000 lb excavators, equipped with breakers, and a track loader. Starting at one end of the Flue system, URS/CWC sequentially demolished the Flue structure in a top down approach. The roof of the Flue was first demolished to allow debris to fall to the ground within the Flue walls. The walls of the structure were then collapsed allowing the debris to fall within the footprint of the structure. Utilizing a track dozer, the broken concrete and brick was loaded into haul trucks for placement into the CAMU Phase 2 Cell.

The few areas of the Blast Furnace Flue and Monier Flue that were not pre-cleaned (vehicle overpasses, flue transitions, and confined areas) were treated with extreme caution during

demolition. Water was applied liberally to these areas and demolition was conducted slowly and carefully to minimize fugitive dust emissions.

2.2.5 Demolition Material Stockpiling

As steel structure and concrete/masonry demolition of the Blast Furnace Flue and Monier Flue progressed, the majority of the material was loaded directly into haul trucks and transported to the CAMU Phase 2 Cell. Any necessary sizing of CAMU bound demolition debris took place at the demolition site. Recyclable materials were hauled and stockpiled in designated material staging and processing areas located within the demolition area footprints, sized to meet the requirements of the final disposition location, and cleaned. Sized and cleaned recyclable materials were loaded into haul trucks and transported to the recycling facility.

2.2.6 Debris Transport

Measures were taken by URS/CWC to ensure that the transport of demolition waste debris did not generate dust or spread waste debris outside the limits of the loading area and the final CAMU Phase 2 Cell placement area. URS/CWC utilized water trucks equipped with fire hoses to keep debris moist during the demolition and loading process. This operation minimized airborne dust during the loading operation and was the first step in prevention of airborne dust during transport. All trucks used for the transport of waste to the CAMU were equipped with sealed tail gates, which were closed at all times during transport, ensuring that debris was not released outside the limits of the loading and placement areas. The top of the waste was lightly misted with water at the loading site, adding a final barrier/binder to the debris before being transported to the CAMU Phase 2 Cell. Transport vehicles were limited to a maximum speed of 10 miles per hour while both on site and during transport to the CAMU Phase 2 Cell.

The transport of waste on-site followed prescribed paths, which were determined during the course of demolition and discussed every morning at daily safety meetings. These designated haul routes were maintained to mitigate dust and debris migration and prevent the spread of

contamination. Maintenance of haul routes included daily inspection to ensure debris was not being released, wetting of haul routes on a frequent basis to prevent the generation of dust from vehicular traffic, and the use of a street sweeper to clean the haul routes of accumulated dust and debris. All debris and dust sweepings were dumped on-site and handled as demolition debris for placement in the CAMU Phase 2 Cell.

2.2.7 Waste Sampling and Characterization

Representative samples of demolition waste being hauled from the Blast Furnace Flue and Monier Flue to the CAMU Phase 2 Cell were collected and analyzed to better characterize the waste. The follow tasks were conducted to obtain representative samples of waste and to characterize the waste being hauled to the CAMU Phase 2 Cell.

- Description of payload inside haul trucks,
- Photos of truck payload,
- Weight of truck payload,
- Grab samples of wood, dirt, dust, brick, and concrete materials, and
- Laboratory analyses of collected grab samples.

The contents and weight of each haul truck were recorded prior to the haul truck leaving the smelter facility. Truck weights are included in Appendix A. Photos characterizing waste hauled from the Blast Furnace Flue and Monier Flue are included in Appendix C of the 2008 Construction Report for Asarco East Helena Plant, Corrective Action Management Unit (CAMU) – Phase II Cell, Construction Project. Waste characterization determined the types of waste being placed in the CAMU Phase 2 Cell, ensured waste had been reduced in size appropriately prior to being loaded, and verified that waste had been properly moistened prior to leaving the Smelter site.

The Blast Furnace Flue and Monier Flue demolition waste mainly consisted of brick. However, a mixture of wood, metal, concrete, broken brick debris, and soil was also generated. A large quantity of soil was generated towards the end of the Flue demolition

during the excavation of soil three feet below grade in the Flue footprint. A total of 607 truck loads weighing approximately 11,260 tons were hauled from the Blast Furnace Flue and Monier Flue to the CAMU Phase 2 Cell.

A total of 29 samples were collected and analyzed from waste generated from Blast Furnace Flue and Monier Flue demolition. Waste was sampled at an average sampling interval of 1 in 20.93 trucks. Icy conditions during the hauling of waste from the Monier Flue did not allow for safe sampling of the two prescribed loads. The collection of these two additional samples would have generated an average sampling interval of 1 in 19.58 trucks. Arsenic concentrations from the samples collected ranged from 271 to 17,200 mg/kg and averaged 3,710 mg/kg. Sample 0809-CAMU-147, collected from the Blast Furnace Flue (consisting of flue dust, soil, and broken brick debris) produced the highest concentration of arsenic (17,200 mg/kg) of all the samples collected. Cadmium concentrations from the samples collected ranged from 163 to 86,900 mg/kg and averaged 9,350 mg/kg. Sample 0809-CAMU-150, collected from the Monier Flue (consisting of broken concrete debris) produced the highest concentrations of cadmium and zinc (86,900 and 151,000 mg/kg, respectively) of all the samples collected. Copper concentrations from the samples collected ranged from 152 to 22,200 mg/kg and averaged 3,471 mg/kg. Mercury concentrations from the samples collected ranged from 9 to 700 mg/kg and averaged 235 mg/kg. Lead concentrations from the samples collected ranged from 753 to 49,400 mg/kg and averaged 20,223 mg/kg. Selenium concentrations from the samples collected ranged from 7 to 1,450 mg/kg and averaged 157 mg/kg. Zinc concentrations from the samples collected ranged from 836 to 151,000 mg/kg and averaged 20,055 mg/kg. The sample results collected under the Work Plan are included in Appendix A.

2.3 FINAL CLEANING ACTIONS

The final cleaning of concrete covered demolition footprint areas involved a three-phased approach. First, the concrete footprint underwent a rough cleaning using conventional scraping and shoveling methods to remove solid residues that accumulated during the demolition process. Second, the concrete footprint was mechanically swept to remove

surface materials that were not completely removed during scraping and shoveling. Finally, the concrete footprint was cleaned using a high velocity, truck-mounted vacuum to remove any fine material.

Once demolition was complete and all debris had been removed, a final inspection of the floor footprint of the Blast Furnace Flue and Monier Flue was conducted. This visual survey was conducted to catalog any area within the structure footprint where concrete was not present and underlying soils may have been exposed to flue dust or other metal-bearing materials. This survey also documented the condition of concrete within the structures and floors. Figure 2-1 shows a plan view of the demolished structures, and identifies areas of exposed soils, areas covered with sound concrete, and areas where broken or severely cracked concrete exists. This survey was used to determine areas that needed to be covered with the interim cap.

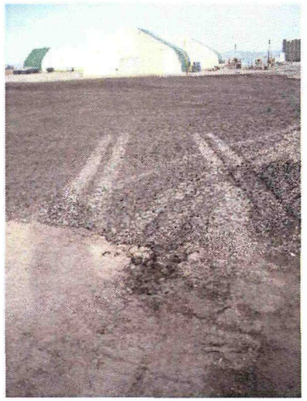

1. BROKEN CONCRETE

4. BROKEN CONCRETE

7. BROKEN ASPHALT

2. EXPOSED DIRT IN OLD BUILDING FOOTING

5. BROKEN CONCRETE

8. EXPOSED DIRT AND BROKEN CONCRETE

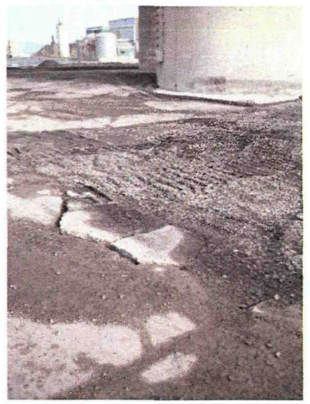

3. BROKEN CONCRETE

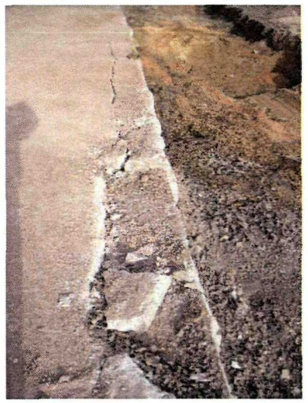

6. BROKEN CONCRETE

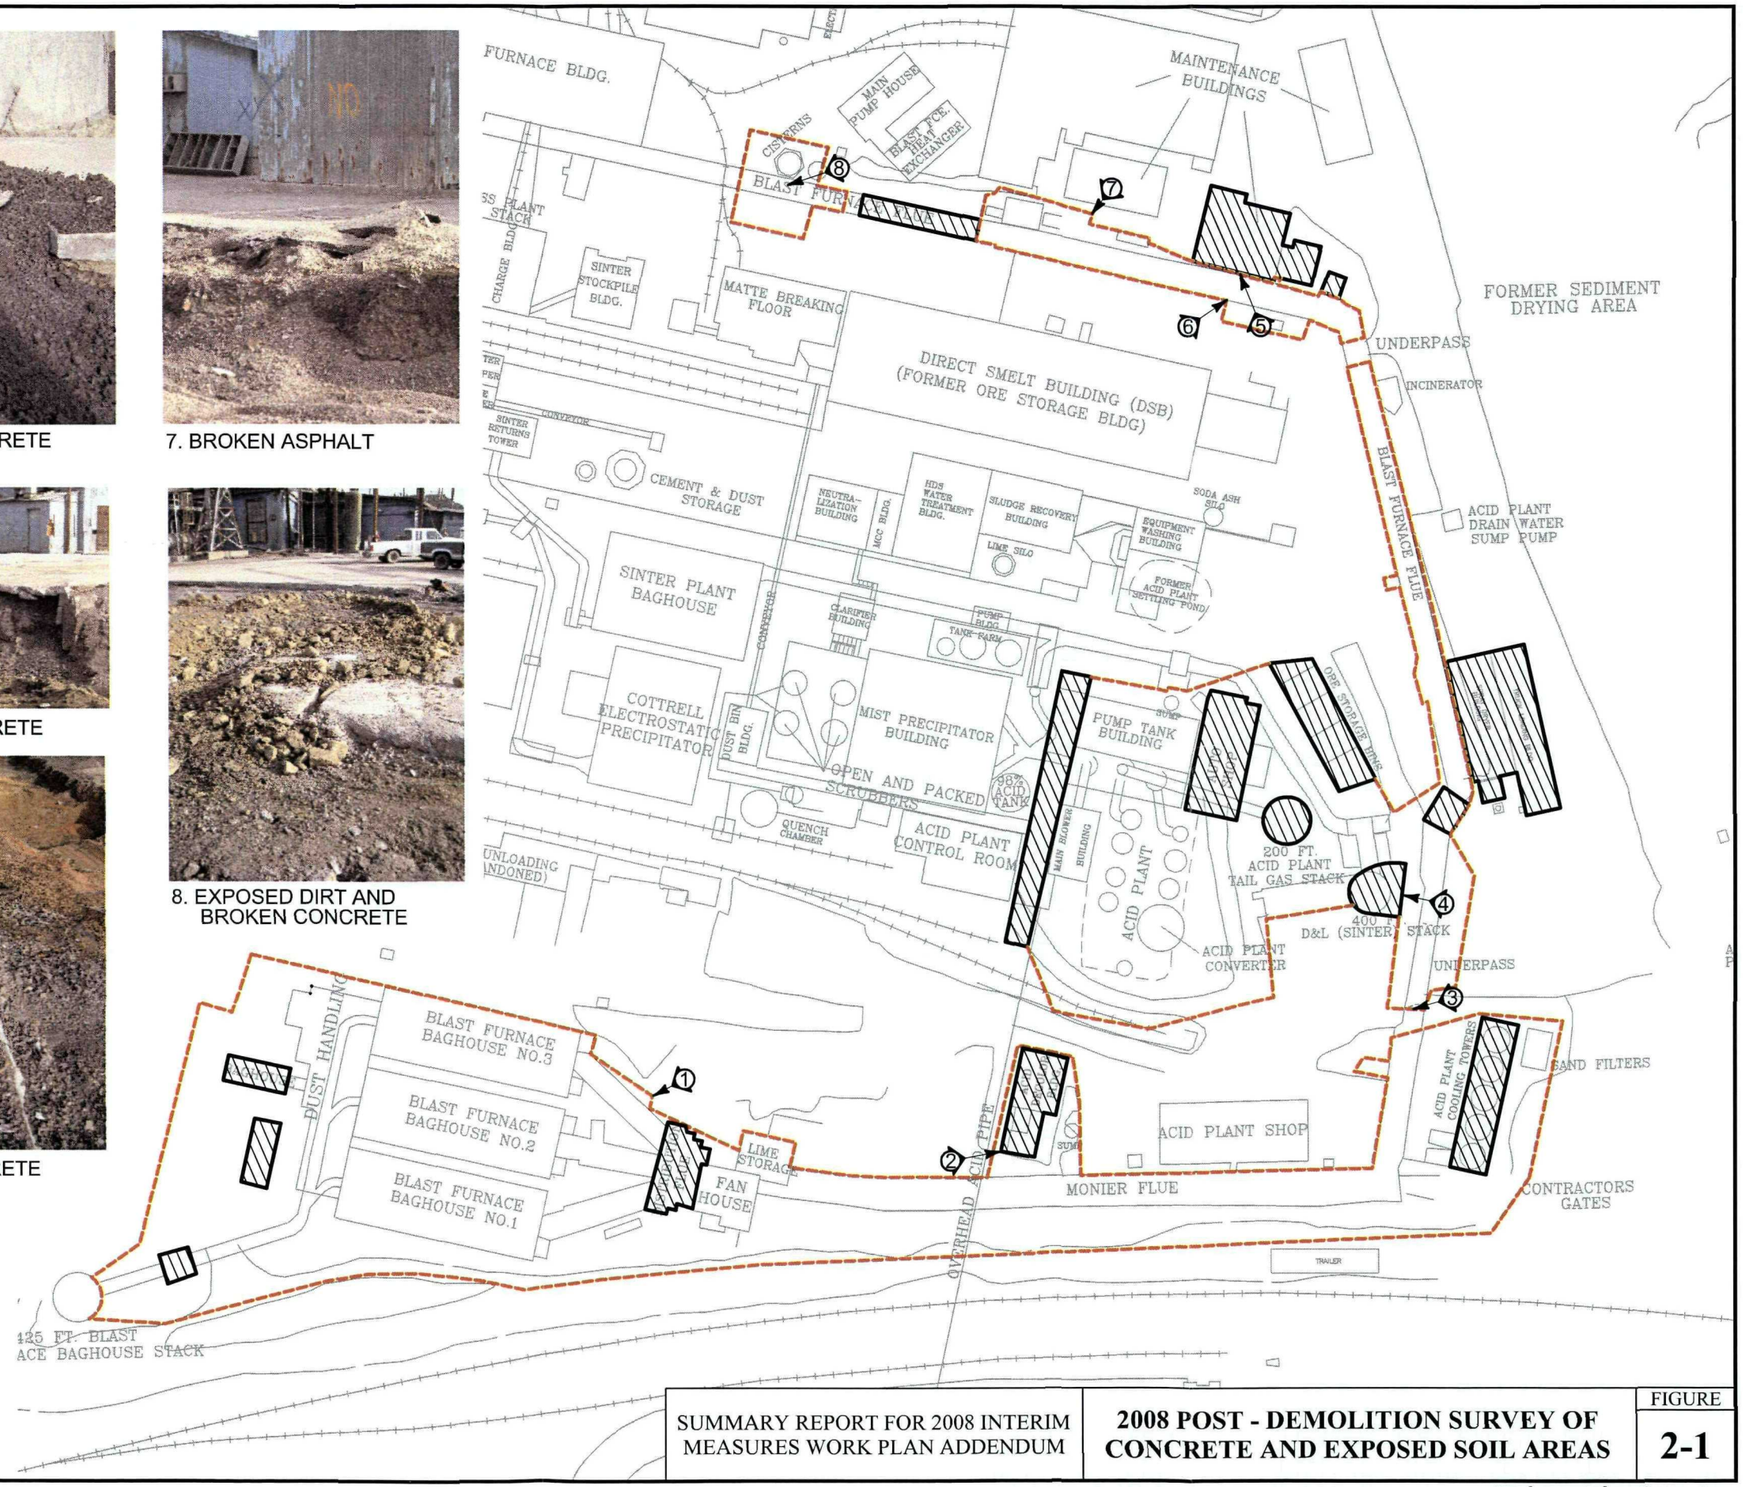

SCALE

0 (In Feet) 100

NORTH

LEGEND

AREA COVERED WITH EXPOSED SOIL

AREA COVERED WITH CONCRETE

PHOTO VIEW POINT LOCATION AND ANGLE WITH PHOTO NUMBER

SUMMARY REPORT FOR 2008 INTERIM MEASURES WORK PLAN ADDENDUM	2008 POST - DEMOLITION SURVEY OF CONCRETE AND EXPOSED SOIL AREAS	FIGURE 2-1

UPDATE TIME: 9:13 AM
I:\ABORSKY\HFI\20090217\I:\LAND PROJECTS\105403\DWG\105403H003.DWG

Hydrometrics, Inc.
Consulting Scientists and Engineers

3.0 DEMOLITION FOOTPRINT EXPOSED AREAS SOIL SAMPLING

The 2008 Interim Measures Work Plan Addendum required Asarco to conduct demolition footprint exposed area soil sampling in unpaved areas of structures that were demolished in 2008. Figure 3-1 illustrates the location of known exposed soils (identified in the field and mapped in 2007) and soil sample locations collected in 2008.

Prior to conducting exposed soil sampling, visually obvious dust (indicated by dark gray or black color and fine-grained in texture) within the demolition footprint areas was removed. This included the removal of three feet of soil from the footprint of the Blast Furnace Flue and Monier Flue, as shown on Figure 3-1. In addition, subsurface soils in a section of the Blast Furnace Flue, shown on Figure 3-1 were excavated to depths of up to 12 feet below grade. This soil removal was conducted to eliminate the visual presence of brick and visibly contaminated soils within this area. All excavated soils were hauled to the CAMU Phase 2 Cell.

Upon completion of demolition and final cleaning actions, Hydrometrics conducted the demolition footprint exposed areas soil sampling. The soil sampling was conducted from October 23, 2008 to October 28, 2008 in 17 locations as shown on the Figure 3-2. Test pit logs for each of the 17 locations are outlined in Table B-1 in Appendix B. Samples were collected in accordance with the work plan sampling procedures and standard operating procedures. Surface soil samples (0"-4") consisted of a composite of five samples collected from the sample areas and were collected using a hand shovel. The remaining soil samples were collected from the bucket of an excavator at the specified sample depth interval. All samples were stored in Ziploc bags, clearly marked with the sample information, and archived for analysis. Appendix B outlines the sampling locations and sample intervals.

SUMMARY REPORT FOR 2008 INTERIM MEASURES WORK PLAN ADDENDUM	CLEANING AND DEMOLITION STRUCTURE FOOTPRINT EXPOSED SOILS SAMPLE AREAS	FIGURE 3-1

UPDATE TIME: 9:26 AM
LTABORSKY\HEL\20090217\I:\LAND PROJECTS\105403\DWG\105403H001.DWG

Hydrometrics, Inc.
Consulting Scientists and Engineers

Summary Report For 2008 Interim Measures Work Plan Addendum	DEMOLITION FOOTPRINT SOIL SAMPLING LOCATION MAP	FIGURE 3-2

K:\PROJECT\7054\TestPitGIS\TP_GPS_Survey.mxd

4.0 PLUG AND ABANDON UNDERGROUND PIPING

The underground piping present within the footprint of cleaning and demolition areas was plugged and sealed in place utilizing flowable fill. Figure 4-1 shows the underground utilities that were grouted in 2008, which included a section of the sanitary sewer system, the abandoned Wilson Irrigation ditch, the Upper Lake acid plant water system, and several sections of the plant water system.

Flowable fill or control density fill (CDF) was used as a low strength, self-consolidating fill material for confined spaces. CDF is characterized by a high maximum slump of 8 inches and consists of Portland Cement, aggregates, water, and fly ash. Actual mix proportions and flow characteristics were determined by the producer of the CDF to meet site conditions. In larger conduits having a slope, flowable fill was introduced by filling the inlet of the underground utility until a steady flow of flowable fill exited the connection pipe outlet. This procedure was performed on the sanitary sewer system and the abandoned Wilson Irrigation ditch. On smaller conduits and large conduits with little to no slope, flowable fill was introduced using pressure. Flowable fill was poured from mixing trucks into a concrete pump truck, from which it was pumped into the underground utility at pressures up to 100 psi. This procedure was performed on the Upper Lake acid plant water system and the plant water system. All piping was flushed with water and blown out with air prior to grouting procedures. An anti-bacterial agent (bleach) was added to the water used to flush out the sanitary sewer system. Water used for this procedure was collected and routed to the Asarco HDS water treatment facility.

Grouting of the abandoned sanitary sewer began on October 23, 2008. Water introduced into the sanitary sewer was pumped out of the most downgradient manhole into a tank and transported to the Asarco HDS water treatment facility. Only a short portion of the sanitary sewer was initially grouted to verify the grout mix would adequately fill the pipe. Once it was determined the grout mix was adequate, the remaining 1,100 linear feet of the sanitary sewer (12-inch pipes) was grouted on October 30, 2008. Grout was poured from the mixing

SUMMARY REPORT FOR 2008 INTERIM MEASURES WORK PLAN ADDENDUM	UTILITIES GROUTED IN 2008	FIGURE 4-1

UPDATE TIME: 9:13 AM
LTABORSKY\HEL\20090217\I:\LAND PROJECTS\105403\DWG\105403H002.DWG

Hydrometrics, Inc.
Consulting Scientists and Engineers

truck into the manhole at one end of the sewer until visible grout was flowing out of the pipe at the next connecting manhole. This procedure was repeated at each accessible manhole until the entire sewer system was full. Manholes were then filled with grout and the covers placed back on the manholes. Approximately 40 cubic yards (cy) of grout was used to seal the sanitary sewer. The calculated volume of grout needed to fill this section of pipe was 32 cy, with the remaining 8 cy filling up the manholes.

On October 28, 2008, the abandoned Wilson Irrigation Ditch was grouted using the same technique previously described for the sanitary sewer pipe. Approximately 130 cy of grout was used to fill the Wilson Irrigation Ditch from Upper Lake to the Hopto Unloading Bins. Since the actual pipe dimension and length of the abandoned Wilson Ditch were unknown, an anticipated quantity of grout was not calculated. Manhole covers were replaced on the access manholes to abandoned Wilson ditch once grouting was complete.

On October 31, 2008, URS/CWC began grouting the water lines in the acid plant area. At first, a blockage in the piping prevented grout from filling the entire pipe. Approximately 17 cy of grout were pumped into these pipes at this time. URS/CWC and Hydrometrics personnel consulted additional plant drawings located in the Asarco East Helena Engineering Office to determine the location of any valves that may have been closed. Several valves were located and opened. In addition to opening valves, access locations along the pipe were excavated by the contractor to prepare the system for pressure grouting. Flanges were welded onto the pipes at several locations to allow a pump truck to pump grout into the acid plant water lines. Water was flushed through the system to ensure unobstructed flow through the pipes. Water was pumped out of the pipes and routed to the Asarco HDS water treatment facility. Pressure grouting of the acid plant water lines continued on November 7, 2008, with approximately 120 cy of grout used to fill the two 18- to 24-inch Upper Lake Acid Plant Water Lines. The calculated volume of grout needed to fill these two lines was approximately 116 cy, with the remaining 4 cy being used to fill the bottoms of the excavated holes along the length of the pipes.

The remaining 6-inch plant water lines near the former Blast Furnace Flue and Baghouse were pressure grouted on November 7 and 11, 2008 and used approximately 11 cubic yards of grout. Flanges were welded on the pipes and water was run through the lines to ensure unobstructed flow. The pipes were then pressure grouted using a cement pump truck.

5.0 INTERIM CAPPING

Upon completion of the demolition operations, final cleaning actions, demolition footprint soil sampling, and plugging and abandoning underground piping; URS/CWC removed all debris and items from slabs that could possibly penetrate the interim cover system. On-site fumed slag was placed over demolished areas filling in low areas to create positive drainage. The fumed slag was graded and rolled to create a smooth surface for liner placement. The interim liner system, consisting of a 10-oz geotextile covered by a 24-mil RPE geomembrane liner was placed on top of the rolled fumed slag. Figure 5-1 shows the locations where the interim liner was placed in 2008.

The geotextile and geomembrane were laid, seamed, and secured as specified in the projects construction documents. Additionally, sandbags were placed continuously along the edges and intermittently within the center liner area to prevent the liner from being picked up by wind uplift or other forces.

5.1 MAINTENANCE OF INTERIM CAP

Periodic inspections of the interim cap continue to be conducted to ensure the interim cap systems were performing adequately and to identify problems and provide proper maintenance of interim cap systems. The inspection program involved three types of inspections: 1) informal inspections, 2) periodic technical inspections, and 3) special inspections after extreme events.

On-site personnel perform informal inspections as part of their normal duties. Periodic technical inspections are performed monthly to document the condition of the cap components. No special inspections were conducted during 2008.

The inspections of the cover systems involve walking the entire site in a systematic fashion to ensure a comprehensive review. The inspector records the location of any problems or deficiencies and documents the problem on appropriate reporting forms with a

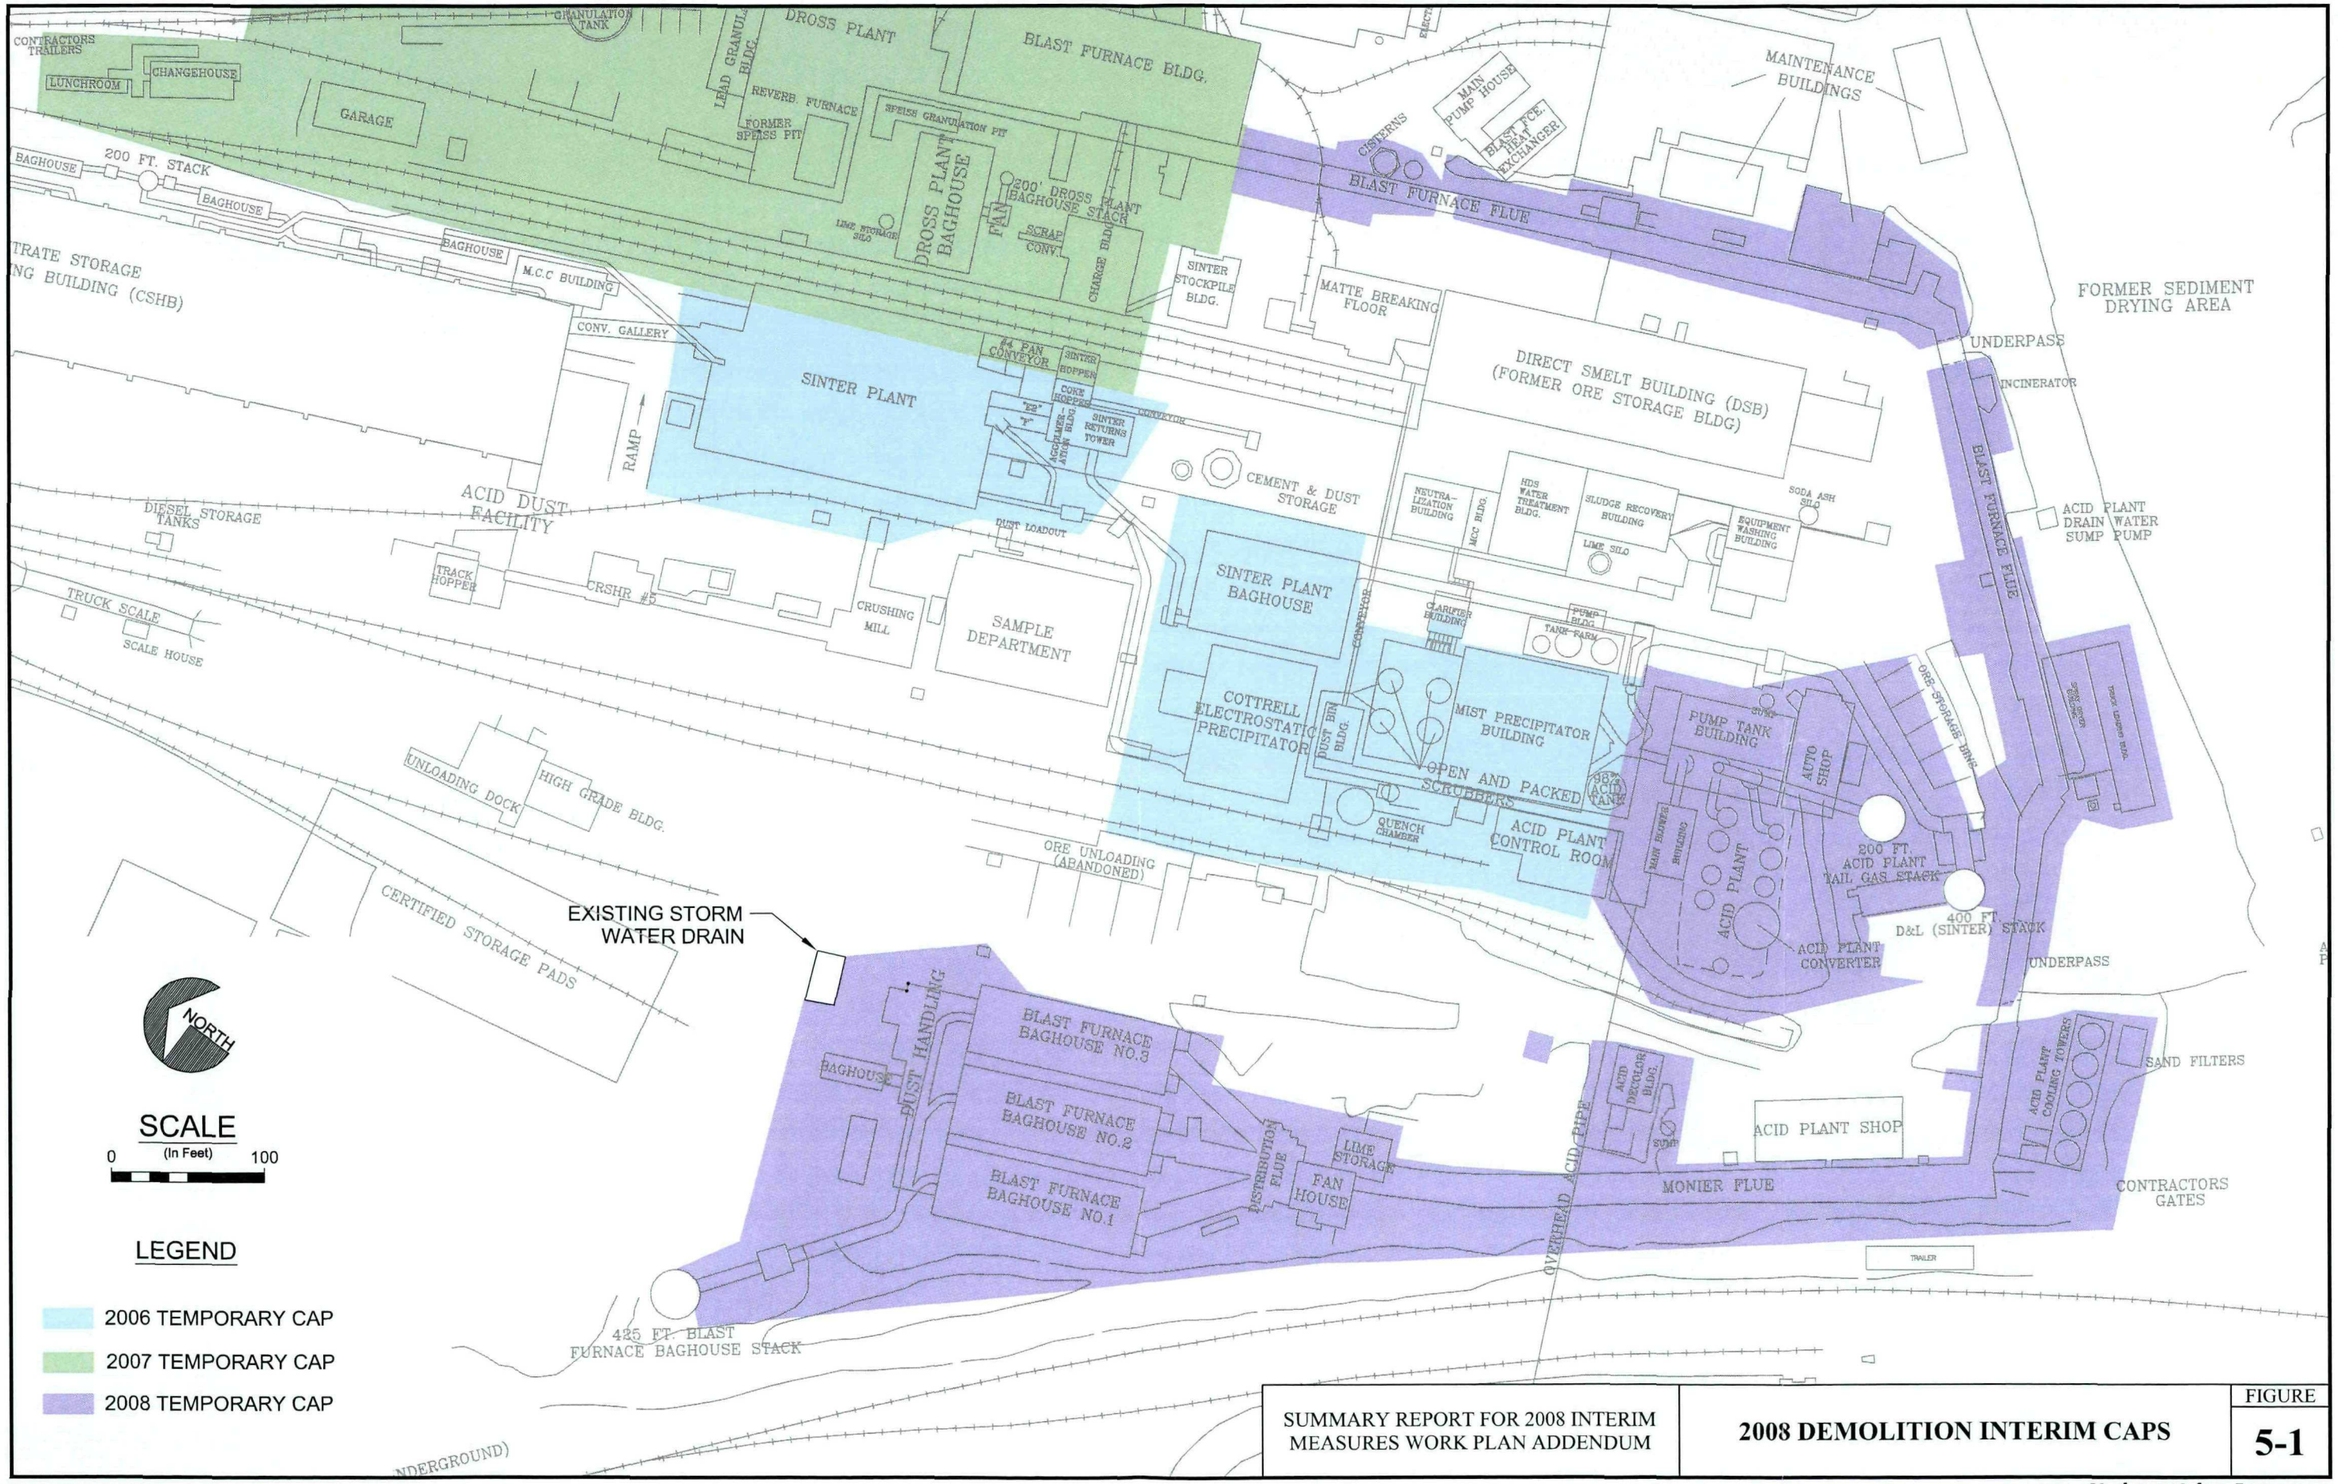

SUMMARY REPORT FOR 2008 INTERIM MEASURES WORK PLAN ADDENDUM	2008 DEMOLITION INTERIM CAPS	FIGURE 5-1

UPDATE TIME: 9:13 AM
I:\ABORSKY\HFI\20090217\I:\LAND PROJECTS\105403\DWG\105403H004.DWG

Hydrometrics, Inc.
Consulting Scientists and Engineers

complete description of the affected area.

During the month of December 2008, strong winds created suction on the leeward portion of the liner northeast of the acid plant and sinter plant stack causing the liner to tear and expose the underlying slag. On January 2, 2009, the exposed liner in this area was replaced and temporarily reinforced with tied tires and sand bags until the installer could make repairs. On January 14-16, 2009 the liner installer secured and anchored the liner with flexible wooden slats and bolts at the base of each stack. Torn pieces of liner were replaced and sewn to competent liner sections. Additional sand bags and tires were also placed in this area to minimize liner disturbance from wind channeling through the stack openings.

6.0 REFERENCES

Asarco, 2008a. Asarco East Helena Smelter 2008 Interim Measures Work Plan Addendum – Blast Furnace Flue and Monier Flue Cleaning and Demolition and Demolition Foot Print Exposed Areas Soil Sampling. May 2008.

Asarco, 2008b. 2008 Cleaning and Demolition Work Plan Asarco East Helena Plant – Introduction, Project Summary, and Reporting and 2008 Work Plan. May 2008.

Hydrometrics, 2009. 2008 Construction Report for the Asarco East Helena Plant, Corrective Action Management Unit (CAMU) – Phase II Cell, Construction Project. January 2009.

APPENDIX A

WASTE SAMPLING AND CHARACTERIZATION SAMPLE RESULTS

TRUCK WEIGHT TABLE

APPENDIX A
TRUCK WEIGHT SUMMARY

Date	Time	Truck ID	Weight	Tare Weight	Material Weight	Load ID	Load #	Waste Origin	Sample Taken
9/25/2008	15:05	510090	51500	27220	24280	0925-80	1866	Blast Furnace Flue	
9/25/2008	15:07	510092	51060	27360	23700	0925-81	1867	Blast Furnace Flue	
9/25/2008	15:13	510335	56840	26120	30720	0925-82	1868	Blast Furnace Flue	
9/25/2008	15:19	510090	52260	27220	25040	0925-83	1869	Blast Furnace Flue	
9/25/2008	15:22	510092	55160	27360	27800	0925-85	1871	Blast Furnace Flue	
9/25/2008	15:33	510335	53280	26120	27160	0925-86	1872	Blast Furnace Flue	
9/25/2008	15:34	510090	53000	27220	25780	0925-87	1873	Blast Furnace Flue	
9/25/2008	15:42	510092	58320	27360	30960	0925-88	1874	Blast Furnace Flue	
9/25/2008	15:50	510335	56280	26120	30160	0925-90	1876	Blast Furnace Flue	0809-CAMU-125
9/25/2008	16:00	510090	59400	27220	32180	0925-91	1877	Blast Furnace Flue	
9/25/2008	16:05	510092	63840	27360	36480	0925-92	1878	Blast Furnace Flue	
9/25/2008	16:11	510335	59560	26120	33440	0925-93	1879	Blast Furnace Flue	
9/25/2008	16:13	510090	49640	27220	22420	0925-94	1880	Blast Furnace Flue	
9/25/2008	16:23	510335	54680	26120	28560	0925-95	1881	Blast Furnace Flue	
9/25/2008	16:27	510090	56280	27220	29060	0925-96	1882	Blast Furnace Flue	
9/25/2008	16:37	510335	42880	26120	16760	0925-97	1883	Blast Furnace Flue	
9/25/2008	16:46	510090	46180	27220	18960	0925-98	1884	Blast Furnace Flue	
9/26/2008	8:34	520990	88460	35540	52920	0926-7	1891	Blast Furnace Flue	
9/26/2008	8:40	524547	78280	35000	43280	0926-8	1892	Blast Furnace Flue	
9/26/2008	8:52	520990	76920	35540	41380	0926-12	1896	Blast Furnace Flue	
9/26/2008	8:58	524547	85340	35000	50340	0926-13	1897	Blast Furnace Flue	
9/26/2008	13:24	520990	84760	35540	49220	0926-50	1934	Blast Furnace Flue	
9/26/2008	13:29	524547	78180	35000	43180	0926-51	1935	Blast Furnace Flue	
9/26/2008	13:40	520990	80320	35540	44780	0926-52	1936	Blast Furnace Flue	
9/26/2008	13:49	524547	81960	35000	46960	0926-53	1937	Blast Furnace Flue	
9/26/2008	13:59	520990	84640	35540	49100	0926-54	1938	Blast Furnace Flue	0809-CAMU-128
9/26/2008	14:09	524547	70840	35000	35840	0926-55	1939	Blast Furnace Flue	
9/26/2008	14:17	510090	52840	27220	25620	0926-56	1940	Blast Furnace Flue	
9/26/2008	14:20	510335	53020	26120	26900	0926-57	1941	Blast Furnace Flue	
9/26/2008	14:31	520990	87580	35540	52040	0926-58	1942	Blast Furnace Flue	
9/26/2008	14:41	524547	75140	35000	40140	0926-59	1943	Blast Furnace Flue	
9/26/2008	14:50	510090	58880	27220	31660	0926-60	1944	Blast Furnace Flue	
9/26/2008	15:17	510335	53100	26120	26980	0926-65	1949	Blast Furnace Flue	
9/26/2008	15:28	524547	82980	35000	47980	0926-66	1950	Blast Furnace Flue	
9/26/2008	15:29	510335	42400	26120	16280	0926-67	1951	Blast Furnace Flue	
9/26/2008	16:24	520990	81800	35540	46260	0926-68	1952	Blast Furnace Flue	
9/26/2008	16:28	524547	74380	35000	39380	0926-69	1953	Blast Furnace Flue	
9/26/2008	16:31	510335	45820	26120	19700	0926-70	1954	Blast Furnace Flue	
9/26/2008	16:39	520990	74340	35540	38800	0926-71	1955	Blast Furnace Flue	
9/26/2008	16:44	524547	78240	35000	43240	0926-72	1956	Blast Furnace Flue	
9/26/2008	16:46	510335	48060	26120	21940	0926-73	1957	Blast Furnace Flue	
9/27/2008	8:15	520990	73940	35540	38400	0927-1	1958	Blast Furnace Flue	
9/27/2008	8:23	524547	78140	35000	43140	0927-2	1959	Blast Furnace Flue	
9/27/2008	8:33	520990	76700	35540	41160	0927-3	1960	Blast Furnace Flue	0809-CAMU-129
9/27/2008	8:43	524547	76620	35000	41620	0927-4	1961	Blast Furnace Flue	
9/27/2008	8:50	520990	77680	35540	42140	0927-5	1962	Blast Furnace Flue	
9/27/2008	9:01	524547	77120	35000	42120	0927-6	1963	Blast Furnace Flue	
9/27/2008	9:08	524545	77860	36000	41860	0927-7	1964	Blast Furnace Flue	
9/27/2008	9:19	520990	78080	35540	42540	0927-8	1965	Blast Furnace Flue	
9/27/2008	9:43	524547	75180	35000	40180	0927-9	1966	Blast Furnace Flue	
9/27/2008	9:54	520990	77480	35540	41940	0927-10	1967	Blast Furnace Flue	
9/27/2008	9:59	524545	75580	36000	39580	0927-11	1968	Blast Furnace Flue	
9/27/2008	10:12	524547	80100	35000	45100	0927-12	1969	Blast Furnace Flue	
9/27/2008	10:21	520990	79880	35540	44340	0927-13	1970	Blast Furnace Flue	
9/27/2008	10:40	524545	85540	36000	49540	0927-14	1971	Blast Furnace Flue	
9/27/2008	10:47	524547	82200	35000	47200	0927-15	1972	Blast Furnace Flue	
9/27/2008	10:57	520990	79300	35540	43760	0927-16	1973	Blast Furnace Flue	
9/27/2008	11:24	524545	78780	36000	42780	0927-17	1974	Blast Furnace Flue	
9/27/2008	11:30	524547	79140	35000	44140	0927-18	1975	Blast Furnace Flue	
9/27/2008	11:33	520990	79960	35540	44420	0927-19	1976	Blast Furnace Flue	
9/27/2008	11:42	524545	79500	36000	43500	0927-20	1977	Blast Furnace Flue	
9/27/2008	11:56	524547	80020	35000	45020	0927-21	1978	Blast Furnace Flue	
9/27/2008	12:00	520990	76740	35540	41200	0927-22	1979	Blast Furnace Flue	
9/27/2008	12:11	524545	81220	36000	45220	0927-23	1980	Blast Furnace Flue	0809-CAMU-130
9/27/2008	12:21	524547	79620	35000	44620	0927-24	1981	Blast Furnace Flue	
9/27/2008	12:24	520990	79040	35540	43500	0927-25	1982	Blast Furnace Flue	
9/27/2008	12:31	524545	78760	36000	42760	0927-26	1983	Blast Furnace Flue	
9/27/2008	12:51	524547	76960	35000	41960	0927-27	1984	Blast Furnace Flue	
9/27/2008	12:55	520990	74920	35540	39380	0927-28	1985	Blast Furnace Flue	
9/30/2008	16:20	524545	78000	36000	42000	0930-38	2087	Blast Furnace Flue	
9/30/2008	16:40	524545	92620	36000	56620	0930-39	2088	Blast Furnace Flue	0809-CAMU-135
10/1/2008	7:47	524545	92060	36000	56060	1001-1	2089	Blast Furnace Flue	
10/1/2008	7:50	510090	51520	27220	24300	1001-2	2090	Blast Furnace Flue	
10/1/2008	7:54	510335	51120	26120	25000	1001-3	2091	Blast Furnace Flue	
10/1/2008	8:10	524545	79020	36000	43020	1001-4	2092	Blast Furnace Flue	
10/1/2008	8:12	510335	49280	26120	23160	1001-5	2093	Blast Furnace Flue	
10/1/2008	8:17	510090	50200	27220	22980	1001-6	2094	Blast Furnace Flue	
10/1/2008	8:25	510335	50900	26120	24780	1001-7	2095	Blast Furnace Flue	
10/1/2008	8:29	524545	40380	36000	4380	1001-8	2096	Blast Furnace Flue	
10/1/2008	8:31	510090	55200	27220	27980	1001-9	2097	Blast Furnace Flue	
10/1/2008	8:40	510335	50640	26120	24520	1001-10	2098	Blast Furnace Flue	

APPENDIX A
TRUCK WEIGHT SUMMARY

Date	Time	Truck ID	Weight	Tare Weight	Material Weight	Load ID	Load #	Waste Origin	Sample Taken
10/1/2008	8:44	510090	55840	27220	28620	1001-11	2099	Blast Furnace Flue	
10/1/2008	8:50	524545	82080	36000	46080	1001-12	2100	Blast Furnace Flue	
10/1/2008	8:56	510335	48200	26120	22080	1001-13	2101	Blast Furnace Flue	
10/1/2008	8:58	510090	53920	27220	26700	1001-14	2102	Blast Furnace Flue	
10/1/2008	9:07	524545	87600	36000	51600	1001-16	2104	Blast Furnace Flue	
10/1/2008	9:10	510335	50540	26120	24420	1001-17	2105	Blast Furnace Flue	
10/1/2008	9:12	510090	51240	27220	24020	1001-18	2106	Blast Furnace Flue	
10/1/2008	9:28	524545	85680	36000	49680	1001-19	2107	Blast Furnace Flue	
10/1/2008	9:29	510335	49860	26120	23740	1001-20	2108	Blast Furnace Flue	
10/1/2008	9:32	510090	50700	27220	23480	1001-21	2109	Blast Furnace Flue	0809-CAMU-136
10/1/2008	9:43	524545	80540	36000	44540	1001-22	2110	Blast Furnace Flue	
10/1/2008	9:46	510335	47880	26120	21760	1001-23	2111	Blast Furnace Flue	
10/1/2008	9:49	510090	49300	27220	22080	1001-24	2112	Blast Furnace Flue	
10/1/2008	9:58	510335	43140	26120	17020	1001-25	2113	Blast Furnace Flue	
10/1/2008	9:59	524545	41760	36000	5760	1001-26	2114	Blast Furnace Flue	
10/1/2008	10:03	510090	46420	27220	19200	1001-27	2115	Blast Furnace Flue	
10/1/2008	10:10	510335	49280	26120	23160	1001-28	2116	Blast Furnace Flue	
10/1/2008	10:14	524545	42980	36000	6980	1001-29	2117	Blast Furnace Flue	
10/1/2008	10:15	510090	52860	27220	25640	1001-30	2118	Blast Furnace Flue	
10/1/2008	10:22	510335	48980	26120	22860	1001-31	2119	Blast Furnace Flue	
10/1/2008	10:28	510090	47540	27220	20320	1001-32	2120	Blast Furnace Flue	
10/1/2008	10:30	524545	44800	36000	8800	1001-33	2121	Blast Furnace Flue	
10/1/2008	10:35	510335	45980	26120	19860	1001-34	2122	Blast Furnace Flue	
10/1/2008	10:40	510090	49980	27220	22760	1001-35	2123	Blast Furnace Flue	
10/1/2008	10:45	524545	45200	36000	9200	1001-36	2124	Blast Furnace Flue	
10/1/2008	10:48	510335	48420	26120	22300	1001-37	2125	Blast Furnace Flue	
10/1/2008	10:51	510090	47600	27220	20380	1001-38	2126	Blast Furnace Flue	
10/1/2008	11:02	510090	52940	27220	25720	1001-39	2127	Blast Furnace Flue	
10/1/2008	11:07	510335	49880	26120	23760	1001-40	2128	Blast Furnace Flue	
10/1/2008	11:08	524545	45100	36000	9100	1001-41	2129	Blast Furnace Flue	
10/1/2008	11:17	510090	57380	27220	30160	1001-42	2130	Blast Furnace Flue	0809-CAMU-137
10/1/2008	11:25	510335	56320	26120	30200	1001-43	2131	Blast Furnace Flue	
10/1/2008	11:30	524545	46100	36000	10100	1001-44	2132	Blast Furnace Flue	
10/1/2008	11:37	510090	47360	27220	20140	1001-45	2133	Blast Furnace Flue	
10/1/2008	11:44	510335	50640	26120	24520	1001-46	2134	Blast Furnace Flue	
10/1/2008	11:48	524545	44620	36000	8620	1001-47	2135	Blast Furnace Flue	
10/1/2008	11:50	510090	48380	27220	21160	1001-48	2136	Blast Furnace Flue	
10/1/2008	13:15	510335	51280	26120	25160	1001-49	2137	Blast Furnace Flue	
10/1/2008	13:18	510090	51620	27220	24400	1001-50	2138	Blast Furnace Flue	
10/1/2008	13:30	510090	50380	27220	23160	1001-51	2139	Blast Furnace Flue	
10/1/2008	13:32	510335	47240	26120	21120	1001-52	2140	Blast Furnace Flue	
10/1/2008	13:38	524545	47440	36000	11440	1001-53	2141	Blast Furnace Flue	
10/1/2008	13:41	510090	50980	27220	23760	1001-54	2142	Blast Furnace Flue	
10/1/2008	13:44	510335	49160	26120	23040	1001-55	2143	Blast Furnace Flue	
10/1/2008	13:53	510090	51420	27220	24200	1001-56	2144	Blast Furnace Flue	
10/1/2008	13:57	510335	49140	26120	23020	1001-57	2145	Blast Furnace Flue	
10/1/2008	14:00	524545	45760	36000	9760	1001-58	2146	Blast Furnace Flue	
10/1/2008	14:06	510090	49960	27220	22740	1001-59	2147	Blast Furnace Flue	
10/1/2008	14:11	510335	50180	26120	24060	1001-60	2148	Blast Furnace Flue	
10/1/2008	14:17	524545	47280	36000	11280	1001-61	2149	Blast Furnace Flue	
10/1/2008	14:19	510090	53880	27220	26660	1001-62	2150	Blast Furnace Flue	0809-CAMU-138
10/1/2008	14:27	510335	52760	26120	26640	1001-63	2151	Blast Furnace Flue	
10/1/2008	14:38	524545	49280	36000	13280	1001-64	2152	Blast Furnace Flue	
10/1/2008	14:43	510335	33220	26120	7100	1001-65	2153	Blast Furnace Flue	
10/1/2008	15:01	510335	58360	26120	32240	1001-66	2154	Blast Furnace Flue	
10/1/2008	15:03	524545	53260	36000	17260	1001-67	2155	Blast Furnace Flue	
10/1/2008	15:13	510335	37720	26120	11600	1001-68	2156	Blast Furnace Flue	
10/1/2008	15:21	524545	67780	36000	31780	1001-69	2157	Blast Furnace Flue	
10/1/2008	15:26	510335	54080	26120	27960	1001-70	2158	Blast Furnace Flue	
10/1/2008	15:40	524545	83480	36000	47480	1001-71	2159	Blast Furnace Flue	
10/1/2008	15:41	510335	46420	26120	20300	1001-72	2160	Blast Furnace Flue	
10/1/2008	15:44	510090	50460	27220	23240	1001-73	2161	Blast Furnace Flue	
10/1/2008	15:52	510335	44120	26120	18000	1001-74	2162	Blast Furnace Flue	
10/1/2008	16:03	524545	61520	36000	25520	1001-75	2163	Blast Furnace Flue	
10/1/2008	16:04	510090	43420	27220	16200	1001-76	2164	Blast Furnace Flue	
10/1/2008	16:24	510090	50140	27220	22920	1001-77	2165	Blast Furnace Flue	
10/1/2008	16:36	524545	76120	36000	40120	1001-78	2166	Blast Furnace Flue	
10/1/2008	16:39	510335	48800	26120	22680	1001-79	2167	Blast Furnace Flue	
10/1/2008	16:43	510090	48120	27220	20900	1001-80	2168	Blast Furnace Flue	
10/1/2008	16:54	524545	77540	36000	41540	1001-81	2169	Blast Furnace Flue	
10/2/2008	8:06	520990	82860	35540	47320	1002-1	2170	Blast Furnace Flue	
10/2/2008	8:13	524545	74200	36000	38200	1002-2	2171	Blast Furnace Flue	0809-CAMU-139
10/2/2008	8:14	510335	46420	26120	20300	1002-3	2172	Blast Furnace Flue	
10/2/2008	8:30	520990	83060	35540	47520	1002-4	2173	Blast Furnace Flue	
10/2/2008	9:20	510335	52020	26120	25900	1002-5	2174	Blast Furnace Flue	
10/2/2008	9:32	524545	75500	36000	39500	1002-6	2175	Blast Furnace Flue	
10/2/2008	9:34	520990	77860	35540	42320	1002-7	2176	Blast Furnace Flue	
10/2/2008	9:38	510335	54060	26120	27940	1002-8	2177	Blast Furnace Flue	
10/2/2008	9:51	524545	85300	36000	49300	1002-9	2178	Blast Furnace Flue	
10/2/2008	10:00	520990	85080	35540	49540	1002-10	2179	Blast Furnace Flue	

APPENDIX A
TRUCK WEIGHT SUMMARY

Date	Time	Truck ID	Weight	Tare Weight	Material Weight	Load ID	Load #	Waste Origin	Sample Taken
10/2/2008	10:03	510335	53660	26120	27540	1002-11	2180	Blast Furnace Flue	
10/2/2008	10:07	524545	82260	36000	46260	1002-12	2181	Blast Furnace Flue	
10/2/2008	10:14	520990	82420	35540	46880	1002-13	2182	Blast Furnace Flue	
10/2/2008	10:17	510335	50300	26120	24180	1002-14	2183	Blast Furnace Flue	
10/2/2008	10:23	524545	83280	36000	47280	1002-15	2184	Blast Furnace Flue	
10/2/2008	10:32	520990	84380	35540	48840	1002-16	2185	Blast Furnace Flue	
10/2/2008	10:36	510335	48020	26120	21900	1002-17	2186	Blast Furnace Flue	
10/2/2008	10:45	524545	82300	36000	46300	1002-18	2187	Blast Furnace Flue	
10/2/2008	10:49	520990	80060	35540	44520	1002-19	2188	Blast Furnace Flue	
10/2/2008	11:00	524545	82220	36000	46220	1002-20	2189	Blast Furnace Flue	
10/2/2008	11:05	520990	82060	35540	46520	1002-21	2190	Blast Furnace Flue	0809-CAMU-140
10/2/2008	11:18	524545	85100	36000	49100	1002-22	2191	Blast Furnace Flue	
10/2/2008	11:27	520990	79100	35540	43560	1002-23	2192	Blast Furnace Flue	
10/2/2008	11:36	524545	87380	36000	51380	1002-24	2193	Blast Furnace Flue	
10/2/2008	11:43	520990	85820	35540	50280	1002-25	2194	Blast Furnace Flue	
10/2/2008	11:52	524545	79940	36000	43940	1002-26	2195	Blast Furnace Flue	
10/2/2008	13:14	510335	47980	26120	21860	1002-27	2196	Blast Furnace Flue	
10/2/2008	13:19	520990	82660	35540	47120	1002-28	2197	Blast Furnace Flue	
10/2/2008	13:30	524545	91500	36000	55500	1002-29	2198	Blast Furnace Flue	
10/2/2008	11:33	510335	52700	26120	26580	1002-30	2199	Blast Furnace Flue	
10/2/2008	13:44	520990	81620	35540	46080	1002-31	2200	Blast Furnace Flue	
10/2/2008	13:50	524545	90440	36000	54440	1002-32	2201	Blast Furnace Flue	
10/2/2008	13:52	510335	49620	26120	23500	1002-33	2202	Blast Furnace Flue	
10/2/2008	13:59	520990	87640	35540	52100	1002-34	2203	Blast Furnace Flue	
10/2/2008	14:06	524545	89560	36000	53560	1002-35	2204	Blast Furnace Flue	
10/2/2008	14:10	510335	59080	26120	32960	1002-36	2205	Blast Furnace Flue	
10/2/2008	14:15	520990	81000	35540	45460	1002-37	2206	Blast Furnace Flue	
10/2/2008	14:21	524545	83760	36000	47760	1002-38	2207	Blast Furnace Flue	
10/2/2008	14:24	510335	50160	26120	24040	1002-39	2208	Blast Furnace Flue	
10/2/2008	14:32	520990	83720	35540	48180	1002-40	2209	Blast Furnace Flue	
10/2/2008	14:37	524545	83100	36000	47100	1002-41	2210	Blast Furnace Flue	
10/2/2008	14:40	510335	43440	26120	17320	1002-42	2211	Blast Furnace Flue	
10/2/2008	14:47	520990	80880	35540	45340	1002-43	2212	Blast Furnace Flue	0809-CAMU-141
10/2/2008	14:54	510335	50480	26120	24360	1002-44	2213	Blast Furnace Flue	
10/2/2008	14:58	524545	80380	36000	44380	1002-45	2214	Blast Furnace Flue	
10/2/2008	15:09	520990	72900	35540	37360	1002-46	2215	Blast Furnace Flue	
10/2/2008	15:11	510335	47220	26120	21100	1002-47	2216	Blast Furnace Flue	
10/2/2008	15:19	524545	75080	36000	39080	1002-48	2217	Blast Furnace Flue	
10/2/2008	15:25	520990	81500	35540	45960	1002-49	2218	Blast Furnace Flue	
10/2/2008	15:28	510335	48420	26120	22300	1002-50	2219	Blast Furnace Flue	
10/2/2008	15:35	524545	82000	36000	46000	1002-51	2220	Blast Furnace Flue	
10/2/2008	15:43	520990	79800	35540	44260	1002-52	2221	Blast Furnace Flue	
10/2/2008	15:46	510335	49960	26120	23840	1002-53	2222	Blast Furnace Flue	
10/2/2008	15:52	524545	80620	36000	44620	1002-54	2223	Blast Furnace Flue	
10/2/2008	16:04	520990	78500	35540	42960	1002-55	2224	Blast Furnace Flue	
10/2/2008	16:06	510335	51180	26120	25060	1002-56	2225	Blast Furnace Flue	
10/2/2008	16:13	524545	79020	36000	43020	1002-57	2226	Blast Furnace Flue	
10/2/2008	16:19	520990	79720	35540	44180	1002-58	2227	Blast Furnace Flue	
10/2/2008	16:22	510335	48540	26120	22420	1002-59	2228	Blast Furnace Flue	
10/2/2008	16:42	524545	77120	36000	41120	1002-60	2229	Blast Furnace Flue	
10/2/2008	16:48	520990	74080	35540	38540	1002-61	2230	Blast Furnace Flue	
10/2/2008	16:50	510335	50480	26120	24360	1002-62	2231	Blast Furnace Flue	
10/3/2008	8:05	520990	78100	35540	42560	1003-1	2232	Blast Furnace Flue	0809-CAMU-142
10/3/2008	8:25	510335	53520	26120	27400	1003-2	2233	Blast Furnace Flue	
10/3/2008	8:30	520990	82180	35540	46640	1003-3	2234	Blast Furnace Flue	
10/3/2008	8:47	520990	85320	35540	49780	1003-4	2235	Blast Furnace Flue	
10/3/2008	8:49	510335	51940	26120	25820	1003-5	2236	Blast Furnace Flue	
10/3/2008	9:03	520990	81800	35540	46260	1003-6	2237	Blast Furnace Flue	
10/3/2008	9:05	510335	51940	26120	25820	1003-7	2238	Blast Furnace Flue	
10/3/2008	9:20	520990	86780	35540	51240	1003-8	2239	Blast Furnace Flue	
10/3/2008	9:24	510335	49960	26120	23840	1003-9	2240	Blast Furnace Flue	
10/3/2008	9:33	524545	84580	36000	48580	1003-10	2241	Blast Furnace Flue	
10/3/2008	9:37	520990	81180	35540	45640	1003-11	2242	Blast Furnace Flue	
10/3/2008	9:40	510335	54600	26120	28480	1003-12	2243	Blast Furnace Flue	
10/3/2008	9:51	524545	88380	36000	52380	1003-13	2244	Blast Furnace Flue	
10/3/2008	9:58	520990	83620	35540	48080	1003-14	2245	Blast Furnace Flue	
10/3/2008	10:02	510335	53300	26120	27180	1003-15	2246	Blast Furnace Flue	
10/3/2008	10:10	524545	75100	36000	39100	1003-16	2247	Blast Furnace Flue	
10/3/2008	10:19	520990	86940	35540	51400	1003-17	2248	Blast Furnace Flue	
10/3/2008	10:22	510335	48080	26120	21960	1003-18	2249	Blast Furnace Flue	
10/3/2008	10:33	524545	86220	36000	50220	1003-19	2250	Blast Furnace Flue	
10/3/2008	10:38	520990	86220	35540	50680	1003-20	2251	Blast Furnace Flue	
10/3/2008	10:41	510335	47820	26120	21700	1003-21	2252	Blast Furnace Flue	0809-CAMU-143
10/3/2008	10:58	524545	78340	36000	42340	1003-22	2253	Blast Furnace Flue	
10/3/2008	11:02	520990	85440	35540	49900	1003-23	2254	Blast Furnace Flue	
10/3/2008	11:05	510335	49780	26120	23660	1003-24	2255	Blast Furnace Flue	
10/3/2008	11:17	524545	83220	36000	47220	1003-25	2256	Blast Furnace Flue	
10/3/2008	11:20	520990	83420	35540	47880	1003-26	2257	Blast Furnace Flue	
10/3/2008	11:23	510335	53000	26120	26880	1003-27	2258	Blast Furnace Flue	
10/3/2008	11:36	524545	84200	36000	48200	1003-28	2259	Blast Furnace Flue	

APPENDIX A
TRUCK WEIGHT SUMMARY

Date	Time	Truck ID	Weight	Tare Weight	Material Weight	Load ID	Load #	Waste Origin	Sample Taken
10/3/2008	11:40	520990	84980	35540	49440	1003-29	2260	Blast Furnace Flue	
10/3/2008	11:53	524545	84840	36000	48840	1003-30	2261	Blast Furnace Flue	
10/3/2008	11:56	520990	81460	35540	45920	1003-31	2262	Blast Furnace Flue	
10/3/2008	13:20	524545	84440	36000	48440	1003-32	2263	Blast Furnace Flue	
10/3/2008	13:23	520990	87700	35540	52160	1003-33	2264	Blast Furnace Flue	
10/3/2008	13:29	524547	83420	35000	48420	1003-34	2265	Blast Furnace Flue	
10/3/2008	13:39	524545	90400	36000	54400	1003-35	2266	Blast Furnace Flue	
10/3/2008	13:54	524545	87880	36000	51880	1003-36	2267	Blast Furnace Flue	
10/3/2008	13:59	524547	82840	35000	47840	1003-37	2268	Blast Furnace Flue	
10/3/2008	14:00	510335	50680	26120	24560	1003-38	2269	Blast Furnace Flue	
10/3/2008	14:13	524545	84340	36000	48340	1003-39	2270	Blast Furnace Flue	
10/3/2008	14:17	524547	80760	35000	45760	1003-40	2271	Blast Furnace Flue	
10/3/2008	14:21	510335	56040	26120	29920	1003-41	2272	Blast Furnace Flue	0809-CAMU-144
10/3/2008	14:31	524545	86140	36000	50140	1003-42	2273	Blast Furnace Flue	
10/3/2008	14:37	524547	84500	35000	49500	1003-43	2274	Blast Furnace Flue	
10/3/2008	14:48	524545	88660	36000	52660	1003-44	2275	Blast Furnace Flue	
10/3/2008	14:50	510335	52500	26120	26380	1003-45	2276	Blast Furnace Flue	
10/3/2008	14:55	524547	83960	35000	48960	1003-46	2277	Blast Furnace Flue	
10/3/2008	15:07	524545	84660	36000	48660	1003-47	2278	Blast Furnace Flue	
10/3/2008	15:09	510335	52000	26120	25880	1003-48	2279	Blast Furnace Flue	
10/3/2008	15:14	524547	86260	35000	51260	1003-49	2280	Blast Furnace Flue	
10/3/2008	15:25	524545	79180	36000	43180	1003-50	2281	Blast Furnace Flue	
10/3/2008	15:35	524547	87400	35000	52400	1003-51	2282	Blast Furnace Flue	
10/3/2008	15:39	510335	51060	26120	24940	1003-52	2283	Blast Furnace Flue	
10/3/2008	15:47	524545	79200	36000	43200	1003-53	2284	Blast Furnace Flue	
10/3/2008	15:59	524547	88920	35000	53920	1003-54	2285	Blast Furnace Flue	
10/3/2008	16:05	524545	81140	36000	45140	1003-55	2286	Blast Furnace Flue	
10/3/2008	16:07	510335	49120	26120	23000	1003-56	2287	Blast Furnace Flue	
10/3/2008	16:21	524547	87220	35000	52220	1003-57	2288	Blast Furnace Flue	
10/3/2008	16:26	524545	88120	36000	52120	1003-58	2289	Blast Furnace Flue	
10/3/2008	16:29	510335	54760	26120	28640	1003-59	2290	Blast Furnace Flue	
10/3/2008	16:38	524547	79200	35000	44200	1003-60	2291	Blast Furnace Flue	
10/3/2008	16:48	524545	83320	36000	47320	1003-61	2292	Blast Furnace Flue	0809-CAMU-145
10/3/2008	16:49	510335	52140	26120	26020	1003-62	2293	Blast Furnace Flue	
10/3/2008	16:55	524547	84800	35000	49800	1003-63	2294	Blast Furnace Flue	
10/4/2008	8:20	524547	82080	35000	47080	1004-01	2295	Blast Furnace Flue	
10/4/2008	8:25	524545	910120	36000	874120	1004-02	2296	Blast Furnace Flue	
10/4/2008	8:27	510335	51600	26120	25480	1004-03	2297	Blast Furnace Flue	
10/4/2008	8:41	524547	81480	35000	46480	1004-04	2298	Blast Furnace Flue	
10/4/2008	8:54	524545	90580	36000	54580	1004-05	2299	Blast Furnace Flue	
10/4/2008	9:02	510335	51360	26120	25240	1004-06	2300	Blast Furnace Flue	
10/4/2008	9:12	524547	80000	35000	45000	1004-07	2301	Blast Furnace Flue	
10/4/2008	9:18	524545	83440	36000	47440	1004-08	2302	Blast Furnace Flue	
10/4/2008	9:22	510335	50200	26120	24080	1004-09	2303	Blast Furnace Flue	
10/4/2008	9:30	524547	80040	35000	45040	1004-10	2304	Blast Furnace Flue	
10/4/2008	9:37	524545	79280	36000	43280	1004-11	2305	Blast Furnace Flue	
10/4/2008	9:41	510335	49760	26120	23640	1004-12	2306	Blast Furnace Flue	
10/4/2008	9:47	524547	76340	35000	41340	1004-13	2307	Blast Furnace Flue	
10/4/2008	9:59	524545	85400	36000	49400	1004-14	2308	Blast Furnace Flue	
10/4/2008	10:02	510335	51960	26120	25840	1004-15	2309	Blast Furnace Flue	
10/4/2008	10:08	524547	80000	35000	45000	1004-16	2310	Blast Furnace Flue	
10/4/2008	10:17	524545	79420	36000	43420	1004-17	2311	Blast Furnace Flue	
10/4/2008	10:19	510335	49440	26120	23320	1004-18	2312	Blast Furnace Flue	0809-CAMU-146
10/4/2008	10:25	524547	80120	35000	45120	1004-19	2313	Blast Furnace Flue	
10/4/2008	10:36	524545	82640	36000	46640	1004-20	2314	Blast Furnace Flue	
10/4/2008	10:39	510335	50800	26120	24680	1004-21	2315	Blast Furnace Flue	
10/4/2008	10:43	524547	81440	35000	46440	1004-22	2316	Blast Furnace Flue	
10/4/2008	10:58	524545	73560	36000	37560	1004-23	2317	Blast Furnace Flue	
10/4/2008	11:00	510335	47340	26120	21220	1004-24	2318	Blast Furnace Flue	
10/4/2008	11:04	524547	78400	35000	43400	1004-25	2319	Blast Furnace Flue	
10/4/2008	11:17	524545	73960	36000	37960	1004-26	2320	Blast Furnace Flue	
10/4/2008	11:19	510335	51180	26120	25060	1004-27	2321	Blast Furnace Flue	
10/4/2008	11:25	524547	79700	35000	44700	1004-28	2322	Blast Furnace Flue	
10/4/2008	11:35	524545	78600	36000	42600	1004-29	2323	Blast Furnace Flue	
10/4/2008	11:37	510335	46820	26120	20700	1004-30	2324	Blast Furnace Flue	
10/4/2008	11:52	524547	78760	35000	43760	1004-31	2325	Blast Furnace Flue	
10/4/2008	11:56	524545	90960	36000	54960	1004-32	2326	Blast Furnace Flue	
10/4/2008	12:00	510335	53740	26120	27620	1004-33	2327	Blast Furnace Flue	
10/6/2008	8:25	524547	77840	35000	42840	1006-01	2328	Blast Furnace Flue	
10/6/2008	8:30	524545	75260	36000	39260	1006-02	2329	Blast Furnace Flue	
10/6/2008	8:34	510335	45700	26120	19580	1006-03	2330	Blast Furnace Flue	
10/6/2008	8:52	524547	78100	35000	43100	1006-04	2331	Blast Furnace Flue	
10/6/2008	8:55	510335	51340	26120	25220	1006-05	2332	Blast Furnace Flue	0809-CAMU-147
10/6/2008	9:00	524545	80820	36000	44820	1006-06	2333	Blast Furnace Flue	
10/6/2008	9:10	524547	77700	35000	42700	1006-07	2334	Blast Furnace Flue	
10/6/2008	9:16	524545	70780	36000	34780	1006-08	2335	Blast Furnace Flue	
10/6/2008	9:25	510335	51360	26120	25240	1006-09	2336	Blast Furnace Flue	
10/6/2008	9:31	524547	80700	35000	45700	1006-10	2337	Blast Furnace Flue	
10/6/2008	9:37	524545	73700	36000	37700	1006-11	2338	Blast Furnace Flue	
10/6/2008	9:41	510335	49020	26120	22900	1006-12	2339	Blast Furnace Flue	

APPENDIX A
TRUCK WEIGHT SUMMARY

Date	Time	Truck ID	Weight	Tare Weight	Material Weight	Load ID	Load #	Waste Origin	Sample Taken
10/6/2008	9:47	524547	77260	35000	42260	1006-13	2340	Blast Furnace Flue	
10/6/2008	9:53	524545	81120	36000	45120	1006-14	2341	Blast Furnace Flue	
10/6/2008	9:55	510335	48980	26120	22860	1006-15	2342	Blast Furnace Flue	
10/6/2008	10:05	524547	77900	35000	42900	1006-16	2343	Blast Furnace Flue	
10/6/2008	10:09	524545	78560	36000	42560	1006-17	2344	Blast Furnace Flue	
10/6/2008	10;13	510335	47340	26120	21220	1006-18	2345	Blast Furnace Flue	
10/6/2008	10:20	524547	77400	35000	42400	1006-19	2346	Blast Furnace Flue	
10/6/2008	10:32	524545	75720	36000	39720	1006-20	2347	Blast Furnace Flue	
10/6/2008	10:34	510335	46100	26120	19980	1006-21	2348	Blast Furnace Flue	
10/6/2008	10:39	524547	74600	35000	39600	1006-22	2349	Blast Furnace Flue	
10/6/2008	10:45	524545	69300	36000	33300	1006-23	2350	Blast Furnace Flue	
10/6/2008	10:48	510335	47280	26120	21160	1006-24	2351	Blast Furnace Flue	
10/6/2008	10:55	524547	81440	35000	46440	1006-25	2352	Blast Furnace Flue	0809-CAMU-148
10/6/2008	11:03	524545	74020	36000	38020	1006-26	2353	Blast Furnace Flue	
10/6/2008	11:04	510335	47280	26120	21160	1006-27	2354	Blast Furnace Flue	
10/6/2008	11:25	524547	77060	35000	42060	1006-28	2355	Blast Furnace Flue	
10/6/2008	11:29	524545	71560	36000	35560	1006-29	2356	Blast Furnace Flue	
10/6/2008	0:00	510335	46480	26120	20360	1006-30	2357	Blast Furnace Flue	
10/6/2008	11:46	524547	66160	35000	31160	1006-31	2358	Blast Furnace Flue	
10/6/2008	11:53	524545	73280	36000	37280	1006-32	2359	Blast Furnace Flue	
10/6/2008	13:23	510335	44720	26120	18600	1006-33	2360	Blast Furnace Flue	
10/6/2008	13:37	524545	80980	36000	44980	1006-34	2361	Blast Furnace Flue	
10/6/2008	13:44	524547	64140	35000	29140	1006-35	2362	Blast Furnace Flue	
10/6/2008	13:46	510335	48840	26120	22720	1006-36	2363	Blast Furnace Flue	
10/6/2008	13:58	524545	81060	36000	45060	1006-37	2364	Blast Furnace Flue	
10/8/2008	8:30	524547	54080	35000	19080	1008-01	2380	Monier Flue	
10/8/2008	8:38	524545	58600	36000	22600	1008-02	2381	Monier Flue	
10/8/2008	8:43	510335	38360	26120	12240	1008-03	2382	Monier Flue	
10/8/2008	9:03	524547	57380	35000	22380	1008-04	2383	Monier Flue	
10/8/2008	9:14	524545	61020	36000	25020	1008-05	2384	Monier Flue	
10/8/2008	9:22	510335	35160	26120	9040	1008-06	2385	Monier Flue	
10/8/2008	9:49	524547	69940	35000	34940	1008-07	2386	Monier Flue	
10/8/2008	9:54	510335	45620	26120	19500	1008-08	2387	Monier Flue	
10/8/2008	10:08	524545	67140	36000	31140	1008-09	2388	Monier Flue	
10/8/2008	10:19	524547	80440	35000	45440	1008-10	2389	Monier Flue	
10/8/2008	10:22	510335	42320	26120	16200	1008-11	2390	Monier Flue	
10/8/2008	10:29	524545	62680	36000	26680	1008-12	2391	Monier Flue	
10/8/2008	10:37	524547	71440	35000	36440	1008-13	2392	Monier Flue	
10/8/2008	10:42	510335	39660	26120	13540	1008-14	2393	Monier Flue	0809-CAMU-150
10/8/2008	10:57	524545	74980	36000	38980	1008-15	2394	Monier Flue	
10/8/2008	11:12	510335	39600	26120	13480	1008-16	2395	Monier Flue	
10/8/2008	11:35	524547	73700	35000	38700	1008-17	2396	Monier Flue	
10/8/2008	11:39	510335	41000	26120	14880	1008-18	2397	Monier Flue	
10/8/2008	11:42	524545	78700	36000	42700	1008-19	2398	Monier Flue	
10/8/2008	11:53	524547	80520	35000	45520	1008-20	2399	Monier Flue	
10/8/2008	13:30	524547	64120	35000	29120	1008-21	2400	Monier Flue	
10/8/2008	13:40	524545	72080	36000	36080	1008-22	2401	Monier Flue	
10/8/2008	13:46	510335	47260	26120	21140	1008-23	2402	Monier Flue	
10/8/2008	13:47	524547	60000	35000	25000	1008-24	2403	Monier Flue	
10/8/2008	13:51	524545	62400	36000	26400	1008-25	2404	Monier Flue	
10/8/2008	14:11	524547	54480	35000	19480	1008-26	2405	Monier Flue	
10/8/2008	14:12	510335	52380	26120	26260	1008-27	2406	Monier Flue	
10/8/2008	14:14	524545	56400	36000	20400	1008-28	2407	Monier Flue	
10/8/2008	14:22	510335	52700	26120	26580	1008-29	2408	Monier Flue	
10/8/2008	14:27	524547	74880	35000	39880	1008-30	2409	Monier Flue	
10/8/2008	14:33	524545	84940	36000	48940	1008-31	2410	Monier Flue	
10/8/2008	14:36	510335	52160	26120	26040	1008-32	2411	Monier Flue	
10/8/2008	14:41	524547	62580	35000	27580	1008-33	2412	Monier Flue	
10/8/2008	14:49	524545	87480	36000	51480	1008-34	2413	Monier Flue	0809-CAMU-151
10/8/2008	14:54	510335	51300	26120	25180	1008-35	2414	Monier Flue	
10/8/2008	14:56	524547	60400	35000	25400	1008-36	2415	Monier Flue	
10/8/2008	15:06	510335	53200	26120	27080	1008-37	2416	Monier Flue	
10/8/2008	15:11	524545	83620	36000	47620	1008-38	2417	Monier Flue	
10/8/2008	15:12	524547	65900	35000	30900	1008-39	2418	Monier Flue	
10/8/2008	15:19	510335	55160	26120	29040	1008-40	2419	Monier Flue	
10/8/2008	15:27	524545	65460	36000	29460	1008-41	2420	Monier Flue	
10/8/2008	15:31	524547	81360	35000	46360	1008-42	2421	Monier Flue	
10/8/2008	15:34	510335	51500	26120	25380	1008-43	2422	Monier Flue	
10/8/2008	15:43	524545	62320	36000	26320	1008-44	2423	Monier Flue	
10/8/2008	15:47	524547	87140	35000	52140	1008-45	2424	Monier Flue	
10/8/2008	15:50	510335	53120	26120	27000	1008-46	2425	Monier Flue	
10/8/2008	15:58	524545	62460	36000	26460	1008-47	2426	Monier Flue	
10/8/2008	16:04	524547	88600	35000	53600	1008-48	2427	Monier Flue	
10/8/2008	16:08	510335	48960	26120	22840	1008-49	2428	Monier Flue	
10/8/2008	16:15	524545	60960	36000	24960	1008-50	2429	Monier Flue	
10/8/2008	16:18	524547	79880	35000	44880	1008-51	2430	Monier Flue	
10/8/2008	16:20	510335	53920	26120	27800	1008-52	2431	Monier Flue	
10/8/2008	16:30	524547	83060	35000	48060	1008-53	2432	Monier Flue	
10/8/2008	16:34	524545	67780	36000	31780	1008-54	2433	Monier Flue	
10/8/2008	16:36	510335	53180	26120	27060	1008-55	2434	Monier Flue	0809-CAMU-152

APPENDIX A
TRUCK WEIGHT SUMMARY

Date	Time	Truck ID	Weight	Tare Weight	Material Weight	Load ID	Load #	Waste Origin	Sample Taken
10/8/2008	16:45	524547	75620	35000	40620	1008-56	2435	Monier Flue	
10/8/2008	16:50	524545	88060	36000	52060	1008-57	2436	Monier Flue	
10/9/2008	8:40	524545	64200	36000	28200	1009-01	2437	Monier Flue	
10/9/2008	8:56	524545	92360	36000	56360	1009-02	2438	Monier Flue	
10/9/2008	9:11	524545	74160	36000	38160	1009-03	2439	Monier Flue	
10/9/2008	9:14	510335	50340	26120	24220	1009-04	2440	Monier Flue	
10/9/2008	9:26	524545	82080	36000	46080	1009-05	2441	Monier Flue	
10/9/2008	9:28	510335	50040	26120	23920	1009-06	2442	Monier Flue	
10/9/2008	9:30	524547	83440	35000	48440	1009-07	2443	Monier Flue	
10/9/2008	9:43	524545	90780	36000	54780	1009-08	2444	Monier Flue	
10/9/2008	9:47	510335	55280	26120	29160	1009-09	2445	Monier Flue	
10/9/2008	9:51	524547	86360	35000	51360	1009-10	2446	Monier Flue	
10/9/2008	9:59	524545	92040	36000	56040	1009-11	2447	Monier Flue	
10/9/2008	10:03	510335	56200	26120	30080	1009-12	2448	Monier Flue	
10/9/2008	10:08	524547	85960	35000	50960	1009-13	2449	Monier Flue	
10/9/2008	10:18	524545	90860	36000	54860	1009-14	2450	Monier Flue	
10/9/2008	10:21	510335	48280	26120	22160	1009-15	2451	Monier Flue	
10/9/2008	10:30	524547	85580	35000	50580	1009-16	2452	Monier Flue	
10/9/2008	10:37	524545	82220	36000	46220	1009-17	2453	Monier Flue	
10/9/2008	10:44	510335	54300	26120	28180	1009-18	2454	Monier Flue	
10/9/2008	10:53	524547	85760	35000	50760	1009-19	2455	Monier Flue	
10/9/2008	11:00	524545	83020	36000	47020	1009-20	2456	Monier Flue	
10/9/2008	11:09	510335	59480	26120	33360	1009-21	2457	Monier Flue	0809-CAMU-153
10/9/2008	11:20	524547	77740	35000	42740	1009-22	2458	Monier Flue	
10/9/2008	11:28	524545	73980	36000	37980	1009-23	2459	Monier Flue	
10/9/2008	11:33	510335	45700	26120	19580	1009-24	2460	Monier Flue	
10/9/2008	11:38	524547	61860	35000	26860	1009-25	2461	Monier Flue	
10/9/2008	11:47	524545	68640	36000	32640	1009-26	2462	Monier Flue	
10/9/2008	11:53	510335	47920	26120	21800	1009-27	2463	Monier Flue	
10/9/2008	13:26	524547	86020	35000	51020	1009-28	2464	Monier Flue	
10/9/2008	13:32	524545	72500	36000	36500	1009-29	2465	Monier Flue	
10/9/2008	13:33	510335	47580	26120	21460	1009-30	2466	Monier Flue	
10/9/2008	13:51	524547	72240	35000	37240	1009-31	2467	Monier Flue	
10/9/2008	14:09	524545	90140	36000	54140	1009-32	2468	Monier Flue	
10/9/2008	14:13	510335	46080	26120	19960	1009-33	2469	Monier Flue	
10/9/2008	14:25	524547	94120	35000	59120	1009-34	2470	Monier Flue	
10/9/2008	14:30	524545	79900	36000	43900	1009-35	2471	Monier Flue	
10/9/2008	14:33	510335	51220	26120	25100	1009-36	2472	Monier Flue	
10/9/2008	14:51	524545	74280	36000	38280	1009-37	2473	Monier Flue	
10/9/2008	14:53	524547	86700	35000	51700	1009-38	2474	Monier Flue	
10/9/2008	14:54	510335	49980	26120	23860	1009-39	2475	Monier Flue	
10/9/2008	15:08	524547	92560	35000	57560	1009-40	2476	Monier Flue	
10/10/2008	8:11	524547	86680	35000	51680	1010-01	2477	Monier Flue	
10/10/2008	8:13	510335	56540	26120	30420	1010-02	2478	Monier Flue	0809-CAMU-154
10/10/2008	8:33	524547	84280	35000	49280	1010-03	2479	Monier Flue	
10/10/2008	8:38	510335	53600	26120	27480	1010-04	2480	Monier Flue	
10/10/2008	8:48	524547	89580	35000	54580	1010-05	2481	Monier Flue	
10/10/2008	8:50	510335	52560	26120	26440	1010-06	2482	Monier Flue	
10/10/2008	9:06	524547	85760	35000	50760	1010-07	2483	Monier Flue	
10/10/2008	9:07	510335	55240	26120	29120	1010-08	2484	Monier Flue	
10/10/2008	9:21	524547	90780	35000	55780	1010-09	2485	Monier Flue	
10/10/2008	9:31	510335	56780	26120	30660	1010-10	2486	Monier Flue	
10/10/2008	9:40	524547	89420	35000	54420	1010-11	2487	Monier Flue	
10/10/2008	9:45	524545	86600	36000	50600	1010-12	2488	Monier Flue	
10/10/2008	9:46	510335	49660	26120	23540	1010-13	2489	Monier Flue	
10/10/2008	9:56	524547	89800	35000	54800	1010-14	2490	Monier Flue	
10/10/2008	9:59	510335	56900	26120	30780	1010-15	2491	Monier Flue	
10/10/2008	10:10	524547	88560	35000	53560	1010-16	2492	Monier Flue	
10/10/2008	10:12	510335	53080	26120	26960	1010-17	2493	Monier Flue	
10/10/2008	10:25	524547	75960	35000	40960	1010-18	2494	Monier Flue	
10/10/2008	10:28	510335	50560	26120	24440	1010-19	2495	Monier Flue	
10/10/2008	10:46	524547	80140	35000	45140	1010-20	2496	Monier Flue	
10/10/2008	10:47	510335	47460	26120	21340	1010-21	2497	Monier Flue	
10/10/2008	10:58	524547	92420	35000	57420	1010-22	2498	Monier Flue	0809-CAMU-155
10/10/2008	11:00	510335	51040	26120	24920	1010-23	2499	Monier Flue	
10/10/2008	11:12	510335	57340	26120	31220	1010-24	2500	Monier Flue	
10/10/2008	11:18	524547	83120	35000	48120	1010-25	2501	Monier Flue	
10/10/2008	11:28	510335	41580	26120	15460	1010-26	2502	Monier Flue	
10/10/2008	11:39	524547	72660	35000	37660	1010-27	2503	Monier Flue	
10/10/2008	11:41	510335	52360	26120	26240	1010-28	2504	Monier Flue	
10/10/2008	13:34	524547	51140	35000	16140	1010-29	2505	Monier Flue	
10/11/2008	8:11	524547	89860	35000	54860	1011-01	2506	Monier Flue	
10/11/2008	8:16	524545	83760	36000	47760	1011-02	2507	Monier Flue	
10/11/2008	8:18	510335	50500	26120	24380	1011-03	2508	Monier Flue	
10/11/2008	8:30:00	524547	90180	35000	55180	1011-04	2509	Monier Flue	
10/11/2008	8:35	524545	81840	36000	45840	1011-05	2510	Monier Flue	
10/11/2008	8:37	510335	49300	26120	23180	1011-06	2511	Monier Flue	
10/11/2008	8:48	524547	88920	35000	53920	1011-07	2512	Monier Flue	
10/11/2008	8:52	524545	90080	36000	54080	1011-08	2513	Monier Flue	
10/11/2008	8:53	510335	49000	26120	22880	1011-09	2514	Monier Flue	

APPENDIX A
TRUCK WEIGHT SUMMARY

Date	Time	Truck ID	Weight	Tare Weight	Material Weight	Load ID	Load #	Waste Origin	Sample Taken
10/11/2008	9:02	524547	76000	35000	41000	1011-10	2515	Monier Flue	
10/11/2008	9:07	524545	80400	36000	44400	1011-11	2516	Monier Flue	
10/11/2008	9:09	510335	53680	26120	27560	1011-12	2517	Monier Flue	
10/11/2008	9:27	510335	51560	26120	25440	1011-13	2518	Monier Flue	
10/11/2008	9:30	524545	81160	36000	45160	1011-14	2519	Monier Flue	0809-CAMU-156
10/11/2008	9:41	510335	54520	26120	28400	1011-15	2520	Monier Flue	
10/11/2008	9:49	524545	85880	36000	49880	1011-16	2521	Monier Flue	
10/11/2008	10:04	524545	76580	36000	40580	1011-17	2522	Monier Flue	
10/11/2008	10:05	510335	48680	26120	22560	1011-18	2523	Monier Flue	
10/11/2008	10:18	524547	81640	35000	46640	1011-19	2524	Monier Flue	
10/11/2008	10:22	510335	57580	26120	31460	1011-20	2525	Monier Flue	
10/11/2008	10:29	524545	87200	36000	51200	1011-21	2526	Monier Flue	
10/11/2008	10:32	524547	85960	35000	50960	1011-22	2527	Monier Flue	
10/11/2008	10:37	510335	55500	26120	29380	1011-23	2528	Monier Flue	
10/11/2008	10:42	524545	90020	36000	54020	1011-24	2529	Monier Flue	
10/11/2008	10:46	524547	82420	35000	47420	1011-25	2530	Monier Flue	
10/11/2008	10:51	510335	47940	26120	21820	1011-26	2531	Monier Flue	
10/11/2008	10:57	524545	82420	36000	46420	1011-27	2532	Monier Flue	
10/11/2008	11:00	524547	85260	35000	50260	1011-28	2533	Monier Flue	
10/11/2008	11:03	510335	51640	26120	25520	1011-29	2534	Monier Flue	
10/11/2008	11:10	524545	82860	36000	46860	1011-30	2535	Monier Flue	
10/11/2008	11:14	524547	88920	35000	53920	1011-31	2536	Monier Flue	
10/11/2008	11:17	510335	50840	26120	24720	1011-32	2537	Monier Flue	
10/11/2008	11:25	524545	83600	36000	47600	1011-33	2538	Monier Flue	
10/11/2008	11:28	524547	85280	35000	50280	1011-34	2539	Monier Flue	
10/11/2008	11:32	510335	61460	26120	35340	1011-35	2540	Monier Flue	
10/11/2008	11:45	524545	87820	36000	51820	1011-36	2541	Monier Flue	
10/11/2008	11:50	524547	91920	35000	56920	1011-37	2542	Monier Flue	
10/11/2008	11:52	510335	57640	26120	31520	1011-38	2543	Monier Flue	
10/11/2008	12:01	524545	90120	36000	54120	1011-39	2544	Monier Flue	
10/11/2008	12:06	524547	86420	35000	51420	1011-40	2545	Monier Flue	
10/11/2008	12:10	510335	54560	26120	28440	1011-41	2546	Monier Flue	
10/23/2008	8:16	524545	86880	36000	50880	1023-02	3219	Monier Flue	
10/23/2008	8:17	510335	60960	26120	34840	1023-03	3220	Monier Flue	
10/23/2008	8:26	524545	87240	36000	51240	1023-04	3221	Monier Flue	
10/23/2008	8:29	520989	83620	36280	47340	1023-05	3222	Monier Flue	
10/23/2008	8:33	510335	63560	26120	37440	1023-06	3223	Monier Flue	
10/23/2008	8:35	524547	90520	35000	55520	1023-07	3224	Monier Flue	
10/23/2008	8:51	510335	55060	26120	28940	1023-08	3225	Monier Flue	0809-CAMU-189
10/23/2008	8:57	524547	88140	35000	53140	1023-09	3226	Monier Flue	
10/23/2008	9:11	510335	51240	26120	25120	1023-10	3227	Monier Flue	
10/23/2008	9:18	524547	80900	35000	45900	1023-11	3228	Monier Flue	
10/23/2008	9:20	510335	53960	26120	27840	1023-12	3229	Monier Flue	
10/23/2008	9:34	524547	85020	35000	50020	1023-13	3230	Monier Flue	
10/23/2008	9:41	510335	54960	26120	28840	1023-14	3231	Monier Flue	
10/23/2008	10:04	524547	84940	35000	49940	1023-15	3232	Monier Flue	
10/23/2008	10:05	510335	56440	26120	30320	1023-16	3233	Monier Flue	
10/23/2008	10:24	510335	53180	26120	27060	1023-17	3234	Monier Flue	
10/23/2008	10:30	524547	76960	35000	41960	1023-18	3235	Monier Flue	
10/23/2008	10:40	524545	79320	36000	43320	1023-19	3236	Monier Flue	
10/23/2008	10:47	510335	43920	26120	17800	1023-20	3237	Monier Flue	
10/23/2008	11:02	524547	78680	35000	43680	1023-21	3238	Monier Flue	
10/23/2008	11:14	524545	77980	36000	41980	1023-22	3239	Monier Flue	
10/23/2008	11:24	510335	34840	26120	8720	1023-23	3240	Monier Flue	
10/23/2008	11:53	520989	56780	36280	20500	1023-24	3241	Monier Flue	
10/25/2008	8:04	510335	54400	26120	28280	1025-01	3255	Monier Flue	
10/25/2008	8:13	524547	75700	35000	40700	1025-02	3256	Monier Flue	
10/25/2008	8:18	520989	72940	36280	36660	1025-03	3257	Monier Flue	
10/25/2008	8:25	524545	69920	36000	33920	1025-04	3258	Monier Flue	
10/25/2008	8:26	510335	47340	26120	21220	1025-05	3259	Monier Flue	
10/25/2008	8:34	524547	69660	35000	34660	1025-06	3260	Monier Flue	0809-CAMU-191
10/25/2008	8:36	520989	67480	36280	31200	1025-07	3261	Monier Flue	
10/25/2008	8:43	524545	65880	36000	29880	1025-08	3262	Monier Flue	
10/25/2008	8:49	510335	48780	26120	22660	1025-09	3263	Monier Flue	
10/25/2008	8:59	524547	68360	35000	33360	1025-10	3264	Monier Flue	
10/25/2008	9:00	520989	65880	36280	29600	1025-11	3265	Monier Flue	
10/25/2008	9:04	524545	72300	36000	36300	1025-12	3266	Monier Flue	
10/25/2008	9:06	510335	46900	26120	20780	1025-13	3267	Monier Flue	
10/25/2008	9:15	524547	65280	35000	30280	1025-14	3268	Monier Flue	
10/25/2008	9:19	520989	69860	36280	33580	1025-15	3269	Monier Flue	
10/25/2008	9:25	524545	75220	36000	39220	1025-16	3270	Monier Flue	
10/25/2008	9:29	510335	51880	26120	25760	1025-17	3271	Monier Flue	
10/25/2008	9:41	524547	85480	35000	50480	1025-18	3272	Monier Flue	
10/25/2008	9:53	520989	83980	36280	47700	1025-19	3273	Monier Flue	
10/25/2008	10:04	524545	93520	36000	57520	1025-20	3274	Monier Flue	
10/25/2008	10:06	510335	58180	26120	32060	1025-21	3275	Monier Flue	
10/25/2008	10:09	524547	76600	35000	41600	1025-22	3276	Monier Flue	
10/25/2008	10:14	520989	76840	36280	40560	1025-23	3277	Monier Flue	
10/25/2008	10:20	510335	53560	26120	27440	1025-24	3278	Monier Flue	
10/25/2008	10:27	524545	69040	36000	33040	1025-25	3279	Monier Flue	

APPENDIX A
TRUCK WEIGHT SUMMARY

Date	Time	Truck ID	Weight	Tare Weight	Material Weight	Load ID	Load #	Waste Origin	Sample Taken
10/25/2008	10:35	524547	60080	35000	25080	1025-26	3280	Monier Flue	
10/25/2008	10:45	520989	68760	36280	32480	1025-27	3281	Monier Flue	
10/25/2008	10:49	510335	44480	26120	18360	1025-28	3282	Monier Flue	0809-CAMU-192
10/25/2008	10:53	524545	74340	36000	38340	1025-29	3283	Monier Flue	
10/25/2008	11:02	524547	85560	35000	50560	1025-30	3284	Monier Flue	
10/25/2008	11:09	520989	79260	36280	42980	1025-31	3285	Monier Flue	
10/25/2008	11:19	524545	90300	36000	54300	1025-32	3286	Monier Flue	
10/25/2008	11:21	510335	57540	26120	31420	1025-33	3287	Monier Flue	
10/25/2008	11:25	524547	85160	35000	50160	1025-34	3288	Monier Flue	
10/25/2008	11:32	520989	82760	36280	46480	1025-35	3289	Monier Flue	
10/25/2008	11:40	510335	66900	26120	40780	1025-36	3290	Monier Flue	
10/25/2008	11:50	524547	90200	35000	55200	1025-37	3291	Monier Flue	
10/25/2008	12:24	510335	45480	26120	19360	1025-38	3292	Monier Flue	
10/25/2008	12:43	524545	91320	36000	55320	1025-39	3293	Monier Flue	
10/25/2008	12:49	510335	59100	26120	32980	1025-40	3294	Monier Flue	
10/25/2008	13:00	524545	82500	36000	46500	1025-41	3295	Monier Flue	
10/25/2008	13:02	510335	61480	26120	35360	1025-42	3296	Monier Flue	
10/25/2008	13:12	524545	91620	36000	55620	1025-43	3297	Monier Flue	
10/25/2008	13:14	510335	65340	26120	39220	1025-44	3298	Monier Flue	
10/25/2008	13:25	524545	94980	36000	58980	1025-45	3299	Monier Flue	
10/25/2008	13:30	510335	63320	26120	37200	1025-46	3300	Monier Flue	
10/25/2008	13:40	524545	81260	36000	45260	1025-47	3301	Monier Flue	
10/27/2008	11:25	524545	74820	36000	38820	1027-01	3302	Monier Flue	
10/27/2008	11:50	524545	77840	36000	41840	1027-02	3303	Monier Flue	
10/27/2008	13:58	524545	79500	36000	43500	1027-03	3304	Monier Flue	0809-CAMU-193
10/27/2008	13:53	520989	85800	36280	49520	1027-04	3305	Monier Flue	
10/27/2008	14:28	520989	46600	36280	10320	1027-05	3306	Monier Flue	
11/3/2008	10:21	510335	46800	26120	20680	1103-01	3307	Monier Flue	
11/3/2008	10:39	510335	63500	26120	37380	1103-02	3308	Monier Flue	
11/3/2008	10:49	510335	60440	26120	34320	1103-03	3309	Monier Flue	
11/3/2008	10:58	510335	55920	26120	29800	1103-04	3310	Monier Flue	
11/3/2008	11:07	510335	60820	26120	34700	1103-05	3311	Monier Flue	
11/3/2008	11:17	510335	61860	26120	35740	1103-06	3312	Monier Flue	
11/3/2008	11:25	510335	56900	26120	30780	1103-07	3313	Monier Flue	
11/3/2008	11:36	510335	59540	26120	33420	1103-08	3314	Monier Flue	
11/3/2008	11:46	510335	67440	26120	41320	1103-09	3315	Monier Flue	
11/3/2008	11:56	510335	61120	26120	35000	1103-10	3316	Monier Flue	
11/3/2008	12:11	510335	62000	26120	35880	1103-11	3317	Monier Flue	
11/3/2008	12:26	510335	57580	26120	31460	1103-12	3318	Monier Flue	
11/3/2008	13:14	510335	49980	26120	23860	1103-13	3319	Monier Flue	
11/3/2008	13:25	510335	60220	26120	34100	1103-14	3320	Monier Flue	
11/3/2008	13:38	510335	66980	26120	40860	1103-15	3321	Monier Flue	
11/3/2008	13:51	510335	41880	26120	15760	1103-16	3322	Monier Flue	
11/3/2008	14:08	510335	49840	26120	23720	1103-17	3323	Monier Flue	
11/3/2008	14:31	510335	41220	26120	15100	1103-18	3324	Monier Flue	
11/3/2008	14:42	510335	35540	26120	9420	1103-19	3325	Monier Flue	

SAMPLE RESULTS TABLE

APPENDIX A
SAMPLE LOG

Date	Time	Origin of Waste	Sample ID	Truck ID	Material Weight	Description
9/25/2008	15:50	Blast Furnace Flue	0809-CAMU-125	510335	30160	Sample consists of broken concrete from 5 locations.
9/26/2008	13:59	Blast Furnace Flue	0809-CAMU-128	520990	49100	Sample consists of concrete from 4 locations, brick from 1 location and soil from 1 location.
9/27/2008	8:33	Blast Furnace Flue	0809-CAMU-129	520990	41160	Sample consists of brick from 5 locations.
9/27/2008	12:11	Blast Furnace Flue	0809-CAMU-130	524545	45220	Sample consists of brick from 4 locations and soil from 1 location.
9/30/2008	16:40	Blast Furnace Flue	0809-CAMU-135	524545	56620	Sample consists of brick from 4 locations and soil from 1 location.
10/1/2008	9:32	Blast Furnace Flue	0809-CAMU-136	510090	23480	Sample consists of brick from 4 locations, soil from 1 location and concrete from 1 location.
10/1/2008	11:17	Blast Furnace Flue	0809-CAMU-137	510090	30160	Sample consists of brick from 3 locations, soil from 1 location and concrete from 1 location.
10/1/2008	14:19	Blast Furnace Flue	0809-CAMU-138	510090	26660	Sample consists of brick from 3 locations, soil from 2 locations and wood from 1 location.
10/2/2008	8:13	Blast Furnace Flue	0809-CAMU-139	524545	38200	Sample consists of soil from 2 locations, brick from 2 locations and wood from 1 location.
10/2/2008	11:05	Blast Furnace Flue	0809-CAMU-140	520990	46520	Sample consists of soil from 2 locations, brick from 2 locations, concrete from 2 locations and wood from 1 location.
10/2/2008	14:47	Blast Furnace Flue	0809-CAMU-141	520990	45340	Sample consists of brick from 2 locations, concrete from 2 locations and wood from 1 location.
10/3/2008	8:05	Blast Furnace Flue	0809-CAMU-142	520990	42560	Sample consists of soil from 1 location, wood from 1 location, brick from 1 location and concrete from 2 locations.
10/3/2008	10:41	Blast Furnace Flue	0809-CAMU-143	510335	21700	Sample consists of brick from 2 locations, concrete from 2 locations and soil from 1 location.
10/3/2008	14:21	Blast Furnace Flue	0809-CAMU-144	510335	29920	Sample consists of brick from 2 locations, soil from 1 location, concrete from 1 location and wood from 1 location.
10/3/2008	16:48	Blast Furnace Flue	0809-CAMU-145	524545	47320	Sample consists of concrete from 4 locations and soil from 1 location.
10/4/2008	10:19	Blast Furnace Flue	0809-CAMU-146	510335	23320	Sample consists of brick from 4 locations, concrete from 1 location and wood from 1 location.
10/6/2008	8:55	Blast Furnace Flue	0809-CAMU-147	510335	25220	Sample consists of soil from 4 locations.
10/6/2008	10:55	Blast Furnace Flue	0809-CAMU-148	524547	46440	Sample consists of 4 soil and 2 brick samples all from different locations.
10/23/2008	8:51	Blast Furnace Flue	0809-CAMU-189	510335	28940	Sample consists of soil from 5 locations.
10/25/2008	8:36	Blast Furnace Flue	0809-CAMU-191	520989	34660	Sample consists of soil from 5 locations.
10/25/2008	10:49	Blast Furnace Flue	0809-CAMU-192	510335	18360	Sample consists of soil from 4 locations and BRKK from 1 location.
10/27/2008	13:58	Blast Furnace Flue	0809-CAMU-193	524545	43500	Sample consists of soil from 5 locations.
10/8/2008	10:42	Monier Flue	0809-CAMU-150	510335	13540	Sample consists of concrete from 5 locations.
10/8/2008	14:49	Monier Flue	0809-CAMU-151	524545	51480	Sample consists of broken concrete from 5 locations in trailer.
10/8/2008	16:36	Monier Flue	0809-CAMU-152	510335	27060	Sample consists of gravel and concrete from 5 locations in truck.
10/9/2008	11:09	Monier Flue	0809-CAMU-153	510335	33360	Sample consists of gravel, concrete, and soil from 5 locations in truck.
10/10/2008	8:13	Monier Flue	0809-CAMU-154	510335	30420	Sample consists of mixed broken brick, rock, and soil from 5 locations in truck.
10/10/2008	10:58	Monier Flue	0809-CAMU-155	524547	57420	Sample consists of mixed brick, soil, and concrete from 5 locations in truck.
10/11/2008	9:30	Monier Flue	0809-CAMU-156	524545	45160	Sample consists of mixed soil, brick, and rock from 5 locations in truck.

APPENDIX A
SAMPLE RESULTS
All sample results reported in mg/kg

	Sample ID	CollectionDate	Ag-T	Al-T	As-T	Ba-T	Be-T	Cd-T	Co-T	Cr-T	Cu-T	Fe-T	Hg	Mn-T	Ni-T	Pb-T	Sb-T	Se-T	Sn-T	Tl-T	V-T	Zn-T
Blast Furnace Flue	0809-CAMU-125	9/25/2008 15:50	99	5860	697	121	<5	301	12	18	1590	15500	60	538	24	8970	133	15	25	11	83	2560
	0809-CAMU-128	9/26/2008 13:59	22	9340	1370	187	<5	2910	5	13	483	20500	370	865	10	12700	42	21	68	38	18	7080
	0809-CAMU-129	9/27/2008 8:33	32	9190	1630	90	<5	2380	6	14	580	14000	190	253	11	6610	49	18	24	25	38	3450
	0809-CAMU-130	9/27/2008 12:11	35	7560	1990	235	<5	1620	9	19	645	28800	160	681	33	6590	32	11	32	53	39	4330
	0809-CAMU-135	9/30/2008 16:40	50	8120	2750	426	<5	1940	13	13	1120	26400	97	1620	17	8610	48	13	41	78	33	8530
	0809-CAMU-136	10/1/2008 9:32	89	8160	13400	198	<5	9220	8	11	1390	16300	80	630	18	38300	122	13	57	181	34	11800
	0809-CAMU-137	10/1/2008 11:17	102	7840	4870	131	<5	14200	13	17	3960	15800	170	386	24	38200	260	82	314	120	32	25000
	0809-CAMU-138	10/1/2008 14:19	112	9510	2220	244	<5	5330	10	18	2040	16200	170	650	26	18500	102	45	109	48	32	8240
	0809-CAMU-139	10/2/2008 8:13	47	5880	1150	97	<5	1800	6	86	940	11600	160	337	15	6460	57	16	35	17	24	3360
	0809-CAMU-140	10/2/2008 11:05	38	11200	696	650	<5	937	9	14	714	23000	26	472	21	6570	33	7	20	20	47	2910
	0809-CAMU-141	10/2/2008 14:47	68	10200	2140	119	<5	2770	9	18	1070	18700	230	470	20	7250	58	19	36	16	32	3350
	0809-CAMU-142	10/3/2008 8:05	139	5800	5850	175	<5	19000	28	31	10300	14400	110	525	118	43000	985	360	887	218	17	41900
	0809-CAMU-143	10/3/2008 10:41	118	3760	2450	135	<5	6030	15	19	3560	16500	62	414	57	28800	256	83	293	69	13	14000
	0809-CAMU-144	10/3/2008 14:21	141	4060	6960	245	<5	22600	100	74	17100	20900	48	975	620	45300	1820	729	1290	157	16	46200
	0809-CAMU-145	10/3/2008 16:48	169	6640	3170	402	<5	5760	20	26	4570	26800	160	2180	120	35500	230	170	498	74	19	27200
	0809-CAMU-146	10/4/2008 10:19	75	7500	3680	202	<5	3280	12	14	1520	18300	420	323	37	11900	75	40	54	194	29	7490
	0809-CAMU-147	10/6/2008 8:55	254	2130	17200	93	<5	39600	67	21	22200	29000	530	788	131	47400	4140	514	1320	506	7	118000
	0809-CAMU-148	10/6/2008 10:55	156	4390	5050	81	<5	8080	12	9	3860	15700	610	614	25	39200	338	75	232	91	11	21200
	0809-CAMU-189	10/23/2008 8:51	22	12200	2890	457	<5	1150	9	15	478	24600	35	403	18	3580	33	<5	<5	152	50	2700
	0809-CAMU-191	10/25/2008 8:36	5	13800	271	714	<5	163	<5	8	152	13500	9	233	16	753	<5	<5	<5	<5	31	836
	0809-CAMU-192	10/25/2008 10:49	19	9140	1500	191	<5	2600	8	6	599	13600	16	485	16	2820	15	<5	<5	20	31	3960
	0809-CAMU-193	10/27/2008 13:58	69	9510	1960	261	<5	2300	22	811	1200	31400	170	840	782	12000	61	26	65	43	44	6020
Monier Flue	0809-CAMU-150	10/8/2008 10:42	294	3770	8980	110	<5	86900	28	39	8880	11400	660	338	101	48200	1240	1450	2590	1280	11	151000
	0809-CAMU-151	10/8/2008 14:49	29	10200	982	141	<5	2260	11	15	535	14200	310	545	11	6900	33	29	56	38	36	3940
	0809-CAMU-152	10/8/2008 16:36	25	7110	862	126	<5	920	8	12	531	20700	190	691	10	4440	22	11	24	14	27	2550
	0809-CAMU-153	10/9/2008 11:09	113	10500	1680	168	<5	3900	16	18	1720	20700	470	632	29	14000	82	55	93	44	37	9170
	0809-CAMU-154	10/10/2008 8:13	145	6070	2580	124	<5	5960	12	14	2800	15800	400	473	32	23900	170	95	199	90	25	13100
	0809-CAMU-155	10/10/2008 10:58	225	6000	5900	114	<5	13700	27	15	5750	15700	700	584	53	49400	442	173	365	155	21	24400
	0809-CAMU-156	10/11/2008 9:30	26	11400	2700	279	<5	3550	8	18	376	26600	190	954	16	10600	22	24	43	111	38	7320

APPENDIX B

DEMOLITION FOOTPRINT EXPOSED SOIL SAMPLING RESULTS

On Thursday, October 23, 2008, samples were collected from the three Monier Flue sample locations MOF1, MOF2, and MOF3; as well as from three of the five Baghouse locations BFB1, BFB2, and BFB3. All six samples were collected at the specified sampling intervals 0-4", 4-12", 1-2', 2-4', 4-6', 6-8', 8-10', 10-12', and 12-15'.

On Friday, October 24, 2008, samples were collected from the remaining two Baghouse locations BFB4 and BFB5. Both samples were collected at the specified sampling intervals 0-4", 4-12", 1-2', 2-4', 4-6', 6-8', 8-10', 10-12', and 12-15'.

On Monday, October 27, 2008, samples were collected from the two Acid Plant sample locations ACP1 and ACP2, as well as from two of the seven Blast Furnace Flue sample locations BLF1 and BLF2. All four samples were collected at the specified sampling intervals 0-4", 4-12", 1-2', 2-4', 4-6', 6-8', 8-10', 10-12', and 12-15'. The location of ACP2 was moved from within the 200 feet. Acid Plant stack footprint approximately 50 feet to the west due to access.

On Tuesday, October 28, 2008, samples were collected from the remaining five Blast Furnace Flue sample locations BLF3, BLF4, BLF5, BLF6, and BLF7 at the proper sampling interval to the following depths:

- BLF3-0-6' Groundwater was encountered at 4' with the hole remaining open to 4'; therefore a sample was collected from 4-6'. Samples below this interval were not collected, as the hole was caving and they were not considered to be representative.

- BLF4-0-4' Groundwater was encountered at 2' with the hole remaining open to 2'; therefore a sample was collected from 2-4'. Samples below this interval were not collected, as the hole was caving and they were not considered to be representative.

- BLF5-0-10' Groundwater was encountered at 6' with the hole remaining open to 8'; therefore a sample was collected from 8-10'. Samples below this interval were not collected, as the hole was caving and they were not considered to be representative.

- BLF6-0-6' Groundwater was encountered at 2.5' with the hole remaining open to 4'; therefore a sample was collected from 4-6'. Samples below this interval were not collected, as the hole was caving and they were not considered to be representative.

- BLF7-0-15' All samples were collected at the specified intervals from this sample location.

Table B-2 is a sample matrix table, which includes the latitude and longitude of each test pit, the samples taken from each location, and the laboratory analysis performed on each sample. All analytical work was conducted within the 6-month holding time limit for metals. Table B-2 also indicates the locations where duplicate samples were obtained. Table B-3 is a summary table of the indicator metals (As, Cd, Cu, Pb, Se, and Zn) for each of the samples collected and Table B-4 summarizes the results of all laboratory tests conducted on the samples, including supplemental metals and SPLP tests.

TABLE B-1. DEMOLITION FOOTPRINT TEST PIT LOGS

Site/ Sample #	Depth Interval (ft)	Interval Description
MOF1		
	0 - 1.5	Grayish flue dust soil.
	1.5 - 3.5	Silty sand (dense).
	3.5 - 15	Coarse sand, gravel, cobbles (GW)
MOF2		
	0 - 2.5	Grayish flue dust soil.
	2.5 - 3.5	Slag Backfill
	3.5 - 8.5	Silty, clayey matrix-silt loam (SM)
	8.5 - 15	Coarse sand, gravel, cobbles (GW)
MOF3		
	0 - 1.5	Grayish flue dust soil.
	1.5 - 4.5	Silty sand (dense).
	4.5 - 6.5	Silty, clayey matrix-silt loam (SM)
	6.5 - 14	Coarse sand, gravel, cobbles (GW)
BFB1		
	0 - 3	Silty sand.
	3 - 7	Silty, clayey matrix-silt loam (SM)
	7 - 15	Coarse sand, gravel, cobbles (GW)
BFB2		
	0 - 4	Silty sand.
	4 - 11	Silty, clayey matrix-silt loam (SM)
	11 - 15	Coarse sand, gravel, cobbles (GW)
BFB3		
	0 - 3	Silty Sand
	3 - 7	Silty, clayey matrix-silt loam (SM)
	7 - 15	Coarse sand, gravel, cobbles (GW)
BFB4		
	0 - 1.2	Backfill, mixed gravel and sand.
	1.2 - 10	Silty, clayey matrix-silt loam (SM)
	10 - 15	Coarse sand, gravel, cobbles (GW)
BFB5		
	0 - 7	Tan silty-clayey loam soil (SM)
	7 - 15	Coarse sand, gravel, cobbles (GW)
ACP1		
	0 - 8	Silty sand with gravels.
	8 - 15	Coarse sand, gravel, cobbles (GW)
ACP2		
	0 - 8	Silty sand with gravels.
	8 - 15	Coarse sand, gravel, cobbles (GW)
BLF1		
	0 - 1	Grayish flue dust soil.
	1 - 15	Silty sand, gravel, cobbles (GW)
BLF2		
	0 -15	Silty sand, gravel, cobbles (GW) with brick debris.
		Groundwater at 10' below ground surface slowly infiltrating pit.

TABLE B-1. DEMOLITION FOOTPRINT TEST PIT LOGS

Site/ Sample #	Depth Interval (ft)	Interval Description
BLF3		
	0 - 6	Sand and gravel size brick debris and other fill.
		Groundwater at 4" below ground surface.
BLF4		
	0 - 4	Crushed brick and other debris to depth.
		Groundwater at 2' below ground surface. Hole caving after 4'.
BLF5		
	0 - 6	Crushed red brick
	6 - 8	Angular white/red fill to 8'. Groundwater at 6' below ground surface.
	8 - 10	Organic-rich clay mud.
BLF6		
	0 - 4	Brick debris and brown silty sand. Groundwater at 2.5' below ground surface.
	4 - 6	Coarse sand, gravel, cobbles (GW). (Old PP Creek Channel Deposits). Saturated
BLF7		
	0 - 1	Dark brown/reddish brown silty sand and gravel.
	1 - 2	Clay, silt, sand, and dark brown gravel.
	2 - 6	Red-brown silty sand, gravel, and cobbles.
	6 - 15	Coarse silty sand, cobbles, and boulders. Small amount of groundwater inflow at 11'.

TABLE B-2. DEMOLITION FOOTPRINT SOIL SAMPLE TABLE MATRIX

Demoltion Footprint Exposed Soil Sample Area	Sample Location Code	Sample ID	Sample Date	Depth Interval	GPS Coordinates		Analytical Parameters			Notes
					Latitude	Longitude	Indicator Metals (Total)	Supplemental Metals (Total)	Indicator Metals (SPLP)	
Monier Flue	MOF1	MOF1-A	10/23/2008	0-4"	46.580449	-111.922087				
Monier Flue	MOF1	MOF1-B	10/23/2008	4-12"						
Monier Flue	MOF1	MOF1-C	10/23/2008	1-2'						
Monier Flue	MOF1	MOF1-D	10/23/2008	2-4'						
Monier Flue	MOF1	MOF1-E	10/23/2008	4-6'						
Monier Flue	MOF1	MOF1-F	10/23/2008	6-8'						
Monier Flue	MOF1	MOF1-G	10/23/2008	8-10'						
Monier Flue	MOF1	MOF1-H	10/23/2008	10-12'						
Monier Flue	MOF1	MOF1-I	10/23/2008	12-15'						
Monier Flue	MOF2	MOF2-A	10/23/2008	0-4"	46.580796	-111.922440				
Monier Flue	MOF2	MOF2-B	10/23/2008	4-12"						
Monier Flue	MOF2	MOF2-C	10/23/2008	1-2'						
Monier Flue	MOF2	MOF2-D	10/23/2008	2-4'						
Monier Flue	MOF2	MOF2-E	10/23/2008	4-6'						
Monier Flue	MOF2	MOF2-F	10/23/2008	6-8'						
Monier Flue	MOF2	MOF2-G	10/23/2008	8-10'						
Monier Flue	MOF2	MOF2-H	10/23/2008	10-12'						
Monier Flue	MOF2	MOF2-I	10/23/2008	12-15'						
Monier Flue	MOF3	MOF3-A	10/23/2008	0-4"	46.581143	-111.922828				
Monier Flue	MOF3	MOF3-A2	10/23/2008	0-4"						DUPLICATE
Monier Flue	MOF3	MOF3-B	10/23/2008	4-12"						
Monier Flue	MOF3	MOF3-C	10/23/2008	1-2'						
Monier Flue	MOF3	MOF3-D	10/23/2008	2-4'						
Monier Flue	MOF3	MOF3-E	10/23/2008	4-6'						
Monier Flue	MOF3	MOF3-F	10/23/2008	6-8'						
Monier Flue	MOF3	MOF3-G	10/23/2008	8-10'						
Monier Flue	MOF3	MOF3-H	10/23/2008	10-12'						
Monier Flue	MOF3	MOF3-I	10/23/2008	12-15'						

TABLE B-2. DEMOLITION FOOTPRINT SOIL SAMPLE TABLE MATRIX

Demoltion Footprint Exposed Soil Sample Area	Sample Location Code	Sample ID	Sample Date	Depth Interval	GPS Coordinates		Analytical Parameters			Notes
					Latitude	Longitude	Indicator Metals (Total)	Supplemental Metals (Total)	Indicator Metals (SPLP)	
Blast Furnace Baghouse	BFB1	BFB1-A	10/23/2008	0-4"	46.581923	-111.923368				
Blast Furnace Baghouse	BFB1	BFB1-B	10/23/2008	4-12"						
Blast Furnace Baghouse	BFB1	BFB1-C	10/23/2008	1-2'						
Blast Furnace Baghouse	BFB1	BFB1-D	10/23/2008	2-4'						
Blast Furnace Baghouse	BFB1	BFB1-E	10/23/2008	4-6'						
Blast Furnace Baghouse	BFB1	BFB1-F	10/23/2008	6-8'						
Blast Furnace Baghouse	BFB1	BFB1-G	10/23/2008	8-10'						
Blast Furnace Baghouse	BFB1	BFB1-H	10/23/2008	10-12'						
Blast Furnace Baghouse	BFB1	BFB1-I	10/23/2008	12-15'						
Blast Furnace Baghouse	BFB2	BFB2-A	10/23/2008	0-4"	46.581843	-111.923588				
Blast Furnace Baghouse	BFB2	BFB2-B	10/23/2008	4-12"						
Blast Furnace Baghouse	BFB2	BFB2-C	10/23/2008	1-2'						
Blast Furnace Baghouse	BFB2	BFB2-D	10/23/2008	2-4'						
Blast Furnace Baghouse	BFB2	BFB2-D2	10/23/2008	2-4'						DUPLICATE
Blast Furnace Baghouse	BFB2	BFB2-E	10/23/2008	4-6'						
Blast Furnace Baghouse	BFB2	BFB2-F	10/23/2008	6-8'						
Blast Furnace Baghouse	BFB2	BFB2-G	10/23/2008	8-10'						
Blast Furnace Baghouse	BFB2	BFB2-H	10/23/2008	10-12'						
Blast Furnace Baghouse	BFB2	BFB2-I	10/23/2008	12-15'						
Blast Furnace Baghouse	BFB3	BFB3-A	10/23/2008	0-4"	46.581993	-111.923158				
Blast Furnace Baghouse	BFB3	BFB3-B	10/23/2008	4-12"						
Blast Furnace Baghouse	BFB3	BFB3-B2	10/23/2008	4-12"						DUPLICATE
Blast Furnace Baghouse	BFB3	BFB3-C	10/23/2008	1-2'						
Blast Furnace Baghouse	BFB3	BFB3-D	10/23/2008	2-4'						
Blast Furnace Baghouse	BFB3	BFB3-E	10/23/2008	4-6'						
Blast Furnace Baghouse	BFB3	BFB3-F	10/23/2008	6-8'						
Blast Furnace Baghouse	BFB3	BFB3-G	10/23/2008	8-10'						
Blast Furnace Baghouse	BFB3	BFB3-H	10/23/2008	10-12'						
Blast Furnace Baghouse	BFB3	BFB3-I	10/23/2008	12-15'						

TABLE B-2. DEMOLITION FOOTPRINT SOIL SAMPLE TABLE MATRIX

Demoltion Footprint Exposed Soil Sample Area	Sample Location Code	Sample ID	Sample Date	Depth Interval	GPS Coordinates		Analytical Parameters			Notes
					Latitude	Longitude	Indicator Metals (Total)	Supplemental Metals (Total)	Indicator Metals (SPLP)	
Blast Furnace Baghouse	BFB4	BFB4-A	10/24/2008	0-4"	46.582023	-111.923908				
Blast Furnace Baghouse	BFB4	BFB4-B	10/24/2008	4-12"						
Blast Furnace Baghouse	BFB4	BFB4-C	10/24/2008	1-2'						
Blast Furnace Baghouse	BFB4	BFB4-D	10/24/2008	2-4'						
Blast Furnace Baghouse	BFB4	BFB4-E	10/24/2008	4-6'						
Blast Furnace Baghouse	BFB4	BFB4-F	10/24/2008	6-8'						
Blast Furnace Baghouse	BFB4	BFB4-G	10/24/2008	8-10'						
Blast Furnace Baghouse	BFB4	BFB4-H	10/24/2008	10-12'						
Blast Furnace Baghouse	BFB4	BFB4-I	10/24/2008	12-15'						
Blast Furnace Baghouse	BFB5	BFB5-A	10/24/2008	0-4"	46.581453	-111.923028				
Blast Furnace Baghouse	BFB5	BFB5-B	10/24/2008	4-12"						
Blast Furnace Baghouse	BFB5	BFB5-C	10/24/2008	1-2'						
Blast Furnace Baghouse	BFB5	BFB5-D	10/24/2008	2-4'						
Blast Furnace Baghouse	BFB5	BFB5-E	10/24/2008	4-6'						
Blast Furnace Baghouse	BFB5	BFB5-F	10/24/2008	6-8'						
Blast Furnace Baghouse	BFB5	BFB5-F2	10/24/2008	6-8'						DUPLICATE
Blast Furnace Baghouse	BFB5	BFB5-G	10/24/2008	8-10'						
Blast Furnace Baghouse	BFB5	BFB5-H	10/24/2008	10-12'						
Blast Furnace Baghouse	BFB5	BFB5-I	10/24/2008	12-15'						
Acid Plant	ACP1	ACP1-A	10/27/2008	0-4"	46.581133	-111.921988				
Acid Plant	ACP1	ACP1-B	10/27/2008	4-12"						
Acid Plant	ACP1	ACP1-C	10/27/2008	1-2'						
Acid Plant	ACP1	ACP1-D	10/27/2008	2-4'						
Acid Plant	ACP1	ACP1-E	10/27/2008	4-6'						
Acid Plant	ACP1	ACP1-F	10/27/2008	6-8'						
Acid Plant	ACP1	ACP1-G	10/27/2008	8-10'						
Acid Plant	ACP1	ACP1-H	10/27/2008	10-12'						
Acid Plant	ACP1	ACP1-I	10/27/2008	12-15'						

TABLE B-2. DEMOLITION FOOTPRINT SOIL SAMPLE TABLE MATRIX

Demoltion Footprint Exposed Soil Sample Area	Sample Location Code	Sample ID	Sample Date	Depth Interval	GPS Coordinates		Analytical Parameters			Notes
					Latitude	Longitude	Indicator Metals (Total)	Supplemental Metals (Total)	Indicator Metals (SPLP)	
Acid Plant	ACP2	ACP2-A	10/27/2008	0-4"	46.580993	-111.921668				
Acid Plant	ACP2	ACP2-B	10/27/2008	4-12"						
Acid Plant	ACP2	ACP2-C	10/27/2008	1-2'						
Acid Plant	ACP2	ACP2-D	10/27/2008	2-4'						
Acid Plant	ACP2	ACP2-E	10/27/2008	4-6'						
Acid Plant	ACP2	ACP2-F	10/27/2008	6-8'						
Acid Plant	ACP2	ACP2-G	10/27/2008	8-10'						
Acid Plant	ACP2	ACP2-H	10/27/2008	10-12'						
Acid Plant	ACP2	ACP2-I	10/27/2008	12-15'						
Acid Plant	ACP2	ACP2-I2	10/27/2008	12-15'						DUPLICATE
Blast Furnace Flue	BLF1	BLF1-A	10/27/2008	0-4"	46.580703	-111.921368				
Blast Furnace Flue	BLF1	BLF1-B	10/27/2008	4-12"						
Blast Furnace Flue	BLF1	BLF1-C	10/27/2008	1-2'						
Blast Furnace Flue	BLF1	BLF1-D	10/27/2008	2-4'						
Blast Furnace Flue	BLF1	BLF1-E	10/27/2008	4-6'						
Blast Furnace Flue	BLF1	BLF1-F	10/27/2008	6-8'						
Blast Furnace Flue	BLF1	BLF1-G	10/27/2008	8-10'						
Blast Furnace Flue	BLF1	BLF1-H	10/27/2008	10-12'						
Blast Furnace Flue	BLF1	BLF1-I	10/27/2008	12-15'						
Blast Furnace Flue	BLF2	BLF2-A	10/27/2008	0-4"	46.580843	-111.921018				
Blast Furnace Flue	BLF2	BLF2-B	10/27/2008	4-12"						
Blast Furnace Flue	BLF2	BLF2-B2	10/27/2008	4-12"						DUPLICATE
Blast Furnace Flue	BLF2	BLF2-C	10/27/2008	1-2'						
Blast Furnace Flue	BLF2	BLF2-D	10/27/2008	2-4'						
Blast Furnace Flue	BLF2	BLF2-E	10/27/2008	4-6'						
Blast Furnace Flue	BLF2	BLF2-F	10/27/2008	6-8'						
Blast Furnace Flue	BLF2	BLF2-G	10/27/2008	8-10'						
Blast Furnace Flue	BLF2	BLF2-H	10/27/2008	10-12'						
Blast Furnace Flue	BLF2	BLF2-I	10/27/2008	12-15'						
Blast Furnace Flue	BLF3	BLF3-A	10/28/2008	0-4"	46.581173	-111.920578				
Blast Furnace Flue	BLF3	BLF3-B	10/28/2008	4-12"						
Blast Furnace Flue	BLF3	BLF3-C	10/28/2008	1-2'						
Blast Furnace Flue	BLF3	BLF3-D	10/28/2008	2-4'						
Blast Furnace Flue	BLF3	BLF3-E	10/28/2008	4-6'						GW @ 4' bgs; able to sample to 6'

TABLE B-2. DEMOLITION FOOTPRINT SOIL SAMPLE TABLE MATRIX

Demoltion Footprint Exposed Soil Sample Area	Sample Location Code	Sample ID	Sample Date	Depth Interval	GPS Coordinates		Analytical Parameters			Notes
					Latitude	Longitude	Indicator Metals (Total)	Supplemental Metals (Total)	Indicator Metals (SPLP)	
Blast Furnace Flue	BLF4	BLF4-A	10/28/2008	0-4"	46.581353	-111.920338				
Blast Furnace Flue	BLF4	BLF4-B	10/28/2008	4-12"						
Blast Furnace Flue	BLF4	BLF4-C	10/28/2008	1-2'						
Blast Furnace Flue	BLF4	BLF4-D	10/28/2008	2-4'						GW @ 2' bgs; able to sample to 4'
Blast Furnace Flue	BLF5	BLF5-A	10/28/2008	0-4"	46.581713	-111.920428				
Blast Furnace Flue	BLF5	BLF5-B	10/28/2008	4-12"						
Blast Furnace Flue	BLF5	BLF5-C	10/28/2008	1-2'						
Blast Furnace Flue	BLF5	BLF5-D	10/28/2008	2-4'						
Blast Furnace Flue	BLF5	BLF5-E	10/28/2008	4-6'						
Blast Furnace Flue	BLF5	BLF5-E2	10/28/2008	4-6'						DUPLICATE
Blast Furnace Flue	BLF5	BLF5-F	10/28/2008	6-8'						
Blast Furnace Flue	BLF5	BLF5-G	10/28/2008	8-10'						GW @ 6' bgs; able to sample to 10'
Blast Furnace Flue	BLF6	BLF6-A	10/28/2008	0-4"	46.582043	-111.920628				
Blast Furnace Flue	BLF6	BLF6-B	10/28/2008	4-12"						
Blast Furnace Flue	BLF6	BLF6-C	10/28/2008	1-2'						
Blast Furnace Flue	BLF6	BLF6-D	10/28/2008	2-4'						
Blast Furnace Flue	BLF6	BLF6-E	10/28/2008	4-6'						GW @ 2.5' bgs; able to sample to 6'
Blast Furnace Flue	BLF7	BLF7-A	10/28/2008	0-4"	46.582463	-111.920858				
Blast Furnace Flue	BLF7	BLF7-B	10/28/2008	4-12"						
Blast Furnace Flue	BLF7	BLF7-C	10/28/2008	1-2'						
Blast Furnace Flue	BLF7	BLF7-C2	10/28/2008	1-2'						DUPLICATE
Blast Furnace Flue	BLF7	BLF7-D	10/28/2008	2-4'						
Blast Furnace Flue	BLF7	BLF7-E	10/28/2008	4-6'						
Blast Furnace Flue	BLF7	BLF7-F	10/28/2008	6-8'						
Blast Furnace Flue	BLF7	BLF7-G	10/28/2008	8-10'						
Blast Furnace Flue	BLF7	BLF7-H	10/28/2008	10-12'						
Blast Furnace Flue	BLF7	BLF7-I	10/28/2008	12-15'						GW @ 11' bgs; able to sample to 15'

Total # Samples:	**146**	**36**	**18**
Duplicate Samples:	**8**	**2**	**1**

TABLE B-3 . DEMOLITION FOOTPRINT SOIL SAMPLE INDICATOR METALS SUMMARY TABLE

Site/ Sample #	Sample Interval (ft)	Sample Date (m/d/y)	Sample Time (hr/min/sec)	Description Interval (ft)	Analytical Parameters	As (mg/kg)	Cd (mg/kg)	CU (mg/kg)	Pb (mg/kg)	Se (mg/kg)	Zn (mg/kg)
ACP1											
	A	10/27/2008	13:45	0-4"	Total Metals	302	385	910	5650	13	4290
	B	10/27/2008	13:50	4-12"	Total Metals	109	37	110	494	35	332
	C	10/27/2008	13:52	1-2'	Total Metals	413	435	820	7330	42	8370
	D	10/27/2008	13:54	2-4'	Total Metals	52	11	43	175	31	112
	E	10/27/2008	13:57	4-6'	Total Metals	71	27	126	626	31	532
	F	10/27/2008	13:59	6-8'	Total Metals	33	19	34	95	18	97
	G	10/27/2008	14:08	8-10'	Total Metals	32	20	58	170	19	167
	H	10/27/2008	14:15	10-12'	Total Metals	27	4	55	71	30	130
	I	10/27/2008	14:22	12-15'	Total Metals	21	10	48	90	<5	167
	I	10/27/2008	14:22	12-15'	SPLP (mg/L)	<0.1	<0.1	<0.1	<0.1	<0.1	<0.1
ACP2											
	A	10/27/2008	14:40	0-4"	Total Metals	1000	160	1020	7630	12	6070
	B	10/27/2008	14:44	4-12"	Total Metals	50	25	125	16	34	678
	C	10/27/2008	14:46	1-2'	Total Metals	27	1	14	19	31	196
	D	10/27/2008	14:48	2-4'	Total Metals	24	1	15	35	28	44
	E	10/27/2008	14:50	4-6'	Total Metals	31	3	17	28	48	42
	F	10/27/2008	14:53	6-8'	Total Metals	39	1	25	23	29	52
	G	10/27/2008	14:55	8-10'	Total Metals	30	<1	25	18	27	50
	H	10/27/2008	14:59	10-12'	Total Metals	22	<1	23	16	30	57
	I	10/27/2008	15:09	12-15'	Total Metals	31	<1	33	33	<5	47
	I	10/27/2008	15:09	12-15'	SPLP (mg/L)	<0.1	<0.1	<0.1	<0.1	<0.1	<0.1
BFB1											
	A	10/23/2008	15:02	0-4"	Total Metals	930	1790	70	1180	<5	3770
	B	10/23/2008	15:05	4-12"	Total Metals	15	6	21	26	42	55
	C	10/23/2008	15:07	1-2'	Total Metals	<5	3	13	10	20	42
	D	10/23/2008	15:09	2-4'	Total Metals	<5	3	13	10	16	46
	E	10/23/2008	15:11	4-6'	Total Metals	8	4	12	14	12	43
	F	10/23/2008	15:12	6-8'	Total Metals	14	3	10	15	27	33
	G	10/23/2008	15:14	8-10'	Total Metals	38	8	12	14	18	43
	H	10/23/2008	15:16	10-12'	Total Metals	15	8	25	30	20	65
	I	10/23/2008	15:30	12-15'	Total Metals	26	<1	52	24	<5	43
	I	10/23/2008	15:30	12-15'	SPLP (mg/L)	<0.1	<0.1	<0.1	<0.1	<0.1	<0.1
BFB2											
	A	10/23/2008	15:48	0-4"	Total Metals	2890	2720	773	3500	7	3460
	B	10/23/2008	15:50	4-12"	Total Metals	1370	202	25	16	41	50
	C	10/23/2008	15:52	1-2'	Total Metals	742	148	22	21	33	143
	D	10/23/2008	15:53	2-4'	Total Metals	192	10	16	14	27	45
	E	10/23/2008	15:55	4-6'	Total Metals	252	12	15	12	27	47
	F	10/23/2008	15:56	6-8'	Total Metals	128	3	15	11	25	44
	G	10/23/2008	15:58	8-10'	Total Metals	87	3	12	8	23	42
	H	10/23/2008	16:00	10-12'	Total Metals	135	3	12	10	22	43
	I	10/23/2008	16:05	12-15'	Total Metals	130	<1	19	25	<5	38
	I	10/23/2008	16:05	12-15'	SPLP (mg/L)	0.5	<0.1	<0.1	<0.1	<0.1	<0.1

TABLE B-3 . DEMOLITION FOOTPRINT SOIL SAMPLE INDICATOR METALS SUMMARY TABLE

Site/ Sample #	Sample Interval (ft)	Sample Date (m/d/y)	Sample Time (hr/min/sec)	Description Interval (ft)	Analytical Parameters	As (mg/kg)	Cd (mg/kg)	CU (mg/kg)	Pb (mg/kg)	Se (mg/kg)	Zn (mg/kg)
BFB3											
	A	10/23/2008	16:19	0-4"	Total Metals	1850	762	33	367	12	860
	B	10/23/2008	16:21	4-12"	Total Metals	23	4	17	15	44	45
	C	10/23/2008	16:23	1-2'	Total Metals	21	1	16	10	46	43
	D	10/23/2008	16:24	2-4'	Total Metals	13	2	17	7	49	47
	E	10/23/2008	16:25	4-6'	Total Metals	22	2	12	9	22	39
	F	10/23/2008	16:27	6-8'	Total Metals	12	3	14	21	22	45
	G	10/23/2008	16:29	8-10'	Total Metals	72	17	18	23	31	67
	H	10/23/2008	16:32	10-12'	Total Metals	19	5	17	23	20	47
	I	10/23/2008	16:38	12-15'	Total Metals	7	3	14	15	<5	33
	I	10/23/2008	16:38	12-15'	SPLP (mg/L)	<0.1	<0.1	<0.1	<0.1	<0.1	<0.1
BFB4											
	A	10/24/2008	8:15	0-4"	Total Metals	1760	17300	1650	35200	164	21000
	B	10/24/2008	8:17	4-12"	Total Metals	1170	6820	647	13900	106	9630
	C	10/24/2008	8:20	1-2'	Total Metals	3440	9200	2440	42300	123	23100
	D	10/24/2008	8:21	2-4'	Total Metals	121	314	228	1430	43	1050
	E	10/24/2008	8:23	4-6'	Total Metals	135	408	175	1710	36	1030
	F	10/24/2008	8:26	6-8'	Total Metals	225	960	133	2890	73	2230
	G	10/24/2008	8:27	8-10'	Total Metals	17	20	21	79	35	92
	H	10/24/2008	8:30	10-12'	Total Metals	17	24	15	58	33	68
	I	10/24/2008	8:35	12-15'	Total Metals	8	3	20	24	<5	41
	I	10/24/2008	8:35	12-15'	SPLP (mg/L)	<0.1	<0.1	<0.1	<0.1	<0.1	<0.1
BFB5											
	A	10/24/2008	9:04	0-4"	Total Metals	3520	5270	1390	36500	30	22200
	B	10/24/2008	9:07	4-12"	Total Metals	462	1030	395	5100	49	3380
	C	10/24/2008	9:08	1-2'	Total Metals	1220	789	4380	6290	40	4190
	D	10/24/2008	9:10	2-4'	Total Metals	1030	1290	974	9690	50	5740
	E	10/24/2008	9:13	4-6'	Total Metals	50	4	18	34	33	47
	F	10/24/2008	9:14	6-8'	Total Metals	65	101	35	197	41	218
	G	10/24/2008	9:17	8-10'	Total Metals	29	5	23	22	32	56
	H	10/24/2008	9:24	10-12'	Total Metals	24	4	14	12	12	35
	I	10/24/2008	9:29	12-15'	Total Metals	39	29	32	179	<5	159
	I	10/24/2008	9:29	12-15'	SPLP (mg/L)	<0.1	<0.1	<0.1	<0.1	<0.1	<0.1
BLF1											
	A	10/27/2008	15:20	0-4"	Total Metals	3580	9680	2610	25600	80	22200
	B	10/27/2008	15:23	4-12"	Total Metals	145	873	315	3030	59	1460
	C	10/27/2008	15:26	1-2'	Total Metals	55	220	86	684	26	427
	D	10/27/2008	15:29	2-4'	Total Metals	56	194	67	492	21	351
	E	10/27/2008	15:32	4-6'	Total Metals	62	290	92	917	27	517
	F	10/27/2008	15:36	6-8'	Total Metals	82	523	137	1410	28	862
	G	10/27/2008	15:42	8-10'	Total Metals	25	29	33	98	22	79
	H	10/27/2008	15:47	10-12'	Total Metals	23	95	55	286	15	193
	I	10/27/2008	15:55	12-15'	Total Metals	19	7	80	33	<5	53
	I	10/27/2008	15:55	12-15'	SPLP (mg/L)	<0.1	<0.1	<0.1	<0.1	<0.1	<0.1

TABLE B-3 . DEMOLITION FOOTPRINT SOIL SAMPLE INDICATOR METALS SUMMARY TABLE

Site/ Sample #	Sample Interval (ft)	Sample Date (m/d/y)	Sample Time (hr/min/sec)	Description Interval (ft)	Analytical Parameters	As (mg/kg)	Cd (mg/kg)	CU (mg/kg)	Pb (mg/kg)	Se (mg/kg)	Zn (mg/kg)
BLF2											
	A	10/27/2008	16:10	0-4"	Total Metals	1100	894	400	2300	7	2080
	B	10/27/2008	16:15	4-12"	Total Metals	1500	1550	73	95	24	3100
	C	10/27/2008	16:17	1-2'	Total Metals	2200	1920	116	225	28	3590
	D	10/27/2008	16:19	2-4'	Total Metals	757	312	32	26	15	1020
	E	10/27/2008	16:20	4-6'	Total Metals	1020	508	37	41	21	1440
	F	10/27/2008	16:23	6-8'	Total Metals	2250	753	68	31	35	2610
	G	10/27/2008	16:28	8-10'	Total Metals	740	290	33	14	24	861
	H	10/27/2008	16:32	10-12'	Total Metals	1420	541	73	19	30	2530
	I	10/27/2008	16:39	12-15'	Total Metals	649	160	52	17	<5	553
	I	10/27/2008	16:39	12-15'	SPLP (mg/L)	5.5	<0.1	<0.1	<0.1	<0.1	<0.1
BLF3											
	A	10/28/2008	8:10	0-4"	Total Metals	2400	648	690	3630	11	2360
	B	10/28/2008	8:30	4-12"	Total Metals	1330	1540	397	4900	30	4190
	C	10/28/2008	8:32	1-2'	Total Metals	907	1390	244	1750	17	3120
	D	10/28/2008	8:35	2-4'	Total Metals	901	404	69	374	30	1060
	E	10/28/2008	8:36	4-6'	Total Metals	217	83	44	97	7	215
	E	10/28/2008	8:36	4-6'	SPLP (mg/L)	0.4	<0.1	<0.1	<0.1	<0.1	0.2
BLF4											
	A	10/28/2008	8:45	0-4"	Total Metals	1050	494	472	2760	<5	1240
	B	10/28/2008	8:50	4-12"	Total Metals	125	6	112	958	9	90
	C	10/28/2008	8:52	1-2'	Total Metals	111	3	62	145	<5	36
	D	10/28/2008	8:55	2-4'	Total Metals	33	30	22	20	<5	68
	D	10/28/2008	8:55	2-4'	SPLP (mg/L)	0.2	<0.1	<0.1	<0.1	<0.1	<0.1
BLF5											
	A	10/28/2008	9:25	0-4"	Total Metals	797	172	246	1650	<5	1360
	B	10/28/2008	9:28	4-12"	Total Metals	28	15	36	<5	19	52
	C	10/28/2008	9:31	1-2'	Total Metals	17	5	16	<5	8	21
	D	10/28/2008	9:33	2-4'	Total Metals	25	29	12	<5	6	41
	E	10/28/2008	9:35	4-6'	Total Metals	14	4	12	<5	13	20
	F	10/28/2008	9:36	6-8'	Total Metals	546	34	15	597	14	188
	G	10/28/2008	9:39	8-10'	Total Metals	69	1	27	24	<5	59
	G	10/28/2008	9:39	8-10'	SPLP (mg/L)	0.2	<0.1	<0.1	<0.1	<0.1	0.3
BLF6											
	A	10/28/2008	9:52	0-4"	Total Metals	680	526	606	2780	9	2620
	B	10/28/2008	9:54	4-12"	Total Metals	247	700	87	290	29	371
	C	10/28/2008	9:56	1-2'	Total Metals	900	483	267	54	20	787
	D	10/28/2008	9:58	2-4'	Total Metals	389	110	69	102	17	695
	E	10/28/2008	10:00	4-6'	Total Metals	646	53	39	29	<5	429
	E	10/28/2008	10:00	4-6'	SPLP (mg/L)	2.3	<0.1	<0.1	<0.1	<0.1	0.5

TABLE B-3 . DEMOLITION FOOTPRINT SOIL SAMPLE INDICATOR METALS SUMMARY TABLE

Site/ Sample #	Sample Interval (ft)	Sample Date (m/d/y)	Sample Time (hr/min/sec)	Description Interval (ft)	Analytical Parameters	As (mg/kg)	Cd (mg/kg)	CU (mg/kg)	Pb (mg/kg)	Se (mg/kg)	Zn (mg/kg)
BLF7											
	A	10/28/2008	10:10	0-4"	Total Metals	1720	2200	11100	17600	28	6690
	B	10/28/2008	10:12	4-12"	Total Metals	1520	456	175	1120	35	974
	C	10/28/2008	10:14	1-2'	Total Metals	29400	11200	1840	53400	133	15700
	D	10/28/2008	10:15	2-4'	Total Metals	1600	216	99	820	50	480
	E	10/28/2008	10:17	4-6'	Total Metals	1720	91	84	204	39	228
	F	10/28/2008	10:20	6-8'	Total Metals	887	152	70	258	35	176
	G	10/28/2008	10:23	8-10'	Total Metals	1220	260	172	306	57	321
	H	10/28/2008	10:35	10-12'	Total Metals	652	580	86	55	28	749
	I	10/28/2008	10:44	12-15'	Total Metals	186	137	34	19	<5	188
	I	10/28/2008	10:44	12-15'	SPLP (mg/L)	1.8	0.2	<0.1	0.1	<0.1	0.4
MOF1											
	A	10/23/2008	10:05	0-4"	Total Metals	3850	14600	7640	52900	229	29700
	B	10/23/2008	10:10	4-12"	Total Metals	3230	13100	4820	49300	251	24200
	C	10/23/2008	10:12	1-2'	Total Metals	409	5120	568	4940	57	8020
	D	10/23/2008	10:15	2-4'	Total Metals	84	5830	52	253	41	3690
	E	10/23/2008	10:52	4-6'	Total Metals	120	2850	121	706	31	2680
	F	10/23/2008	10:55	6-8'	Total Metals	51	348	43	174	21	451
	G	10/23/2008	11:05	8-10'	Total Metals	113	1560	146	668	28	1730
	H	10/23/2008	11:19	10-12'	Total Metals	56	484	79	225	22	928
	I	10/23/2008	11:33	12-15'	Total Metals	37	341	52	76	<5	736
	I	10/23/2008	11:33	12-15'	SPLP (mg/L)	<0.1	<0.1	<0.1	<0.1	<0.1	<0.1
MOF2											
	A	10/23/2008	11:50	0-4"	Total Metals	4090	21400	7080	59200	374	41400
	B	10/23/2008	13:20	4-12"	Total Metals	11500	75300	17100	52800	1310	113000
	C	10/23/2008	13:22	1-2'	Total Metals	1110	8420	2140	16800	83	13800
	D	10/23/2008	13:25	2-4'	Total Metals	1100	8310	2600	16500	77	13800
	E	10/23/2008	13:28	4-6'	Total Metals	15	49	30	156	13	131
	F	10/23/2008	13:30	6-8'	Total Metals	33	63	51	201	38	174
	G	10/23/2008	13:35	8-10'	Total Metals	13	190	20	52	34	102
	H	10/23/2008	13:40	10-12'	Total Metals	42	22	64	56	23	114
	I	10/23/2008	13:45	12-15'	Total Metals	126	374	241	1520	<5	971
	I	10/23/2008	13:45	12-15'	SPLP (mg/L)	<0.1	<0.1	<0.1	<0.1	<0.1	<0.1
MOF3											
	A	10/23/2008	13:55	0-4"	Total Metals	1500	7350	2340	22900	93	13500
	B	10/23/2008	14:00	4-12"	Total Metals	7550	24200	8450	52500	312	62700
	C	10/23/2008	14:02	1-2'	Total Metals	2890	9350	3540	38300	130	26200
	D	10/23/2008	14:05	2-4'	Total Metals	74	135	84	485	25	420
	E	10/23/2008	14:07	4-6'	Total Metals	17	12	19	49	27	66
	F	10/23/2008	14:10	6-8'	Total Metals	33	15	27	54	8	76
	G	10/23/2008	14:15	8-10'	Total Metals	25	34	34	104	6	98
	H	10/23/2008	14:20	10-12'	Total Metals	63	223	89	691	16	434
	I	10/23/2008	14:25	12-15'	Total Metals	7	9	20	43	<5	36
	I	10/23/2008	14:25	12-15'	SPLP (mg/L)	<0.1	<0.1	<0.1	<0.1	<0.1	<0.1

TABLE B-4. DEMOLITION FOOTPRINT SOIL SAMPLE LABORATORY RESULTS

Sample ID	Collection Date	Analyte	TResult	NResult	Runits	Rlimit	ParLabel
ACP1-A	10/27/2008 13:45	Silver		59	mg/kg	5	AG
ACP1-A	10/27/2008 13:45	Aluminum		5090	mg/kg	5	AL
ACP1-A	10/27/2008 13:45	Arsenic		302	mg/kg	5	AS
ACP1-A	10/27/2008 13:45	Barium		111	mg/kg	5	BA
ACP1-A	10/27/2008 13:45	Beryllium	ND		mg/kg	5	BE
ACP1-A	10/27/2008 13:45	Cadmium		385	mg/kg	1	CD
ACP1-A	10/27/2008 13:45	Cobalt		21	mg/kg	5	CO
ACP1-A	10/27/2008 13:45	Chromium		31	mg/kg	5	CR
ACP1-A	10/27/2008 13:45	Copper		910	mg/kg	5	CU
ACP1-A	10/27/2008 13:45	Iron		26300	mg/kg	10	FE
ACP1-A	10/27/2008 13:45	Mercury		280	mg/kg	40	HG
ACP1-A	10/27/2008 13:45	Manganese		1110	mg/kg	5	MN
ACP1-A	10/27/2008 13:45	Nickel		86	mg/kg	5	NI
ACP1-A	10/27/2008 13:45	Lead		5650	mg/kg	5	PB
ACP1-A	10/27/2008 13:45	Antimony		65	mg/kg	5	SB
ACP1-A	10/27/2008 13:45	Selenium		13	mg/kg	5	SE
ACP1-A	10/27/2008 13:45	Thallium		8	mg/kg	5	TL
ACP1-A	10/27/2008 13:45	Vanadium		23	mg/kg	5	V
ACP1-A	10/27/2008 13:45	Zinc		4290	mg/kg	5	ZN
ACP1-B	10/27/2008 13:50	Arsenic		109	mg/kg	5	AS
ACP1-B	10/27/2008 13:50	Cadmium		37	mg/kg	1	CD
ACP1-B	10/27/2008 13:50	Copper		110	mg/kg	5	CU
ACP1-B	10/27/2008 13:50	Lead		494	mg/kg	5	PB
ACP1-B	10/27/2008 13:50	Selenium		35	mg/kg	5	SE
ACP1-B	10/27/2008 13:50	Zinc		332	mg/kg	5	ZN
ACP1-C	10/27/2008 13:52	Arsenic		413	mg/kg	5	AS
ACP1-C	10/27/2008 13:52	Cadmium		435	mg/kg	1	CD
ACP1-C	10/27/2008 13:52	Copper		820	mg/kg	5	CU
ACP1-C	10/27/2008 13:52	Lead		7330	mg/kg	5	PB
ACP1-C	10/27/2008 13:52	Selenium		42	mg/kg	5	SE
ACP1-C	10/27/2008 13:52	Zinc		8370	mg/kg	5	ZN
ACP1-D	10/27/2008 13:54	Arsenic		52	mg/kg	5	AS
ACP1-D	10/27/2008 13:54	Cadmium		11	mg/kg	1	CD
ACP1-D	10/27/2008 13:54	Copper		43	mg/kg	5	CU
ACP1-D	10/27/2008 13:54	Lead		175	mg/kg	5	PB
ACP1-D	10/27/2008 13:54	Selenium		31	mg/kg	5	SE
ACP1-D	10/27/2008 13:54	Zinc		112	mg/kg	5	ZN
ACP1-E	10/27/2008 13:57	Arsenic		71	mg/kg	5	AS
ACP1-E	10/27/2008 13:57	Cadmium		27	mg/kg	1	CD
ACP1-E	10/27/2008 13:57	Copper		126	mg/kg	5	CU
ACP1-E	10/27/2008 13:57	Lead		626	mg/kg	5	PB
ACP1-E	10/27/2008 13:57	Selenium		31	mg/kg	5	SE
ACP1-E	10/27/2008 13:57	Zinc		532	mg/kg	5	ZN
ACP1-F	10/27/2008 13:59	Arsenic		33	mg/kg	5	AS
ACP1-F	10/27/2008 13:59	Cadmium		19	mg/kg	1	CD
ACP1-F	10/27/2008 13:59	Copper		34	mg/kg	5	CU
ACP1-F	10/27/2008 13:59	Lead		95	mg/kg	5	PB
ACP1-F	10/27/2008 13:59	Selenium		18	mg/kg	5	SE
ACP1-F	10/27/2008 13:59	Zinc		97	mg/kg	5	ZN
ACP1-G	10/27/2008 14:08	Arsenic		32	mg/kg	5	AS
ACP1-G	10/27/2008 14:08	Cadmium		20	mg/kg	1	CD

TABLE B-4. DEMOLITION FOOTPRINT SOIL SAMPLE LABORATORY RESULTS

Sample ID	Collection Date	Analyte	TResult	NResult	Runits	Rlimit	ParLabel
ACP1-G	10/27/2008 14:08	Copper		58	mg/kg	5	CU
ACP1-G	10/27/2008 14:08	Lead		170	mg/kg	5	PB
ACP1-G	10/27/2008 14:08	Selenium		19	mg/kg	5	SE
ACP1-G	10/27/2008 14:08	Zinc		167	mg/kg	5	ZN
ACP1-H	10/27/2008 14:15	Arsenic		27	mg/kg	5	AS
ACP1-H	10/27/2008 14:15	Cadmium		4	mg/kg	1	CD
ACP1-H	10/27/2008 14:15	Copper		55	mg/kg	5	CU
ACP1-H	10/27/2008 14:15	Lead		71	mg/kg	5	PB
ACP1-H	10/27/2008 14:15	Selenium		30	mg/kg	5	SE
ACP1-H	10/27/2008 14:15	Zinc		130	mg/kg	5	ZN
ACP1-I	10/27/2008 14:22	Silver	ND		mg/kg	5	AG
ACP1-I	10/27/2008 14:22	Aluminum		6350	mg/kg	5	AL
ACP1-I	10/27/2008 14:22	Arsenic	ND		mg/L	0.1	AS
ACP1-I	10/27/2008 14:22	Arsenic		21	mg/kg	5	AS
ACP1-I	10/27/2008 14:22	Barium		84	mg/kg	5	BA
ACP1-I	10/27/2008 14:22	Beryllium	ND		mg/kg	5	BE
ACP1-I	10/27/2008 14:22	Cadmium	ND		mg/L	0.1	CD
ACP1-I	10/27/2008 14:22	Cadmium		10	mg/kg	1	CD
ACP1-I	10/27/2008 14:22	Cobalt		5	mg/kg	5	CO
ACP1-I	10/27/2008 14:22	Chromium		9	mg/kg	5	CR
ACP1-I	10/27/2008 14:22	Copper	ND		mg/L	0.1	CU
ACP1-I	10/27/2008 14:22	Copper		48	mg/kg	5	CU
ACP1-I	10/27/2008 14:22	Iron		15800	mg/kg	10	FE
ACP1-I	10/27/2008 14:22	Mercury		2.4	mg/kg	0.4	HG
ACP1-I	10/27/2008 14:22	Manganese		625	mg/kg	5	MN
ACP1-I	10/27/2008 14:22	Nickel		7	mg/kg	5	NI
ACP1-I	10/27/2008 14:22	Lead	ND		mg/L	0.1	PB
ACP1-I	10/27/2008 14:22	Lead		90	mg/kg	5	PB
ACP1-I	10/27/2008 14:22	Antimony	ND		mg/kg	5	SB
ACP1-I	10/27/2008 14:22	Selenium	ND		mg/L	0.1	SE
ACP1-I	10/27/2008 14:22	Selenium	ND		mg/kg	5	SE
ACP1-I	10/27/2008 14:22	Thallium	ND		mg/kg	5	TL
ACP1-I	10/27/2008 14:22	Vanadium		36	mg/kg	5	V
ACP1-I	10/27/2008 14:22	Zinc	ND		mg/L	0.1	ZN
ACP1-I	10/27/2008 14:22	Zinc		167	mg/kg	5	ZN
ACP2-A	10/27/2008 14:40	Silver		58	mg/kg	5	AG
ACP2-A	10/27/2008 14:40	Aluminum		7430	mg/kg	5	AL
ACP2-A	10/27/2008 14:40	Arsenic		1000	mg/kg	5	AS
ACP2-A	10/27/2008 14:40	Barium		308	mg/kg	5	BA
ACP2-A	10/27/2008 14:40	Beryllium	ND		mg/kg	5	BE
ACP2-A	10/27/2008 14:40	Cadmium		160	mg/kg	1	CD
ACP2-A	10/27/2008 14:40	Cobalt		13	mg/kg	5	CO
ACP2-A	10/27/2008 14:40	Chromium		19	mg/kg	5	CR
ACP2-A	10/27/2008 14:40	Copper		1020	mg/kg	5	CU
ACP2-A	10/27/2008 14:40	Iron		61700	mg/kg	10	FE
ACP2-A	10/27/2008 14:40	Mercury		550	mg/kg	40	HG
ACP2-A	10/27/2008 14:40	Manganese		2230	mg/kg	5	MN
ACP2-A	10/27/2008 14:40	Nickel		9	mg/kg	5	NI
ACP2-A	10/27/2008 14:40	Lead		7630	mg/kg	5	PB
ACP2-A	10/27/2008 14:40	Antimony		64	mg/kg	5	SB
ACP2-A	10/27/2008 14:40	Selenium		12	mg/kg	5	SE

TABLE B-4. DEMOLITION FOOTPRINT SOIL SAMPLE LABORATORY RESULTS

Sample ID	Collection Date	Analyte	TResult	NResult	Runits	Rlimit	ParLabel
ACP2-A	10/27/2008 14:40	Thallium		6	mg/kg	5	TL
ACP2-A	10/27/2008 14:40	Vanadium		29	mg/kg	5	V
ACP2-A	10/27/2008 14:40	Zinc		6070	mg/kg	5	ZN
ACP2-B	10/27/2008 14:44	Arsenic		50	mg/kg	5	AS
ACP2-B	10/27/2008 14:44	Cadmium		25	mg/kg	1	CD
ACP2-B	10/27/2008 14:44	Copper		125	mg/kg	5	CU
ACP2-B	10/27/2008 14:44	Lead		16	mg/kg	5	PB
ACP2-B	10/27/2008 14:44	Selenium		34	mg/kg	5	SE
ACP2-B	10/27/2008 14:44	Zinc		678	mg/kg	5	ZN
ACP2-C	10/27/2008 14:46	Arsenic		27	mg/kg	5	AS
ACP2-C	10/27/2008 14:46	Cadmium		1	mg/kg	1	CD
ACP2-C	10/27/2008 14:46	Copper		14	mg/kg	5	CU
ACP2-C	10/27/2008 14:46	Lead		19	mg/kg	5	PB
ACP2-C	10/27/2008 14:46	Selenium		31	mg/kg	5	SE
ACP2-C	10/27/2008 14:46	Zinc		196	mg/kg	5	ZN
ACP2-D	10/27/2008 14:48	Arsenic		24	mg/kg	5	AS
ACP2-D	10/27/2008 14:48	Cadmium		1	mg/kg	1	CD
ACP2-D	10/27/2008 14:48	Copper		15	mg/kg	5	CU
ACP2-D	10/27/2008 14:48	Lead		35	mg/kg	5	PB
ACP2-D	10/27/2008 14:48	Selenium		28	mg/kg	5	SE
ACP2-D	10/27/2008 14:48	Zinc		44	mg/kg	5	ZN
ACP2-E	10/27/2008 14:50	Arsenic		31	mg/kg	5	AS
ACP2-E	10/27/2008 14:50	Cadmium		3	mg/kg	1	CD
ACP2-E	10/27/2008 14:50	Copper		17	mg/kg	5	CU
ACP2-E	10/27/2008 14:50	Lead		28	mg/kg	5	PB
ACP2-E	10/27/2008 14:50	Selenium		48	mg/kg	5	SE
ACP2-E	10/27/2008 14:50	Zinc		42	mg/kg	5	ZN
ACP2-F	10/27/2008 14:53	Arsenic		39	mg/kg	5	AS
ACP2-F	10/27/2008 14:53	Cadmium		1	mg/kg	1	CD
ACP2-F	10/27/2008 14:53	Copper		25	mg/kg	5	CU
ACP2-F	10/27/2008 14:53	Lead		23	mg/kg	5	PB
ACP2-F	10/27/2008 14:53	Selenium		29	mg/kg	5	SE
ACP2-F	10/27/2008 14:53	Zinc		52	mg/kg	5	ZN
ACP2-G	10/27/2008 14:55	Arsenic		30	mg/kg	5	AS
ACP2-G	10/27/2008 14:55	Cadmium	ND		mg/kg	1	CD
ACP2-G	10/27/2008 14:55	Copper		25	mg/kg	5	CU
ACP2-G	10/27/2008 14:55	Lead		18	mg/kg	5	PB
ACP2-G	10/27/2008 14:55	Selenium		27	mg/kg	5	SE
ACP2-G	10/27/2008 14:55	Zinc		50	mg/kg	5	ZN
ACP2-H	10/27/2008 14:59	Arsenic		22	mg/kg	5	AS
ACP2-H	10/27/2008 14:59	Cadmium	ND		mg/kg	1	CD
ACP2-H	10/27/2008 14:59	Copper		23	mg/kg	5	CU
ACP2-H	10/27/2008 14:59	Lead		16	mg/kg	5	PB
ACP2-H	10/27/2008 14:59	Selenium		30	mg/kg	5	SE
ACP2-H	10/27/2008 14:59	Zinc		57	mg/kg	5	ZN
ACP2-I	10/27/2008 15:09	Silver	ND		mg/kg	5	AG
ACP2-I	10/27/2008 15:09	Aluminum		9540	mg/kg	5	AL
ACP2-I	10/27/2008 15:09	Arsenic	ND		mg/L	0.1	AS
ACP2-I	10/27/2008 15:09	Arsenic		31	mg/kg	5	AS
ACP2-I	10/27/2008 15:09	Barium		50	mg/kg	5	BA
ACP2-I	10/27/2008 15:09	Beryllium	ND		mg/kg	5	BE

TABLE B-4. DEMOLITION FOOTPRINT SOIL SAMPLE LABORATORY RESULTS

Sample ID	Collection Date	Analyte	TResult	NResult	Runits	Rlimit	ParLabel
ACP2-I	10/27/2008 15:09	Cadmium	ND		mg/L	0.1	CD
ACP2-I	10/27/2008 15:09	Cadmium	ND		mg/kg	1	CD
ACP2-I	10/27/2008 15:09	Cobalt		6	mg/kg	5	CO
ACP2-I	10/27/2008 15:09	Chromium		14	mg/kg	5	CR
ACP2-I	10/27/2008 15:09	Copper	ND		mg/L	0.1	CU
ACP2-I	10/27/2008 15:09	Copper		33	mg/kg	5	CU
ACP2-I	10/27/2008 15:09	Iron		20700	mg/kg	10	FE
ACP2-I	10/27/2008 15:09	Mercury	ND		mg/kg	0.05	HG
ACP2-I	10/27/2008 15:09	Manganese		360	mg/kg	5	MN
ACP2-I	10/27/2008 15:09	Nickel		8	mg/kg	5	NI
ACP2-I	10/27/2008 15:09	Lead		33	mg/kg	5	PB
ACP2-I	10/27/2008 15:09	Lead	ND		mg/L	0.1	PB
ACP2-I	10/27/2008 15:09	Antimony	ND		mg/kg	5	SB
ACP2-I	10/27/2008 15:09	Selenium	ND		mg/L	0.1	SE
ACP2-I	10/27/2008 15:09	Selenium	ND		mg/kg	5	SE
ACP2-I	10/27/2008 15:09	Thallium	ND		mg/kg	5	TL
ACP2-I	10/27/2008 15:09	Vanadium		58	mg/kg	5	V
ACP2-I	10/27/2008 15:09	Zinc		47	mg/kg	5	ZN
ACP2-I	10/27/2008 15:09	Zinc	ND		mg/L	0.1	ZN
ACP2-I2	10/27/2008 15:11	Silver	ND		mg/kg	5	AG
ACP2-I2	10/27/2008 15:11	Aluminum		12000	mg/kg	5	AL
ACP2-I2	10/27/2008 15:11	Arsenic	ND		mg/L	0.1	AS
ACP2-I2	10/27/2008 15:11	Arsenic		28	mg/kg	5	AS
ACP2-I2	10/27/2008 15:11	Barium		86	mg/kg	5	BA
ACP2-I2	10/27/2008 15:11	Beryllium	ND		mg/kg	5	BE
ACP2-I2	10/27/2008 15:11	Cadmium	ND		mg/L	0.1	CD
ACP2-I2	10/27/2008 15:11	Cadmium	ND		mg/kg	1	CD
ACP2-I2	10/27/2008 15:11	Cobalt		8	mg/kg	5	CO
ACP2-I2	10/27/2008 15:11	Chromium		17	mg/kg	5	CR
ACP2-I2	10/27/2008 15:11	Copper	ND		mg/L	0.1	CU
ACP2-I2	10/27/2008 15:11	Copper		43	mg/kg	5	CU
ACP2-I2	10/27/2008 15:11	Iron		27800	mg/kg	10	FE
ACP2-I2	10/27/2008 15:11	Mercury		0.36	mg/kg	0.05	HG
ACP2-I2	10/27/2008 15:11	Manganese		400	mg/kg	5	MN
ACP2-I2	10/27/2008 15:11	Nickel		9	mg/kg	5	NI
ACP2-I2	10/27/2008 15:11	Lead	ND		mg/L	0.1	PB
ACP2-I2	10/27/2008 15:11	Lead		24	mg/kg	5	PB
ACP2-I2	10/27/2008 15:11	Antimony	ND		mg/kg	5	SB
ACP2-I2	10/27/2008 15:11	Selenium	ND		mg/kg	5	SE
ACP2-I2	10/27/2008 15:11	Selenium	ND		mg/L	0.1	SE
ACP2-I2	10/27/2008 15:11	Thallium	ND		mg/kg	5	TL
ACP2-I2	10/27/2008 15:11	Vanadium		75	mg/kg	5	V
ACP2-I2	10/27/2008 15:11	Zinc		57	mg/kg	5	ZN
ACP2-I2	10/27/2008 15:11	Zinc	ND		mg/L	0.1	ZN
BFB1-A	10/23/2008 15:02	Silver	ND		mg/kg	5	AG
BFB1-A	10/23/2008 15:02	Aluminum		11600	mg/kg	5	AL
BFB1-A	10/23/2008 15:02	Arsenic		930	mg/kg	5	AS
BFB1-A	10/23/2008 15:02	Barium		124	mg/kg	5	BA
BFB1-A	10/23/2008 15:02	Beryllium	ND		mg/kg	5	BE
BFB1-A	10/23/2008 15:02	Cadmium		1790	mg/kg	1	CD
BFB1-A	10/23/2008 15:02	Cobalt		6	mg/kg	5	CO

TABLE B-4. DEMOLITION FOOTPRINT SOIL SAMPLE LABORATORY RESULTS

Sample ID	Collection Date	Analyte	TResult	NResult	Runits	Rlimit	ParLabel
BFB1-A	10/23/2008 15:02	Chromium		16	mg/kg	5	CR
BFB1-A	10/23/2008 15:02	Copper		70	mg/kg	5	CU
BFB1-A	10/23/2008 15:02	Iron		14800	mg/kg	10	FE
BFB1-A	10/23/2008 15:02	Mercury		9.8	mg/kg	0.4	HG
BFB1-A	10/23/2008 15:02	Manganese		312	mg/kg	5	MN
BFB1-A	10/23/2008 15:02	Nickel		12	mg/kg	5	NI
BFB1-A	10/23/2008 15:02	Lead		1180	mg/kg	5	PB
BFB1-A	10/23/2008 15:02	Antimony	ND		mg/kg	5	SB
BFB1-A	10/23/2008 15:02	Selenium	ND		mg/kg	5	SE
BFB1-A	10/23/2008 15:02	Thallium		15	mg/kg	5	TL
BFB1-A	10/23/2008 15:02	Vanadium		34	mg/kg	5	V
BFB1-A	10/23/2008 15:02	Zinc		3770	mg/kg	5	ZN
BFB1-B	10/23/2008 15:05	Arsenic		15	mg/kg	5	AS
BFB1-B	10/23/2008 15:05	Cadmium		6	mg/kg	1	CD
BFB1-B	10/23/2008 15:05	Copper		21	mg/kg	5	CU
BFB1-B	10/23/2008 15:05	Lead		26	mg/kg	5	PB
BFB1-B	10/23/2008 15:05	Selenium		42	mg/kg	5	SE
BFB1-B	10/23/2008 15:05	Zinc		55	mg/kg	5	ZN
BFB1-C	10/23/2008 15:07	Arsenic	ND		mg/kg	5	AS
BFB1-C	10/23/2008 15:07	Cadmium		3	mg/kg	1	CD
BFB1-C	10/23/2008 15:07	Copper		13	mg/kg	5	CU
BFB1-C	10/23/2008 15:07	Lead		10	mg/kg	5	PB
BFB1-C	10/23/2008 15:07	Selenium		20	mg/kg	5	SE
BFB1-C	10/23/2008 15:07	Zinc		42	mg/kg	5	ZN
BFB1-D	10/23/2008 15:09	Arsenic	ND		mg/kg	5	AS
BFB1-D	10/23/2008 15:09	Cadmium		3	mg/kg	1	CD
BFB1-D	10/23/2008 15:09	Copper		13	mg/kg	5	CU
BFB1-D	10/23/2008 15:09	Lead		10	mg/kg	5	PB
BFB1-D	10/23/2008 15:09	Selenium		16	mg/kg	5	SE
BFB1-D	10/23/2008 15:09	Zinc		46	mg/kg	5	ZN
BFB1-E	10/23/2008 15:11	Arsenic		8	mg/kg	5	AS
BFB1-E	10/23/2008 15:11	Cadmium		4	mg/kg	1	CD
BFB1-E	10/23/2008 15:11	Copper		12	mg/kg	5	CU
BFB1-E	10/23/2008 15:11	Lead		14	mg/kg	5	PB
BFB1-E	10/23/2008 15:11	Selenium		12	mg/kg	5	SE
BFB1-E	10/23/2008 15:11	Zinc		43	mg/kg	5	ZN
BFB1-F	10/23/2008 15:12	Arsenic		14	mg/kg	5	AS
BFB1-F	10/23/2008 15:12	Cadmium		3	mg/kg	1	CD
BFB1-F	10/23/2008 15:12	Copper		10	mg/kg	5	CU
BFB1-F	10/23/2008 15:12	Lead		15	mg/kg	5	PB
BFB1-F	10/23/2008 15:12	Selenium		27	mg/kg	5	SE
BFB1-F	10/23/2008 15:12	Zinc		33	mg/kg	5	ZN
BFB1-G	10/23/2008 15:14	Arsenic		38	mg/kg	5	AS
BFB1-G	10/23/2008 15:14	Cadmium		8	mg/kg	1	CD
BFB1-G	10/23/2008 15:14	Copper		12	mg/kg	5	CU
BFB1-G	10/23/2008 15:14	Lead		14	mg/kg	5	PB
BFB1-G	10/23/2008 15:14	Selenium		18	mg/kg	5	SE
BFB1-G	10/23/2008 15:14	Zinc		43	mg/kg	5	ZN
BFB1-H	10/23/2008 15:16	Arsenic		15	mg/kg	5	AS
BFB1-H	10/23/2008 15:16	Cadmium		8	mg/kg	1	CD
BFB1-H	10/23/2008 15:16	Copper		25	mg/kg	5	CU

TABLE B-4. DEMOLITION FOOTPRINT SOIL SAMPLE LABORATORY RESULTS

Sample ID	Collection Date	Analyte	TResult	NResult	Runits	Rlimit	ParLabel
BFB1-H	10/23/2008 15:16	Lead		30	mg/kg	5	PB
BFB1-H	10/23/2008 15:16	Selenium		20	mg/kg	5	SE
BFB1-H	10/23/2008 15:16	Zinc		65	mg/kg	5	ZN
BFB1-I	10/23/2008 15:30	Silver	ND		mg/kg	5	AG
BFB1-I	10/23/2008 15:30	Aluminum		8090	mg/kg	5	AL
BFB1-I	10/23/2008 15:30	Arsenic	ND		mg/L	0.1	AS
BFB1-I	10/23/2008 15:30	Arsenic		26	mg/kg	5	AS
BFB1-I	10/23/2008 15:30	Barium		34	mg/kg	5	BA
BFB1-I	10/23/2008 15:30	Beryllium	ND		mg/kg	5	BE
BFB1-I	10/23/2008 15:30	Cadmium	ND		mg/kg	1	CD
BFB1-I	10/23/2008 15:30	Cadmium	ND		mg/L	0.1	CD
BFB1-I	10/23/2008 15:30	Cobalt		9	mg/kg	5	CO
BFB1-I	10/23/2008 15:30	Chromium		23	mg/kg	5	CR
BFB1-I	10/23/2008 15:30	Copper	ND		mg/L	0.1	CU
BFB1-I	10/23/2008 15:30	Copper		52	mg/kg	5	CU
BFB1-I	10/23/2008 15:30	Iron		40100	mg/kg	10	FE
BFB1-I	10/23/2008 15:30	Mercury	ND		mg/kg	0.05	HG
BFB1-I	10/23/2008 15:30	Manganese		369	mg/kg	5	MN
BFB1-I	10/23/2008 15:30	Nickel		9	mg/kg	5	NI
BFB1-I	10/23/2008 15:30	Lead	ND		mg/L	0.1	PB
BFB1-I	10/23/2008 15:30	Lead		24	mg/kg	5	PB
BFB1-I	10/23/2008 15:30	Antimony	ND		mg/kg	5	SB
BFB1-I	10/23/2008 15:30	Selenium	ND		mg/L	0.1	SE
BFB1-I	10/23/2008 15:30	Selenium	ND		mg/kg	5	SE
BFB1-I	10/23/2008 15:30	Thallium	ND		mg/kg	5	TL
BFB1-I	10/23/2008 15:30	Vanadium		115	mg/kg	5	V
BFB1-I	10/23/2008 15:30	Zinc		43	mg/kg	5	ZN
BFB1-I	10/23/2008 15:30	Zinc	ND		mg/L	0.1	ZN
BFB2-A	10/23/2008 15:48	Silver		17	mg/kg	5	AG
BFB2-A	10/23/2008 15:48	Aluminum		13700	mg/kg	5	AL
BFB2-A	10/23/2008 15:48	Arsenic		2890	mg/kg	5	AS
BFB2-A	10/23/2008 15:48	Barium		150	mg/kg	5	BA
BFB2-A	10/23/2008 15:48	Beryllium	ND		mg/kg	5	BE
BFB2-A	10/23/2008 15:48	Cadmium		2720	mg/kg	1	CD
BFB2-A	10/23/2008 15:48	Cobalt		12	mg/kg	5	CO
BFB2-A	10/23/2008 15:48	Chromium		16	mg/kg	5	CR
BFB2-A	10/23/2008 15:48	Copper		773	mg/kg	5	CU
BFB2-A	10/23/2008 15:48	Iron		18400	mg/kg	10	FE
BFB2-A	10/23/2008 15:48	Mercury		58	mg/kg	4	HG
BFB2-A	10/23/2008 15:48	Manganese		429	mg/kg	5	MN
BFB2-A	10/23/2008 15:48	Nickel		20	mg/kg	5	NI
BFB2-A	10/23/2008 15:48	Lead		3500	mg/kg	5	PB
BFB2-A	10/23/2008 15:48	Antimony		36	mg/kg	5	SB
BFB2-A	10/23/2008 15:48	Selenium		7	mg/kg	5	SE
BFB2-A	10/23/2008 15:48	Thallium		26	mg/kg	5	TL
BFB2-A	10/23/2008 15:48	Vanadium		41	mg/kg	5	V
BFB2-A	10/23/2008 15:48	Zinc		3460	mg/kg	5	ZN
BFB2-B	10/23/2008 15:50	Arsenic		1370	mg/kg	5	AS
BFB2-B	10/23/2008 15:50	Cadmium		202	mg/kg	1	CD
BFB2-B	10/23/2008 15:50	Copper		25	mg/kg	5	CU
BFB2-B	10/23/2008 15:50	Lead		16	mg/kg	5	PB

TABLE B-4. DEMOLITION FOOTPRINT SOIL SAMPLE LABORATORY RESULTS

Sample ID	Collection Date	Analyte	TResult	NResult	Runits	Rlimit	ParLabel
BFB2-B	10/23/2008 15:50	Selenium		41	mg/kg	5	SE
BFB2-B	10/23/2008 15:50	Zinc		50	mg/kg	5	ZN
BFB2-C	10/23/2008 15:52	Arsenic		742	mg/kg	5	AS
BFB2-C	10/23/2008 15:52	Cadmium		148	mg/kg	1	CD
BFB2-C	10/23/2008 15:52	Copper		22	mg/kg	5	CU
BFB2-C	10/23/2008 15:52	Lead		21	mg/kg	5	PB
BFB2-C	10/23/2008 15:52	Selenium		33	mg/kg	5	SE
BFB2-C	10/23/2008 15:52	Zinc		143	mg/kg	5	ZN
BFB2-D	10/23/2008 15:53	Arsenic		192	mg/kg	5	AS
BFB2-D	10/23/2008 15:53	Cadmium		10	mg/kg	1	CD
BFB2-D	10/23/2008 15:53	Copper		16	mg/kg	5	CU
BFB2-D	10/23/2008 15:53	Lead		14	mg/kg	5	PB
BFB2-D	10/23/2008 15:53	Selenium		27	mg/kg	5	SE
BFB2-D	10/23/2008 15:53	Zinc		45	mg/kg	5	ZN
BFB2-D2	10/23/2008 15:54	Arsenic		252	mg/kg	5	AS
BFB2-D2	10/23/2008 15:54	Cadmium		12	mg/kg	1	CD
BFB2-D2	10/23/2008 15:54	Copper		15	mg/kg	5	CU
BFB2-D2	10/23/2008 15:54	Lead		12	mg/kg	5	PB
BFB2-D2	10/23/2008 15:54	Selenium		27	mg/kg	5	SE
BFB2-D2	10/23/2008 15:54	Zinc		47	mg/kg	5	ZN
BFB2-E	10/23/2008 15:55	Arsenic		128	mg/kg	5	AS
BFB2-E	10/23/2008 15:55	Cadmium		3	mg/kg	1	CD
BFB2-E	10/23/2008 15:55	Copper		15	mg/kg	5	CU
BFB2-E	10/23/2008 15:55	Lead		11	mg/kg	5	PB
BFB2-E	10/23/2008 15:55	Selenium		25	mg/kg	5	SE
BFB2-E	10/23/2008 15:55	Zinc		44	mg/kg	5	ZN
BFB2-F	10/23/2008 15:56	Arsenic		105	mg/kg	5	AS
BFB2-F	10/23/2008 15:56	Cadmium		3	mg/kg	1	CD
BFB2-F	10/23/2008 15:56	Copper		13	mg/kg	5	CU
BFB2-F	10/23/2008 15:56	Lead		17	mg/kg	5	PB
BFB2-F	10/23/2008 15:56	Selenium		30	mg/kg	5	SE
BFB2-F	10/23/2008 15:56	Zinc		40	mg/kg	5	ZN
BFB2-G	10/23/2008 15:58	Arsenic		87	mg/kg	5	AS
BFB2-G	10/23/2008 15:58	Cadmium		3	mg/kg	1	CD
BFB2-G	10/23/2008 15:58	Copper		12	mg/kg	5	CU
BFB2-G	10/23/2008 15:58	Lead		8	mg/kg	5	PB
BFB2-G	10/23/2008 15:58	Selenium		23	mg/kg	5	SE
BFB2-G	10/23/2008 15:58	Zinc		42	mg/kg	5	ZN
BFB2-H	10/23/2008 16:00	Arsenic		135	mg/kg	5	AS
BFB2-H	10/23/2008 16:00	Cadmium		3	mg/kg	1	CD
BFB2-H	10/23/2008 16:00	Copper		12	mg/kg	5	CU
BFB2-H	10/23/2008 16:00	Lead		10	mg/kg	5	PB
BFB2-H	10/23/2008 16:00	Selenium		22	mg/kg	5	SE
BFB2-H	10/23/2008 16:00	Zinc		43	mg/kg	5	ZN
BFB2-I	10/23/2008 16:05	Silver	ND		mg/kg	5	AG
BFB2-I	10/23/2008 16:05	Aluminum		13800	mg/kg	5	AL
BFB2-I	10/23/2008 16:05	Arsenic		130	mg/kg	5	AS
BFB2-I	10/23/2008 16:05	Arsenic		0.5	mg/L	0.1	AS
BFB2-I	10/23/2008 16:05	Barium		136	mg/kg	5	BA
BFB2-I	10/23/2008 16:05	Beryllium	ND		mg/kg	5	BE
BFB2-I	10/23/2008 16:05	Cadmium	ND		mg/kg	1	CD

TABLE B-4. DEMOLITION FOOTPRINT SOIL SAMPLE LABORATORY RESULTS

Sample ID	Collection Date	Analyte	TResult	NResult	Runits	Rlimit	ParLabel
BFB2-I	10/23/2008 16:05	Cadmium	ND		mg/L	0.1	CD
BFB2-I	10/23/2008 16:05	Cobalt		6	mg/kg	5	CO
BFB2-I	10/23/2008 16:05	Chromium		14	mg/kg	5	CR
BFB2-I	10/23/2008 16:05	Copper	ND		mg/L	0.1	CU
BFB2-I	10/23/2008 16:05	Copper		19	mg/kg	5	CU
BFB2-I	10/23/2008 16:05	Iron		23300	mg/kg	10	FE
BFB2-I	10/23/2008 16:05	Mercury		0.11	mg/kg	0.05	HG
BFB2-I	10/23/2008 16:05	Manganese		323	mg/kg	5	MN
BFB2-I	10/23/2008 16:05	Nickel		7	mg/kg	5	NI
BFB2-I	10/23/2008 16:05	Lead	ND		mg/L	0.1	PB
BFB2-I	10/23/2008 16:05	Lead		25	mg/kg	5	PB
BFB2-I	10/23/2008 16:05	Antimony	ND		mg/kg	5	SB
BFB2-I	10/23/2008 16:05	Selenium	ND		mg/L	0.1	SE
BFB2-I	10/23/2008 16:05	Selenium	ND		mg/kg	5	SE
BFB2-I	10/23/2008 16:05	Thallium	ND		mg/kg	5	TL
BFB2-I	10/23/2008 16:05	Vanadium		59	mg/kg	5	V
BFB2-I	10/23/2008 16:05	Zinc	ND		mg/L	0.1	ZN
BFB2-I	10/23/2008 16:05	Zinc		38	mg/kg	5	ZN
BFB3-A	10/23/2008 16:19	Silver	ND		mg/kg	5	AG
BFB3-A	10/23/2008 16:19	Aluminum		14100	mg/kg	5	AL
BFB3-A	10/23/2008 16:19	Arsenic		1850	mg/kg	5	AS
BFB3-A	10/23/2008 16:19	Barium		300	mg/kg	5	BA
BFB3-A	10/23/2008 16:19	Beryllium	ND		mg/kg	5	BE
BFB3-A	10/23/2008 16:19	Cadmium		762	mg/kg	1	CD
BFB3-A	10/23/2008 16:19	Cobalt		6	mg/kg	5	CO
BFB3-A	10/23/2008 16:19	Chromium		15	mg/kg	5	CR
BFB3-A	10/23/2008 16:19	Copper		33	mg/kg	5	CU
BFB3-A	10/23/2008 16:19	Iron		16500	mg/kg	10	FE
BFB3-A	10/23/2008 16:19	Mercury		5.8	mg/kg	0.4	HG
BFB3-A	10/23/2008 16:19	Manganese		308	mg/kg	5	MN
BFB3-A	10/23/2008 16:19	Nickel		12	mg/kg	5	NI
BFB3-A	10/23/2008 16:19	Lead		367	mg/kg	5	PB
BFB3-A	10/23/2008 16:19	Antimony	ND		mg/kg	5	SB
BFB3-A	10/23/2008 16:19	Selenium		12	mg/kg	5	SE
BFB3-A	10/23/2008 16:19	Thallium		7	mg/kg	5	TL
BFB3-A	10/23/2008 16:19	Vanadium		34	mg/kg	5	V
BFB3-A	10/23/2008 16:19	Zinc		860	mg/kg	5	ZN
BFB3-B	10/23/2008 16:21	Arsenic		23	mg/kg	5	AS
BFB3-B	10/23/2008 16:21	Cadmium		4	mg/kg	1	CD
BFB3-B	10/23/2008 16:21	Copper		17	mg/kg	5	CU
BFB3-B	10/23/2008 16:21	Lead		15	mg/kg	5	PB
BFB3-B	10/23/2008 16:21	Selenium		44	mg/kg	5	SE
BFB3-B	10/23/2008 16:21	Zinc		45	mg/kg	5	ZN
BFB3-B2	10/23/2008 16:22	Arsenic		21	mg/kg	5	AS
BFB3-B2	10/23/2008 16:22	Cadmium		1	mg/kg	1	CD
BFB3-B2	10/23/2008 16:22	Copper		16	mg/kg	5	CU
BFB3-B2	10/23/2008 16:22	Lead		10	mg/kg	5	PB
BFB3-B2	10/23/2008 16:22	Selenium		46	mg/kg	5	SE
BFB3-B2	10/23/2008 16:22	Zinc		43	mg/kg	5	ZN
BFB3-C	10/23/2008 16:23	Arsenic		34	mg/kg	5	AS
BFB3-C	10/23/2008 16:23	Cadmium		9	mg/kg	1	CD

TABLE B-4. DEMOLITION FOOTPRINT SOIL SAMPLE LABORATORY RESULTS

Sample ID	Collection Date	Analyte	TResult	NResult	Runits	Rlimit	ParLabel
BFB3-C	10/23/2008 16:23	Copper		19	mg/kg	5	CU
BFB3-C	10/23/2008 16:23	Lead		16	mg/kg	5	PB
BFB3-C	10/23/2008 16:23	Selenium		39	mg/kg	5	SE
BFB3-C	10/23/2008 16:23	Zinc		51	mg/kg	5	ZN
BFB3-D	10/23/2008 16:24	Arsenic		13	mg/kg	5	AS
BFB3-D	10/23/2008 16:24	Cadmium		2	mg/kg	1	CD
BFB3-D	10/23/2008 16:24	Copper		17	mg/kg	5	CU
BFB3-D	10/23/2008 16:24	Lead		7	mg/kg	5	PB
BFB3-D	10/23/2008 16:24	Selenium		49	mg/kg	5	SE
BFB3-D	10/23/2008 16:24	Zinc		47	mg/kg	5	ZN
BFB3-E	10/23/2008 16:25	Arsenic		22	mg/kg	5	AS
BFB3-E	10/23/2008 16:25	Cadmium		2	mg/kg	1	CD
BFB3-E	10/23/2008 16:25	Copper		12	mg/kg	5	CU
BFB3-E	10/23/2008 16:25	Lead		9	mg/kg	5	PB
BFB3-E	10/23/2008 16:25	Selenium		22	mg/kg	5	SE
BFB3-E	10/23/2008 16:25	Zinc		39	mg/kg	5	ZN
BFB3-F	10/23/2008 16:27	Arsenic		12	mg/kg	5	AS
BFB3-F	10/23/2008 16:27	Cadmium		3	mg/kg	1	CD
BFB3-F	10/23/2008 16:27	Copper		14	mg/kg	5	CU
BFB3-F	10/23/2008 16:27	Lead		21	mg/kg	5	PB
BFB3-F	10/23/2008 16:27	Selenium		22	mg/kg	5	SE
BFB3-F	10/23/2008 16:27	Zinc		45	mg/kg	5	ZN
BFB3-G	10/23/2008 16:29	Arsenic		72	mg/kg	5	AS
BFB3-G	10/23/2008 16:29	Cadmium		17	mg/kg	1	CD
BFB3-G	10/23/2008 16:29	Copper		18	mg/kg	5	CU
BFB3-G	10/23/2008 16:29	Lead		23	mg/kg	5	PB
BFB3-G	10/23/2008 16:29	Selenium		31	mg/kg	5	SE
BFB3-G	10/23/2008 16:29	Zinc		67	mg/kg	5	ZN
BFB3-H	10/23/2008 16:32	Arsenic		19	mg/kg	5	AS
BFB3-H	10/23/2008 16:32	Cadmium		5	mg/kg	1	CD
BFB3-H	10/23/2008 16:32	Copper		17	mg/kg	5	CU
BFB3-H	10/23/2008 16:32	Lead		23	mg/kg	5	PB
BFB3-H	10/23/2008 16:32	Selenium		20	mg/kg	5	SE
BFB3-H	10/23/2008 16:32	Zinc		47	mg/kg	5	ZN
BFB3-I	10/23/2008 16:38	Silver	ND		mg/kg	5	AG
BFB3-I	10/23/2008 16:38	Aluminum		4960	mg/kg	5	AL
BFB3-I	10/23/2008 16:38	Arsenic	ND		mg/L	0.1	AS
BFB3-I	10/23/2008 16:38	Arsenic		7	mg/kg	5	AS
BFB3-I	10/23/2008 16:38	Barium		42	mg/kg	5	BA
BFB3-I	10/23/2008 16:38	Beryllium	ND		mg/kg	5	BE
BFB3-I	10/23/2008 16:38	Cadmium	ND		mg/L	0.1	CD
BFB3-I	10/23/2008 16:38	Cadmium		3	mg/kg	1	CD
BFB3-I	10/23/2008 16:38	Cobalt	ND		mg/kg	5	CO
BFB3-I	10/23/2008 16:38	Chromium		13	mg/kg	5	CR
BFB3-I	10/23/2008 16:38	Copper	ND		mg/L	0.1	CU
BFB3-I	10/23/2008 16:38	Copper		14	mg/kg	5	CU
BFB3-I	10/23/2008 16:38	Iron		16500	mg/kg	10	FE
BFB3-I	10/23/2008 16:38	Mercury		0.062	mg/kg	0.05	HG
BFB3-I	10/23/2008 16:38	Manganese		188	mg/kg	5	MN
BFB3-I	10/23/2008 16:38	Nickel	ND		mg/kg	5	NI
BFB3-I	10/23/2008 16:38	Lead	ND		mg/L	0.1	PB

TABLE B-4. DEMOLITION FOOTPRINT SOIL SAMPLE LABORATORY RESULTS

Sample ID	Collection Date	Analyte	TResult	NResult	Runits	Rlimit	ParLabel
BFB3-I	10/23/2008 16:38	Lead		15	mg/kg	5	PB
BFB3-I	10/23/2008 16:38	Antimony	ND		mg/kg	5	SB
BFB3-I	10/23/2008 16:38	Selenium	ND		mg/L	0.1	SE
BFB3-I	10/23/2008 16:38	Selenium	ND		mg/kg	5	SE
BFB3-I	10/23/2008 16:38	Thallium	ND		mg/kg	5	TL
BFB3-I	10/23/2008 16:38	Vanadium		50	mg/kg	5	V
BFB3-I	10/23/2008 16:38	Zinc	ND		mg/L	0.1	ZN
BFB3-I	10/23/2008 16:38	Zinc		33	mg/kg	5	ZN
BFB4-A	10/24/2008 8:15	Silver		103	mg/kg	5	AG
BFB4-A	10/24/2008 8:15	Aluminum		4600	mg/kg	5	AL
BFB4-A	10/24/2008 8:15	Arsenic		1760	mg/kg	7	AS
BFB4-A	10/24/2008 8:15	Barium		189	mg/kg	5	BA
BFB4-A	10/24/2008 8:15	Beryllium	ND		mg/kg	5	BE
BFB4-A	10/24/2008 8:15	Cadmium		17300	mg/kg	1	CD
BFB4-A	10/24/2008 8:15	Cobalt		14	mg/kg	5	CO
BFB4-A	10/24/2008 8:15	Chromium		13	mg/kg	5	CR
BFB4-A	10/24/2008 8:15	Copper		1650	mg/kg	5	CU
BFB4-A	10/24/2008 8:15	Iron		13700	mg/kg	20	FE
BFB4-A	10/24/2008 8:15	Mercury		8.4	mg/kg	0.4	HG
BFB4-A	10/24/2008 8:15	Manganese		532	mg/kg	5	MN
BFB4-A	10/24/2008 8:15	Nickel		16	mg/kg	5	NI
BFB4-A	10/24/2008 8:15	Lead		35200	mg/kg	5	PB
BFB4-A	10/24/2008 8:15	Antimony		121	mg/kg	6	SB
BFB4-A	10/24/2008 8:15	Selenium		164	mg/kg	5	SE
BFB4-A	10/24/2008 8:15	Thallium		272	mg/kg	5	TL
BFB4-A	10/24/2008 8:15	Vanadium		16	mg/kg	5	V
BFB4-A	10/24/2008 8:15	Zinc		21000	mg/kg	5	ZN
BFB4-B	10/24/2008 8:17	Arsenic		1170	mg/kg	5	AS
BFB4-B	10/24/2008 8:17	Cadmium		6820	mg/kg	1	CD
BFB4-B	10/24/2008 8:17	Copper		647	mg/kg	5	CU
BFB4-B	10/24/2008 8:17	Lead		13900	mg/kg	5	PB
BFB4-B	10/24/2008 8:17	Selenium		106	mg/kg	5	SE
BFB4-B	10/24/2008 8:17	Zinc		9630	mg/kg	5	ZN
BFB4-C	10/24/2008 8:20	Arsenic		3440	mg/kg	5	AS
BFB4-C	10/24/2008 8:20	Cadmium		9200	mg/kg	1	CD
BFB4-C	10/24/2008 8:20	Copper		2440	mg/kg	5	CU
BFB4-C	10/24/2008 8:20	Lead		42300	mg/kg	5	PB
BFB4-C	10/24/2008 8:20	Selenium		123	mg/kg	5	SE
BFB4-C	10/24/2008 8:20	Zinc		23100	mg/kg	5	ZN
BFB4-D	10/24/2008 8:21	Arsenic		121	mg/kg	5	AS
BFB4-D	10/24/2008 8:21	Cadmium		314	mg/kg	1	CD
BFB4-D	10/24/2008 8:21	Copper		228	mg/kg	5	CU
BFB4-D	10/24/2008 8:21	Lead		1430	mg/kg	5	PB
BFB4-D	10/24/2008 8:21	Selenium		43	mg/kg	5	SE
BFB4-D	10/24/2008 8:21	Zinc		1050	mg/kg	5	ZN
BFB4-E	10/24/2008 8:23	Arsenic		135	mg/kg	5	AS
BFB4-E	10/24/2008 8:23	Cadmium		408	mg/kg	1	CD
BFB4-E	10/24/2008 8:23	Copper		175	mg/kg	5	CU
BFB4-E	10/24/2008 8:23	Lead		1710	mg/kg	5	PB
BFB4-E	10/24/2008 8:23	Selenium		36	mg/kg	5	SE
BFB4-E	10/24/2008 8:23	Zinc		1030	mg/kg	5	ZN

TABLE B-4. DEMOLITION FOOTPRINT SOIL SAMPLE LABORATORY RESULTS

Sample ID	Collection Date	Analyte	TResult	NResult	Runits	Rlimit	ParLabel
BFB4-F	10/24/2008 8:26	Arsenic		225	mg/kg	5	AS
BFB4-F	10/24/2008 8:26	Cadmium		960	mg/kg	1	CD
BFB4-F	10/24/2008 8:26	Copper		133	mg/kg	5	CU
BFB4-F	10/24/2008 8:26	Lead		2890	mg/kg	5	PB
BFB4-F	10/24/2008 8:26	Selenium		73	mg/kg	5	SE
BFB4-F	10/24/2008 8:26	Zinc		2230	mg/kg	5	ZN
BFB4-G	10/24/2008 8:27	Arsenic		17	mg/kg	5	AS
BFB4-G	10/24/2008 8:27	Cadmium		20	mg/kg	1	CD
BFB4-G	10/24/2008 8:27	Copper		21	mg/kg	5	CU
BFB4-G	10/24/2008 8:27	Lead		79	mg/kg	5	PB
BFB4-G	10/24/2008 8:27	Selenium		35	mg/kg	5	SE
BFB4-G	10/24/2008 8:27	Zinc		92	mg/kg	5	ZN
BFB4-H	10/24/2008 8:30	Arsenic		17	mg/kg	5	AS
BFB4-H	10/24/2008 8:30	Cadmium		24	mg/kg	1	CD
BFB4-H	10/24/2008 8:30	Copper		15	mg/kg	5	CU
BFB4-H	10/24/2008 8:30	Lead		58	mg/kg	5	PB
BFB4-H	10/24/2008 8:30	Selenium		33	mg/kg	5	SE
BFB4-H	10/24/2008 8:30	Zinc		68	mg/kg	5	ZN
BFB4-I	10/24/2008 8:35	Silver	ND		mg/kg	5	AG
BFB4-I	10/24/2008 8:35	Aluminum		7730	mg/kg	5	AL
BFB4-I	10/24/2008 8:35	Arsenic	ND		mg/L	0.1	AS
BFB4-I	10/24/2008 8:35	Arsenic		8	mg/kg	5	AS
BFB4-I	10/24/2008 8:35	Barium		60	mg/kg	5	BA
BFB4-I	10/24/2008 8:35	Beryllium	ND		mg/kg	5	BE
BFB4-I	10/24/2008 8:35	Cadmium	ND		mg/L	0.1	CD
BFB4-I	10/24/2008 8:35	Cadmium		3	mg/kg	1	CD
BFB4-I	10/24/2008 8:35	Cobalt	ND		mg/kg	5	CO
BFB4-I	10/24/2008 8:35	Chromium		13	mg/kg	5	CR
BFB4-I	10/24/2008 8:35	Copper	ND		mg/L	0.1	CU
BFB4-I	10/24/2008 8:35	Copper		20	mg/kg	5	CU
BFB4-I	10/24/2008 8:35	Iron		16700	mg/kg	10	FE
BFB4-I	10/24/2008 8:35	Mercury	ND		mg/kg	0.05	HG
BFB4-I	10/24/2008 8:35	Manganese		350	mg/kg	5	MN
BFB4-I	10/24/2008 8:35	Nickel		7	mg/kg	5	NI
BFB4-I	10/24/2008 8:35	Lead	ND		mg/L	0.1	PB
BFB4-I	10/24/2008 8:35	Lead		24	mg/kg	5	PB
BFB4-I	10/24/2008 8:35	Antimony	ND		mg/kg	5	SB
BFB4-I	10/24/2008 8:35	Selenium	ND		mg/L	0.1	SE
BFB4-I	10/24/2008 8:35	Selenium	ND		mg/kg	5	SE
BFB4-I	10/24/2008 8:35	Thallium	ND		mg/kg	5	TL
BFB4-I	10/24/2008 8:35	Vanadium		48	mg/kg	5	V
BFB4-I	10/24/2008 8:35	Zinc		41	mg/kg	5	ZN
BFB4-I	10/24/2008 8:35	Zinc	ND		mg/L	0.1	ZN
BFB5-A	10/24/2008 9:04	Silver		63	mg/kg	5	AG
BFB5-A	10/24/2008 9:04	Aluminum		8810	mg/kg	5	AL
BFB5-A	10/24/2008 9:04	Arsenic		3520	mg/kg	5	AS
BFB5-A	10/24/2008 9:04	Barium		180	mg/kg	5	BA
BFB5-A	10/24/2008 9:04	Beryllium	ND		mg/kg	5	BE
BFB5-A	10/24/2008 9:04	Cadmium		5270	mg/kg	1	CD
BFB5-A	10/24/2008 9:04	Cobalt		10	mg/kg	5	CO
BFB5-A	10/24/2008 9:04	Chromium		14	mg/kg	5	CR

TABLE B-4. DEMOLITION FOOTPRINT SOIL SAMPLE LABORATORY RESULTS

Sample ID	Collection Date	Analyte	TResult	NResult	Runits	Rlimit	ParLabel
BFB5-A	10/24/2008 9:04	Copper		1390	mg/kg	5	CU
BFB5-A	10/24/2008 9:04	Iron		18300	mg/kg	10	FE
BFB5-A	10/24/2008 9:04	Mercury		44	mg/kg	4	HG
BFB5-A	10/24/2008 9:04	Manganese		528	mg/kg	5	MN
BFB5-A	10/24/2008 9:04	Nickel		24	mg/kg	5	NI
BFB5-A	10/24/2008 9:04	Lead		36500	mg/kg	5	PB
BFB5-A	10/24/2008 9:04	Antimony		102	mg/kg	5	SB
BFB5-A	10/24/2008 9:04	Selenium		30	mg/kg	5	SE
BFB5-A	10/24/2008 9:04	Thallium		35	mg/kg	5	TL
BFB5-A	10/24/2008 9:04	Vanadium		30	mg/kg	5	V
BFB5-A	10/24/2008 9:04	Zinc		22200	mg/kg	6	ZN
BFB5-B	10/24/2008 9:07	Arsenic		462	mg/kg	5	AS
BFB5-B	10/24/2008 9:07	Cadmium		1030	mg/kg	1	CD
BFB5-B	10/24/2008 9:07	Copper		395	mg/kg	5	CU
BFB5-B	10/24/2008 9:07	Lead		5100	mg/kg	5	PB
BFB5-B	10/24/2008 9:07	Selenium		49	mg/kg	5	SE
BFB5-B	10/24/2008 9:07	Zinc		3380	mg/kg	5	ZN
BFB5-C	10/24/2008 9:08	Arsenic		1220	mg/kg	5	AS
BFB5-C	10/24/2008 9:08	Cadmium		789	mg/kg	1	CD
BFB5-C	10/24/2008 9:08	Copper		4380	mg/kg	5	CU
BFB5-C	10/24/2008 9:08	Lead		6290	mg/kg	5	PB
BFB5-C	10/24/2008 9:08	Selenium		40	mg/kg	5	SE
BFB5-C	10/24/2008 9:08	Zinc		4190	mg/kg	5	ZN
BFB5-D	10/24/2008 9:10	Arsenic		1030	mg/kg	5	AS
BFB5-D	10/24/2008 9:10	Cadmium		1290	mg/kg	1	CD
BFB5-D	10/24/2008 9:10	Copper		974	mg/kg	5	CU
BFB5-D	10/24/2008 9:10	Lead		9690	mg/kg	5	PB
BFB5-D	10/24/2008 9:10	Selenium		50	mg/kg	5	SE
BFB5-D	10/24/2008 9:10	Zinc		5740	mg/kg	5	ZN
BFB5-E	10/24/2008 9:13	Arsenic		50	mg/kg	5	AS
BFB5-E	10/24/2008 9:13	Cadmium		4	mg/kg	1	CD
BFB5-E	10/24/2008 9:13	Copper		18	mg/kg	5	CU
BFB5-E	10/24/2008 9:13	Lead		34	mg/kg	5	PB
BFB5-E	10/24/2008 9:13	Selenium		33	mg/kg	5	SE
BFB5-E	10/24/2008 9:13	Zinc		47	mg/kg	5	ZN
BFB5-F	10/24/2008 9:14	Arsenic		65	mg/kg	5	AS
BFB5-F	10/24/2008 9:14	Cadmium		101	mg/kg	1	CD
BFB5-F	10/24/2008 9:14	Copper		35	mg/kg	5	CU
BFB5-F	10/24/2008 9:14	Lead		197	mg/kg	5	PB
BFB5-F	10/24/2008 9:14	Selenium		41	mg/kg	5	SE
BFB5-F	10/24/2008 9:14	Zinc		218	mg/kg	5	ZN
BFB5-F2	10/24/2008 9:15	Arsenic		71	mg/kg	5	AS
BFB5-F2	10/24/2008 9:15	Cadmium		247	mg/kg	1	CD
BFB5-F2	10/24/2008 9:15	Copper		36	mg/kg	5	CU
BFB5-F2	10/24/2008 9:15	Lead		182	mg/kg	5	PB
BFB5-F2	10/24/2008 9:15	Selenium		38	mg/kg	5	SE
BFB5-F2	10/24/2008 9:15	Zinc		309	mg/kg	5	ZN
BFB5-G	10/24/2008 9:17	Arsenic		29	mg/kg	5	AS
BFB5-G	10/24/2008 9:17	Cadmium		5	mg/kg	1	CD
BFB5-G	10/24/2008 9:17	Copper		23	mg/kg	5	CU
BFB5-G	10/24/2008 9:17	Lead		22	mg/kg	5	PB

TABLE B-4. DEMOLITION FOOTPRINT SOIL SAMPLE LABORATORY RESULTS

Sample ID	Collection Date	Analyte	TResult	NResult	Runits	Rlimit	ParLabel
BFB5-G	10/24/2008 9:17	Selenium		32	mg/kg	5	SE
BFB5-G	10/24/2008 9:17	Zinc		56	mg/kg	5	ZN
BFB5-H	10/24/2008 9:24	Arsenic		24	mg/kg	5	AS
BFB5-H	10/24/2008 9:24	Cadmium		4	mg/kg	1	CD
BFB5-H	10/24/2008 9:24	Copper		14	mg/kg	5	CU
BFB5-H	10/24/2008 9:24	Lead		12	mg/kg	5	PB
BFB5-H	10/24/2008 9:24	Selenium		12	mg/kg	5	SE
BFB5-H	10/24/2008 9:24	Zinc		35	mg/kg	5	ZN
BFB5-I	10/24/2008 9:29	Silver	ND		mg/kg	5	AG
BFB5-I	10/24/2008 9:29	Aluminum		8800	mg/kg	5	AL
BFB5-I	10/24/2008 9:29	Arsenic	ND		mg/L	0.1	AS
BFB5-I	10/24/2008 9:29	Arsenic		39	mg/kg	5	AS
BFB5-I	10/24/2008 9:29	Barium		66	mg/kg	5	BA
BFB5-I	10/24/2008 9:29	Beryllium	ND		mg/kg	5	BE
BFB5-I	10/24/2008 9:29	Cadmium	ND		mg/L	0.1	CD
BFB5-I	10/24/2008 9:29	Cadmium		29	mg/kg	1	CD
BFB5-I	10/24/2008 9:29	Cobalt		6	mg/kg	5	CO
BFB5-I	10/24/2008 9:29	Chromium		13	mg/kg	5	CR
BFB5-I	10/24/2008 9:29	Copper	ND		mg/L	0.1	CU
BFB5-I	10/24/2008 9:29	Copper		32	mg/kg	5	CU
BFB5-I	10/24/2008 9:29	Iron		19800	mg/kg	10	FE
BFB5-I	10/24/2008 9:29	Mercury		0.31	mg/kg	0.05	HG
BFB5-I	10/24/2008 9:29	Manganese		318	mg/kg	5	MN
BFB5-I	10/24/2008 9:29	Nickel		7	mg/kg	5	NI
BFB5-I	10/24/2008 9:29	Lead		179	mg/kg	5	PB
BFB5-I	10/24/2008 9:29	Lead	ND		mg/L	0.1	PB
BFB5-I	10/24/2008 9:29	Antimony	ND		mg/kg	5	SB
BFB5-I	10/24/2008 9:29	Selenium	ND		mg/L	0.1	SE
BFB5-I	10/24/2008 9:29	Selenium	ND		mg/kg	5	SE
BFB5-I	10/24/2008 9:29	Thallium	ND		mg/kg	5	TL
BFB5-I	10/24/2008 9:29	Vanadium		51	mg/kg	5	V
BFB5-I	10/24/2008 9:29	Zinc		159	mg/kg	5	ZN
BFB5-I	10/24/2008 9:29	Zinc	ND		mg/L	0.1	ZN
BLF1-A	10/27/2008 15:20	Silver		148	mg/kg	5	AG
BLF1-A	10/27/2008 15:20	Aluminum		7820	mg/kg	5	AL
BLF1-A	10/27/2008 15:20	Arsenic		3580	mg/kg	5	AS
BLF1-A	10/27/2008 15:20	Barium		114	mg/kg	5	BA
BLF1-A	10/27/2008 15:20	Beryllium	ND		mg/kg	5	BE
BLF1-A	10/27/2008 15:20	Cadmium		9680	mg/kg	1	CD
BLF1-A	10/27/2008 15:20	Cobalt		11	mg/kg	5	CO
BLF1-A	10/27/2008 15:20	Chromium		15	mg/kg	5	CR
BLF1-A	10/27/2008 15:20	Copper		2610	mg/kg	5	CU
BLF1-A	10/27/2008 15:20	Iron		16600	mg/kg	10	FE
BLF1-A	10/27/2008 15:20	Mercury		60	mg/kg	4	HG
BLF1-A	10/27/2008 15:20	Manganese		376	mg/kg	5	MN
BLF1-A	10/27/2008 15:20	Nickel		32	mg/kg	5	NI
BLF1-A	10/27/2008 15:20	Lead		25600	mg/kg	5	PB
BLF1-A	10/27/2008 15:20	Antimony		153	mg/kg	5	SB
BLF1-A	10/27/2008 15:20	Selenium		80	mg/kg	5	SE
BLF1-A	10/27/2008 15:20	Thallium		154	mg/kg	5	TL
BLF1-A	10/27/2008 15:20	Vanadium		27	mg/kg	5	V

TABLE B-4. DEMOLITION FOOTPRINT SOIL SAMPLE LABORATORY RESULTS

Sample ID	Collection Date	Analyte	TResult	NResult	Runits	Rlimit	ParLabel
BLF1-A	10/27/2008 15:20	Zinc		22200	mg/kg	6	ZN
BLF1-B	10/27/2008 15:23	Arsenic		145	mg/kg	5	AS
BLF1-B	10/27/2008 15:23	Cadmium		873	mg/kg	1	CD
BLF1-B	10/27/2008 15:23	Copper		315	mg/kg	5	CU
BLF1-B	10/27/2008 15:23	Lead		3030	mg/kg	5	PB
BLF1-B	10/27/2008 15:23	Selenium		59	mg/kg	5	SE
BLF1-B	10/27/2008 15:23	Zinc		1460	mg/kg	5	ZN
BLF1-C	10/27/2008 15:26	Arsenic		55	mg/kg	5	AS
BLF1-C	10/27/2008 15:26	Cadmium		220	mg/kg	1	CD
BLF1-C	10/27/2008 15:26	Copper		86	mg/kg	5	CU
BLF1-C	10/27/2008 15:26	Lead		684	mg/kg	5	PB
BLF1-C	10/27/2008 15:26	Selenium		26	mg/kg	5	SE
BLF1-C	10/27/2008 15:26	Zinc		427	mg/kg	5	ZN
BLF1-D	10/27/2008 15:29	Arsenic		56	mg/kg	5	AS
BLF1-D	10/27/2008 15:29	Cadmium		194	mg/kg	1	CD
BLF1-D	10/27/2008 15:29	Copper		67	mg/kg	5	CU
BLF1-D	10/27/2008 15:29	Lead		492	mg/kg	5	PB
BLF1-D	10/27/2008 15:29	Selenium		21	mg/kg	5	SE
BLF1-D	10/27/2008 15:29	Zinc		351	mg/kg	5	ZN
BLF1-E	10/27/2008 15:32	Arsenic		62	mg/kg	5	AS
BLF1-E	10/27/2008 15:32	Cadmium		290	mg/kg	1	CD
BLF1-E	10/27/2008 15:32	Copper		92	mg/kg	5	CU
BLF1-E	10/27/2008 15:32	Lead		917	mg/kg	5	PB
BLF1-E	10/27/2008 15:32	Selenium		27	mg/kg	5	SE
BLF1-E	10/27/2008 15:32	Zinc		517	mg/kg	5	ZN
BLF1-F	10/27/2008 15:36	Arsenic		82	mg/kg	5	AS
BLF1-F	10/27/2008 15:36	Cadmium		523	mg/kg	1	CD
BLF1-F	10/27/2008 15:36	Copper		137	mg/kg	5	CU
BLF1-F	10/27/2008 15:36	Lead		1410	mg/kg	5	PB
BLF1-F	10/27/2008 15:36	Selenium		28	mg/kg	5	SE
BLF1-F	10/27/2008 15:36	Zinc		862	mg/kg	5	ZN
BLF1-G	10/27/2008 15:42	Arsenic		25	mg/kg	5	AS
BLF1-G	10/27/2008 15:42	Cadmium		29	mg/kg	1	CD
BLF1-G	10/27/2008 15:42	Copper		33	mg/kg	5	CU
BLF1-G	10/27/2008 15:42	Lead		98	mg/kg	5	PB
BLF1-G	10/27/2008 15:42	Selenium		22	mg/kg	5	SE
BLF1-G	10/27/2008 15:42	Zinc		79	mg/kg	5	ZN
BLF1-H	10/27/2008 15:47	Arsenic		23	mg/kg	5	AS
BLF1-H	10/27/2008 15:47	Cadmium		95	mg/kg	1	CD
BLF1-H	10/27/2008 15:47	Copper		55	mg/kg	5	CU
BLF1-H	10/27/2008 15:47	Lead		286	mg/kg	5	PB
BLF1-H	10/27/2008 15:47	Selenium		15	mg/kg	5	SE
BLF1-H	10/27/2008 15:47	Zinc		193	mg/kg	5	ZN
BLF1-I	10/27/2008 15:55	Silver	ND		mg/kg	5	AG
BLF1-I	10/27/2008 15:55	Aluminum		10300	mg/kg	5	AL
BLF1-I	10/27/2008 15:55	Arsenic	ND		mg/L	0.1	AS
BLF1-I	10/27/2008 15:55	Arsenic		19	mg/kg	5	AS
BLF1-I	10/27/2008 15:55	Barium		220	mg/kg	5	BA
BLF1-I	10/27/2008 15:55	Beryllium	ND		mg/kg	5	BE
BLF1-I	10/27/2008 15:55	Cadmium	ND		mg/L	0.1	CD
BLF1-I	10/27/2008 15:55	Cadmium		7	mg/kg	1	CD

TABLE B-4. DEMOLITION FOOTPRINT SOIL SAMPLE LABORATORY RESULTS

Sample ID	Collection Date	Analyte	TResult	NResult	Runits	Rlimit	ParLabel
BLF1-I	10/27/2008 15:55	Cobalt		12	mg/kg	5	CO
BLF1-I	10/27/2008 15:55	Chromium		12	mg/kg	5	CR
BLF1-I	10/27/2008 15:55	Copper	ND		mg/L	0.1	CU
BLF1-I	10/27/2008 15:55	Copper		80	mg/kg	5	CU
BLF1-I	10/27/2008 15:55	Iron		24100	mg/kg	10	FE
BLF1-I	10/27/2008 15:55	Mercury	ND		mg/kg	0.05	HG
BLF1-I	10/27/2008 15:55	Manganese		1140	mg/kg	5	MN
BLF1-I	10/27/2008 15:55	Nickel		10	mg/kg	5	NI
BLF1-I	10/27/2008 15:55	Lead	ND		mg/L	0.1	PB
BLF1-I	10/27/2008 15:55	Lead		33	mg/kg	5	PB
BLF1-I	10/27/2008 15:55	Antimony	ND		mg/kg	5	SB
BLF1-I	10/27/2008 15:55	Selenium	ND		mg/L	0.1	SE
BLF1-I	10/27/2008 15:55	Selenium	ND		mg/kg	5	SE
BLF1-I	10/27/2008 15:55	Thallium	ND		mg/kg	5	TL
BLF1-I	10/27/2008 15:55	Vanadium		49	mg/kg	5	V
BLF1-I	10/27/2008 15:55	Zinc	ND		mg/L	0.1	ZN
BLF1-I	10/27/2008 15:55	Zinc		53	mg/kg	5	ZN
BLF2-A	10/27/2008 16:10	Silver		23	mg/kg	5	AG
BLF2-A	10/27/2008 16:10	Aluminum		9490	mg/kg	5	AL
BLF2-A	10/27/2008 16:10	Arsenic		1100	mg/kg	5	AS
BLF2-A	10/27/2008 16:10	Barium		172	mg/kg	5	BA
BLF2-A	10/27/2008 16:10	Beryllium	ND		mg/kg	5	BE
BLF2-A	10/27/2008 16:10	Cadmium		894	mg/kg	1	CD
BLF2-A	10/27/2008 16:10	Cobalt		7	mg/kg	5	CO
BLF2-A	10/27/2008 16:10	Chromium		12	mg/kg	5	CR
BLF2-A	10/27/2008 16:10	Copper		400	mg/kg	5	CU
BLF2-A	10/27/2008 16:10	Iron		19200	mg/kg	10	FE
BLF2-A	10/27/2008 16:10	Mercury		17	mg/kg	4	HG
BLF2-A	10/27/2008 16:10	Manganese		415	mg/kg	5	MN
BLF2-A	10/27/2008 16:10	Nickel		12	mg/kg	5	NI
BLF2-A	10/27/2008 16:10	Lead		2300	mg/kg	5	PB
BLF2-A	10/27/2008 16:10	Antimony		20	mg/kg	5	SB
BLF2-A	10/27/2008 16:10	Selenium		7	mg/kg	5	SE
BLF2-A	10/27/2008 16:10	Thallium		82	mg/kg	5	TL
BLF2-A	10/27/2008 16:10	Vanadium		41	mg/kg	5	V
BLF2-A	10/27/2008 16:10	Zinc		2080	mg/kg	5	ZN
BLF2-B	10/27/2008 16:15	Arsenic		1500	mg/kg	5	AS
BLF2-B	10/27/2008 16:15	Cadmium		1550	mg/kg	1	CD
BLF2-B	10/27/2008 16:15	Copper		73	mg/kg	5	CU
BLF2-B	10/27/2008 16:15	Lead		95	mg/kg	5	PB
BLF2-B	10/27/2008 16:15	Selenium		24	mg/kg	5	SE
BLF2-B	10/27/2008 16:15	Zinc		3100	mg/kg	5	ZN
BLF2-B2	10/27/2008 16:16	Arsenic		1590	mg/kg	5	AS
BLF2-B2	10/27/2008 16:16	Cadmium		1610	mg/kg	1	CD
BLF2-B2	10/27/2008 16:16	Copper		74	mg/kg	5	CU
BLF2-B2	10/27/2008 16:16	Lead		86	mg/kg	5	PB
BLF2-B2	10/27/2008 16:16	Selenium		28	mg/kg	5	SE
BLF2-B2	10/27/2008 16:16	Zinc		3160	mg/kg	5	ZN
BLF2-C	10/27/2008 16:17	Arsenic		2200	mg/kg	5	AS
BLF2-C	10/27/2008 16:17	Cadmium		1920	mg/kg	1	CD
BLF2-C	10/27/2008 16:17	Copper		116	mg/kg	5	CU

TABLE B-4. DEMOLITION FOOTPRINT SOIL SAMPLE LABORATORY RESULTS

Sample ID	Collection Date	Analyte	TResult	NResult	Runits	Rlimit	ParLabel
BLF2-C	10/27/2008 16:17	Lead		225	mg/kg	5	PB
BLF2-C	10/27/2008 16:17	Selenium		28	mg/kg	5	SE
BLF2-C	10/27/2008 16:17	Zinc		3590	mg/kg	5	ZN
BLF2-D	10/27/2008 16:19	Arsenic		757	mg/kg	5	AS
BLF2-D	10/27/2008 16:19	Cadmium		312	mg/kg	1	CD
BLF2-D	10/27/2008 16:19	Copper		32	mg/kg	5	CU
BLF2-D	10/27/2008 16:19	Lead		26	mg/kg	5	PB
BLF2-D	10/27/2008 16:19	Selenium		15	mg/kg	5	SE
BLF2-D	10/27/2008 16:19	Zinc		1020	mg/kg	5	ZN
BLF2-E	10/27/2008 16:20	Arsenic		1020	mg/kg	5	AS
BLF2-E	10/27/2008 16:20	Cadmium		508	mg/kg	1	CD
BLF2-E	10/27/2008 16:20	Copper		37	mg/kg	5	CU
BLF2-E	10/27/2008 16:20	Lead		41	mg/kg	5	PB
BLF2-E	10/27/2008 16:20	Selenium		21	mg/kg	5	SE
BLF2-E	10/27/2008 16:20	Zinc		1440	mg/kg	5	ZN
BLF2-F	10/27/2008 16:23	Arsenic		2250	mg/kg	5	AS
BLF2-F	10/27/2008 16:23	Cadmium		753	mg/kg	1	CD
BLF2-F	10/27/2008 16:23	Copper		68	mg/kg	5	CU
BLF2-F	10/27/2008 16:23	Lead		31	mg/kg	5	PB
BLF2-F	10/27/2008 16:23	Selenium		35	mg/kg	5	SE
BLF2-F	10/27/2008 16:23	Zinc		2610	mg/kg	5	ZN
BLF2-G	10/27/2008 16:28	Arsenic		740	mg/kg	5	AS
BLF2-G	10/27/2008 16:28	Cadmium		290	mg/kg	1	CD
BLF2-G	10/27/2008 16:28	Copper		33	mg/kg	5	CU
BLF2-G	10/27/2008 16:28	Lead		14	mg/kg	5	PB
BLF2-G	10/27/2008 16:28	Selenium		24	mg/kg	5	SE
BLF2-G	10/27/2008 16:28	Zinc		861	mg/kg	5	ZN
BLF2-H	10/27/2008 16:32	Arsenic		1420	mg/kg	5	AS
BLF2-H	10/27/2008 16:32	Cadmium		541	mg/kg	1	CD
BLF2-H	10/27/2008 16:32	Copper		73	mg/kg	5	CU
BLF2-H	10/27/2008 16:32	Lead		19	mg/kg	5	PB
BLF2-H	10/27/2008 16:32	Selenium		30	mg/kg	5	SE
BLF2-H	10/27/2008 16:32	Zinc		2530	mg/kg	5	ZN
BLF2-I	10/27/2008 16:39	Silver	ND		mg/kg	5	AG
BLF2-I	10/27/2008 16:39	Aluminum		8400	mg/kg	5	AL
BLF2-I	10/27/2008 16:39	Arsenic		5.5	mg/L	0.1	AS
BLF2-I	10/27/2008 16:39	Arsenic		649	mg/kg	5	AS
BLF2-I	10/27/2008 16:39	Barium		71	mg/kg	5	BA
BLF2-I	10/27/2008 16:39	Beryllium	ND		mg/kg	5	BE
BLF2-I	10/27/2008 16:39	Cadmium		160	mg/kg	1	CD
BLF2-I	10/27/2008 16:39	Cadmium	ND		mg/L	0.1	CD
BLF2-I	10/27/2008 16:39	Cobalt	ND		mg/kg	5	CO
BLF2-I	10/27/2008 16:39	Chromium		10	mg/kg	5	CR
BLF2-I	10/27/2008 16:39	Copper	ND		mg/L	0.1	CU
BLF2-I	10/27/2008 16:39	Copper		52	mg/kg	5	CU
BLF2-I	10/27/2008 16:39	Iron		14400	mg/kg	10	FE
BLF2-I	10/27/2008 16:39	Mercury		1.8	mg/kg	0.08	HG
BLF2-I	10/27/2008 16:39	Manganese		159	mg/kg	5	MN
BLF2-I	10/27/2008 16:39	Nickel		6	mg/kg	5	NI
BLF2-I	10/27/2008 16:39	Lead		17	mg/kg	5	PB
BLF2-I	10/27/2008 16:39	Lead	ND		mg/L	0.1	PB

TABLE B-4. DEMOLITION FOOTPRINT SOIL SAMPLE LABORATORY RESULTS

Sample ID	Collection Date	Analyte	TResult	NResult	Runits	Rlimit	ParLabel
BLF2-I	10/27/2008 16:39	Antimony	ND		mg/kg	5	SB
BLF2-I	10/27/2008 16:39	Selenium	ND		mg/L	0.1	SE
BLF2-I	10/27/2008 16:39	Selenium	ND		mg/kg	5	SE
BLF2-I	10/27/2008 16:39	Thallium		21	mg/kg	5	TL
BLF2-I	10/27/2008 16:39	Vanadium		36	mg/kg	5	V
BLF2-I	10/27/2008 16:39	Zinc	ND		mg/L	0.1	ZN
BLF2-I	10/27/2008 16:39	Zinc		553	mg/kg	5	ZN
BLF3-A	10/28/2008 8:10	Silver		30	mg/kg	5	AG
BLF3-A	10/28/2008 8:10	Aluminum		7660	mg/kg	5	AL
BLF3-A	10/28/2008 8:10	Arsenic		2400	mg/kg	5	AS
BLF3-A	10/28/2008 8:10	Barium		191	mg/kg	5	BA
BLF3-A	10/28/2008 8:10	Beryllium	ND		mg/kg	5	BE
BLF3-A	10/28/2008 8:10	Cadmium		648	mg/kg	1	CD
BLF3-A	10/28/2008 8:10	Cobalt		5	mg/kg	5	CO
BLF3-A	10/28/2008 8:10	Chromium		8	mg/kg	5	CR
BLF3-A	10/28/2008 8:10	Copper		690	mg/kg	5	CU
BLF3-A	10/28/2008 8:10	Iron		12600	mg/kg	10	FE
BLF3-A	10/28/2008 8:10	Mercury		28	mg/kg	4	HG
BLF3-A	10/28/2008 8:10	Manganese		347	mg/kg	5	MN
BLF3-A	10/28/2008 8:10	Nickel		14	mg/kg	5	NI
BLF3-A	10/28/2008 8:10	Lead		3630	mg/kg	5	PB
BLF3-A	10/28/2008 8:10	Antimony		37	mg/kg	5	SB
BLF3-A	10/28/2008 8:10	Selenium		11	mg/kg	5	SE
BLF3-A	10/28/2008 8:10	Thallium		34	mg/kg	5	TL
BLF3-A	10/28/2008 8:10	Vanadium		33	mg/kg	5	V
BLF3-A	10/28/2008 8:10	Zinc		2360	mg/kg	5	ZN
BLF3-B	10/28/2008 8:30	Arsenic		1330	mg/kg	5	AS
BLF3-B	10/28/2008 8:30	Cadmium		1540	mg/kg	1	CD
BLF3-B	10/28/2008 8:30	Copper		397	mg/kg	5	CU
BLF3-B	10/28/2008 8:30	Lead		4900	mg/kg	5	PB
BLF3-B	10/28/2008 8:30	Selenium		30	mg/kg	5	SE
BLF3-B	10/28/2008 8:30	Zinc		4190	mg/kg	5	ZN
BLF3-C	10/28/2008 8:32	Arsenic		907	mg/kg	5	AS
BLF3-C	10/28/2008 8:32	Cadmium		1390	mg/kg	1	CD
BLF3-C	10/28/2008 8:32	Copper		244	mg/kg	5	CU
BLF3-C	10/28/2008 8:32	Lead		1750	mg/kg	5	PB
BLF3-C	10/28/2008 8:32	Selenium		17	mg/kg	5	SE
BLF3-C	10/28/2008 8:32	Zinc		3120	mg/kg	5	ZN
BLF3-D	10/28/2008 8:35	Arsenic		901	mg/kg	5	AS
BLF3-D	10/28/2008 8:35	Cadmium		404	mg/kg	1	CD
BLF3-D	10/28/2008 8:35	Copper		69	mg/kg	5	CU
BLF3-D	10/28/2008 8:35	Lead		374	mg/kg	5	PB
BLF3-D	10/28/2008 8:35	Selenium		30	mg/kg	5	SE
BLF3-D	10/28/2008 8:35	Zinc		1060	mg/kg	5	ZN
BLF3-E	10/28/2008 8:36	Silver	ND		mg/kg	5	AG
BLF3-E	10/28/2008 8:36	Aluminum		9100	mg/kg	5	AL
BLF3-E	10/28/2008 8:36	Arsenic		217	mg/kg	5	AS
BLF3-E	10/28/2008 8:36	Arsenic		0.4	mg/L	0.1	AS
BLF3-E	10/28/2008 8:36	Barium		640	mg/kg	5	BA
BLF3-E	10/28/2008 8:36	Beryllium	ND		mg/kg	5	BE
BLF3-E	10/28/2008 8:36	Cadmium		83	mg/kg	1	CD

TABLE B-4. DEMOLITION FOOTPRINT SOIL SAMPLE LABORATORY RESULTS

Sample ID	Collection Date	Analyte	TResult	NResult	Runits	Rlimit	ParLabel
BLF3-E	10/28/2008 8:36	Cadmium	ND		mg/L	0.1	CD
BLF3-E	10/28/2008 8:36	Cobalt	ND		mg/kg	5	CO
BLF3-E	10/28/2008 8:36	Chromium		5	mg/kg	5	CR
BLF3-E	10/28/2008 8:36	Copper		44	mg/kg	5	CU
BLF3-E	10/28/2008 8:36	Copper	ND		mg/L	0.1	CU
BLF3-E	10/28/2008 8:36	Iron		8590	mg/kg	10	FE
BLF3-E	10/28/2008 8:36	Mercury		0.35	mg/kg	0.05	HG
BLF3-E	10/28/2008 8:36	Manganese		72	mg/kg	5	MN
BLF3-E	10/28/2008 8:36	Nickel		11	mg/kg	5	NI
BLF3-E	10/28/2008 8:36	Lead		97	mg/kg	5	PB
BLF3-E	10/28/2008 8:36	Lead	ND		mg/L	0.1	PB
BLF3-E	10/28/2008 8:36	Antimony		12	mg/kg	5	SB
BLF3-E	10/28/2008 8:36	Selenium		7	mg/kg	5	SE
BLF3-E	10/28/2008 8:36	Selenium	ND		mg/L	0.1	SE
BLF3-E	10/28/2008 8:36	Thallium	ND		mg/kg	5	TL
BLF3-E	10/28/2008 8:36	Vanadium		22	mg/kg	5	V
BLF3-E	10/28/2008 8:36	Zinc		215	mg/kg	5	ZN
BLF3-E	10/28/2008 8:36	Zinc		0.2	mg/L	0.1	ZN
BLF4-A	10/28/2008 8:45	Silver		70	mg/kg	5	AG
BLF4-A	10/28/2008 8:45	Aluminum		5430	mg/kg	5	AL
BLF4-A	10/28/2008 8:45	Arsenic		1050	mg/kg	5	AS
BLF4-A	10/28/2008 8:45	Barium		192	mg/kg	5	BA
BLF4-A	10/28/2008 8:45	Beryllium	ND		mg/kg	5	BE
BLF4-A	10/28/2008 8:45	Cadmium		494	mg/kg	1	CD
BLF4-A	10/28/2008 8:45	Cobalt		5	mg/kg	5	CO
BLF4-A	10/28/2008 8:45	Chromium		7	mg/kg	5	CR
BLF4-A	10/28/2008 8:45	Copper		472	mg/kg	5	CU
BLF4-A	10/28/2008 8:45	Iron		18300	mg/kg	10	FE
BLF4-A	10/28/2008 8:45	Mercury		11	mg/kg	0.8	HG
BLF4-A	10/28/2008 8:45	Manganese		596	mg/kg	5	MN
BLF4-A	10/28/2008 8:45	Nickel		8	mg/kg	5	NI
BLF4-A	10/28/2008 8:45	Lead		2760	mg/kg	5	PB
BLF4-A	10/28/2008 8:45	Antimony		24	mg/kg	5	SB
BLF4-A	10/28/2008 8:45	Selenium	ND		mg/kg	5	SE
BLF4-A	10/28/2008 8:45	Thallium		19	mg/kg	5	TL
BLF4-A	10/28/2008 8:45	Vanadium		28	mg/kg	5	V
BLF4-A	10/28/2008 8:45	Zinc		1240	mg/kg	5	ZN
BLF4-B	10/28/2008 8:50	Arsenic		125	mg/kg	5	AS
BLF4-B	10/28/2008 8:50	Cadmium		6	mg/kg	1	CD
BLF4-B	10/28/2008 8:50	Copper		112	mg/kg	5	CU
BLF4-B	10/28/2008 8:50	Lead		958	mg/kg	5	PB
BLF4-B	10/28/2008 8:50	Selenium		9	mg/kg	5	SE
BLF4-B	10/28/2008 8:50	Zinc		90	mg/kg	5	ZN
BLF4-C	10/28/2008 8:52	Arsenic		111	mg/kg	5	AS
BLF4-C	10/28/2008 8:52	Cadmium		3	mg/kg	1	CD
BLF4-C	10/28/2008 8:52	Copper		62	mg/kg	5	CU
BLF4-C	10/28/2008 8:52	Lead		145	mg/kg	5	PB
BLF4-C	10/28/2008 8:52	Selenium	ND		mg/kg	5	SE
BLF4-C	10/28/2008 8:52	Zinc		36	mg/kg	5	ZN
BLF4-D	10/28/2008 8:55	Silver		15	mg/kg	5	AG
BLF4-D	10/28/2008 8:55	Aluminum		3510	mg/kg	5	AL

TABLE B-4. DEMOLITION FOOTPRINT SOIL SAMPLE LABORATORY RESULTS

Sample ID	Collection Date	Analyte	TResult	NResult	Runits	Rlimit	ParLabel
BLF4-D	10/28/2008 8:55	Arsenic		0.2	mg/L	0.1	AS
BLF4-D	10/28/2008 8:55	Arsenic		33	mg/kg	5	AS
BLF4-D	10/28/2008 8:55	Barium		12	mg/kg	5	BA
BLF4-D	10/28/2008 8:55	Beryllium	ND		mg/kg	5	BE
BLF4-D	10/28/2008 8:55	Cadmium	ND		mg/L	0.1	CD
BLF4-D	10/28/2008 8:55	Cadmium		30	mg/kg	1	CD
BLF4-D	10/28/2008 8:55	Cobalt	ND		mg/kg	5	CO
BLF4-D	10/28/2008 8:55	Chromium	ND		mg/kg	5	CR
BLF4-D	10/28/2008 8:55	Copper	ND		mg/L	0.1	CU
BLF4-D	10/28/2008 8:55	Copper		22	mg/kg	5	CU
BLF4-D	10/28/2008 8:55	Iron		1070	mg/kg	7	FE
BLF4-D	10/28/2008 8:55	Mercury		3.7	mg/kg	0.4	HG
BLF4-D	10/28/2008 8:55	Manganese		31	mg/kg	5	MN
BLF4-D	10/28/2008 8:55	Nickel	ND		mg/kg	5	NI
BLF4-D	10/28/2008 8:55	Lead	ND		mg/L	0.1	PB
BLF4-D	10/28/2008 8:55	Lead		20	mg/kg	5	PB
BLF4-D	10/28/2008 8:55	Antimony	ND		mg/kg	5	SB
BLF4-D	10/28/2008 8:55	Selenium	ND		mg/L	0.1	SE
BLF4-D	10/28/2008 8:55	Selenium	ND		mg/kg	5	SE
BLF4-D	10/28/2008 8:55	Thallium	ND		mg/kg	5	TL
BLF4-D	10/28/2008 8:55	Vanadium		5	mg/kg	5	V
BLF4-D	10/28/2008 8:55	Zinc	ND		mg/L	0.1	ZN
BLF4-D	10/28/2008 8:55	Zinc		68	mg/kg	5	ZN
BLF5-A	10/28/2008 9:25	Silver		8	mg/kg	5	AG
BLF5-A	10/28/2008 9:25	Aluminum		8800	mg/kg	5	AL
BLF5-A	10/28/2008 9:25	Arsenic		797	mg/kg	5	AS
BLF5-A	10/28/2008 9:25	Barium		545	mg/kg	5	BA
BLF5-A	10/28/2008 9:25	Beryllium	ND		mg/kg	5	BE
BLF5-A	10/28/2008 9:25	Cadmium		172	mg/kg	1	CD
BLF5-A	10/28/2008 9:25	Cobalt	ND		mg/kg	5	CO
BLF5-A	10/28/2008 9:25	Chromium		6	mg/kg	5	CR
BLF5-A	10/28/2008 9:25	Copper		246	mg/kg	5	CU
BLF5-A	10/28/2008 9:25	Iron		17900	mg/kg	10	FE
BLF5-A	10/28/2008 9:25	Mercury		8.2	mg/kg	0.4	HG
BLF5-A	10/28/2008 9:25	Manganese		509	mg/kg	5	MN
BLF5-A	10/28/2008 9:25	Nickel		10	mg/kg	5	NI
BLF5-A	10/28/2008 9:25	Lead		1650	mg/kg	5	PB
BLF5-A	10/28/2008 9:25	Antimony		18	mg/kg	5	SB
BLF5-A	10/28/2008 9:25	Selenium	ND		mg/kg	5	SE
BLF5-A	10/28/2008 9:25	Thallium	ND		mg/kg	5	TL
BLF5-A	10/28/2008 9:25	Vanadium		40	mg/kg	5	V
BLF5-A	10/28/2008 9:25	Zinc		1360	mg/kg	5	ZN
BLF5-B	10/28/2008 9:28	Arsenic		28	mg/kg	5	AS
BLF5-B	10/28/2008 9:28	Cadmium		15	mg/kg	1	CD
BLF5-B	10/28/2008 9:28	Copper		36	mg/kg	5	CU
BLF5-B	10/28/2008 9:28	Lead	ND		mg/kg	5	PB
BLF5-B	10/28/2008 9:28	Selenium		19	mg/kg	5	SE
BLF5-B	10/28/2008 9:28	Zinc		52	mg/kg	5	ZN
BLF5-C	10/28/2008 9:31	Arsenic		17	mg/kg	5	AS
BLF5-C	10/28/2008 9:31	Cadmium		5	mg/kg	1	CD
BLF5-C	10/28/2008 9:31	Copper		16	mg/kg	5	CU

TABLE B-4. DEMOLITION FOOTPRINT SOIL SAMPLE LABORATORY RESULTS

Sample ID	Collection Date	Analyte	TResult	NResult	Runits	Rlimit	ParLabel
BLF5-C	10/28/2008 9:31	Lead	ND		mg/kg	5	PB
BLF5-C	10/28/2008 9:31	Selenium		8	mg/kg	5	SE
BLF5-C	10/28/2008 9:31	Zinc		21	mg/kg	5	ZN
BLF5-D	10/28/2008 9:33	Arsenic		25	mg/kg	5	AS
BLF5-D	10/28/2008 9:33	Cadmium		29	mg/kg	1	CD
BLF5-D	10/28/2008 9:33	Copper		12	mg/kg	5	CU
BLF5-D	10/28/2008 9:33	Lead	ND		mg/kg	5	PB
BLF5-D	10/28/2008 9:33	Selenium		6	mg/kg	5	SE
BLF5-D	10/28/2008 9:33	Zinc		41	mg/kg	5	ZN
BLF5-E	10/28/2008 9:35	Arsenic		14	mg/kg	5	AS
BLF5-E	10/28/2008 9:35	Cadmium		4	mg/kg	1	CD
BLF5-E	10/28/2008 9:35	Copper		12	mg/kg	5	CU
BLF5-E	10/28/2008 9:35	Lead	ND		mg/kg	5	PB
BLF5-E	10/28/2008 9:35	Selenium		13	mg/kg	5	SE
BLF5-E	10/28/2008 9:35	Zinc		20	mg/kg	5	ZN
BLF5-E2	10/28/2008 9:37	Arsenic		8	mg/kg	5	AS
BLF5-E2	10/28/2008 9:37	Cadmium		6	mg/kg	1	CD
BLF5-E2	10/28/2008 9:37	Copper		14	mg/kg	5	CU
BLF5-E2	10/28/2008 9:37	Lead	ND		mg/kg	5	PB
BLF5-E2	10/28/2008 9:37	Selenium		10	mg/kg	5	SE
BLF5-E2	10/28/2008 9:37	Zinc		25	mg/kg	5	ZN
BLF5-F	10/28/2008 9:36	Arsenic		546	mg/kg	5	AS
BLF5-F	10/28/2008 9:36	Cadmium		34	mg/kg	1	CD
BLF5-F	10/28/2008 9:36	Copper		15	mg/kg	5	CU
BLF5-F	10/28/2008 9:36	Lead		597	mg/kg	5	PB
BLF5-F	10/28/2008 9:36	Selenium		14	mg/kg	5	SE
BLF5-F	10/28/2008 9:36	Zinc		188	mg/kg	5	ZN
BLF5-G	10/28/2008 9:39	Silver	ND		mg/kg	5	AG
BLF5-G	10/28/2008 9:39	Aluminum		12400	mg/kg	5	AL
BLF5-G	10/28/2008 9:39	Arsenic		0.2	mg/L	0.1	AS
BLF5-G	10/28/2008 9:39	Arsenic		69	mg/kg	5	AS
BLF5-G	10/28/2008 9:39	Barium		129	mg/kg	5	BA
BLF5-G	10/28/2008 9:39	Beryllium	ND		mg/kg	5	BE
BLF5-G	10/28/2008 9:39	Cadmium	ND		mg/L	0.1	CD
BLF5-G	10/28/2008 9:39	Cadmium		1	mg/kg	1	CD
BLF5-G	10/28/2008 9:39	Cobalt		6	mg/kg	5	CO
BLF5-G	10/28/2008 9:39	Chromium		15	mg/kg	5	CR
BLF5-G	10/28/2008 9:39	Copper	ND		mg/L	0.1	CU
BLF5-G	10/28/2008 9:39	Copper		27	mg/kg	5	CU
BLF5-G	10/28/2008 9:39	Iron		15000	mg/kg	10	FE
BLF5-G	10/28/2008 9:39	Mercury	ND		mg/kg	0.05	HG
BLF5-G	10/28/2008 9:39	Manganese		338	mg/kg	5	MN
BLF5-G	10/28/2008 9:39	Nickel		11	mg/kg	5	NI
BLF5-G	10/28/2008 9:39	Lead	ND		mg/L	0.1	PB
BLF5-G	10/28/2008 9:39	Lead		24	mg/kg	5	PB
BLF5-G	10/28/2008 9:39	Antimony	ND		mg/kg	5	SB
BLF5-G	10/28/2008 9:39	Selenium	ND		mg/L	0.1	SE
BLF5-G	10/28/2008 9:39	Selenium	ND		mg/kg	5	SE
BLF5-G	10/28/2008 9:39	Thallium	ND		mg/kg	5	TL
BLF5-G	10/28/2008 9:39	Vanadium		28	mg/kg	5	V
BLF5-G	10/28/2008 9:39	Zinc		0.3	mg/L	0.1	ZN

TABLE B-4. DEMOLITION FOOTPRINT SOIL SAMPLE LABORATORY RESULTS

Sample ID	Collection Date	Analyte	TResult	NResult	Runits	Rlimit	ParLabel
BLF5-G	10/28/2008 9:39	Zinc		59	mg/kg	5	ZN
BLF6-A	10/28/2008 9:52	Silver		19	mg/kg	5	AG
BLF6-A	10/28/2008 9:52	Aluminum		12100	mg/kg	5	AL
BLF6-A	10/28/2008 9:52	Arsenic		680	mg/kg	5	AS
BLF6-A	10/28/2008 9:52	Barium		874	mg/kg	5	BA
BLF6-A	10/28/2008 9:52	Beryllium	ND		mg/kg	5	BE
BLF6-A	10/28/2008 9:52	Cadmium		526	mg/kg	1	CD
BLF6-A	10/28/2008 9:52	Cobalt		9	mg/kg	5	CO
BLF6-A	10/28/2008 9:52	Chromium		14	mg/kg	5	CR
BLF6-A	10/28/2008 9:52	Copper		606	mg/kg	5	CU
BLF6-A	10/28/2008 9:52	Iron		31300	mg/kg	10	FE
BLF6-A	10/28/2008 9:52	Mercury		15	mg/kg	0.8	HG
BLF6-A	10/28/2008 9:52	Manganese		1060	mg/kg	5	MN
BLF6-A	10/28/2008 9:52	Nickel		19	mg/kg	5	NI
BLF6-A	10/28/2008 9:52	Lead		2780	mg/kg	5	PB
BLF6-A	10/28/2008 9:52	Antimony		17	mg/kg	5	SB
BLF6-A	10/28/2008 9:52	Selenium		9	mg/kg	5	SE
BLF6-A	10/28/2008 9:52	Thallium		16	mg/kg	5	TL
BLF6-A	10/28/2008 9:52	Vanadium		54	mg/kg	5	V
BLF6-A	10/28/2008 9:52	Zinc		2620	mg/kg	5	ZN
BLF6-B	10/28/2008 9:54	Arsenic		247	mg/kg	5	AS
BLF6-B	10/28/2008 9:54	Cadmium		700	mg/kg	1	CD
BLF6-B	10/28/2008 9:54	Copper		87	mg/kg	5	CU
BLF6-B	10/28/2008 9:54	Lead		290	mg/kg	5	PB
BLF6-B	10/28/2008 9:54	Selenium		29	mg/kg	5	SE
BLF6-B	10/28/2008 9:54	Zinc		371	mg/kg	5	ZN
BLF6-C	10/28/2008 9:56	Arsenic		900	mg/kg	5	AS
BLF6-C	10/28/2008 9:56	Cadmium		483	mg/kg	1	CD
BLF6-C	10/28/2008 9:56	Copper		267	mg/kg	5	CU
BLF6-C	10/28/2008 9:56	Lead		54	mg/kg	5	PB
BLF6-C	10/28/2008 9:56	Selenium		20	mg/kg	5	SE
BLF6-C	10/28/2008 9:56	Zinc		787	mg/kg	5	ZN
BLF6-D	10/28/2008 9:58	Arsenic		389	mg/kg	5	AS
BLF6-D	10/28/2008 9:58	Cadmium		110	mg/kg	1	CD
BLF6-D	10/28/2008 9:58	Copper		69	mg/kg	5	CU
BLF6-D	10/28/2008 9:58	Lead		102	mg/kg	5	PB
BLF6-D	10/28/2008 9:58	Selenium		17	mg/kg	5	SE
BLF6-D	10/28/2008 9:58	Zinc		695	mg/kg	5	ZN
BLF6-E	10/28/2008 10:00	Silver	ND		mg/kg	5	AG
BLF6-E	10/28/2008 10:00	Aluminum		2060	mg/kg	5	AL
BLF6-E	10/28/2008 10:00	Arsenic		2.3	mg/L	0.1	AS
BLF6-E	10/28/2008 10:00	Arsenic		646	mg/kg	5	AS
BLF6-E	10/28/2008 10:00	Barium		28	mg/kg	5	BA
BLF6-E	10/28/2008 10:00	Beryllium	ND		mg/kg	5	BE
BLF6-E	10/28/2008 10:00	Cadmium	ND		mg/L	0.1	CD
BLF6-E	10/28/2008 10:00	Cadmium		53	mg/kg	1	CD
BLF6-E	10/28/2008 10:00	Cobalt	ND		mg/kg	5	CO
BLF6-E	10/28/2008 10:00	Chromium	ND		mg/kg	5	CR
BLF6-E	10/28/2008 10:00	Copper	ND		mg/L	0.1	CU
BLF6-E	10/28/2008 10:00	Copper		39	mg/kg	5	CU
BLF6-E	10/28/2008 10:00	Iron		7790	mg/kg	7	FE

TABLE B-4. DEMOLITION FOOTPRINT SOIL SAMPLE LABORATORY RESULTS

Sample ID	Collection Date	Analyte	TResult	NResult	Runits	Rlimit	ParLabel
BLF6-E	10/28/2008 10:00	Mercury		5.9	mg/kg	0.4	HG
BLF6-E	10/28/2008 10:00	Manganese		328	mg/kg	5	MN
BLF6-E	10/28/2008 10:00	Nickel	ND		mg/kg	5	NI
BLF6-E	10/28/2008 10:00	Lead	ND		mg/L	0.1	PB
BLF6-E	10/28/2008 10:00	Lead		29	mg/kg	5	PB
BLF6-E	10/28/2008 10:00	Antimony	ND		mg/kg	5	SB
BLF6-E	10/28/2008 10:00	Selenium	ND		mg/L	0.1	SE
BLF6-E	10/28/2008 10:00	Selenium	ND		mg/kg	5	SE
BLF6-E	10/28/2008 10:00	Thallium	ND		mg/kg	5	TL
BLF6-E	10/28/2008 10:00	Vanadium		16	mg/kg	5	V
BLF6-E	10/28/2008 10:00	Zinc		0.5	mg/L	0.1	ZN
BLF6-E	10/28/2008 10:00	Zinc		429	mg/kg	5	ZN
BLF7-A	10/28/2008 10:10	Silver		150	mg/kg	5	AG
BLF7-A	10/28/2008 10:10	Aluminum		6700	mg/kg	5	AL
BLF7-A	10/28/2008 10:10	Arsenic		1720	mg/kg	5	AS
BLF7-A	10/28/2008 10:10	Barium		380	mg/kg	5	BA
BLF7-A	10/28/2008 10:10	Beryllium	ND		mg/kg	5	BE
BLF7-A	10/28/2008 10:10	Cadmium		2200	mg/kg	1	CD
BLF7-A	10/28/2008 10:10	Cobalt		29	mg/kg	5	CO
BLF7-A	10/28/2008 10:10	Chromium		17	mg/kg	5	CR
BLF7-A	10/28/2008 10:10	Copper		11100	mg/kg	5	CU
BLF7-A	10/28/2008 10:10	Iron		45600	mg/kg	10	FE
BLF7-A	10/28/2008 10:10	Mercury		14	mg/kg	0.8	HG
BLF7-A	10/28/2008 10:10	Manganese		3680	mg/kg	5	MN
BLF7-A	10/28/2008 10:10	Nickel		50	mg/kg	5	NI
BLF7-A	10/28/2008 10:10	Lead		17600	mg/kg	5	PB
BLF7-A	10/28/2008 10:10	Antimony		110	mg/kg	5	SB
BLF7-A	10/28/2008 10:10	Selenium		28	mg/kg	5	SE
BLF7-A	10/28/2008 10:10	Thallium		39	mg/kg	5	TL
BLF7-A	10/28/2008 10:10	Vanadium		31	mg/kg	5	V
BLF7-A	10/28/2008 10:10	Zinc		6690	mg/kg	5	ZN
BLF7-B	10/28/2008 10:12	Arsenic		1520	mg/kg	5	AS
BLF7-B	10/28/2008 10:12	Cadmium		456	mg/kg	1	CD
BLF7-B	10/28/2008 10:12	Copper		175	mg/kg	5	CU
BLF7-B	10/28/2008 10:12	Lead		1120	mg/kg	5	PB
BLF7-B	10/28/2008 10:12	Selenium		35	mg/kg	5	SE
BLF7-B	10/28/2008 10:12	Zinc		974	mg/kg	5	ZN
BLF7-C	10/28/2008 10:14	Arsenic		29400	mg/kg	5	AS
BLF7-C	10/28/2008 10:14	Cadmium		11200	mg/kg	1	CD
BLF7-C	10/28/2008 10:14	Copper		1840	mg/kg	5	CU
BLF7-C	10/28/2008 10:14	Lead		53400	mg/kg	5	PB
BLF7-C	10/28/2008 10:14	Selenium		133	mg/kg	5	SE
BLF7-C	10/28/2008 10:14	Zinc		15700	mg/kg	5	ZN
BLF7-C2	10/28/2008 10:16	Arsenic		23700	mg/kg	5	AS
BLF7-C2	10/28/2008 10:16	Cadmium		10100	mg/kg	1	CD
BLF7-C2	10/28/2008 10:16	Copper		1720	mg/kg	5	CU
BLF7-C2	10/28/2008 10:16	Lead		51700	mg/kg	5	PB
BLF7-C2	10/28/2008 10:16	Selenium		120	mg/kg	5	SE
BLF7-C2	10/28/2008 10:16	Zinc		14500	mg/kg	5	ZN
BLF7-D	10/28/2008 10:15	Arsenic		1600	mg/kg	5	AS
BLF7-D	10/28/2008 10:15	Cadmium		216	mg/kg	1	CD

TABLE B-4. DEMOLITION FOOTPRINT SOIL SAMPLE LABORATORY RESULTS

Sample ID	Collection Date	Analyte	TResult	NResult	Runits	Rlimit	ParLabel
BLF7-D	10/28/2008 10:15	Copper		99	mg/kg	5	CU
BLF7-D	10/28/2008 10:15	Lead		820	mg/kg	5	PB
BLF7-D	10/28/2008 10:15	Selenium		50	mg/kg	5	SE
BLF7-D	10/28/2008 10:15	Zinc		480	mg/kg	5	ZN
BLF7-E	10/28/2008 10:17	Arsenic		1720	mg/kg	5	AS
BLF7-E	10/28/2008 10:17	Cadmium		91	mg/kg	1	CD
BLF7-E	10/28/2008 10:17	Copper		84	mg/kg	5	CU
BLF7-E	10/28/2008 10:17	Lead		204	mg/kg	5	PB
BLF7-E	10/28/2008 10:17	Selenium		39	mg/kg	5	SE
BLF7-E	10/28/2008 10:17	Zinc		228	mg/kg	5	ZN
BLF7-F	10/28/2008 10:20	Arsenic		887	mg/kg	5	AS
BLF7-F	10/28/2008 10:20	Cadmium		152	mg/kg	1	CD
BLF7-F	10/28/2008 10:20	Copper		70	mg/kg	5	CU
BLF7-F	10/28/2008 10:20	Lead		258	mg/kg	5	PB
BLF7-F	10/28/2008 10:20	Selenium		35	mg/kg	5	SE
BLF7-F	10/28/2008 10:20	Zinc		176	mg/kg	5	ZN
BLF7-G	10/28/2008 10:23	Arsenic		1220	mg/kg	5	AS
BLF7-G	10/28/2008 10:23	Cadmium		260	mg/kg	1	CD
BLF7-G	10/28/2008 10:23	Copper		172	mg/kg	5	CU
BLF7-G	10/28/2008 10:23	Lead		306	mg/kg	5	PB
BLF7-G	10/28/2008 10:23	Selenium		57	mg/kg	5	SE
BLF7-G	10/28/2008 10:23	Zinc		321	mg/kg	5	ZN
BLF7-H	10/28/2008 10:35	Arsenic		652	mg/kg	5	AS
BLF7-H	10/28/2008 10:35	Cadmium		580	mg/kg	1	CD
BLF7-H	10/28/2008 10:35	Copper		86	mg/kg	5	CU
BLF7-H	10/28/2008 10:35	Lead		55	mg/kg	5	PB
BLF7-H	10/28/2008 10:35	Selenium		28	mg/kg	5	SE
BLF7-H	10/28/2008 10:35	Zinc		749	mg/kg	5	ZN
BLF7-I	10/28/2008 10:44	Silver	ND		mg/kg	5	AG
BLF7-I	10/28/2008 10:44	Aluminum		4670	mg/kg	5	AL
BLF7-I	10/28/2008 10:44	Arsenic		1.8	mg/L	0.1	AS
BLF7-I	10/28/2008 10:44	Arsenic		186	mg/kg	5	AS
BLF7-I	10/28/2008 10:44	Barium		58	mg/kg	5	BA
BLF7-I	10/28/2008 10:44	Beryllium	ND		mg/kg	5	BE
BLF7-I	10/28/2008 10:44	Cadmium		137	mg/kg	1	CD
BLF7-I	10/28/2008 10:44	Cadmium		0.2	mg/L	0.1	CD
BLF7-I	10/28/2008 10:44	Cobalt	ND		mg/kg	5	CO
BLF7-I	10/28/2008 10:44	Chromium		6	mg/kg	5	CR
BLF7-I	10/28/2008 10:44	Copper	ND		mg/L	0.1	CU
BLF7-I	10/28/2008 10:44	Copper		34	mg/kg	5	CU
BLF7-I	10/28/2008 10:44	Iron		10300	mg/kg	10	FE
BLF7-I	10/28/2008 10:44	Mercury		2.9	mg/kg	0.2	HG
BLF7-I	10/28/2008 10:44	Manganese		509	mg/kg	5	MN
BLF7-I	10/28/2008 10:44	Nickel	ND		mg/kg	5	NI
BLF7-I	10/28/2008 10:44	Lead		0.1	mg/L	0.1	PB
BLF7-I	10/28/2008 10:44	Lead		19	mg/kg	5	PB
BLF7-I	10/28/2008 10:44	Antimony	ND		mg/kg	5	SB
BLF7-I	10/28/2008 10:44	Selenium	ND		mg/L	0.1	SE
BLF7-I	10/28/2008 10:44	Selenium	ND		mg/kg	5	SE
BLF7-I	10/28/2008 10:44	Thallium	ND		mg/kg	5	TL
BLF7-I	10/28/2008 10:44	Vanadium		25	mg/kg	5	V

TABLE B-4. DEMOLITION FOOTPRINT SOIL SAMPLE LABORATORY RESULTS

Sample ID	Collection Date	Analyte	TResult	NResult	Runits	Rlimit	ParLabel
BLF7-I	10/28/2008 10:44	Zinc		188	mg/kg	5	ZN
BLF7-I	10/28/2008 10:44	Zinc		0.4	mg/L	0.1	ZN
MOF1-A	10/23/2008 10:05	Silver		405	mg/kg	5	AG
MOF1-A	10/23/2008 10:05	Aluminum		5610	mg/kg	5	AL
MOF1-A	10/23/2008 10:05	Arsenic		3850	mg/kg	5	AS
MOF1-A	10/23/2008 10:05	Barium		255	mg/kg	5	BA
MOF1-A	10/23/2008 10:05	Beryllium	ND		mg/kg	5	BE
MOF1-A	10/23/2008 10:05	Cadmium		14600	mg/kg	1	CD
MOF1-A	10/23/2008 10:05	Cobalt		19	mg/kg	5	CO
MOF1-A	10/23/2008 10:05	Chromium		20	mg/kg	5	CR
MOF1-A	10/23/2008 10:05	Copper		7640	mg/kg	5	CU
MOF1-A	10/23/2008 10:05	Iron		17400	mg/kg	10	FE
MOF1-A	10/23/2008 10:05	Mercury		120	mg/kg	20	HG
MOF1-A	10/23/2008 10:05	Manganese		654	mg/kg	5	MN
MOF1-A	10/23/2008 10:05	Nickel		79	mg/kg	5	NI
MOF1-A	10/23/2008 10:05	Lead		52900	mg/kg	5	PB
MOF1-A	10/23/2008 10:05	Antimony		590	mg/kg	6	SB
MOF1-A	10/23/2008 10:05	Selenium		229	mg/kg	5	SE
MOF1-A	10/23/2008 10:05	Thallium		209	mg/kg	5	TL
MOF1-A	10/23/2008 10:05	Vanadium		19	mg/kg	5	V
MOF1-A	10/23/2008 10:05	Zinc		29700	mg/kg	20	ZN
MOF1-B	10/23/2008 10:10	Arsenic		3230	mg/kg	5	AS
MOF1-B	10/23/2008 10:10	Cadmium		13100	mg/kg	1	CD
MOF1-B	10/23/2008 10:10	Copper		4820	mg/kg	5	CU
MOF1-B	10/23/2008 10:10	Lead		49300	mg/kg	5	PB
MOF1-B	10/23/2008 10:10	Selenium		251	mg/kg	5	SE
MOF1-B	10/23/2008 10:10	Zinc		24200	mg/kg	5	ZN
MOF1-C	10/23/2008 10:12	Arsenic		409	mg/kg	5	AS
MOF1-C	10/23/2008 10:12	Cadmium		5120	mg/kg	1	CD
MOF1-C	10/23/2008 10:12	Copper		568	mg/kg	5	CU
MOF1-C	10/23/2008 10:12	Lead		4940	mg/kg	5	PB
MOF1-C	10/23/2008 10:12	Selenium		57	mg/kg	5	SE
MOF1-C	10/23/2008 10:12	Zinc		8020	mg/kg	5	ZN
MOF1-D	10/23/2008 10:15	Arsenic		84	mg/kg	5	AS
MOF1-D	10/23/2008 10:15	Cadmium		5830	mg/kg	1	CD
MOF1-D	10/23/2008 10:15	Copper		52	mg/kg	5	CU
MOF1-D	10/23/2008 10:15	Lead		253	mg/kg	5	PB
MOF1-D	10/23/2008 10:15	Selenium		41	mg/kg	5	SE
MOF1-D	10/23/2008 10:15	Zinc		3690	mg/kg	5	ZN
MOF1-E	10/23/2008 10:52	Arsenic		120	mg/kg	5	AS
MOF1-E	10/23/2008 10:52	Cadmium		2850	mg/kg	1	CD
MOF1-E	10/23/2008 10:52	Copper		121	mg/kg	5	CU
MOF1-E	10/23/2008 10:52	Lead		706	mg/kg	5	PB
MOF1-E	10/23/2008 10:52	Selenium		31	mg/kg	5	SE
MOF1-E	10/23/2008 10:52	Zinc		2680	mg/kg	5	ZN
MOF1-F	10/23/2008 10:55	Arsenic		51	mg/kg	5	AS
MOF1-F	10/23/2008 10:55	Cadmium		348	mg/kg	1	CD
MOF1-F	10/23/2008 10:55	Copper		43	mg/kg	5	CU
MOF1-F	10/23/2008 10:55	Lead		174	mg/kg	5	PB
MOF1-F	10/23/2008 10:55	Selenium		21	mg/kg	5	SE
MOF1-F	10/23/2008 10:55	Zinc		451	mg/kg	5	ZN

TABLE B-4. DEMOLITION FOOTPRINT SOIL SAMPLE LABORATORY RESULTS

Sample ID	Collection Date	Analyte	TResult	NResult	Runits	Rlimit	ParLabel
MOF1-G	10/23/2008 11:05	Arsenic		113	mg/kg	5	AS
MOF1-G	10/23/2008 11:05	Cadmium		1560	mg/kg	1	CD
MOF1-G	10/23/2008 11:05	Copper		146	mg/kg	5	CU
MOF1-G	10/23/2008 11:05	Lead		668	mg/kg	5	PB
MOF1-G	10/23/2008 11:05	Selenium		28	mg/kg	5	SE
MOF1-G	10/23/2008 11:05	Zinc		1730	mg/kg	5	ZN
MOF1-H	10/23/2008 11:19	Arsenic		56	mg/kg	5	AS
MOF1-H	10/23/2008 11:19	Cadmium		484	mg/kg	1	CD
MOF1-H	10/23/2008 11:19	Copper		79	mg/kg	5	CU
MOF1-H	10/23/2008 11:19	Lead		225	mg/kg	5	PB
MOF1-H	10/23/2008 11:19	Selenium		22	mg/kg	5	SE
MOF1-H	10/23/2008 11:19	Zinc		928	mg/kg	5	ZN
MOF1-I	10/23/2008 11:33	Silver	ND		mg/kg	5	AG
MOF1-I	10/23/2008 11:33	Aluminum		10600	mg/kg	5	AL
MOF1-I	10/23/2008 11:33	Arsenic		37	mg/kg	5	AS
MOF1-I	10/23/2008 11:33	Arsenic	ND		mg/L	0.1	AS
MOF1-I	10/23/2008 11:33	Barium		90	mg/kg	5	BA
MOF1-I	10/23/2008 11:33	Beryllium	ND		mg/kg	5	BE
MOF1-I	10/23/2008 11:33	Cadmium		341	mg/kg	1	CD
MOF1-I	10/23/2008 11:33	Cadmium	ND		mg/L	0.1	CD
MOF1-I	10/23/2008 11:33	Cobalt		6	mg/kg	5	CO
MOF1-I	10/23/2008 11:33	Chromium		16	mg/kg	5	CR
MOF1-I	10/23/2008 11:33	Copper		52	mg/kg	5	CU
MOF1-I	10/23/2008 11:33	Copper	ND		mg/L	0.1	CU
MOF1-I	10/23/2008 11:33	Iron		23200	mg/kg	10	FE
MOF1-I	10/23/2008 11:33	Mercury		1.3	mg/kg	0.08	HG
MOF1-I	10/23/2008 11:33	Manganese		642	mg/kg	5	MN
MOF1-I	10/23/2008 11:33	Nickel		8	mg/kg	5	NI
MOF1-I	10/23/2008 11:33	Lead		76	mg/kg	5	PB
MOF1-I	10/23/2008 11:33	Lead	ND		mg/L	0.1	PB
MOF1-I	10/23/2008 11:33	Antimony	ND		mg/kg	5	SB
MOF1-I	10/23/2008 11:33	Selenium	ND		mg/kg	5	SE
MOF1-I	10/23/2008 11:33	Selenium	ND		mg/L	0.1	SE
MOF1-I	10/23/2008 11:33	Thallium		19	mg/kg	5	TL
MOF1-I	10/23/2008 11:33	Vanadium		60	mg/kg	5	V
MOF1-I	10/23/2008 11:33	Zinc		736	mg/kg	5	ZN
MOF1-I	10/23/2008 11:33	Zinc	ND		mg/L	0.1	ZN
MOF2-A	10/23/2008 11:50	Silver		427	mg/kg	5	AG
MOF2-A	10/23/2008 11:50	Aluminum		6170	mg/kg	5	AL
MOF2-A	10/23/2008 11:50	Arsenic		4090	mg/kg	5	AS
MOF2-A	10/23/2008 11:50	Barium		619	mg/kg	5	BA
MOF2-A	10/23/2008 11:50	Beryllium	ND		mg/kg	5	BE
MOF2-A	10/23/2008 11:50	Cadmium		21400	mg/kg	1	CD
MOF2-A	10/23/2008 11:50	Cobalt		23	mg/kg	5	CO
MOF2-A	10/23/2008 11:50	Chromium		30	mg/kg	5	CR
MOF2-A	10/23/2008 11:50	Copper		7080	mg/kg	5	CU
MOF2-A	10/23/2008 11:50	Iron		28400	mg/kg	10	FE
MOF2-A	10/23/2008 11:50	Mercury		160	mg/kg	20	HG
MOF2-A	10/23/2008 11:50	Manganese		1020	mg/kg	5	MN
MOF2-A	10/23/2008 11:50	Nickel		104	mg/kg	5	NI
MOF2-A	10/23/2008 11:50	Lead		59200	mg/kg	5	PB

TABLE B-4. DEMOLITION FOOTPRINT SOIL SAMPLE LABORATORY RESULTS

Sample ID	Collection Date	Analyte	TResult	NResult	Runits	Rlimit	ParLabel
MOF2-A	10/23/2008 11:50	Antimony		467	mg/kg	6	SB
MOF2-A	10/23/2008 11:50	Selenium		374	mg/kg	5	SE
MOF2-A	10/23/2008 11:50	Thallium		298	mg/kg	5	TL
MOF2-A	10/23/2008 11:50	Vanadium		19	mg/kg	5	V
MOF2-A	10/23/2008 11:50	Zinc		41400	mg/kg	20	ZN
MOF2-B	10/23/2008 13:20	Arsenic		11500	mg/kg	5	AS
MOF2-B	10/23/2008 13:20	Cadmium		75300	mg/kg	1	CD
MOF2-B	10/23/2008 13:20	Copper		17100	mg/kg	5	CU
MOF2-B	10/23/2008 13:20	Lead		52800	mg/kg	5	PB
MOF2-B	10/23/2008 13:20	Selenium		1310	mg/kg	5	SE
MOF2-B	10/23/2008 13:20	Zinc		113000	mg/kg	5	ZN
MOF2-C	10/23/2008 13:22	Arsenic		1110	mg/kg	5	AS
MOF2-C	10/23/2008 13:22	Cadmium		8420	mg/kg	1	CD
MOF2-C	10/23/2008 13:22	Copper		2140	mg/kg	5	CU
MOF2-C	10/23/2008 13:22	Lead		16800	mg/kg	5	PB
MOF2-C	10/23/2008 13:22	Selenium		83	mg/kg	5	SE
MOF2-C	10/23/2008 13:22	Zinc		13800	mg/kg	5	ZN
MOF2-D	10/23/2008 13:25	Arsenic		1100	mg/kg	5	AS
MOF2-D	10/23/2008 13:25	Cadmium		8310	mg/kg	1	CD
MOF2-D	10/23/2008 13:25	Copper		2600	mg/kg	5	CU
MOF2-D	10/23/2008 13:25	Lead		16500	mg/kg	5	PB
MOF2-D	10/23/2008 13:25	Selenium		77	mg/kg	5	SE
MOF2-D	10/23/2008 13:25	Zinc		13800	mg/kg	5	ZN
MOF2-E	10/23/2008 13:28	Arsenic		15	mg/kg	5	AS
MOF2-E	10/23/2008 13:28	Cadmium		49	mg/kg	1	CD
MOF2-E	10/23/2008 13:28	Copper		30	mg/kg	5	CU
MOF2-E	10/23/2008 13:28	Lead		156	mg/kg	5	PB
MOF2-E	10/23/2008 13:28	Selenium		13	mg/kg	5	SE
MOF2-E	10/23/2008 13:28	Zinc		131	mg/kg	5	ZN
MOF2-F	10/23/2008 13:30	Arsenic		33	mg/kg	5	AS
MOF2-F	10/23/2008 13:30	Cadmium		63	mg/kg	1	CD
MOF2-F	10/23/2008 13:30	Copper		51	mg/kg	5	CU
MOF2-F	10/23/2008 13:30	Lead		201	mg/kg	5	PB
MOF2-F	10/23/2008 13:30	Selenium		38	mg/kg	5	SE
MOF2-F	10/23/2008 13:30	Zinc		174	mg/kg	5	ZN
MOF2-G	10/23/2008 13:35	Arsenic		13	mg/kg	5	AS
MOF2-G	10/23/2008 13:35	Cadmium		190	mg/kg	1	CD
MOF2-G	10/23/2008 13:35	Copper		20	mg/kg	5	CU
MOF2-G	10/23/2008 13:35	Lead		52	mg/kg	5	PB
MOF2-G	10/23/2008 13:35	Selenium		34	mg/kg	5	SE
MOF2-G	10/23/2008 13:35	Zinc		102	mg/kg	5	ZN
MOF2-H	10/23/2008 13:40	Arsenic		42	mg/kg	5	AS
MOF2-H	10/23/2008 13:40	Cadmium		22	mg/kg	1	CD
MOF2-H	10/23/2008 13:40	Copper		64	mg/kg	5	CU
MOF2-H	10/23/2008 13:40	Lead		56	mg/kg	5	PB
MOF2-H	10/23/2008 13:40	Selenium		23	mg/kg	5	SE
MOF2-H	10/23/2008 13:40	Zinc		114	mg/kg	5	ZN
MOF2-I	10/23/2008 13:45	Silver		10	mg/kg	5	AG
MOF2-I	10/23/2008 13:45	Aluminum		7290	mg/kg	5	AL
MOF2-I	10/23/2008 13:45	Arsenic	ND		mg/L	0.1	AS
MOF2-I	10/23/2008 13:45	Arsenic		126	mg/kg	5	AS

TABLE B-4. DEMOLITION FOOTPRINT SOIL SAMPLE LABORATORY RESULTS

Sample ID	Collection Date	Analyte	TResult	NResult	Runits	Rlimit	ParLabel
MOF2-I	10/23/2008 13:45	Barium		66	mg/kg	5	BA
MOF2-I	10/23/2008 13:45	Beryllium	ND		mg/kg	5	BE
MOF2-I	10/23/2008 13:45	Cadmium	ND		mg/L	0.1	CD
MOF2-I	10/23/2008 13:45	Cadmium		374	mg/kg	1	CD
MOF2-I	10/23/2008 13:45	Cobalt		6	mg/kg	5	CO
MOF2-I	10/23/2008 13:45	Chromium		16	mg/kg	5	CR
MOF2-I	10/23/2008 13:45	Copper	ND		mg/L	0.1	CU
MOF2-I	10/23/2008 13:45	Copper		241	mg/kg	5	CU
MOF2-I	10/23/2008 13:45	Iron		23700	mg/kg	10	FE
MOF2-I	10/23/2008 13:45	Mercury		1	mg/kg	0.2	HG
MOF2-I	10/23/2008 13:45	Manganese		356	mg/kg	5	MN
MOF2-I	10/23/2008 13:45	Nickel		8	mg/kg	5	NI
MOF2-I	10/23/2008 13:45	Lead	ND		mg/L	0.1	PB
MOF2-I	10/23/2008 13:45	Lead		1520	mg/kg	5	PB
MOF2-I	10/23/2008 13:45	Antimony		17	mg/kg	5	SB
MOF2-I	10/23/2008 13:45	Selenium	ND		mg/L	0.1	SE
MOF2-I	10/23/2008 13:45	Selenium	ND		mg/kg	5	SE
MOF2-I	10/23/2008 13:45	Thallium		13	mg/kg	5	TL
MOF2-I	10/23/2008 13:45	Vanadium		64	mg/kg	5	V
MOF2-I	10/23/2008 13:45	Zinc	ND		mg/L	0.1	ZN
MOF2-I	10/23/2008 13:45	Zinc		971	mg/kg	5	ZN
MOF3-A	10/23/2008 13:55	Silver		122	mg/kg	5	AG
MOF3-A	10/23/2008 13:55	Aluminum		6990	mg/kg	5	AL
MOF3-A	10/23/2008 13:55	Arsenic		1500	mg/kg	5	AS
MOF3-A	10/23/2008 13:55	Barium		182	mg/kg	5	BA
MOF3-A	10/23/2008 13:55	Beryllium	ND		mg/kg	5	BE
MOF3-A	10/23/2008 13:55	Cadmium		7350	mg/kg	1	CD
MOF3-A	10/23/2008 13:55	Cobalt		16	mg/kg	5	CO
MOF3-A	10/23/2008 13:55	Chromium		16	mg/kg	5	CR
MOF3-A	10/23/2008 13:55	Copper		2340	mg/kg	5	CU
MOF3-A	10/23/2008 13:55	Iron		20600	mg/kg	10	FE
MOF3-A	10/23/2008 13:55	Mercury		46	mg/kg	8	HG
MOF3-A	10/23/2008 13:55	Manganese		691	mg/kg	5	MN
MOF3-A	10/23/2008 13:55	Nickel		25	mg/kg	5	NI
MOF3-A	10/23/2008 13:55	Lead		22900	mg/kg	5	PB
MOF3-A	10/23/2008 13:55	Antimony		138	mg/kg	5	SB
MOF3-A	10/23/2008 13:55	Selenium		93	mg/kg	5	SE
MOF3-A	10/23/2008 13:55	Thallium		124	mg/kg	5	TL
MOF3-A	10/23/2008 13:55	Vanadium		24	mg/kg	5	V
MOF3-A	10/23/2008 13:55	Zinc		13500	mg/kg	6	ZN
MOF3-A2	10/23/2008 13:57	Silver		97	mg/kg	5	AG
MOF3-A2	10/23/2008 13:57	Aluminum		6120	mg/kg	5	AL
MOF3-A2	10/23/2008 13:57	Arsenic		1280	mg/kg	5	AS
MOF3-A2	10/23/2008 13:57	Barium		193	mg/kg	5	BA
MOF3-A2	10/23/2008 13:57	Beryllium	ND		mg/kg	5	BE
MOF3-A2	10/23/2008 13:57	Cadmium		6070	mg/kg	1	CD
MOF3-A2	10/23/2008 13:57	Cobalt		13	mg/kg	5	CO
MOF3-A2	10/23/2008 13:57	Chromium		12	mg/kg	5	CR
MOF3-A2	10/23/2008 13:57	Copper		1960	mg/kg	5	CU
MOF3-A2	10/23/2008 13:57	Iron		18700	mg/kg	10	FE
MOF3-A2	10/23/2008 13:57	Mercury		73	mg/kg	8	HG

TABLE B-4. DEMOLITION FOOTPRINT SOIL SAMPLE LABORATORY RESULTS

Sample ID	Collection Date	Analyte	TResult	NResult	Runits	Rlimit	ParLabel
MOF3-A2	10/23/2008 13:57	Manganese		1310	mg/kg	5	MN
MOF3-A2	10/23/2008 13:57	Nickel		20	mg/kg	5	NI
MOF3-A2	10/23/2008 13:57	Lead		19600	mg/kg	5	PB
MOF3-A2	10/23/2008 13:57	Antimony		125	mg/kg	5	SB
MOF3-A2	10/23/2008 13:57	Selenium		98	mg/kg	5	SE
MOF3-A2	10/23/2008 13:57	Thallium		104	mg/kg	5	TL
MOF3-A2	10/23/2008 13:57	Vanadium		21	mg/kg	5	V
MOF3-A2	10/23/2008 13:57	Zinc		11800	mg/kg	6	ZN
MOF3-B	10/23/2008 14:00	Arsenic		7550	mg/kg	5	AS
MOF3-B	10/23/2008 14:00	Cadmium		24200	mg/kg	1	CD
MOF3-B	10/23/2008 14:00	Copper		8450	mg/kg	5	CU
MOF3-B	10/23/2008 14:00	Lead		52500	mg/kg	5	PB
MOF3-B	10/23/2008 14:00	Selenium		312	mg/kg	5	SE
MOF3-B	10/23/2008 14:00	Zinc		62700	mg/kg	5	ZN
MOF3-C	10/23/2008 14:02	Arsenic		2890	mg/kg	5	AS
MOF3-C	10/23/2008 14:02	Cadmium		9350	mg/kg	1	CD
MOF3-C	10/23/2008 14:02	Copper		3540	mg/kg	5	CU
MOF3-C	10/23/2008 14:02	Lead		38300	mg/kg	5	PB
MOF3-C	10/23/2008 14:02	Selenium		130	mg/kg	5	SE
MOF3-C	10/23/2008 14:02	Zinc		26200	mg/kg	5	ZN
MOF3-D	10/23/2008 14:05	Arsenic		74	mg/kg	5	AS
MOF3-D	10/23/2008 14:05	Cadmium		135	mg/kg	1	CD
MOF3-D	10/23/2008 14:05	Copper		84	mg/kg	5	CU
MOF3-D	10/23/2008 14:05	Lead		485	mg/kg	5	PB
MOF3-D	10/23/2008 14:05	Selenium		25	mg/kg	5	SE
MOF3-D	10/23/2008 14:05	Zinc		420	mg/kg	5	ZN
MOF3-E	10/23/2008 14:07	Arsenic		17	mg/kg	5	AS
MOF3-E	10/23/2008 14:07	Cadmium		12	mg/kg	1	CD
MOF3-E	10/23/2008 14:07	Copper		19	mg/kg	5	CU
MOF3-E	10/23/2008 14:07	Lead		49	mg/kg	5	PB
MOF3-E	10/23/2008 14:07	Selenium		27	mg/kg	5	SE
MOF3-E	10/23/2008 14:07	Zinc		66	mg/kg	5	ZN
MOF3-F	10/23/2008 14:10	Arsenic		33	mg/kg	5	AS
MOF3-F	10/23/2008 14:10	Cadmium		15	mg/kg	1	CD
MOF3-F	10/23/2008 14:10	Copper		27	mg/kg	5	CU
MOF3-F	10/23/2008 14:10	Lead		54	mg/kg	5	PB
MOF3-F	10/23/2008 14:10	Selenium		8	mg/kg	5	SE
MOF3-F	10/23/2008 14:10	Zinc		76	mg/kg	5	ZN
MOF3-G	10/23/2008 14:15	Arsenic		25	mg/kg	5	AS
MOF3-G	10/23/2008 14:15	Cadmium		34	mg/kg	1	CD
MOF3-G	10/23/2008 14:15	Copper		34	mg/kg	5	CU
MOF3-G	10/23/2008 14:15	Lead		104	mg/kg	5	PB
MOF3-G	10/23/2008 14:15	Selenium		6	mg/kg	5	SE
MOF3-G	10/23/2008 14:15	Zinc		98	mg/kg	5	ZN
MOF3-H	10/23/2008 14:20	Arsenic		63	mg/kg	5	AS
MOF3-H	10/23/2008 14:20	Cadmium		223	mg/kg	1	CD
MOF3-H	10/23/2008 14:20	Copper		89	mg/kg	5	CU
MOF3-H	10/23/2008 14:20	Lead		691	mg/kg	5	PB
MOF3-H	10/23/2008 14:20	Selenium		16	mg/kg	5	SE
MOF3-H	10/23/2008 14:20	Zinc		434	mg/kg	5	ZN
MOF3-I	10/23/2008 14:25	Silver	ND		mg/kg	5	AG

TABLE B-4. DEMOLITION FOOTPRINT SOIL SAMPLE LABORATORY RESULTS

Sample ID	Collection Date	Analyte	TResult	NResult	Runits	Rlimit	ParLabel
MOF3-I	10/23/2008 14:25	Aluminum		5900	mg/kg	5	AL
MOF3-I	10/23/2008 14:25	Arsenic	ND		mg/L	0.1	AS
MOF3-I	10/23/2008 14:25	Arsenic		7	mg/kg	5	AS
MOF3-I	10/23/2008 14:25	Barium		36	mg/kg	5	BA
MOF3-I	10/23/2008 14:25	Beryllium	ND		mg/kg	5	BE
MOF3-I	10/23/2008 14:25	Cadmium	ND		mg/L	0.1	CD
MOF3-I	10/23/2008 14:25	Cadmium		9	mg/kg	1	CD
MOF3-I	10/23/2008 14:25	Cobalt	ND		mg/kg	5	CO
MOF3-I	10/23/2008 14:25	Chromium		17	mg/kg	5	CR
MOF3-I	10/23/2008 14:25	Copper	ND		mg/L	0.1	CU
MOF3-I	10/23/2008 14:25	Copper		20	mg/kg	5	CU
MOF3-I	10/23/2008 14:25	Iron		23600	mg/kg	10	FE
MOF3-I	10/23/2008 14:25	Mercury		0.12	mg/kg	0.05	HG
MOF3-I	10/23/2008 14:25	Manganese		231	mg/kg	5	MN
MOF3-I	10/23/2008 14:25	Nickel	ND		mg/kg	5	NI
MOF3-I	10/23/2008 14:25	Lead	ND		mg/L	0.1	PB
MOF3-I	10/23/2008 14:25	Lead		43	mg/kg	5	PB
MOF3-I	10/23/2008 14:25	Antimony	ND		mg/kg	5	SB
MOF3-I	10/23/2008 14:25	Selenium	ND		mg/L	0.1	SE
MOF3-I	10/23/2008 14:25	Selenium	ND		mg/kg	5	SE
MOF3-I	10/23/2008 14:25	Thallium	ND		mg/kg	5	TL
MOF3-I	10/23/2008 14:25	Vanadium		74	mg/kg	5	V
MOF3-I	10/23/2008 14:25	Zinc	ND		mg/L	0.1	ZN
MOF3-I	10/23/2008 14:25	Zinc		36	mg/kg	5	ZN

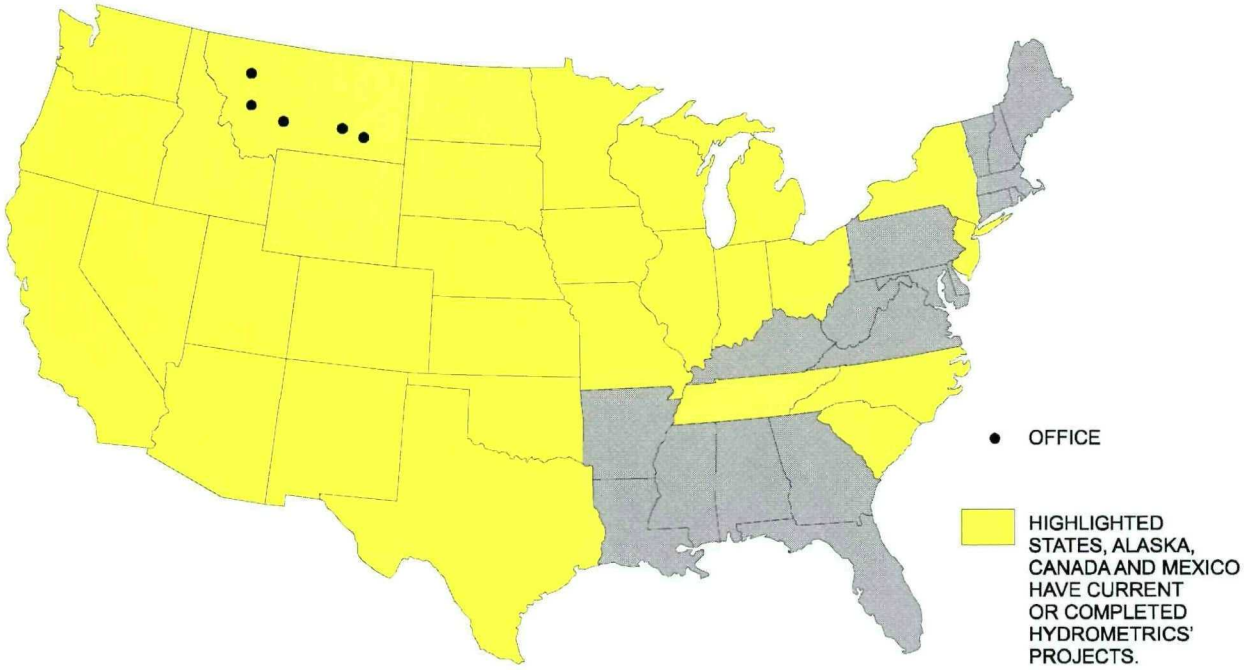

HYDROMETRICS, INC. MONTANA OFFICES

HELENA (Corporate)
3020 Bozeman Avenue
Helena, MT 59601
Phone: (406) 443-4150
FAX: (406) 443-4155

BILLINGS
5602 Hesper Road
Billings, MT 59106
Phone: (406) 656-1172
FAX: (406) 656-8912

MISSOULA
667 East Beckwith
Missoula, MT 59801
Phone: (406) 721-8243
FAX: (406) 542-2619

COLSTRIP
Phone: (406) 656-8305
Fax: (406) 656-8912

KALISPELL
300 Learn Lane
Kalispell, MT 59901
Phone: (406) 471-8635
