CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 543-4.1.1
(908) 754-8383
Fax: (908) 754-8633

NJ EDA approved testing laboratory • MBE/DBE Certified • NJ DOT Certified
www.ANSConsultants.com

ASPHALT COMPACTION TEST REPORT

☒ As per ASTM D-2950-91 (Nuclear Density Gauge)

CLIENT : Capo Environmental Inc.
45 Pine Street, Suite 110
Rockaway, NJ 07866

Attn. Mr. Paul Ferroni

PROJECT : Rockaway Borough Sportfund Site
122 Jackson Avenue
Rockaway, NJ

DATE : 8/8/2011

FILE NO. : ANX – 1743

REPORT # : 01

ENGINEER : Kiren Nagar

TIME : 7:00 a.m. – 9:00 p.m.

CERTIFICATE OF INSPECTION

As per your request asphalt compaction tests were performed at the above referenced project site on 08/08/2011.

TEST NO.	*1 LOCATION/ ELEVATION	DENSITY (LB/CU FT) FIELD	COMPACTION (%)	TEST NO.	*1 LOCATION/ ELEVATION	DENSITY (LB/CU FT) FIELD	COMPACTION (%)
2" Base Course (1 - 2)				2" Surface Course (1-6)			
1	"	149.1	94.1	5	"	149.6	92.6
2	"	150.4	94.8	6	"	151.7	95.4
3	"	148.4	93.7	7	"	150.9	94.7
4	"	148.2	93.6	8	"	151.9	95.2
TROXLER # 28 DAY OF 26 -6592 DS2 OF W3 -1503							

Remarks :

1 A Marshall number of 154.7 lb./ft.³ and A of Rice number 160.4 lb./ft.³ was provided by the Client. A Rice number of 156.4 lb./ft.³ was utilized for test # 1 to 4. (Base course 1-4).

2 A Marshall number of 151.6 lb./ft.³ and A of Rice number 157.9 lb./ft.³ was provided by the Client. A Rice number of 157.3 lb./ft.³ was utilized for test # 5 to 8. (Surface course 1-6).

Truck Temperature 280°F, 278°F, 275° - (1-4) Truck Temperature 280°F, 280°F, 280°F - (1-6). Asphalt temperature was consumed between 275°F to 280°F for both mixes. Thickness verification made at every 5' distance for both courses and found satisfactory.

Location/Elevation : Test were taken over base course and surface course (2" and 2") between Ogden Avenue and Manitoba - 1. (See attached sketch).

Specification Requirements : 93% to 98% of the Rice Density.

☒ Complied With : Test # 1 – 8

☐ Not Complied With :

☒ Sliding block covering the source rod was checked before placing the gauge in the storage box.

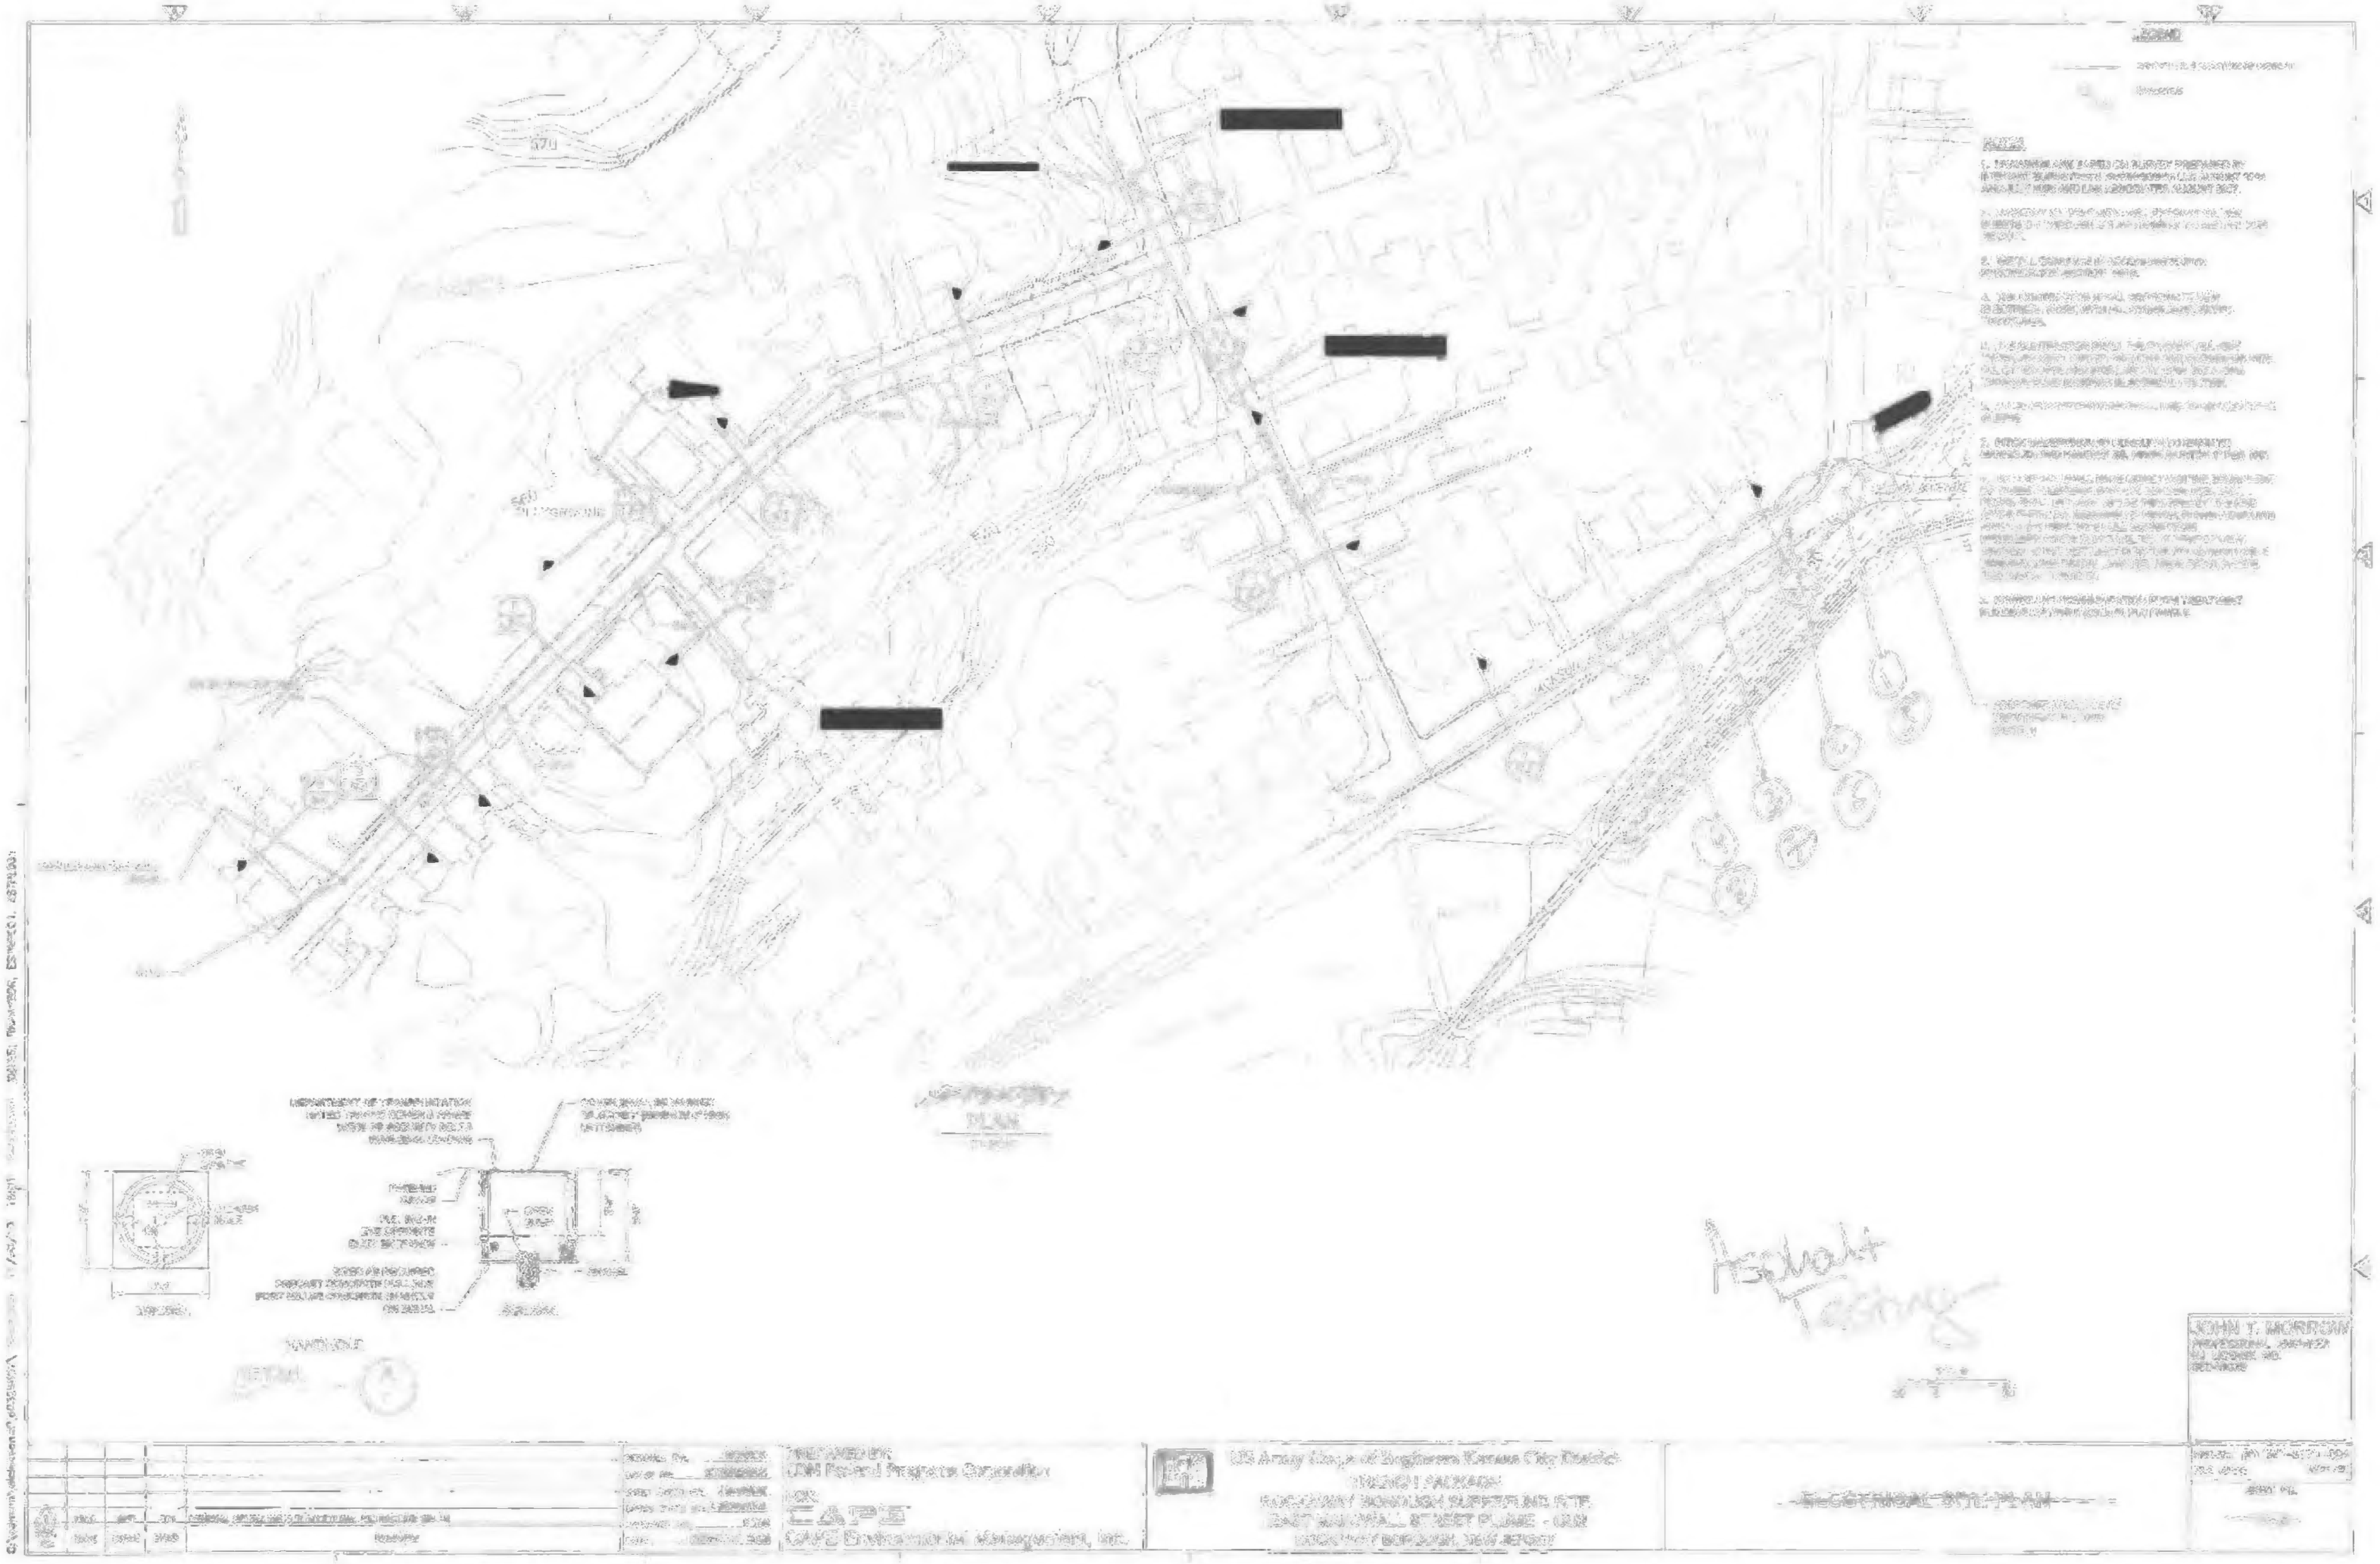
Asphalt Testing
JOHN T. MORRISON
US Army Corps of Engineers Kansas City District
CAPE
CAPE Environmental Management, Inc.

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATUI
(908) 754-8393
Fax: (908) 754-8633

NJ EDA Approved Testing Laboratory • AASHTO/ACE Certified • NJ DEP Certified
www.ANSConsultants.com

All Services Involved, Rings, Analysis, Drawings and Field Notes, Plans, Designs, Specifications, Reports, Inc. Analysis, Computations, Drawings, Specifications, Notes, Reports

ASPHALT COMPACTION TEST REPORT

☒ As per ASTM D-2950-91 (Nuclear Density Gauge)

CLIENT : Cano Environmental Inc.
45 Pine Street, Suite 110
Rockaway, NJ 07866

Attn. Mr. Paul Ferroni

PROJECT : Rockaway Borough Superfund Site
102 Jackson Avenue
Rockaway, NJ

DATE : 08/08/2011

FILE NO. : ANX - 1743

REPORT # : 01

ENGINEER : Ripan Nagar

TIME : 7:00 a.m. - 5:00 p.m.

CERTIFICATE OF INSPECTION

As per your request asphalt compaction tests were performed at the above referenced project site on 08/08/2011.

	*1	DENSITY (LBS/CU.FT)			*1	DENSITY (LBS/CU.FT)	
TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)	TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)
3" Base Course (1 - 2)				2" Surface Course (5-8)			
1	-	150.4	96.4	5	-	150.2	96.3
2	-	150.3	96.3	6	-	151.2	96.9
3	-	150.4	96.4	7	-	150.9	96.7
4	-	150.2	96.2	8	-	151.0	96.7
TROXLER 3241 SN: CF 35-8362 DSP CF MS-4439							

Remarks :

1. A Marshall number of 154.7 lb/ft³ and A of Rice number 159.4 lb/ft³ was provided by the Client. A Rice number of 159.4 lb/ft³ was utilized for test # 1 to 4. (Base course 1-2).

2. A Marshall number of 151.6 lb/ft³ and A of Rice number 157.3 lb/ft³ was provided by the Client. A Rice number of 157.3 lb/ft³ was utilized for test # 5 to 8. (Surface course 5-8).

   Truck Temperature 282°F, 276°F, 279° - (1-2). Truck Temperature 280°F, 282°F, 282°F - (5-8). Asphalt temperature was encountered between 276°F to 280°F for both mixes. Thickness verification made at every 5' distance for both courses and found satisfactory.

Location/Elevation : Test were taken over base course and surface course (3" and 2") between Ogden Avenue and Manhole - 1. (See attached sketch).

Specification Requirements : 92% to 98% of the Rice Density.

☒ Complied With : Test # 1 - 8

☐ Not Complied With :

☒ Sliding block covering the source rod was checked before placing the gauge in the storage box.

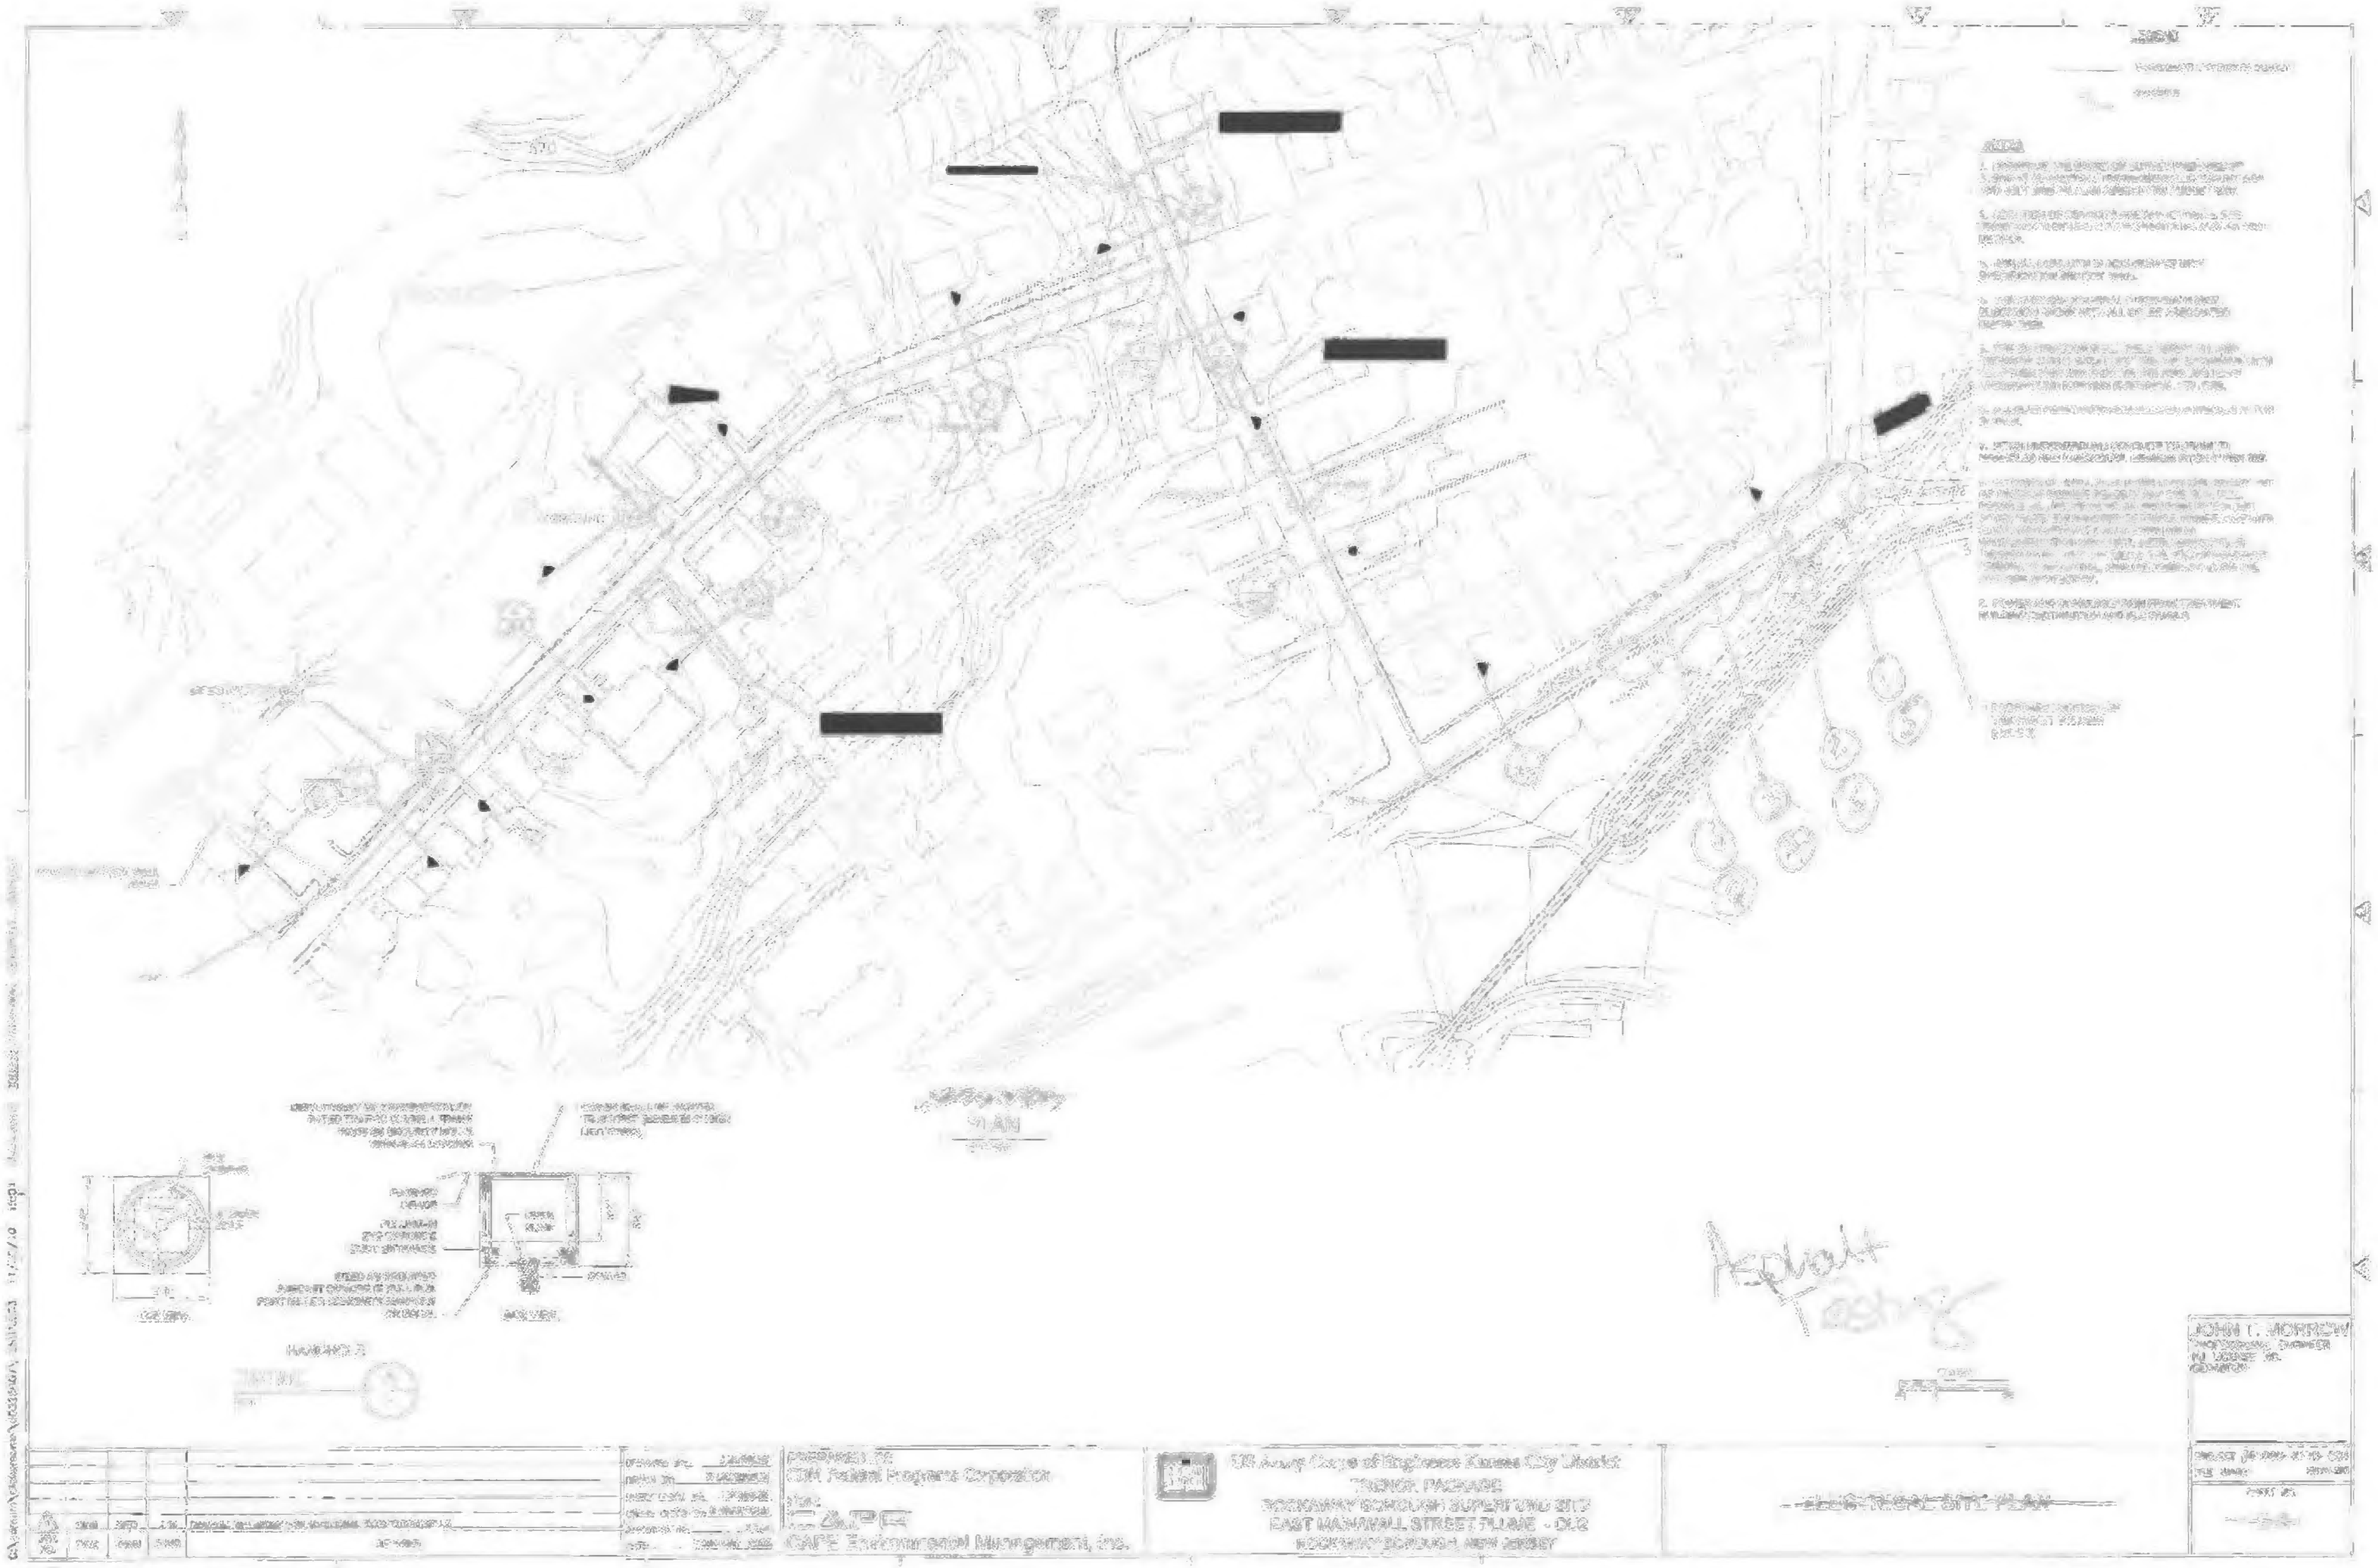
PLAN
JOHN T. MONTROW
CDM Federal Programs Corporation
CAPE
CAPE Environmental Management, Inc.
US Army Corps of Engineers Kansas City District
TRENCH PACKAGE
ROCKAWAY BOROUGH SUPERFUND SITE
EAST MANNWALL STREET PLUME - OU2
ROCKAWAY BOROUGH, NEW JERSEY
SITE PLAN

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATTL
(908) 754-8383
Fax: (908) 754-8633

NJ EDA Approved Testing Laboratory • MBE/SBE Certified • NJDEP Certified
www.ANSConsultants.net

[illegible]

ASPHALT COMPACTION TEST REPORT

☒ As per ASTM D-2950-91 (Nuclear Density Gauge)

CLIENT :	Cape Environmental Inc. 45 Pine Street, Suite 110 Rockaway, NJ 07866	DATE :	8/8/2011
		FILE NO. :	ANX - 1748
	Attn. Mr. Paul Ferroni	REPORT # :	01
PROJECT :	Rockaway Borough Superfund Site 122 Jackson Avenue Rockaway, NJ	ENGINEER :	Ripen Nagal
		TIME :	7:00 a.m. - 5:00 p.m.

CERTIFICATE OF INSPECTION

As per your request asphalt compaction tests were performed at the above referenced project site on 08/08/2011

	*	DENSITY (LB/CU FT)			*	DENSITY (LB/CU FT)	
TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)	TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)
2" Base Course (1 - 2)				2" Surface Course (1-8)			
1	-	150.8	94.4	5	-	148.6	92.9
2	-	150.4	93.8	6	-	151.2	94.4
3	-	149.4	93.4	7	-	150.8	94.7
4	-	144.2	90.2	8	-	151.4	94.6
TROXLER # 25 DS1 OF DS - 8862 DS2 OF MS - 7933							

Remarks :

1 A Marshall number of 154.7 lb./ft.³ and A of Rice number 158.4 lb./ft.³ was provided by the Client. A Rice number of 158.4 lb./ft.³ was utilized for test # 1 to 4. (Base course 1-2).

2 A Marshall number of 151.6 lb./ft.³ and A of Rice number 157.3 lb./ft.³ was provided by the Client. A Rice number of 157.3 lb./ft.³ was utilized for test # 5 to 8. (Surface course 1-8).

Truck Temperature 262°F, 278°F, 276° - (1-2) Truck Temperature 280°F, 282°F, 282°F - (1-8). Aspalt temperature was encountered between 270°F to 280°F for both mixes. Thickness verification made at every 5' distance for both courses and found satisfactory.

Location/Elevation : Test were taken over base course and surface course (6" and 2") between Ogden Avenue and Manhole - 1. (See attached sketch).

Specification Requirements : 92% to 96% of the Rice Density.

☒ Complied With : Test # 1 - 8

☐ Not Complied With :

☒ Sliding Block covering the source rod was checked before placing the gauge in the storage box.

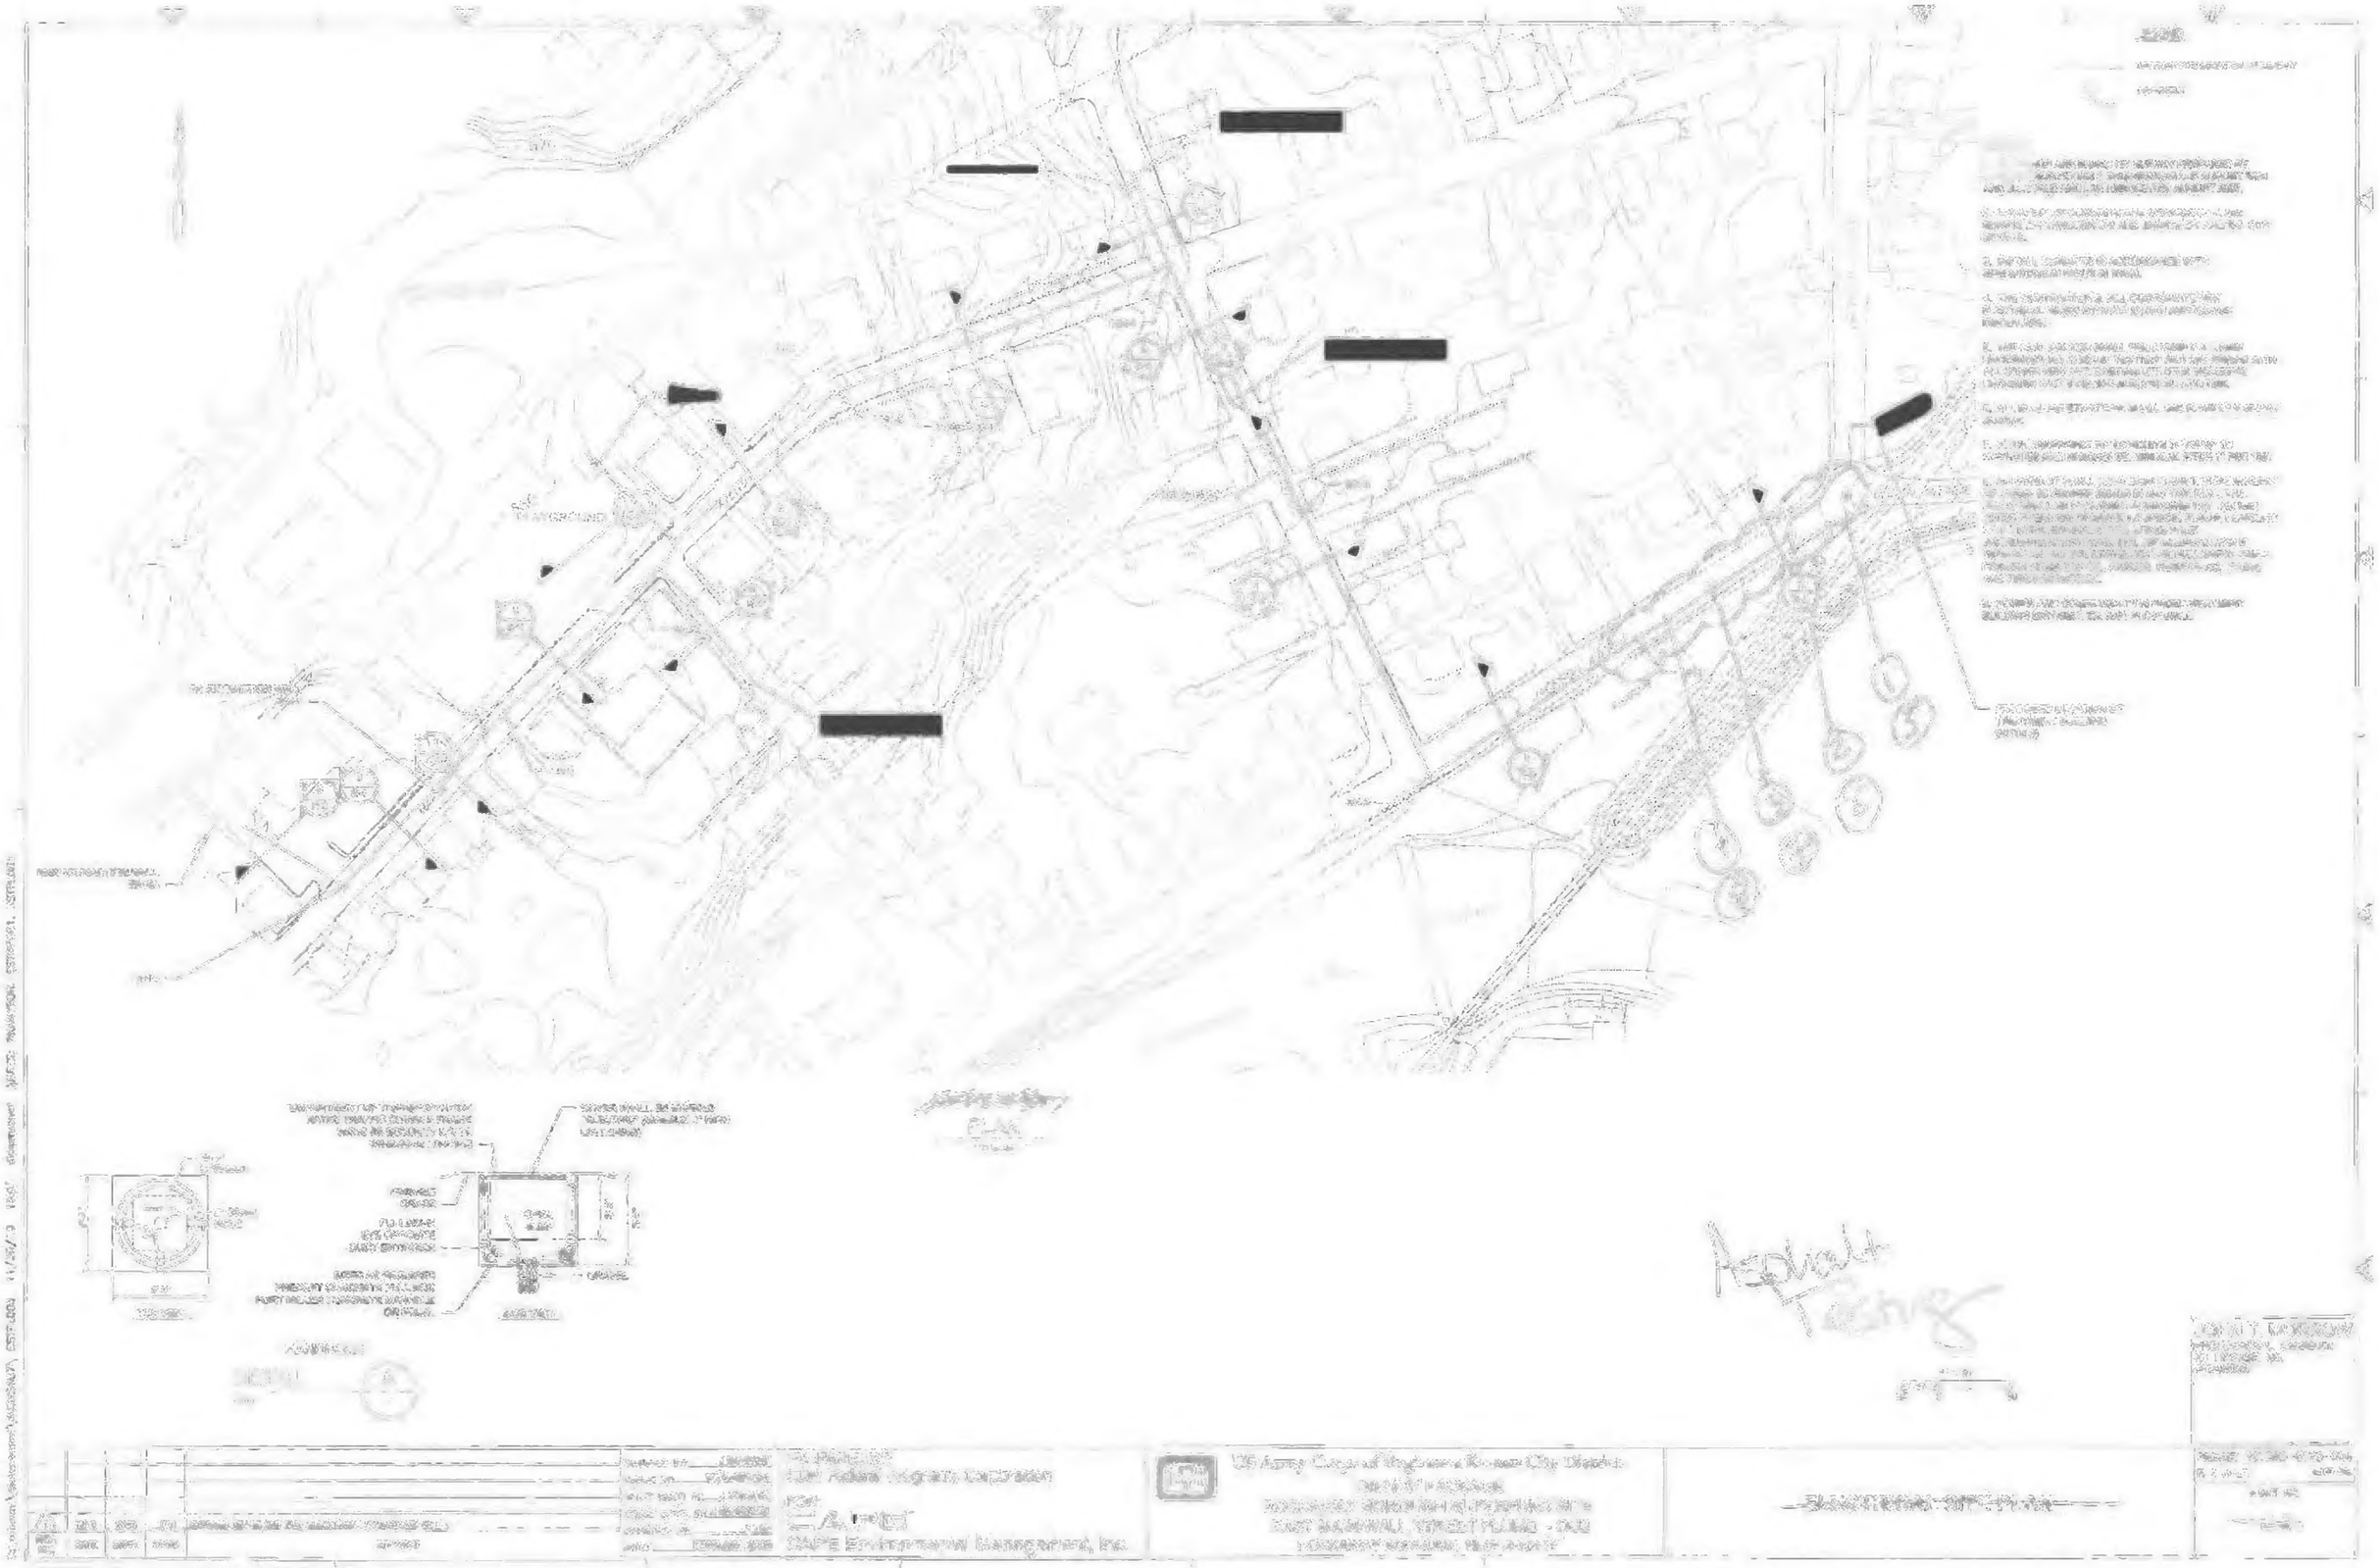
Asphalt Paving

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 345-ATUI
(908) 754-0383
Fax: (908) 754-3633

NJ EDA Approved Testing Laboratory • AASHTO/ASTM Certified • NJ DEP Certified
www.ANSconsultants.net

No Copies, Scanned Data, Modified Reports, Logos, File Copies, Photocopies, Faxes, All Parts, Complete Copies, Or Signed Reproductions Are Prohibited

ASPHALT COMPACTION TEST REPORT

☒ As per ASTM D-2950-91 (Nuclear Density Gauge)

CLIENT : Cape Environmental Inc.
45 Pine Street, Suite 113
Rockaway, NJ 07866

Attn. Mr. Paul Ferroni

DATE : 6/9/2011

FILE NO. : ANX - 1743

REPORT # : 02

PROJECT : Rockaway Borough Superfund Site
122 Jackson Avenue
Rockaway, NJ

ENGINEER : Ripen Nagar &
Rishor Soni

TIME : 7:00 a.m. - 3:30 p.m.

CERTIFICATE OF INSPECTION

As per your request asphalt compaction tests were performed at the above referenced project site on 06/09/2011

	%	DENSITY (LB./CU.FT)			%	DENSITY (LB./CU.FT)	
TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)	TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)
± 3" Base Course				± 3" Top Course			
1	-	149.0	95.7	4	-	149.5	91.5
2	-	151.5	96.8	5	-	149.8	92.9
3	-	150.7	96.4				
TROXLER # 25 DS1 OF DS-6872 DS2 OF MS-1950							

Remarks :

1 A Marshall number of 154.4 lb./ft.³ and A of Rice number 158.1 lb./ft.³ was provided by the Client. A Rice number of 158.1 lb./ft.³ was utilized for test # 1 to 3. (Base course).

2 A Marshall number of 152.4 lb./ft.³ and A of Rice number 156.0 lb./ft.³ was provided by the Client. A Rice number of 156.0 lb./ft.³ was utilized for test # 4 to 5. (Top course).

Truck Temperature 300°F, 300°F and 298° - (1-3 Base). Truck Temperature 320°F and 280°F (4-5 Top). Surface course was paved during rain and did not tested. Contractor was informed along with Cape Rep. decided to finish next day.

Location/Elevation : See attached sketch.

Specification Requirements : 92% to 99% of the Rice Density.

☒ Complied With : Test # 1 - 5

☐ Not Complied With :

☒ Sliding block covering the source rod was checked before placing the gauge in the storage box.

See Additional Page Ref.

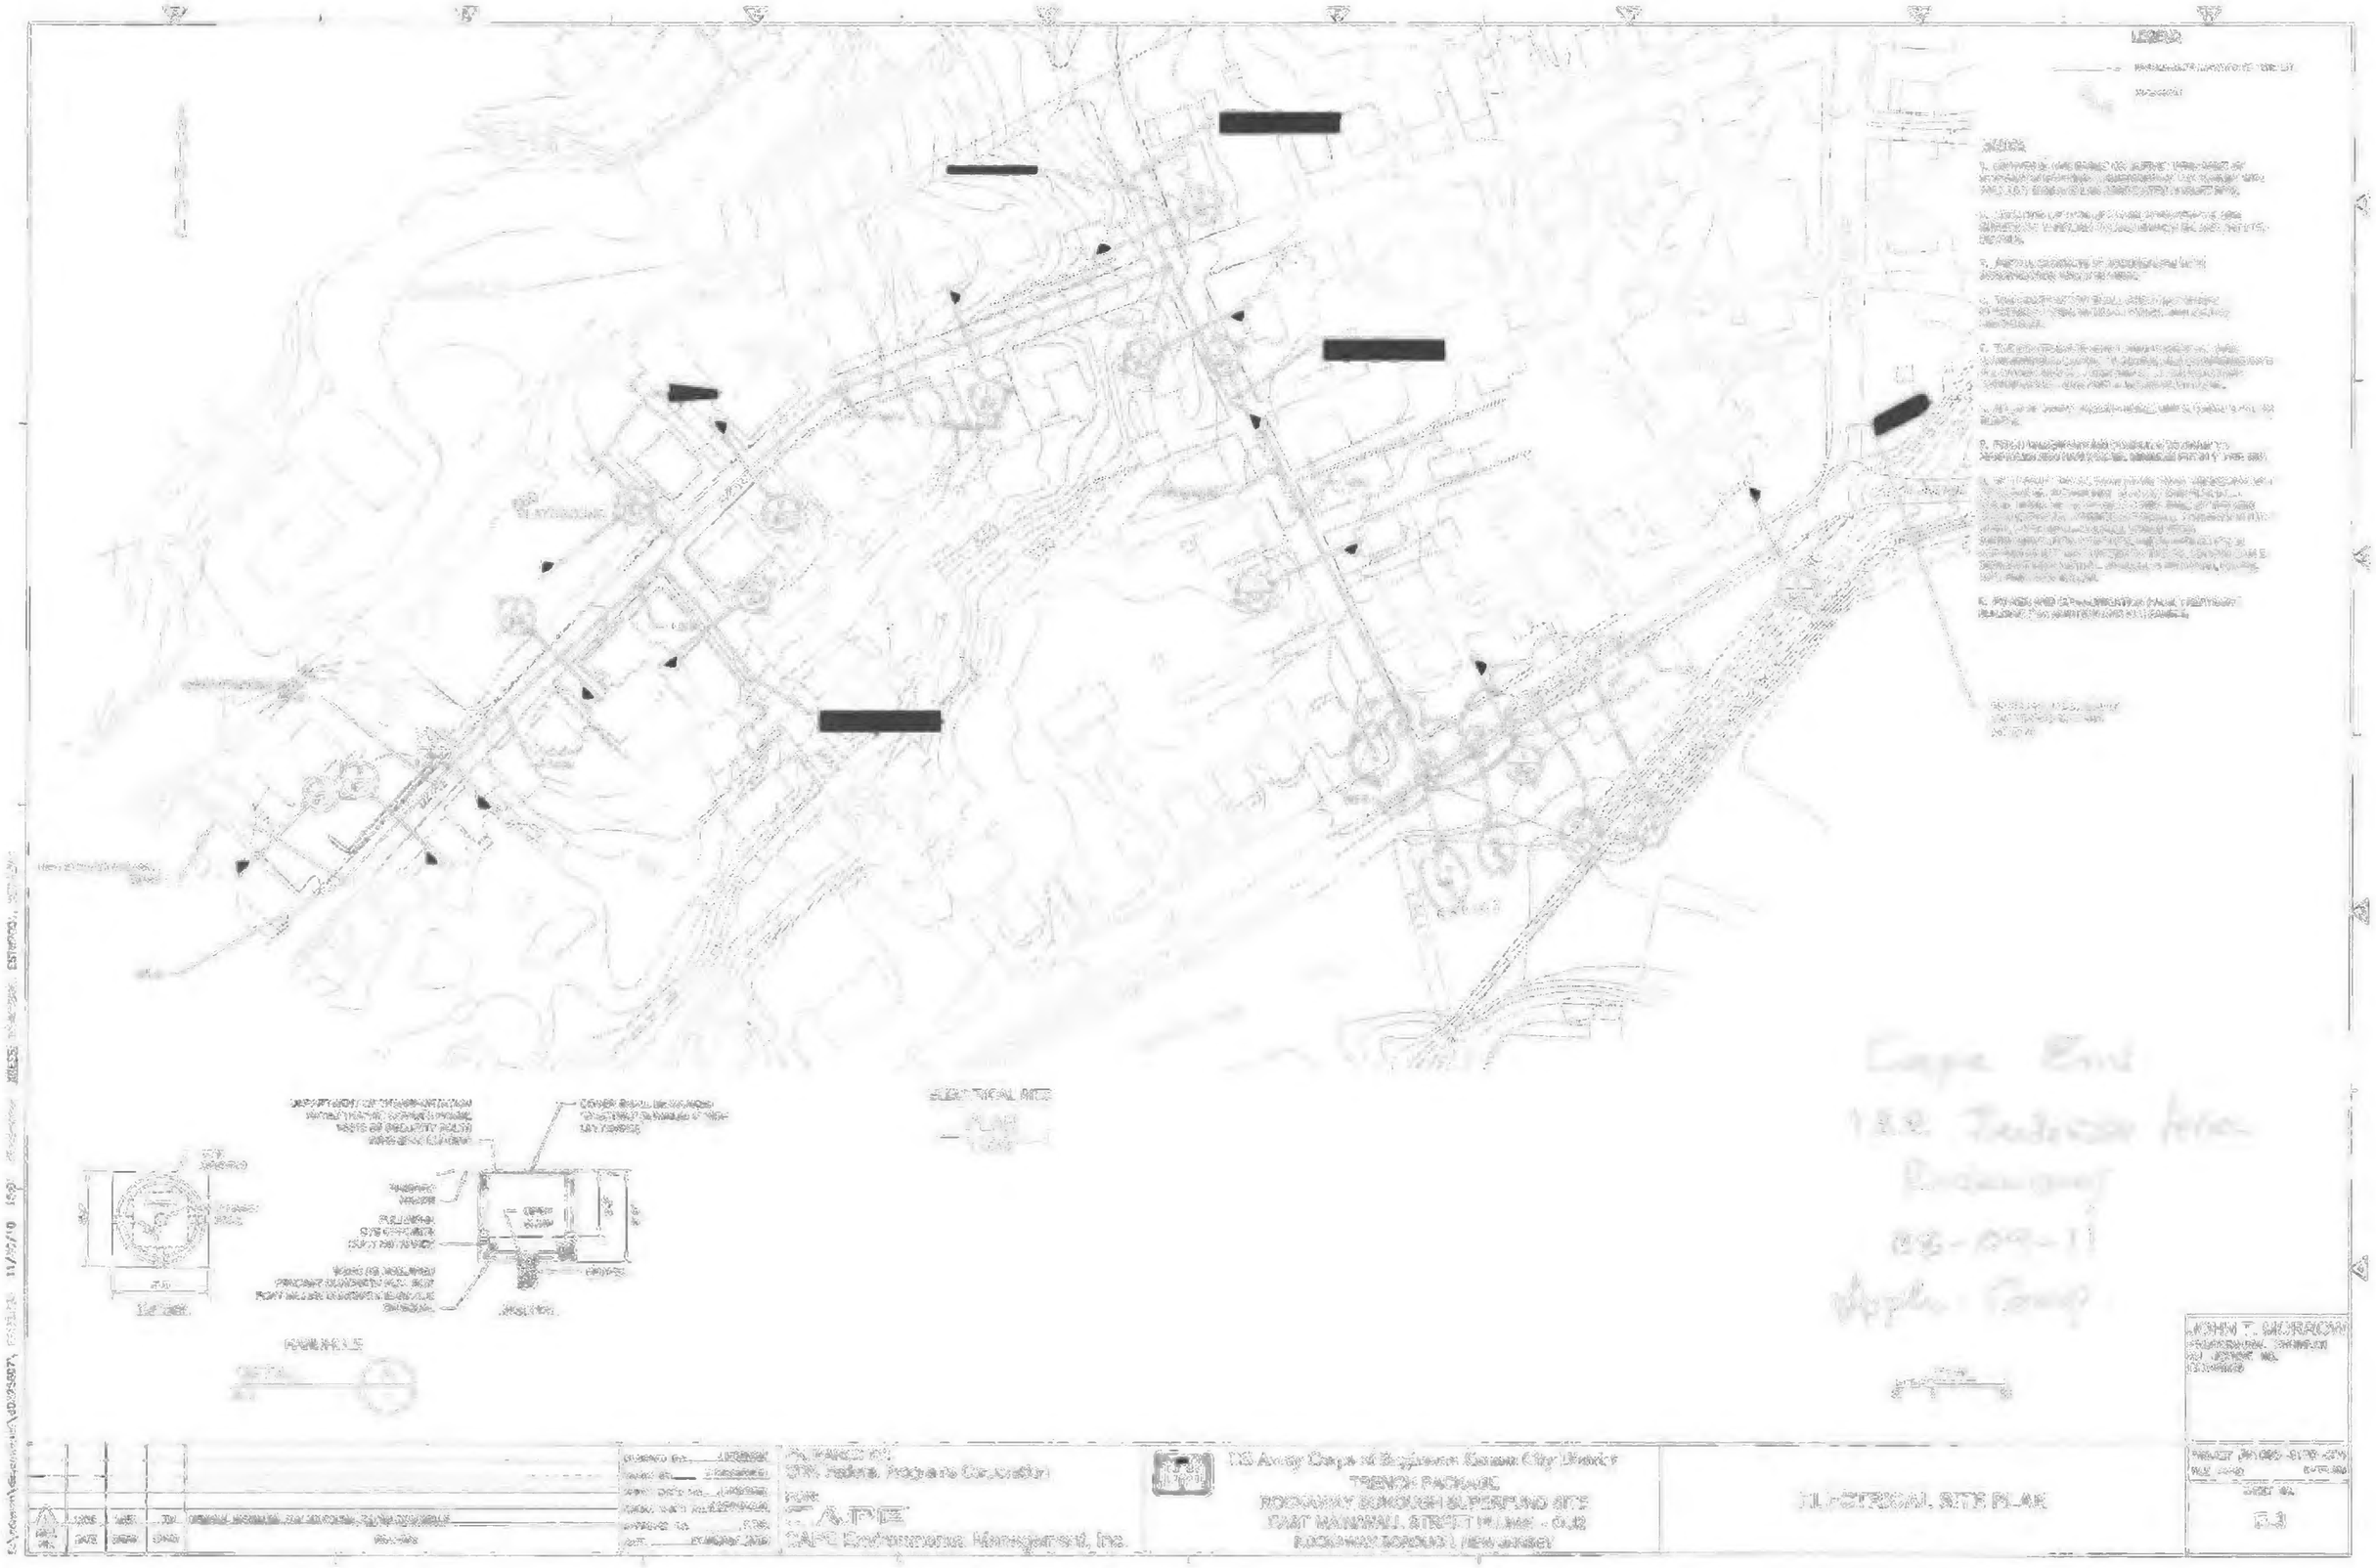
LEGEND
NOTES
Cape End
TRC Jackson Area
Redevelopment
03-09-11
Apple Comp
JOHN T. MORROW
TRENCH PACKAGE
ROCKAWAY BOROUGH SUPERFUND SITE
EAST MANSFIELD STREET TO LINE - 0.02
ROCKAWAY BOROUGH, NEW JERSEY
CAPE Environmental Management, Inc.
HISTORICAL SITE PLAN
E.3

CONSULTANTS, INC.
4428 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATLL
(908) 754-8383
Fax: (908) 754-8633

NJ EDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSConsultants

ASPHALT COMPACTION TEST REPORT

☒ As per ASTM D-2950-91 (Nuclear Density Gauge)

CLIENT :	Cape Environmental Inc. 45 Pine Street, Suite 110 Rockaway, NJ 07866	DATE :	8/8/2011
		FILE NO. :	ANX - 1743
	Attn. Mr. Paul Ferroni	REPORT # :	02
PROJECT :	Rockaway Borough Superfund Site 122 Jackson Avenue Rockaway, NJ	ENGINEER :	Nipen Nagar & Kishor Soni
		TIME :	7:00 a.m. - 3:00 p.m.

CERTIFICATE OF INSPECTION

As per your request asphalt compaction tests were performed at the above referenced project site on 08/08/2011

TEST NO.	LOCATION/ ELEVATION	DENSITY (LB/CU FT) FIELD	DENSITY (LB/CU FT) COMPACTION (%)	TEST NO.	LOCATION/ ELEVATION	DENSITY (LB/CU FT) FIELD	DENSITY (LB/CU FT) COMPACTION (%)
1-3" Base Course				4-3" Top Course			
1	-	150.1	92.7	4	-	150.6	94.0
2	-	147.9	91.4	5	-	149.8	93.5
3	-	148.7	92.2				
TROXLER # 26 DSC OF DB - 4872 DS2 OF MB - 1856							

Remarks :

1 A Marshall number of 154.4 lb./ft.³ and A of Rice number 159.7 lb./ft.³ was provided by the Client. A Rice number of 159.1 lb./ft.³ was utilized for test # 1 to 3. (Base course).

2 A Marshall number of 152.4 lb./ft.³ and A of Rice number 158.0 lb./ft.³ was provided by the Client. A Rice number of 158.0 lb./ft.³ was utilized for test # 4 to 5. (Top course).

Truck Temperature 308°F, 308°F and 298° - (1-3 Base). Truck Temperature 290°F and 292°F (4-5 Top). Surface course was paved during rain and did not tested. Contractor was informed along with Cape Rep. decided to check next day.

Location/Elevation : See attached sketch.

Specification Requirements : 92% to 98% of the Rice Density.

☒ Complied With : Test # 1 - 5

☐ Not Complied With :

☒ Sliding block covering the source rod was checked before placing the gauge in the storage box.

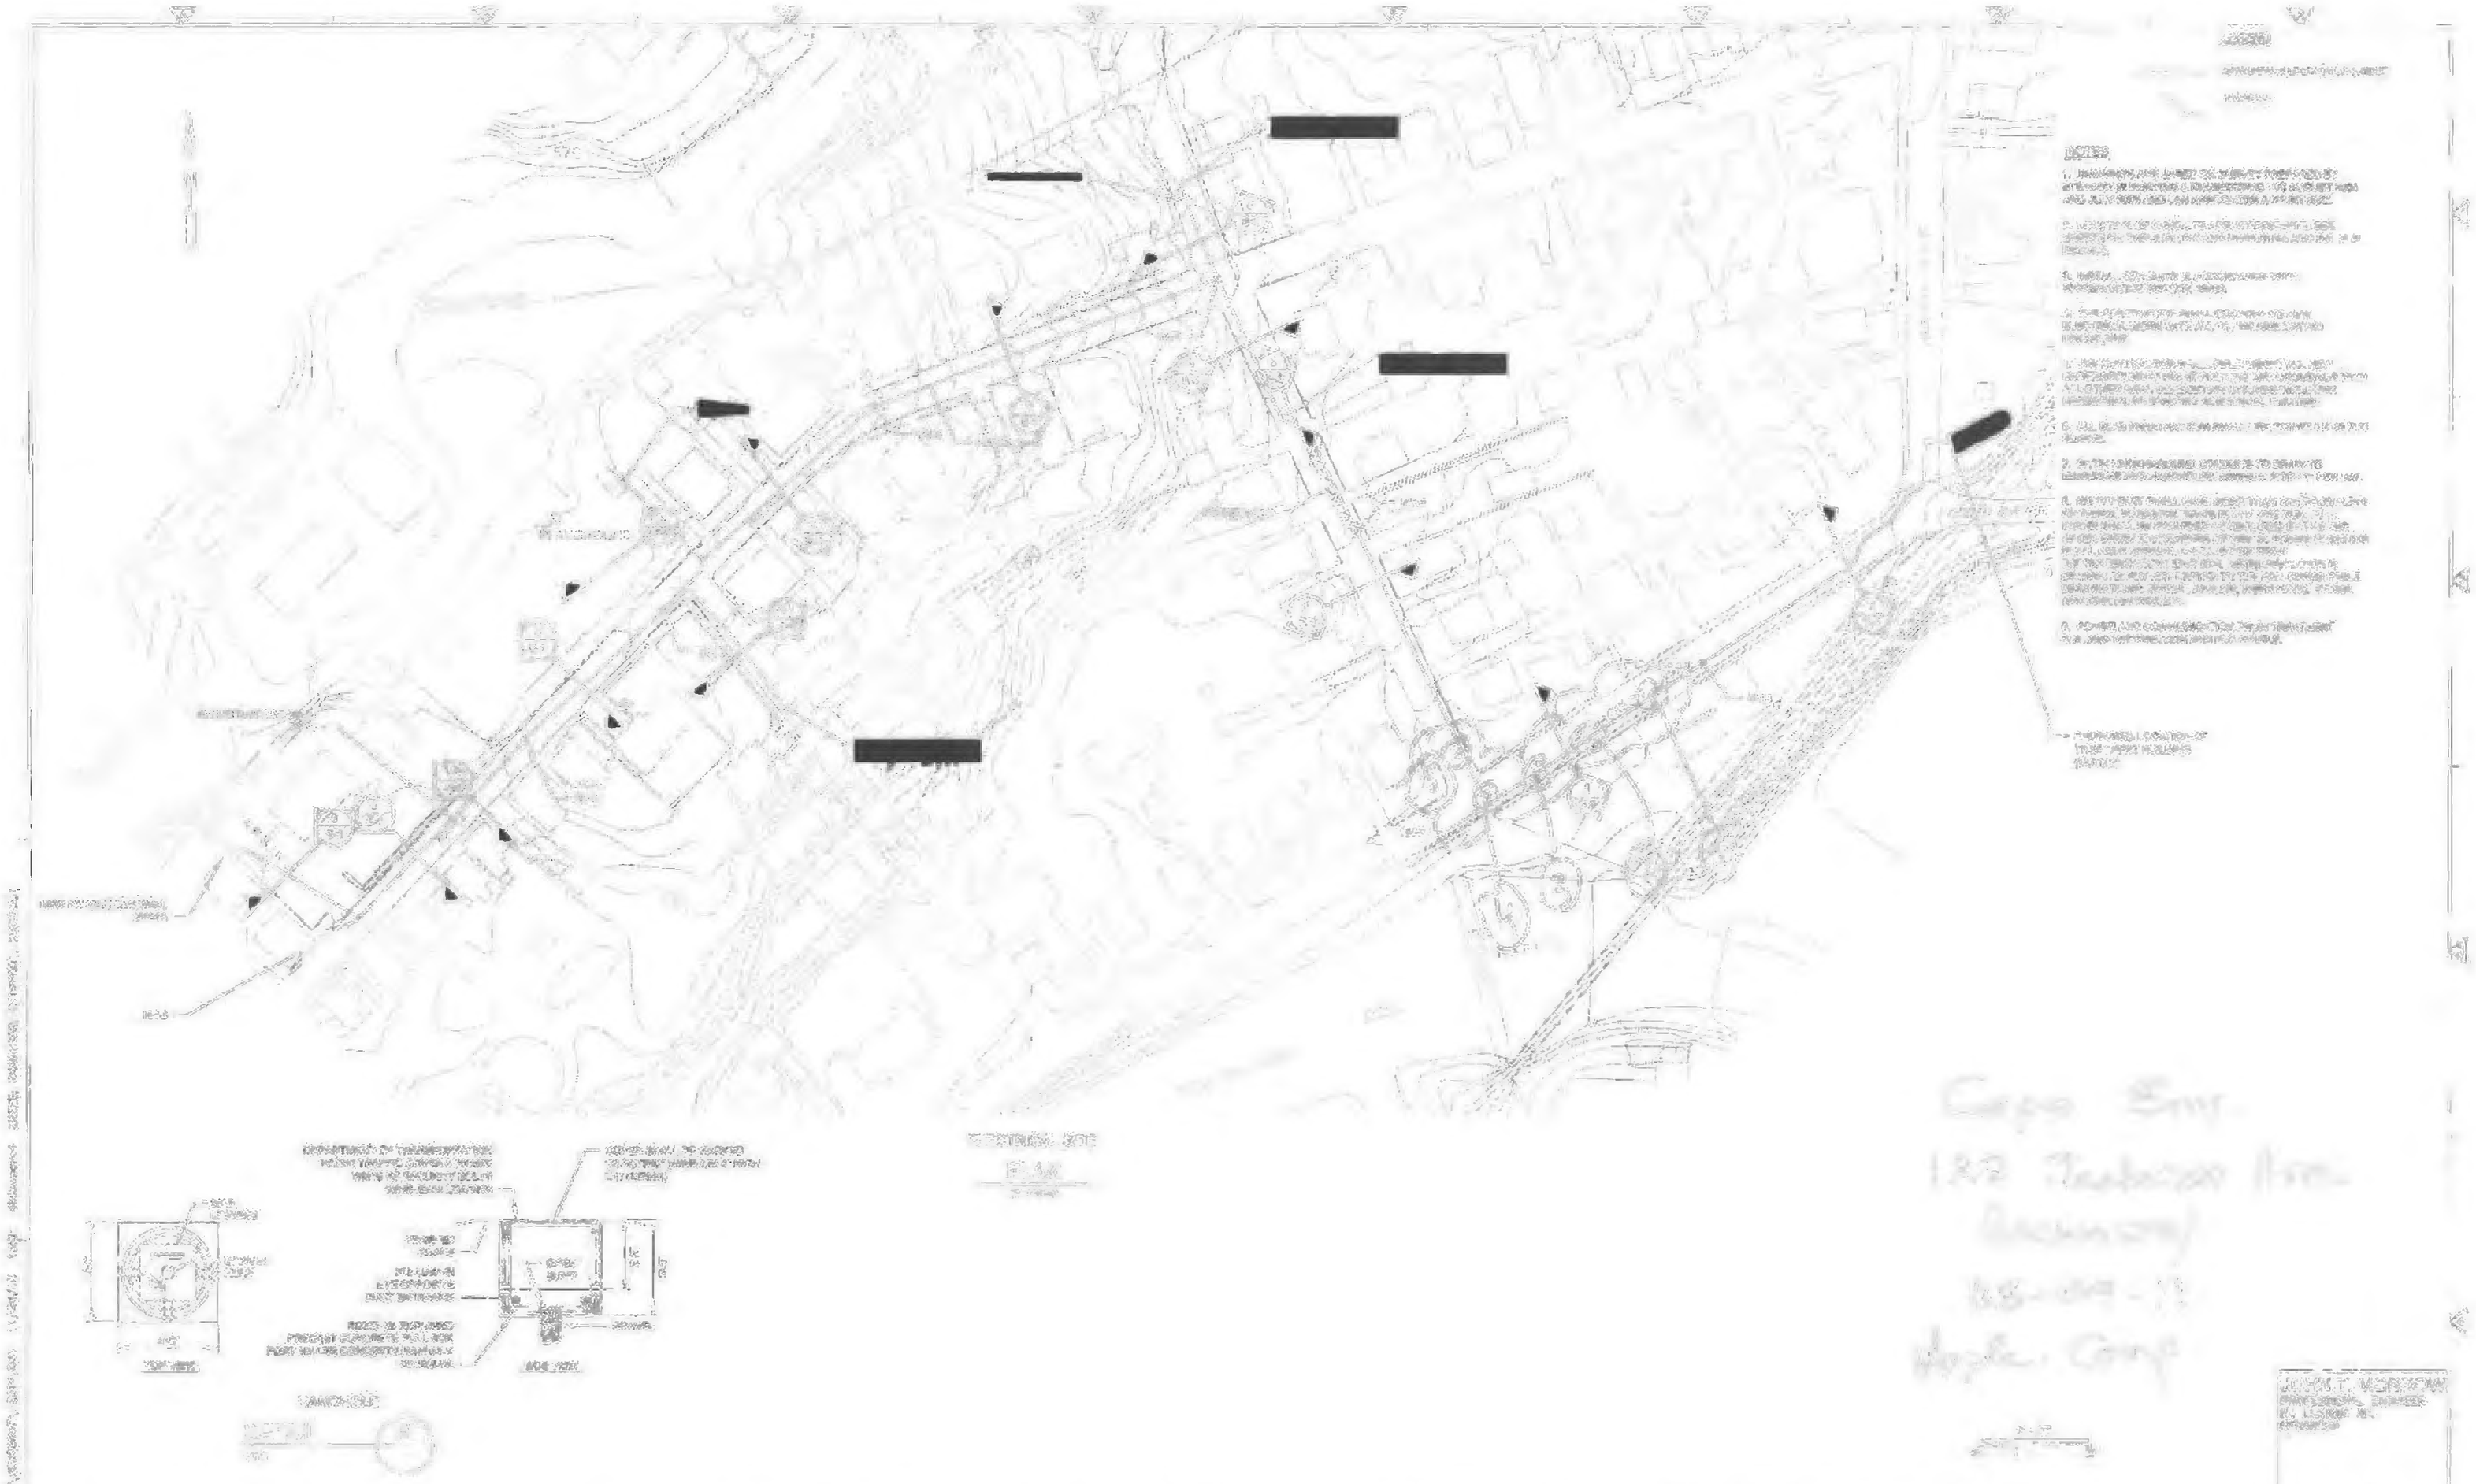

ELECTRICAL SITE PLAN

E-3

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ACUT
(908) 754-8353
Fax: (908) 754-8533

NJ EDA Approved Testing Laboratory • AASHTO Certified • NJ DEP Certified
www.AnsConsultants.com

ASPHALT COMPACTION TEST REPORT

☒ As per ASTM D-2950-91 (Nuclear Density Gauge)

CLIENT : Cape Environmental Inc.
49 Pine Street, Suite 110
Rockaway, NJ 07866

Attn. Mr. Paul Ferroni

PROJECT : Rockaway Borough Superfund Site
122 Jackson Avenue
Rockaway, NJ

DATE : 8/9/2011

FILE NO. : ANX - 1749

REPORT # : 02

ENGINEER : Hoon Nagar &
Kishor Soni

TIME : 7:00 a.m. - 3:30 p.m.

CERTIFICATE OF INSPECTION

As per your request asphalt compaction tests were performed at the above referenced project site on 08/09/2011.

	#	DENSITY (LB/CU FT)			#	DENSITY (LB/CU FT)	
TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)	TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)
± 3" Base Course				± 3" Top Course			
1	*	148.1	93.7	4	*	148.6	94.0
2	*	147.5	93.3	5	*	148.6	94.0
3	*	148.7	94.1				
TROXLER # 29 DS1 OF DS-WH72 DS2 OF WS-1850							

Remarks :

1 A Marshall number of 154.4 lb./ft.³ and A of Rice number 158.1 lb./ft.³ was provided by the Client. A Rice number of 158.1 lb./ft.³ was utilized for test # 1 to 3. (Base course).

2 A Marshall number of 152.4 lb./ft.³ and A of Rice number 158.0 lb./ft.³ was provided by the Client. A Rice number of 158.0 lb./ft.³ was utilized for test # 4 to 5. (top course).

Truck Temperature 300°F, 308°F and 299° - (1-3 Base) Truck Temperature 290°F and 298°F (4-5 Top). Surface course was paved during rain and did not test. Contractor was informed along with Cape Rep. decided to check next day.

Location/Elevation : See attached sketch.

Specification Requirements : 92% to 98% of the Rice Density.

☒ Complied With : Test # 1 - 5

☐ Not Complied With :

☒ Sliding block covering the source rod was checked before placing the gauge in the storage box.

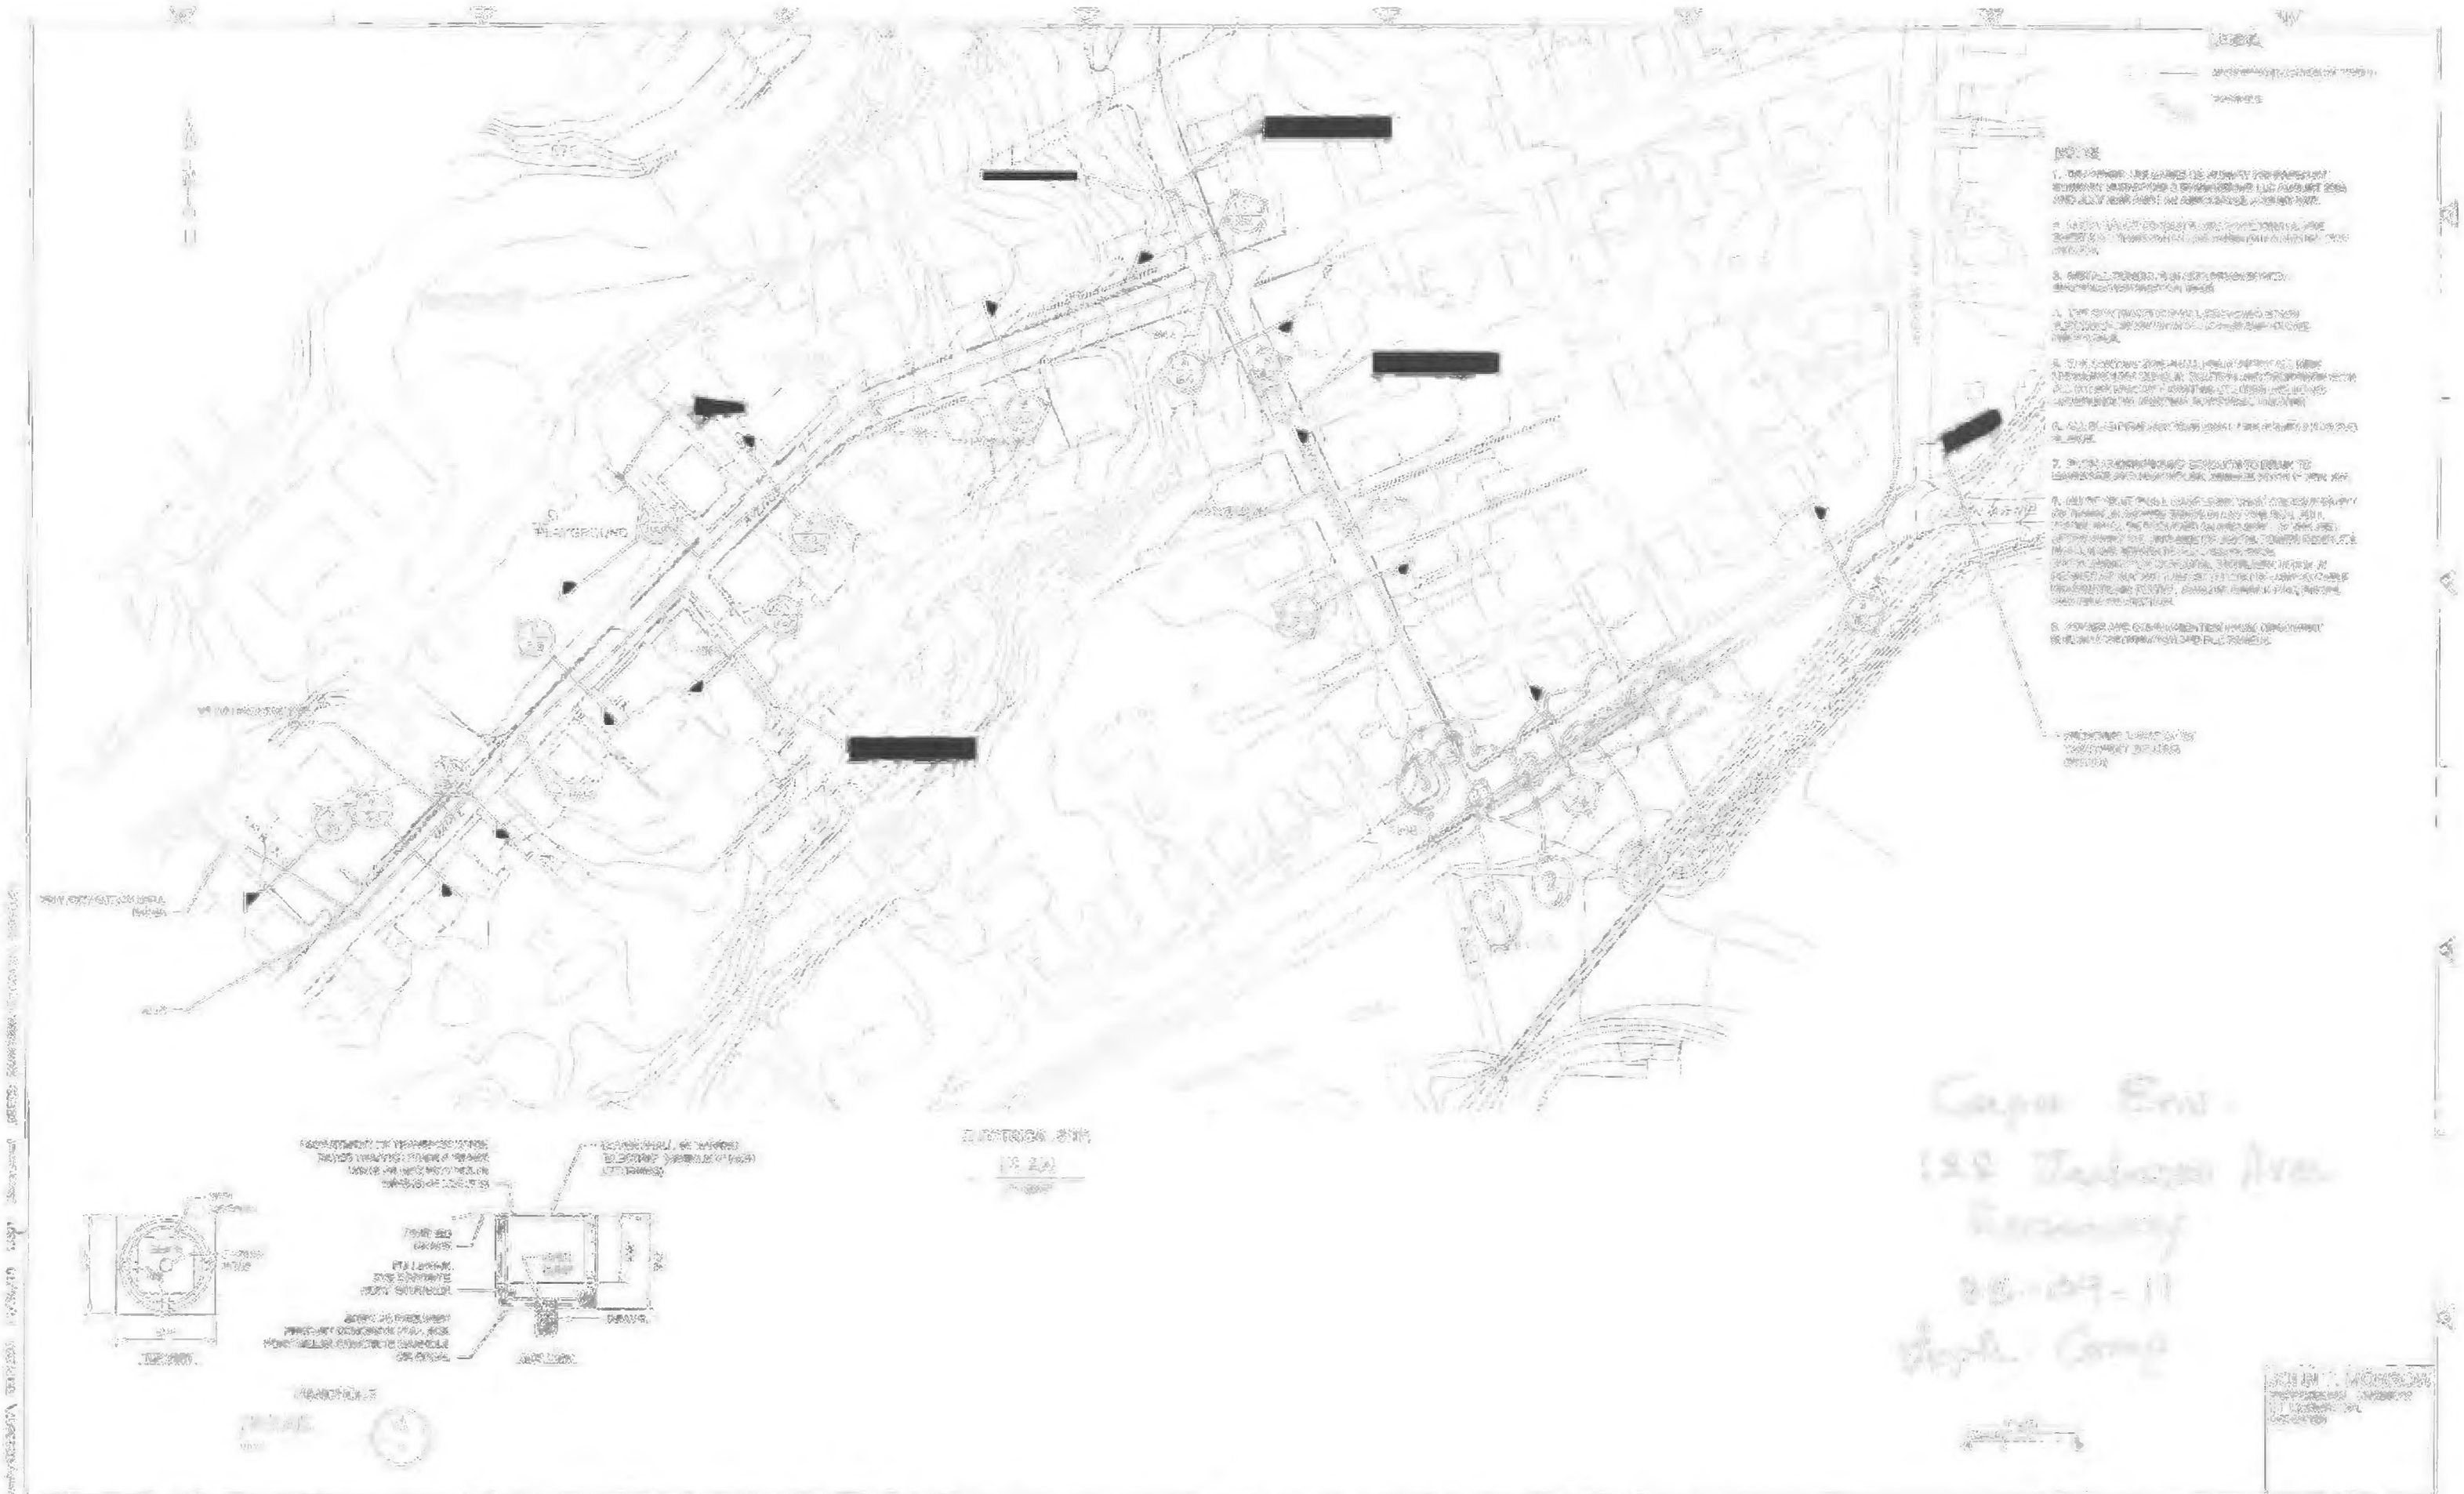
ELECTRICAL SITE PLAN

ANS CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 510-ATSI
(908) 754-8383
Fax: (908) 754-8633

NJ EDA Approved Testing Laboratory • AASHTO/ASTM Certified • NJ DEP Certified
www.ANSConsultants.net

ASPHALT COMPACTION TEST REPORT

☒ As per ASTM D-2950-91 (Nuclear Density Gauge)

CLIENT :	Cape Environmental Inc. 45 Pine Street, Suite 110 Rockaway, NJ 07866	DATE :	8/10/2011
		FILE NO. :	ANX - 1743
	Attn. Mr. Paul Ferroni	REPORT # :	03
PROJECT :	Rockaway Borough Superfund Site 122 Jackson Avenue Rockaway, NJ	ENGINEER :	Ripen Nagar
		TIME :	7:00 a.m. - 3:30 p.m.

CERTIFICATE OF INSPECTION

As per your request asphalt compaction tests were performed at the above referenced project site on 08/10/2011.

		DENSITY (LB/CU FT)				DENSITY (LB/CU FT)	
TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)	TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)
2" Surface Course (1-5)				8" Base Course (1-2)			
1	*	148.8	94.7	6	*	149.4	94.8
2	*	149.0	94.8	7	*	149.4	94.8
3	*	148.7	94.6	8	*	150.3	95.8
4	*	148.1	94.2	9	*	151.0	95.4
				10	*	152.8	96.9
TROXLER # 29 DS1: OF 35-4557 DS2: OF MS-1674							

Remarks :

1. A Marshall number of 152.4 lb/ft³ and A of Rice number 158.0 lb/ft³ was provided by the Client. A Rice number of 158.0 lb/ft³ was utilized for test # 1 to 5. (Surface course).

2. A Marshall number of 154.5 lb/ft³ and A of Rice number 159.3 lb/ft³ was provided by the Client. A Rice number of 159.3 lb/ft³ was utilized for test # 6 to 10. (Base course).

   Note: Tests # 1 to 4 were checked on previous day paving of surface course between manhole #1 manhole #2 due to rain.

   Temperature from the trucks were found between 285°F to 350°F for the base course. Thickness of the pavement for base course checked and verified for the entire paved area and found satisfactory.

Location/Elevation : See attached sketch.

Specification Requirements : 92% to 98% of the Rice Density

☒ Complied With : Test # 1 - 10

☐ Not Complied With :

☒ Sliding block covering the source rod was checked before placing the gauge in the storage box.

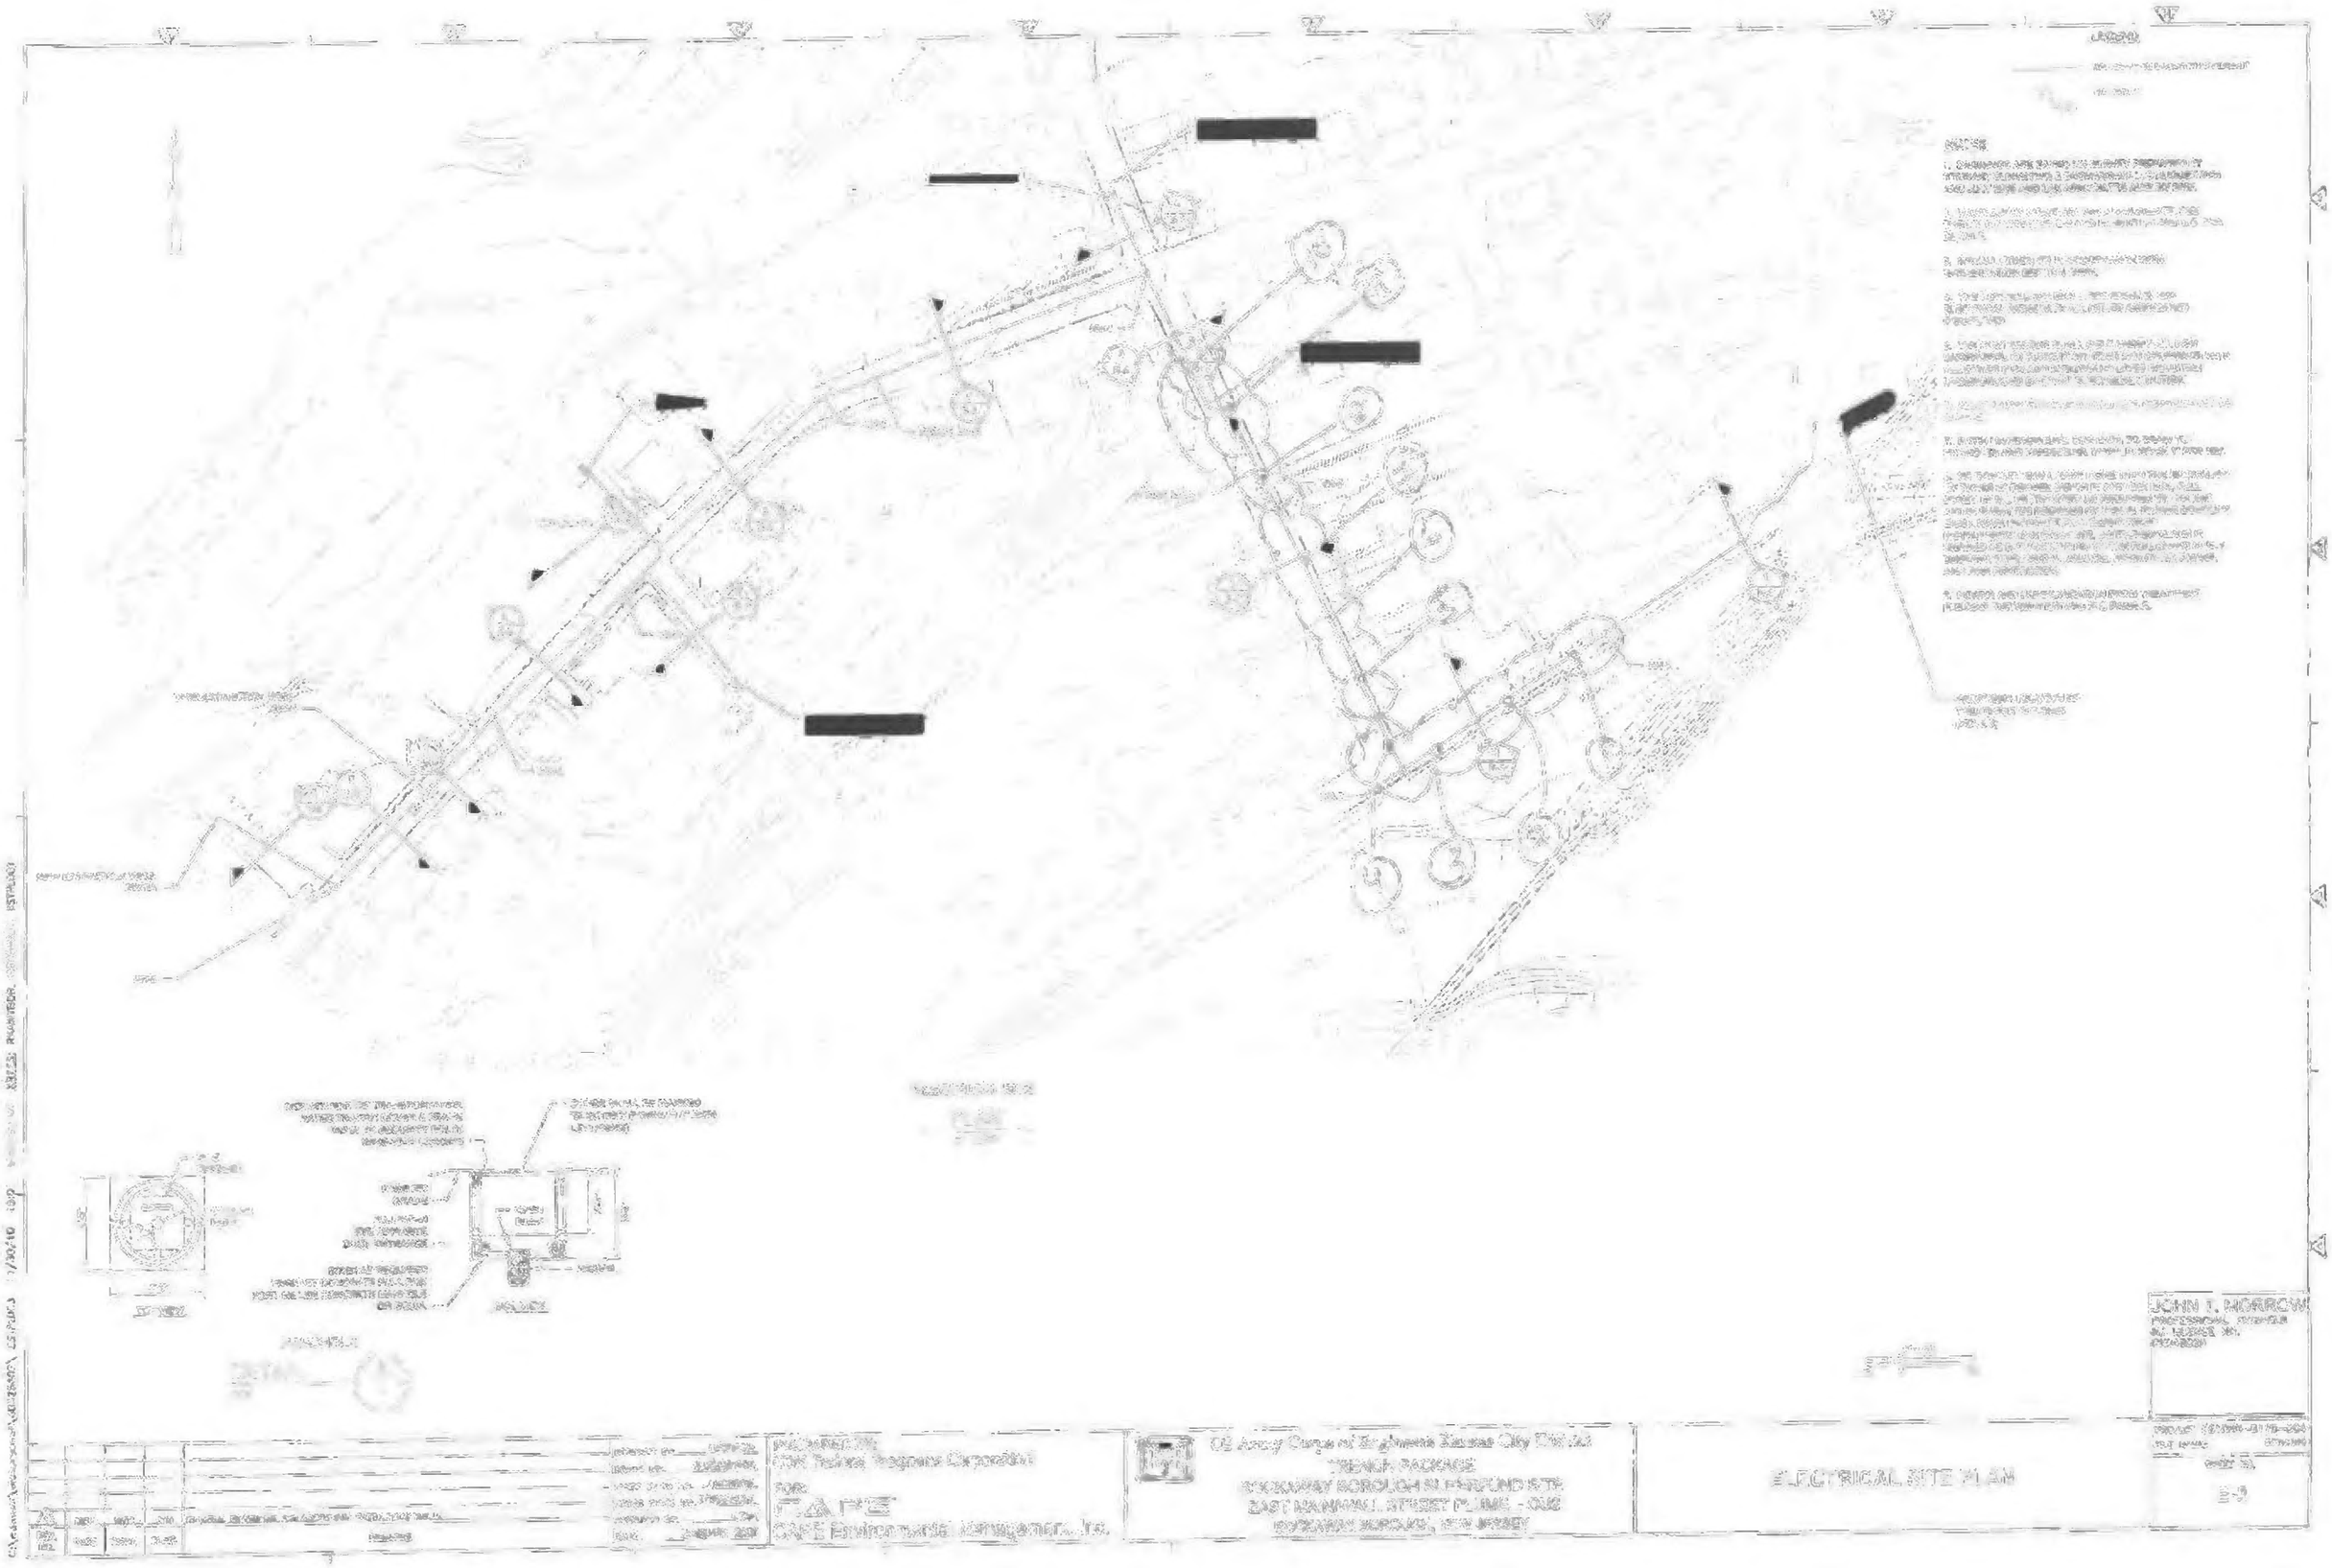
JOHN T. MORROW
US Army Corps of Engineers Kansas City District
TRENCH PACKAGE
ROCKAWAY BOROUGH SUPERFUND SITE
EAST MANNHALL STREET PLUME - OU2
ROCKAWAY BOROUGH, NEW JERSEY
ELECTRICAL SITE PLAN
E-3
PROPERTY OF:
FOR:
FAPE
CAPE Environmental Management, Inc.

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ACTL
(908) 754-8353
Fax: (908) 754-8613

NJ EDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.AnsConsultants.net

Air Pollution Testing, Stack Testing, Source Test, Emissions Test, Field Test, Stack Sampling, Source Sampling, Testing, Building Pressurization Testing, USP 797 Testing, Environmental Testing Services

ASPHALT COMPACTION TEST REPORT

☒ As per ASTM D-2950-91 (Nuclear Density Gauge)

CLIENT : Cape Environmental Inc.
45 Pine Street, Suite 110
Rockaway, NJ 07866

Attn. Mr. Paul Perroni

DATE : 8/10/2011

FILE NO. : ANX - 1743

REPORT # : 03

PROJECT : Rockaway Borough Superfund Site
122 Jackson Avenue
Rockaway, NJ

ENGINEER : Ripan Nagar

TIME : 7:00 a.m. - 2:00 p.m.

CERTIFICATE OF INSPECTION

As per your request asphalt compaction tests were performed at the above referenced project site on 08/10/2011.

	*1	DENSITY (LB/CU FT)			*1	DENSITY (LB/CU FT)	
TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)	TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)
2" Surface Course (1-5)				3" Base Course (1-2)			
1	-	[illegible]	[illegible]	6	-	155.8	[illegible]
2	-	[illegible]	[illegible]	7	-	[illegible]	[illegible]
3	-	[illegible]	[illegible]	8	-	160.4	[illegible]
4	-	[illegible]	[illegible]	9	-	[illegible]	[illegible]
				10	-	153.8	[illegible]
				11	-	152.8	[illegible]
TRUCK NO. #28 WT. OF DS-6857 DEP. OF MS-1874							

Remarks :

1. A Marshall number of 152.4 lb/ft³ and A of Rice number 158.3 lb/ft³ was provided by the Client. A Rice number of 158.3 lb/ft³ was utilized for tests # 1 to 5. (Surface course).

2. A Marshall number of 151.5 lb/ft³ and A of Rice number 158.5 lb/ft³ was provided by the Client. A Rice number of 158.5 lb/ft³ was utilized for tests # 6 to 10. (Base course).

   Note: Test # 1 is a were checked on previous day paving of surface course between manhole - 1 manhole 4 due to rain.

   Temperature for the mixes were found between 285°F to 305°F for the base course. Thickness of the pavement for base courses checked and verified for the entire paved area and found satisfactory.

Location/Elevation : See attached sketch.

Specification Requirements : 92% to 98% of the Rice Density.

☒ Complied With : Test # 1 - 10

☐ Not Complied With :

☒ Sliding block covering the source rod was checked before placing the gauge in the storage box.

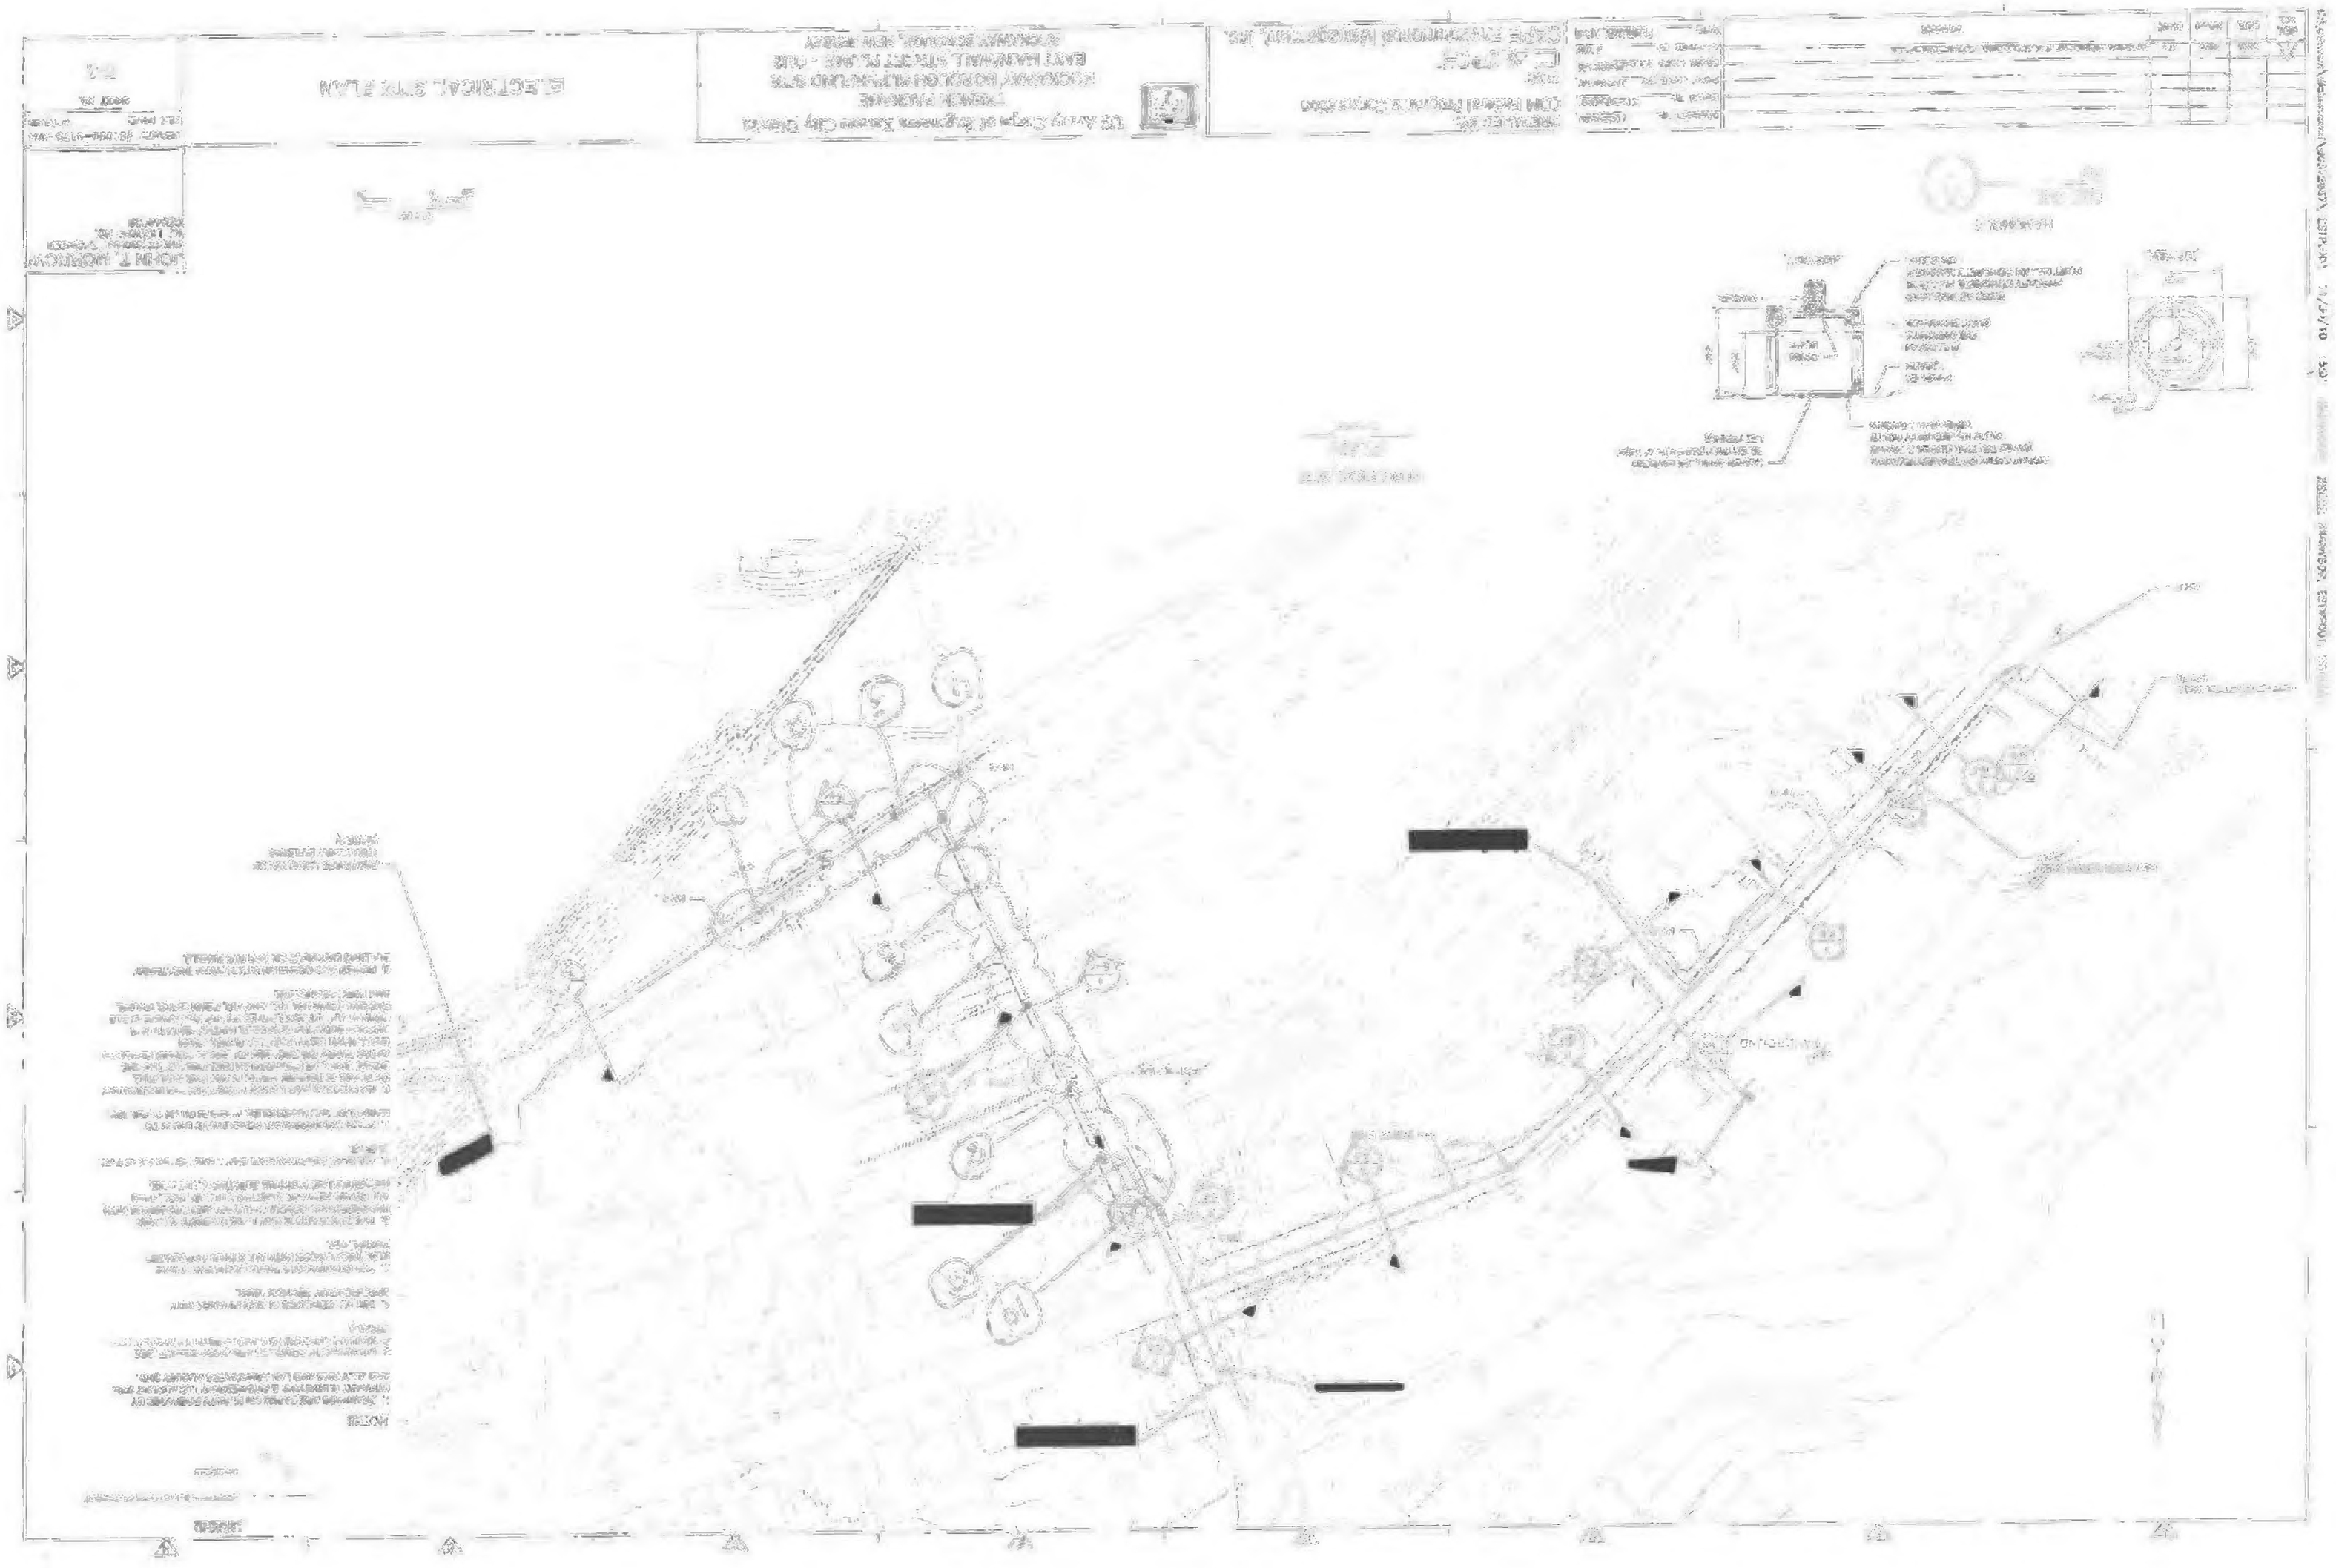

CONSULTANTS, INC.
4485 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATUL
(908) 754-8383
Fax: (908) 754-8533

NJ EDA Approved Testing Laboratory * AASHTOBE Certified * NJ DEP Certified
www.ANSconsultants.com

Soil Density, Moisture, Sieve, Atterberg Limits, Sand Cone, Plate, Proctor, Sieve Analysis, Reporting, Testing, Technical Consultation, Quality Assurance, Environmental Testing & Design

ASPHALT COMPACTION TEST REPORT

☒ As per ASTM D-2950-91 (Nuclear Density Gauge)

CLIENT : Cape Environmental Inc.
45 Pine Street, Suite 113
Rockaway, NJ 07866

Attn. Mr. Paul Petroni

PROJECT : Rockaway Borough Superfund Site
122 Jackson Avenue
Rockaway, NJ

DATE : 8/10/2011

FILE NO. : ANX - 1743

REPORT # : 03

ENGINEER : Hiren Nagar

TIME : 7:00 a.m. - 3:30 p.m.

CERTIFICATE OF INSPECTION

As per your request asphalt compaction tests were performed at the above referenced project site on 08/10/2011.

	%	DENSITY (LB/CU FT)			%	DENSITY (LB/CU FT)	
TEST NO.	LOCATION ELEVATION	FIELD	COMPACTION (%)	TEST NO.	LOCATION ELEVATION	FIELD	COMPACTION (%)
2" Surface Course (1-3)				3" Base Course (1-2)			
1	-	149.8	94.7	5	-	148.9	93.4
2	-	149.5	94.5	6	-	148.4	93.0
3	-	148.7	93.9	7	-	152.8	95.8
4	-	149.1	94.2	8	-	151.2	94.8
				9	-	150.9	95.0
				10	-	152.6	95.9
TROXLER # 25 DS1 OF 26 -4657 DS2 OF MS -1874							

Remarks :

1 A Marshall number of 152.4 lb./ft.³ and A of Rice number 155.6 lb./ft.³ was provided by the Client. A Rice number of "93.0 lb./ft.³ was utilized for test # 1 to4. (Surface course).

2 A Marshall number of 154.6 lb./ft.³ and A of Rice number 158.3 lb./ft.³ was provided by the Client. A Rice number of "152.3 lb./ft.³ was utilized for test # 5 to 10. (Base course).

Note: Test # 1 to 4 were checked on previous day paving of surface course between manhole - 1 manhole - 2 due to rain.

Temperature from the trucks were found between 260°F to 330°F for the base course. Thickness of the pavement for base courses checked and verified for the entire paved area and found satisfactory.

Location/Elevation : See attached sketch.

Specification Requirements : 92% to 98% of the Rice Density

☒ Complied With : Test # 1 - 10

☐ Not Complied With :

☒ Sliding block covering the source rod was checked before placing the gauge in the storage box.

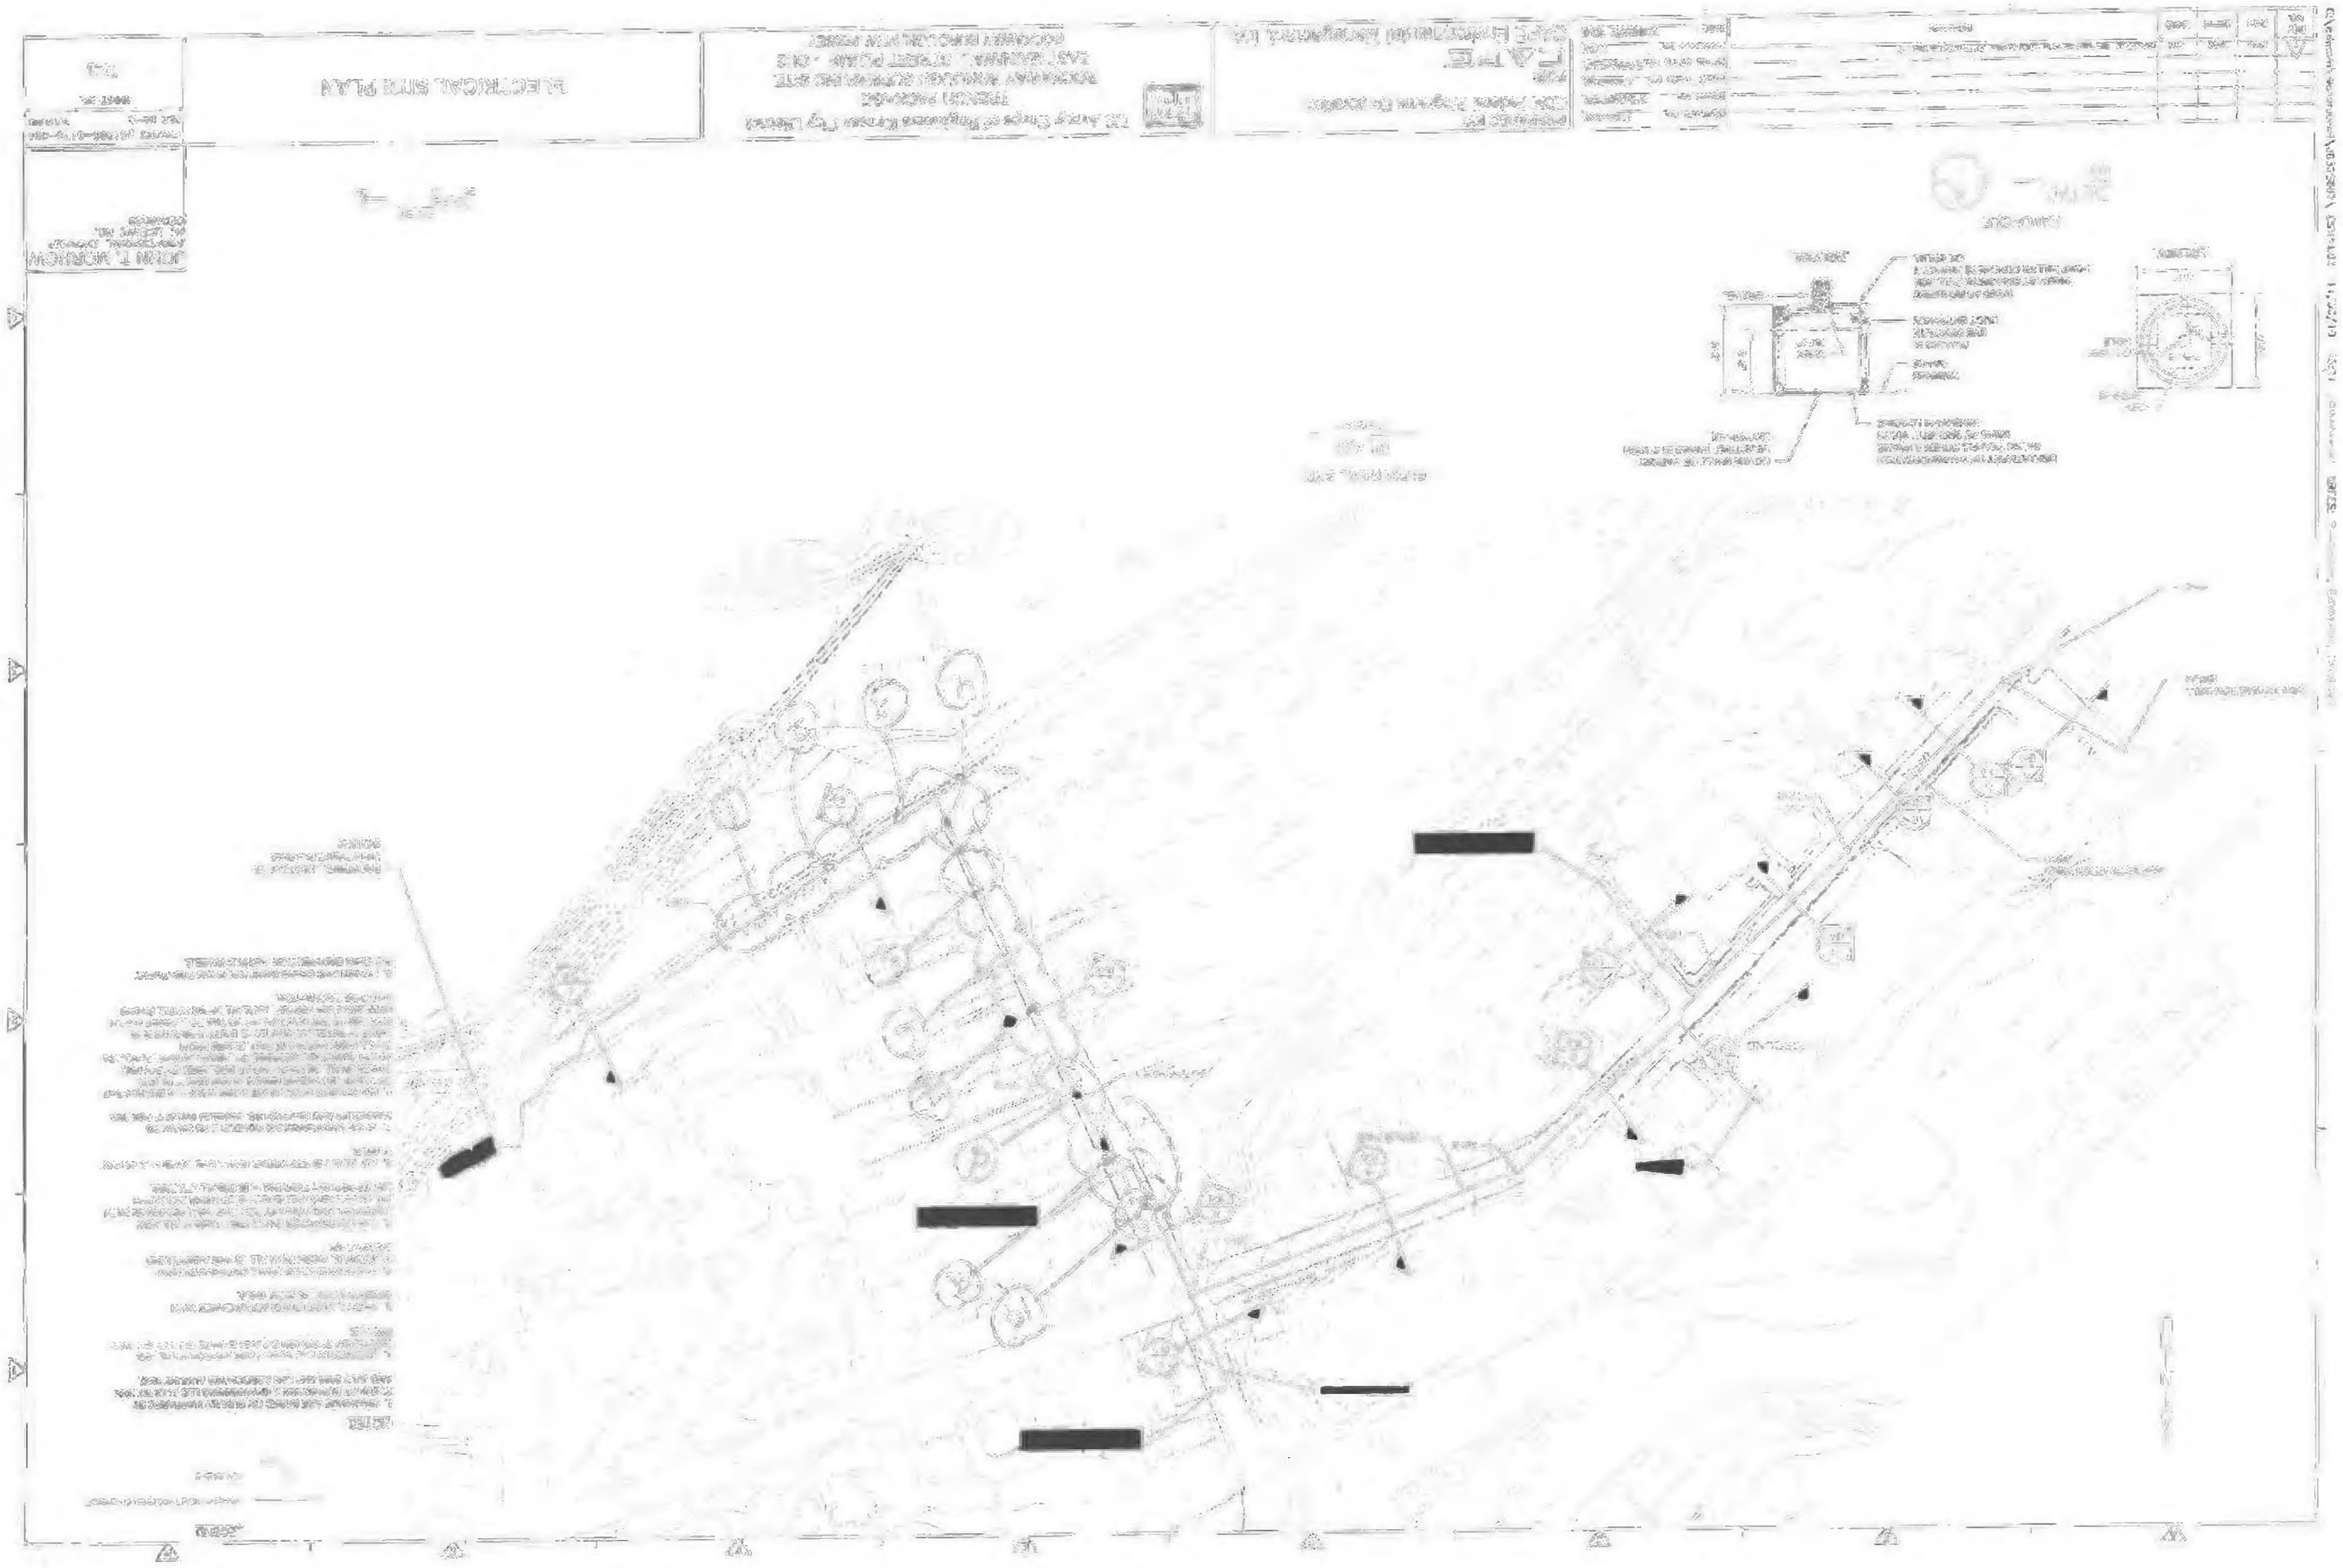

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATUL
(908) 754-8388
Fax: (908) 754-8613

NJDOT Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSconsultants.com

ASPHALT COMPACTION TEST REPORT

☒ As per ASTM D-2950-91 (Nuclear Density Gauge)

CLIENT : Cape Environmental Inc.
38 Pine Street, Suite 110
Rockaway, NJ 07866

Attn. Mr. Paul Ferroni

PROJECT : Rockaway Borough Superfund Site
122 Jackson Avenue
Rockaway, NJ

DATE : 8/11/2011

FILE NO. : ANX - 1748

REPORT # : 04

ENGINEER : Kishor Bari

TIME : 7:00 a.m. - 3:30 p.m.

CERTIFICATE OF INSPECTION

As per your request asphalt compaction tests were performed at the above referenced project site on 08/11/2011.

	*	DENSITY (LB./CU.FT.)			*	DENSITY (LB./CU.FT.)	
TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)	TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)
4.3" Base Course (1-2)				4.3" Base Course (1-2)			
1	-	150.4	94.0	3	-	150.2	93.8
2	-	150.8	94.3	4	-	150.4	94.0
				5	-	150.7	94.2
TROXLER # 5A DST OF 05-2455 DST OF VS-732							

Remarks :

1 A Marshall number of "94.0 lb./ft.³" and A of Rice number "94.5 lb./ft.³" was provided by the Client. A Rice number of "93.3 lb./ft.³" was utilized for test # 1 to 5. (Base Course).

Contractor used material 1 - 5. 1st load Temperature - 294°F, 2nd load - 283°F, 3rd Load - 288°F and 4th load temperature 273°F.

Location/Elevation : See attached sketch.

Specification Requirements : 92% to 98% of the Rice Density.

☒ Complied With : Test # 1 - 5

☐ Not Complied With :

☒ Sliding block covering the source rod was checked before placing the gauge in the storage box.

copy to: Lemus (NJ, Tex.)

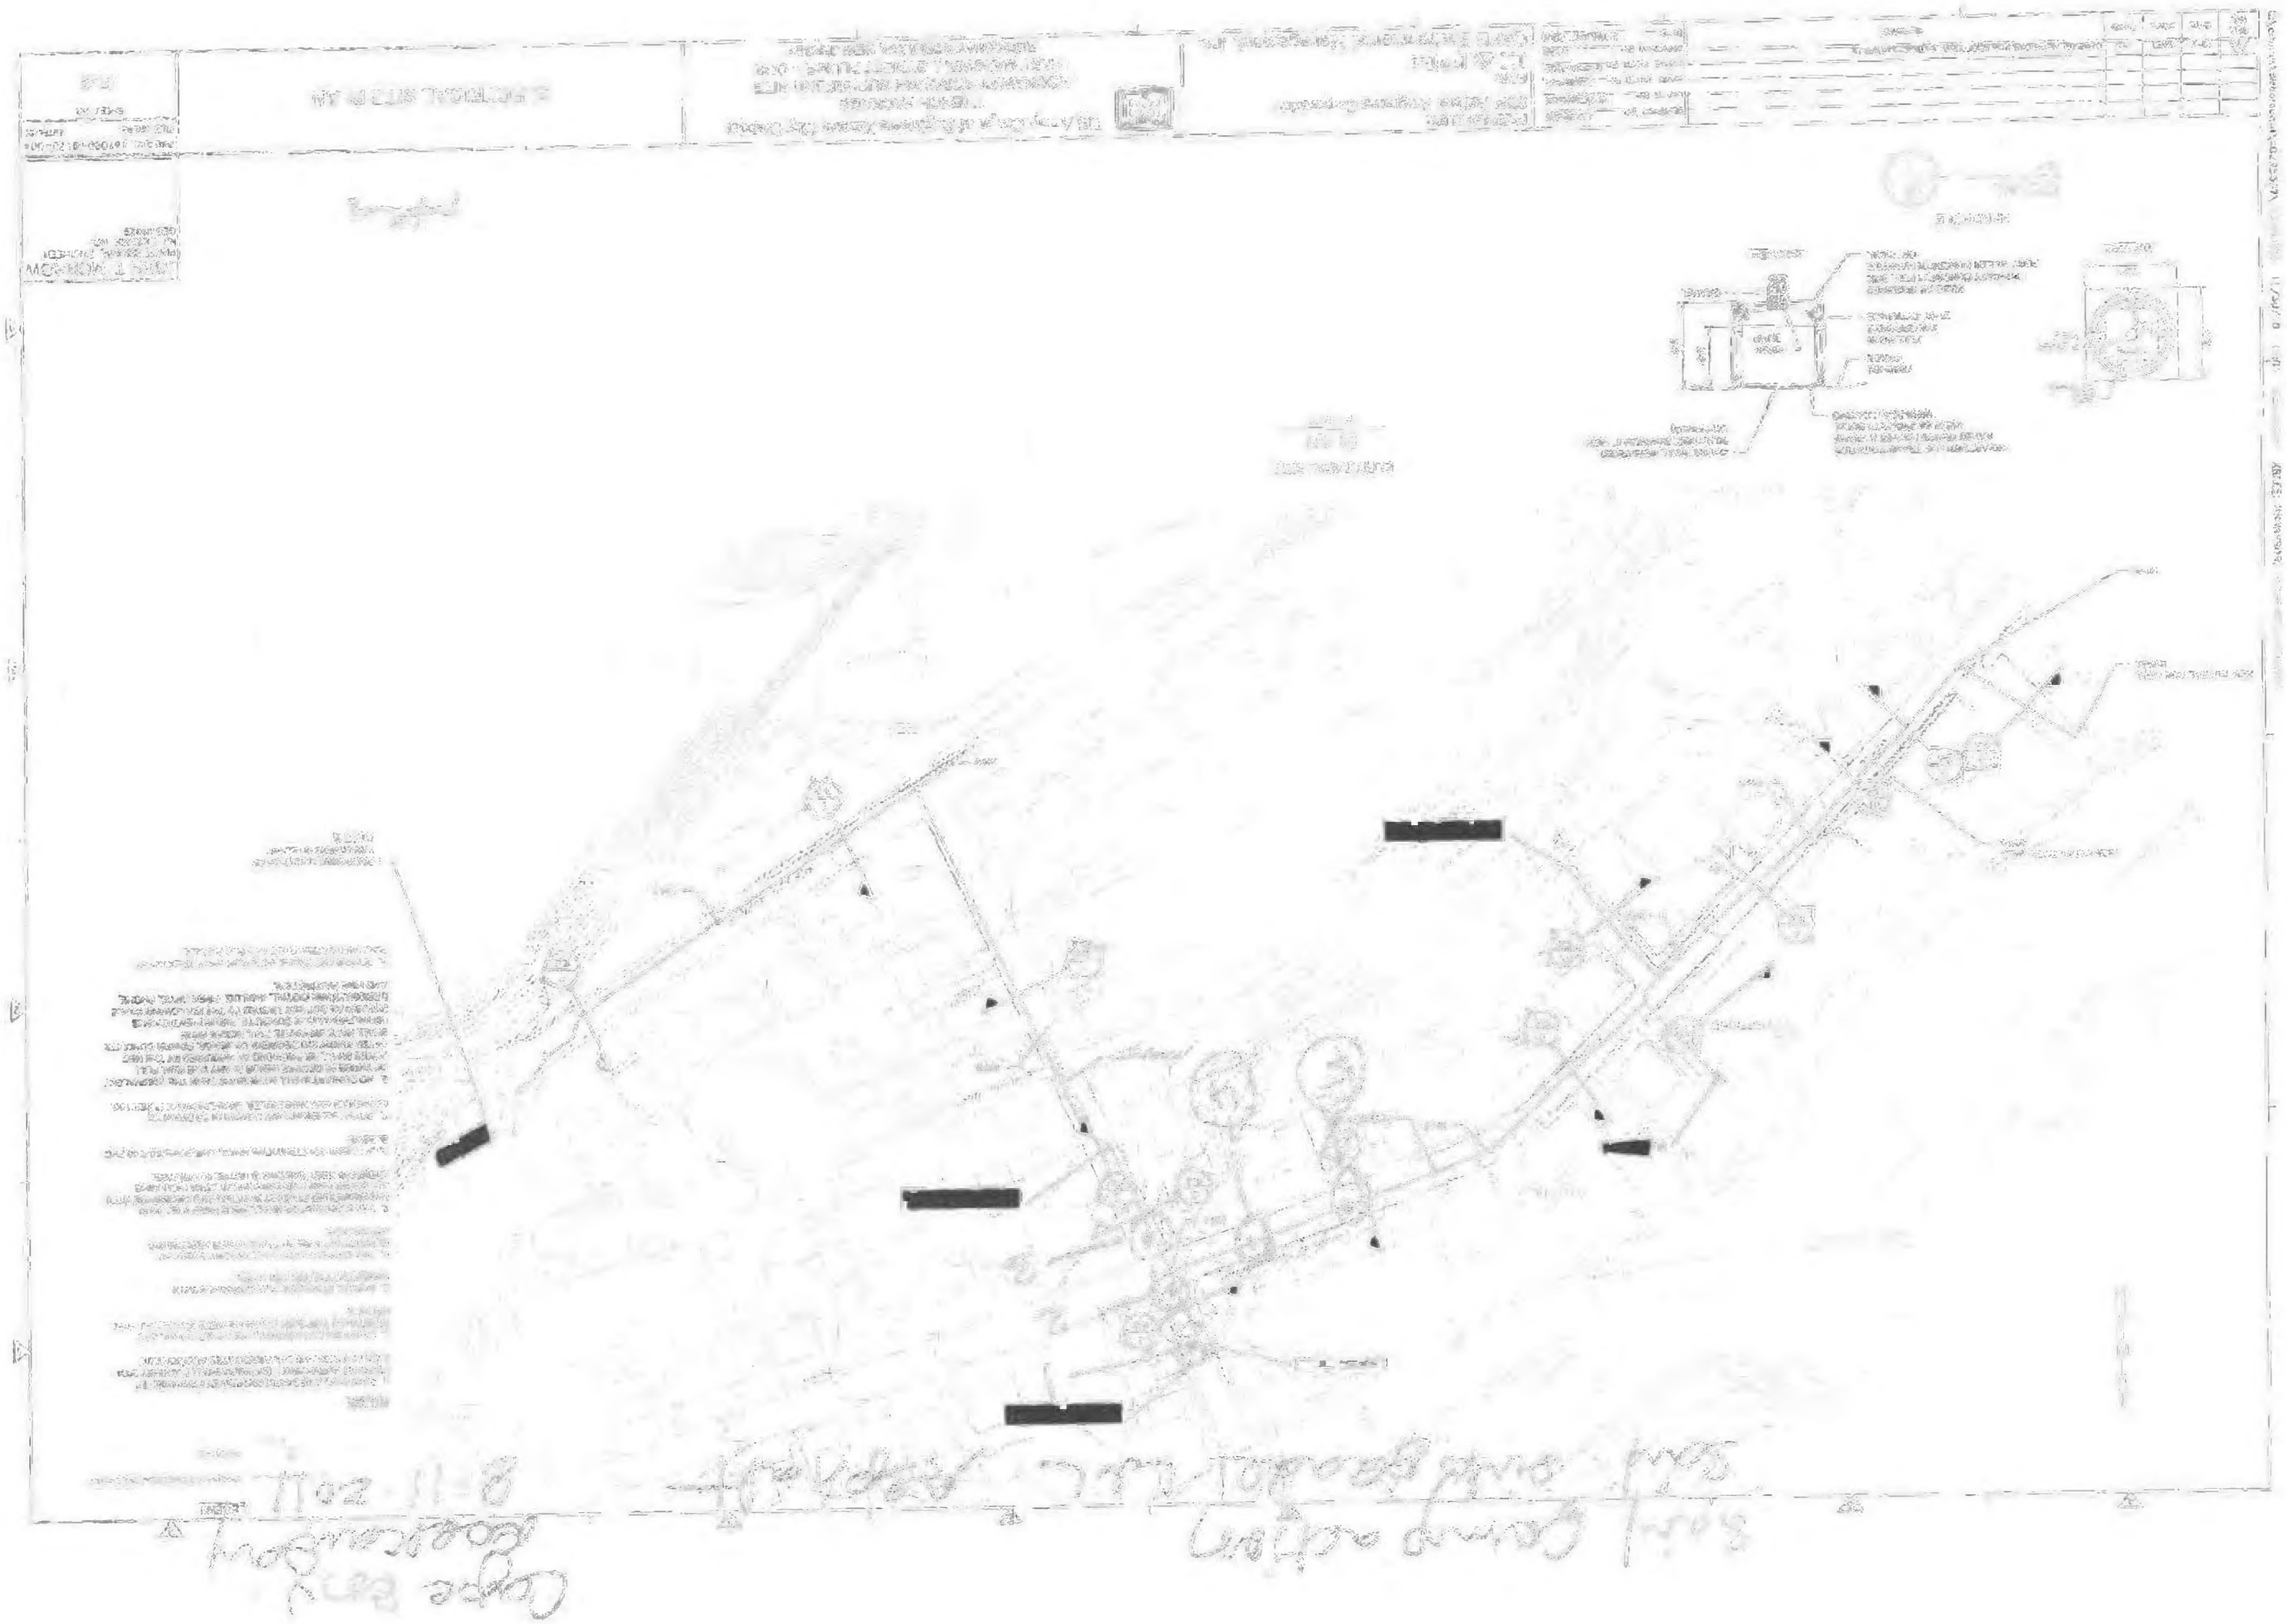

CONSULTANTS, INC.
4405 Sandy Center Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATLI
(908) 754-8361
Fax: (908) 754-8633

NJ EDA Approved Testing Laboratory • AASHTO Certified • NJ DEP Certified
www.ANSconsultants.net

ASPHALT COMPACTION TEST REPORT

☒ As per ASTM D-2950-91 (Nuclear Density Gauge)

CLIENT :	Cape Environmental Inc. 48 Pine Street, Suite 110 Rockaway, NJ 07866	DATE :	07/17/2011
		FILE NO. :	ANX - 1743
	Attn. Mr. Paul Ferroni	REPORT # :	04
PROJECT :	Rockaway Borough Superfund Site 122 Jackson Avenue Rockaway, NJ	ENGINEER :	Kishor Soni
		TIME :	7:00 a.m. - 3:30 p.m.

CERTIFICATE OF INSPECTION

As per your request asphalt compaction tests were performed at the above referenced project site on 07/17/2011.

	#	DENSITY (LBS/CU.FT)			#	DENSITY (LBS/CU.FT)	
TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)	TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)
2" Base Course (1-2)				3" Base Course (1-2)			
1	-	150.4	96.7	3	-	150.4	96.7
2	-	150.2	96.0	4	-	150.4	96.7
				5	-	150.1	96.5
TROXLER # 2A EST OF DS 4463 DEC OF MS -732							

Remarks :

1. A Maximum number of 154.6 lb/ft³ and A of Rice number 159.5 lb/ft³ was provided by the Client. A Rice number of 150.5 lb/ft³ was utilized for test # 1 to 5. (Base course).

Contractor used mater#1 - 2. 1st load Temperature - 284°F, 2nd load - 282°F, 3rd Load - 280°F and 4th load temperature 278°F.

Location/Elevation : See attached sketch.

Specification Requirements : 92% to 98% of the Rice Density.

☒ Complied With : Test # 1 - 5

☐ Not Complied With :

☒ Sliding block covering the source rod was checked before placing the gauge in the storage box.

"ANSwer to your construction inspection and testing needs"
In your partnership analysis

Soil compaction
Salt and pepper asphalt

Cape Girardeau
Boundary
2011

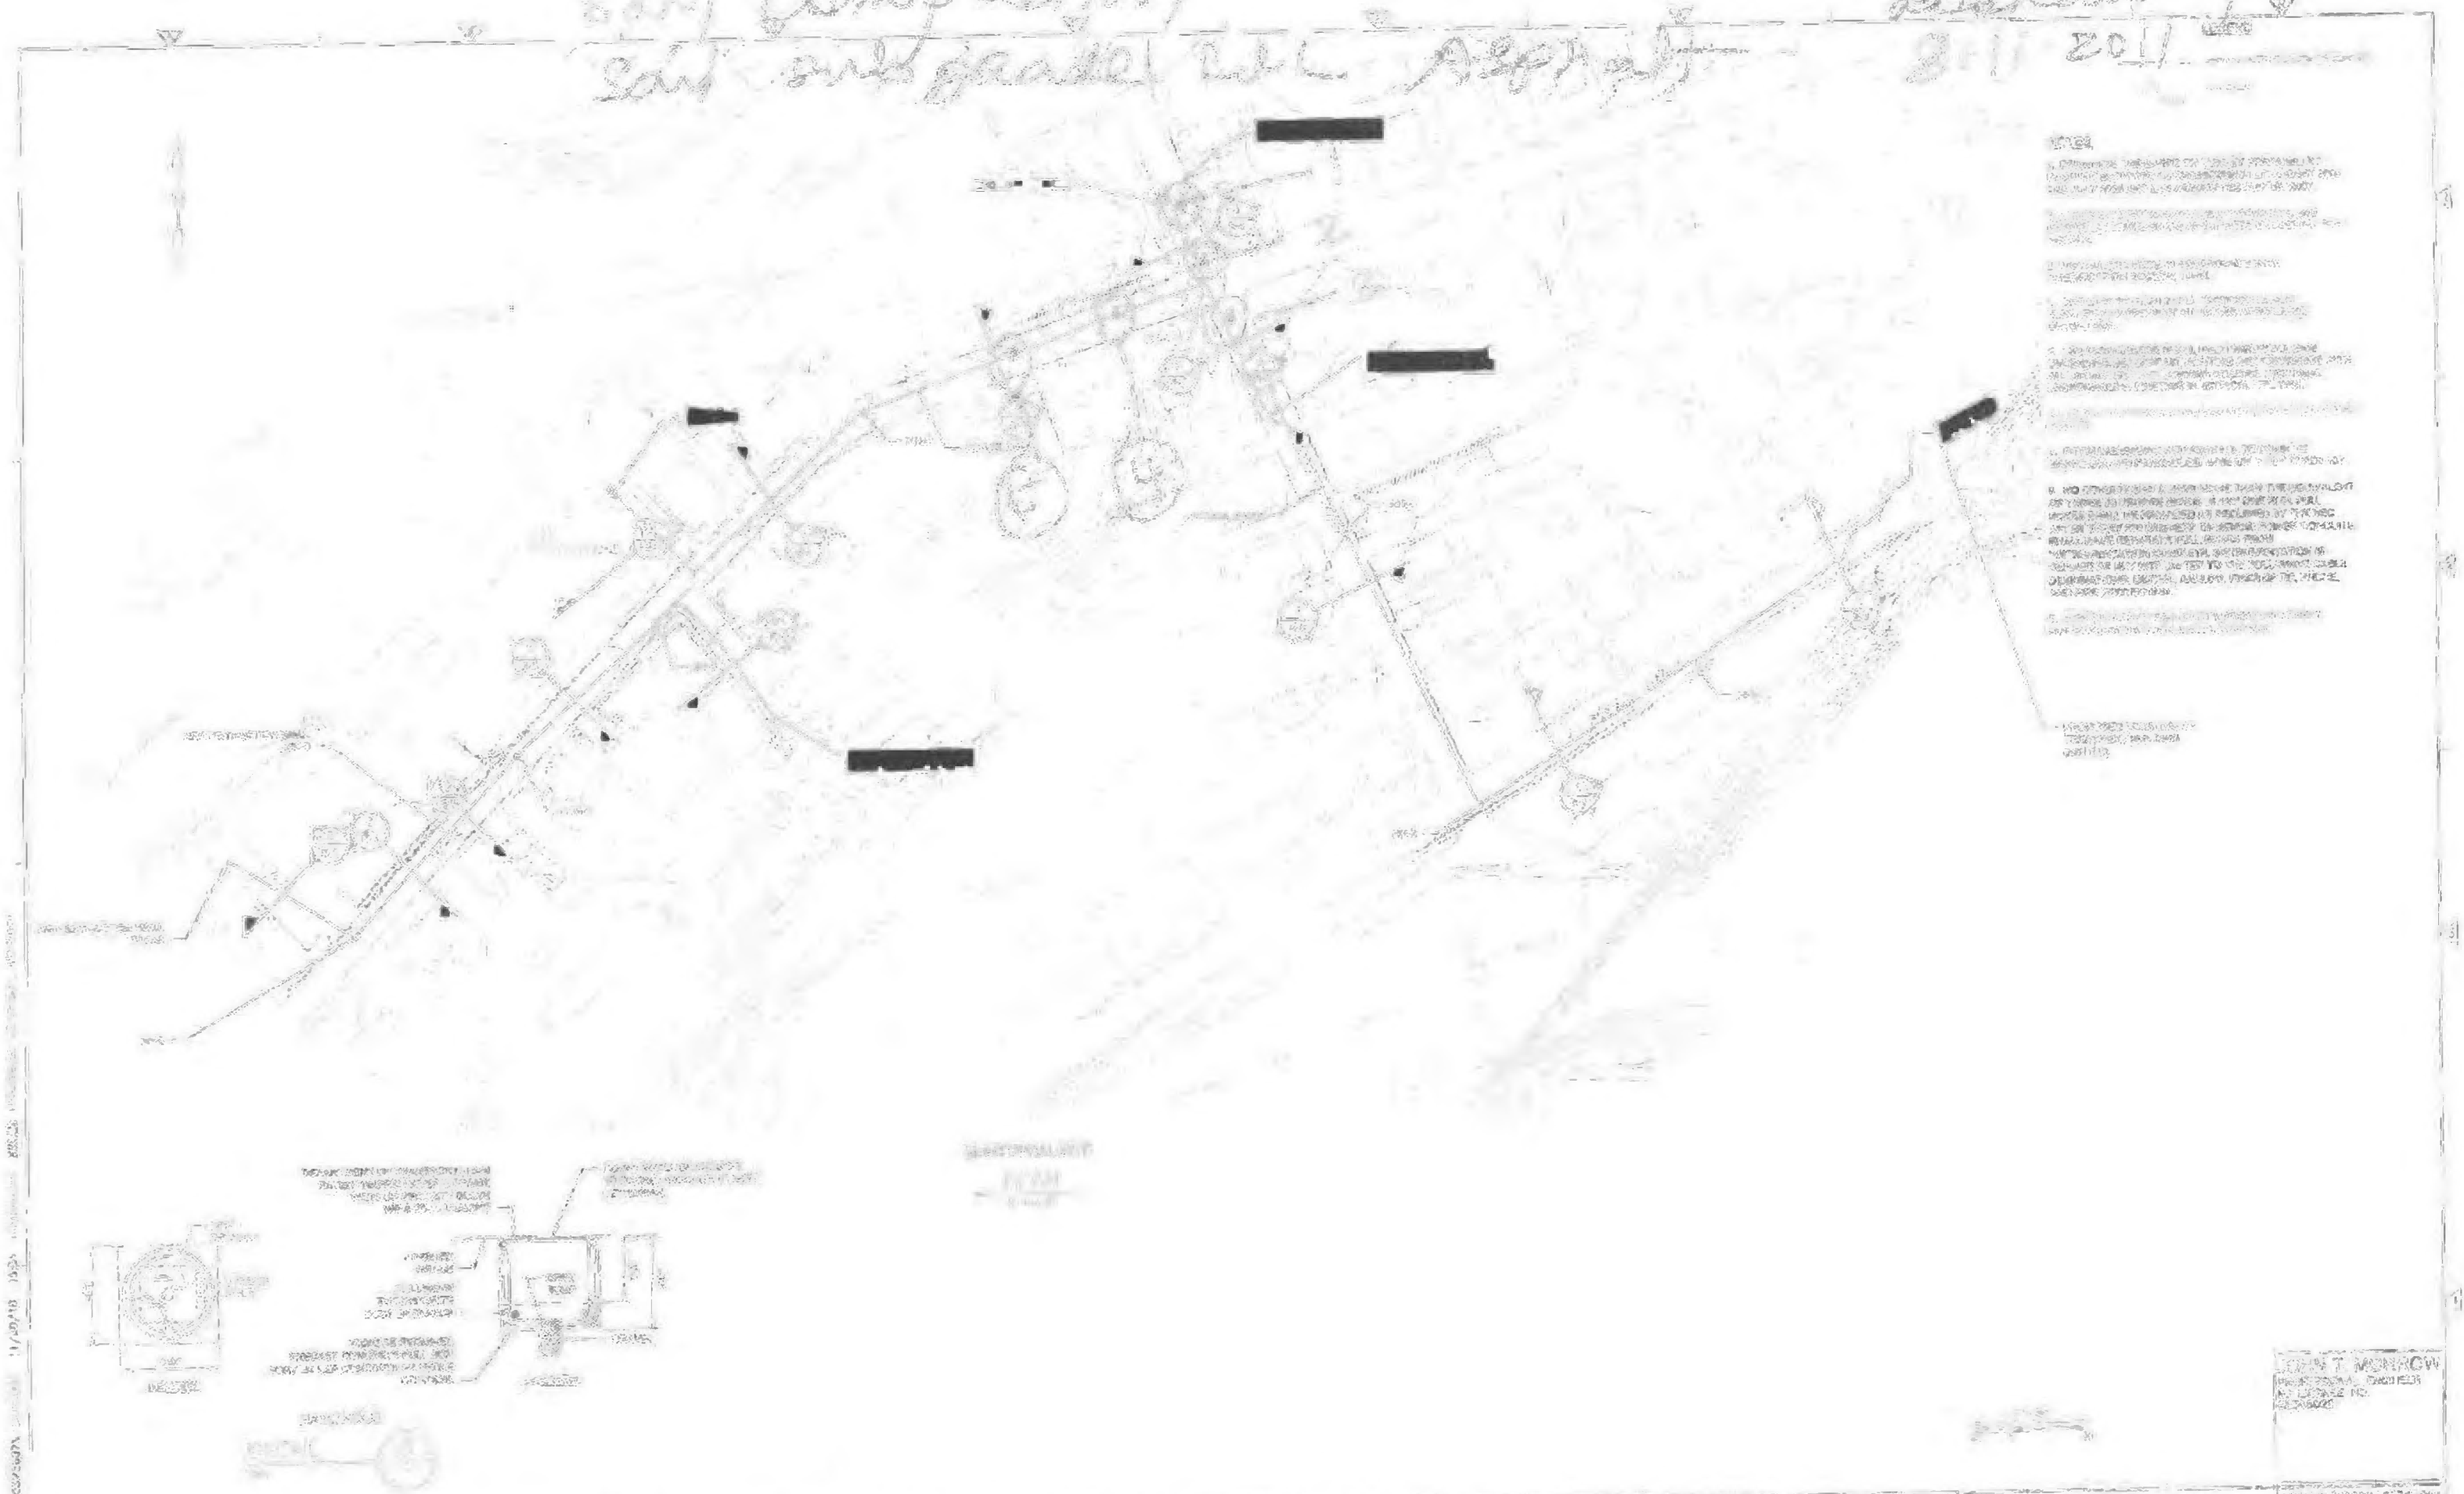

JOHN T. MONROW
PROFESSIONAL ENGINEER
MO LICENSE NO.

PREPARED BY:
Burns & McDonnell Engineering Corporation
FOR:
U.S. ARMY
CORPS OF ENGINEERS, KANSAS CITY, MO

US Army Corps of Engineers Kansas City District
PROJECT TITLE:
FORMERLY USED DEFENSE SITE
FORT LEAVENWORTH, STRIP TRENCH - OU2
LEAVENWORTH COUNTY, KANSAS

ELECTRICAL SITE PLAN

PROJECT DESIGN: 0172-004
FILE NAME:
SHEET NO.
E-1

CONSULTANTS, INC.
4425 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATUL
(908) 754-8383
Fax: (908) 754-8633

NJ EDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSConsultants.com

ASPHALT COMPACTION TEST REPORT

☒ As per ASTM D-2950-91 (Nuclear Density Gauge)

CLIENT : Cape Environmental Inc.
45 Pine Street, Suite 110
Rockaway, NJ 07866

Attn. Mr. Paul Ferron

DATE : 9/11/2001

FILE NO. : ANX - 1743

REPORT # : 04

PROJECT : Rockaway Borough Superfund Site
122 Jackson Avenue
Rockaway, NJ

ENGINEER : Nishar Sod

TIME : 7:00 a.m. - 3:30 p.m.

CERTIFICATE OF INSPECTION

As per your request asphalt compaction tests were performed at the above referenced project site on 09/11/2001.

	#	DENSITY (LB/CU FT)			#	DENSITY (LB/CU FT)	
TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)	TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)
± 3" Base Course (1-2)				± 3" Base Course (1-2)			
1	*	150.4	96.7	3	*	150.8	95.4
2	*	150.3	96.6	4	*	150.4	95.2
				5	*	150.0	94.8
TROXLER # 5A DS1 OF DS -7498 DS2 OF MS -732							

Remarks :

1 A Marshall number of 154.6 lb/ft³ and A of Rice number 156.3 lb/ft³ was provided by the Client. A Rice number of 150.5 lb/ft³ was utilized for test # 1 to 5 (Base course).

Contractor used material 1 - 2. 1st bed Temperature - 280°F, 2nd bed - 285°F, 3rd Load - 280°F and the bed temperature 270°F

Location/Elevation : See attached sketch.

Specification Requirements : 92% to 98% of the Rice Density.

☒ Complied With : Test # 1 - 5

☐ Not Complied With :

☒ Sliding block covering the source rod was checked before placing the gauge in the storage box.

Page 1 of 1 (Form-1)

Soil compaction
soil, subgrade

Cope Boundary
8-11-2011

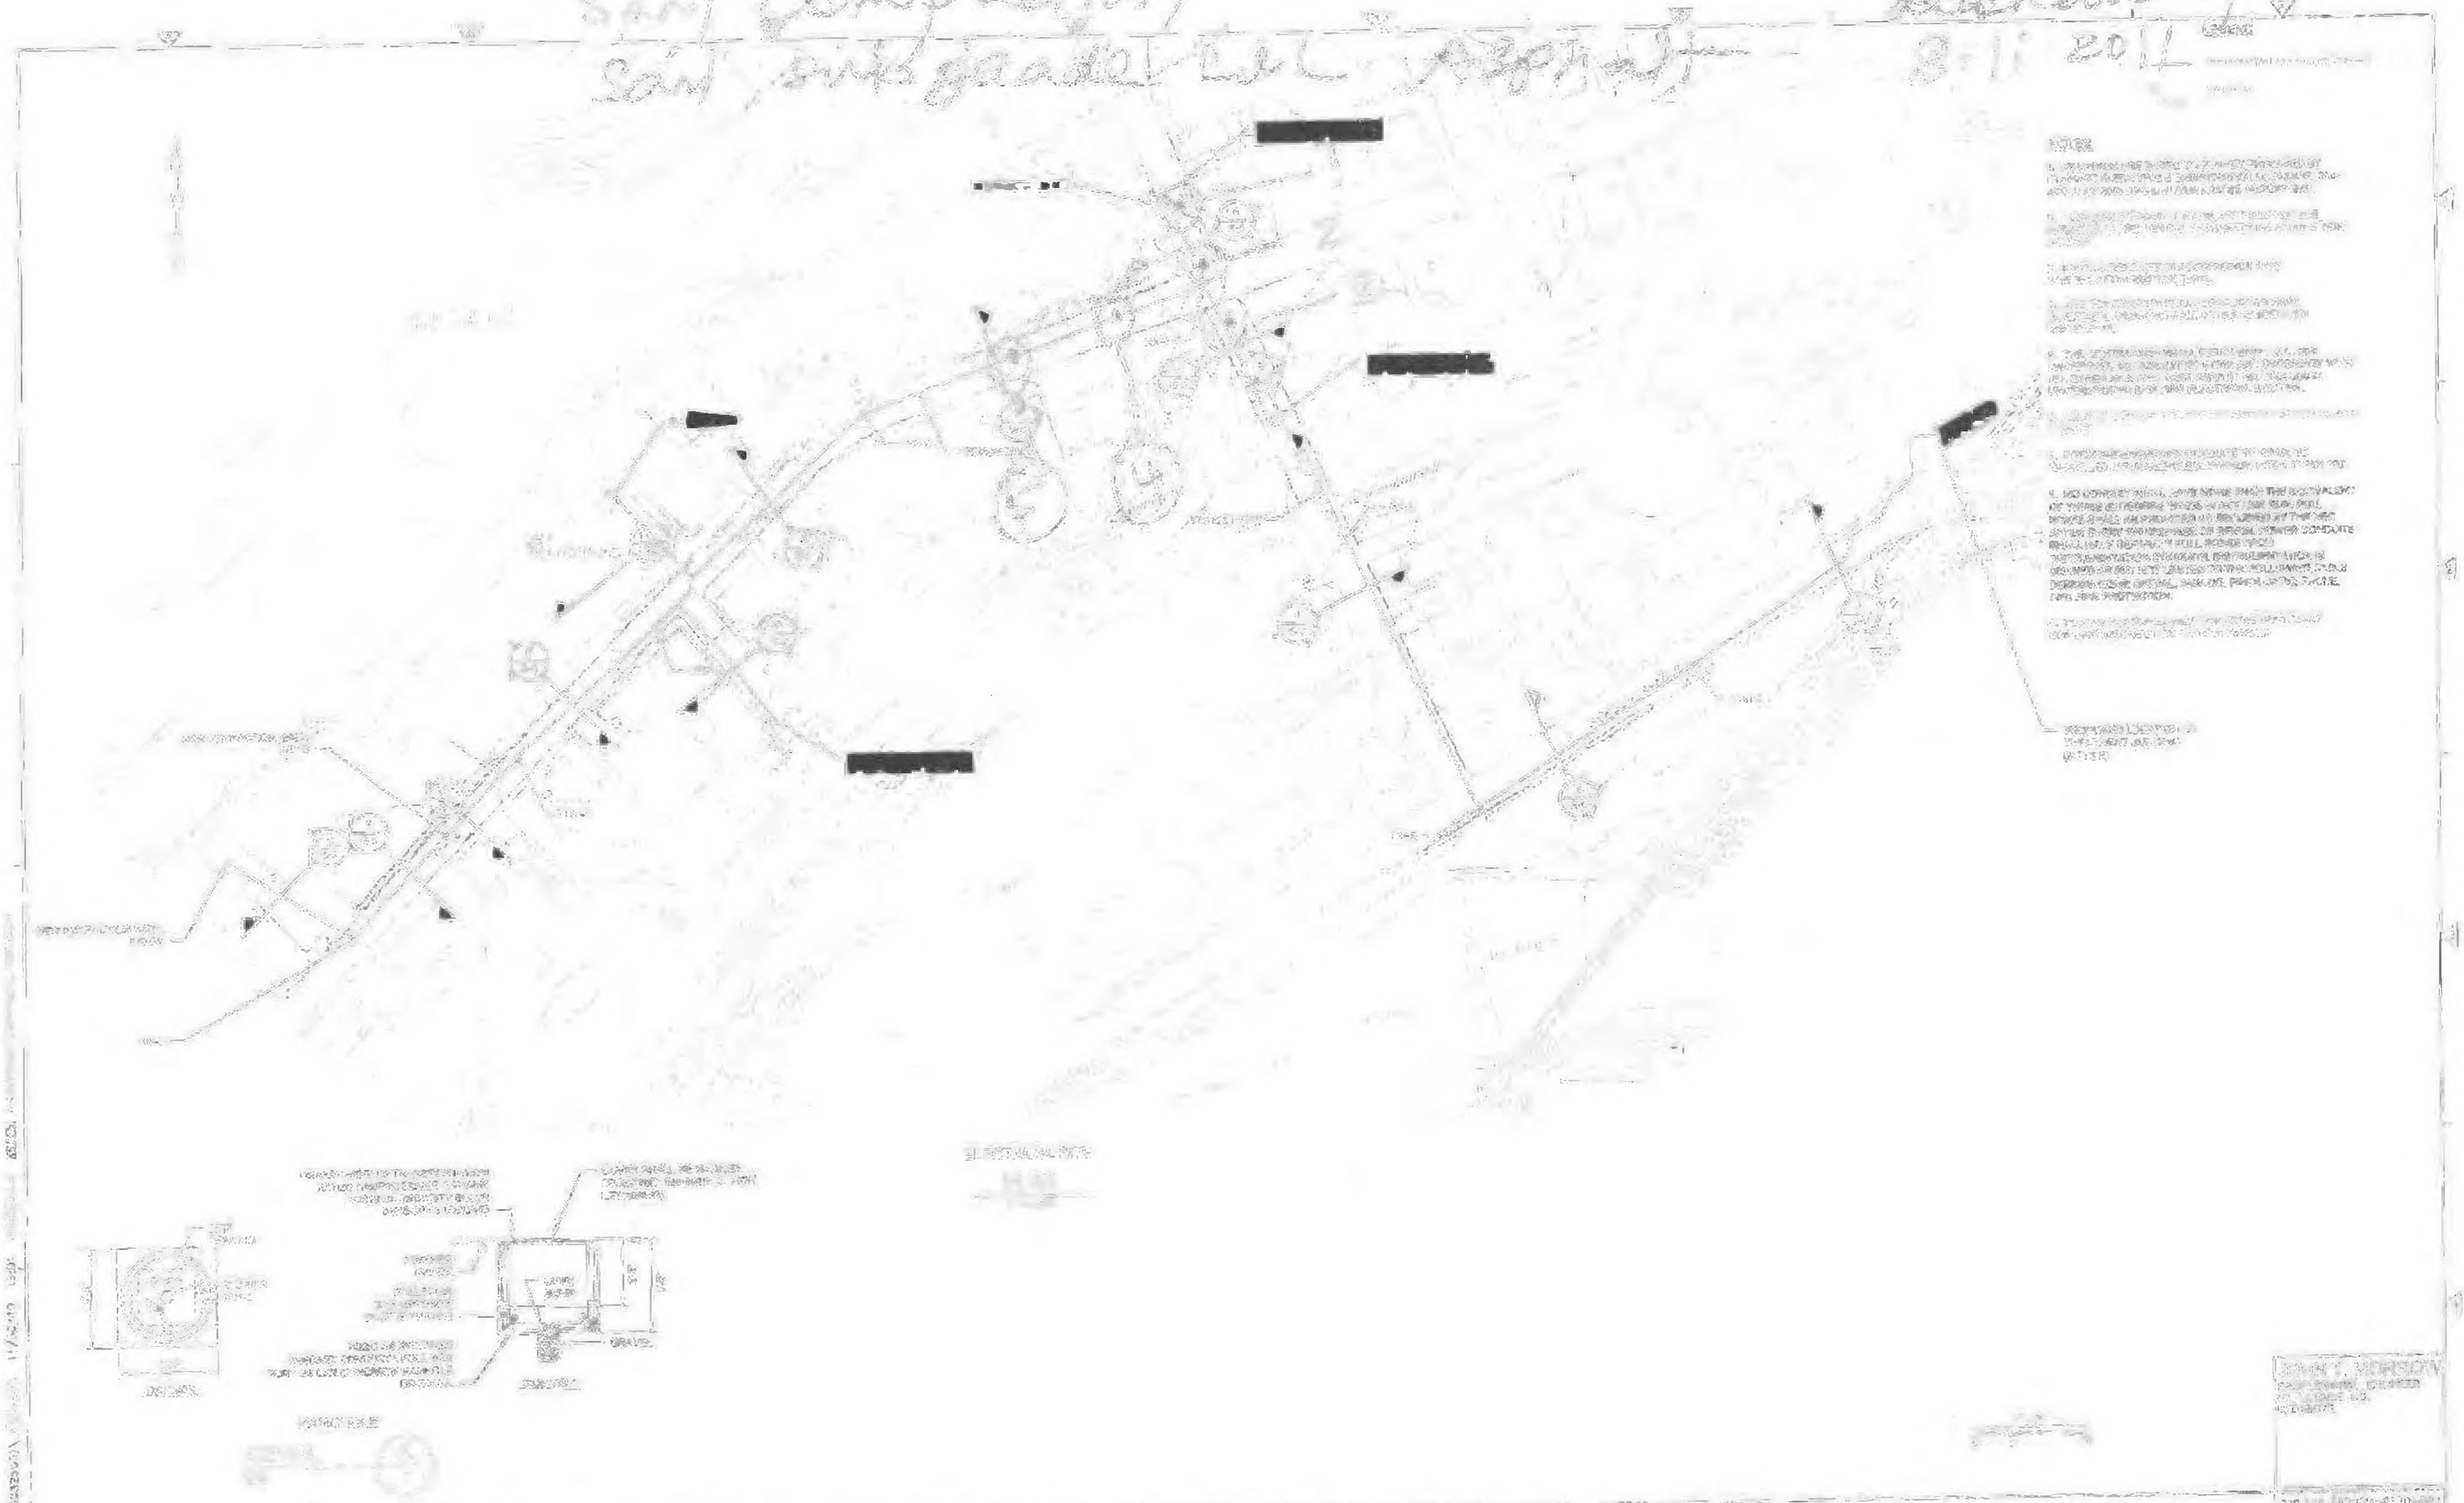

ELECTRICAL SITE PLAN

E-3

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 546-ATUL
(908) 754-8783
Fax: (908) 754-8633

NJ DDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.AnsConsultants.net

ASPHALT COMPACTION TEST REPORT

☒ As per AASHTO-2002-91 (Nuclear Density Gauge)

CLIENT : Cape Environmental Inc.
45 Pine Street, Suite 110
Rockaway, NJ 07866

Attn. Mr. Paul Ferreni

PROJECT : Rockaway Borough Superfund Site
132 Jackson Avenue
Rockaway, NJ

DATE : 8/12/2011

FILE NO. : ANX - 1743

REPORT # : 05

ENGINEER : Ripen Nagar

TIME : 7:00 a.m. - 3:00 p.m.

CERTIFICATE OF INSPECTION

As per your request asphalt compaction tests were performed at the above referenced project site on 08/12/2011.

	*1	DENSITY (LB/CU FT)			*	DENSITY (LB/CU FT)	
TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)	TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)
2" Surface Course				2" Surface Course			
1	*	145.4	93.7	1	*	145.3	94.0
2	*	143.3	94.0	2	*	144.1	93.2
3	*	147.3	95.8	3	*	147.5	95.6
4	*	146.2	94.7	4	*	145.4	94.2
5	*	149.8	95.7	5	*	148.5	94.9
6		142.5	92.3	6	*	144.8	93.1
TROXLER # 25 DS1 OF DS -3806 DS2 OF MS -1869							

Remarks :

1 A Marshall number of 151.1 lb/ft³ and A of Rice number 157.3lb/ft³ was provided by the Client.
A Rice number of 157.3lb/ft³ was utilized for test # 1 to 12. (Surface course).

Rice # was utilized to verify compaction requirements. 2" thick surface course placed over entire area.
Temperature from the truck for HMA was encountered between 286°F to 305°F.

Location/Elevation : Test were taken over 2" thick I-5 surface course over electrical conduits and around well vault. (See attached sketch).

Specification Requirements : 92% to 98% of the Rice Density.

☒ Complied With : Test # 1 - 12

☐ Not Complied With :

☒ Sliding block covering the source rod was checked before placing the gauge in the storage box.

Report Name/Ph-5 File-1

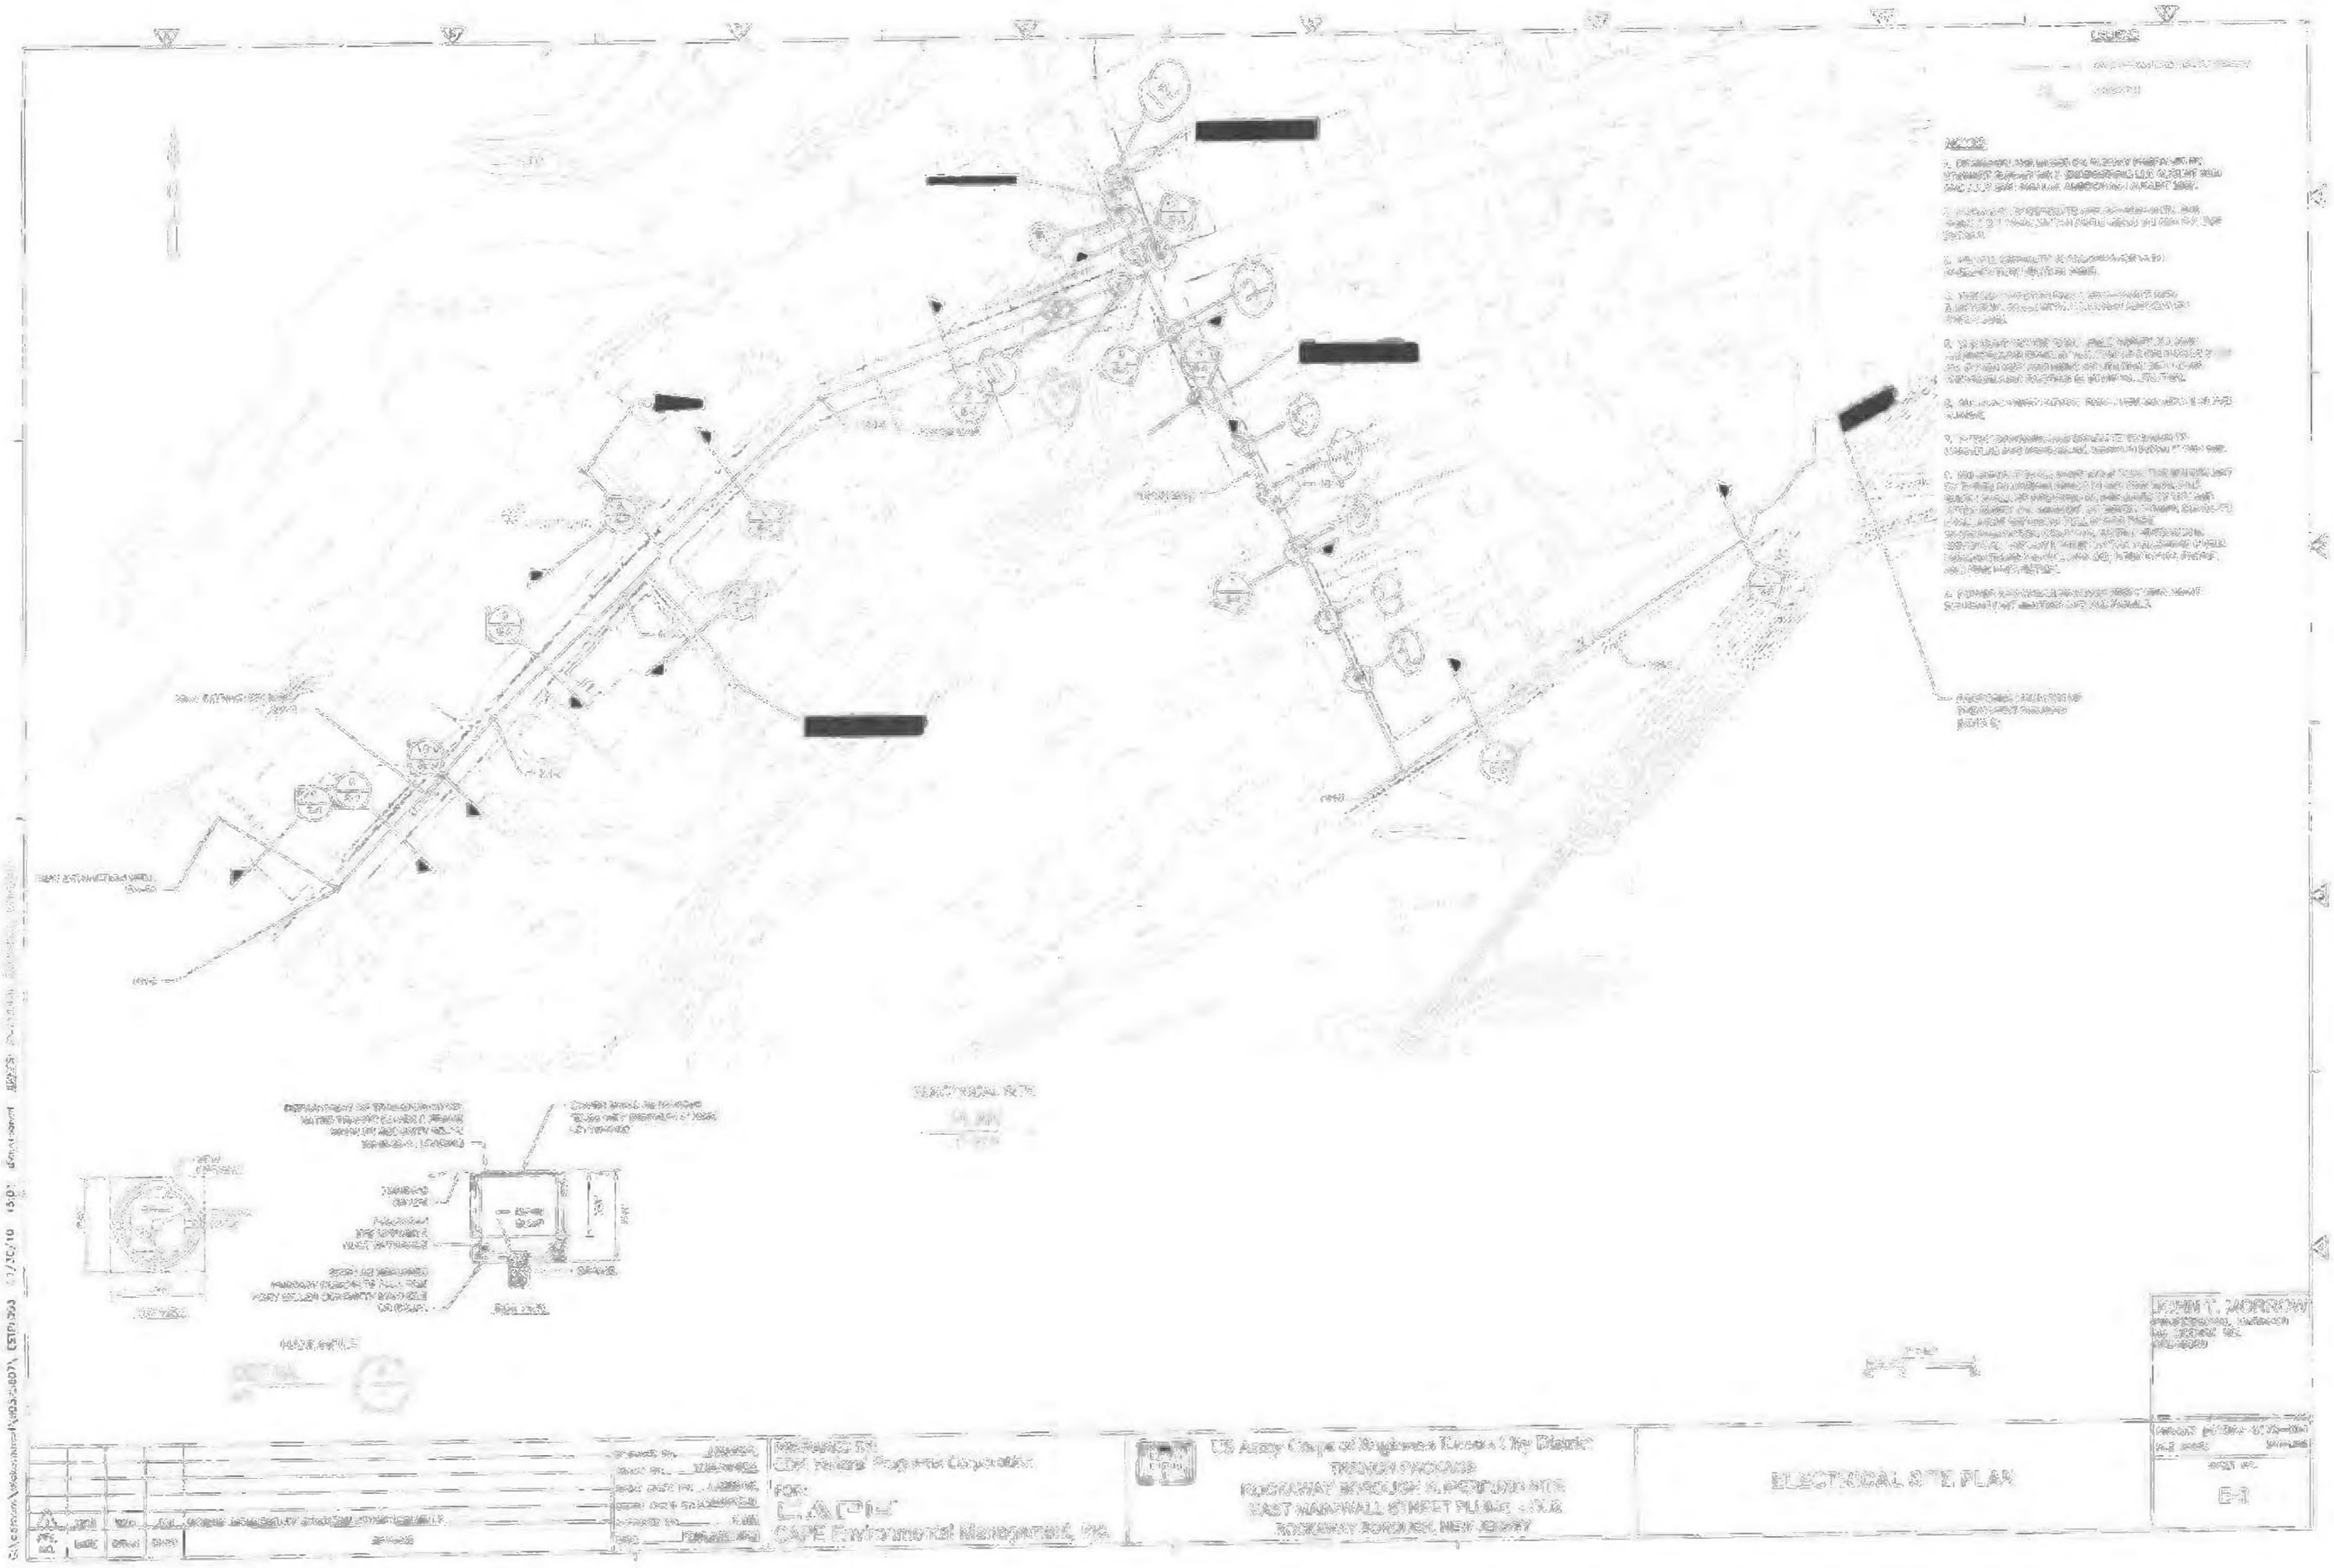
NOTES
ELECTRICAL SITE PLAN
PLAN
MAST ARMS
US Army Corps of Engineers Kansas City District
TRENCH DIVOCARB
ROCKAWAY BOROUGH SUPERFUND SITE
EAST MARSHALL STREET PLUME - OU2
ROCKAWAY BOROUGH, NEW JERSEY
ELECTRICAL SITE PLAN
E-1
PREPARED BY:
CDM Federal Programs Corporation
FOR:
CAPE Environmental Management, Inc.

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 845-ATLJ1
(908) 754-8383
Fax: (908) 754-8633

NJ EDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSConsultants.net

[illegible]

ASPHALT COMPACTION TEST REPORT

☒ As per ASTM D-2950-91 (Nuclear Density Gauge)

CLIENT : Cape Environmental Inc.
48 Pine Street, Suite 110
Rockaway, NJ 07866

Attn. Mr. Paul Ferrari

PROJECT : Rockaway Borough Superfund Site
122 Jackson Avenue
Rockaway, NJ

DATE : 8/12/2011

FILE NO. : ANX - 1743

REPORT # : 06

ENGINEER : Ripon Nagar

TIME : 7:00 a.m. - 3:30 p.m.

CERTIFICATE OF INSPECTION

As per your request asphalt compaction tests were performed at the above referenced project site on 08/12/2011.

	*	DENSITY (LB./CU.FT.)			*	DENSITY (LB./CU.FT.)	
TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)	TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)
2" Surface Course				2" Surface Course			
1	*	145.4	90.7	7	*	149.4	94.0
2	*	145.8	91.0	8	*	152.1	95.3
3	*	147.8	92.2	9	*	150.3	93.8
4	*	149.5	93.7	10	*	149.4	93.2
5	*	149.8	94.7	11	*	148.4	92.6
6	*	146.8	93.3	12	*	144.8	90.1
TROXLER # 25 DS1 OF DS -6868 DS2 OF MS -1853							

Remarks :

* A Marshall number of 154.1 lb./ft.³ and A of Rice number 157.3lb./ft.³ was provided by the Client.
A Rice number of 157.3lb./ft.³ was utilized for tests 1 to 12. (surface course).

Rice # was utilized to verify compaction requirements. 2" thick surface course placed over entire area.
Temperature from the truck for HMA was encountered between 280°F to 300°F.

Location/Elevation : Test were taken over 2" thick S-9 surface course over electrical conduits and around wall vault. (See attached sketch).

Specification Requirements : 92% to 98% of the Rice Density.

☒ Complied With : Test # 1 – 12

☐ Not Complied With :

☒ Sliding block covering the source rod was checked before placing the gauge in the storage box.

Copy to: [illegible]

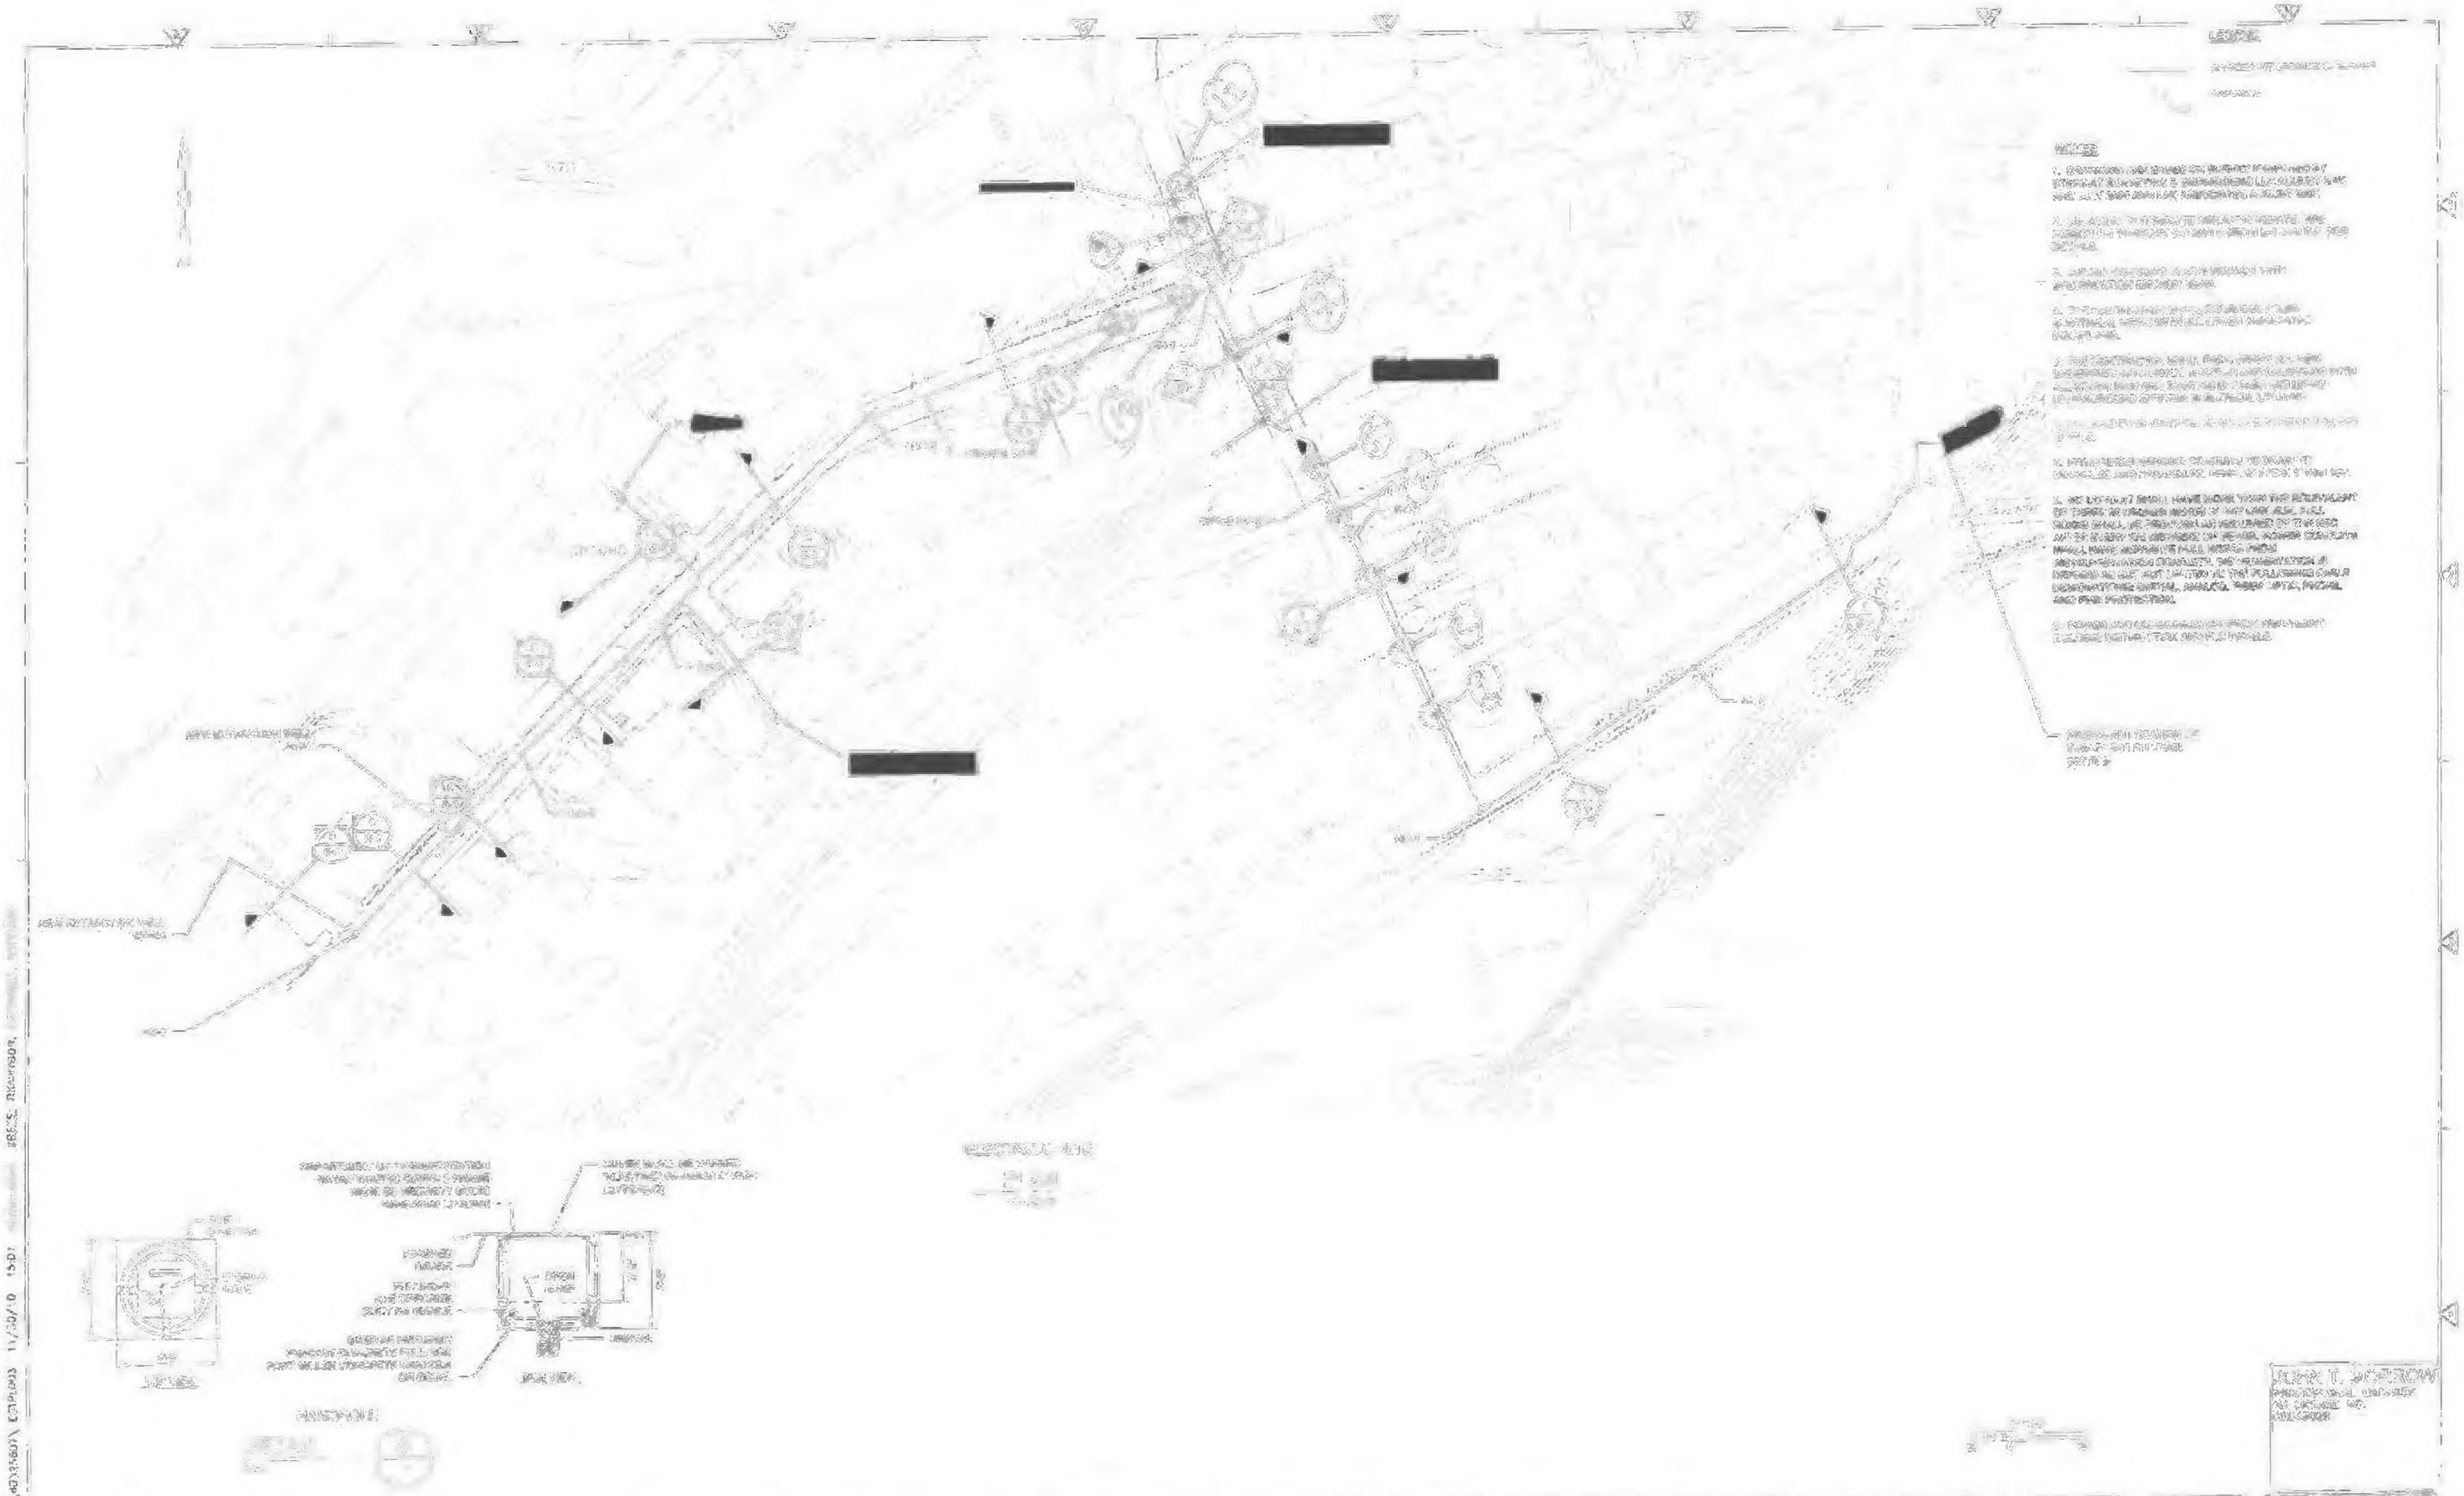

PREPARED BY:
CDM Federal Programs Corporation

FOR:
CAPE
CAPE Environmental Management, Inc.

US Army Corps of Engineers Kansas City District
TRENCH PACKAGE
MONMOUTH BOROUGH & PERTH AMBOY
EAST MARSHALL STREET PLUME - OU2
MONMOUTH BOROUGH, NEW JERSEY

ELECTRICAL SITE PLAN

2-3

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATSJ
(908) 754-3383
Fax: (908) 754-8633

NJ DOA Approved Testing Laboratory • AASHTO/ASTM Certified • NJ DEP Certified
www.ANSconsultants.com

Our compliance with NELAC standards and these rules, does not imply that we are qualified to perform work in accordance with Prevailing Wage Laws.

ASPHALT COMPACTION TEST REPORT

☒ As per ASTM D-2950-91 (Nuclear Density Gauge)

CLIENT : Cape Environmental Inc.
46 Pine Street, Suite 110
Rockaway, NJ 07866

Attn. Mr. Paul Perron

PROJECT : Rockaway Borough Superfund Site
122 Jackson Avenue
Rockaway, NJ

DATE : 8/12/2011

FILE NO. : ANX - 1743

REPORT # : 05

ENGINEER : Ripan Nagar

TIME : 7:00 a.m. - 3:00 p.m.

CERTIFICATE OF INSPECTION

As per your request asphalt compaction tests were performed at the above referenced project site on 08/12/2011.

	%	DENSITY (LB./CU.FT)			%	DENSITY (LB./CU.FT)	
TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)	TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)
2" Surface Course				2" Surface Course			
1	-	147.4	93.7	7	-	148.2	94.2
2	-	147.8	94.0	8	-	146.1	92.9
3	-	147.3	93.6	9	-	147.2	93.6
4	-	147.0	93.4	10	-	144.4	91.8
5	-	149.0	94.7	11	-	148.4	94.3
6	-	146.8	93.3	12	-	144.8	92.1
TROXLER # 29 DS1 OF DS-6085 DS2 OF NS-1853							

Remarks :

1 A Marshall number of 151.1 lb/ft³ and A of Rice number 157.3lb/ft.³ was provided by the Client. A Rice number of 157.9lb/ft.³ was utilized for test # 1 to 12. (Surface course).

Rice # was utilized to verify compaction requirements. 2" thick surface course placed over entire area. Temperature from the truck for HMA was encountered between 286°F to 300°F.

Location/Elevation : Test were taken over 2" thick I-6 surface course over electrical conduits and ground well vault. (See attached sketch).

Specification Requirements : 92% to 98% of the Rice Density.

☒ Complied With : Test # 1 - 12

☐ Not Complies With :

☒ Sliding Block covering the source rod was checked before placing the gauge in the storage box.

Copy to client, PFE, File 1

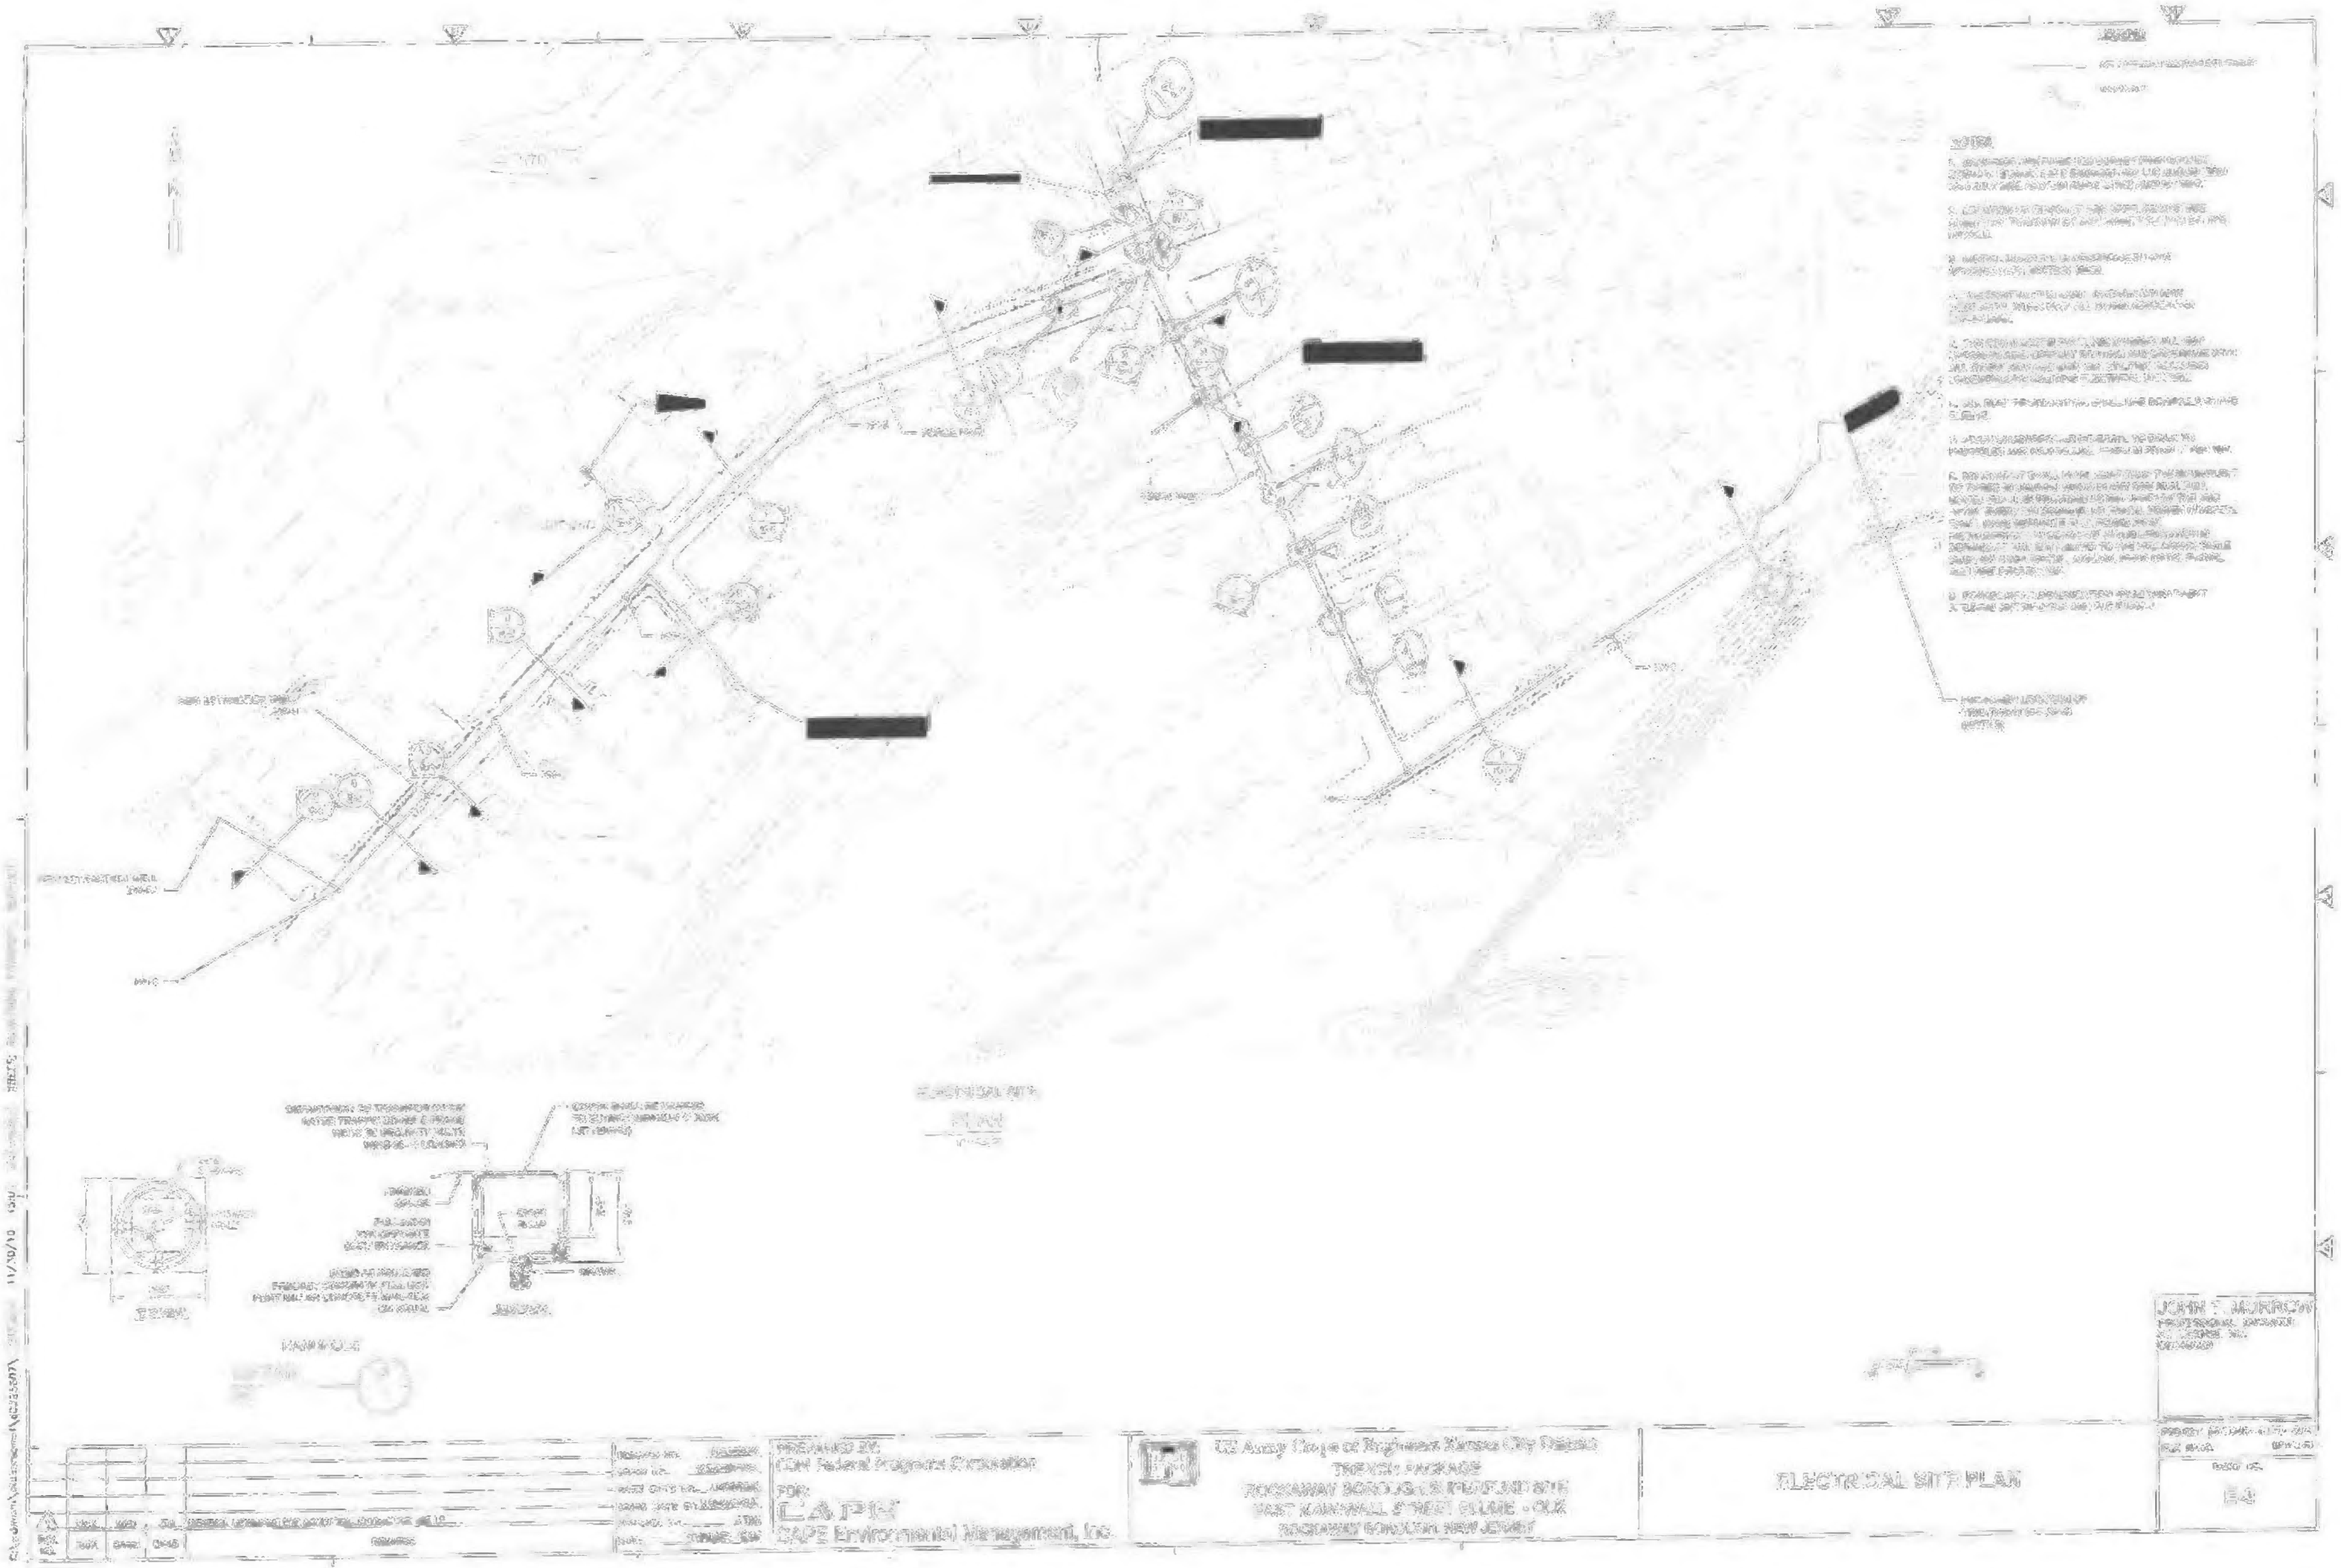
ELECTRICAL SITE PLAN
JOHN T. MORRISON
US Army Corps of Engineers Kansas City District
PREPARED BY:
FOR:
LAPIN
ELECTRICAL SITE PLAN
E-3

CONSULTANTS, INC.
4403 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 51b-ACTL
(908) 754-8888
Fax: (908) 754-8833

NJ EDA Approved Testing Laboratory • AASHTO/DBE Certified • NJ DEP Certified
www.AnSConsultants.com

ASPHALT COMPACTION TEST REPORT

☒ As per ASTM D-2950-91 (Nuclear Density Gauge)

CLIENT :	Cape Environmental Inc. 45 Pine Street, Suite 110 Rockaway, NJ 07866	DATE :	08/15/2011
		FILE NO. :	ANX - 1743
	Attn. Mr. Paul Ferroni	REPORT # :	08
PROJECT :	Rockaway Borough Superfund Site 122 Jackson Avenue Rockaway, NJ	ENGINEER :	Ripen Nagar
		TIME :	7:00 a.m. - 10:00 a.m.

CERTIFICATE OF INSPECTION

As per your request asphalt compaction tests were performed at the above referenced project site on 08/15/2011.

	*	DENSITY (LB/CU.FT)			*	DENSITY (LB/CU.FT)	
TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)	TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)
TROXLER # 0081 OF 03 , 0082 OF 03							

Remarks :

1 Inspector went to the site as scheduled, site was cancelled due to rain. Seven (7) tons of Asphalt base course was placed over exposed area to protect from the rain. Asphalt base course was placed and compacted during rain and did not tested. This is a cancellation report.

Location/Elevation :

Specification Requirements : 92% to 98% of the Rice Density.

☐ Complied With :
☐ Not Complied With :
☒ Sliding block covering the source rod was checked before placing the gauge in the storage box.

Cape Rockaway, Rev1

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 345-ATUL
(908) 754-8383
Fax: (908) 754-0613

NJ EDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ans-consultants.com

All reports, opinions, work, submittals, creations, inventions, discoveries, ideas, and any other contributions by ANS shall remain the property of ANS and shall be returned upon request.

ASPHALT COMPACTION TEST REPORT

☒ As per ASTM D 2950-91 (Nuclear Density Gauge)

CLIENT : Cape Environmental Inc.
45 Pine Street, Suite 110
Rockaway, NJ 07866

Attn. Mr. Paul Ferroni

PROJECT : Rockaway Borough Superfund Site
122 Jackson Avenue
Rockaway, NJ

DATE : 8/15/2011

FILE NO. : ANX - 1743

REPORT # : 00

ENGINEER : Hiren Negvi

TIME : 7:00 a.m. - 10:00 a.m.

CERTIFICATE OF INSPECTION

As per your request asphalt compaction tests were performed at the above referenced project site on 08/15/2011.

	*	DENSITY (LB/CU FT)			*	DENSITY (LB/CU FT)	
TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)	TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)
TROXLER # 0551 OF DS - 0552 OF RS -							

Remarks :

1 Inspector went to the site as scheduled, site was cancelled due to rain. Seven (7) tons of Asphalt base course was placed over exposed area to correct from the rain. Asphalt base course was placed and compacted during rain and did not bond. There is a cancellation report.

Location/Elevation :

Specification Requirements : 92% to 98% of the Rice Density.

☐ Complied With :
☐ Not Complied With :
☒ Sliding block covering the source rod was checked before placing the gauge in the storage box.

Page 1 of 1 Form FR-02, Rev 1

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATLC
(908) 754-8383
Fax: (908) 754-8633

NJ EDA Approved Testing Laboratory • MBE/SBE Certified • NJ DEP Certified
www.ANSConsultants.net

ASPHALT COMPACTION TEST REPORT

☒ As per ASTM D2950-91 (Nuclear Density Gauge)

CLIENT :	Cape Environmental Inc. 45 First Street, Suite 110 Rockaway, NJ 07866	DATE :	8/15/2011
		FILE NO. :	AAX - 1743
	Attn. Mr. Paul Ferrari	REPORT # :	38
PROJECT :	Rockaway Borough Superfund Site 122 Jackson Avenue Rockaway, NJ	ENGINEER :	Ripan Nagar
		TIME :	7:00 a.m. - 10:00 a.m.

CERTIFICATE OF INSPECTION

As per your request asphalt compaction tests were performed at the above referenced project site on 08/15/2011.

#1		DENSITY (LB/CU.FT.)		#		DENSITY (LB/CU.FT.)	
TEST NO.	LOCATION ELEVATION	FIELD	COMPACTION (%)	TEST NO.	LOCATION ELEVATION	FIELD	COMPACTION (%)
TROXLER #		DST OF 06		DSZ OF 18			

Remarks :

1. Inspector went to the site as schedule, site was cancelled due to rain. Seven (7) tons of Asphalt base course was placed over exposed area to protect from the rain. Asphalt base course was placed and compacted during rain and did not bleed. This is a cancellation report.

Location/Elevation :

Specification Requirements : 92% to 98% of the Rice Density.

☐ Complied With :
☐ Not Complied With :
☒ Sliding block covering the source rod was checked before placing the gauge in the storage box.

Sample Copy Not A Report

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel (800) 545-ATUL
(908) 754-8383
Fax (908) 754-8633

NJ EDA Approved Testing Laboratory • AASHTO/ASTM Certified • NJ DEP Certified
www.ANSConsultants.net

ASPHALT COMPACTION TEST REPORT

☒ As per ASTM D-2950-91 (Nuclear Density Gauge)

CLIENT :	Cape Environmental Inc. 45 Pine Street, Suite 110 Rockaway, NJ 07866	DATE :	06/17/2011
		FILE NO. :	ANX - 1743
	Attn. Mr. Paul Ferrari	REPORT # :	04
PROJECT :	Rockaway Borough Superfund Site 122 Jackson Avenue Rockaway, NJ	ENGINEER :	Rajesh Nagar
		TIME :	7:00 a.m. - 3:30 p.m.

CERTIFICATE OF INSPECTION

As per your request asphalt compaction tests were performed at the above referenced project site on 06/17/2011.

	%	DENSITY (LB./CU.FT)			%	DENSITY (LB./CU.FT)	
TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)	TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)
3" Base Course (1-2)				9" Base Course (1-2)			
1	-	149.8	95.3	5	-	151.3	94.4
2	-	150.1	95.5	6	-	150.4	93.9
3	-	150.7	94.8	7	-	150.1	93.6
4	-	152.1	95.0	8	-	150.0	94.3
TROXLER # 25 DS1 OF RS -4510 DS2 OF MS -1535							

Remarks :

1. A Marshall number of 150.6 lb./ft.³ and Act Rice number 150.1 lb./ft.³ was provided by the Client. A Rice number of 150.1 lb./ft.³ was used for test # 1 to 8 (base course).

2. 3" thick base course was placed for highlighted area. Asphalt temperature from truck was encountered as 285°F to 310°F.

Location/Elevation : Test were taken over 5' - 9' wide trench. (See attached sketch).

Specification Requirements : 92% to 98% of the Rice Density.

☒ Complied With : Test # 1 - 8

☐ Not Complied With :

☒ Sliding block covering the source rod was checked before placing the gauge in the storage box.

Copy to: Client/ANS Files

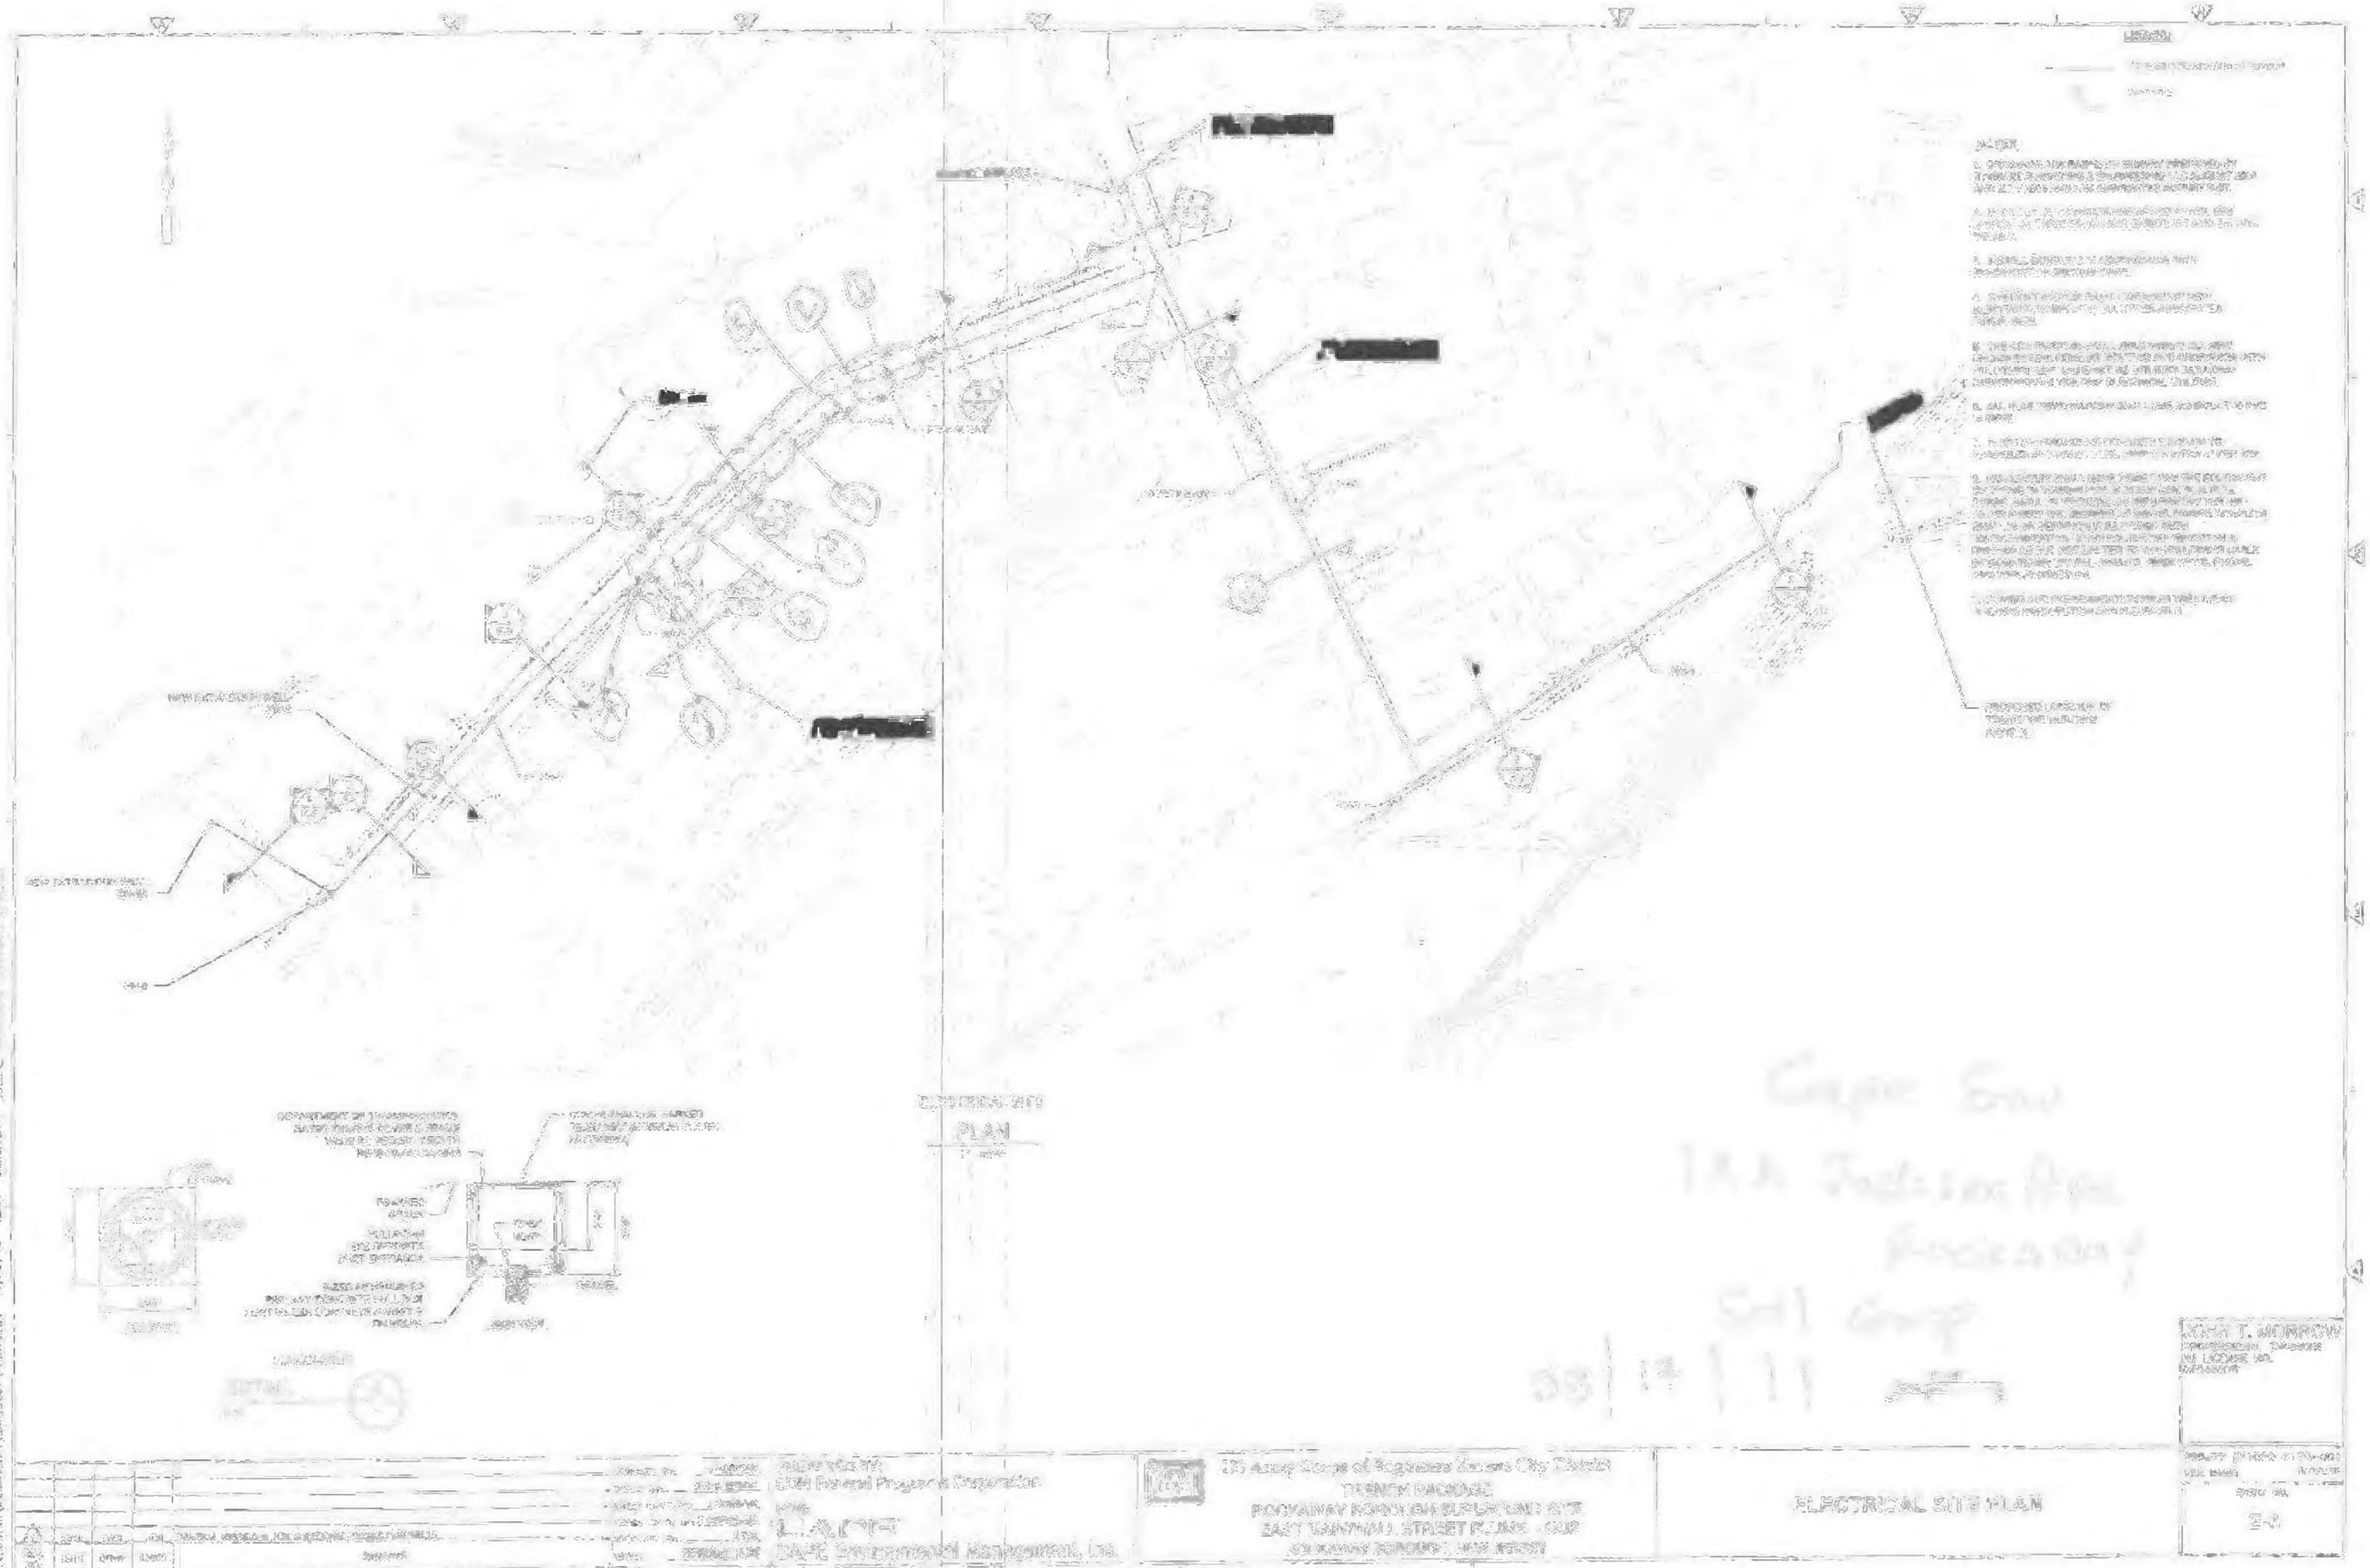
LEGEND
PLAN
Cape Cod
IAA Tedder Ave
Roadway
Soil Grip
08 | 14 | 11
JOHN T. MORRISON
ELECTRICAL SITE PLAN
E-2
LAPCI
DAVE Environmental Management, Inc.
US Army Corps of Engineers Kansas City District
DESIGN PACKAGE
ROCKAWAY NOTCH SUPERFUND SITE
EAST MAINTHALL STREET PLANT - OUS
ROCKAWAY BOROUGH, NEW JERSEY
ELECTRICAL SITE PLAN
E-2

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ANJC
(908) 754-8381
Fax: (908) 754-8633

NJ DOA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANJCo.com

Soil Testing, Asphalt, Concrete, Masonry, Fireproofing, Fireproofing, Steel Decking, Welding, Roofing, Air Force Decontamination Group, UST Removal, Environmental Sampling & Testing

ASPHALT COMPACTION TEST REPORT

☒ As per ASTM D2950-91 (Nuclear Density Gauge)

CLIENT : Cape Environmental Inc.
45 Pine Street, Suite 110
Rockaway, NJ 07866

Attn. Mr. Paul Ferrari

PROJECT : Rockaway Borough Superfund Site
128 Jackson Avenue
Rockaway, NJ

DATE : 8/17/2011

FILE NO. : ANX - 1743

REPORT # : 6A

ENGINEER : Robert Nagel

TIME : 7:00 a.m. - 3:30 p.m.

CERTIFICATE OF INSPECTION

As per your request asphalt compaction tests were performed at the above referenced project site on 08/17/2011.

	1	DENSITY (LB/CU FT)			1	DENSITY (LB/CU FT)	
TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)	TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)
3" Base Course (1-2)				3" Base Course (1-2)			
1	-	146.3	93.3	5	-	151.0	97.0
2	-	150.1	95.7	6	-	150.8	96.1
3	-	151.0	96.3	7	-	150.4	95.9
4	-	152.1	96.0	8	-	150.8	96.3
TROXLER # 24 DS1 OF DS -6B6C DS2 OF MS -1630							

Remarks :

1 A Marshall number of "02 3 0-0" and A of Rice number 150 lb/ft.³ was provided by the Client. A Rice number of 150 lb/ft.³ was utilized for tests 1 to 8 (Base course).

2 Thick base course was placed for high traffic area. Asphalt temperature from truck was recorded as 290°F to 310°F.

Location/Elevation : Test were taken over 5' - 6' wide trench. (See attached sketch)

Specification Requirements : 92% to 98% of the Rice Density.

☒ Complied With : Test # 1 - 8

☐ Not Complied With :

☒ Sliding block covering the source rod was checked before placing the gauge in the storage box.

Copy to: Active File / File

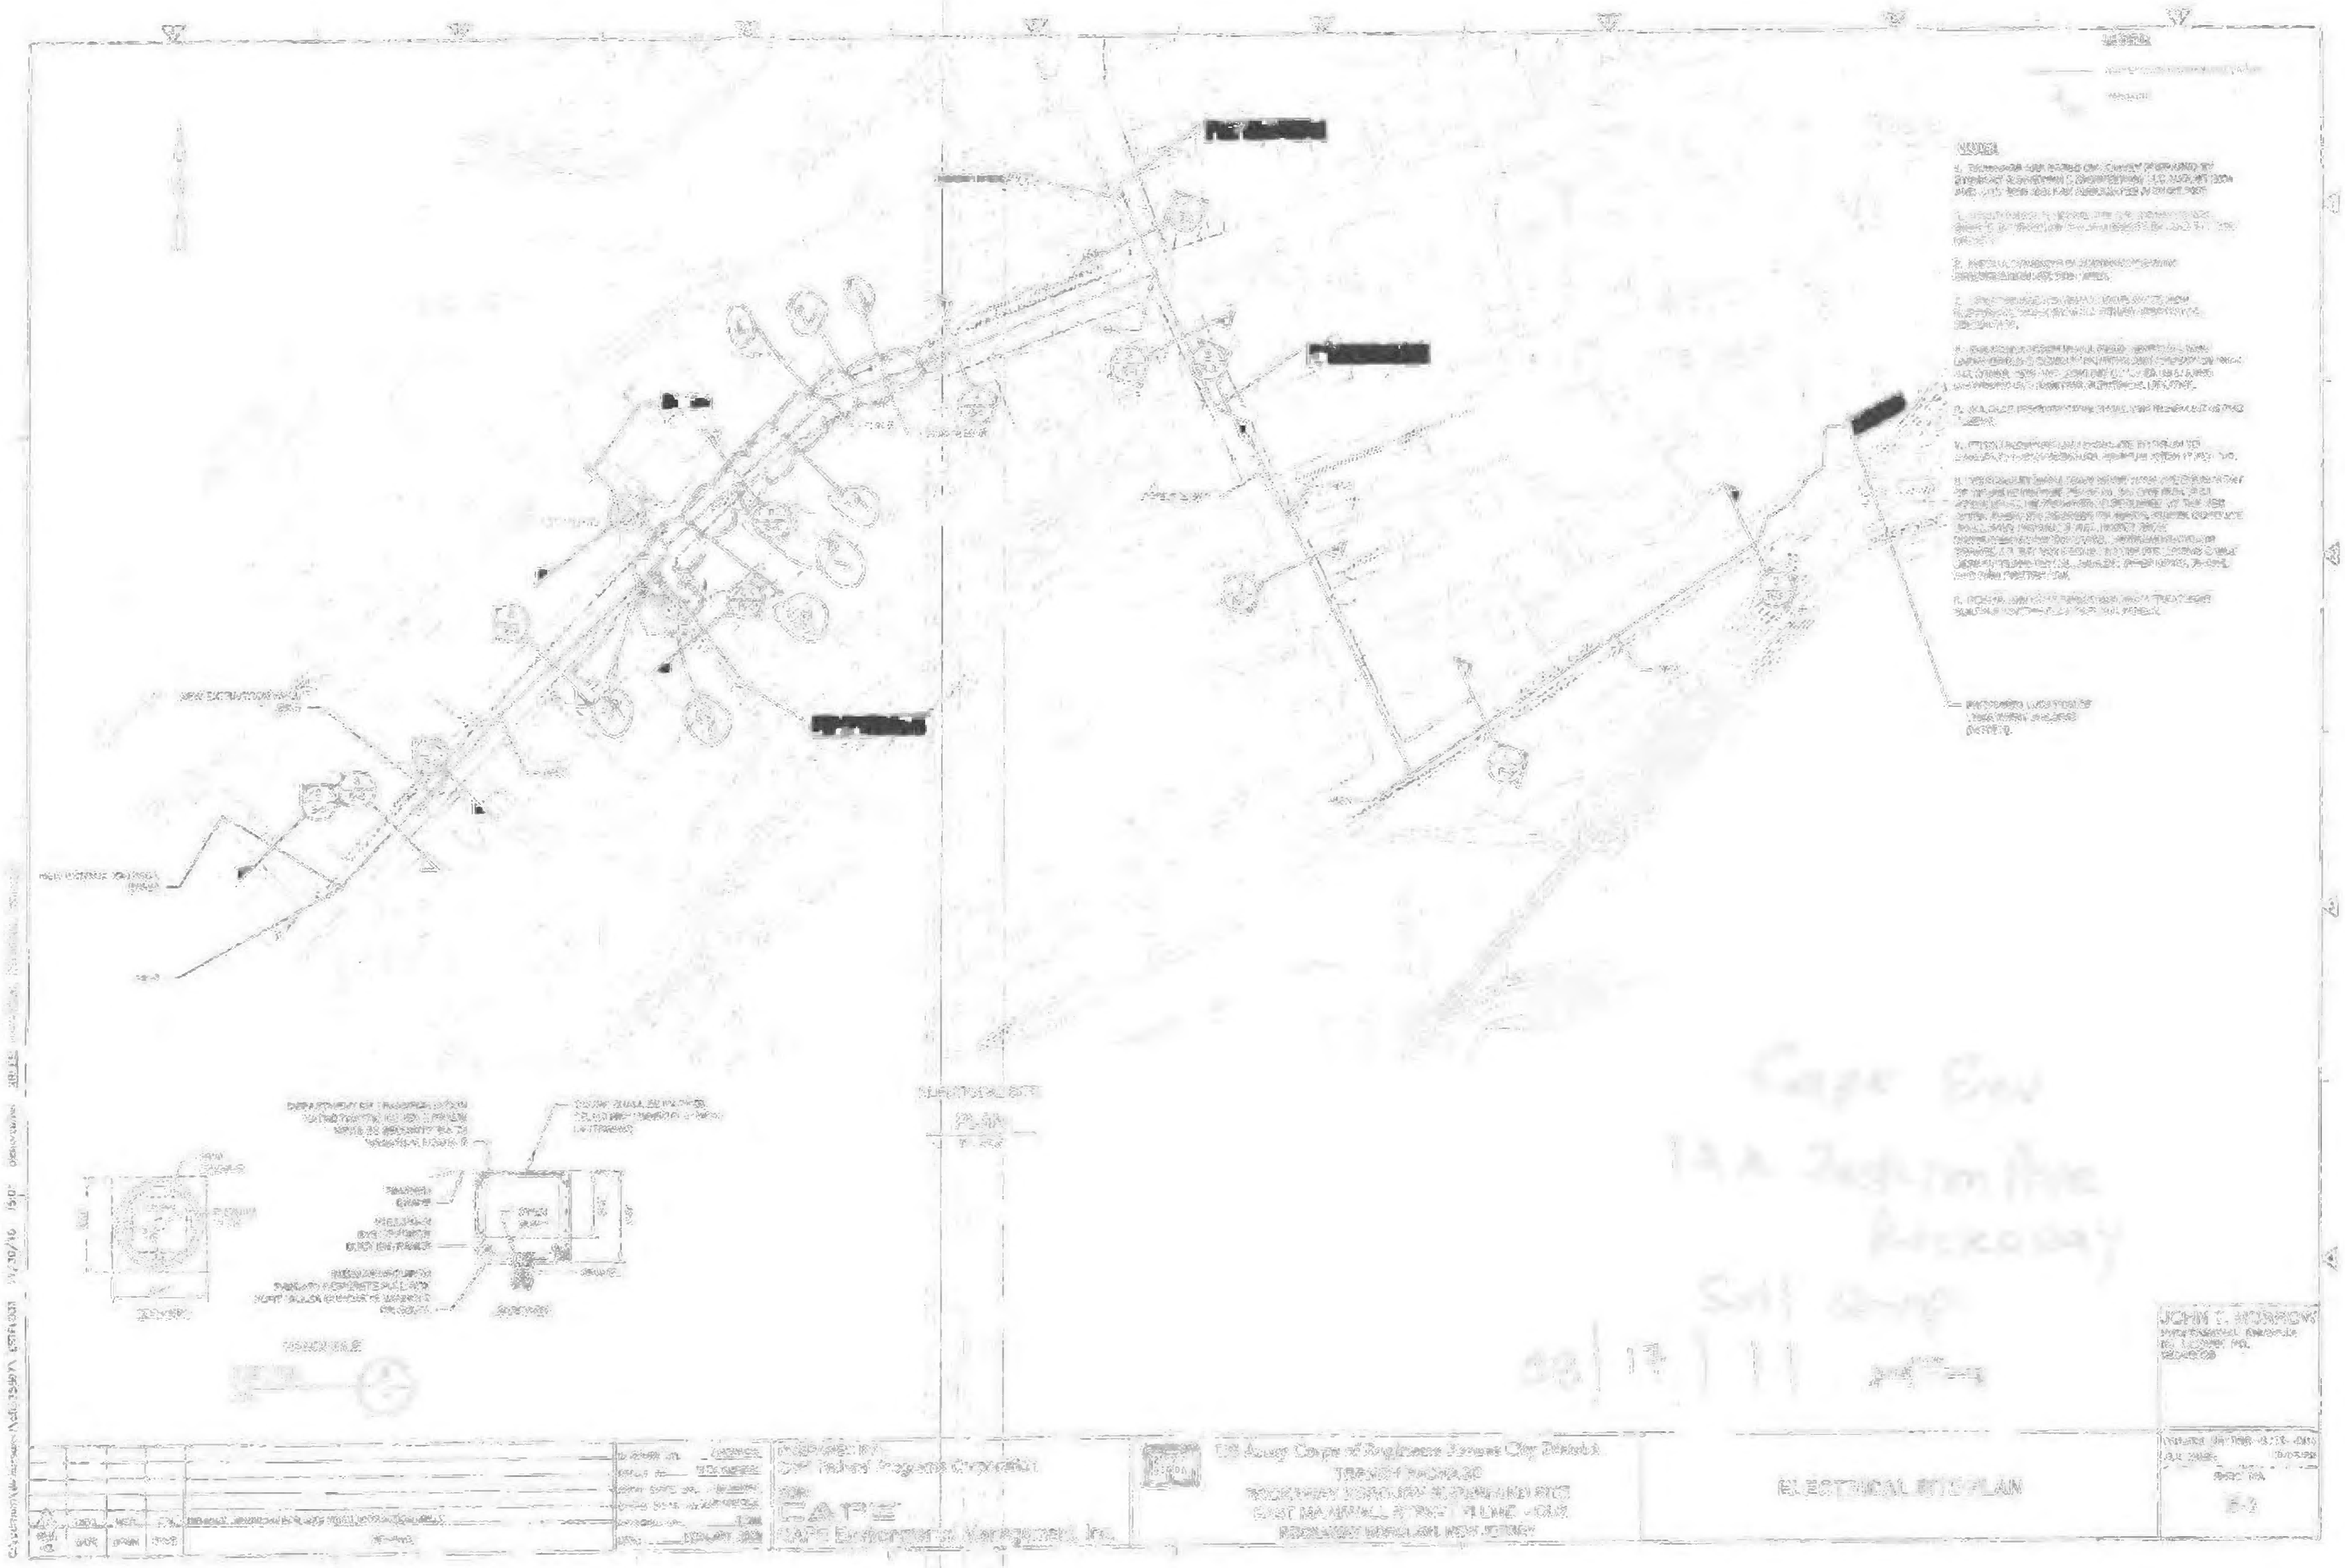
NOTES
JOHN T. MORROW
ELECTRICAL SITE PLAN
E-2
US Army Corps of Engineers Fresno City Schools
CAPE
CAPE Environmental Management, Inc.

CONSULTANTS, INC.
4485 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATLC
(908) 754-8383
Fax: (908) 754-8633

NJ DDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSConsultants.net

ASPHALT COMPACTION TEST REPORT

☒ As per ASTM D 2950-91 (Nuclear Density Gauge)

CLIENT : Cape Environmental Inc.
45 Pine Street, Suite 110
Rockaway, NJ 07866

Attr. Mr. Paul Ferrari

PROJECT : Rockaway Borough Superfund Site
122 Jackson Avenue
Rockaway, NJ

DATE : 8/17/2011

FILE NO. : ANS - 1743

REPORT # : 6A

ENGINEER : Rajen Nagar

TIME : 7:00 a.m. - 9:30 a.m.

CERTIFICATE OF INSPECTION

As per your request asphalt compaction tests were performed at the above referenced project site on 08/17/2011.

		DENSITY (LB/CU FT)				DENSITY (LB/CU FT)	
TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)	TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)
3" Base Course (1-2)				3" Base Course (1-2)			
1	"	150.4	93.4	5	"	151.8	94.3
2	"	150.1	93.2	6	"	150.4	93.4
3	"	151.2	94.0	7	"	150.0	93.1
4	"	152.1	95.0	8	"	150.9	94.3
TROXLER # 25 DS1 OF DS -5830 DS2 OF DS -1830							

Remarks :

1. A Marshall number of "152.8 lb/ft³" and A or Rice number "152.1lb/ft³" was provided by the Client.
   A Rice number of 152.1lb/ft³ was utilized for test # 1 to 8. (Base course).

   3" thick base course was placed for highlighted area. Asphalt temperature from truck was encountered bet. 280°F to 310°F.

Location/Elevation : Test were taken over 5' - 6' wide bench. (See attached sketch).

Specification Requirements : 92% to 98% of the Rice Density.

☒ Complied With : Test # 1 - 8

☐ Not Complied With :

☒ Sliding block covering the source rod was checked before placing the gauge in the storage box.

Rajen Nagar, P.E.

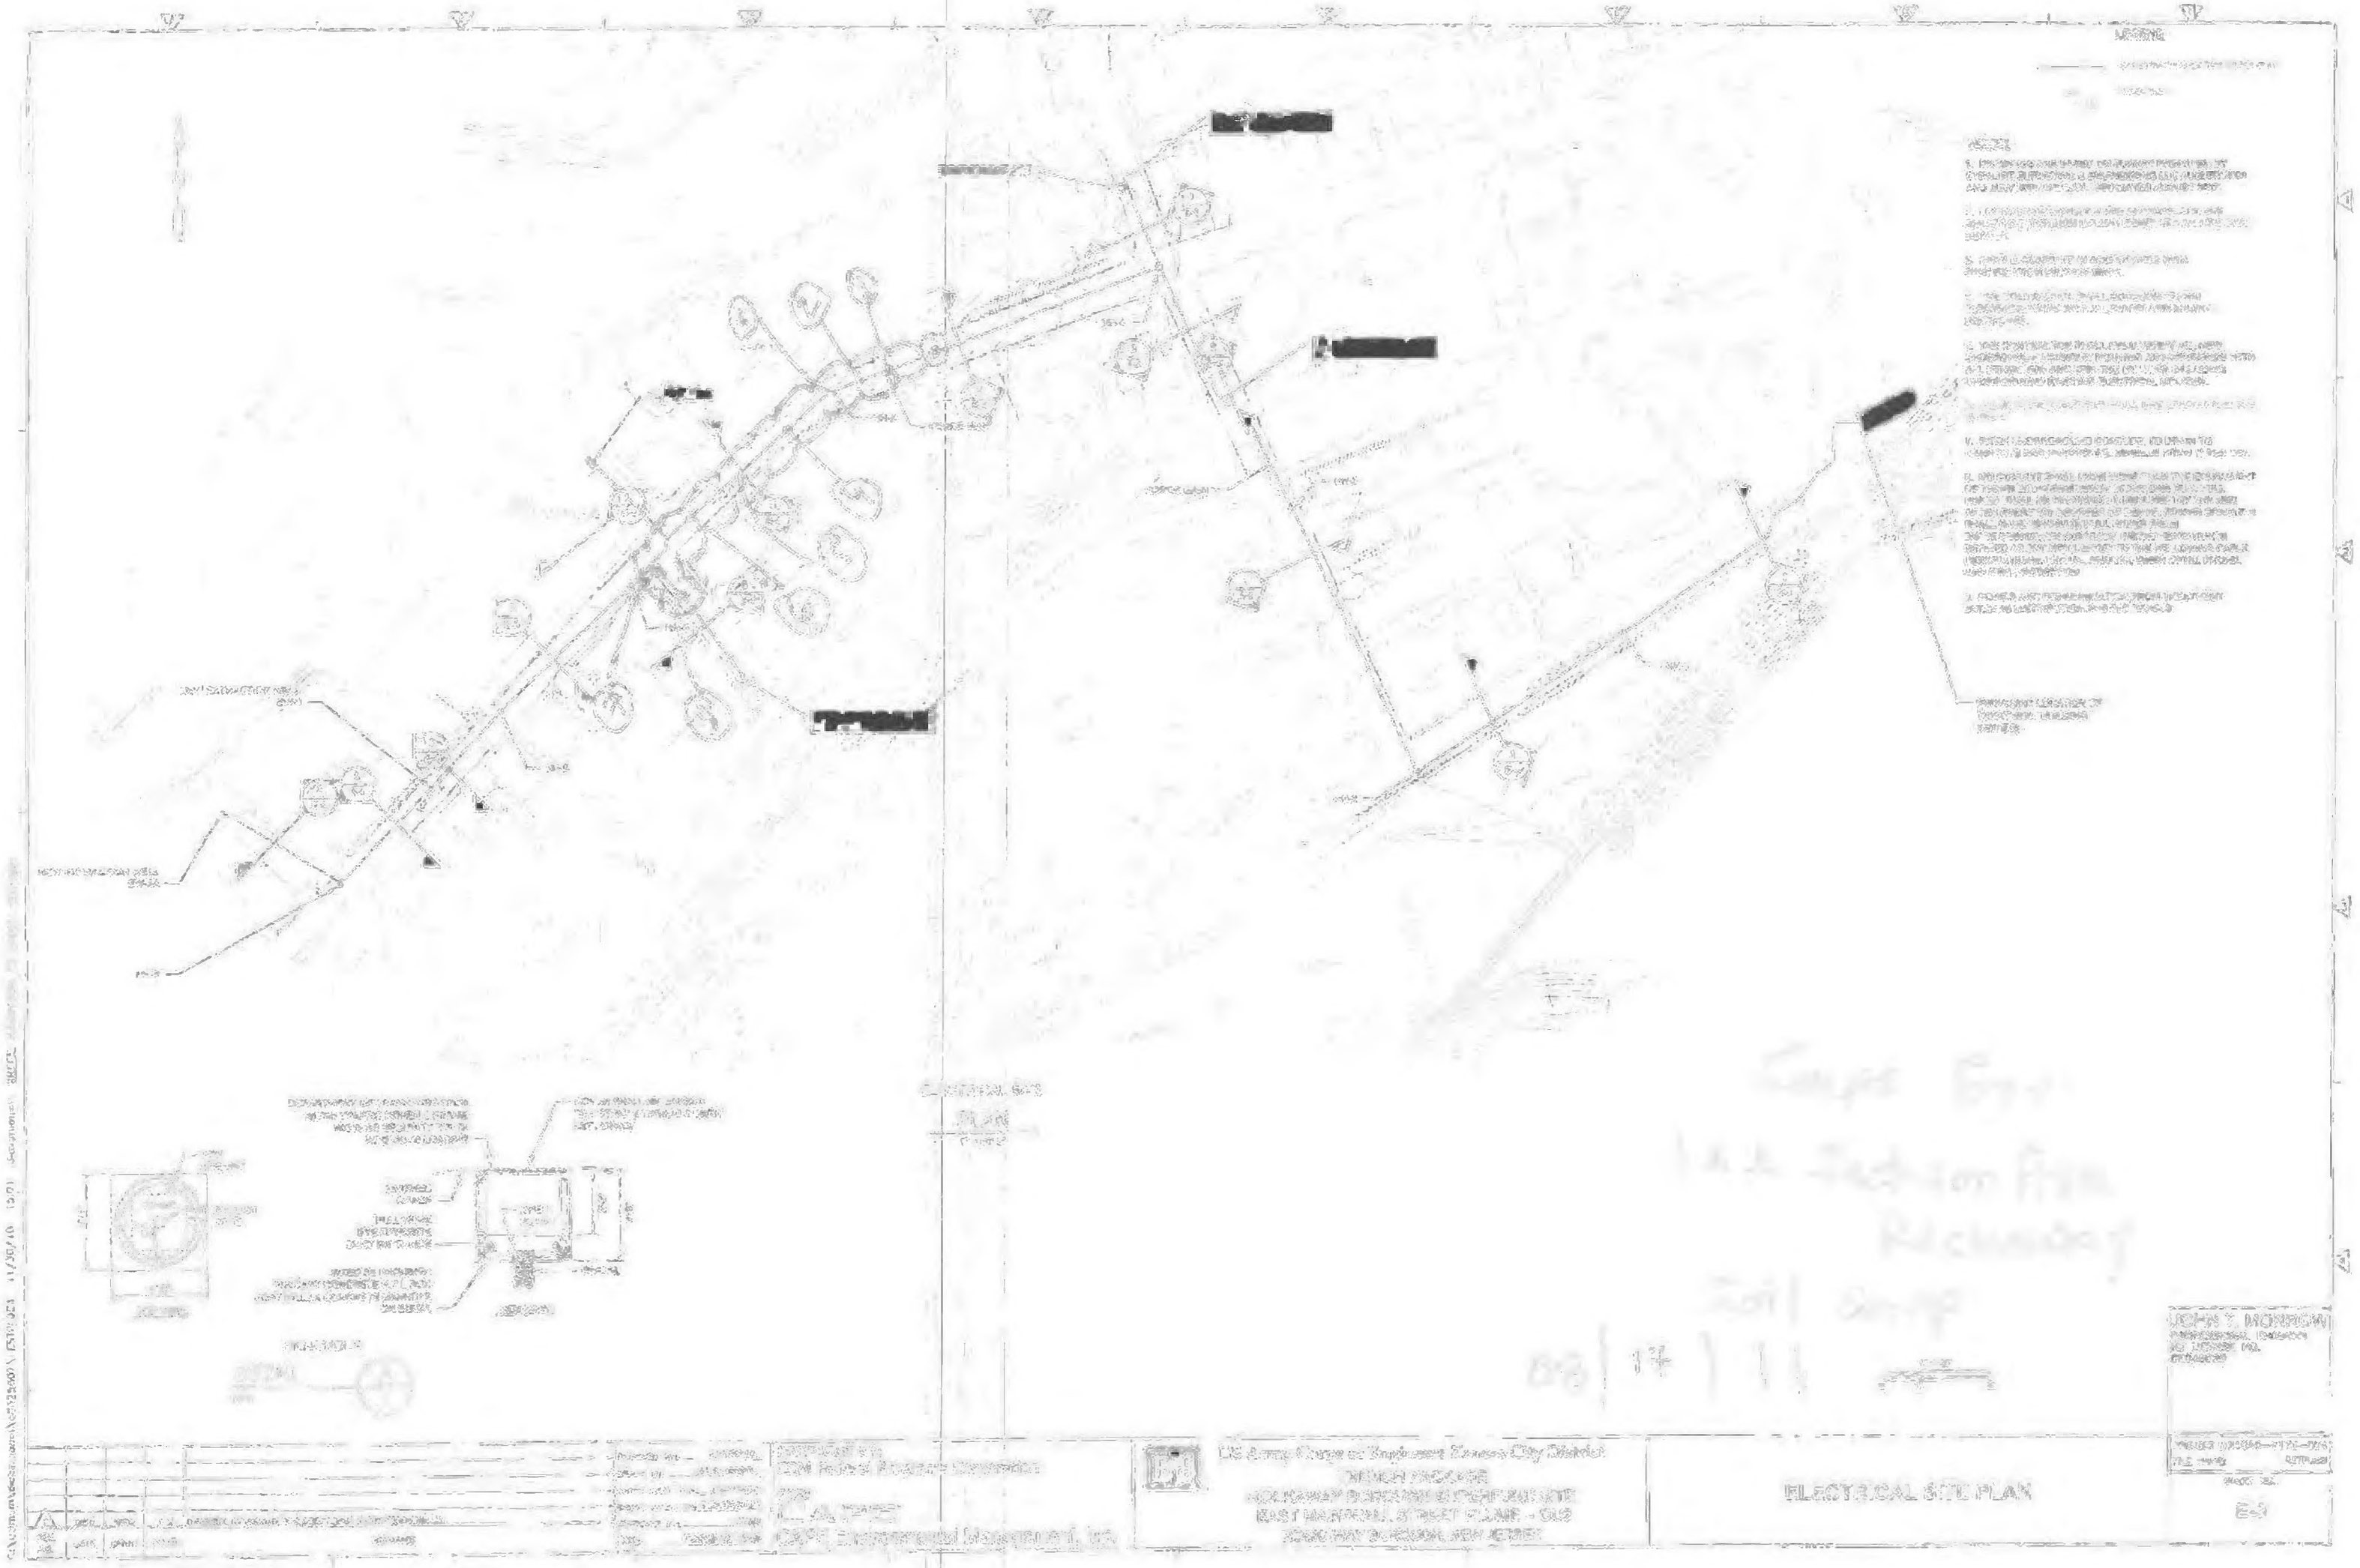
LEGEND
ELECTRICAL SITE PLAN
US Army Corps of Engineers Kansas City District
EAST MANSFIELD, STREET CLARE - OLD
ROAD WAY BLACKTOP, NEW JERSEY
E-1

CONSULTANTS, INC.
4405 Sayre Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ACTL
(908) 754-6383
Fax: (908) 754-6533

NJ EDA Approved Testing Laboratory • AASHTO/ASTE Certified • NJ DEP Certified
www.ANSconsultants.com

ASPHALT COMPACTION TEST REPORT

☒ As per ASTM D-2950-91 (Nuclear Density Gauge)

CLIENT : Gaga Enviromental Inc.
46 Pine Street, Suite 118
Rockaway, NJ 07866

Attn. Mr. Paul Ferroni

PROJECT : Rockaway Borough Superfund Site
122 Jackson Avenue
Rockaway, NJ

DATE : 8/19/2011

FILE NO. : ANS - 1743

REPORT # : 07

ENGINEER : Kishor Soni

TIME : 7:00 a.m. - 2:30 p.m.

CERTIFICATE OF INSPECTION

As per your request asphalt compaction tests were performed at the above referenced project site on 08/18/2011.

	*	DENSITY (LB/CU FT)			*	DENSITY (LB/CU FT)	
TEST NO.	LOCATION ELEVATION	FIELD	COMPACTION (%)	TEST NO.	LOCATION ELEVATION	FIELD	COMPACTION (%)
± 2" Top Course (1-5) Material				±9" Base Course (1-4) Material			
1	-	[illegible]	[illegible]	1A	-	[illegible]	[illegible]
2	-	[illegible]	[illegible]	2A	-	[illegible]	[illegible]
3	-	[illegible]	[illegible]	3A	-	[illegible]	[illegible]
4	-	142.5	[illegible]				
TROXLER # 35 DS1 OF DS-6/65 DS2 OF MS-1830							

Remarks :

1 A Marshall number of 152.2 lb/ft³ and A of Rice number 157 lb/ft³ was provided by the Client. A Rice number of 157 lb/ft³ was utilized for test # 1 to 4. (Top course).

2 A Marshall number of 151.5 lb/ft³ and A of Rice number 157.5lb/ft³ was provided by the Client. A Rice number of 157.5lb/ft³ was utilized for test # 1A to 3A. (Base course).

Temperature 280°F - 1st load - (1-5) material, Temperature 280°F - 2nd load - (1-5) material, Temperature 290°F - 3rd load - (1-5) material, Temperature - 284°F - 1st load - (1-4) material and Temperature - 280°F - 2nd load (1-4) material.

Location/Elevation : See attached sketch

Specification Requirements : 92% to 98% of the Rice Density

☒ Complied With : Test # 1 - 4 and 1A - 3A

☐ Not Complied With :

☒ Sliding block covering the source rod was checked before placing the gauge in the storage box.

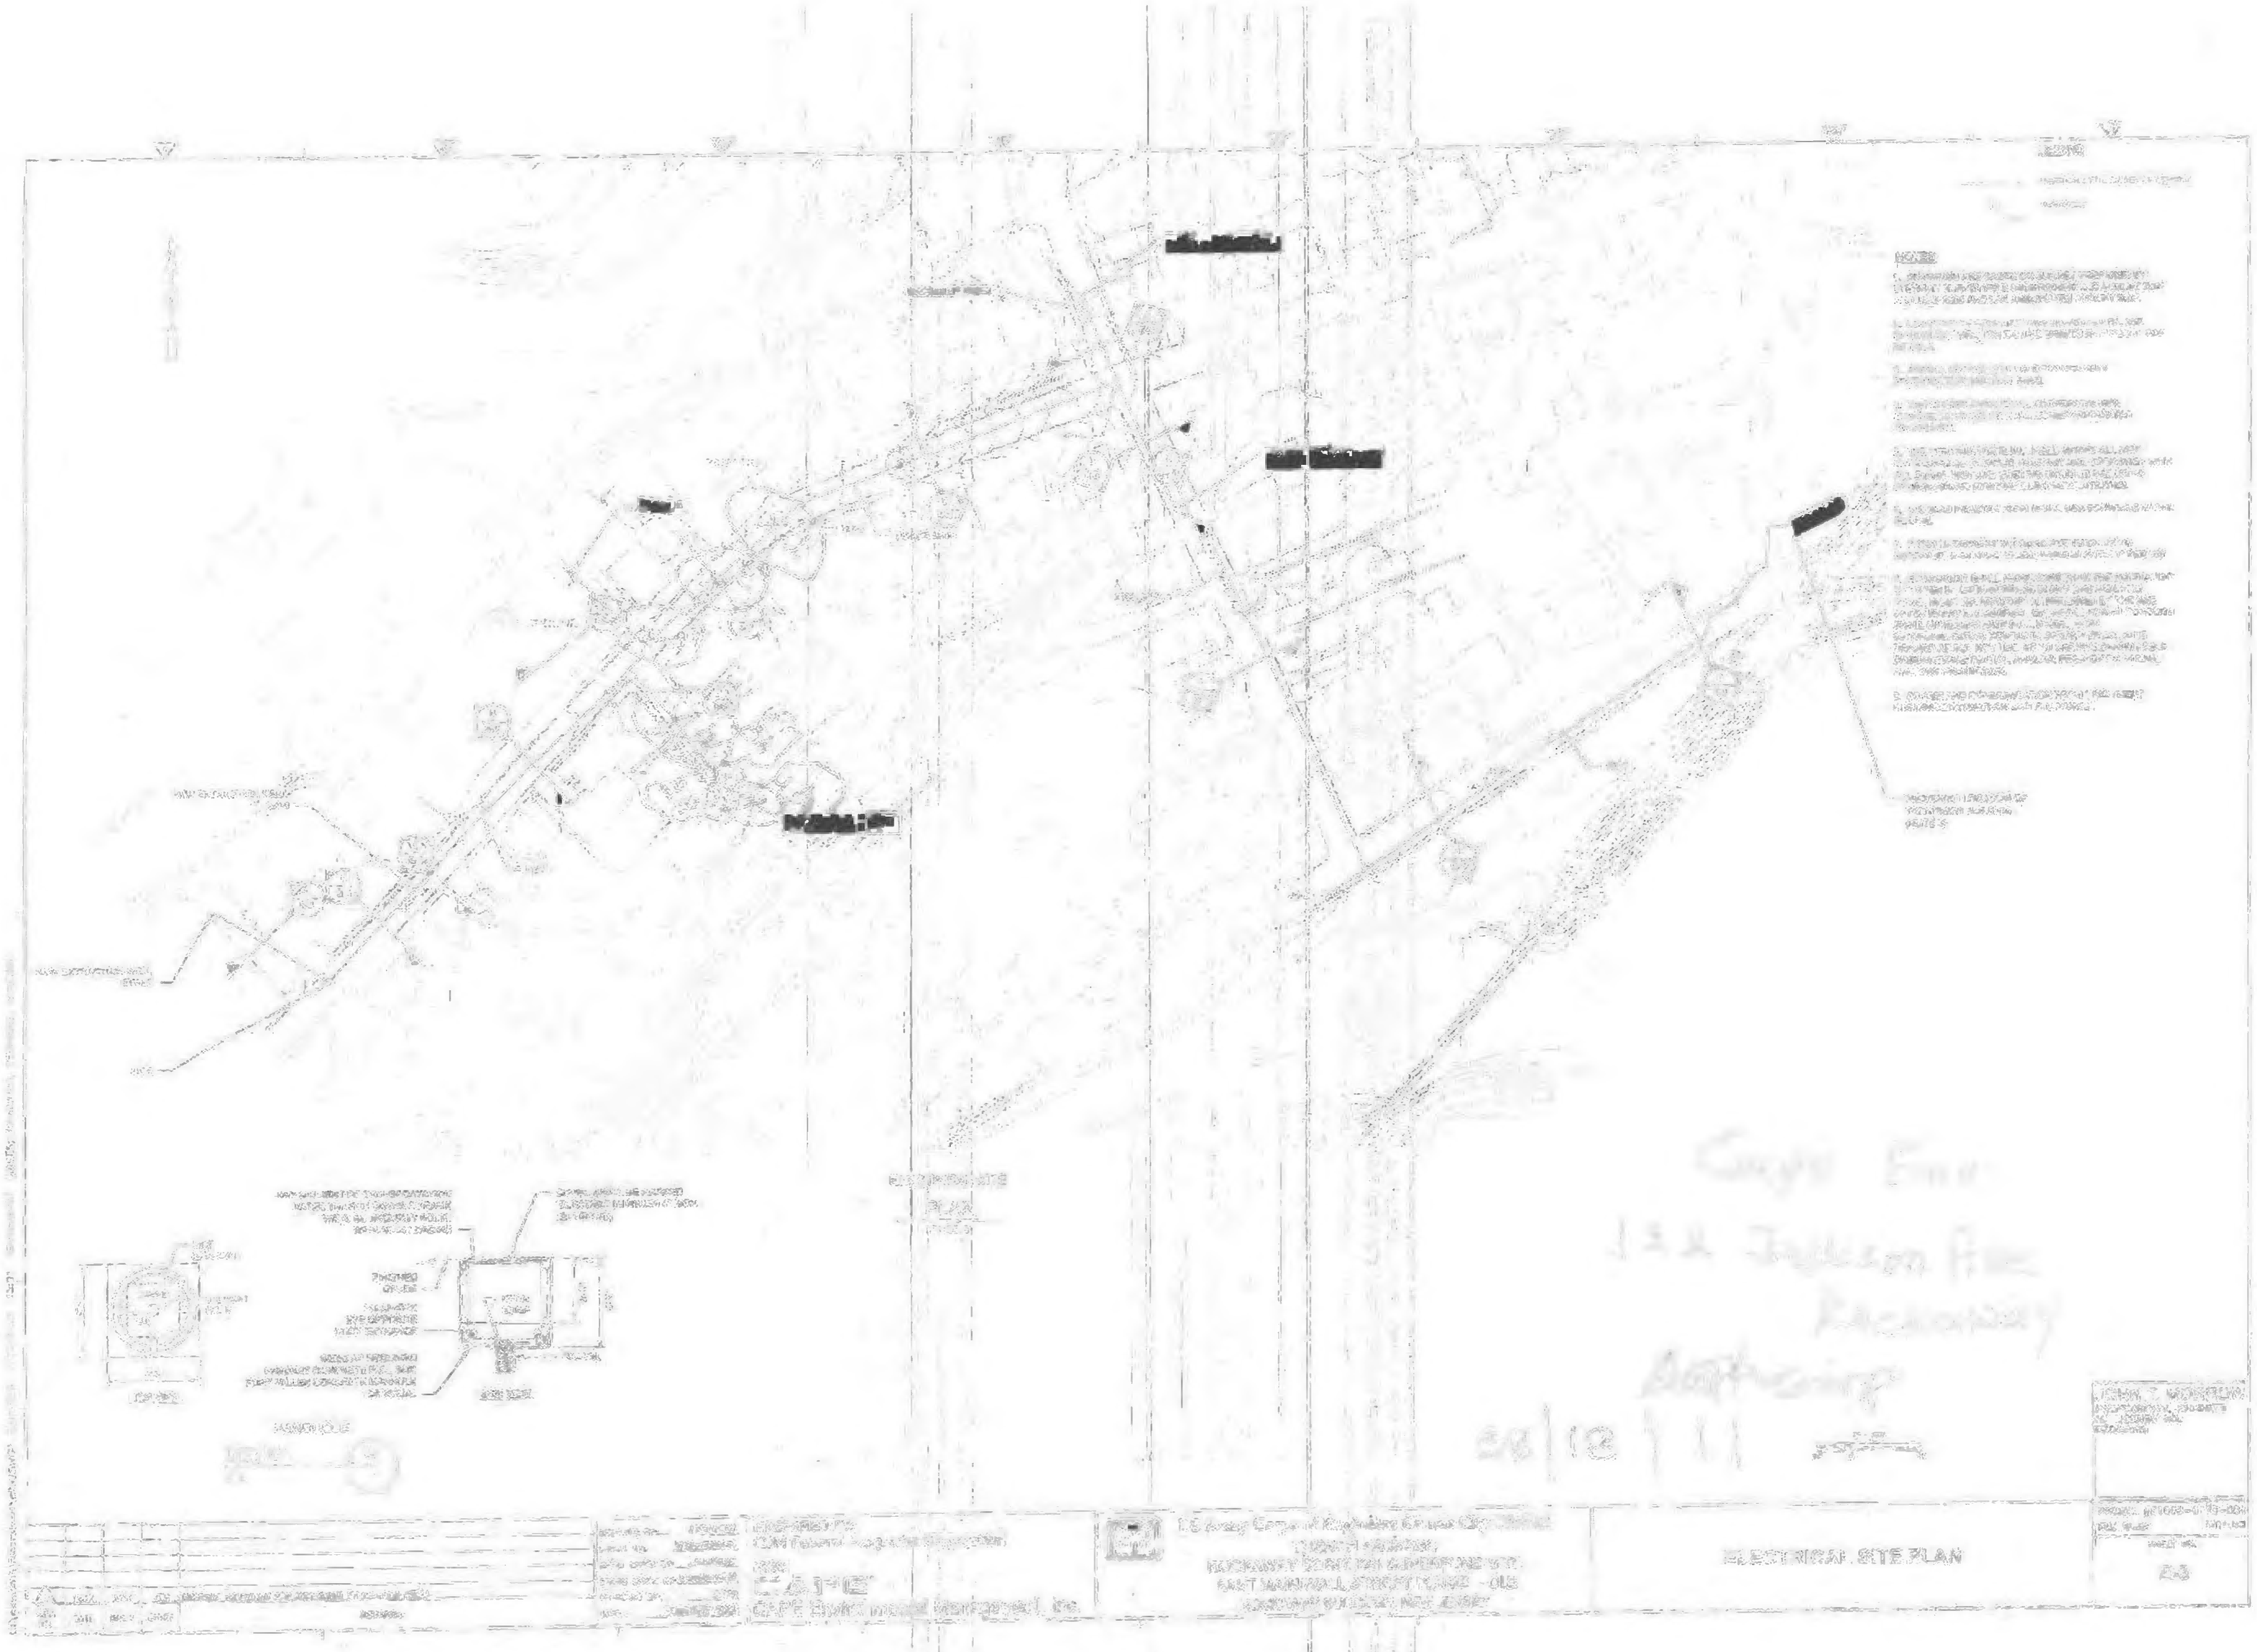
ELECTRICAL SITE PLAN

CONSULTANTS, INC.
4425 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATUL
(908) 754-8383
Fax: (908) 754-8633

NJ EDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSconsultants.net

ASPHALT COMPACTION TEST REPORT

☒ As per ASTM D2950-91 (Nuclear Density Gauge)

CLIENT : Cape Environmental Inc.
45 Pine Street, Suite 110
Rockaway, NJ 07866

Attn. Mr. Paul Ferrari

DATE : 8/18/2011

FILE NO. : ANX - 1743

REPORT # : 07

PROJECT : Rockaway Borough Superfund Site
122 Jackson Avenue
Rockaway, NJ

ENGINEER : Ramy Sorl

TIME : 7:00 a.m. - 3:30 p.m.

CERTIFICATE OF INSPECTION

As per your request asphalt compaction tests were performed at the above referenced project site on 08/18/2011.

		DENSITY (LB./CU.FT)				DENSITY (LB./CU.FT)	
TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)	TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)
1-2" Top Course (1-3) Material				2-3" Base Course (1-2) Material			
1	*	145.8	92.9	1A	*	148.9	92.9
2	*	146	93.0	2A	*	149.7	93.0
3	*	146.7	93.4	3A	*	149.4	93.2
4	*	146.3	92.9				
TROXLER # 28 DS1 OF DS-6703 DS2 OF MS-1930							

Remarks :

1 A Marshall number of 152.2 lb./ft.³ and A of Rice number 157.7lb/ft.³ was provided by the Client. A Rice number of 157.7lb/ft.³ was utilized for test # 1 to 4 (Top course).

2 A Marshall number of 152.5 lb./ft.³ and A of Rice number 157.5lb/ft.³ was provided by the Client. A Rice number of 157.5lb/ft.³ was utilized for tests 1A to 3A. (Base course).

Temperature 282°F - 1st load - (1-3) material, Temperature 286°F - 2nd load - (1-3) material, Temperature 282°F - 3rd Load - (1-3) material. Temperature - 284°F - 1st load - (1-2) material and Temperature - 280°F - 2nd load (1-2) material.

Location/Elevation : See attached sketch.

Specification Requirements : 92% to 98% of the Rice Density

☒ Complied With : Test # 1 - 4 and 1A - 3A.

☐ Not Complied With :

☒ Sliding block covering the source rod was checked before placing the gauge in the storage box.

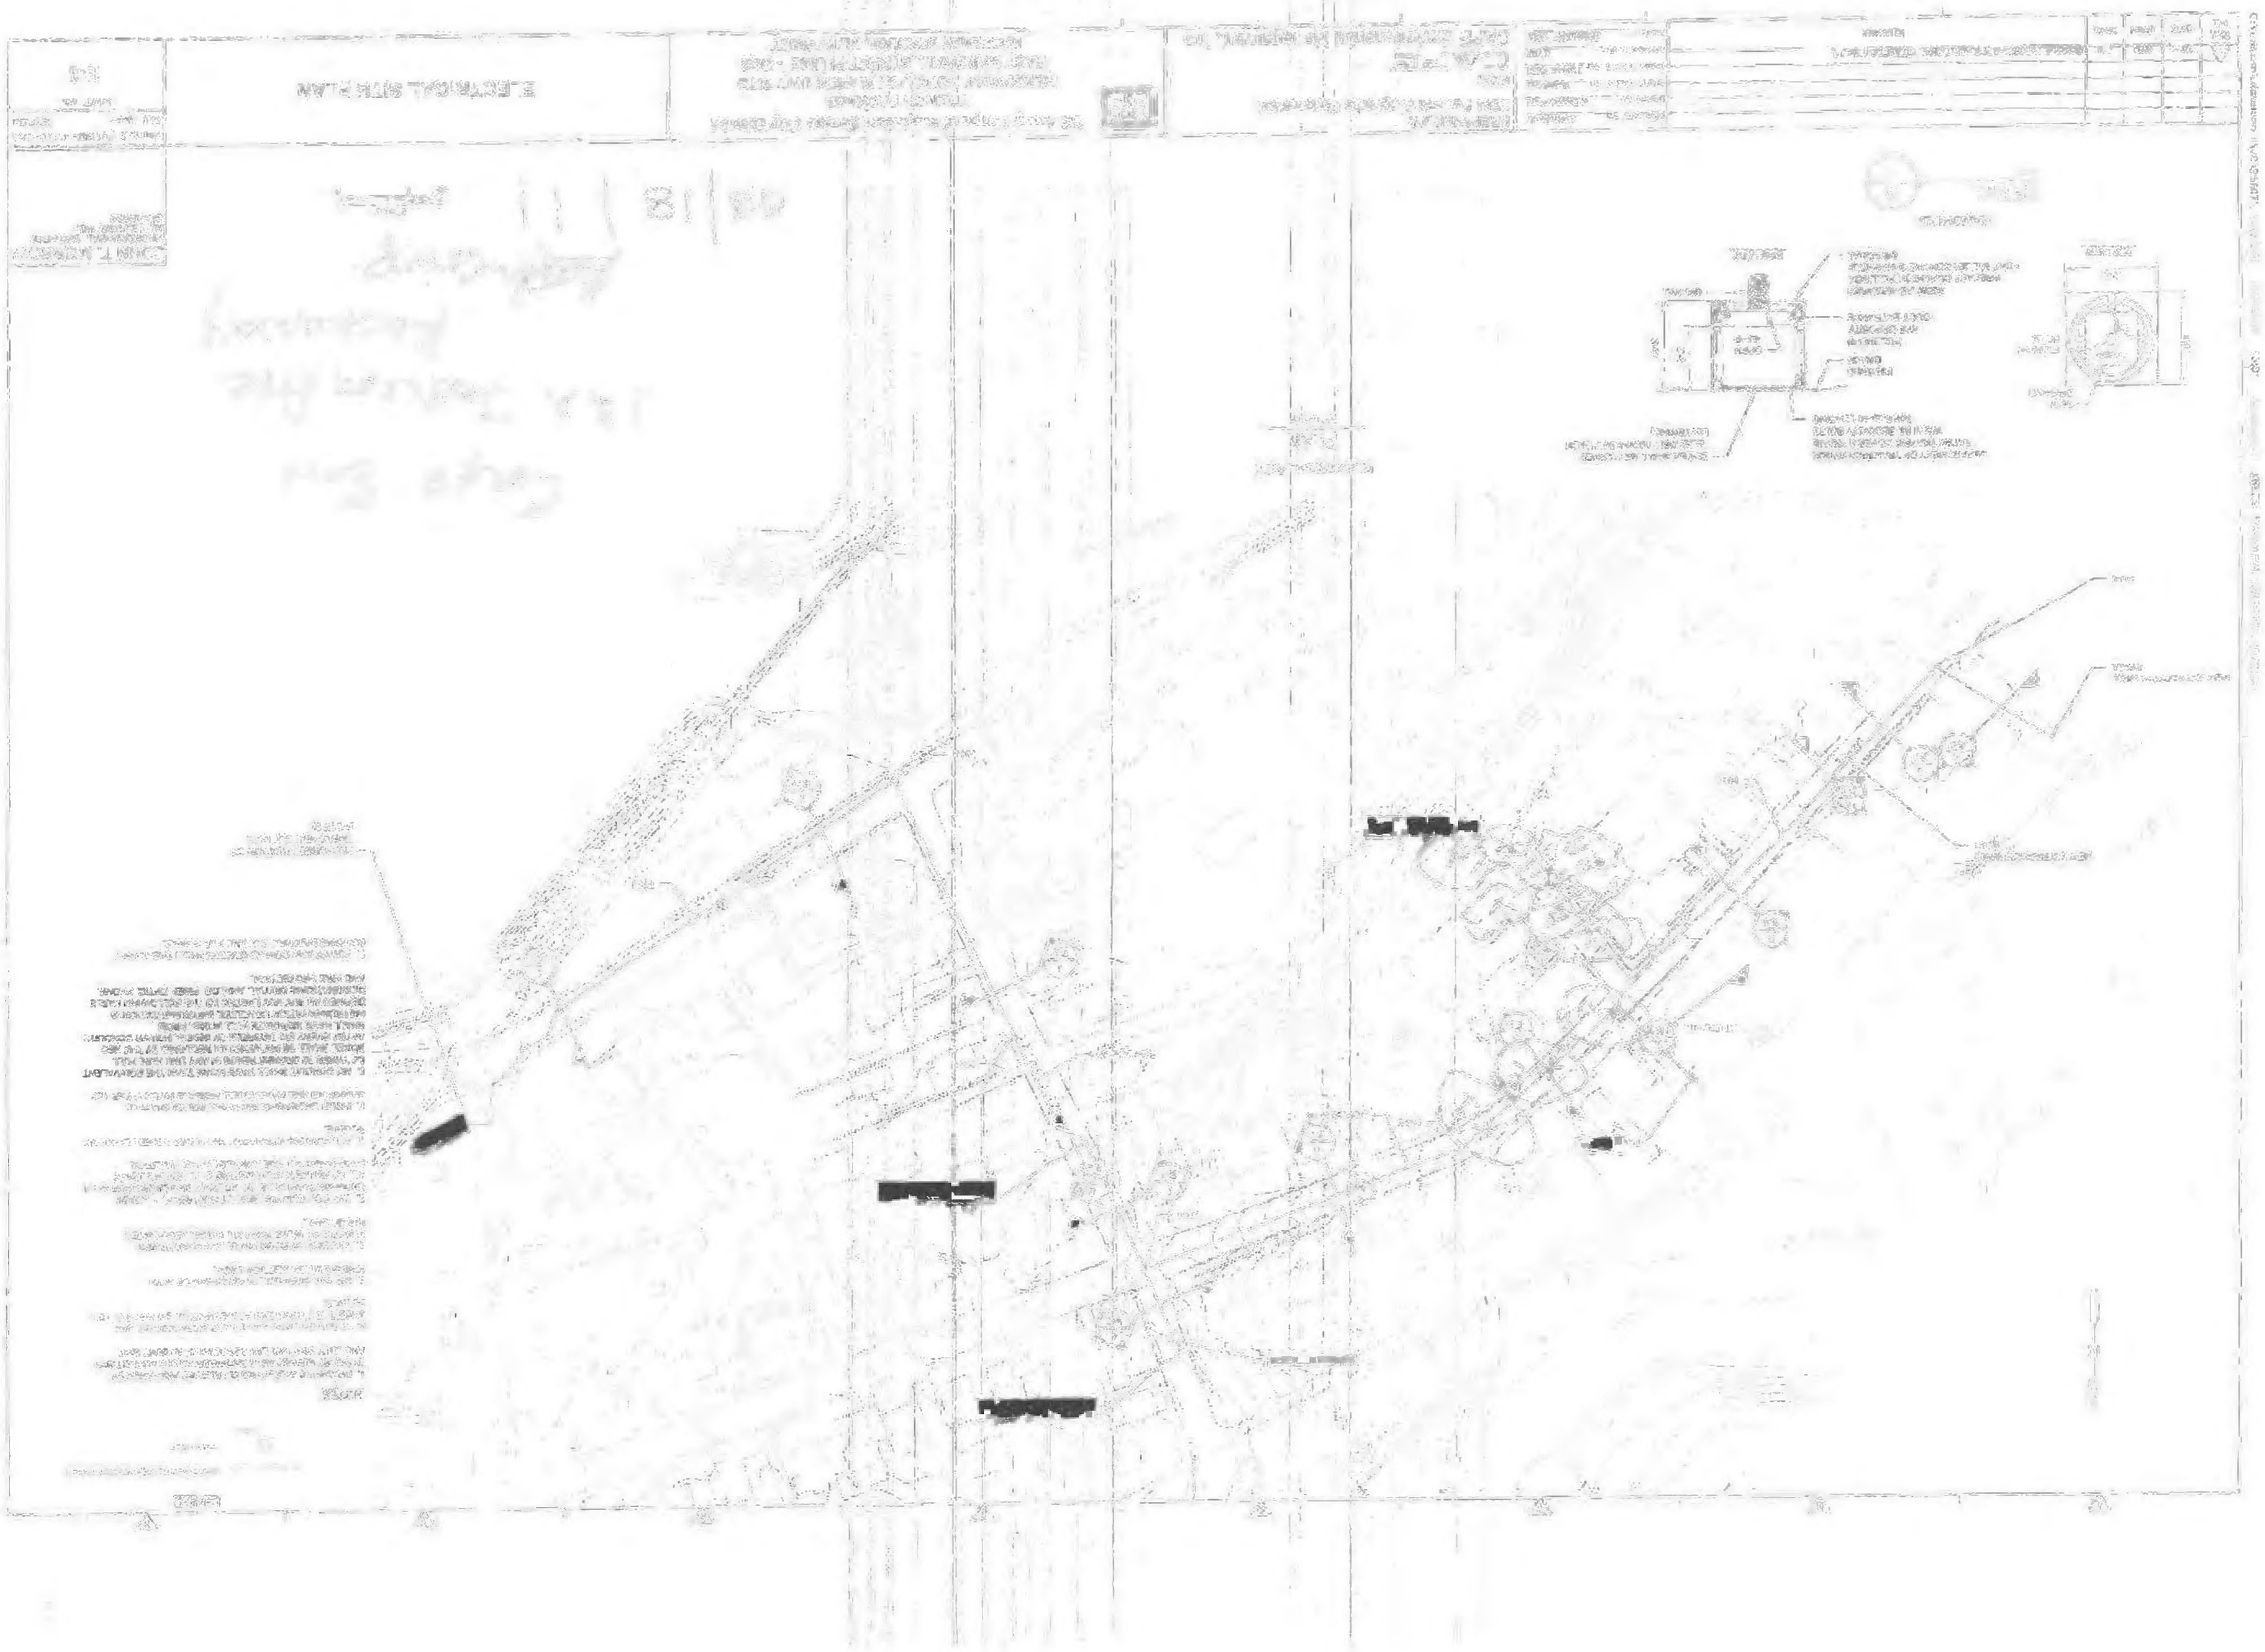

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATCL
(908) 754-6383
Fax: (908) 754-8639

NJ DDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSConsultants.net

Soil Compaction Testing, Asphalt Compaction Testing, Concrete Testing, Concrete Cylinders, Concrete Cores, Concrete Footings, Concrete Block Testing, Soil Testing, Soil Compaction Testing, Soil Density Testing, Soil Density, Clay Cleanup Technical Inspection Services, Grout Testing, Grout Cubes, Grout Prisms, Grout Cores, Grout Footings, Grout Block Testing, Grout Compaction Testing, Grout Density Testing, Grout Density, Grout Cleanup Technical Inspection Services, Asphalt Testing, Asphalt Cores, Asphalt Density Testing, Asphalt Density, Asphalt Cleanup Technical Inspection Services, Asphalt Compaction Testing, Asphalt Compaction

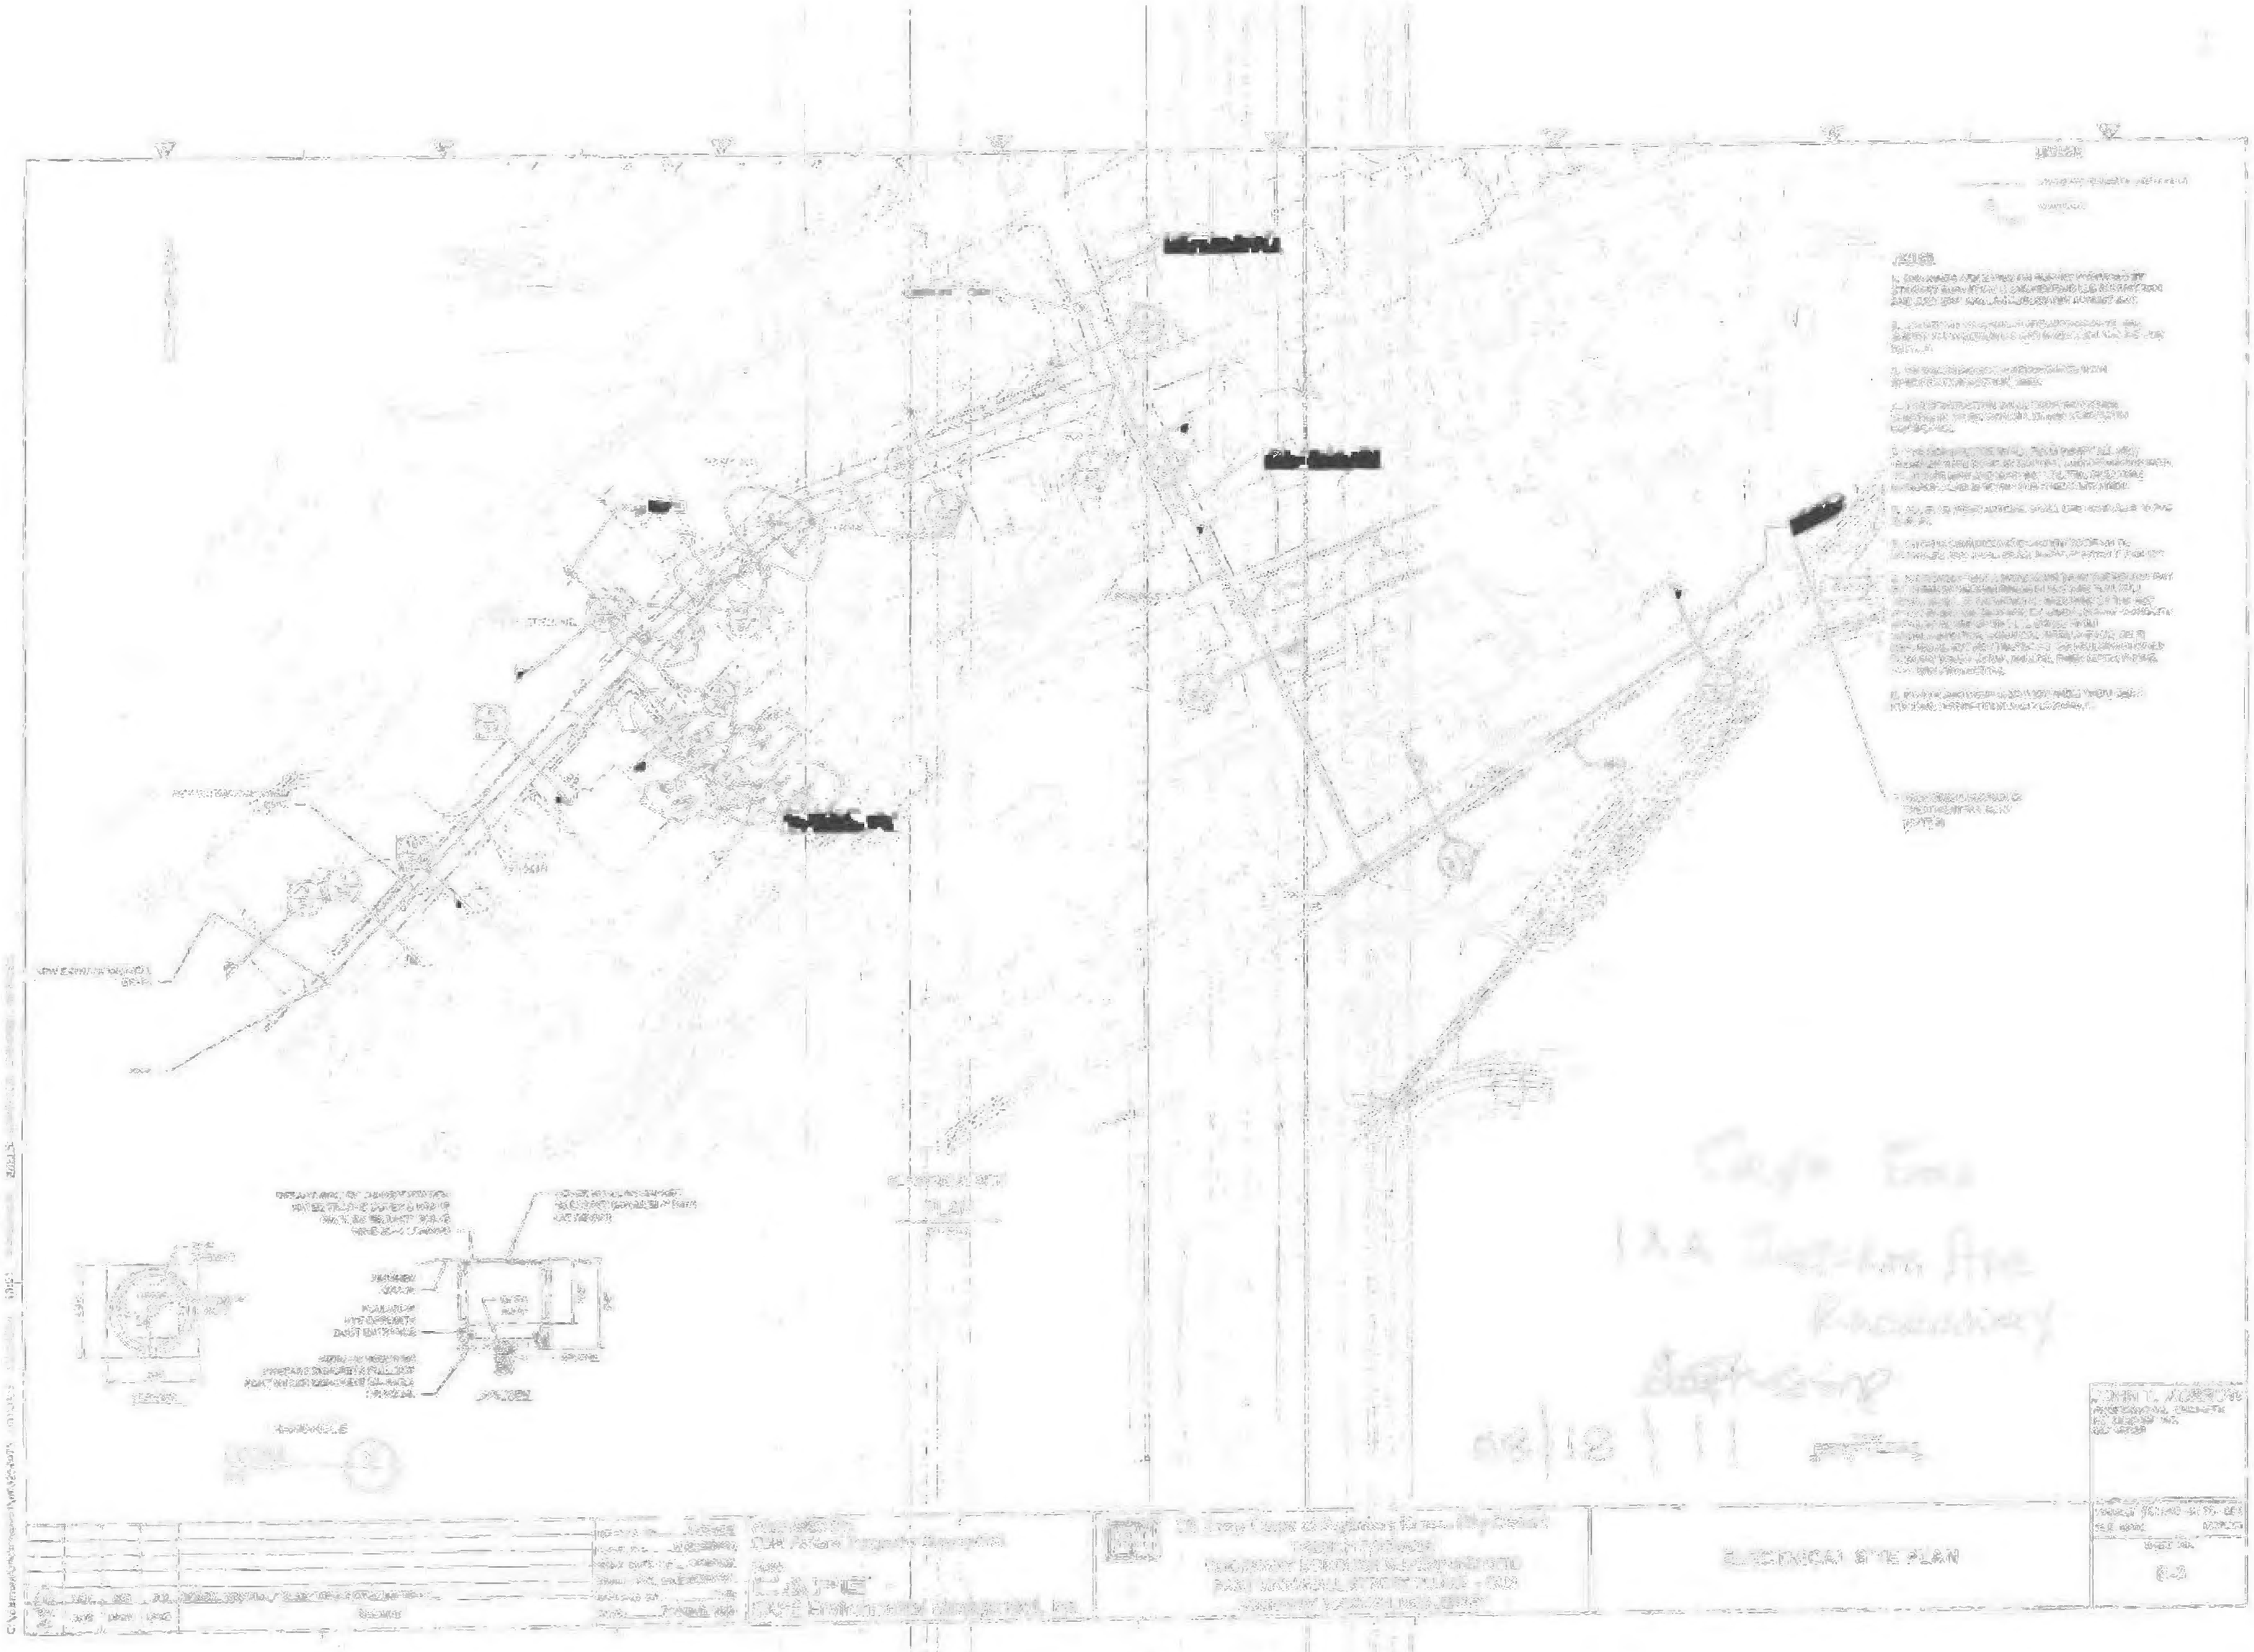
ELECTRICAL SITE PLAN

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATUC
(908) 754-8383
Fax: (908) 754-8633

NJ EDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSConsultants.net

Soil Compaction, Density, Asphalt, Concrete, Masonry, Steel, Grouts, Piles, Concrete Cylinders, Geotechnical Testing, Soil Borings, Test Pits, Geotechnical Testing, Underground Storage Tanks, Environmental Testing, Asbestos, Lead Paint, Indoor Air Quality, Water, Wastewater, Hazardous Waste, Industrial Hygiene, Phase I, Phase II, Phase III, Phase IV, Phase V, Phase VI, Phase VII, Phase VIII, Phase IX, Phase X, Phase XI, Phase XII, Phase XIII, Phase XIV, Phase XV, Phase XVI, Phase XVII, Phase XVIII, Phase XIX, Phase XX, Phase XXI, Phase XXII, Phase XXIII, Phase XXIV, Phase XXV, Phase XXVI, Phase XXVII, Phase XXVIII, Phase XXIX, Phase XXX, Phase XXXI, Phase XXXII, Phase XXXIII, Phase XXXIV, Phase XXXV, Phase XXXVI, Phase XXXVII, Phase XXXVIII, Phase XXXIX, Phase XL, Phase XLI, Phase XLII, Phase XLIII, Phase XLIV, Phase XLV, Phase XLVI, Phase XLVII, Phase XLVIII, Phase XLIX, Phase L, Phase LI, Phase LII, Phase LIII, Phase LIV, Phase LV, Phase LVI, Phase LVII, Phase LVIII, Phase LIX, Phase LX, Phase LXI, Phase LXII, Phase LXIII, Phase LXIV, Phase LXV, Phase LXVI, Phase LXVII, Phase LXVIII, Phase LXIX, Phase LXX, Phase LXXI, Phase LXXII, Phase LXXIII, Phase LXXIV, Phase LXXV, Phase LXXVI, Phase LXXVII, Phase LXXVIII, Phase LXXIX, Phase LXXX, Phase LXXXI, Phase LXXXII, Phase LXXXIII, Phase LXXXIV, Phase LXXXV, Phase LXXXVI, Phase LXXXVII, Phase LXXXVIII, Phase LXXXIX, Phase XC, Phase XCI, Phase XCII, Phase XCIII, Phase XCIV, Phase XCV, Phase XCVI, Phase XCVII, Phase XCVIII, Phase XCIX, Phase C, Phase CI, Phase CII, Phase CIII, Phase CIV, Phase CV, Phase CVI, Phase CVII, Phase CVIII, Phase CIX, Phase CX, Phase CXI, Phase CXII, Phase CXIII, Phase CXIV, Phase CXV, Phase CXVI, Phase CXVII, Phase CXVIII, Phase CXIX, Phase CXX, Phase CXXI, Phase CXXII, Phase CXXIII, Phase CXXIV, Phase CXXV, Phase CXXVI, Phase CXXVII, Phase CXXVIII, Phase CXXIX, Phase CXXX, Phase CXXXI, Phase CXXXII, Phase CXXXIII, Phase CXXXIV, Phase CXXXV, Phase CXXXVI, Phase CXXXVII, Phase CXXXVIII, Phase CXXXIX, Phase CXL, Phase CXLI, Phase CXLII, Phase CXLIII, Phase CXLIV, Phase CXLV, Phase CXLVI, Phase CXLVII, Phase CXLVIII, Phase CXLIX, Phase CL, Phase CLI, Phase CLII, Phase CLIII, Phase CLIV, Phase CLV, Phase CLVI, Phase CLVII, Phase CLVIII, Phase CLIX, Phase CLX, Phase CLXI, Phase CLXII, Phase CLXIII, Phase CLXIV, Phase CLXV, Phase CLXVI, Phase CLXVII, Phase CLXVIII, Phase CLXIX, Phase CLXX, Phase CLXXI, Phase CLXXII, Phase CLXXIII, Phase CLXXIV, Phase CLXXV, Phase CLXXVI, Phase CLXXVII, Phase CLXXVIII, Phase CLXXIX, Phase CLXXX, Phase CLXXXI, Phase CLXXXII, Phase CLXXXIII, Phase CLXXXIV, Phase CLXXXV, Phase CLXXXVI, Phase CLXXXVII, Phase CLXXXVIII, Phase CLXXXIX, Phase CXC, Phase CXCI, Phase CXCII, Phase CXCIII, Phase CXCIV, Phase CXCV, Phase CXCVI, Phase CXCVII, Phase CXCVIII, Phase CXCIX, Phase CC, Phase CCI, Phase CCII, Phase CCIII, Phase CCIV, Phase CCV, Phase CCVI, Phase CCVII, Phase CCVIII, Phase CCIX, Phase CCX, Phase CCXI, Phase CCXII, Phase CCXIII, Phase CCXIV, Phase CCXV, Phase CCXVI, Phase CCXVII, Phase CCXVIII, Phase CCXIX, Phase CCXX, Phase CCXXI, Phase CCXXII, Phase CCXXIII, Phase CCXXIV, Phase CCXXV, Phase CCXXVI, Phase CCXXVII, Phase CCXXVIII, Phase CCXXIX, Phase CCXXX, Phase CCXXXI, Phase CCXXXII, Phase CCXXXIII, Phase CCXXXIV, Phase CCXXXV, Phase CCXXXVI, Phase CCXXXVII, Phase CCXXXVIII, Phase CCXXXIX, Phase CCXL, Phase CCXLI, Phase CCXLII, Phase CCXLIII, Phase CCXLIV, Phase CCXLV, Phase CCXLVI, Phase CCXLVII, Phase CCXLVIII, Phase CCXLIX, Phase CCL, Phase CCLI, Phase CCLII, Phase CCLIII, Phase CCLIV, Phase CCLV, Phase CCLVI, Phase CCLVII, Phase CCLVIII, Phase CCLIX, Phase CCLX, Phase CCLXI, Phase CCLXII, Phase CCLXIII, Phase CCLXIV, Phase CCLXV, Phase CCLXVI, Phase CCLXVII, Phase CCLXVIII, Phase CCLXIX, Phase CCLXX, Phase CCLXXI, Phase CCLXXII, Phase CCLXXIII, Phase CCLXXIV, Phase CCLXXV, Phase CCLXXVI, Phase CCLXXVII, Phase CCLXXVIII, Phase CCLXXIX, Phase CCLXXX, Phase CCLXXXI, Phase CCLXXXII, Phase CCLXXXIII, Phase CCLXXXIV, Phase CCLXXXV, Phase CCLXXXVI, Phase CCLXXXVII, Phase CCLXXXVIII, Phase CCLXXXIX, Phase CCXC, Phase CCXCI, Phase CCXCII, Phase CCXCIII, Phase CCXCIV, Phase CCXCV, Phase CCXCVI, Phase CCXCVII, Phase CCXCVIII, Phase CCXCIX, Phase CCC, Phase CCCI, Phase CCCII, Phase CCCIII, Phase CCCIV, Phase CCCV, Phase CCCVI, Phase CCCVII, Phase CCCVIII, Phase CCCIX, Phase CCCX, Phase CCCXI, Phase CCCXII, Phase CCCXIII, Phase CCCXIV, Phase CCCXV, Phase CCCXVI, Phase CCCXVII, Phase CCCXVIII, Phase CCCXIX, Phase CCCXX, Phase CCCXXI, Phase CCCXXII, Phase CCCXXIII, Phase CCCXXIV, Phase CCCXXV, Phase CCCXXVI, Phase CCCXXVII, Phase CCCXXVIII, Phase CCCXXIX, Phase CCCXXX, Phase CCCXXXI, Phase CCCXXXII, Phase CCCXXXIII, Phase CCCXXXIV, Phase CCCXXXV, Phase CCCXXXVI, Phase CCCXXXVII, Phase CCCXXXVIII, Phase CCCXXXIX, Phase CCCXL, Phase CCCXLI, Phase CCCXLII, Phase CCCXLIII, Phase CCCXLIV, Phase CCCXLV, Phase CCCXLVI, Phase CCCXLVII, Phase CCCXLVIII, Phase CCCXLIX, Phase CCCL, Phase CCCLI, Phase CCCLII, Phase CCCLIII, Phase CCCLIV, Phase CCCLV, Phase CCCLVI, Phase CCCLVII, Phase CCCLVIII, Phase CCCLIX, Phase CCCLX, Phase CCCLXI, Phase CCCLXII, Phase CCCLXIII, Phase CCCLXIV, Phase CCCLXV, Phase CCCLXVI, Phase CCCLXVII, Phase CCCLXVIII, Phase CCCLXIX, Phase CCCLXX, Phase CCCLXXI, Phase CCCLXXII, Phase CCCLXXIII, Phase CCCLXXIV, Phase CCCLXXV, Phase CCCLXXVI, Phase CCCLXXVII, Phase CCCLXXVIII, Phase CCCLXXIX, Phase CCCLXXX, Phase CCCLXXXI, Phase CCCLXXXII, Phase CCCLXXXIII, Phase CCCLXXXIV, Phase CCCLXXXV, Phase CCCLXXXVI, Phase CCCLXXXVII, Phase CCCLXXXVIII, Phase CCCLXXXIX, Phase CCCXC, Phase CCCXCI, Phase CCCXCII, Phase CCCXCIII, Phase CCCXCIV, Phase CCCXCV, Phase CCCXCVI, Phase CCCXCVII, Phase CCCXCVIII, Phase CCCXCIX, Phase CCCC, Phase CCCCI, Phase CCCCII, Phase CCCCIII, Phase CCCCIV, Phase CCCCV, Phase CCCCVI, Phase CCCCVII, Phase CCCCVIII, Phase CCCCIX, Phase CCCCX, Phase CCCCXI, Phase CCCCXII, Phase CCCCXIII, Phase CCCCXIV, Phase CCCCXV, Phase CCCCXVI, Phase CCCCXVII, Phase CCCCXVIII, Phase CCCCXIX, Phase CCCCXX, Phase CCCCXXI, Phase CCCCXXII, Phase CCCCXXIII, Phase CCCCXXIV, Phase CCCCXXV, Phase CCCCXXVI, Phase CCCCXXVII, Phase CCCCXXVIII, Phase CCCCXXIX, Phase CCCCXXX, Phase CCCCXXXI, Phase CCCCXXXII, Phase CCCCXXXIII, Phase CCCCXXXIV, Phase CCCCXXXV, Phase CCCCXXXVI, Phase CCCCXXXVII, Phase CCCCXXXVIII, Phase CCCCXXXIX, Phase CCCCXL, Phase CCCCXLI, Phase CCCCXLII, Phase CCCCXLIII, Phase CCCCXLIV, Phase CCCCXLV, Phase CCCCXLVI, Phase CCCCXLVII, Phase CCCCXLVIII, Phase CCCCXLIX, Phase CCCCL, Phase CCCCLI, Phase CCCCLII, Phase CCCCLIII, Phase CCCCLIV, Phase CCCCLV, Phase CCCCLVI, Phase CCCCLVII, Phase CCCCLVIII, Phase CCCCLIX, Phase CCCCLX, Phase CCCCLXI, Phase CCCCLXII, Phase CCCCLXIII, Phase CCCCLXIV, Phase CCCCLXV, Phase CCCCLXVI, Phase CCCCLXVII, Phase CCCCLXVIII, Phase CCCCLXIX, Phase CCCCLXX, Phase CCCCLXXI, Phase CCCCLXXII, Phase CCCCLXXIII, Phase CCCCLXXIV, Phase CCCCLXXV, Phase CCCCLXXVI, Phase CCCCLXXVII, Phase CCCCLXXVIII, Phase CCCCLXXIX, Phase CCCCLXXX, Phase CCCCLXXXI, Phase CCCCLXXXII, Phase CCCCLXXXIII, Phase CCCCLXXXIV, Phase CCCCLXXXV, Phase CCCCLXXXVI, Phase CCCCLXXXVII, Phase CCCCLXXXVIII, Phase CCCCLXXXIX, Phase CCCCXC, Phase CCCCXCI, Phase CCCCXCII, Phase CCCCXCIII, Phase CCCCXCIV, Phase CCCCXCV, Phase CCCCXCVI, Phase CCCCXCVII, Phase CCCCXCVIII, Phase CCCCXCIX, Phase CCCCC, Phase CCCCCI, Phase CCCCCII, Phase CCCCCIII, Phase CCCCCIV, Phase CCCCCV, Phase CCCCCVI, Phase CCCCCVII, Phase CCCCCVIII, Phase CCCCCIX, Phase CCCCCX, Phase CCCCCXI, Phase CCCCCXII, Phase CCCCCXIII, Phase CCCCCXIV, Phase CCCCCXV, Phase CCCCCXVI, Phase CCCCCXVII, Phase CCCCCXVIII, Phase CCCCCXIX, Phase CCCCCXX, Phase CCCCCXXI, Phase CCCCCXXII, Phase CCCCCXXIII, Phase CCCCCXXIV, Phase CCCCCXXV, Phase CCCCCXXVI, Phase CCCCCXXVII, Phase CCCCCXXVIII, Phase CCCCCXXIX, Phase CCCCCXXX, Phase CCCCCXXXI, Phase CCCCCXXXII, Phase CCCCCXXXIII, Phase CCCCCXXXIV, Phase CCCCCXXXV, Phase CCCCCXXXVI, Phase CCCCCXXXVII, Phase CCCCCXXXVIII, Phase CCCCCXXXIX, Phase CCCCCXL, Phase CCCCCXLI, Phase CCCCCXLII, Phase CCCCCXLIII, Phase CCCCCXLIV, Phase CCCCCXLV, Phase CCCCCXLVI, Phase CCCCCXLVII, Phase CCCCCXLVIII, Phase CCCCCXLIX, Phase CCCCCL, Phase CCCCCLI, Phase CCCCCLII, Phase CCCCCLIII, Phase CCCCCLIV, Phase CCCCCLV, Phase CCCCCLVI, Phase CCCCCLVII, Phase CCCCCLVIII, Phase CCCCCLIX, Phase CCCCCLX, Phase CCCCCLXI, Phase CCCCCLXII, Phase CCCCCLXIII, Phase CCCCCLXIV, Phase CCCCCLXV, Phase CCCCCLXVI, Phase CCCCCLXVII, Phase CCCCCLXVIII, Phase CCCCCLXIX, Phase CCCCCLXX, Phase CCCCCLXXI, Phase CCCCCLXXII, Phase CCCCCLXXIII, Phase CCCCCLXXIV, Phase CCCCCLXXV, Phase CCCCCLXXVI, Phase CCCCCLXXVII, Phase CCCCCLXXVIII, Phase CCCCCLXXIX, Phase CCCCCLXXX, Phase CCCCCLXXXI, Phase CCCCCLXXXII, Phase CCCCCLXXXIII, Phase CCCCCLXXXIV, Phase CCCCCLXXXV, Phase CCCCCLXXXVI, Phase CCCCCLXXXVII, Phase CCCCCLXXXVIII, Phase CCCCCLXXXIX, Phase CCCCCXC, Phase CCCCCXCI, Phase CCCCCXCII, Phase CCCCCXCIII, Phase CCCCCXCIV, Phase CCCCCXCV, Phase CCCCCXCVI, Phase CCCCCXCVII, Phase CCCCCXCVIII, Phase CCCCCXCIX, Phase CCCCCC, Phase CCCCCCI, Phase CCCCCCII, Phase CCCCCCIII, Phase CCCCCCIV, Phase CCCCCCV, Phase CCCCCCVI, Phase CCCCCCVII, Phase CCCCCCVIII, Phase CCCCCCIX, Phase CCCCCCX, Phase CCCCCCXI, Phase CCCCCCXII, Phase CCCCCCXIII, Phase CCCCCCXIV, Phase CCCCCCXV, Phase CCCCCCXVI, Phase CCCCCCXVII, Phase CCCCCCXVIII, Phase CCCCCCXIX, Phase CCCCCCXX, Phase CCCCCCXXI, Phase CCCCCCXXII, Phase CCCCCCXXIII, Phase CCCCCCXXIV, Phase CCCCCCXXV, Phase CCCCCCXXVI, Phase CCCCCCXXVII, Phase CCCCCCXXVIII, Phase CCCCCCXXIX, Phase CCCCCCXXX, Phase CCCCCCXXXI, Phase CCCCCCXXXII, Phase CCCCCCXXXIII, Phase CCCCCCXXXIV, Phase CCCCCCXXXV, Phase CCCCCCXXXVI, Phase CCCCCCXXXVII, Phase CCCCCCXXXVIII, Phase CCCCCCXXXIX, Phase CCCCCCXL, Phase CCCCCCXLI, Phase CCCCCCXLII, Phase CCCCCCXLIII, Phase CCCCCCXLIV, Phase CCCCCCXLV, Phase CCCCCCXLVI, Phase CCCCCCXLVII, Phase CCCCCCXLVIII, Phase CCCCCCXLIX, Phase CCCCCCL, Phase CCCCCCLI, Phase CCCCCCLII, Phase CCCCCCLIII, Phase CCCCCCLIV, Phase CCCCCCLV, Phase CCCCCCLVI, Phase CCCCCCLVII, Phase CCCCCCLVIII, Phase CCCCCCLIX, Phase CCCCCCLX, Phase CCCCCCLXI, Phase CCCCCCLXII, Phase CCCCCCLXIII, Phase CCCCCCLXIV, Phase CCCCCCLXV, Phase CCCCCCLXVI, Phase CCCCCCLXVII, Phase CCCCCCLXVIII, Phase CCCCCCLXIX, Phase CCCCCCLXX, Phase CCCCCCLXXI, Phase CCCCCCLXXII, Phase CCCCCCLXXIII, Phase CCCCCCLXXIV, Phase CCCCCCLXXV, Phase CCCCCCLXXVI, Phase CCCCCCLXXVII, Phase CCCCCCLXXVIII, Phase CCCCCCLXXIX, Phase CCCCCCLXXX, Phase CCCCCCLXXXI, Phase CCCCCCLXXXII, Phase CCCCCCLXXXIII, Phase CCCCCCLXXXIV, Phase CCCCCCLXXXV, Phase CCCCCCLXXXVI, Phase CCCCCCLXXXVII, Phase CCCCCCLXXXVIII, Phase CCCCCCLXXXIX, Phase CCCCCCXC, Phase CCCCCCXCI, Phase CCCCCCXCII, Phase CCCCCCXCIII, Phase CCCCCCXCIV, Phase CCCCCCXCV, Phase CCCCCCXCVI, Phase CCCCCCXCVII, Phase CCCCCCXCVIII, Phase CCCCCCXCIX, Phase CCCCCCC, Phase CCCCCCCI, Phase CCCCCCCII, Phase CCCCCCCIII, Phase CCCCCCCIV, Phase CCCCCCCV, Phase CCCCCCCVI, Phase CCCCCCCVII, Phase CCCCCCCVIII, Phase CCCCCCCIX, Phase CCCCCCCX, Phase CCCCCCCXI, Phase CCCCCCCXII, Phase CCCCCCCXIII, Phase CCCCCCCXIV, Phase CCCCCCCXV, Phase CCCCCCCXVI, Phase CCCCCCCXVII, Phase CCCCCCCXVIII, Phase CCCCCCCXIX, Phase CCCCCCCXX, Phase CCCCCCCXXI, Phase CCCCCCCXXII, Phase CCCCCCCXXIII, Phase CCCCCCCXXIV, Phase CCCCCCCXXV, Phase CCCCCCCXXVI, Phase CCCCCCCXXVII, Phase CCCCCCCXXVIII, Phase CCCCCCCXXIX, Phase CCCCCCCXXX, Phase CCCCCCCXXXI, Phase CCCCCCCXXXII, Phase CCCCCCCXXXIII, Phase CCCCCCCXXXIV, Phase CCCCCCCXXXV, Phase CCCCCCCXXXVI, Phase CCCCCCCXXXVII, Phase CCCCCCCXXXVIII, Phase CCCCCCCXXXIX, Phase CCCCCCCXL, Phase CCCCCCCXLI, Phase CCCCCCCXLII, Phase CCCCCCCXLIII, Phase CCCCCCCXLIV, Phase CCCCCCCXLV, Phase CCCCCCCXLVI, Phase CCCCCCCXLVII, Phase CCCCCCCXLVIII, Phase CCCCCCCXLIX, Phase CCCCCCCL, Phase CCCCCCCLI, Phase CCCCCCCLII, Phase CCCCCCCLIII, Phase CCCCCCCLIV, Phase CCCCCCCLV, Phase CCCCCCCLVI, Phase CCCCCCCLVII, Phase CCCCCCCLVIII, Phase CCCCCCCLIX, Phase CCCCCCCLX, Phase CCCCCCCLXI, Phase CCCCCCCLXII, Phase CCCCCCCLXIII, Phase CCCCCCCLXIV, Phase CCCCCCCLXV, Phase CCCCCCCLXVI, Phase CCCCCCCLXVII, Phase CCCCCCCLXVIII, Phase CCCCCCCLXIX, Phase CCCCCCCLXX, Phase CCCCCCCLXXI, Phase CCCCCCCLXXII, Phase CCCCCCCLXXIII, Phase CCCCCCCLXXIV, Phase CCCCCCCLXXV, Phase CCCCCCCLXXVI, Phase CCCCCCCLXXVII, Phase CCCCCCCLXXVIII, Phase CCCCCCCLXXIX, Phase CCCCCCCLXXX, Phase CCCCCCCLXXXI, Phase CCCCCCCLXXXII, Phase CCCCCCCLXXXIII, Phase CCCCCCCLXXXIV, Phase CCCCCCCLXXXV, Phase CCCCCCCLXXXVI, Phase CCCCCCCLXXXVII, Phase CCCCCCCLXXXVIII, Phase CCCCCCCLXXXIX, Phase CCCCCCCXC, Phase CCCCCCCXCI, Phase CCCCCCCXCII, Phase CCCCCCCXCIII, Phase CCCCCCCXCIV, Phase CCCCCCCXCV, Phase CCCCCCCXCVI, Phase CCCCCCCXCVII, Phase CCCCCCCXCVIII, Phase CCCCCCCXCIX, Phase CCCCCCCC, Phase CCCCCCCCI, Phase CCCCCCCCII, Phase CCCCCCCCIII, Phase CCCCCCCCIV, Phase CCCCCCCCV, Phase CCCCCCCCVI, Phase CCCCCCCCVII, Phase CCCCCCCCVIII, Phase CCCCCCCCIX, Phase CCCCCCCCX, Phase CCCCCCCCXI, Phase CCCCCCCCXII, Phase CCCCCCCCXIII, Phase CCCCCCCCXIV, Phase CCCCCCCCXV, Phase CCCCCCCCXVI, Phase CCCCCCCCXVII, Phase CCCCCCCCXVIII, Phase CCCCCCCCXIX, Phase CCCCCCCCXX, Phase CCCCCCCCXXI, Phase CCCCCCCCXXII, Phase CCCCCCCCXXIII, Phase CCCCCCCCXXIV, Phase CCCCCCCCXXV, Phase CCCCCCCCX

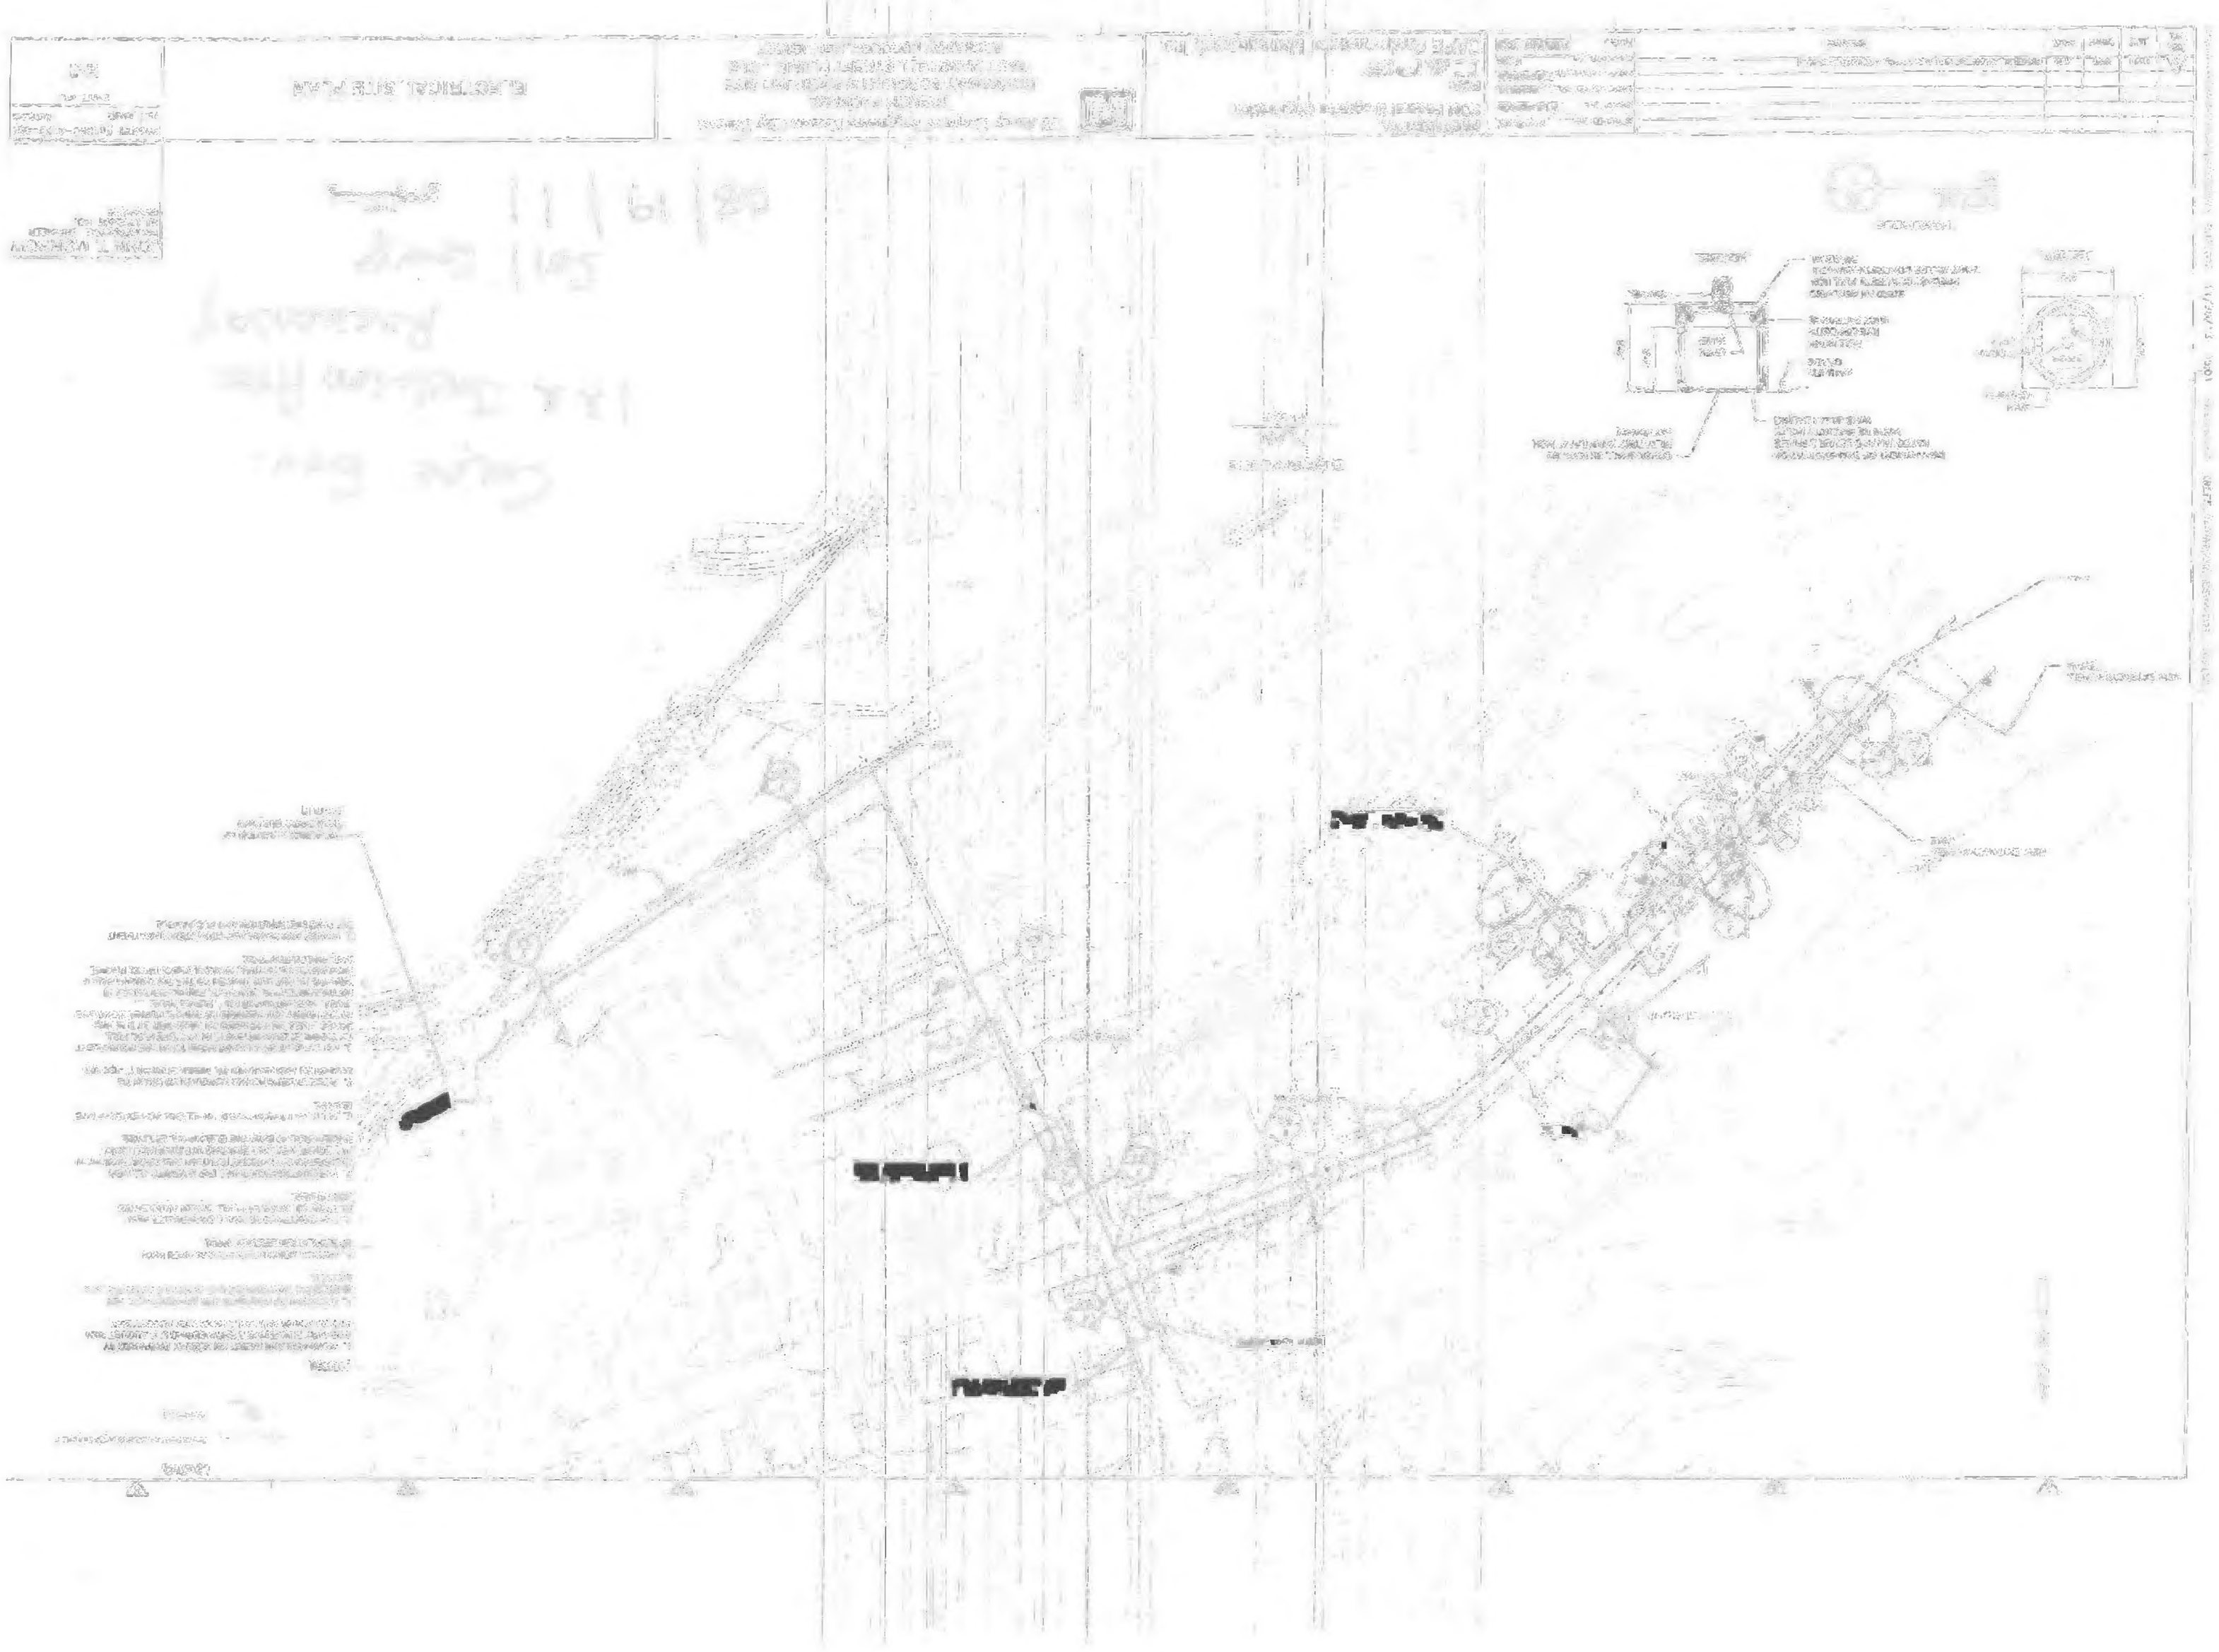

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 544-ATUL
(908) 754-8383
Fax: (908) 754-8633

NJDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSCorp.com

ASPHALT COMPACTION TEST REPORT

☒ As per ASTM D-2950-91 (Nuclear Density Gauge)

CLIENT :	Cape Environmental Inc. 48 Pine Street, Suite 110 Rockaway, NJ 07866	DATE :	8/18/2011
		FILE NO. :	ANX – 1748
	Attn. Mr. Paul Ferroni	REPORT # :	06
PROJECT :	Rockaway Borough Superfund Site 122 Jackson Avenue Rockaway, NJ	ENGINEER :	Kisher Bori
		TIME :	7:00 a.m. – 3:30 p.m.

CERTIFICATE OF INSPECTION

As per your request asphalt compaction tests were performed at the above referenced project site on 08/18/2011.

	#	DENSITY (LB/CU FT)			#	DENSITY (LB/CU FT)	
TEST NO.	LOCATION ELEVATION	FIELD	COMPACTION (%)	TEST NO.	LOCATION ELEVATION	FIELD	COMPACTION (%)
± 2" Top Course (1-5) Material				±3" Base Course (1-2) Material			
1	-	148.8	94.5	1A	-	148.8	94.5
2	-	148.3	93.1	2A	-	148.5	93.8
3	-	148.8	94.0	3A	-	148.2	94.1
4	-	149.7	95.0				
5	-	149.4	95.5				
6	-	146.9	92.5				
TROXLER # 22 DS1 OF DS-2956 DS2 OF MS-2005							

Remarks :

1 A Marshall number of 162.2 lb/ft³ and A of Rice number 157.7 lb/ft³ was provided by the Client.
A Rice number of 157.7lb/ft³ was utilized for test # 1 to 6. (Top course - 1-5 material).

2 A Marshall number of 154.4 lb/ft³ and A of Rice number 152.1 lb/ft³ was provided by the Client.
A Rice number of 152.1lb/ft³ was utilized for test # 1A to 3A. (Base course 1 – 2 material).

Temperature 295°F - 1st load - (1-5) material, Temperature 295°F - 2nd load - (1-5) material, Temperature 297°F - 3rd Load - (1-5) material and Temperature 290° - 4th Load - (1 - 5) material.
Temperature 295°F - 1st load - (1-2) material, Temperature 292°F - 2nd load - (1-2) material and Temperature 298°F - 3rd load - (1-2) material.

Location/Elevation : See attached sketch.

Specification Requirements : 92% to 98% of the Rice Density.

☒ Complied With : Test # 1 – 6 and 1A – 3A.

☐ Not Complied With :

☒ Sliding block covering the source rod was checked before placing the gauge in the storage box.

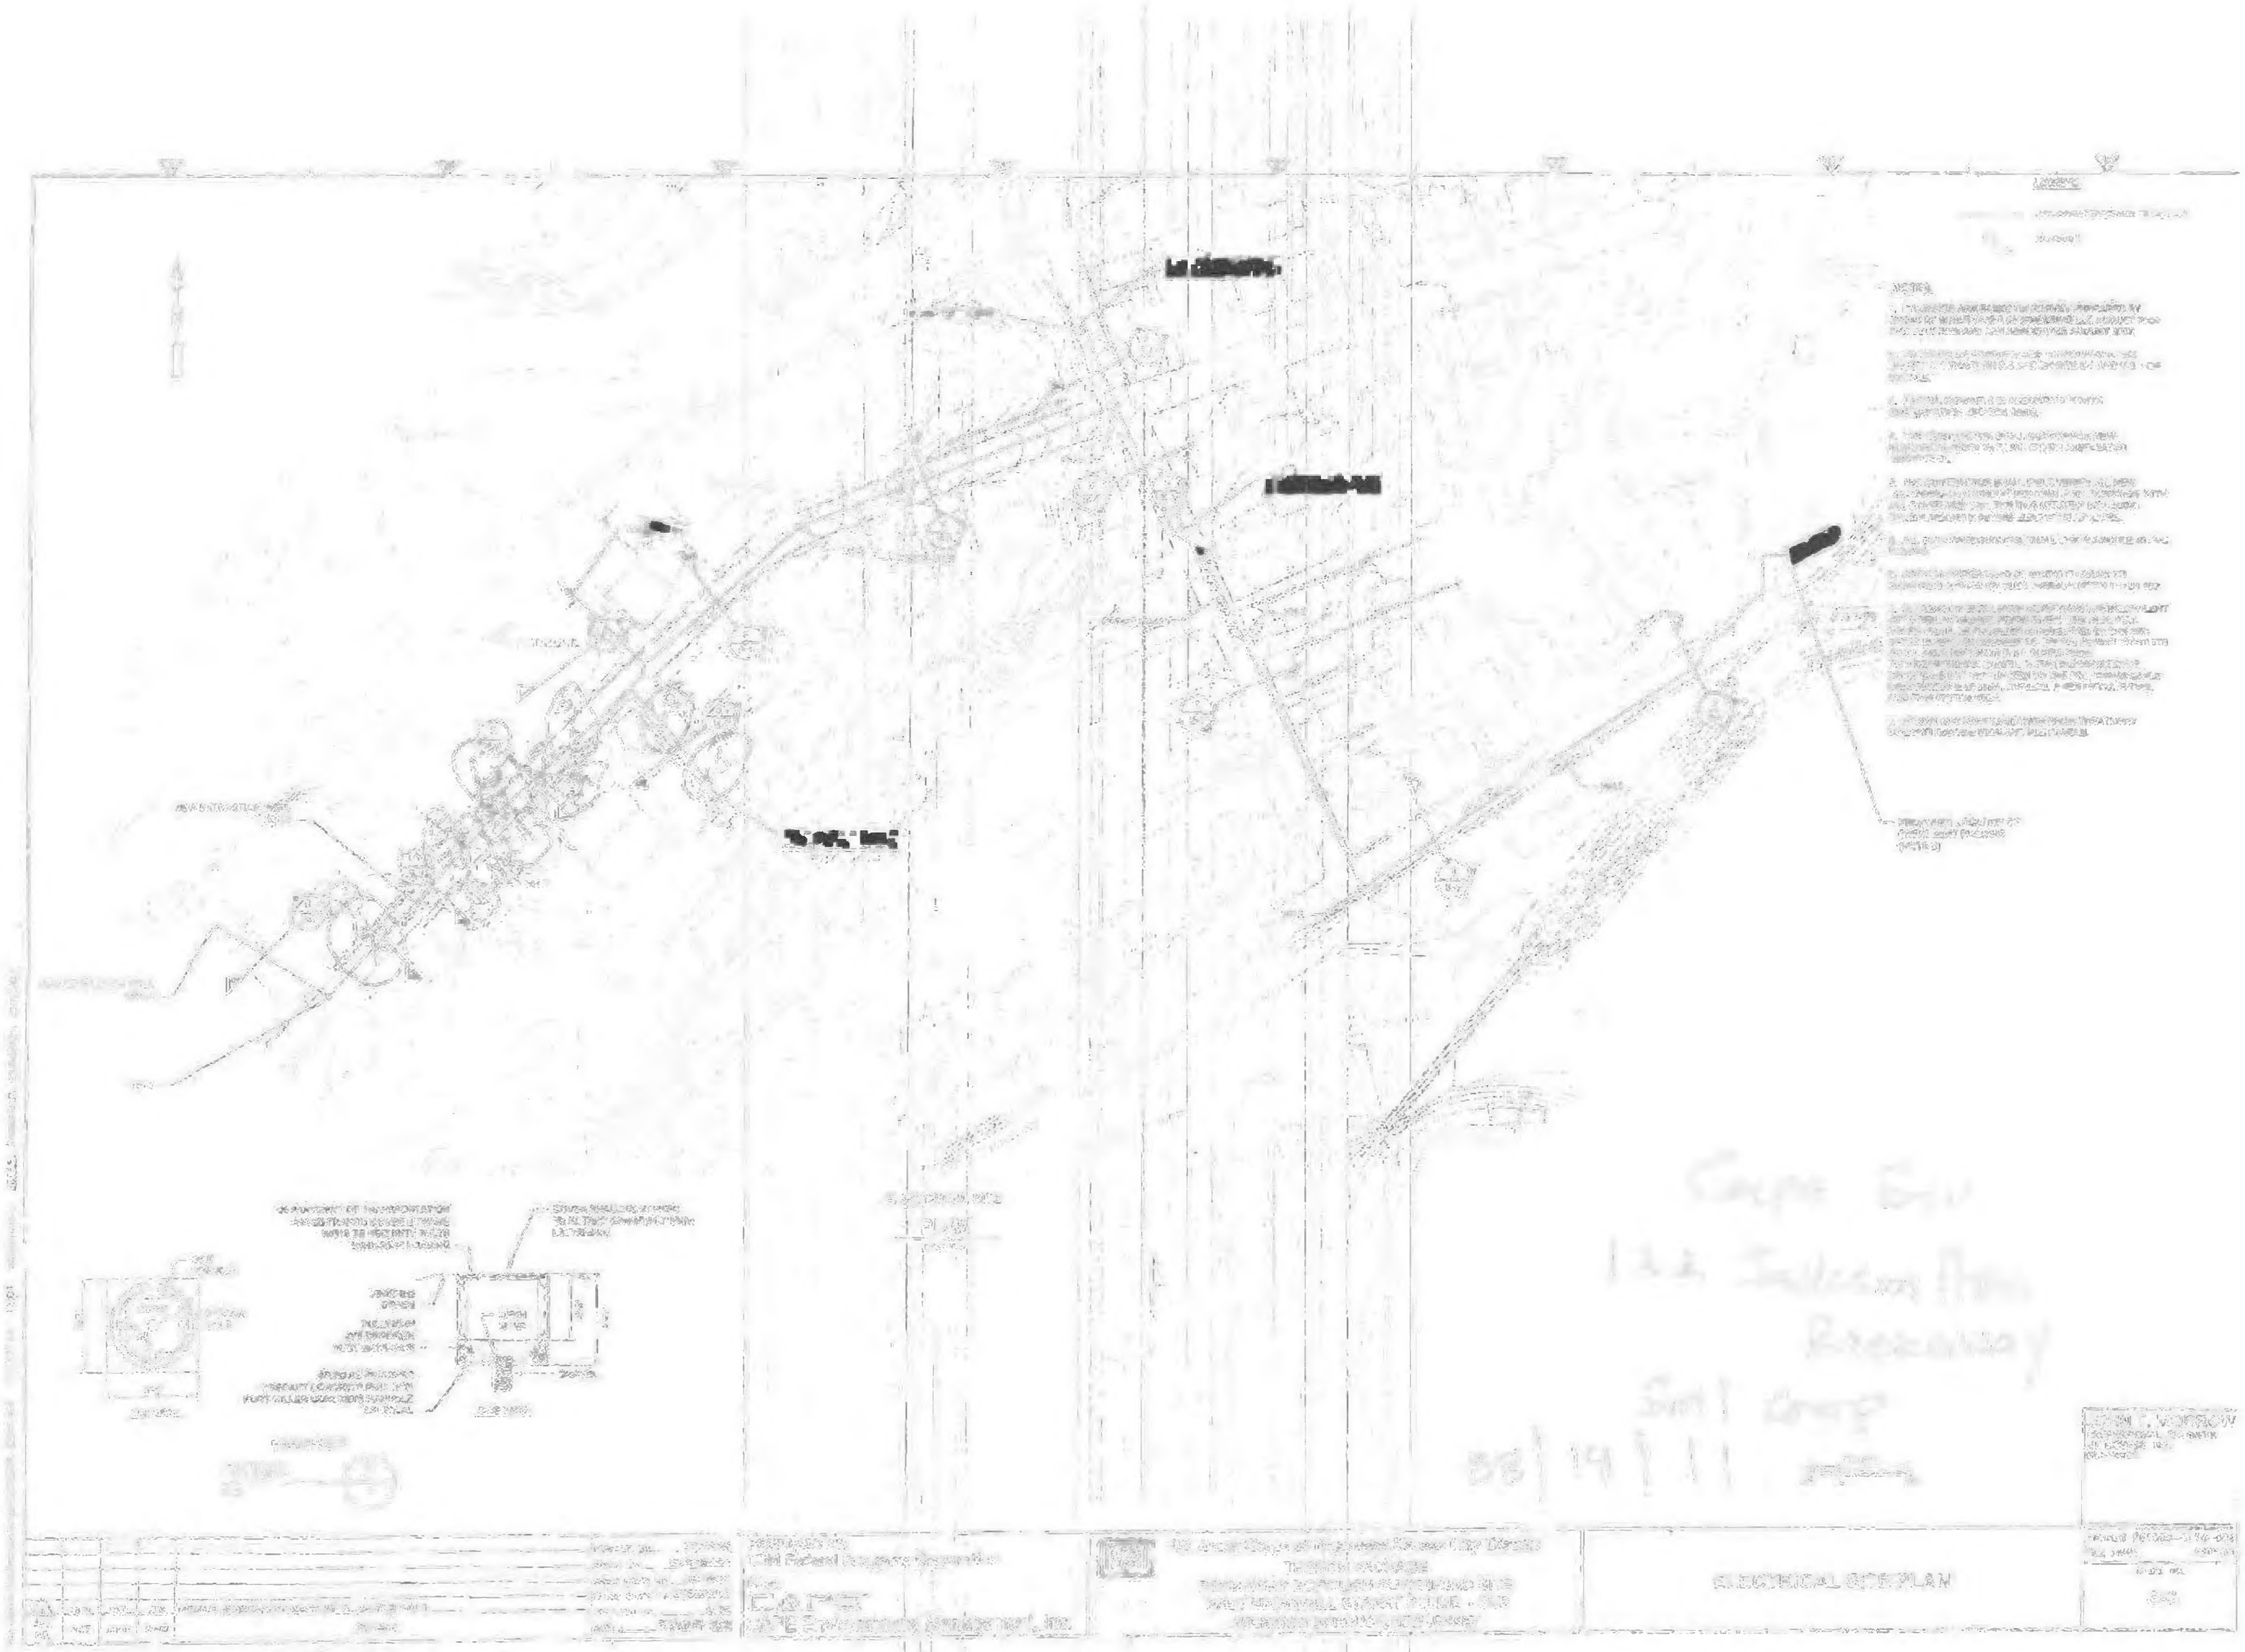
ELECTRICAL SITE PLAN

CONSULTANTS, INC.
4403 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 345-ATLC
(908) 754-8383
Fax: (908) 754-8633

NJ EDA Approved Testing Laboratory • AASHTOre Certified • NJ DEP Certified
www.ANSconsultants.com

Soil Density, Asphalt Compaction, Nuclear Gauge Calibration, Soil Boring, Sampling, Laboratory Testing, Concrete, Masonry, Steel Inspection

ASPHALT COMPACTION TEST REPORT

☒ As per ASTM D-2950-91 (Nuclear Density Gauge)

CLIENT : Cape Environmental Inc.
48 Pine Street, Suite 110
Rockaway, NJ 07866

Attn. Mr. Paul Ferroni

PROJECT : Rockaway Borough Superfund Site
122 Jackson Avenue
Rockaway, NJ

DATE : 8/18/2011

FILE NO. : ANX- 1745

REPORT # : 08

ENGINEER : Kishor Soni

TIME : 7:00 a.m. - 3:30 p.m.

CERTIFICATE OF INSPECTION

As per your request asphalt compaction tests were performed at the above referenced project site on 08/18/2011

	**	DENSITY (LB/CU FT)			*	DENSITY (LB/CU FT)	
TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)	TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)
±1" Top Course (1 - 5) Material				±3" Base Course (1-2) Material			
1	-	145.8	92.1	1A	-	146.3	92.4
2	-	146.8	92.7	2A	-	148.9	94.0
3	-	146.0	92.2	3A	-	148.4	93.7
4	-	146.7	92.6				
5	-	146.4	92.5				
6	-	145.8	92.1				
TROXLER # 22 DS/ OF 3N-6553 DS2 OF VS-2065							

Remarks :

1 A Marshall number of 152.2 lb./ft.³ and A of Rice number 157.7lb./ft.³ was provided by the Client. A Rice number of 157.7lb./ft.³ was utilized for test # 1 to 6. (Top course - 1-5 material).

2 A Marshall number of 154.4 lb./ft.³ and A of Rice number 158.1lb./ft.³ was provided by the Client. A Rice number of 158.1lb./ft.³ was utilized for test # 1A to 3A. (Base course 1 - 2 material).

Temperature 295°F - 1st load - (1-5) material, Temperature 285°F - 2nd load - (1-5) material, Temperature 287°F 3rd load - (1-5) material and Temperature 290° - 4th Load - (1 - 5) material.
Temperature 290°F - 1st load - (1-2) material, Temperature 282°F - 2nd load - (1-2) material and Temperature 285°F - 3rd load - (1-2) material.

Location/Elevation : See attached sketch.

Specification Requirements : 92% to 98% of the Rice Density.

☒ Complied With : Test # 1 - 6 and 1A - 3A.

☐ Not Complied With :

☒ Sliding block covering the source rod was checked before placing the gauge in the storage box.

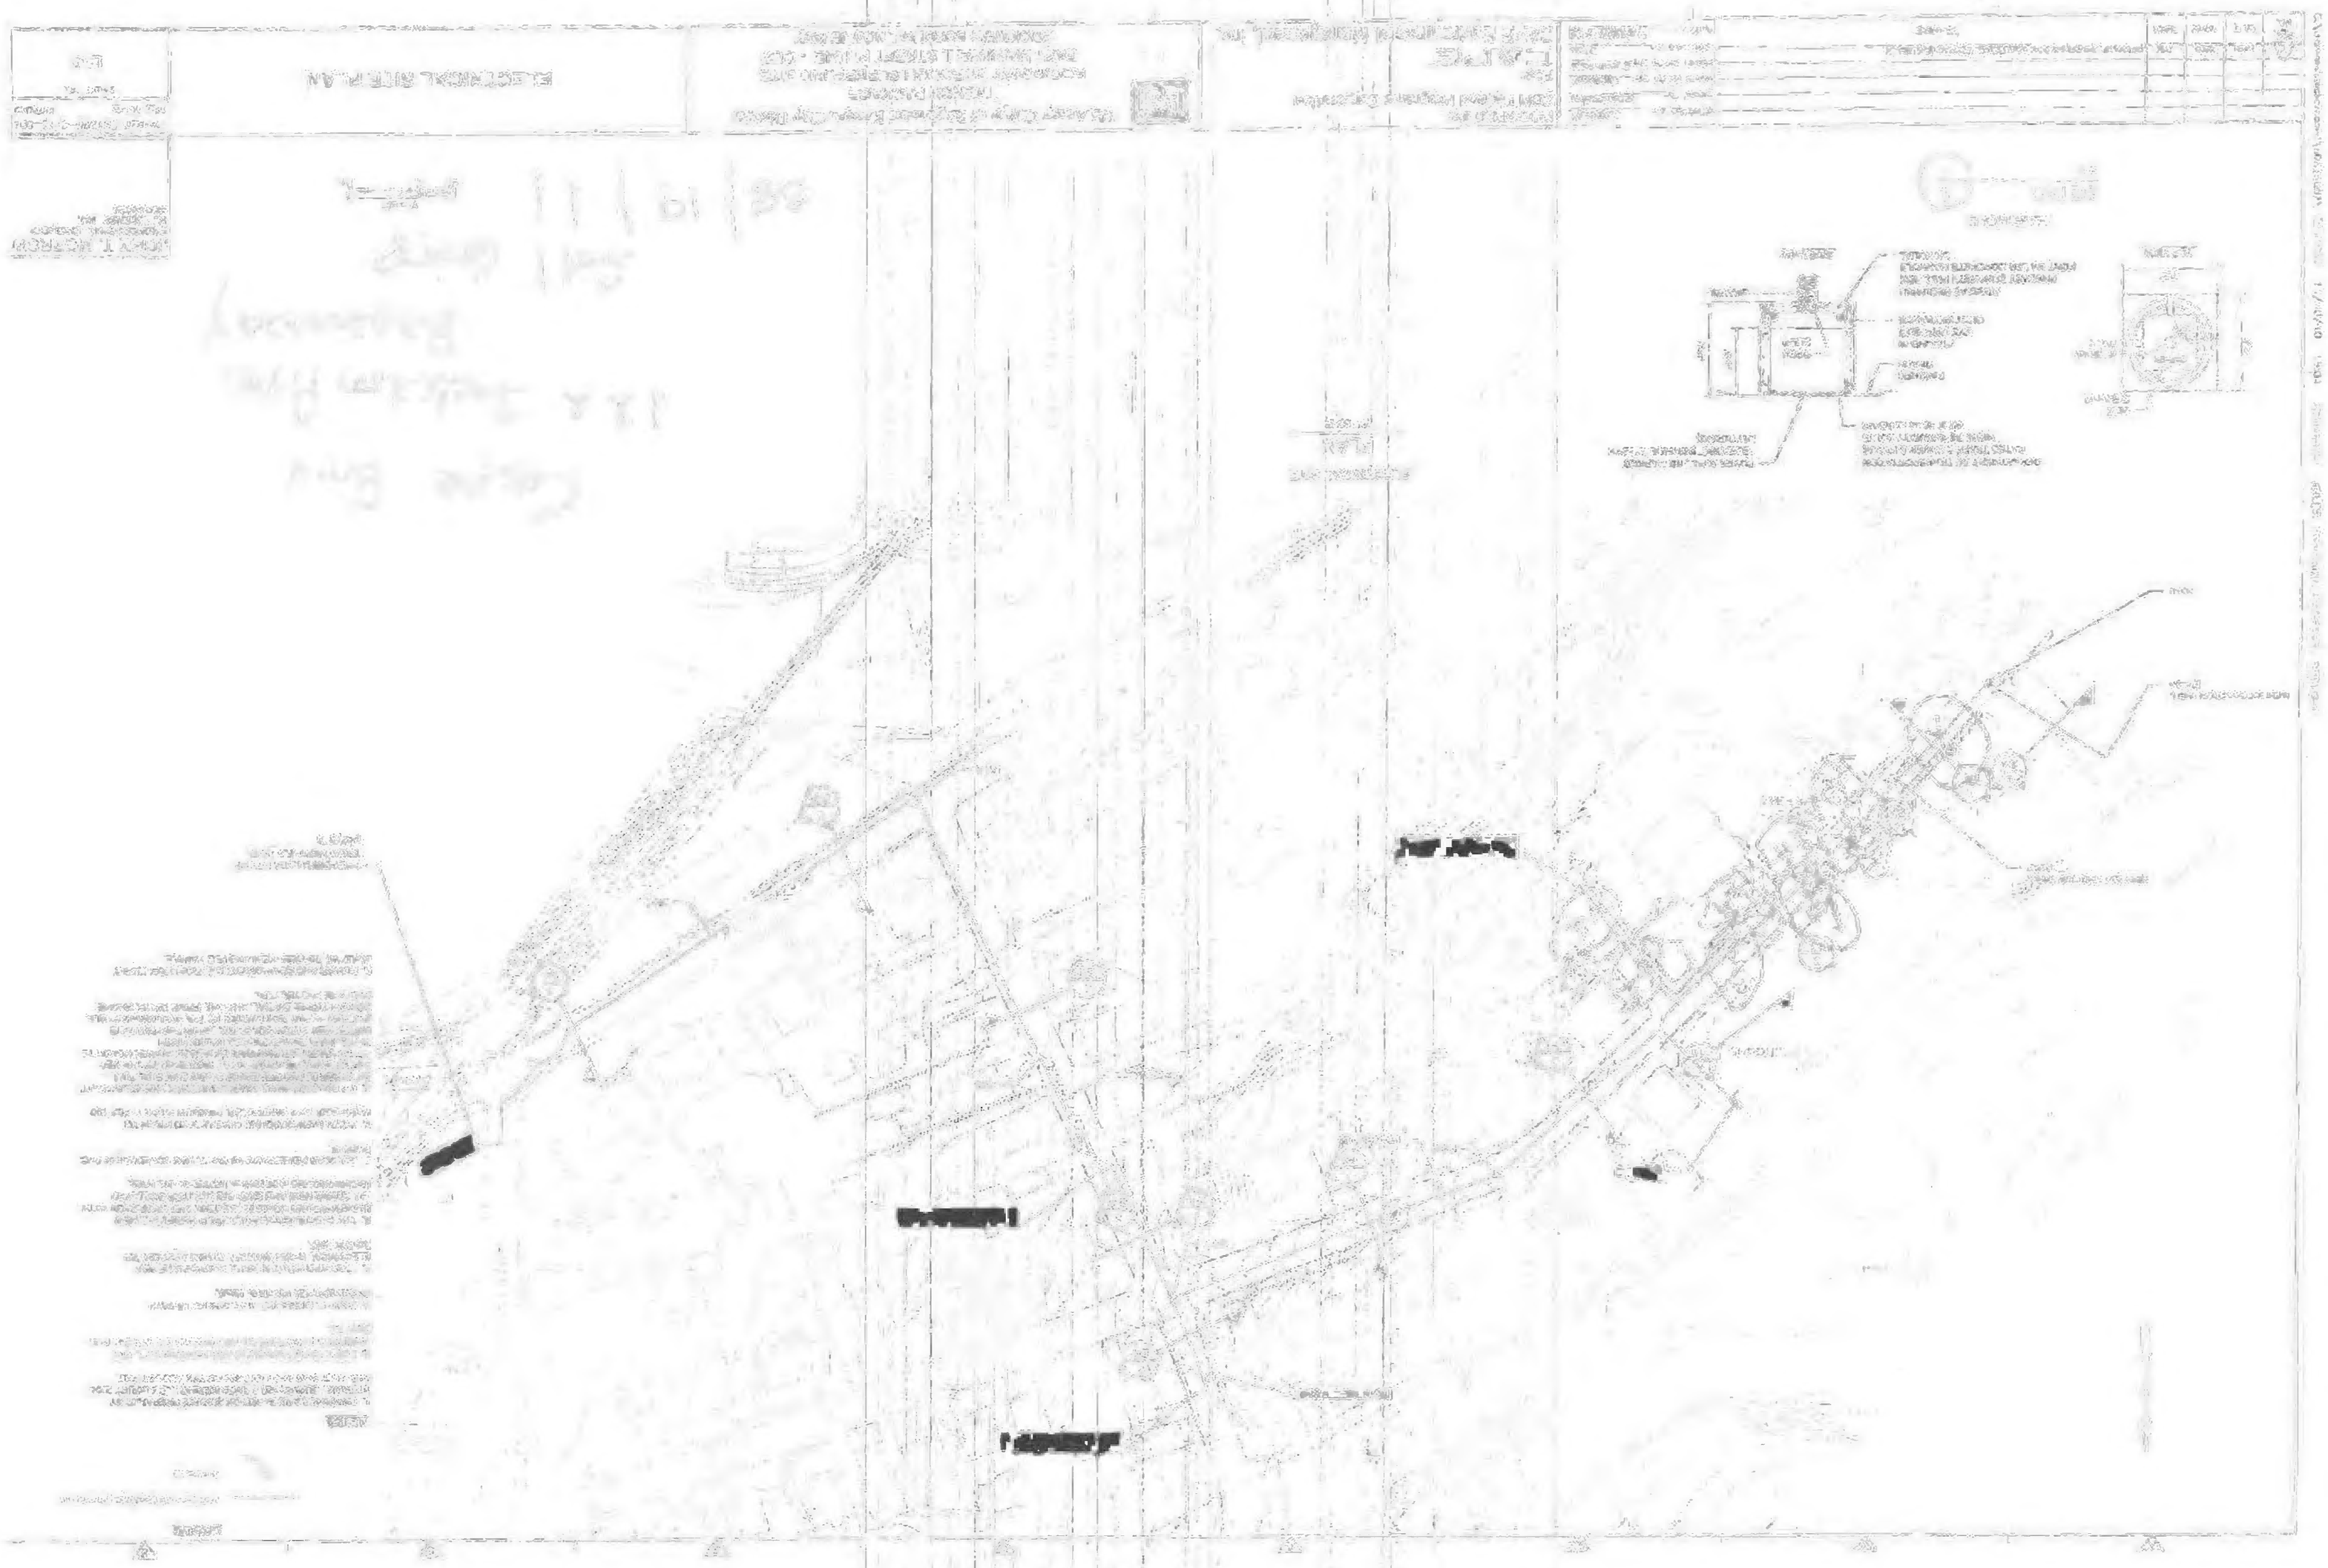

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATUL
(908) 754-8383
Fax: (908) 754-8633

NJ DOA Accredited Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSconsultants.net

All reports, work product, data, documentation, notes, instruments, analysis, drawings, or other deliverables, or portions thereof, shall remain the property of ANS Consultants, Inc. and shall be returned upon request.

ASPHALT COMPACTION TEST REPORT

☒ As per ASTM D-2950-91 (Nuclear Density Gauge)

CLIENT : Cape Environmental Inc.
45 Pine Street, Suite 110
Rockaway, NJ 07866

Attn. Mr. Paul Ferroni

PROJECT : Rockaway Borough Superfund Site
122 Jackson Avenue
Rockaway, NJ

DATE : 8/22/2011

FILE NO. : ANX - 1743

REPORT # : 08

ENGINEER : Kishor Soni

TIME : 7:00 a.m. - 4:30 p.m.

CERTIFICATE OF INSPECTION

As per your request asphalt compaction tests were performed at the above referenced project site on 08/22/2011

	*	DENSITY (LB./CU. FT)			*	DENSITY (LB./CU. FT)	
TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)	TEST NO.	LOCATION/ ELEVATION	FIELD	COMPACTION (%)
±3" Base Course				±2" Top Course			
1	-	150.0	92.2	1	-	150.1	92.7
2	-	150.7	92.6	2	-	150.3	92.5
3	-	150.1	92.3	3	-	149.2	91.7
4	-	150.3	92.5	4	-	150.2	92.3
5	-	149.4	91.8	5	-	150.4	92.4
6	-	149.2	92.3	12	-	149.3	92.3
TROXLER # 32 DS1 OF DS - 2183 DS2 OF WS - 1588							

Remarks :

1. A Marshall number of 152.5 lb./ft.³ and A of Rice number 150.6lb./ft.³ was provided by the Client. A Rice number of 150.6lb./ft.³ was utilized for test # 1 to 6. (Base course - ±3 inches).

2. A Marshall number of 152.0 lb./ft.³ and A of Rice number 150.2lb./ft.³ was provided by the Client. A Rice number of 150.2lb./ft.³ was utilized for test # 7 to 12. (Top course 1 - 2 inches).

Temperature 289°F - 1st load - (1-2) material, Temperature 287°F - 2nd load - (1-2) material, Temperature 284°F 3rd Load - (1-2) material and Temperature 287°F - 4th Load - (1 - 2) material. Temperature 285°F (1-2 material) Temperature 289°F - 1st load - (1-5) material, Temperature 284°F - 2nd load - (1-5) material and Temperature 285°F - 3rd load - (1-5) material. As per Mr. Ciorlia, Inspector do not have to check current mesh.

Location/Elevation : See attached sketch.

Specification Requirements : 92% to 98% of the Rice Density.

☒ Complied With : Test # 1 - 12

☐ Not Complied With :

☒ Sliding block covering the source rod was checked before placing the gauge in the storage box.

"ANS were is your construction inspection and testing needs"
An equal opportunity employer

Project: 123 Hickory Ave, Rockaway

Sheet: Cape Cod.

ARC CONSULTANTS, INC.
1405 South Stelton Avenue
South Plainfield, NJ 07080
908-756-2161

By: Sapis

Date: 08/22

CONSULTANTS, INC.
4485 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATUL
(908) 754-8382
Fax: (908) 754-8633

NJ EDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSConsultants.net

ASPHALT COMPACTION TEST REPORT

☒ As per ASTM D-2950-91 (Nuclear Density Gauge)

CLIENT :	Capo Environmental Inc. 48 Pine Street, Suite 110 Rockaway, NJ 07866 Attn. Mr. Paul Ferroni	DATE :	8/23/2011
		FILE NO. :	ANS - 1743
		REPORT # :	10
PROJECT :	Rockaway Borough Superfund Site 122 Jackson Avenue Rockaway, NJ	ENGINEER :	Kishor Soni
		TIME :	7:00 a.m. – 4:30 p.m.

CERTIFICATE OF INSPECTION

As per your request asphalt compaction tests were performed at the above referenced project site on 08/23/2011.

		DENSITY (LB./CU.FT)				DENSITY (LB./CU.FT)	
TEST NO.	LOCATION ELEVATION	FIELD	COMPACTION (%)	TEST NO.	LOCATION ELEVATION	FIELD	COMPACTION (%)
1	±2" @ Bldg. Base	148.2	92.1	7	±2" @ Maple (Base)	149.5	92.9
2	±2" @ Bldg. Top	148.3	92.2	8	±2" @ Maple (Top)	148.1	92.0
±3" @ 115 Jackson Ave. (Base)				±3" @ Entrance of Borough (Base)			
3		148.4	92.3	9		149.4	92.9
±2" @ 115 Jackson Ave. (Top)				±2" @ Entrance of Borough (Top)			
4		148.7	93.1	10		148.7	93.1
±3" @ 109 Jackson Ave. (Base)				11	±2" @ Maple	151.1	94.0
5		148.4	92.3	12	±2" @ Maple	147.8	92.0
±2" @ 109 Jackson Ave. (Top)							
6		147.9	92.0				
TROXLER # 22 DS1 OF DS-7004 DS2 OF MS - 2008							

Remarks :

1. A Marshall number of 154.1 lb./ft.³ and A of Rice number 151.2lb./ft.³ was provided by the Client. A Rice number of 151.2lb./ft.³ was utilized for test # 1, 3, 5, 7 & 9 (Base course - 1-2 material).

2. A Marshall number of 151.1 lb./ft.³ and A of Rice number 157.1lb./ft.³ was provided by the Client. A Rice number of 157.1lb./ft.³ was utilized for test # 2, 4, 6, 8, 10 - 12 (Top course 1 - 6 material).

Temperature 289°F - 1st load - (1-2) Base material, Temperature 290°F - 2nd load - (1-6) Top material and Temperature 280°F - 3rd Load - (7 - 9) Top material.
Inspector was told to need to check asphalt batch as informed by Mr. Oberto client representative.

Location/Elevation : See attached sketch.

Specification Requirements : 92% to 98% of the Rice Density.

☒ Complied With : Test # 1 - 12.

☐ Not Complied With :

☒ Milling block prior to the source roll was checked before placing the gauge in the storage box.

"A Winner to your construction inspection and testing needs."
ANS CONSULTANTS, INC.

Project: 123 Dickson Ave, Rockaway

Client: Cape Bryl.

AMS CONSULTANTS, INC.
[illegible]
South Plainfield, NJ 07080
(908) [illegible]

Drawn by: [illegible] | Date: [illegible] | Scale: [illegible]

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATUL
(908) 754-8383
Fax: (908) 754-8633

NJ EDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSConsultants.net

Soil Density, Proctor, Lime, Asphalt, Concrete Cores, Cylinders, Concrete Batching, Masonry, Soil Nailing, Concrete Block, Grout, Prestressed Concrete, Structural Steel, Welding, Fireproofing

FILE NO.: ANX-1743 REPORT NO.: 01 DATE: (03/04/21) PAGE NO.: 1 of 1

CLIENT: Dilps Environmental Inc., 49 Pine Street, Suite - 112, Rockaway, NJ 07866 WEATHER: Clear AIR TEMP.: 40°F

PROJECT: 122 Jackson Ave., Rockaway, NJ FINE AGG.: N/A

CONTRACTOR: Aimi Construction COARSE AGG.: N/A

CONCRETE SUPPLIER: Joel Tanis & Sons Inc CEMENT BRAND: N/A

REPORT OF CONCRETE INSPECTION AND TESTING — C-31

CLASS	4000 PSI				PSI				PLANT	FIELD
CUBIC YD.	DESIGN WEIGHT LBS	DRYER WEIGHT LBS			DESIGN WEIGHT LBS	DRYER WEIGHT LBS			PREVIOUS YARDAGE	N/A
CEMENT									YARDAGE	30.00 CU. YDS.
FINE AGG.									INSPECTED	30.00 CU. YDS.
COARSE AGG.									TOTAL TO DATE	30.00 CU. YDS.
COARSE AGG.									START	10:30 AM
WATER GALS.									FINISH	6:00 PM
ADMIX. 02./YDS.									TOTAL HRS.	6.30 Hrs.
ADMIX. 02.									INSP.	S. S. Patel

% PASSING	100	90	80	70	8	4	3/8	1/2	3/4	1	1 1/2	F.M.	% MOIST
FINE AGG.													
COARSE AGG.													
COARSE AGG.													

NO. OF CYLS. & CLASS: Seven (7) cylinders - 4000 PSI AIR CONTENT (%) (C-231): 5.0%

SLUMP (C-143): 5" DENSITY (lbs./ft.³) (C-138): 145 PC CONC. TEMP (°F) (C-1064): 68°F

LOCATION: Concrete was placed for testing for Ground Water Treatment Facilities Building

REMARK: 30 cu. yds. – 3 trucks using Joel O. Cassano Co. Supplier informed the contractor & plant plant supplier Co. different. Contractor & plant advised to use same concrete supplier A, not need test & only 160 yds. one test cylinder

CYL NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI*	CYL NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI*
1.	ANX-1743-01	Shear	7 days	48,740	3,250	7.	ANX-1743-07	Shear	3 days	44,250	2,950
2.	ANX-1743-02	Cone & Shear	7 days	38,400	4,810						
3.	ANX-1743-03		14 days								
4.	ANX-1743-04		14 days								
5.	ANX-1743-05		28 days								
6.	ANX-1743-06		28 days								

SPECIMEN (4" x 8") CYL. AREA: 12.56 SQ. IN. Test performed as per A.S.T.M. specifications ** C-39

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATUL
(908) 754-8383
Fax: (908) 754-8633

NJ EDA Approved Testing Laboratory • MBE/DBE Certified • NJ DOP Certified
www.ANSCorp.net

Air Density, Porosity, Water Permeability, Concrete Cores, Masonry, Mortar, Fire-Stopping, Roofing, Soil Testing, Concrete Curing, 28 Day Storage, Preliminary Tests & Mixes

FILE NO. : ANX-1743 REPORT NO. : 01 DATE : 08/04/2011 PAGE NO. : 1 of 1

CLIENT : Capel Environmental Inc., 48 Pine Street, Suite 410, Rockaway, NJ 07866 WEATHER : Clear AIR TEMP. : 70°F

PROJECT : 122 Jackson Ave., Rockaway, NJ FINE AGG. : N/A

CONTRACTOR : ATIE Construction COARSE AGG. : N/A

CONCRETE SUPPLIER : Joel Tanis & Sons Inc CEMENT BRAND : N/A

REPORT OF CONCRETE INSPECTION AND TESTING — C-31

CLASS	4000	PSI		PSI	PLANT	FIELD
BATCH NO.	BATCH WEIGHT LBS	BATCH WEIGHT LBS	BATCH WEIGHT LBS	BATCH WEIGHT LBS	PREVIOUS YARDAGE	N/A
CEMENT					YARDAGE	30.00 Cu. yds.
FINE AGG.					INSPECTED	30.00 Cu. yds.
COARSE AGG.					TOTAL TO DATE	30.00 Cu. yds.
COARSE AGG.					START	10:30 AM
WATER/GALS.					FINISH	5:00 PM
ADMIX. OF AEA					TOTAL HRS.	6:30 Hrs.
ADMIX. OF					INSP	B. S. Patel

% PASSING	100	50	30	16	8	4	3/8	½	3/4	1	1½	F.M.	% MOIST
FINE AGG.													
COARSE AGG.													
COARSE AGG.													

NO. OF CYL. & CLASS Seven (7) cylinders – 4000 PSI AIR CONTENT (%) (C-231) 5.0%

SLUMP (C-143) 5" DENSITY (PCF) (C-138) TARE CONC. TEMP (°F) (C-1064) 68°F

LOCATION: Concrete was placed for footing for Ground Water Treatment Facilities building

REMARK: 28 cu. yds. x 2 trucks mixed Service Concrete Inc. Supplier informed the contractor & client about supplier Co. different. Contractor & client advised to use same concrete supplier & not need test & only 150 yds. one test require.

CYL. NO.	LAB. ID NO	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI	CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI
1.	ANX-1743-01	Shear	7 days	46,740	2,968	5.	ANX-1743-07	Shear	7 days	44,220	2,920
2.	ANX-1743-02	Cone & Shear	7 days	60,420	4,870						
3.	ANX-1743-03		14 days								
4.	ANX-1743-04		14 days								
5.	ANX-1743-05		28 days								
6.	ANX-1743-06		28 days								

SPECIMEN (6" x 12") – AREA 12.56 SQ. IN. Test performed as per A.S.T.M. specifications C-39

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 546-ATLE
(908) 754-8383
Fax: (908) 754-8633

NJ SDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSConsultants.net

FILE NO. : ANX-1743 REPORT NO. : 01 DATE : 03/04/2015 PAGE NO. : 1 of 1

CLIENT : Dase Environmental Inc., 45 Pine Street, Suite - 719, Rockaway, NJ 07866 WEATHER : Clear AIR TEMP. : 48°F

PROJECT : 127, Jackson Ave., Rockaway, NJ FINE AGG. : N/A

CONTRACTOR : Alini Construction COARSE AGG. : N/A

CONCRETE SUPPLIER : Joel Tarsa & Sons Inc CEMENT BRAND : N/A

REPORT OF CONCRETE INSPECTION AND TESTING — C-31

CLASS	4000	PSI		PSI	PLANT	FIELD
CUBIC YD.	DESIGN WEIGHT LBS	ACTUAL WEIGHT LBS	DESIGN WEIGHT LBS	ACTUAL WEIGHT LBS	PREVIOUS YARDAGE	N/A
CEMENT					VARIANCE	36.00 Cu. yds.
FINE AGG.					INVOICED	36.00 Cu. yds.
COARSE AGG.					TOTAL TO DATE	36.00 Cu. yds.
COARSE AGG.					START	10 : 30 AM
WATER GALS.					FINISH	5 : 00 PM
ADMIX. OZ./LBS.					TOTAL HRS.	6 : 30 Hrs.
ADMIX. OZ.					INSP.	D. S. Patel

% PASSING	100	60	30	16	8	4	3/8	16	30	1	1/2	F.M.	% MOIST
FINE AGG.													
COARSE AGG.													
COARSE AGG.													

NO. OF CYLS. & CLASS Seven (7) cylinders - 4000 PSI AIR CONTENT (%) (C-231) 6.0%

SLUMP (C-143) 3" DENSITY (Wet) lb. (C-138) 148 lb. CONC. TEMP (°F) (C-209) 56°F

LOCATION Concrete was placed for testing for Ground Water Treatment Facilities Building.

REMARK 28 cu. yds. - 2 trucks added having Concrete Co. Supplier informed the customer & client about supplier Co. different Contractor & client advised to use same concrete supplier & not need test & only 150 yds. one test require.

CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI	CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI
1.	ANX-1743-01	Shear	7 days	48,740	3,980	2.	ANX-1743-07	Shear	7 days	54,720	4,540
3.	ANX-1743-02	Cone & Shear	7 days	60,490	4,935						
3.	ANX-1743-03		14 days								
4.	ANX-1743-04		28 days								
5.	ANX-1743-05		28 days								
6.	ANX-1743-06		28 days								

SPECIMEN: 6" x 12" CYLINDER (0.05 cu. ft.) Test performed under A.S.T.M. specifications T-22-M

CONSULTANTS, INC.
4205 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATCJ
(908) 754-8383
Fax: (908) 754-0633

NJ LDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSConsultants.com

Soil Concrete Masonry Steel Asphalt Structural Field Inspect Fire Stations Hazardous Analysis for Radio Communications Tower, IR Thermal, Submersible Tanks & Vessels

FILE NO. : ANX-1743 REPORT NO. : 01 DATE : 08/04/2011 PAGE NO. : 01 of 1

CLIENT : Cape Environmental Inc., 43 Pine Street, Suite - 110, Rockaway, NJ 07866 WEATHER : Clear AIR TEMP. : 68°F

PROJECT : 100 Jackson Ave., Rockaway, NJ FINE AGG. : N/A

CONTRACTOR : ANSI Construction COARSE AGG. : N/A

CONCRETE SUPPLIER : Joel Tanis & Sons Inc CEMENT BRAND : N/A

REPORT OF CONCRETE INSPECTION AND TESTING — C-31

CLASS	4000	PSI		PSI	PLANT	FIELD
CONCRETE	DENSITY WEIGHT LBS	DATE WEIGHT LBS	DENSITY WEIGHT LBS	DATE WEIGHT LBS	PREVIOUS YARDAGE	N/A
CEMENT					YARDAGE	30.00 Cu. yds.
FINE AGG.					INSPECTED	30.00 Cu. yds.
COARSE AGG.					TOTAL TO DATE	30.00 Cu. yds.
COARSE AGG.					START	10 : 30 AM
WATER GALS.					FINISH	3 : 00 PM
ADMIX. OZ./CSR					TOTAL HRS.	6 : 30 Hrs.
ADMIX. OZ.					NSP	B. S. Patel

% PASSING	100	90	80	10	5	4	3/8	1/2	3/4	1	1½	F.M.	% ASPHT
FINE AGG.													
COARSE AGG.													
COARSE AGG.													

NO. OF CYLS. & CLASS Seven (7) cylinders – 4000 PSI AIR CONTENT (%) (C-231) 6.0%

SLUMP (C-143) 7" DENSITY (lbs./cu. ft.) (C-138) LAB. 51 CONC. TEMP (°F) (C-1064) 65°F

LOCATION Concrete was placed for footing for Ground Water Treatment Facilities Building.

REMARK 30 cu. yds. – 2 trucks called Service Concrete Co. Supplier informed the contractor & client about supplier to different Contractor & client advised to use same concrete supplier & not need test & only 150 yds. one test require

CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI	CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI
1.	ANX-1743-01	Shear	7 days	68, 190	3, 860	7.	ANX-1743-07	Shear	9 days	46, 250	6, 325
2.	ANX-1743-02	Cone & Shear	7 days	67, 450	4, 310						
3.	ANX-1743-03	Cone	14 days	85, 500	4, 797						
4.	ANX-1743-04	Cone	14 days	84, 160	4, 700						
5.	ANX-1743-05		28 days								
6.	ANX-1743-06		28 days								

SPECIMEN (6" x 12") CYL. AREA: 28.26 SQ. IN. Test performed as per A.S.T.M. specifications

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07050

Tel: (800) 545-ATUL
(908) 754-8383
Fax: (908) 754-8633

N. EDA Approved Testing Laboratory • MRF/DRE Certified • NJ DEP Certified
www.ANSconsultants.com

Soil, Concrete, Masonry, Rock, Asphalt, Structural Steel, Welding, Fireproofing, Curtain Wall, Roofing, Concrete Cores, UT, Magnetic Particle, Penetrant, Coating Inspection

FILE NO. : ANS-1743 REPORT NO. : 01 DATE : 05/04/2011 PAGE NO. : 1 of 1

CLIENT : Dade Environmental Inc., 48 Pine Street, Suite 110, Rockaway, NJ 07866 WEATHER : Clear AIR TEMP. : 48°F

PROJECT : 165, Jackson Ave., Rockaway, NJ FINE AGG. : N/A

CONTRACTOR : Alnil Construction COARSE AGG. : N/A

CONCRETE SUPPLIER : Joe Tarla & Sons Inc CEMENT BRAND : N/A

REPORT OF CONCRETE INSPECTION AND TESTING — C-31

CLASS	4000 PSI		PSI		PLANT	MTHLD
DESIG MIX	DESIGN WEIGHT LBS	AS OF WEIGHT LBS	DESIGN WEIGHT LBS	AS OF WEIGHT LBS	REQUIRED YARDAGE	N/A
CEMENT					YARDAGE	30.00 Cu. yds.
FINE AGG.					INSPECTED	30.00 Cu. yds.
COARSE AGG.					TOTAL TO DATE	30.00 Cu. yds.
COARSE AGG.					START	10 : 30 AM
WATER GALS.					FINISH	3 : 00 PM
ADMIX. GE. ASA					TOTAL HRS.	6 : 30 Hrs.
ADMIX. W.					INSP.	H. S. Patel

% PASSING	1½	1	¾	½	⅜	4	8	16	30	50	100	200	PAN	% MOIST
FINE AGG.														
COARSE AGG.														
COARSE AGG.														

NO. OF CYLS. & CLASS Seven (7) cylinder - 4000 PSI AIR CONTENT (%) (C-231) 6.0%

SLUMP (C-143) 3" TEMPTE (C-94) 150 [illegible] CONC. TEMP (°F) (C-1064) 68°F

LOCATION Concrete was placed for footing for Ground Water Treatment Facilities Building.

REMARK 50 cu. yds. = 2 loads; noted for the concrete co. supplier informed the contractor & client about supplier is different. Contractor & client advised to use same concrete supplier & not need test & only 150 yds. one test required.

CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI	CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI
1.	ANS-1743-01	Shear	7 days	42, 740	3, 080	7.	ANS-1743-07	Shear	3 days	44, 320	3, 220
2.	ANS-1743-02	Cone & Shear	7 days	62, 420	4, 510						
3.	ANS-1743-03	Cone	14 days	66, 650	4, 797						
4.	ANS-1743-04	Cone	14 days	64, 180	4, 617						
5.	ANS-1743-05		28 days								
6.	ANS-1743-06		28 days								

SPECIMEN (4" x 8") CYL. AREA: 12.56 SQ. IN. Test performed as per ASTM specifications

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATCU
(908) 754-8383
Fax: (908) 754-8633

NJ DOA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSConsultants.net

Soils & Base Materials, Asphalt, Concrete Field Work, Mix Designs, Proportioning, Testing, Air Entry, Slump, Compressive Strength, Unit Weight, Temperature, Cylinders, Reinforced Concrete Inspection

FILE NO. : ANX-1743 REPORT NO. : 01 DATE : 08/24/2017 PAGE NO. 1 of 1

CLIENT : Cerro Environmental Inc., 45 Pine Street, Suite - 119, Rockaway, NJ 07866 WEATHER : Clear AIR TEMP. : 65°F

PROJECT : 152, Jackson Ave., Roseland, NJ FINE AGG. : N/A

CONTRACTOR : Alto Construction COARSE AGG. : N/A

CONCRETE SUPPLIER : Joel Tech & Sons Inc CEMENT BRAND : N/A

REPORT OF CONCRETE INSPECTION AND TESTING — C-31

CLASS	4000	PSI		PSI	PLANT	FIELD
SUMMIT	SCENIC WEIGHT Lbs	DATE WEIGHT Lbs	SCENIC WEIGHT Lbs	DATE WEIGHT Lbs	PREVIOUS YARDAGE	N/A
CEMENT					YARDAGE	50.00 Cu. yds.
FINE AGG.					INSPECTED	50.00 Cu. yds.
COARSE AGG.					TOTAL TO DATE	50.00 Cu. yds.
COARSE AGG.					START	10 : 30 AM
WATER GALS.					FINISH	5 : 00 PM
ADMIX. WR-AEA					TOTAL HRS.	6 : 30 Hrs.
ADMIX. 92					INSP.	E. S. Patel

% PASSING	100	90	80	75	2	1	3/8	#4	#8	#16	1	1½	F.M.	% MOIST
FINE AGG.														
COARSE AGG.														
COARSE AGG.														

NO. OF CYLS. & CLASS Seven (7) cylinders - 4000 PSI AIR CONTENT (%) (C-231) 5.0%

SLUMP (C-143) 5" DENSITY (Unit Wt.) (C-138) LBS/Cf CONC. TEMP (°F) (C-1064) 80°F

LOCATION Concrete was placed for footing for Ground Water Treatment Facilities Building.

REMARK 50 cu. yds. - 5 trucks noted Stanley Concrete Co. Supplier. Informed the contractor & client about supplier Co. different. Contractor & client advised to use same concrete supplier & not need test & only 150 yds. one test require.

CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI	CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI
1.	ANX-1743-01	Shear	7 days	46, 740	2, 669	7.	ANX-1743-07	Shear	28 days	44, 220	2, 670
2.	ANX-1743-02	Cone & Shear	7 days	80, 420	4, 919						
3.	ANX-1743-03	Cone	14 days	80, 535	4, 927						
4.	ANX-1743-04	Cone	14 days	84, 189	4, 171						
5.	ANX-1743-05		28 days								
6.	ANX-1743-06		28 days								

SPECIMEN (6" x 12" CYL.) AREA 28.26 SQ. IN. Test performed as per A.S.T.M. specifications 1 - 2-09

ANS CONSULTANTS, INC.
4495 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATUC
(908) 754-8383
Fax: (908) 754-8633

NJ DOA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSconsultants.net

FILE NO.: ANS-1743

REPORT NO.: 01

CLIENT: Cape Environmental Inc., 45 Pine Street, Suite 1TR, Rockaway, NJ 07866

DATE: 10/24/2012

PAGE NO.: 01 of 1

PROJECT: 122 Jackson Ave., Secaucus, NJ

WEATHER: Clear

AIR TEMP.: 48°F

CONTRACTOR: Alint Construction

FINE AGG.: N/A

CONCRETE SUPPLIER: Joel Tang & Sons Inc

COARSE AGG.: N/A

CEMENT BRAND: N/A

REPORT OF CONCRETE INSPECTION AND TESTING — C-31

| CLASS | 4000 PSI | | | | | | | | PSI | | | | | | | |

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATUL
(908) 754-8383
Fax: (908) 754-8633

NJ EDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSConsultants.com

FILE NO. : ANX-1743 REPORT NO. : 37 DATE : 03/04/2011 PAGE NO. : C of 1

CLIENT : Cape Environmental Inc. 48 Pine Street, Suite - 101, Rockaway, NJ 07866 WEATHER : Clear AIR TEMP. : 44°F

PROJECT : 102 Jackson Ave., Rockaway, NJ FINE AGG. : N/A

CONTRACTOR : Alini Construction COARSE AGG. : N/A

CONCRETE SUPPLIER : Joel Farris & Sons Inc CEMENT BRAND : N/A

REPORT OF CONCRETE INSPECTION AND TESTING — C 31

CLASS	4000	PSI		PSI	PLANT	FIELD
SLUMP, in.	DESIGN WEIGHT LBS	RATIO WEIGHT LBS	DESIGN WEIGHT LBS	RATIO WEIGHT LBS	PREVIOUS TAKEDOWN	N/A
CEMENT					YARDAGE	30.00 Cu. yds.
FINE AGG.					INSPECTED	30.00 Cu. yds.
COARSE AGG.					TOTAL TO DATE	30.00 Cu. yds.
COARSE AGG.					START	10 : 30 AM
WATER GALS.					FINISH	5 : 00 PM
ADMIX. REL-AEA					TOTAL HRS.	6 : 30 Hrs.
ADMIX. OZ.					INSP.	E. S. Patel

% PASSING	150	100	50	30	16	8	4	3/8	1/2	3/4	1	1½	C.M.	% MOIST
FINE AGG.														
COARSE AGG.														
COARSE AGG.														

NO. OF CYLS. & CLASS Seven (7) cylinders - 4000 PSI AIR CONTENT (%) (C-231) 5.0%

SLUMP (C-143) 8" DENSITY (wet), lb. (C-138) 145 lbs CONC. TEMP (°F) (C-1064) 55°F

LOCATION Concrete was placed for footing for Grease Trap Treatment Facility Building.

REMARK 30 cu. yds. - 3 trucks Joel Farris Service Concrete Inc. Supplier informed the contractor & client about supplier Co. different. Contractor & client advised to use same concrete supplier & not need test & only 150 yds. one test require.

CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI*	CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI*
1.	ANX-1743-01	Shear	7 days	45,180	3,990	7.	ANX-1743-07	Shear	28 days	48,920	3,320
2.	ANX-1743-02	Cone & Shear	7 days	55,400	4,410						
3.	ANX-1743-03	Cone	14 days	58,200	4,190						
4.	ANX-1743-04	Cone	14 days	64,120	5,111						
5.	ANX-1743-05	Cone & Split	28 days	71,500	5,740						
6.	ANX-1743-06	Cone & Split	28 days	74,910	5,940						

SPECIMEN (4" x 8") CYLINDER 12.56 SQ. IN. Test performed as per A.S.T.M. specifications * Corr.

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 345-ATUL
(908) 754-8383
Fax: (908) 754-8633

NJ EDA Approved Testing Laboratory • AASHTO Certified • NJ DEP Certified
www.ANSConsultants.net

Soil, Concrete, Masonry, Asbestos, Structural Steel, Asphalt, Wood, Glass, Geotechnical, Roofing, Soil Gas, Construction Safety, Environmental, Testing & Inspection

FILE NO. : ANX-1743 REPORT NO. : 01 DATE : 10/24/2017 PAGE NO. : 1 of 1

CLIENT : Cape Environmental Inc., 46 Five Street, Suite 110, Rockaway, NJ 07866 WEATHER : Clear AIR TEMP. : 60°F

PROJECT : 122, Jackson Ave., Rockaway, NJ FINE AGG. : N/A

CONTRACTOR : Allini Construction COARSE AGG. : N/A

CONCRETE SUPPLIER : Joel Tarris & Sons Inc CEMENT BRAND : N/A

REPORT OF CONCRETE INSPECTION AND TESTING — C-31

CLASS	4000	PSI		PSI	PLANT	FIELD
SUBG.YD.	DESIGN WEIGHT LBS	DESIGN WEIGHT LBS	DESIGN WEIGHT LBS	DESIGN WEIGHT LBS	CREW/OUR VACUUM	N/A
CEMENT					MIXDATE	35.00 Cu. yds.
FINE AGG.					PREPRINTED	35.00 Cu. yds.
COARSE AGG.					TOTAL TO DATE	35.00 Cu. yds.
COARSE AGG.					START	10 : 00 AM
WATER GAL.S.					FINISH	5 : 00 PM
ADMIX. OZ./CEA					TOTAL HRS.	6 . 30 hrs.
ADMIX. OZ.					INSP.	B. S. Patel

S.PASSING	150	50	30	15	8	4	3/8	1/2	3/4	1	1 1/2	P.M.	12 NOON
FINE AGG.													
COARSE AGG.													
COARSE AGG.													

NO. OF CYLS. & CLASS Seven (7) c.Orders - 4000 PSI AIR CONTENT (%) (C-231) 5.0%

SLUMP (C-143) 9" DENSITY (C-138) SPEC. lb. MEET COND. TEMP (°F) (C-1064) 65°F

LOCATION Concrete was placed for footing for Ground Water Treatment Facility Building

REMARK 30 cu. yds. - 2 trucks MIXED Fredon Concrete Co. Supplier informed the inspector & client about supplier Co. different. Contractor & client advised to use same concrete supplier & not need test & only 150 yds. one test require.

CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI	CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI
1.	ANX-1743-01	Shear	7 days	42,750	5,500	7.	ANX-1743-07	Shear	28days	44,720	5,500
2.	ANX-1743-02	Cone & Shear	7 days	50,420	6,930						
3.	ANX-1743-03	Cone	14 days	59,590	6,750						
4.	ANX-1743-04	Cone	14 days	54,190	6,710						
5.	ANX-1743-05	Cone & Split	28 days	71,550	8,750						
6.	ANX-1743-06	Cone & Split	28 days	74,610	8,940						

SPECIMEN 6" x 8" CYL. (AREA 32.86 SQ.IN.) Test performed as per A.S.T.M. specifications 11-6-16

ANS CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080
Ph.: (908) 754-9393
Fax: (908) 754-9993

Project Sign-In Sheet

Client: _____

_____

Project: _____

_____

Date: _____ Time In: _____

Day: _____ Time Out: _____

Total Hours Worked: _____ Overtime: _____

Description of Work Performed:

- ☐ Concrete Inspection Field, Yds. / Cyls made: _____
- ☐ Swiss Hammer / Windsor Probe / Coring: _____
- ☐ Concrete Inspection Plant, Yds. Inspected: _____
- ☐ Masonry Inspection, Samples Made: _____
- ☐ Grout Inspection, Samples Made Today: _____
- ☐ Reinforcing Steel Inspection
- ☐ Footing Bottom Inspection
- ☐ Soil Compaction Testing
- ☐ No. of Soil Samples Picked Up: _____
- ☐ Soil Boring / Test Pits
- ☐ Asphalt Compaction Testing, HMA Sample (s): _____
- ☐ Structural Steel Inspection
- ☐ Visual Welding ☐ PT ☐ MT ☐ UT
- ☐ Flatness ☐ Torque Testing of bolts
- ☐ Fireproofing Inspection, No. of Density Samples: _____
- ☐ Adhesion & Cohesion Test, No. of Tests done: _____
- ☐ Paint Thickness Testing
- ☐ Anchor Bolt Pull Test, No. of Tests done: _____
- ☐ Floor Flatness Testing
- ☐ Water Sample Collection / Testing, No. of Samples Collected: _____
- ☐ Asbestos / Lead Base Paint Sampling: _____
- ☐ Miscellaneous Testing: _____
- ☐ Report Provided: ☐ No ☐ Yes, if yes, ☐ Written or ☐ Verbal
- ☐ Did Client Schedule follow-up Inspection? ☐ No ☐ Yes

Sign: _____ Sign Client: _____

ANS CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 543-ATU1
(908) 754-8383
Fax: (908) 754-8533

NJ EDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSConsultants.net

Soil Chemical, Masonry, Glass, Metal / Welding, Steel, Fireproofing, Roofing, Infrared Scan, Construction Materials Testing, Structural Steel Bolts

FILE NO. : 4900-0745 REPORT NO. : 02 DATE : 03/14/2017 PAGE NO. : 1 of 1

CLIENT : Cape Environmental Inc., 45 Pine Street, Suite 140, Rockaway, NJ 07866 WEATHER : Cloudy AIR TEMP. : 32°F

PROJECT : 125 Jackson Ave., Rockaway, NJ FINE AGG. : N/A

CONTRACTOR : N/A COARSE AGG. : N/A

CONCRETE SUPPLIER : Service Concrete CEMENT BRAND : N/A

REPORT OF CONCRETE INSPECTION AND TESTING — C-31

CLASS	4000 PSI				PSI		PLANT	FIELD
CURB TO.	DESIGN WEIGHT LBS	WATER WEIGHT LBS	DESIGN WEIGHT LBS	WATER WEIGHT LBS			PREVIOUS YARDAGE	30.00 Cu. yds.
CEMENT							YARDAGE	18.00 Cu. yds.
FINE AGG.							INSPECTED	18.00 Cu. yds.
COARSE AGG.							TOTAL TO DATE	48.00 Cu. yds.
COARSE AGG.							START	8 : 00 AM
WATER GALS.							FINISH	4 : 30 PM
ADMIX. GRADE							TOTAL HRS	7 : 00 Hrs.
ADMIX. SIZE							INSP.	Dipen

% PASSING	100	50	30	16	8	4	3/8	16	30	1	1½	F.M.	% MOIST
FINE AGG.													
COARSE AGG.													
COARSE AGG.													

NO. OF CYLS. & CLASS Seven (7) cylinders - 4000 PSI AIR CONTENT (%) (C-231) 6.0%

SLUMP (C-143) 4½" DENSITY (lbs./ft.³) (C-138) 141.38 CONC. TEMP (°F) (C-1064) 32°F

LOCATION Concrete was placed for footing wall concrete between grid line C-F, part a wall elevation between: [illegible] A pa

REMARK 8 cyl. (5 test to be made)
Field ID/Wtg. S-4, S-7

CYL NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI*	CYL NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI*
1.	ANX-1743-08	Shear	7 days	46,000	2,340	7.	ANX-1743-14		Hold		
2.	ANX-1743-09	Cone	7 days	42,100	5,000						
3.	ANX-1743-10		14 days								
4.	ANX-1743-11		14 days								
5.	ANX-1743-12		28 days								
6.	ANX-1743-13		28 days								

SPECIMEN (6" x 12") CYL. AREA 12.56 SQ. IN. Test performed as per A.S.T.M. specification 1-C-39

ANS CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATCC
(908) 754-8383
Fax: (908) 754-8613

NJ EDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSConsultants.net

Soil, Concrete, Asphalt, Steel, Hydraulic Soil Stabilization, Pavers, Slip, Chemical, Electrical, Footing Soil Bearing, Geotechnical, Geotechnical, Underground Utility Locating

FILE NO. : ANX-1743 REPORT NO. : 32 DATE : 09/04/2011 PAGE NO. 11 of 1

CLIENT : Cape Environmental Inc., 46 Pine Street, Suite - 200, Rockaway, NJ 07866 WEATHER : Cloudy AIR TEMP. 8 PM

PROJECT : 122, Jackson Ave., Roselle, NJ FINE AGG. : NA

CONTRACTOR : N/A COARSE AGG. : NA

CONCRETE SUPPLIER : Service Concrete CEMENT BRAND : NA

REPORT OF CONCRETE INSPECTION AND TESTING — C-31

CLASS	4000 PSI													PSI		PLANT	FIELD
CUBIC YD.	DESIGN WEIGHT LBS													DESIGN WEIGHT LBS	BATCH WEIGHT LBS		
CEMENT																PREVIOUS YARDAGE	30.00 Cu. yds.
FINE AGG.																YARDAGE	18.00 Cu. yds.
COARSE AGG.																INSPECTED	18.00 Cu. yds.
COARSE AGG.																TOTAL TO DATE	48.00 Cu. yds.
WATER GALS.																START	9 : 00 AM
POWER SPLASH																FINISH	4 : 30 PM
ADM. & OTH.																TOTAL LBS.	7 : 00 hrs.
% PASSING	100	90	80	70	60	40	30	20	10	5	3/4	1	1½	F.M.	% MOIST.	TYPE	Class
FINE AGG.																	
COARSE AGG.																	
COARSE AGG.																	

NO. OF CYLS. & CLASS Seven (7) cylinders - 4000 PSI AIR CONTENT (%) (C-231) 6.0%

SLUMP (C-143) 4½" DENSITY (Unit Wt.) (C-138) 143.82 CONC. TEMP. (°F.) (C-1064) 60°F

LOCATION Concrete was placed for footing wall concrete between grid line C-D, and a wall elevation between 5'11"S' + 8, 6'8.5" & pa

REMARK Transit mixed in 20A yd.
Pour drawing S-1, S-2

CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI*	CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI*
1	ANX-1743-06	Shear	3 days	42,400	3,540	5	ANX-1743-14		28d		
2	ANX-1743-09	Cone	7 days	42,160	3,350						
3	ANX-1743-15		14 days								
4	ANX-1743-11		21 days								
5	ANX-1743-12		28 days								
6	ANX-1743-13		28 days								

SPECIMEN 4" x 8" CYL. AREA 12.56 SQ. IN.

*Rounded off per A.S.T.M. specification

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATCL
(908) 754-8383
Fax: (908) 754-8633

NJ FDA Approved Testing Laboratory • MSE/DSF Certified • NJ DIP Certified
www.ANSConsultants.net

Soil, Concrete, Asphalt, Epoxy, Aggregate, Structural Steel, Welding, Fireproofing, Roofing, Exterior Curtain Wall, Concrete Coring, Core Drilling, Environmental Studies & Reports

FILE NO. : ANS-1743 REPORT NO. : 99 DATE : 03/16/2017 PAGE NO. : 1 of 1

CLIENT : Case Environmental Inc., 46 Pine Street, Suite - 100, Rockaway, NJ 07866 WEATHER : Cloudy AIR TEMP. : 60°F

PROJECT : 122 Jackson Ave., Rockaway, NJ FINE AGG. : N/A

CONTRACTOR : N/A COARSE AGG. : N/A

CONCRETE SUPPLIER : Service Concrete CEMENT BRAND : N/A

REPORT OF CONCRETE INSPECTION AND TESTING ---- C-31

CLASS	4000	PSI		PSI	PLANT	FIELD
CUBO NO.	DESIGN WEIGHT LBS	ACTUAL WEIGHT LBS	DESIGN WEIGHT LBS	ACTUAL WEIGHT LBS	PREVIOUS YARDAGE	30.50 Cu. yds.
CEMENT					YARDAGE	18.00 Cu. yds.
FINE AGG.					DISPATCH	18.00 Cu. yds.
COARSE AGG.					TOTAL TO DATE	48.00 Cu. yds.
COARSE AGG.					START	9 : 00 AM
WATER GALS.					FINISH	4 : 30 PM
ADMIX. OZ./CWT					TOTAL HRS.	7.00 Hrs.
					INSP.	Dipen

% PASSING	100	90	80	50	8	4	3/8	16	30	1	1/2	H.M.	% MOIST
FINE AGG.													
COARSE AGG.													
COARSE AGG.													

NO. OF CYLS. & CLASS Seven (7) cylinders - 4000 PSI AIR CONTENT (%) (C-231) 5.0%

SLUMP (C-143) 4 1/2" DENSITY (lbs./cu. ft.) (C-138) 143.38 COND. TEMP (°F) (C-1064) 82°F

LOCATION Concrete was placed for footing, wall concrete between grid line C-2, next 8 wall elevation between 5'-10 1/2" + 11'-0 1/2" & ins

REMARK 4 SAMPLES TAKEN, 3 KEPT
Refer drawing S-4, S-7

CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI	CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI
1.	ANS-1743-01	Shear	7 days	42,100	2,346	2.	ANS-1743-14		28 days		
3.	ANS-1743-02	Shear	7 days	49,160	2,736						
5.	ANS-1743-15		14 days								
4.	ANS-1743-17		14 days								
6.	ANS-1743-12		28 days								
8.	ANS-1743-13		28 days								

SPECIMEN (6" x 6") CYL. ARE A - 28.86 SQ. IN. Test performed as per A.S.T.M. specifications * = 2.54

ANS CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (908) 545-ATUL
(908) 754-8383
Fax: (908) 754-8633

NJ EDA Approved Testing Laboratory • AISC/DBE Certified • NJ DEP Certified
www.ANSConsultants.com

Soil, Concrete Cores & Cylinders, Masonry Assist, Welding Shop, Fireproofing, Roofing, Soil Testing, Concrete Batching, 24 Hours, Construction Testing & Inspections

FILE NO. : ANX-0742 REPORT NO. : 02 DATE : 03/14/2001 PAGE NO. : 0-31

CLIENT : Gage Environmental Inc., 45 Pine Street, Suite - 110, Rockaway, NJ 07866 WEATHER : Cloudy AIR TEMP. : 42°F

PROJECT : 122, Jackson Ave., Rockaway, NJ FINE AGG. : N/A

CONTRACTOR : N/A COARSE AGG. : N/A

CONCRETE SUPPLIER : Service Concrete CEMENT BRAND : N/A

REPORT OF CONCRETE INSPECTION AND TESTING — C-31

CLASS	4000	PSI		PSI	PLANT	FIELD
CUBIC YD.	DESIGN WEIGHT LBS	BATCH WEIGHT LBS	DESIGN WEIGHT LBS	BATCH WEIGHT LBS	PREVIOUS YARDAGE	30.00 Cu. yds.
CEMENT					YARDAGE	18.00 Cu. yds.
FINE AGG.					REPORTED	18.00 Cu. yds.
COARSE AGG.					TOTAL TO DATE	48.00 Cu. yds.
COARSE AGG.					START	8 : 00 AM
WATER GALS.					FINISH	4 : 30 PM
NAMX. SZ. AGG.					TOTAL HRS.	7 : 00 Hrs.
AIRMIX. OZ.					INSP.	Dipen

% PASSING	100	95	90	75	8	4	3/8	16	30	1	1/2	F.M.	% MOIST
FINE AGG.													
COARSE AGG.													
COARSE AGG.													

NO. OF CYLS. & CLASS Seven (7) cylinders - 4000 PSI AIR CONTENT (%) (C-231) 6.0%

S. (IN) (C-143) "OK" DENSITY (lbs/cu.ft.) (C-138) 148.55 CONC. TEMP (°F) (C-1064) 62°F

LOCATION Concrete was placed for footing wall concrete between grid line G-E, part a wall elevation between 61142' + 0, 563.25'N. (a

REMARK Sheet R1-401 to R3-401
Refer drawing F-4, S-2

CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI*	CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI*
1.	ANX-1743-08	Shear	7 days	42,000	3,545	5.	ANX-1743-12		Hold		
2.	ANX-1743-09	Cone	7 days	48,150	4,060						
3.	ANX-1743-10	Cone & Shear	14 days	49,340	4,160						
4.	ANX-1743-11	Shear	14 days	51,500	4,128						
6.	ANX-1743-13		28 days								
7.	ANX-1743-14		28 days								

REFERENCE (4" x 8" CYL.) AREA 12.56 SQ. IN. Test performed as per A.S.T.M. specifications * - C-39

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 543-ATUL
(908) 754-8383
Fax: (908) 754-8633

NJ EDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSConsultants.com

FILE NO. : ANX-1743 REPORT NO. : 62 DATE : 08/14/2011 PAGE NO. : 1 of 1

CLIENT : Cape Environmental Inc., 65 Hire Street, Suite - 110, Roxbury, NJ 07850 WEATHER : Cloudy AIR TEMP. : 82°F

PROJECT : 122, Jackson Ave., Roxbury, NJ FINE AGG. : N/A

CONTRACTOR : N/A COARSE AGG. : N/A

CONCRETE SUPPLIER : Service Concrete CEMENT BRAND : N/A

REPORT OF CONCRETE INSPECTION AND TESTING ---- C-31

CLASS	4000 PSI		PSI		PLANT	FIELD
CUBIC YD.	DESIGN WEIGHT LBS	ACTUAL WEIGHT LBS	DESIGN WEIGHT LBS	ACTUAL WEIGHT LBS	PREVIOUS YARDAGE	90.00 Cu. yds.
CEMENT					YARDAGE	18.00 Cu. yds.
FINE AGG.					INSPECTED	18.00 Cu. yds.
COARSE AGG.					TOTAL TO DATE	48.00 Cu. yds.
COARSE AGG.					START	8 : 00 AM
WATER GALS					FINISH	4 : 30 PM
ADMIX. GE-AEA					TOTAL HRS	7 : 00 Hrs.
ADMIX. DF.					MSP	Dipon

% PASSING	1½	1	¾	½	⅜	4	#8	#16	#30	#50	#100	#200	% VOIDS
FINE AGG.													
COARSE AGG.													
COARSE AGG.													

NO. OF CYLS. & CLASS Seven (7) cylinders - 4000 PSI AIR CONTENT (%) (C-231) 5.0%

SLUMP (C-143) 4½" DENSITY (lbs/ft³) (C-138) 145.30 CONC. TEMP (°F) (C-1064) 85°F

LOCATION Concrete was placed for footing wall separate pour line C-5, part a wall elevation between El 142 - 0, El 5.10 & pr 3 wall ELEV to El 5.50

REMARK Rebar drawing S-4, S-2

CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI*	CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI*
1.	ANX-1743-02	Shear	7 days	42,000	5,940	7.	ANX-1743-14		28		
2.	ANX-1743-05	Cone	7 days	42,100	5,950						
3.	ANX-1743-10	Cone & Shear	14 days	49,300	6,970						
4.	ANX-1743-11	Shear	14 days	37,300	5,130						
5.	ANX-1743-12		28 days								
6.	ANX-1743-13		28 days								

SPECIMEN 6" x 12" (CYL.) AREA 12.56 SQ. IN. Test performed as per A.S.T.M. Specifications C-39

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Toll: (800) 5ANSATUL
(908) 754-8383
Fax: (908) 754-8633

NJ SDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSConsultants.net

Soil Borings, Footings, Piles, Asphalt, Structural Steel, Precast Plant Services, Fireproofing Testing, Soil Testing, Concrete Block Testing, UST Removal, Environmental Testing & Disposal

FILE NO. : ANX-1743 REPORT NO. : 02 DATE : 08/14/2017 PAGE NO. : 1 of 1

CLIENT : Cape Environmental, Inc., 40 Pine Street, Suite - 110, Rockaway, NJ 07866 WEATHER : Cloudy AIR TEMP. : 82°F

PROJECT : 102, Jackson Ave., Roseland, NJ FINE AGG. : N/A

CONTRACTOR : N/A COARSE AGG. : N/A

CONCRETE SUPPLIER : Service Concrete CEMENT BRAND : N/A

REPORT OF CONCRETE INSPECTION AND TESTING — C-31

CLASS	4000 PSI		PSI		PLANT	FIELD
CUBIC YD.	DESIGN WEIGHT LBS	BATCH WEIGHT LBS	DESIGN WEIGHT LBS	BATCH WEIGHT LBS	PREVIOUS YARDAGE	30.25 Cu. yds.
CEMENT					YARDAGE	18.00 Cu. yds.
FINE AGG.					INSPECTED	18.00 Cu. yds.
COARSE AGG.					TOTAL TO DATE	48.00 Cu. yds.
COARSE AGG.					START	8 : 30 AM
WATER GAL.					FINISH	4 : 30 PM
ADMIX. OZ./BAG					TOTAL HRS.	7 : 00 Hrs.
ADMIX. OZ.					INSP.	Dipen

% PASSING	1½	1	¾	½	⅜	#4	#8	#16	#30	#50	#100	#200	% MOIST
FINE AGG.													
COARSE AGG.													
COARSE AGG.													

NO. OF CYLS. & CLASS Seven (7) cylinders - 4000 PSI AIR CONTENT (%) (C-231) 5.0%

SLUMP (C-143) 4½" DENSITY (Wgt. R. (C-138)) 142.0 lb CONC. TEMP (°F.) (C-1064) 82°F

LOCATION Concrete was placed for footing wall opposite between grid line D-G, part a wall elevation between B1142' + 5.818.19' E pe

REMARK Refer drawing S-4, S-2

CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI	CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI
1.	ANX-1743-08	Shear	7 days	45,200	4,340	5.	ANX-1743-11		Held		
2.	ANX-1743-09	Cone	7 days	46,120	4,430						
3.	ANX-1743-10	Cone & Shear	14 days	46,360	4,460						
4.	ANX-1743-11	Shear	14 days	45,800	4,400						
5.	ANX-1743-12		28 days								
6.	ANX-1743-13		28 days								

SPECIMEN DIM'S 6" DIA. AREA 28.26 SQ. IN. Test performed as per A.S.T.M. specifications

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 565-ATUP
(908) 754-8383
Fax: (908) 754-8633

NJ EDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSConsultants.net

Soil Borings, Hydrology, Water Analysis, Subsurface Gas Probes, Pile Driving, Pile Load Testing, Soil Boring, Foundation Coring, Dry Wetwell, Underground Storage Tanks

FILE NO. : ANX-1743 REPORT NO. : 02 DATE : 03/15/2011 PAGE NO. : 2 of 1

CLIENT : Cape Environmental Inc., 46 Pine Street, Suite - 110, Rockaway, NJ 07866 WEATHER : Cloudy AIR TEMP. : 32/F

PROJECT : 122, Jackson Ave., Rockaway, NJ FINE AGG. : N/A

CONTRACTOR : N/A COARSE AGG. : N/A

CONCRETE SUPPLIER : Service Concrete CEMENT BRAND : N/A

REPORT OF CONCRETE INSPECTION AND TESTING — C-31

CLASS	4000	PSI		PSI	PLANT	FIELD
CUBIC YD.	DESIGN WEIGHT LBS	ACTUAL WEIGHT LBS	DESIGN WEIGHT LBS	ACTUAL WEIGHT LBS	PREVIOUS YARDAGE	30.00 Cu. yds.
CEMENT					YARDAGE	18.00 Cu. yds.
FINE AGG.					INSPECTED	18.00 Cu. yds.
COARSE AGG.					TOTAL TO DATE	48.00 Cu. yds.
COARSE AGG.					START	9:00 AM
WATER GALS.					FINISH	4:30 PM
ADMIX. BRAND					TOTAL HRS.	7:00 Hrs.
ADMIX. DM.					INSP.	Dipen

% PASSING	150	90	80	75	3	2	1½	1	¾	½	⅜	#4	#8	% MOIST
FINE AGG.														
COARSE AGG.														
COARSE AGG.														

NO. OF CYLS. & CLASS Seven (7) cylinders - 4000 PSI AIR CONTENT (%) (C-231) 5.0%

SLUMP (C-143) 4½" UNIT WGT. (C-138) 143.00 CONC. TEMP. (°F.) (C-1064) 62°F

LOCATION Concrete was placed for footing wall. Concrete between grid line C-E, part a wall elevation between 51.142' + 0.613.10' & pa

REMARK Refer drawing S-4, S-7

CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI*	CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI*
1.	ANX-1743-08	Shear	3 days	43,500	3,350	7.	ANX-1743-14		Hold		
2.	ANX-1743-09	Cone	7 days	42,160	3,350						
3.	ANX-1743-10	Cone & Shear	10 days	48,360	3,860						
4.	ANX-1743-11	Shear	14 days	51,520	4,150						
5.	ANX-1743-12	Cone & split	18 days	55,480	4,350						
6.	ANX-1743-13	Cone	28 days	58,640	4,720						

SPECIMEN : 6" x 12" CYL. AREA : 28.26 SQ. IN. Test performed in per A.S.T.M. specifications *: Corr.

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATOL
(908) 754-8383
Fax: (908) 754-8633

NJ EDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSconsultants.net

Soil, Concrete, Masonry, Asphalt, Structural Steel, Welds, Fireproofing, Roofing, Soil Borings, Underground Tanks, UST Removal, Environmental Testing, Asbestos

FILE NO.: ANX-1743 REPORT NO.: 02 DATE: 03/14/2011 PAGE NO.: 1 of 1

CLIENT: Cape Environmental, Inc., 45 Pine Street, Suite - 170, Rockaway, NJ 07866 WEATHER: Cloudy AIR TEMP.: 37°F

PROJECT: 123, Jackson Ave., Rockaway, NJ FINE AGG.: N/A

CONTRACTOR: N/A COARSE AGG.: N/A

CONCRETE SUPPLIER: Service Concrete CEMENT BRAND: N/A

REPORT OF CONCRETE INSPECTION AND TESTING — C-31

CLASS	4000	PSI		PSI	PLANT	FIELD
CUBIC YD.	DESIGN WEIGHT / LBS	DATED WEIGHT / LBS	DESIGN WEIGHT / LBS	DATED WEIGHT / LBS	PREVIOUS YARDAGE	30.00 Cu. yds.
CEMENT					YARDAGE	18.00 Cu. yds.
FINE AGG.					INSPECTED	18.00 Cu. yds.
COARSE AGG.					TOTAL TO DATE	48.00 Cu. yds.
COARSE AGG.					START	9:00 AM
WATER GALS.					FINISH	4:30 PM
ADMIX. OZ. AGA					TOTAL HRS.	7.00 Hrs.
ADMIX. OZ.					INSP.	Dixon

% PASSING	100	50	30	16	8	4	3/8	3/4	3/4	1	1½	2½	3½	% ASCIST
FINE AGG.														
COARSE AGG.														
COARSE AGG.														

NO. OF CYLS. & CLASS Seven (7) cylinders - 4000 PSI AIR CONTENT (%) (C-231): 5.0%

SLUMP (C-143): 4½" DENSITY (PCF) (C-138): 143.30 CONC. TEMP (°F) (C-1064): 68°F

LOCATION Concrete was placed for footing wall concrete between grid line E-H, part a wall elevation between El 14.2' + to 15.5' (4 pa

REMARK 1 Bucket 30 (C-172) (C-94 C-31)
Refer drawing S-4, S-2

CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI	CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI
A.	ANX-1743-08	Shear	7 days	42,390	6,043	A.	ANX-1743-14		28d		
B.	ANX-1743-09	Cone	7 days	42,180	6,030						
B.	ANX-1743-10	Cone & Shear	14 days	49,350	6,930						
A.	ANX-1743-11	Shear	14 days	39,850	5,690						
A.	ANX-1743-12	Cone & Shear	28 days	50,450	7,200						
A.	ANX-1743-13	Cone	28 days	53,040	7,750						

SPECIMEN: 6" x 12" CYL. / ASTM C31, C39, C42, 74 Test accredited by NVLAP, A.S.T.M. specifications (C-39)

"ANS exists to your construction inspection and testing needs."

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATUL
(908) 754-8383
Fax: (908) 754-8633

NJ EDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSConsultants.net

Soil Sampling, Testing, Proctor, Asphalt, Nuclear Density Gauge Testing, Plate Bearing, Expansion, Testing, Mix Testing, Concrete Cylinder Curing, ACI Mobile Laboratory, Inspection Services

FILE NO. : ANX-1743 REPORT NO. : 02 DATE : 03/19/2010 PAGE NO. : 1 of 1

CLIENT : Cape Environmental Inc., 46 Pine Street, Suite 518, Rockaway, NJ 07866 WEATHER : Cloudy AIR TEMP. : 37°F

PROJECT : 123 Jackson Ave., Rockaway, NJ FINE AGG. : N/A

CONTRACTOR : N/A COARSE AGG. : N/A

CONCRETE SUPPLIER : Service Concrete CEMENT BRAND : N/A

REPORT OF CONCRETE INSPECTION AND TESTING — C-31

CLASS	4000	PSI		PSI	PLANT	FIELD
MIX NO.	DESIGN WEIGHT LBS	WATER WEIGHT LBS	DESIGN WEIGHT LBS	WATER WEIGHT LBS	PREVIOUS YARDAGE	30.00 Cu. yds.
CEMENT					YARDAGE	19.00 Cu. yds.
FINE AGG.					REPORTED	18.00 Cu. yds.
COARSE AGG.					TOTAL TO DATE	48.00 Cu. yds.
COARSE AGG.					START	9:00 AM
WATER RED.					FINISH	4:30 PM
ADMIX. DR-AEA					TOTAL HRS.	7:00 Hrs.
ADMIX. DR.					MSP	Direct

% PASSING	1½	1	¾	½	⅜	#4	#8	#16	#30	#50	#100	#200	F.M.	% MOIST
FINE AGG.														
COARSE AGG.														
COARSE AGG.														

NO. OF CYLS. & CLASS Seven (7) cylinders - 4000 PSI AIR CONTENT (%) (C-231) 6.0%

SLUMP (C-143) 4½" DENSITY (PCF) (C-138) 143.99 CONC. TEMP (°F) (C-1064) 62°F

LOCATION Concrete was placed for footing wall (concrete) between grid line D-E, pad & wall elevation between @1142' + 0, 312.10' & pa

REMARK Rebar drawing S-4, S-2

CYL NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI	CYL NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI
1.	ANX-1743-08	Shear	7 days	42,330	5,340	7.	ANX-1743-14		HOLD		
2.	ANX-1743-09	Cone	7 days	45,190	5,690						
3.	ANX-1743-10	Cone & Shear	14 days	50,350	6,350						
4.	ANX-1743-11	Shear	14 days	51,950	6,150						
5.	ANX-1743-12	Cone & split	28 days	58,490	6,250						
6.	ANX-1743-13	Cone	28 days	58,000	6,150						

SPECIMEN (4" x 8" CYL.) AREA 12.56 SQ. IN. Test performed in accord. ASTM specifications C-39

CONSULTANTS, INC.
4403 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 345-ATCL
(908) 754-8383
Fax: (908) 754-8633

NJ EDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSConsultants.net

Soil, Concrete, Masonry, Asphalt, Structural Steel, Prestressed Steel, Welding, Coatings, Geotechnical, Geology, Dry Rooting, Environmental Chemistry, Lab Services, Environmental Testing & Training

FILE NO. : ANX-4743 REPORT NO. : 03 DATE : 03/25/2011 PAGE NO. : 1 of 1

CLIENT : Cape Construction Inc., 45 Pine Street, Bldg. 1, Rm 10, Keyhaven, NJ 07086 WEATHER : N/A AIR TEMP. : N/A

PROJECT : 132, Jackson Ave., Keyhaven, NJ FINE AGG. : N/A

CONTRACTOR : N/A COARSE AGG. : N/A

CONCRETE SUPPLIER : N/A CEMENT BRAND : N/A

REPORT OF CONCRETE INSPECTION AND TESTING ---- C-31

CLASS	4000 PSI				PSI		PLANT	FIELD
MIX ID.	DESIGN WEIGHT LBS	BATCH WEIGHT LBS	DESIGN WEIGHT LBS	BATCH WEIGHT LBS			PREVIOUS YARDAGE	48.00 Cu. yds.
CEMENT							TAKEDAIL	20.00 Cu. yds.
FINE AGG.							INSPECTED	00.00 Cu. yds.
COARSE AGG.							TOTAL TO DATE	48.00 Cu. yds.
COARSE AGG.							START	11:30 AM
WATER GALS.							FINISH	2:00 PM
ADMIX. OZ./100#							TOTAL HRS.	3 : 30 Hrs.
AIRMIX. OZ.							INSP.	Soni

% PASSING	100	90	80	70	60	50	40	30	20	10	5	2.5	1.25	% MOIST
FINE AGG.														
COARSE AGG.														
COARSE AGG.														

NO. OF CYLS. & CLASS None AIR CONTENT (%) (C-231) N/A

SLUMP (C-143) N/A DENSITY (KG/M³) (C-138) CONC. TEMP (°C) (C-1064) N/A

LOCATION

REMARK Concrete placement was cancelled

CYL NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI	CYL NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI

SPECIMEN 4"x8" CYL. UNDER 12.00 SQ. IN. TEST performed as per A.S.T.M. specifications C-39

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATUL
(908) 754-8383
Fax: (908) 754-8633

NJ EDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSconsultants.net

Soil Borings in Vehicle Impact Areas, Standard Test Pitting, Plate Bearing, Compaction Grouting, Vibration Monitoring, Underpinning, Soil Nailing, Construction Monitoring, LDR Permit, Environmental Testing Services

FILE NO. : ANS-1745 REPORT NO. : 09 DATE : 12/29/2011 PAGE NO. : 1 of 1

CLIENT : Cape Environmental Inc., 46 Pine Street, Suite 1-19, Rockaway, NJ 07866 WEATHER : N/A AIR TEMP. : N/A

PROJECT : 152, Jackson Ave., Roseland, NJ FINE AGG. : N/A

CONTRACTOR : N/A COARSE AGG. : N/A

CONCRETE SUPPLIER : N/A CEMENT BRAND : N/A

REPORT OF CONCRETE INSPECTION AND TESTING — C-31

CLASS	4000	PSI		PSI	PLANT	FIELD
CUBIC YD.	DESIGN WEIGHT LBS	WEIGH WEIGHT LBS	DESIGN WEIGHT LBS	WEIGH WEIGHT LBS	PREVIOUS TARDAGE	40.00 Cu. yds.
CEMENT					TARDAGE	50.00 Cu. yds.
FINE AGG.					INSPECTED	05.00 Cu. yds.
COARSE AGG.					TOTAL TO DATE	45.00 Cu. yds.
COARSE AGG.					START	11:00 AM
WATER/GALS.					FINISH	2:30 PM
ADMIX. 02.-AEA					TOTAL TIME	3.30 Hrs.
ADMIX. OZ.					INSP.	Soni

% PASSING	100	90	80	70	3/8	4	8	16	30	50	100	F.M.	% MOIST
FINE AGG.													
COARSE AGG.													
COARSE AGG.													

NO. OF CYLS. & CLASS None AIR CONTENT (%) (C-231) N/A

SLUMP (C-143) N/A DENSITY (Unit Wt.) (C-138) CONC. TEMP (°F) (C-1064) N/A

LOCATION

REMARK Concrete placement was cancelled.

CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI*	CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI*

*SPECIMEN (4" x 8") (6" x 12") (3" x 6") (2" x 4") Test performed as per A.S.T.M. specifications

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATTJ
(908) 754-6383
Fax: (908) 754-6633

NJ MDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.AnsConsultants.net

FILE NO. : ANS-1763 REPORT NO. : 09 DATE : 03/25/2011 PAGE NO. : 1 of 1

CLIENT : Dapo Environmental Inc., 45 Pine Street, Suite - 1 Hl, Rockaway, NJ 07866 WEATHER : N/A AIR TEMP. : N/A

PROJECT : 122, Jackson Ave, Rockaway, NJ FINE AGG. : N/A

CONTRACTOR : N/A COARSE AGG. : N/A

CONCRETE SUPPLIER : N/A CEMENT BRAND : N/A

REPORT OF CONCRETE INSPECTION AND TESTING ---- C-31

CLASS	4000 PSI		PSI		PLANT	FIELD
GUAGE NO.	DESIGN WEIGHT LBS	DATON WEIGHT LBS	DESIGN WEIGHT LBS	DATON WEIGHT LBS	PREVIOUS YARDAGE	48.50 Cu. yds.
CEMENT					YARDAGE	60.00 Cu. yds.
FINE AGG.					INSPECTOR	30.00 Cu. yds.
COARSE AGG.					TOTAL TO DATE	48.50 Cu. yds.
COARSE AGG.					START	11:00 AM
WATER GALS.					FINISH	2:30 PM
AGWA DEMAND					TOTAL HRS.	3:30 Hrs.
AGWA CO.					INSP.	Son

% PASSING	100	95	90	16	8	4	3/8	16	30	50	100	200	% MOIST
FINE AGG.													
COARSE AGG.													
COARSE AGG.													

NO. OF CYLS. & CLASS None AIR CONTENT (%) (C-231) N/A

SLUMP (C-143) N/A TEMPERATURE (Deg. F) (C-1064) CONC. TEMP (°F) (C-1064) N/A

LOCATION

REMARK Concrete placement was cancelled

CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI	CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI

SPECIMEN: 6"x 9" CYLINDER 12.56 SQ. IN. Test performed as per A.S.T.M. specification * (C-39)

CONSULTANTS, INC.
4485 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATUL
(908) 754-8383
Fax: (908) 754-8633

NJ FDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSconsultants.net

Full Service Laboratory, Water Analysis, Structural Steel, Concrete, Non-Destructive Concrete Testing, Roofing, Soil Borings, Geotechnical Engineering, Asbestos Sampling & Analysis, Air Monitoring, Industrial Hygiene

FILE NO. : ANX-1743 REPORT NO. : 04 DATE : 03/29/201[illegible] PAGE NO. : 1 of 1

CLIENT : Dade Environmental Inc., 48 Pine Street, Suite - 110, Rockaway, NJ 07866 WEATHER : Sunny AIR TEMP. : 48°F

PROJECT : 125, Jackson Ave., Rockaway, NJ FINE AGG. : N/A

CONTRACTOR : Alinj Corp. COARSE AGG. : N/A

CONCRETE SUPPLIER : Joel Tanis & Sons Concrete CEMENT BRAND : N/A

REPORT OF CONCRETE INSPECTION AND TESTING — C-31

CLASS	4000	PSI		PSI	PLANT	FIELD
CUBIC YD.	DESIGN WEIGHT Lbs	BATCH WEIGHT Lbs	DESIGN WEIGHT Lbs	BATCH WEIGHT Lbs	PROV SALE YARDAGE	48.00 Cu. yds.
CEMENT					YARDAGE	25.00 Cu. yds.
FINE AGG.					INSPECTED	25.00 Cu. yds.
COARSE AGG.					TOTAL TO DATE	75.00 Cu. yds.
COARSE AGG.					START	8 : 00 AM
WATER GALS.					FINISH	2 : 00 PM
ADMIX. GALLONS					TOTAL HRS.	4 . 00 Hrs.
ADMIX. OZ.					INSP.	Soni

% PASSING	100	90	80	70	3"	1"	3/8	8	30	50	100	200	% MOIST
FINE AGG.													
COARSE AGG.													
COARSE AGG.													

NO. OF CYLS. & CLASS Five (5) cylinders - 4000 PSI (A/E) AIR CONTENT (%) 5.5%

SLUMP 6" DENSITY (Wet) lb/cu. ft. CONC. TEMP. (°F) 68°F

LOCATION Concrete was placed for slab on grade.

REMARK See attached inspection plan.

CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI*	CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI*
1.	ANX-1743-15	Shear	7 days	[illegible]	1,7[illegible]						
2.	ANX-1743-16	Cone & Shear	7 days	[illegible]	2,[illegible]						
3.	ANX-1743-17		14 days								
4.	ANX-1743-18		28 days								
5.	ANX-1743-19		28 days								

SPECIMEN DIMENSIONS: 6" x 12" CYLINDER, 78.50 SQ. IN. Test performed as per A.S.T.M. specifications * 0.00

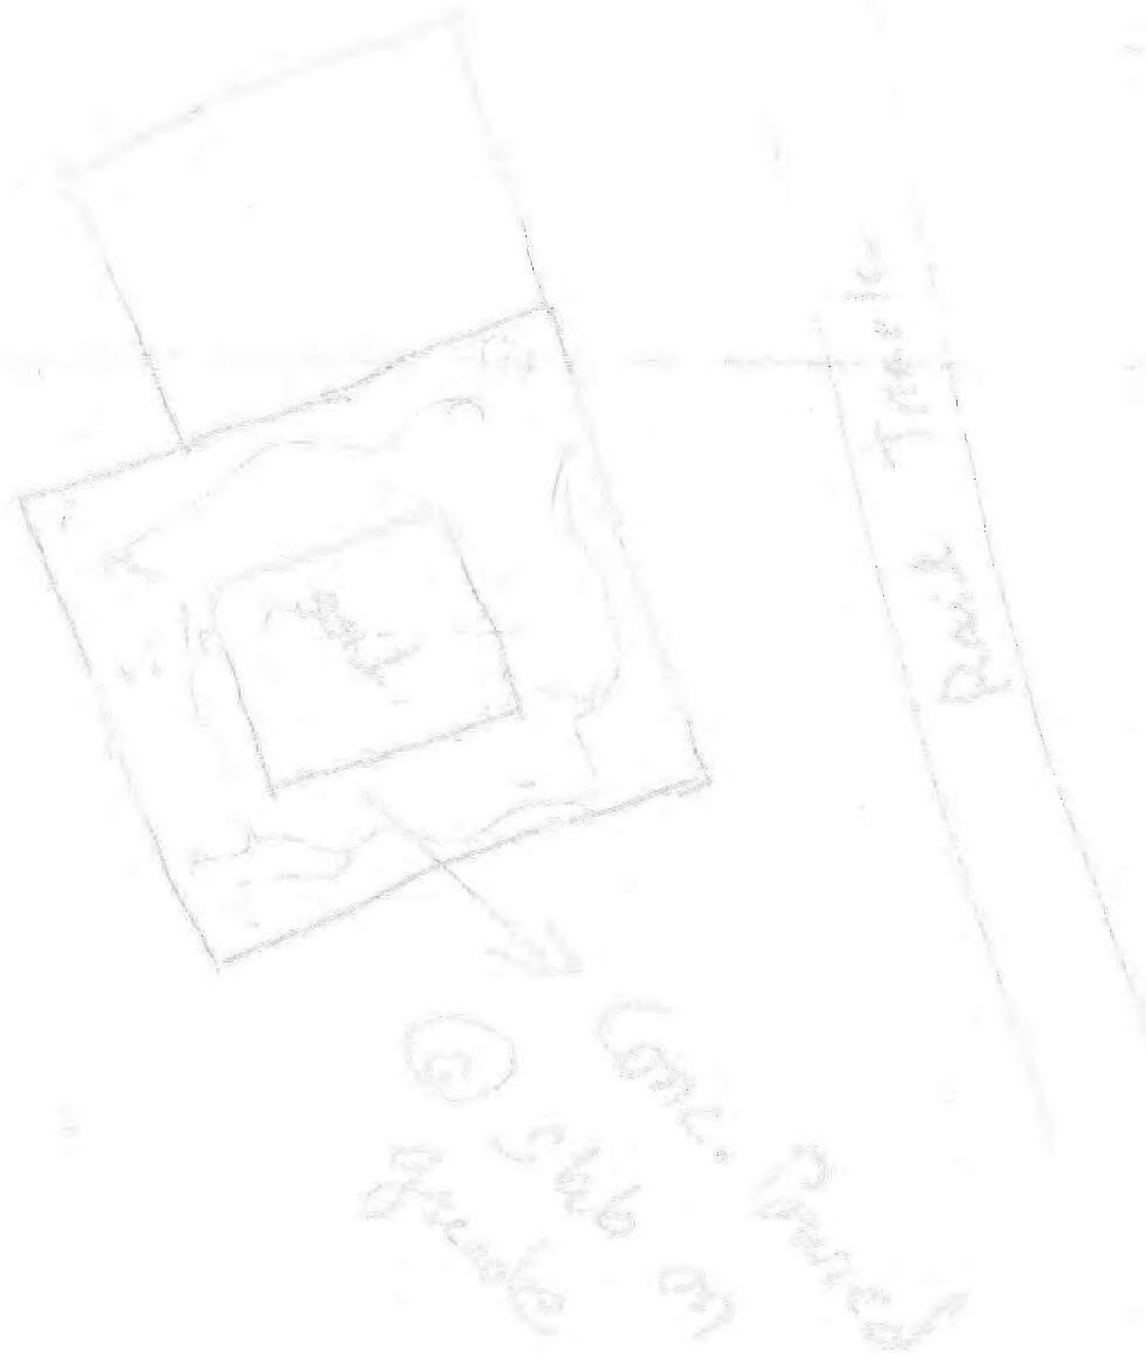

Project: 123 Bayclub Ave Burlingame
Client: CAPE INC.

[illegible]
[illegible]
[illegible]
[illegible]

[illegible]

CONSULTANTS, INC.
4435 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 549-ATUL
(908) 754-8383
Fax: (908) 754-8633

NJ HDA Approved Testing Laboratory • MRF/DSE Certified • NJ DEP Certified
www.ANSConsultants.net

Soil, Concrete, Masonry, Asphalt, Structural Steel, Fireproofing, Curtain Wall, Coatings, Roofing, Pile Driving, Storm/Sanitary Sewer, Underground Tanks & Piping

FILE NO. : ANX-1743 REPORT NO. : 04 DATE : 03/29/2011 PAGE NO. : 1 of 1

CLIENT : Cope Environmental Inc., 46 Pine Street, Suite – 110, Rockaway, NJ 07866 WEATHER : Sunny AIR TEMP. : 48°F

PROJECT : 122, Jackson Ave., Rockaway, NJ FINE AGG. : N/A

CONTRACTOR : Alini Corp. COARSE AGG. : N/A

CONCRETE SUPPLIER : Joel Tank & Sons Concrete CEMENT BRAND : N/A

REPORT OF CONCRETE INSPECTION AND TESTING — C-31

CLASS	4000	PSI		PSI
CUBIC YD.	BATCH WEIGHT LBS	BATCH WEIGHT LBS	BATCH WEIGHT LBS	BATCH WEIGHT LBS
CEMENT				
FINE AGG.				
COARSE AGG.				
COARSE AGG.				
WATER GALS.				
ADMIX. OZ. AEA				
ADMIX. OZ.				

PLANT	FIELD
PREVIOUS YARDAGE	44.00 Cu. yds.
YARDAGE	25.00 Cu. yds.
INSPECTED	13.00 Cu. yds.
TOTAL TO DATE	72.00 Cu. yds.
START	9 : 00 AM
FINISH	4 : 30 PM
TOTAL HRS.	8 : 00 Hrs.
INSP.	Soni

% PASSING	100	95	90	75	5	4	3/8	8	16	1	1½	F.M.	% MOIST
FINE AGG.													
COARSE AGG.													
COARSE AGG.													

NO. OF CYLS. & CLASS Five (5) cylinders - 4000 PSI (A/P) AIR CONTENT (%) (C-231) 6.0%

SLUMP (C-143) 4" DENSITY (C-138) 145 LBS/CU.FT. CONC. TEMP. (C-1064) 60°F

LOCATION Concrete was placed for slab on grade.

REMARK See attached records used.

CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI	CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI
1.	ANX-1743-15	Broke	3 days	51,500	1,718						
2.	ANX-1743-16	Cone & Shear	7 days	68,560	4,571						
3.	ANX-1743-17		14 days								
4.	ANX-1743-18		28 days								
5.	ANX-1743-19		28 days								

SPECIMEN 6" x 12" CYL. / AREA *3.14 SQ. IN.

Test performed as per A.S.T.M. specifications

T. Ch.

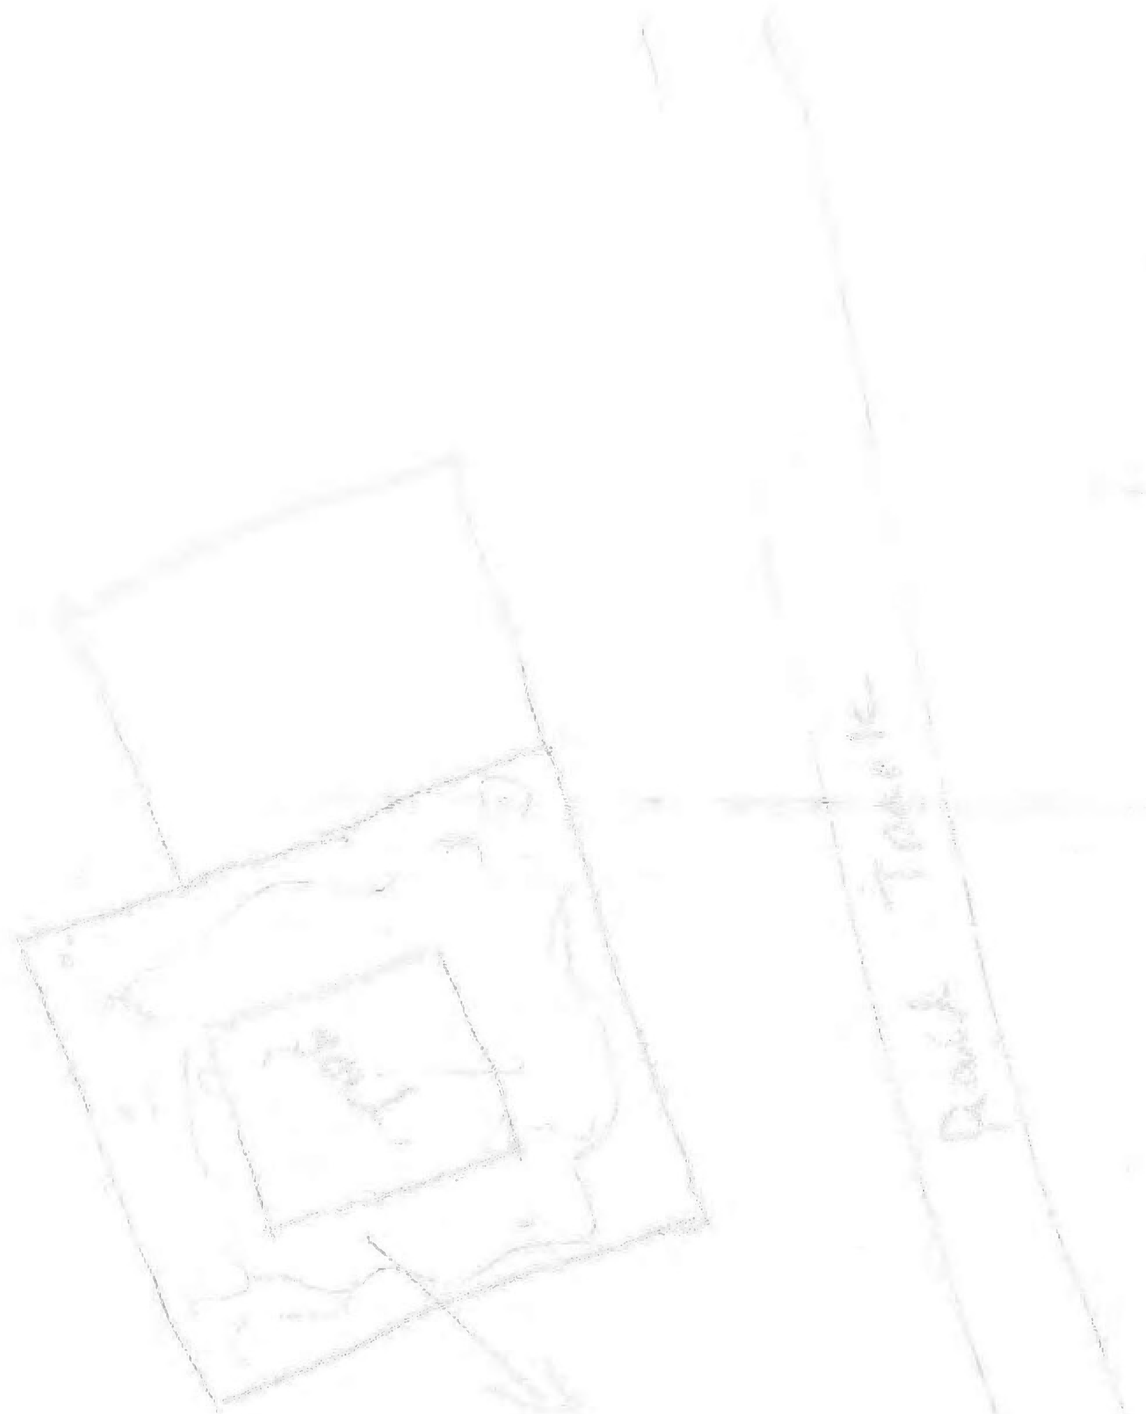

PROJECT:	123 Foundation Road Berkeley Way
DRAWN:	CAPE INC.

ABC CONSULTANTS INC.
1455 Some Street Address
Some Charlotte, ALASKA
(800) 1A-1BC

SHEET: C0.41 DATE: 08/29/11

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 345-ATUL
(908) 754-8383
Fax: (908) 754-8623

NJ DOA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSConsultants.net

Soil / Concrete Masonry / Asphalt Aggregate Steel Wood Fly Ash Cement Plastic Roofing Roof Facing Structural Masonry Curtain Wall Fireproofing Air Control Pavement Coring Diagnostic

FILE NO. : ANX-1743 REPORT NO. : 34 DATE : 03/28/2011 PAGE NO. : 1 of 1

CLIENT : Cuba Environmental Inc., 45 Pine Street, Suite - 7-C, Rockaway, NJ 07866 WEATHER : Sunny AIR TEMP. : 65°F

PROJECT : 122, Jackson Ave., Rockaway, NJ FINE AGG. : NA

CONTRACTOR : Abrd Canal COARSE AGG. : NA

CONCRETE SUPPLIER : Joel Taris & Sons Concrete CEMENT BRAND : NA

REPORT OF CONCRETE INSPECTION AND TESTING — C-31

CLASS	4000	PSI		PSI	PLANT	FIELD
CUBIC YD.	DESIGN WEIGHT LBS	ACTUAL WEIGHT LBS	DESIGN WEIGHT LBS	ACTUAL WEIGHT LBS	PREVIOUS YARDAGE	98.00 Cu. yds.
CEMENT					YARDAGE	25.00 Cu. yds.
FINE AGG.					INSPECTED	35.00 Cu. yds.
COARSE AGG.					TOTAL TO DATE	73.00 Cu. yds.
SCARRF AGG.					START	8 : 00 AM
WATER GALS.					FINISH	4 : 30 PM
ADMIX. 02					TO AL. PRE.	6 : 00 Hrs.
					MIXP.	Sort

% PASSING	1½"	1"	¾"	½"	⅜"	#4	#8	#16	#30	#50	#100	#200	F.M.	% EXCESS
FINE AGG.														
COARSE AGG.														
COMBIN. AGG.														

NO. OF CYLS. & CLASS Five (5) cylinders 4000 PSI (AIE) AIR CONTENT (%) (ASTM) 5.5%

SLUMP (ASTM) 4" UNIT WEIGHT (Lbs./ft.³) (ASTM) 142.54 CONC. TEMP (°F.) (ASTM) 50°F

LOCATION Concrete was placed for slab on grade.

REMARK
See Attached Location Plan

CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI*	CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI*
1.	ANX-1743-15	Shear	3 days	24,500	3,716						
2.	ANX-1743-16	Cone & Shear	7 days	36,500	5,372						
3.	ANX-1743-17		14 days								
4.	ANX-1743-18		28 days								
5.	ANX-1743-19		28 days								

SPECIMEN (6" x 12" CYL.) AREA 28.80 SQ. IN.

*Test performed as per A.S.T.M. specifications

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATCH
(908) 754-8383
Fax: (908) 754-8633

NJ EDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSConsults.net

Reg. Concrete Testing, Soils, Asphalt, Structural Steel, Fireproofing, Roofing, Exterior Curtain Wall, Construction Safety, QC Services, Environmental Testing & Audits

FILE NO. : ANX-1743 REPORT NO. : 04 DATE : 03/29/2011 PAGE NO. 1 of 1

CLIENT : Cape Environmental Inc., 46 Pine Street, Suite - 110, Rockaway, NJ 07866 WEATHER : Sunny AIR TEMP. 48°F

PROJECT : 120, Jackson Ave., Rockaway, NJ FINE AGG. : N/A

CONTRACTOR : Alini Corp. COARSE AGG. : N/A

CONCRETE SUPPLIER : Joel Tarlo & Sons Concrete CEMENT BRAND : N/A

REPORT OF CONCRETE INSPECTION AND TESTING --- 0.01

CLASS	4000	PSI		PSI	PLANT	FIELD
CLASS YD.	DESIGN WEIGHT LBS	PATCH WEIGHT LBS	ACTUAL WEIGHT LBS	ACTUAL WEIGHT LBS	PREVIOUS YARDAGE	48.00 Cu. yds.
CEMENT					YARDAGE	25.00 Cu. yds.
FINE AGG.					INSPECTED	25.00 Cu. yds.
COARSE AGG.					TOTAL TO DATE	73.00 Cu. yds.
COARSE AGG.					START	8 : 00 AM
WATER GALS.					FINISH	4 : 30 PM
ADMIX. DZ./ABA					TOTAL HRS.	8 : 00 Hrs.
ADMIX. DZ.					IN SP.	Sand

% PASSING	100	90	3D	1B	8	4	3/8	16	30	50	100	1K	F.M.	% VOIDS
FINE AGG.														
COARSE AGG.														
COARSE AGG.														

NO. OF CYLS. & CLASS Five (5) cylinders - 4000 PSI (A/E) AIR CONTENT (%) (ASTM C-231) 5.5%

SLUMP (ASTM C-143) 4" DENSITY (Unit. Wt. (ASTM C-138) 146.84 CONC. TEMP (°F) (ASTM C-1064) 60°F

LOCATION Concrete was placed for slab on grade.

REMARK See accompanying location plan.

CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI*	CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI*
1.	ANX-1743-15	Shear	2 days	31,400	1,775						
2.	ANX-1743-16	Cone & Shear	7 days	55,000	3,109						
3.	ANX-1743-17	Cone	14 days	48,000	2,712						
4.	ANX-1743-18		28 days								
5.	ANX-1743-19		56 days								

SPECIMEN (4" x 8" CYL.) AREA 12.56 SQ. IN. TEST performed as per A.S.T.M. specifications * 1 PSI

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 548-ATUL
(908) 754-8383
Fax: (908) 754-8633

NJ EDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSConsultants.net

Soil, Concrete, Masonry, Glass, Asphalt, Structural Steel, Precast, Piles, Drilling, Blasting, Roofing, Tell Beam, Cementitious Coatings, (Q) Fire and Underwriters Labs & Factory

FILE NO. : ANX-1743 REPORT NO. : 04 DATE : 09/20/2017 PAGE NO. : 1 of 1

CLIENT : Cape Environmental Inc., 48 Pine Street, Suite - 119, Rockaway, NJ 07866 WEATHER : Sunny AIR TEMP. : 68°F

PROJECT : 122, Jackson Ave., Rockaway, NJ FINE AGG. : N/A

CONTRACTOR : Allini Const COARSE AGG. : N/A

CONCRETE SUPPLIER : Joel Tanis & Sons Concrete CEMENT BRAND : N/A

REPORT OF CONCRETE INSPECTION AND TESTING — C-31

CLASS	4000	PSI		PSI	PLANT	FIELD
MIX/C YD.	DESIGN WEIGHT Lbs	ACTUAL WEIGHT Lbs	DESIGN WEIGHT Lbs	ACTUAL WEIGHT Lbs	PREVIOUS YARDAGE	48.00 Cu. yds.
CEMENT					YARDAGE	24.00 Cu. yds.
FINE AGG.					INSPECTED	36.00 Cu. yds.
COARSE AGG.					TOTAL TO DATE	72.00 Cu. yds.
COARSE AGG.					START	8 : 00 AM
WATER GALS.					FINISH	4 : 30 PM
ADMIX. OZ./ADA					TOTAL HRS.	8 : 30 Hrs.
ADMIX. OZ.					INSP.	Sant

% PASSING	150	90	30	16	8	4	3/8	3/4	3/4	1	1½	F.M.	% MOIST
FINE AGG.													
COARSE AGG.													
COARSE AGG.													

NO. OF CYLS. & CLASS Five (5) cylinders - 4000 PSI (A/E) AIR CONTENT (%) (C-231) 5.5%

SLUMP (C-143) 4" DENSITY (Wgt. lb. (C-138) 149 lbs CONC. TEMP (°F) (C-1064) 68°F

LOCATION Concrete was placed for slab on grade.

REMARK
Now attached location plan.

CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI*	CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI*
1.	ANX-1743-15	Shear	3 days	25,300	1,700						
2.	ANX-1743-16	Cone & Shear	7 days	36,650	2,500						
3.	ANX-1743-17	Cone	14 days	46,830	3,170						
4.	ANX-1743-18		28 days								
5.	ANX-1743-19		28 days								

SPECIMEN (4" x 8") C.S. AREA 12.56 SQ. IN. Tests performed as per A.S.T.M. specifications

CONSULTANTS, INC.
4405 South Clinton Avenue
South Plainfield, NJ 07080

Tel: (800) 545-ATLL
(908) 754-8383
Fax: (908) 754-8633

NJ EDA Approved Testing Laboratory • MBE/DBE Certified • NJ DEP Certified
www.ANSConsultants.net

Soil Engineer, Materials Testing, Asphalt, Structural Steel, Concrete, Fireproofing, Welding Inspection, Roofing, Concrete Sampling, Soil Mechanics, Environmental Testing & Analysis

FILE NO. : ANX-1743 REPORT NO. : 04 DATE : 03/28/2011 PAGE NO. 0 of 1

CLIENT : Gaga Environmental Inc., 45 Rice Street, Suite 112, Rockaway, NJ 07866 WEATHER : Sunny AIR TEMP. 45°F

PROJECT : 122, Jackson Ave., Middlesex, NJ FINE AGG. : N/A

CONTRACTOR : Albri Corcat COARSE AGG. : N/A

CONCRETE SUPPLIER : Joel Tanis & Sons Concrete CEMENT BRAND : N/A

REPORT OF CONCRETE INSPECTION AND TESTING — C-31

CLASS	4000 PSI		PSI		PLANT	FIELD
CUBIC YD.	DESIGN WEIGHT LBS	SACKS WEIGHT LBS	DESIGN WEIGHT LBS	SACKS WEIGHT LBS	PREVIOUS YARDAGE	48.00 Cu. yds.
CEMENT					YARDAGE	25.00 Cu. yds.
FINE AGG.					INSPECTED	25.00 Cu. yds.
COARSE AGG.					TOTAL TO DATE	73.00 Cu. yds.
COARSE AGG.					START	8 : 00 AM
WATER GALS.					FINISH	4 : 30 PM
ADMIX. OZ.-AEA					TOTAL HRS.	8 . 00 Hrs.
ADMIX. OZ.					INSP.	Soil

% PASSING	150	80	40	16	8	4	3/8	16	30	1	1½	F.M.	% AIR/BT
FINE AGG.													
COARSE AGG.													
COARSE AGG.													

NO. OF CYLS. & CLASS Five (5) Cylinders - 4000 PSI. (A/E) AIR CONTENT (%) (C-231) 5.0%

SLUMP (C-143) 4" SPECIFIC Grav. G. (C-140) 144.24 CONC. TEMP (°F) (C-1064) 80°F

LOCATION Concrete was placed for slab on grade.

REMARK See attached location plan

CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI*	CYL. NO.	LAB. ID NO.	TYPE OF FRACTURE	TESTED AT	TOTAL LOAD	PSI*
1.	ANX-1743-18	Shear	3 days	20,500	1,750						
2.	ANX-1743-19	Cone & Shear	7 days	28,650	2,375						
3.	ANX-1743-17	Cone	14 days	46,650	3,710						
4.	ANX-1743-20		28 days								
5.	ANX-1743-16		28 days								

SPECIMEN: 6" x 12" CYL.(ASTM C 39) 12.56 SQ. IN. Test performed as per A.S.T.M. specifications T: C-39
