Third West Air Monitor Result
Shepherd, Michael
to:
Joyce Ackerman, 'Craig Barnitz (cbamitz@utah.gov)'
07/16/2012 04:55 PM
Hide Details
From: "Shepherd, Michael" <Michael.Shepherd@rockymountainpower.net>

To: Joyce Ackerman/R8/USEPA/US@EPA, "'Craig Bamitz (cbamitz@utah.gov)'" <cbamitz@utah.gov>

1 Attachment

239873-1R.pdf

Joyce & Craig,

We had a positive hit on Monday, July 9, 2012. It was chrysotile, see the attached. Please let me know if you have any questions or concerns.

Thanks,

Mike Shepherd
Project Manager
Rocky Mountain Power - Major Projects
801.220.4584 Office
801.631.1310 Cell
801.220.2797 Fax
michael.shepherd@pacificorp.com

REI LAB Reservoirs Environmentol, Inc.

July 16, 2012

Laboratory Code:	RES
Subcontract Number:	NA
Laboratory Report:	RES 239873-1R
Project # / P.O. #	None Given
Project Description:	3rd West Sub - RMP

Eldon Romney
R & R Environmental
47 West 9000 South #2
Sandy UT 84070

Dear Customer,

Reservoirs Environmental, Inc. is an analytical laboratory accredited for the analysis of Industrial Hygiene and Environmental matrices by the National Voluntary Laboratory Accreditation Program (NVLAP), Lab Code 101896-0 for Transmission Electron Microscopy (TEM) and Polarized Light Microscopy (PLM) analysis and the American Industrial Hygiene Association (AIHA), Lab ID 101533 - Accreditation Certificate #480 for Phase Contrast Microscopy (PCM) analysis. This laboratory is currently proficient in both Proficiency Testing and PAT programs respectively.

Reservoirs Environmental, Inc. has analyzed the following samples for asbestos content as per your request. The analysis has been completed in general accordance with the appropriate methodology as stated in the attached analysis table. The results have been submitted to your office.

RES 239873-1R is the job number assigned to this study. This report is considered highly confidential and the sole property of the customer. Reservoirs Environmental, Inc. will not discuss any part of this study with personnel other than those of the client. The results described in this report only apply to the samples analyzed. This report must not be used to claim endorsement of products or analytical results by NVLAP or any agency of the U.S. Government. This report shall not be reproduced except in full, without written approval from Reservoirs Environmental, Inc. Samples will be disposed of after sixty days unless longer storage is requested. If you have any questions about this report, please feel free to call 303-964-1986.

Sincerely,

Jeanne Spencer
President

RESERVOIRS ENVIRONMENTAL, INC.

NVLAP Lab Code 101896-0; TDH: #30-0015

TABLE I. TEM AIR FILTER SAMPLE DATA AND ANALYTICAL RESULTS

RES Job Number:	RES 239873-1R
Client:	R & R Environmental
Client Project Number / P.O.:	None Given
Client Project Description:	3rd West Sub - RMP
Date Samples Received:	July 11, 2012
Analysis Type:	TEM, AHERA
Turnaround:	24 Hour
Date Samples Analyzed:	July 11, 2012

Client ID Number	Lab ID Number	Area Analyzed	Air Volume Sampled	Number of Asbestos Structures Detected	Analytical Sensitivity	Asbestos Concentration	Filter Loading
		(mm^2)	(L)		(s/cc)	(s/cc)	(s/mm^2)
3W-070912 E	EM 891601	0.1000	812	1	0.0047	0.0047	10.0
3W-070912 N	EM 891602	0.1000	812	ND	0.0047	BAS	BAS
3W-070912 W	EM 891603	0.1000	814	ND	0.0047	BAS	BAS
3W-070912 S	EM 891604	0.1000	815	ND	0.0047	BAS	BAS

NA = Not Analyzed
ND = None Detected
BAS = Below Analytical Sensitivity
Average Grid Opening in mm^2 = 0.010

Filter Material = Mixed Cellulose Ester
Filter Diameter = 25 mm
Effective Filter Area = 385 sq mm

Digitally signed by Gina Valtierra
Date: 2012.07.16 14:35:14 -06'00'

DATA QA

RESERVOIRS ENVIRONMENTAL, INC.

NVLAP Lab Code 101896-0; TDH: #30-0015

TABLE II. SUMMARY OF ANALYTICAL DATA

RES Job Number:	RES 239873-1R
Client:	R & R Environmental
Client Project Number / P.O.:	None Given
Client Project Description:	3rd West Sub - RMP
Date Samples Received:	July 11, 2012
Analysis Type:	TEM, AHERA
Turnaround:	24 Hour
Date Samples Analyzed:	July 11, 2012

Client ID Number	Lab ID Number	Asbestos Mineral	Asbestos Structure Types*				Structures >5 Microns in Length	**Excluded Structures	Asbestos Structures for Concentration
			Fibers	Bundles	Clusters	Matrices			
3W-070912 E	EM 891601	Chrysotile	1	0	0	0	0	0	1
3W-070912 N	EM 891602	ND	0	0	0	0	0	0	0
3W-070912 W	EM 891603	ND	0	0	0	0	0	0	0
3W-070912 S	EM 891604	ND	0	0	0	0	0	0	0

*See Analytical Procedure for definitions
**C = Excluded from total due to lack of confirmation
**L = Excluded from total for length less than 0.5 micron (AHERA only)
**A = Excluded from total due to incorrect aspect ratio
ND = None Detected

Due Date: 7·12·12
Due Time: 9AM

Reservoirs Environmental, Inc.

RES 239873

3601 Logan St. Denver, CO 80216 • Ph: 303 964-1988 • Fax 303-477-4275 • Toll Free :866 RESI-ENV
Pager : 303-609-2098

INVOICE TO: (IF DIFFERENT)		CONTACT INFORMATION:	
Company: R&R Environmental	Company:	Contact: Dave Rockelley	Contact:
Address:	Address:	Phone:	Phone:
		Fm:	Fax:
		Cell/pager: 801 541-1035	Cell/pager:
Project Number and/or P.O. #:		Final Data Deliverable Email Address:	
Project Description/Location: 47W 9X805 #2		dave@rrenviro.com	

ASBESTOS LABORATORY HOURS: Weekdays: 7am - 7pm
PLM / PCM (TEM) ___ RUSH (Same Day) X PRIORITY (Next Day) ___STANDARD
(Rush PCM = 2hr, TEM = 6hr.)

CHEMISTRY LABORATORY HOURS: Weekdays: 8am - 5pm
Metal(s) / Dust ___ RUSH ___ 24 hr. ___3-5 Day
RCRA 8 / Metals & Welding Fume Scan / TCLP ___ RUSH ___ 5 day ___10 day
Organics ___ 24 hr. ___ 3 day ___ 5 Day
Prior notification is required for RUSH turnarounds.

MICROBIOLOGY LABORATORY HOURS: Weekdays: 9am - 6pm
E.coli 0157:H7, Coliforms, S.aureus ___ 24 hr. ___2 Day ___3-5 Day
Salmonella, Listeria, E.coli, APC, Y & M ___ 48 Hr. ___3-5 Day
Mold ___ RUSH ___24 Hr ___48 Hr ___3 Day ___6 Day

Turnaround times establish a laboratory priority, subject to laboratory volume and are not guaranteed. Additional fees apply for afterhours, weekends and holidays.

Special Instructions:

	Client sample ID number (Sample ID's must be unique)	PLM - Short report, Long report, Point Count	TEM - AHERA, Level II, 7402, ISO, +/- Quant, Semi-quant, Micro-vac, ISO-Indirect Preps	PCM - 7400A, 7400B, OSHA	DUST - Total, Respirable	METALS - Analyte(s) RCRA 8, TCLP, Welding Fume, Metals Scan	ORGANICS - METH	MICROBIOLOGY: Salmonella: +/-	E.coli 0157:H7: +/-	Listeria: +/-	Aerobic Plate Count: +/- or Quantification	E.coli: +/- or Quantification	Coliforms: +/- or Quantification	S.aureus: +/- or Quantification	Y & M: +/- or Quantification	Mold: +/-, Identification, Quantification	SAMPLER'S INITIALS OR OTHER NOTES	Sample Volume (L) / Area	Matrix Code	# Containers	Date Collected mm/dd/yy	Time Collected hh/mm a/p	EM Number (Laboratory Use Only)
1	3w-070912 E		X															812	A		7/09/12		891601
2	3w-070912 N		↓															812	↓		↓		2
3	3w-070912 W																	814					3
4	3w-070912 S																	815					4
5																							
6																							
7																							
8																							
9																							
10																							

VALID MATRIX CODES

Air = A	Bulk = B
Dust = D	Paint = P
Soil = S	Wipe = W
Swab = SW	F = Food
Drinking Water = DW	Waste Water = WW
O = Other	

ASTM E1792 approved wipe media only

LAB NOTES:

Nuinber of samples received: 4 (Additional samples shall be listed on attached long form.)

NOTE: REI will analyze incoming samples based upon information received and will not be responsible for errors or omissions in calculations resulting from the inaccuracy of original data. By signing client/company representative agrees that submission of the following samples for requested analysis as indicated on this Chain of Custody shall constitute an analytical services agreement with payment terms of NET 30 days, failure to comply with payment terms may result in a 1.5% monthly interest surcharge.

Relinquished By: [signature] FedEx Date/Time: 7/09/12
Laboratory Use Only
Received By: [signature] Date/Time: 7·11·12 9AM Carrier: FedEx

Sample Condition: On Ice Yes / No — Sealed Yes / No — Intact Yes / No
Temp. (F°) ____

Results: Contact Dave Phone Email Fax Date 7/11 Time 8:45 Initials JK
Contact Phone Email Fax Date 7/12 Time 8:00 Initials
Contact Phone Email Fax Date Time Initials
Contact Phone Email Fax Date Time Initials

7737 4883 4 5336

Attachment I

Key to Count Sheets
Count Sheets
Analytical Procedures

Structures identifications consist of an Asbestos Type followed by a Structure Type

Asbestos Type	Structure Types
A = Amosite	F = Fiber
An = Anthophyllite	B = Bundle
C = Chrysotiie	C = Cluster
Cr = Crocidolite	M = Matrix
T = Tremolite	

ND = no structures detected
M = other structure associated with a matrix
NAM = Non Asbestos Mineral
XGB = partly obscured by a grid bar

Sizing Conversion
1 length unit = 5 mm on screen = 0.278 micron
1.80 length units = 0.5 micron
18.0 length units = 5 microns

1 width unit = 1 mm on screen = 0.0556 micron

TEM Analysts

Jeanne S. Orr	Paul D. LoScalzo
Nathan DelHierro	Mark Steiner
Angela Heitger	Norberto Zimbleman
Jonathan Bernard	Robert Workman

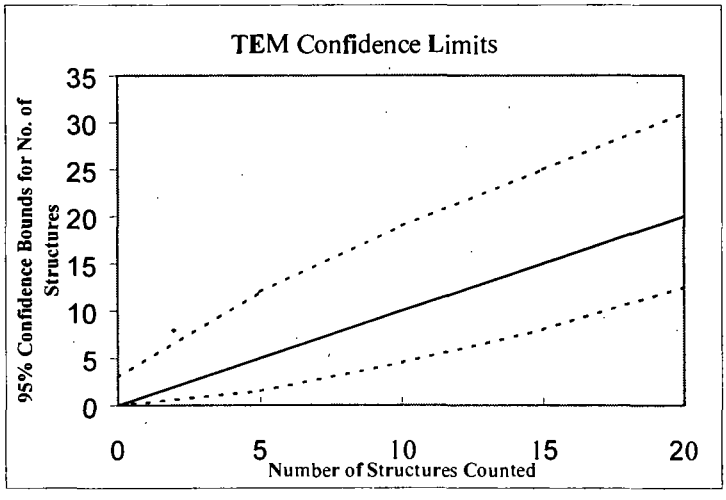

Upper and lower 95% confidence bounds for the number of structures counted assuming a Poisson distribution.

Reservoirs Environmental, Inc.
TEM Asbestos Structure Count

Laboratory name:	Resrvoirs Environmental, Inc.
Instrument	JEOL 100 CX (N) (S)
Voltage (KV)	100 KV
Maanification	20KX 10KX
Grid opening area (mnr2)	0.010
Scale: 1L =	0.28 um
Scale: 1D =	0.056 um
Primary fitter area (mm2)	385
Secondary Filler Area (mm2)	
QA Type	

Client :	R+R
Sample Type (A=Air, D=Dust):	A
Air volume (L) or dust area (cm2)	812
Oate received by lab	7/11/12
Lab Job Number:	239873
Lab Sample Number:	89160

F-Factor Calculation (Indirect Prepa Only):

Fraction of primary filter used	
Total Resuspension Volume (ml)	
Voluma Applied to seeondary filter (ml)	

Analyzed by	TK
Analysis date	7/11/12
Method (D=Direct, I=Indirect, IA=Indirect, astied)	D
Counting rules (ISO, AHERA, ASTM)	AH
Grid storage location	Month Analyzed
Scope Alignmenl	Date Analyzed

Grid	Grid Opening	Stmcture Type	No. of Stnictures		Dimensions		Identification	Mineral Class			Sketch/Comments	1 = yes, blank = no		
			Primary	Total	Length	Width		Amphibole	C	NAM		Sketch	Photo	EDS
A	H3-3	ND												
	G3-3	ND			Prep A 50% intact 0 8 debris									
	F3-3	ND												
	E3-3	ND												
	E3-4	ND												
B	H5-1	ND												
	G5-1	F		1	2	1	CD		-		1			
	F5-1	ND												
	F6-4	ND			Prep B-4H									
	E6-4	ND												

IA = Libby-type amphibole OA = Other (non-Libby type) amphibole C = Chrysofile NAM = Non-asbestos material

Reservoirs Environmental, Inc.
TEM Asbestos Structure Count

Laboratory name:	Resrvoirs Environmental, Inc.
Instrument	JEOL 100 CX (N) (S)
Voltage (KV)	100 KV
Magnification	(20KX) 10KX
Grid opening area (mm2)	0.010
Scale: 1L =	0.28 um
Scale: 1D =	0.056 um
Primary filter area (mm2)	385
Secondary Filter Area (mm2)	
QA Type	

Client :	R+R
Sample Type (A=Air, D=Dust):	A
Air volume (L) or dust area (cm2)	812
Date received by lab	7/11/12
Lab Job Number:	239873
Lab Sample Number:	891602

Analyzed by	[illegible]
Analysis date	7/11/12
Method (D=Direct, I=Indirect, IA=Indirect, ashed)	D
Counting rules (ISO, AHERA, ASTM)	AH
Grid storage location	Month Analyzed
Scope Alignment	Date Analyzed

F-Factor Calculation (Indirect Preps Only):

Fraction of primary filter used	
Total Resuspension Volume (ml)	
Volume Applied to secondary filter (ml)	

Grid	Grid Opening	Structure Type	No. of Structures		Dimensions		Identification	Mineral Class			Sketch/Comments	1 = yes, blank = no		
			Primary	Total	Length	Width		Amphibole	C	NAM		Sketch	Photo	EDS
A	F4-3	ND												
	E4-3	ND			Prep A 50 mtae 52 debris									
	C4-3	ND												
	F4-1	ND			Prep B ~A									
	E4-1	ND												
B	F3-3	ND												
	E3-3	ND												
	C3-3	ND												
	C3-4	ND												
	B3-4	ND												

LA = Libby-type amphibole OA = Other (non-Libby type) amphibole C = Chrysotile NAM = Non-asbestos material

Reservoirs Environmental, Inc.
TEM Asbestos Structure Count

Laboratory name:	Resrvoirs Environmental, Inc.
Instmment	JEOL 100 CX (N) (S)
Voltage (KV)	100 KV
Magnification	(20KX) 10KX
Grid opening area (mm2)	0.010
Scale: 1L =	0.28 um
Scale: 1D =	0.056 um
Primary filter area (mm2)	385
Secondary Filter Area (mm2)	
QA Type	

Client :	R+R
Sample Tyoe (A=Air, D=Dust):	A
Air volume (L) or dust area (cm2)	814
Date received by lab	7/11/12
Lab Job Number:	239873
Lab Sample Number:	891603

F-Factor Calculation (Indirect Preps Only):

Fraction of primary filter used	
Total Resuspension Volume (ml)	
Volume Applied to secondary filter (ml)	

Analyzed by	TK
Analysis date	7/11/12
Method (D=Direct, I=Indirect, IA=Indirect, ashed)	D
Counting rules (ISO, AHERA, ASTM)	AH
Grid storage location	Month Analyzed
Scope Afignment	Date Analyzed

Grid	Grid Opening	Stmcture Type	No. of Structures		Dimensions		Identification	Mineral Class			Sketch/Comments	1 = yes, blank = no		
			Primary	Total	Length	Width		Amphibole	C	NAM		Sketch	Photo	EDS
A	K2-3	ND												
	H2-3	ND				Prep	A ~50% intact 5% debris							
	H3-1	ND												
	G3-1	ND				Prep	B ~60% intact 5% debris							
	E2-6	ND												
B	H3-4	ND												
	G3-4	ND												
	F3-4	ND												
	E3-4	ND												
	C3-3	ND												

LA = Libby-type amphibole OA = Other (non-Libby type) amphibole C = Chrysotile NAM = Non-asbestos material

Reoervoirs Environmental, Inc.
TEM Asbestos Structure Count

Laboratory name:	Resrvoirs Environmental, Inc.
Instmment	JEOL 100 CX (N) (S)
Voltage (KV)	100 KV
Magnification	(20KX) 10KX
Grid opening area (mm2)	0.010
Scale: 1L =	0.28 um
Scale: 1D =	0.056 um
Primary filter area (mm2)	385
Secondary Filter Area (mrh2)	
QA Type	

Client :	R+R
Sample Type (A=Air, D=Dust):	A
Air volume (L) or dust area (cm2)	815
Date received by lab	7/11/12
Lab Job Number:	239873
Lab Sample Number:	891604

F-Factor Calculation (Indirect Preps Only):

Fraction of primary filter used	
Total Resuspension Volume (ml)	
Volume Applied to secondary filter (ml)	

Analyzed by	YK
Analysis date	7/11/12
Method (D=Direct, I=Indirect, IA=Indirect, ashed)	D
Counting mles (ISO, AHERA, ASTM)	AH
Grid storage location	Month Analyzed
Scope Alignment	Date Analyzed

Grid	Grid Opening	Structure Type	No. of Stmctures		Dimensions		Identification	Mineral Class			Sketch/Comments	1 = yes, blank = no		
			Primary	Total	Length	Width		Amphibole	C	NAM		Sketch	Photo	EDS
A	F2-3	ND												
	E2-3	ND			Prep A 50% intact 50% debris									
	C2-3	ND												
	B2-3	ND			Prep B									
	A3-4	ND												
B	E2-6	ND												
	C2-6	ND												
	B2-6	ND												
	A2-6	ND												
	A3-4	ND												

LA = Libby-type amphibole OA = Other (non-Libby type) amphibole C = Chrysofile NAM = Non-asbestos material

Analytical Procedures – AHERA

Transmission electron microscopy/energy dispersive X-ray spectrometry/selected area electron diffraction (TEM/EDX/SAED) was employed in the analysis of the samples, which were collected on 25 mm mixed cellulose ester air filters. A portion of each filter was collapsed with acetone and etched in a plasma asher. The etched filter was then coated with a thin layer of carbon in a carbon side down. The sample was then placed inside a condensation washer and treated with acetone to remove the filter matrix and expose any inert material.

For each sample, enough grid openings on a 200 mesh TEM grid are analyzed to ensure an analytical sensitivity of at least 0.005 structures/cc. A minimum of four grid openings from two preparations are analyzed for each sample. The grid openings are searched for fibrous structures which, if present are analyzed by SAED and/or EDX (elemental analysis). The AHERA protocol requires SAED confirmation of enough chrysotile asbestos structures on each sample to cause the sample to exceed 70 structures/mm^2 (usually 4 or 5 structures). Both SAED and EDX confirmation are required of enough amphibole structures on each sample to cause the sample to exceed 70 structures/mm^2 (usually 4 or 5 structures) per sample. Either SAED or EDX is required for the remaining asbestos structures of either type. The morphology of each structure is determined and the length and the diameter of any asbestos structures are recorded. Asbestos fibers, bundles, cluster and matrices were identified and recorded. The asbestos structures have been defined in AHERA as follows:

Fiber:	is a structure having a minimum length greater than or equal to 0.5 micron with an aspect ratio of 5:1 or greater with substantially parallel sides.
Bundle:	is a structure composed of three or more fibers in parallel arrangement, with each fiber closer than the diameter of one fiber.
Cluster:	is a structure with fibers in random arrangements such that all fibers are intermixed and no single fiber is isolated from the group.
Matrix:	is a fiber or fibers with one end free and the other end embedded or hidden by a particulate. The exposed fiber end must meet the fiber definition given above.

If more than 50 asbestos structures are identified and confirmed on a sample, AHERA analysis may be terminated after completion of the grid opening, which contains the 50^{th} structure. AHERA protocol requires the laboratory to reject any clearance sample which contains in excess of 25% total particulate loading or which appears to be unevenly loaded.

The AHERA protocol includes specific sampling requirements, including minimum numbers of samples and minimum air volumes. Specifically, the 70 structures/mm^2 clearance criteria is only allowed for sets five inside samples (collected in a group of 13 samples including: five outsides and three blanks) with volumes greater than 1200 liters (40 CFR Part 763, page 41894). Deviation from the AHERA sampling protocol may affect the validity of the analytical results. Analysis of samples collected by non-protocol methods are not accredited by NVLAP

Equations Used for Calculations

$$\text{Area Analyzed, } mm^2 = \#\text{ GO counted} \times \text{Average GO Area (mm)}$$

$$\text{Concentration, s/cc} = \frac{\#\text{ Asbestos Structures}}{\#\text{ GO Counted}} \times \frac{1}{\text{Volume (L)}} \times \frac{\text{Eff. Filter Area } (mm^2)}{\text{Average GO area } (mm^2)} \times \frac{1\text{L}}{1000\text{cc}}$$

$$\text{Filter loading, s/mm}^2 = \frac{\#\text{ Asbestos structures}}{\text{Area Analyzed } (mm^2)}$$

GO = TEM grid opening

File: Shared on server T/Offforms.sg/AHERA Procedures
Revised. 02/27/02
