PROJECT: Daikes-Alcoa
DATE: 11/6/13
WEATHER: Cloudy, 61°F
OBJECTIVE: UST inspection

10:05 Arrive
USTs being cut
notified Mark Iafelice (Daikes)

10:10 Inspect USTs
- T-1 - 3 holes at SE corner of Tank (3/4 - 1 1/2" ø)
- Install (3) exploratory test pits to east of USTs
- free product in T-2 excavation
- T-2 - being cut (shell)
- gave M. Iafelice notice of closure and DEP case # 13-10-10-1558-57

10:20 Install test pits

TP-1
0'-8' fill w/ brick, f-c sand, f-c gravel, cobbles + concrete, dry
8'+ bedrock
visual staining, no odor @ 6'-8'

TP-2
0'-4' fill w/ brick, concrete + metal debris, f-c sand, f-c gravel, cobbles + boulders, dry
4'-8' Red/brown f-c sand, weathered rock, dry
8'+ Bedrock
- grey/brown staining @ ~4'-6' (no odor)

- Recommended to M. Iafelice to cut out/save corrosion holes for future evidentiary use
- Requested copies of scrap receipts
- REC/EWMI to mobilize 11/7/13 @ 7 AM
- Updated Matt Vereb (Daikes) via voicemail message

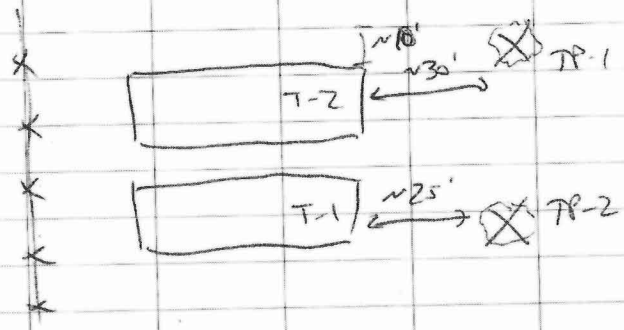

11:04 M. Iafelice leaves

11:10 leave site

Without Call 11/6/13
