MEMORANDUM

State of New Jersey
Department of Environmental Protection

TO: File

INVESTIGATIVE REPORT

1:00

37324

FROM: Jim Edwards

DATE: June 27, 1979

SUBJECT: National Gypsum

I met with Herb May, contractor employed by Gypsum & Bill Bryant, engineer employed by Gypsum on site. I noted two machines working on site, 1 excavator & 1 dozer. The excavator was excavating an approx. 2' trench in channel. Dredging, deposited in channel to block water from filling in trench & dredging also being deposited on bank. Bank is not to be excavated, according to engineer. Riprap will be cemented in trench & built up over bank approx. 4'. Engineer states Gypsum stated approval of this method from our office. Information I had previously received indicated excavation of bank to be redeposited some feet back. The method now in operation will narrow the channel. The operation is to continue the length of the bank.

Jim Edwards

ASB 002 0237

MEMO

NEW JERSEY STATE DEPARTMENT OF ENVIRONMENTAL PROTECTION

TO

FROM DATE

SUBJECT

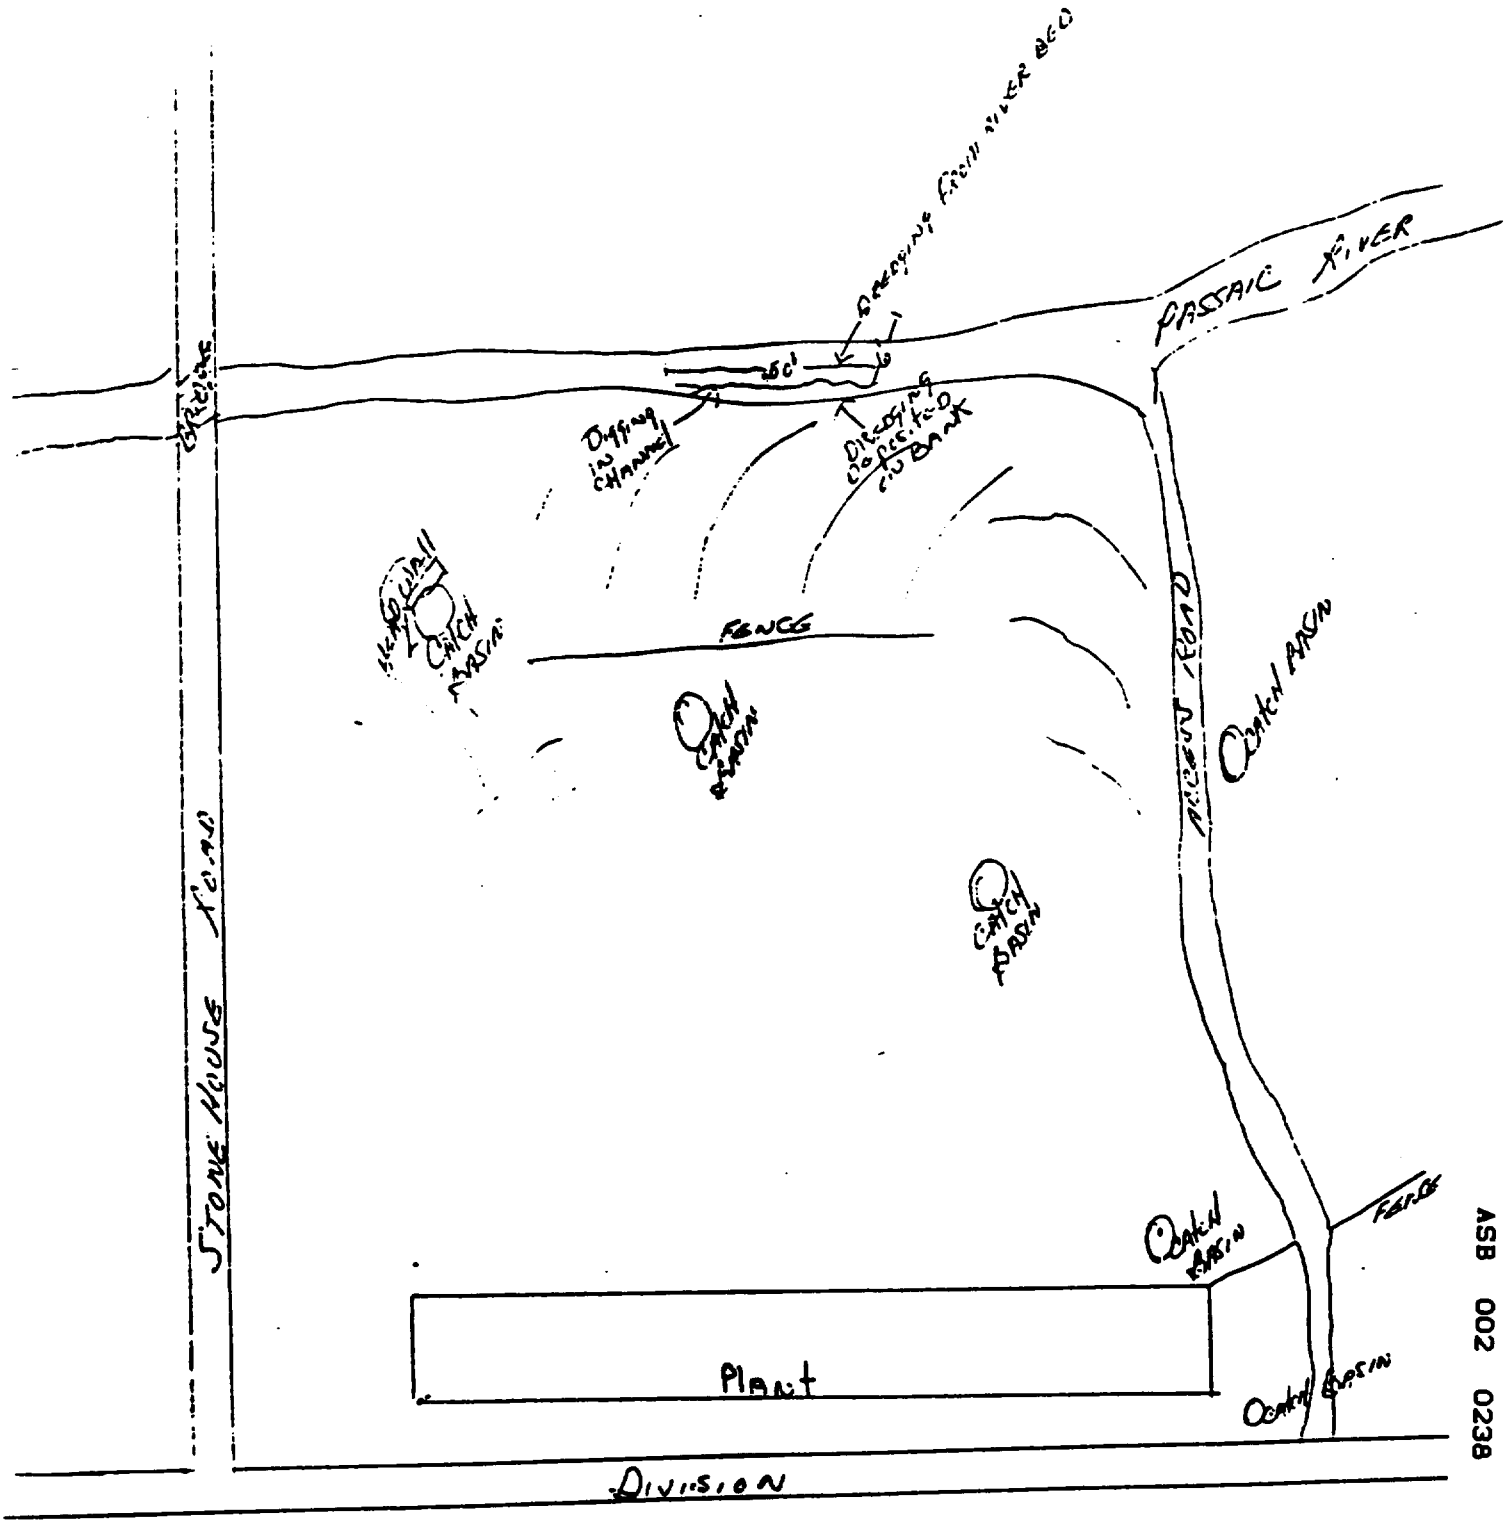

ASB 002 0238
