NATIONWIDE ENVIRONMENTAL SERVICES, INC.

6th Avenue West Business Park
14818 W 6th Ave. Suite 5A
Golden, CO 80401

February 12, 2015

Mr. Tim Drexler
Remedial Project Manager
U.S. Environmental Protection Agency
77 West Jackson Boulevard, HSRM-6J
Chicago, IL 60604

Mr. Doyle W. Wilson
Illinois Environmental Protection Agency
1021 North Grand Avenue East
P.O. Box 19276
Springfield, IL 62794-9276

RE: Southeast Rockford Groundwater Contamination Site
Groundwater Monitoring Report
Semi-Annual Monitoring Event – November 2014

Gentlemen:

Nationwide Environmental Services, Inc. (NES) is submitting the semi-annual monitoring report presenting the analytical data and data interpretation summary for groundwater quality monitoring samples collected at the Southeast Rockford Groundwater Contamination Site (the Site) during the November 2014 semi-annual monitoring event. The groundwater monitoring data obtained for the current reporting period will also be submitted in an MS Excel™ file separately via e-mail.

Please contact me at telephone (303) 232-2134 if you have any questions regarding the information provided or require any additional information.

Sincerely,

William B. Dotterer,
Sr. Project Manager

cc: Nadine Miller, City of Rockford

Enclosures

US EPA RECORDS CENTER REGION 5
521812

Southeast Rockford Groundwater Contamination Site
Groundwater Monitoring Report
Semi-Annual Monitoring Event - November 2014

February 2015

Nationwide Environmental Services, Inc.

Southeast Rockford Groundwater Contamination Site
Groundwater Monitoring Report

Overview

The second semi-annual monitoring event for calendar year 2014 was performed at the Southeast Rockford Groundwater Contamination Site (Site) during November. The field sampling activity and analytical procedures utilized for the current monitoring event were performed in accordance with the Quality Assurance Project Plan (as amended 2008) and the Field Sampling Plan (FSP) (as amended 2010).

The intent of the Site groundwater monitoring program is to monitor the status of the affected aquifer within the Site extents, relative to groundwater clean-up standards established under the Record of Decision (ROD), as well as, monitor the influence of designated Site source areas and associated remediation activities on aquifer restoration goals. The following report presents the results of the current monitoring event, and a comparison of groundwater monitoring data obtained during this monitoring event to analytical data from prior monitoring events.

The results of the current groundwater monitoring event, and pertinent Site information and groundwater monitoring data are presented in the report as follows:

- The groundwater monitoring network layout is shown on **Figure 1**.
- Trend graphs are shown on **Figure 2**.
- Analytical results for collected samples are summarized in **Table 1.**
- Historical groundwater monitoring network analytical results are presented in **Table 2**.
- Groundwater elevations for the current monitoring event are presented in **Table 3**.
- Monitoring Well Inventory is presented in **Table 4**.
- Validated laboratory data sheets and data quality summaries are provided in **Appendix A**.
- Field sampling sheets for the current monitoring event are contained in **Appendix B**.

NES continues to coordinate efforts with IEPA to share groundwater data obtained from common monitoring well locations at the Site. NES is not aware of IEPA sample collection from Site monitoring locations for the current reporting period and no comparative Site data from IEPA is presented in this report.

An updated monitoring well inventory for the Site is presented in **Table 4**. The monitoring well inventory was revised to match the current condition of the individual monitoring wells comprising the Site monitoring well network. In particular, repairs or maintenance performed for certain monitoring well locations resulted in changes to the wellhead elevation, necessitating the noted revisions to the inventory schedule.

Monitoring Event Results

The field sampling sheets presenting pertinent field information and site conditions for the current monitoring event are provided in **Appendix B** of this report. The following field conditions were noted to occur during the current semi-annual monitoring event:

- MW-206C was not sampled because it was not accessible. The well is located on property owned by the Rock River Water Reclamation District (RRWRD), which installed an earthen berm adjacent to the well location as part of a facility expansion. The installed berm has since eroded covering the MW-206C well location. RRWRD has installed a new monitoring well near MW-206 to monitor surficial groundwater conditions at the facility, but its use for purposes of monitoring Site groundwater is yet to be determined.

- MW-203 was sampled with a portable low flow sampling pump. The permanent well pump installed in the well was removed by an unknown party.

- The static water level in MW-133A was determined to be inaccurate due to a level below the top of the dedicated sampling pump. However, the well was sampled because it produced enough water to meet FSP protocol.

The analytical results for groundwater samples collected during the current monitoring event are summarized in **Table 1,** and present concentrations for the chemicals of concern (COC) identified in Section VI of the Site Record of Decision (ROD) and for vinyl chloride. Historical analytical results for groundwater samples collected from the Site monitoring network, by monitoring well location, are presented in **Table 2**. Validated laboratory data sheets and data quality summaries including relevant analytical quality assurance/quality control (QA/QC) are provided in **Appendix A**.

Overall, total VOC concentrations have generally decreased across the Site since inception of the long-term monitoring program in March 1999. The ratios of parent VOC compound concentrations to associated breakdown product concentrations indicate biodegradation, comprising a component of natural attenuation, may be occurring at the Site. The presence of vinyl chloride and chloroethane in groundwater samples are further indicators that natural attenuation may be occurring at the Site.

A series of graphs depicting historical total volatile organic compound (VOC) concentrations for select monitoring wells are shown on **Figure 2** to show total VOC concentration trends occurring at these monitoring locations. The monitoring locations used for comparison of historical analytical data were selected based on their proximity to designated source areas. Although the graphs depict analytical results from 1999 to the present, the evaluation presented in this report for total VOCs in groundwater at the Site is principally devoted to the identification of changes, if any, from the previous semi-annual sampling event conducted in June 2014.

The graphs on **Figure 2** reveal that fluctuations in total VOC concentrations in groundwater have occurred over the period that samples have been collected at the Site under the remedial action. The causal factors for VOC concentration variability are presumed to be source area remedial activities performed by others, variation in groundwater levels, precipitation events, etc. However, NES is not aware of any specifics that would allow an interpretation of the data, other than the general observations presented in this report.

Monitoring Data Review

The status of total VOC concentrations at certain monitoring well locations, relative to the previous monitoring event (June 2014), are summarized below. The noted monitoring well locations are located proximate to, or down-gradient from, identified source areas. The Site source areas are segregated by general geographic location within the Site for the purpose of this report.

East-Source Area 7

The majority of total VOC concentrations reported for groundwater monitoring locations near the Area 7 source area have generally decreased or remained relatively stable from the previous sampling event, except as noted. Relative increases were noted for individual VOC concentrations in water quality samples collected from MW-101A/D and MW-102B from the previous monitoring event. Several VOCs were reported above the maximum contaminant level (MCL) at the monitoring well cluster MW-101A/B/C/D and MW-133B/C. During the previous monitoring event, VOCs were reported above MCLs at these same locations.

North-Source Areas 4, 9, 10, & 11

Evaluation of the analytical results for the current monitoring event resulted in the following observations. Relative increases in individual VOC concentrations were noted in the water quality samples collected from MW-113B, MW-201, and MW-203 from the previous monitoring event. Several VOCs were reported above the MCL at monitoring locations MW-16, MW-113A/B, MW-121, and MW-124. During the previous monitoring event, VOCs were reported above MCLs at these same locations.

West-Rock River

Evaluation of the analytical results for the current semi-annual monitoring event resulted in the following observations for the monitoring locations proximate to the Rock River. Relative increases in specific VOC constituent concentrations did occur in the water quality samples collected from MW-117B/D and MW-205A/B from the previous monitoring event. Several VOCs were reported above the MCL at MW-117C/D, MW-204, MW-205A/B, and MW-206B. During the previous monitoring event, VOCs were reported above MCLs at these same locations.

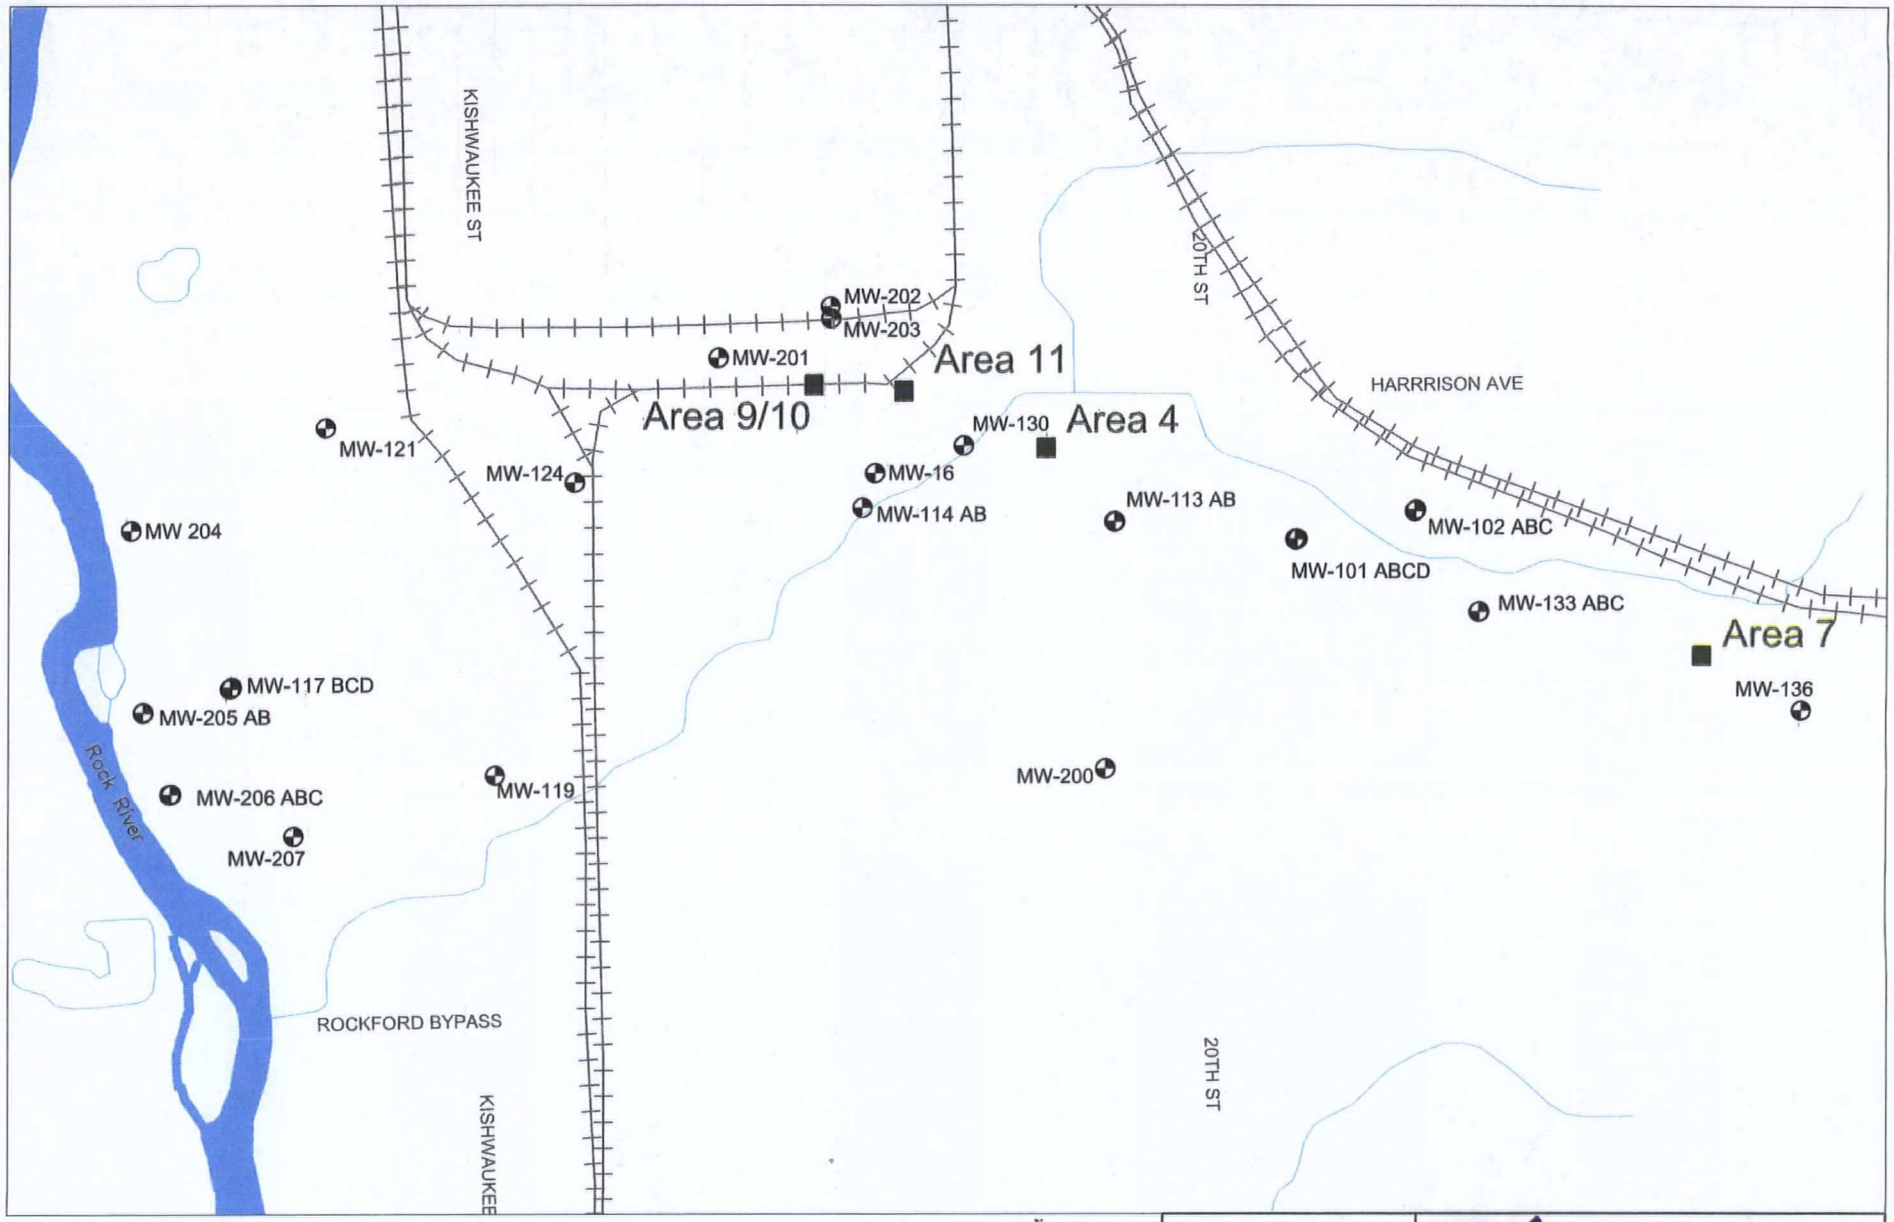

N
W E
S
0 1000' 2000'

LEGEND

Monitoring Well

Area

Figure 1
South East Rockford NPL Site
Ground Water Monitoring Network
and Source Locations
Winnebago County, Illinois

Figure 2 - Southeast Rockford Superfund Site
Monitoring Wells Near Area 7

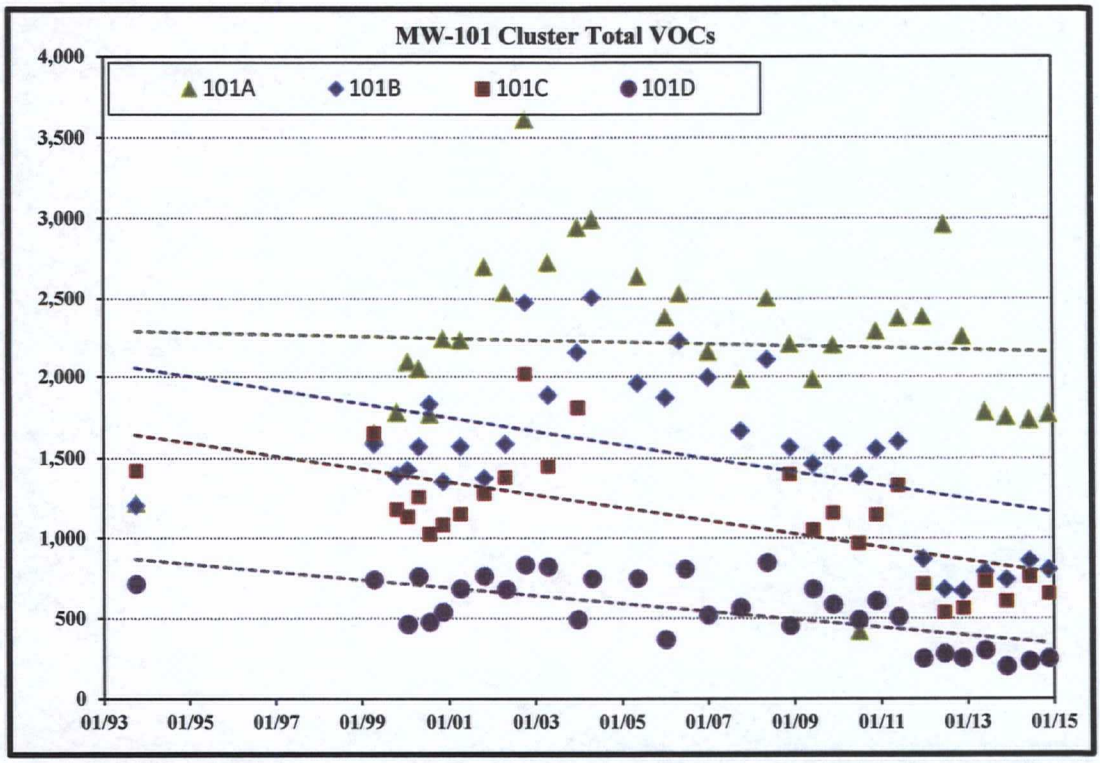

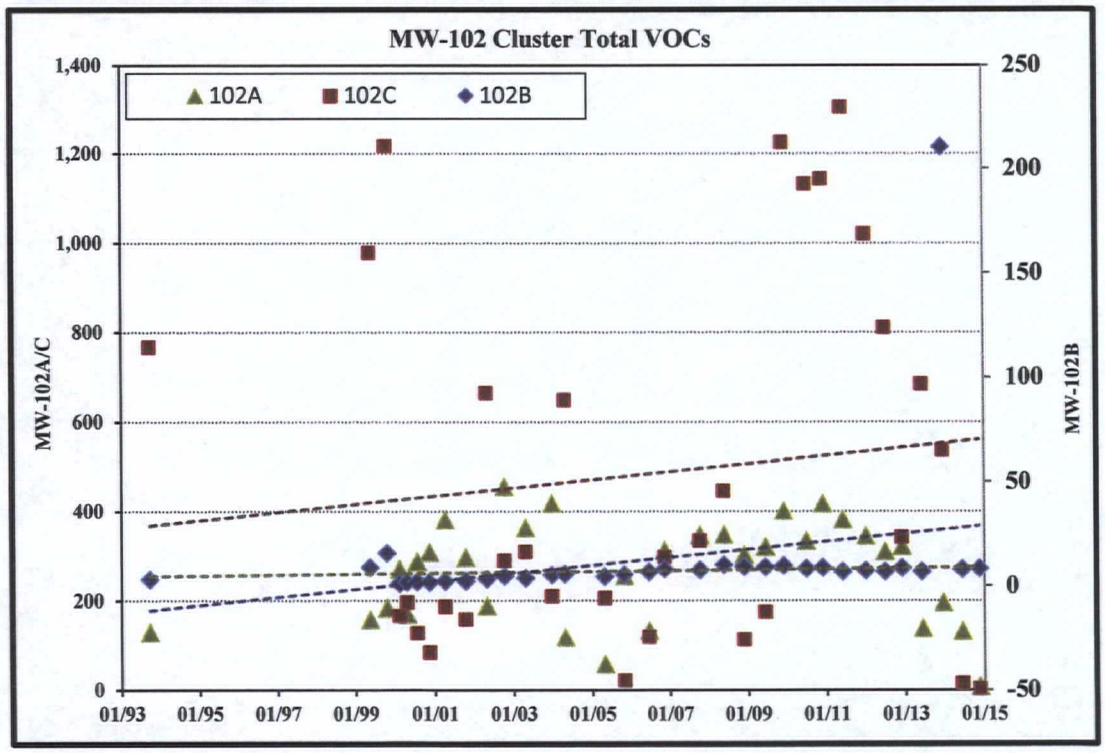

Y-axis = Total VOCs in micrograms per liter; X- axis = Sampling Date

Figure 2 - Southeast Rockford Superfund Site
Monitoring Wells Near Area 7

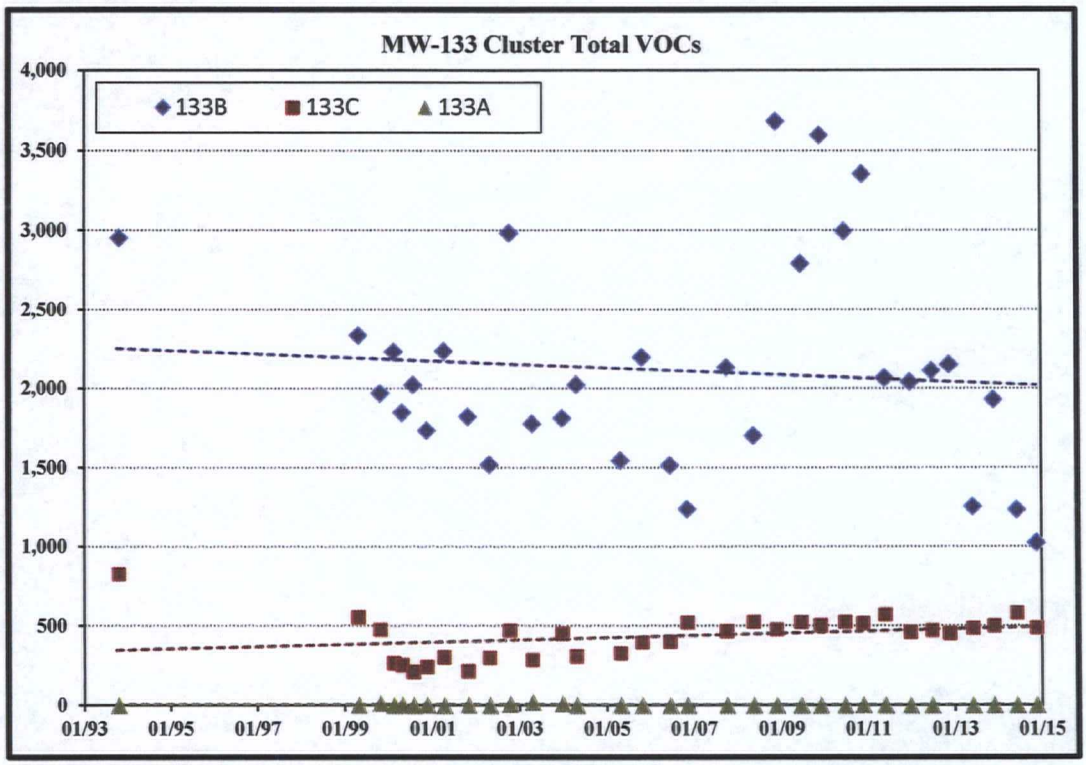

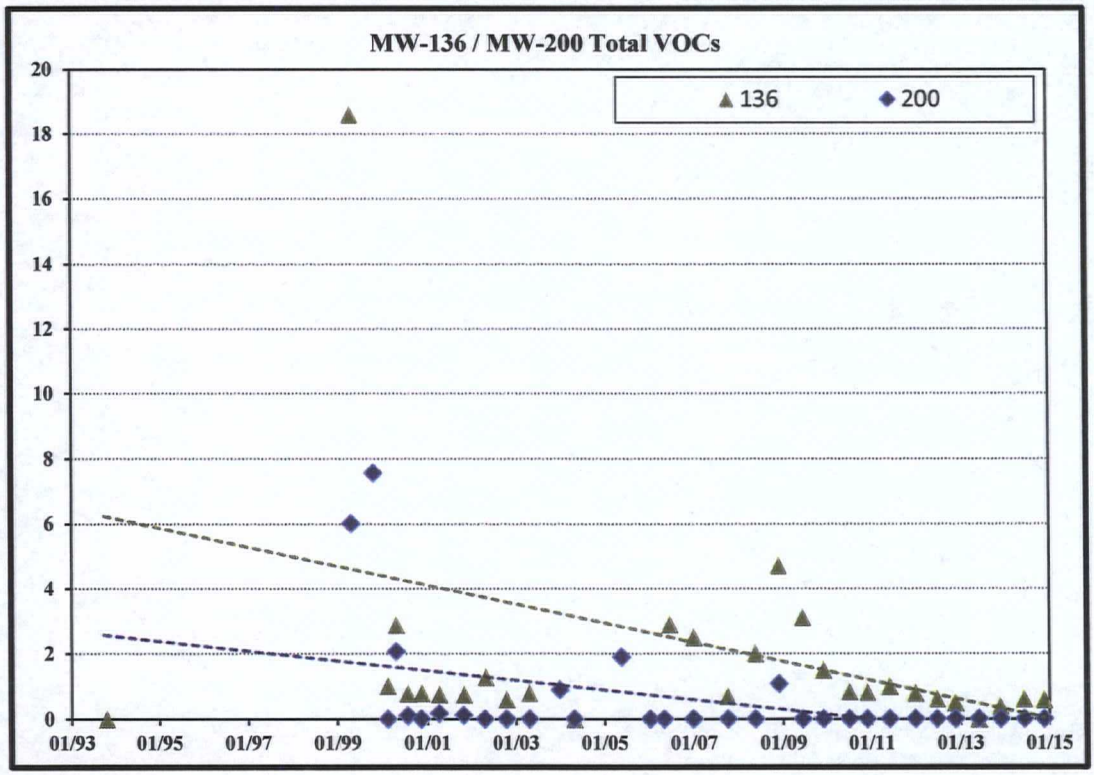

Y-axis = Total VOCs in micrograms per liter; X- axis = Sampling Date

Figure 2 - Southeast Rockford Superfund Site
Monitoring Wells Near Areas 4, 9/10, 11

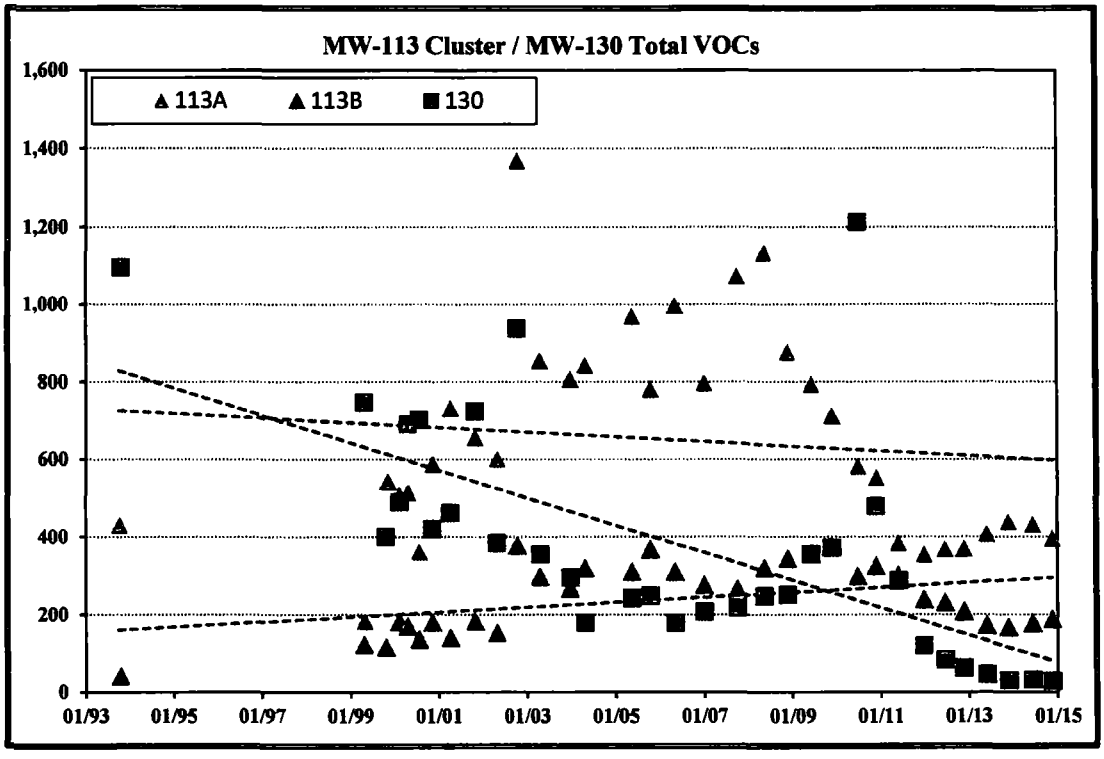

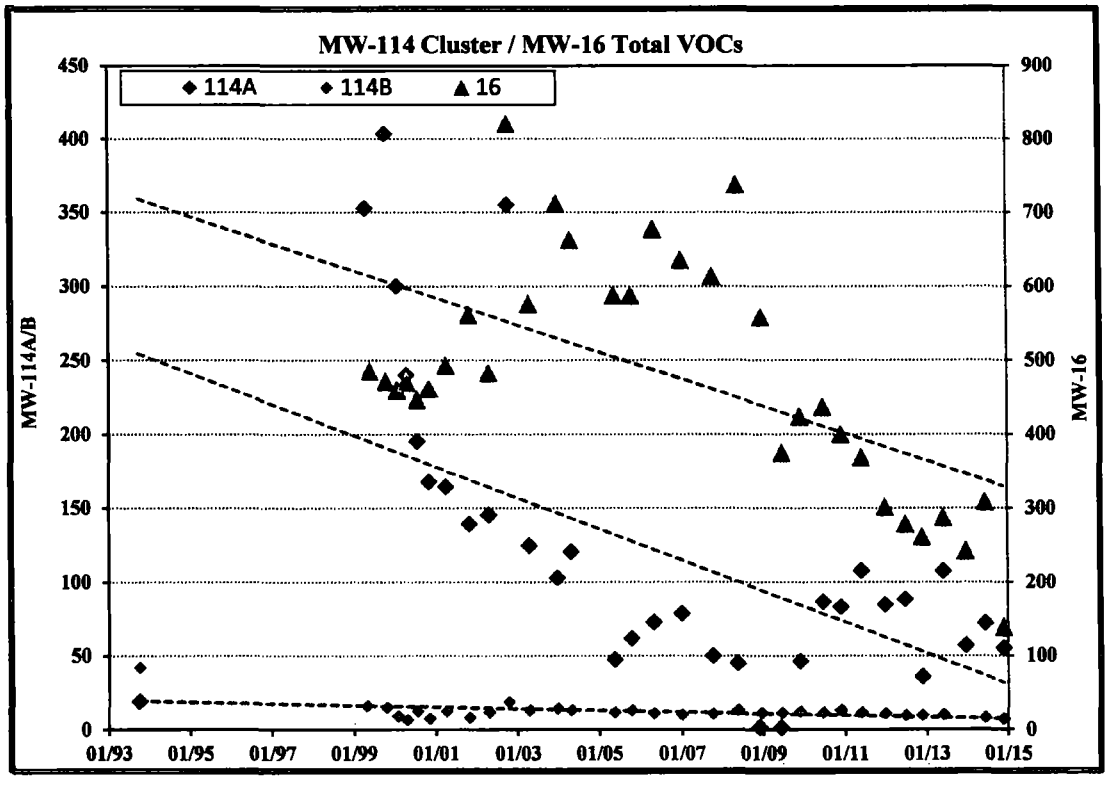

Y-axis = Total VOCs in micrograms per liter; X- axis = Sampling Date

Figure 2 - Southeast Rockford Superfund Site
Monitoring Wells Near Areas 4, 9/10, 11

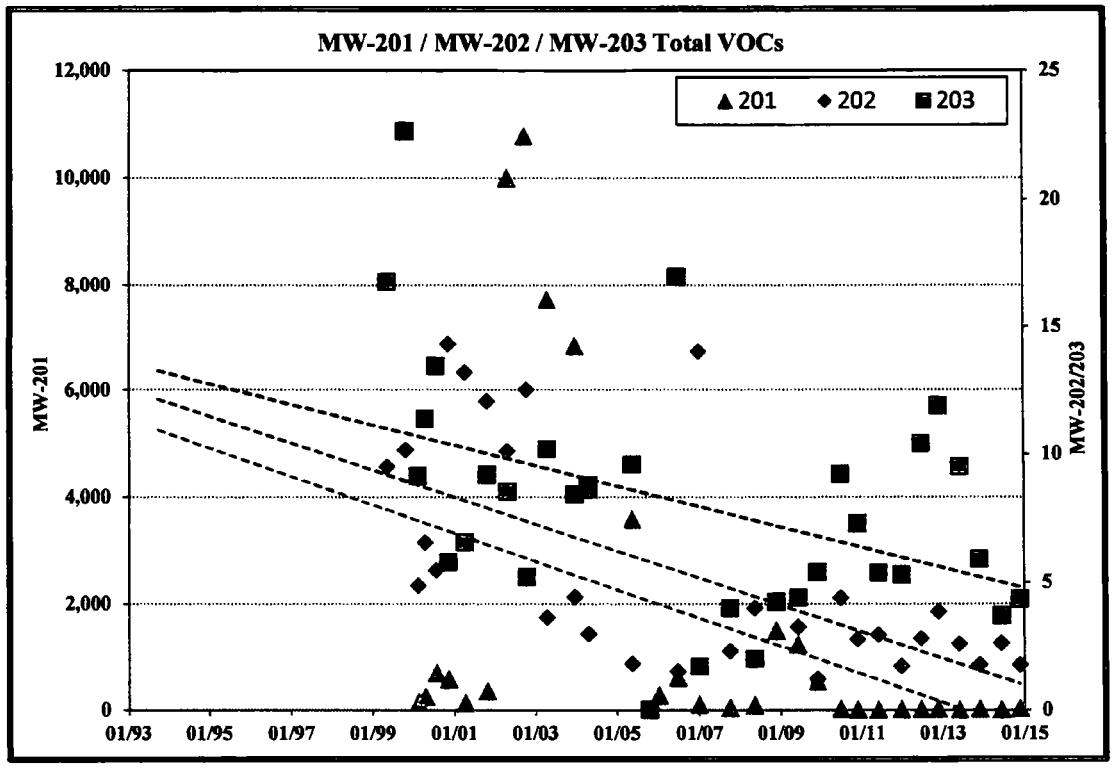

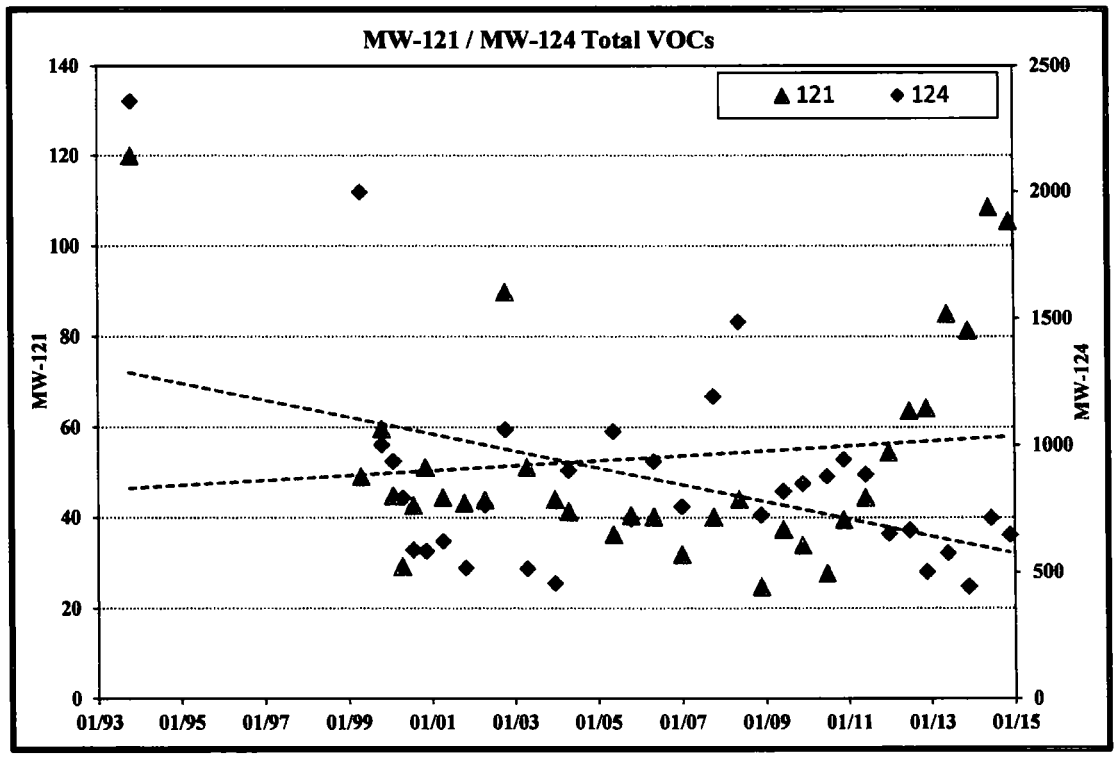

Y-axis = Total VOCs in micrograms per liter; X- axis = Sampling Date

Figure 2 - Southeast Rockford Superfund Site
Monitoring Wells Near Rock River

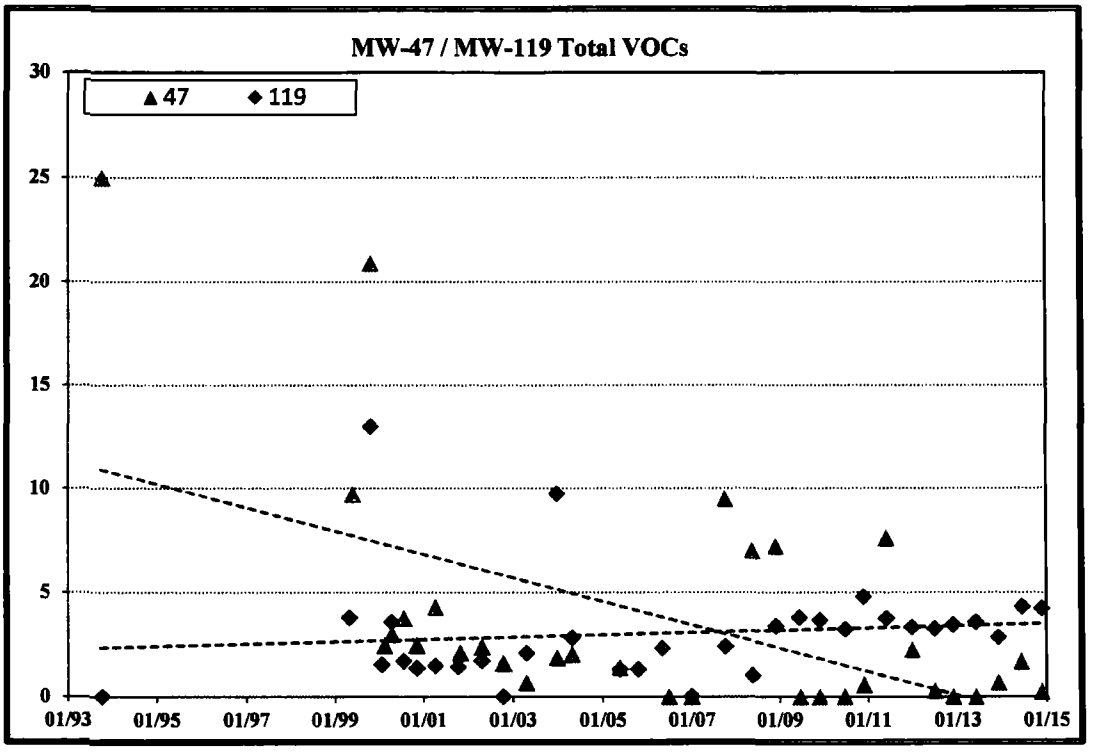

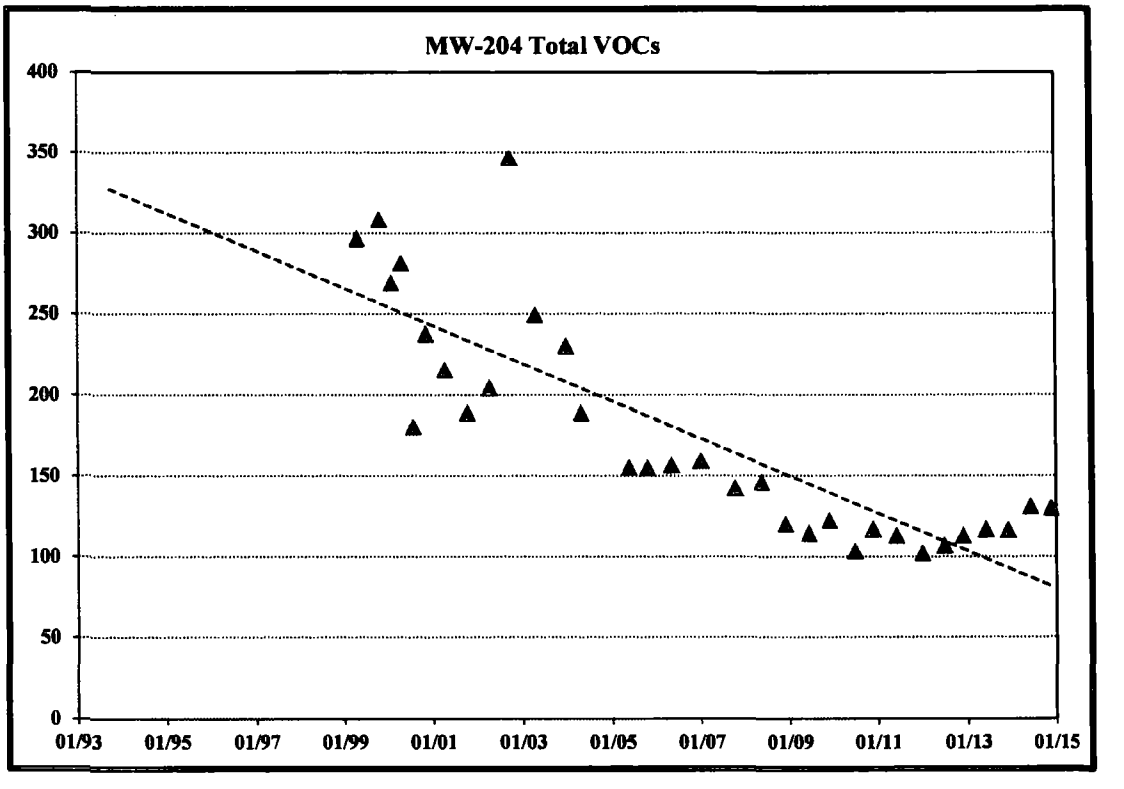

Y-axis = Total VOCs in micrograms per liter; X- axis = Sampling Date

Figure 2 - Southeast Rockford Superfund Site
Monitoring Wells Near Rock River

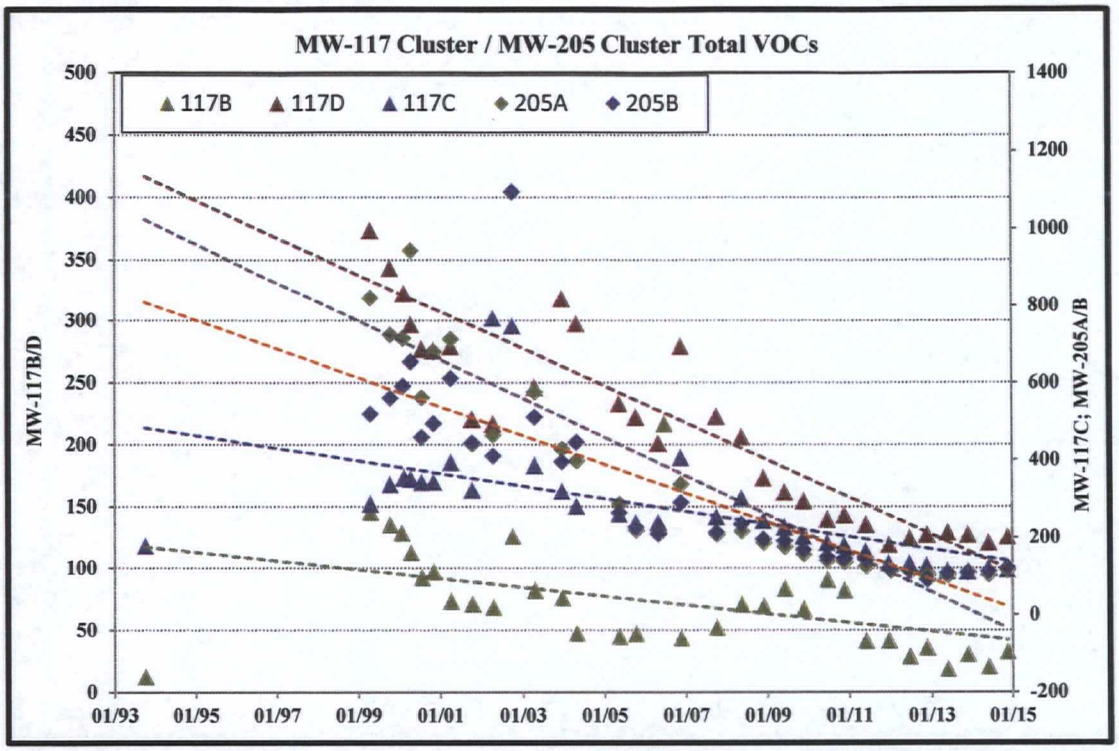

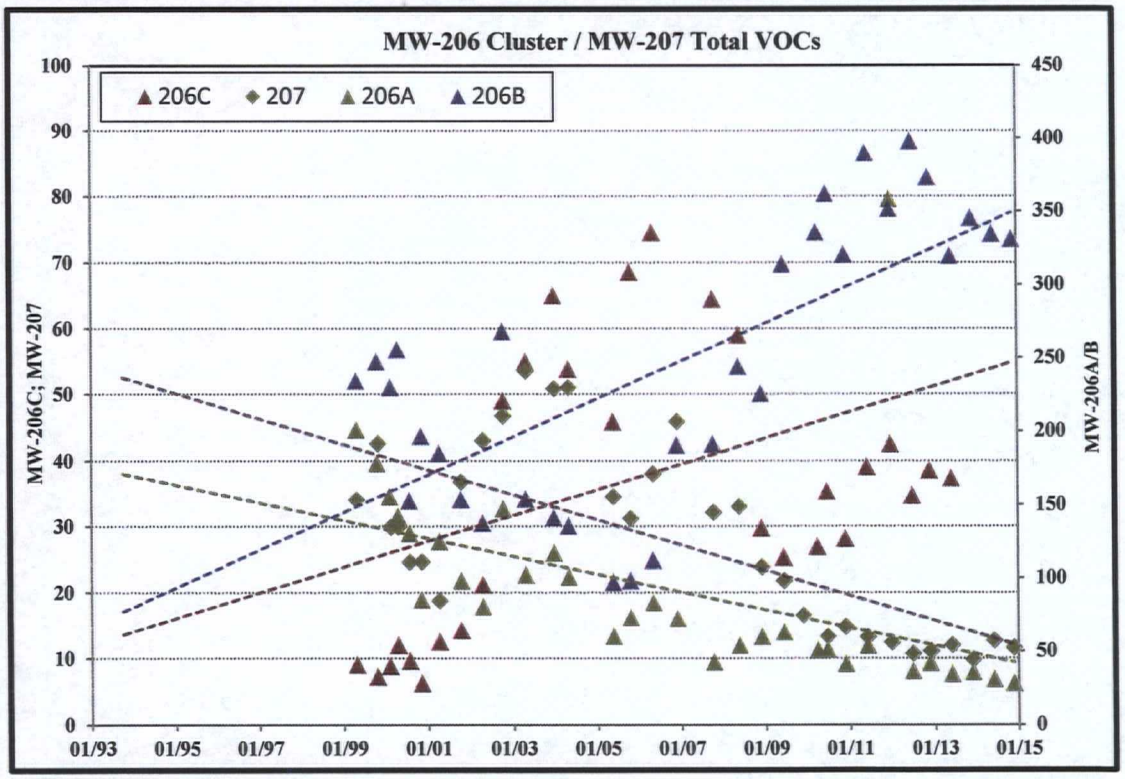

Y-axis = Total VOCs in micrograms per liter; X- axis = Sampling Date

Table 1: Southeast Rockford NPL Site
Summary of Groundwater Analytical Results
Sampling Event #32

Compound	MCL	MW-16 11/24/14	MW-47 11/23/14	MW-101A 11/24/14	MW-101B 11/24/14	MW-101C 11/24/14	MW-101D 11/24/14	MW-102A 11/24/14	MW-102B 11/24/14
Chloroform	N/A	0.62J	1.0U	3.6J	1.9J	1.7J	0.71J	1.0U	1.0U
1,1-Dichloroethane	N/A	45	0.23J	270	150	120	53	2.5	2.6
1,2-Dichloroethane	5	1.0U	1.0U	5.0U	5.0U	5.0U	1.0U	0.61J	0.8J
1,1-Dichloroethene	7	**8.6**	1.0U	**64**	**30**	**25**	**14**	1.0U	1.0U
cis-1,2-Dichloroethene	70	12	1.0U	**520**	26	27	63	3.4	3.5
trans-1,2-Dichloroethene	100	1.1	1.0U	25	5.3	4.4J	2	1.0U	1.0U
Methylene Chloride	5	5.0U	5.0U	25U	25U	25U	5.0U	5.0U	5.0U
Tetrachloroethene	5	4.2	0.36J	**71**	**31**	**25**	**9.6**	1.0U	1.0U
1,1,1-Trichloroethane	200	50	1.0U	**670**	**530**	**430**	90	1.0U	1.0U
Trichloroethene	5	**17**	1.0U	**150**	**30**	**20**	**15**	1.0U	1.0U
Vinyl chloride	2	1.0U	1.0U	5.0U	5.0U	5.0U	0.28J	1.3	1.2

Compound	MCL	MW-102C 11/24/14	MW-113A 11/24/14	MW-113B 11/24/14	MW-114A 11/24/14	MW-114B 11/24/14	MW-117B 11/21/14	MW-117C 11/21/14	MW-117D 11/22/14
Chloroform	N/A	1.0U	1.3	0.4J	1.0U	1.0U	0.3J	0.29J	0.28J
1,1-Dichloroethane	N/A	1	140	66	4.6	1.4	11	39	48
1,2-Dichloroethane	5	1.0U	1.0U	0.52J	1.0U	1.0U	1.0U	1.0U	1.0U
1,1-Dichloroethene	7	1.0U	**18**	**15**	4.9	1.0U	3.7	**13**	**12**
cis-1,2-Dichloroethene	70	1.4	31	55	4.1	1	0.82J	4.5	2.3
trans-1,2-Dichloroethene	100	1.0U	5.2	2.2	1.0U	1.0U	1.0U	1.0U	1.0U
Methylene Chloride	5	5.0U	5.0U	5.0U	5.0U	5.0U	5.0U	5.0U	5.0U
Tetrachloroethene	5	1.0U	**11**	2.1	0.27J	0.28J	4.8	**22**	**18**
1,1,1-Trichloroethane	200	0.26J	140	13	38	0.24J	7.9	25	35
Trichloroethene	5	1.0U	**50**	**22**	3.1	4	4.4	**12**	**10**
Vinyl chloride	2	1.0U	1.0U	**13**	1.0U	1.0U	1.0U	1.0U	1.0U

Table 1: Southeast Rockford NPL Site
Summary of Groundwater Analytical Results
Sampling Event #32

Compound	MCL	MW-119 11/24/14	MW-121 11/23/14	MW-124 11/23/14	MW-130 11/23/14	MW-133A 11/23/14	MW-133B 11/23/14	MW-133C 11/24/14	MW-136 11/23/14
Chloroform	N/A	0.29J	0.84J	2.5U	0.34J	1.0U	4.4J	5.8	0.58J
1,1-Dichloroethane	N/A	1.4	42	420	12	1.0U	170	58	1.0U
1,2-Dichloroethane	5	1.0U	1.0U	2.5U	1.0U	1.0U	5.0U	1.3	1.0U
1,1-Dichloroethene	7	1.0U	**8.7**	**10**	1.5	1.0U	**48**	**47**	1.0U
cis-1,2-Dichloroethene	70	0.47J	6.4	**130**	2.5	1.0U	**160**	**130**	1.0U
trans-1,2-Dichloroethene	100	1.0U	0.92J	1.2J	1.0U	1.0U	12	2.2	1.0U
Methylene Chloride	5	5.0U	5.0U	1.8J	5.0U	5.0U	25U	5.0U	0.39J
Tetrachloroethene	5	0.28J	1.6	**7.8**	0.56J	1.0U	**78**	**6.6**	1.0U
1,1,1-Trichloroethane	200	1.6	20	41	9.3	1.0U	**480**	150	1.0U
Trichloroethene	5	0.46J	**25**	4.9	1.8	1.0U	**68**	**83**	1.0U
Vinyl chloride	2	1.0U	1.0U	**31**	1.0U	1.0U	5.0U	1.0U	1.0U

Compound	MCL	MW-200 11/23/14	MW-201 11/23/14	MW-202 11/24/14	MW-203 11/24/14	MW-204 11/23/14	MW-205A 11/22/14	MW-205B 11/22/14	MW-206A 11/22/14
Chloroform	N/A	1.0U	1.0U	1.0U	1.0U	0.38J	0.29J	0.3J	0.5J
1,1-Dichloroethane	N/A	1.0U	6.5	0.43J	1.0U	9.8	36	38	7.2
1,2-Dichloroethane	5	1.0U	1.0U	1.0U	1.0U	0.94J	1.0U	1.0U	1.0U
1,1-Dichloroethene	7	1.0U	0.83J	1.0U	1.0U	**16**	**12**	**13**	3
cis-1,2-Dichloroethene	70	1.0U	3.2	1.0U	1.0U	40	2.7	4.1	1.2
trans-1,2-Dichloroethene	100	1.0U	1.0U	1.0U	1.0U	0.78J	1.0U	1.0U	1.0U
Methylene Chloride	5	5.0U	5.0U	5.0U	5.0U	5.0U	5.0U	5.0U	5.0U
Tetrachloroethene	5	1.0U	1.7	0.97J	4.1	1.4	**22**	**23**	**5**
1,1,1-Trichloroethane	200	1.0U	18	1.0U	0.24J	10	27	28	6.7
Trichloroethene	5	1.0U	1.4	0.35J	1.0U	**51**	**14**	**14**	4.5
Vinyl chloride	2	1.0U	1.0U	1.0U	1.0U	1.0U	1.0U	1.0U	1.0U

Table 1: Southeast Rockford NPL Site
Summary of Groundwater Analytical Results
Sampling Event #32

Compound	MCL	MW-206B 11/22/14	MW-206C	MW-207 11/23/14	MW-101A(d) 11/24/14	MW-201(d) 11/23/14
Chloroform	N/A	0.82J		0.28J	3.5J	1.0U
1,1-Dichloroethane	N/A	44		0.29J	270	6.1
1,2-Dichloroethane	5	1.2		1.8	5.0U	1.0U
1,1-Dichloroethene	7	**60**		1.7	50	0.82J
cis-1,2-Dichloroethene	70	**120**		1.0U	510	2.8
trans-1,2-Dichloroethene	100	0.36J	NS	1.0U	35	1.0U
Methylene Chloride	5	5.0U		0.58J	25U	5.0U
Tetrachloroethene	5	**20**		0.64J	71	1.5
1,1,1-Trichloroethane	200	46		1.2	670	18
Trichloroethene	5	**38**		1.3	150	1.2
Vinyl chloride	2	0.39J		1.0U	5.0U	1.0U

(d) Field duplicate
All units in micrograms per liter (µg/l) or parts per billion (ppb)
Bold value and outlined cell denotes analytical result > than MCL

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM MCL NA	1,1-DCA NA	1,2-DCA 5	1,1-DCE 7	c1,2-DCE 70	t1,2-DCE 100	MC 5	PCE 5	1,1,1-TCA 200	TCE 5	VC 2	Total VOCs
MW-16	06/01/99		3	76	1.2	24	140	1.8	2 U	5.4	170	64	1 U	**485**
MW-16	10/26/99		2.3 J	73	10 U	23	130	2.5 J	20 U	5.2 J	170	65	10 U	**471**
MW-16	01/31/00		2.3 J	75	10 U	2.2 J	120	16	20 U	5.9 J	170	68	10 U	**459**
MW-16	04/24/00		2.5 J	79	5 U	2 J	130 E	16	10 JB	5.7	170 E	65	5 U	**480**
MW-16	04/24/00	Dilution	50 DJB	75 D	50 U	50 U	130 D	17 DJ	100 DJB	5.3 DJ	160 D	62 D	2.8 DJ	**602**
MW-16	07/27/00		2.7	75	10 U	3.8	130	12	20 U	5.2	160	58	10 U	**447**
MW-16	11/13/00		2.2	87	10 U	20	150	2.8	20 U	5	140	55	10 U	**462**
MW-16	04/12/01		2.3	74	10 U	3.1	150	14	20 U	5.8	180	64	10 U	**493**
MW-16	10/31/01		2.5	88	10 U	10 U	160	22	20 U	7.1	210	72	10 U	**562**
MW-16	04/25/02		2.3	70	10 U	15	170	6.7	20 U	6.6	150	62	10 U	**483**
MW-16	10/15/02		20 U	130	20 U	98	240	22	40 U	20 U	240	91	1 U	**821**
MW-16	04/23/03		2.51	95.6 E	1.08	24.2	244 E	15.7	2 U	9.74	237 E	97.6 E	1 U	**727**
MW-16	04/23/03	Dilution	20 U	75.6	20 U	24.6	200	20 U	40 U	20 U	172	75.3	20 U	**548**
MW-16	12/26/03		2.48	93.9 E	1 U	32.2 E	209 E	13.9	1 U	9.45	208 E	77.8 E	1 U	**647**
MW-16	12/26/03	Dilution	10 U	93.9 D	10 U	31.7 D	247 D	10 U	10 U	9.14 JD	221 D	92.7 D	10 U	**695**
MW-16	12/26/03	Fld Dupe	2.55	96.3 E	1 U	34.5 E	227 D	10 U	1 U	9.85	220 E	72.5 D	1 U	**663**
MW-16	04/28/04		20 U	100	20 U	30.1	254	20 U	40 U	20 U	202	77.3	20 U	**663**
MW-16	05/21/05		1.8	91	1 U	28	230	5.6	2 U	6.5	160	65	1 U	**588**
MW-16	10/20/05		1.8	91	1 U	28	230	5.6	2 U	6.5	160	65	1 U	**588**
MW-16	05/08/06		2	94	1 U	27	290	7.3	2 U	9.1	170	78	1 U	**677**
MW-16	01/04/07		5	94	5 U	24	280	5	10 U	5.3	160	63	5 U	**636**
MW-16	10/08/07		2	100	1	28	260	14	2 U	8	140	61	1 U	**614**
MW-16	05/17/08		20 U	130	20 U	39	320	20 U	40 U	20 U	170	78	20 U	**737**
MW-16	12/18/08	Dilution	1.3 J	100	1 J	2 U	240	35	0.7 J	4.6	120	56	2 U	**559**
MW-16	06/20/09	Dilution	1.6 J	110	2 U	2 U	39	6.8	2 U	5.5	170	42	2 U	**375**
MW-16	11/28/09	Dilution	1.6 J	110	2 U	7.9	56	6.9	0.88 J	6.1	180	55	2 U	**424**
MW-16	06/25/10		1.4	93	0.21 J	21	51	3.8	1 U	8.7	200	58	1 U	**437**
MW-16	11/27/10	Dilution	1.4 J	78	2 U	24	45	1.6 J	2 U	10	180	60	2 U	**400**
MW-16	06/01/11		1.2	81	1 U	19	40	3.2	1 U	11	160	54	1 U	**369**
MW-16	12/28/11		1.1	71	1 U	17	27	2.7	5 U	11	130	42	1 U	**302**
MW-16	06/28/12		1.1	72	1 U	5.2	25	3.3	5 U	11	120	41	1 U	**279**
MW-16	11/24/12		0.9 J	68	1 U	13	22	2.4	5 U	10	110	35	1 U	**261**
MW-16	06/07/13		0.89 J	75	1 U	19	21	2.5	5 U	12	120	37	1 U	**287**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-16	12/19/13		0.8 J	73	1 U	17	18	2.2	5 U	9	93	30	1 U	**243**
MW-16	06/14/14		1	98	1 U	22	18	2.9	5 UB	11	120	36	1 U	**309**
MW-16	11/24/14		0.62 J	45	1 U	8.6	12	1.1	5 U	4.2	50	17	1 U	**139**
MW-47	10/06/93		1 U	5	1 U	2	3	1 U	2 U	1	9	5		**25**
MW-47	06/01/99		1 U	1.1	1 U	0.49	1.3	1 U	2 U	0.53	3.5	2.8	1 U	**10**
MW-47	10/27/99		1 U	1.1	1 U	0.87 J	4.5	0.05 J	2 U	2.2	6.5	5.7	1 U	**21**
MW-47	02/17/00		1 U	0.32 J	1 U	0.1 J	0.18 J	1 U	2 U	0.27 J	1	0.58 J	1 U	**2**
MW-47	04/18/00		1 U	0.53 J	1 U	0.18 J	0.36 J	1 U	2 U	0.27 J	1	0.66 J	1 U	**3**
MW-47	07/27/00		1 U	0.61	1 U	0.13	0.38	1 U	2 U	0.64	1.2	0.82	1 U	**4**
MW-47	11/08/00		0.17	0.55	1 U	0.1	0.25	1 U	2 U	0.45	0.58	0.37	1 U	**2**
MW-47	04/10/01		0.28	0.57	1 U	1	0.31	1 U	2 U	0.48	1.1	0.56	1 U	**4**
MW-47	10/31/01		0.92	0.21	1 U	1 U	1 U	1 U	2 U	0.38	0.34	0.25	1 U	**2**
MW-47	04/30/02		1.3	0.13	1 U	1 U	0.13	1 U	2 U	0.33	0.23	0.27	1 U	**2**
MW-47	10/17/02		1	1 U	1 U	1 U	1 U	1 U	0.6	1 U	1 U	1 U	1 U	**2**
MW-47	04/22/03		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	0.67 J	1 U	1 U	**1**
MW-47	12/28/03		1 U	1 U	1 U	0.51 J	1 U	1 U	1 U	0.77 J	0.59 J	1 U	1 U	**2**
MW-47	04/28/04		1 U	0.54	1 U	1 U	1 U	1 U	2 U	1 U	0.91	0.58	1 U	**2**
MW-47	05/21/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1.4	1 U	1 U	**1**
MW-47	06/28/06		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-47	01/05/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-47	10/08/07		1 U	2	1 U	0.9	2	1 U	2 U	0.6	3	1	1 U	**10**
MW-47	05/17/08		1 U	1	1 U	1 U	1	1 U	2 U	1 U	4	1	1 U	**7**
MW-47	11/29/08	Fld Dupe	0.15 J	1.58	1 U	0.34 J	0.96 J	1 U	1 U	0.61 J	2.89	1.15	1 U	**8**
MW-47	11/29/08		1 U	1.6	1 U	1 U	0.93 J	1 U	1 U	0.62 J	2.91	1.17	1 U	**7**
MW-47	06/20/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**0**
MW-47	11/28/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**0**
MW-47	06/24/10		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**0**
MW-47	11/29/10		1 U	0.27 J	1 U	1 U	1 U	1 U	1 U	1 U	0.3 J	1 U	1 U	**1**
MW-47	06/03/11		1 U	2	1 U	0.68 J	0.7 J	1 U	1 U	0.33 J	2.7	1.2	1 U	**8**
MW-47	12/29/11		1 U	0.35 J	1 U	1 U	1 U	1 U	5 U	0.4 J	0.85 J	0.64 J	1 U	**2**
MW-47	06/26/12		1 U	1 U	1 U	1 U	1 U	1 U	5 U	0.29 J	1 U	1 U	1 U	**0**
MW-47	11/25/12		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	**0**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-47	05/31/13		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	**0**
MW-47	12/01/13		1 U	0.35 J	1 U	1 U	1 U	1 U	5 U	1 U	0.34 J	1 U	1 U	**1**
MW-47	06/05/14		1 U	0.31 J	1 U	1 U	1 U	1 U	5 U	0.41 J	0.61 J	0.35 J	1 U	**2**
MW-47	06/05/14	Fld Dupe	1 U	0.29 J	1 U	1 U	1 U	1 U	5 U	0.35 J	0.57 J	0.35 J	1 U	**2**
MW-47	11/23/14		1 U	0.23 J	1 U	1 U	1 U	1 U	5 U	1 UB	1 U	1 U	1 U	**0**
MW-101A	10/04/93		4	150	17 U	43	190		17 U	17 U	650	180		**1217**
MW-101A	04/20/99		7.3	230	3.4	63	540	9.3	2 U	16	580	200	1 U	**1649**
MW-101A	10/25/99		5.6 J	240	50 U	64	620	7 J	100 U	14 J	610	220	50 U	**1781**
MW-101A	01/27/00		6.2 J	270	50 U	61	690	40 J	100 U	15 J	740	270	50 U	**2092**
MW-101A	04/25/00		7 JB	240	50 U	65	720	7.8 J	100 JB	50 U	690	220	50 U	**2050**
MW-101A	07/26/00		6.1	210	20 U	51	730	10	40 U	4.4	620	140	20 U	**1772**
MW-101A	11/16/00		6.3	310	50 U	77	830	8.3	100 U	15	740	250	50 U	**2237**
MW-101A	04/13/01		5.6	240	50 U	81	780	8.6	100 U	14	830	270	50 U	**2229**
MW-101A	10/30/01		6.3	300	50 U	79	990	12	100 U	15	1000	300	50 U	**2702**
MW-101A	04/22/02		6.8	250	50 U	82	1000	11	100 U	18	890	280	50 U	**2538**
MW-101A	10/10/02		100 U	370	100 U	440	1200	100 U	200 U	64	1200	340	1 U	**3614**
MW-101A	04/23/03		6.28	320 E	1 U	125 E	1080 E	19.4	2 U	26.8 E	919 E	427 E	1 U	**2923**
MW-101A	04/23/03	Dilution	100 U	266	100 U	81.8 J	1110	100 U	200 U	100 U	909	309	100 U	**2676**
MW-101A	12/26/03		8.18	313 E	3.83	128 E	1080 E	21.8	1 U	51.7 E	796 E	344 E	1 U	**2747**
MW-101A	12/26/03	Dilution	100 U	268 D	100 U	101 D	1260 D	100 U	100 U	100 U	950 D	278 D	100 U	**2857**
MW-101A	04/28/04		100 U	265	100 U	98.1	1230	100 U	200 U	56.4	1040	302	100 U	**2992**
MW-101A	05/21/05		10 U	260	10 U	89	1100	13	20 U	80	850	250	10 U	**2642**
MW-101A	01/12/06		4.5	220	5 U	37	990	44	10 U	61	800	220	5 U	**2377**
MW-101A	05/08/06		4.4	25 U	1 U	76	1100	17	2 U	93	970	270	1 U	**2530**
MW-101A	01/04/07		10 U	180	10 U	48	840	21	20 U	56	820	190	10 U	**2155**
MW-101A	10/07/07		4	220	2	38	790	72	2 U	67	590	200	1 U	**1983**
MW-101A	05/17/08		50 U	260	50 U	100	1000	50 U	100	64	740	240	50 U	**2504**
MW-101A	11/28/08	Dilution	4.1 J	233	2.15 J	57.5	908	38.4	1.8 J	56.2	691	214	5 U	**2206**
MW-101A	06/10/09	Dilution	4.3 J	230	2 J	50	870	30	5 U	56	550	190	5 U	**1982**
MW-101A	11/27/09	Dilution	5.2 J	280	10 U	70	990	36	10 U	47	550	220	10 U	**2198**
MW-101A	06/28/10	Dilution	2 U	54	2 U	15	210	6	2 U	6.8	90	38	2 U	**420**
MW-101A	06/28/10	Fld Dupe	2 U	51	2 U	14	200	5.3	2 U	6.3	86	37	2 U	**400**
MW-101A	11/26/10	Dilution	3.2 J	280	10 U	68	1100	18	10 U	36	550	230	10 U	**2285**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-101A	05/31/11	Dilution	4.5 J	310	10 U	46	1200	75	10 U	36	510	190	10 U	**2372**
MW-101A	12/28/11	Dilution	4.3 J	290	2.8 J	62	1200	49	50 U	52	540	180	10 U	**2380**
MW-101A	12/28/11	Fld Dupe	4.3 J	290	10 U	64	1200	52	50 U	52	540	180	10 U	**2382**
MW-101A	06/25/12	Dilution	5.2 J	320	10 U	72	1600	66	2.7 J	56	650	190	10 U	**2962**
MW-101A	11/24/12	Dilution	3.4 J	240	10 U	39	1200	57	50 U	55	500	160	10 U	**2254**
MW-101A	06/04/13	Dilution	10 U	260	10 U	61	730	14	15 J	56	500	150	10 U	**1786**
MW-101A	06/04/13	Fld Dupe	3.1 J	270	5 U	66	750	16	8.3 J	58	540	160	5 U	**1871**
MW-101A	11/30/13	Dilution	3 J	260	5 U	70	610	14	25 UB	67	570	160	5 U	**1754**
MW-101A	06/14/14	Dilution	3.2 J	300	5 U	58	510	23	25 UB	72	620	150	5 U	**1736**
MW-101A	11/24/14	Fld Dupe	3.5 J	270	5 U	50	510	35	25 U	71	670	150	5 U	**1760**
MW-101A	11/24/14	Dilution	3.6 J	270	5 U	64	520	25	25 U	71	670	150	5 U	**1774**
MW-101B	10/04/93		5	140	25 U	42	190		25 U	84	560	180		**1201**
MW-101B	04/20/99		3.6	150	10 U	36	520	10 U	20 U	45	690	140	10 U	**1585**
MW-101B	10/25/99		3.6 J	140	25 U	38	430	3.2 J	50 U	47	580	150	25 U	**1392**
MW-101B	01/27/00		50 U	140	50 U	33 J	490	50 U	100 U	42 J	570	150	50 U	**1425**
MW-101B	04/25/00		4.5 J	150	50 U	37 J	510	5.2 J	100 JB	33 J	590	140	50 U	**1570**
MW-101B	07/26/00		4.4	150	20 U	41	700	4	40 U	39	750	140	20 U	**1828**
MW-101B	11/16/00		3.3	170	25 U	35	550	3.9	50 U	18	450	120	25 U	**1350**
MW-101B	04/13/01		50 U	140	50 U	42	570	50 U	100 U	39	620	160	50 U	**1571**
MW-101B	10/30/01		3.5	150	25 U	33	580	4	50 U	21	440	140	25 U	**1372**
MW-101B	04/22/02		4.4	140	50 U	37	630	4.4	3.3	48	580	140	50 U	**1587**
MW-101B	10/10/02		50 U	230	50 U	290	850	50 U	100 U	80	840	180	1 U	**2470**
MW-101B	04/23/03		3.62	202 E	1 U	66 E	891 E	11.7	2 U	67.1 E	753 E	206 E	1 U	**2200**
MW-101B	04/23/03	Dilution	50 U	162	50 U	45 J	795	50 U	100 U	50.7	656	160	50 U	**1869**
MW-101B	12/26/03		4.11	222 E	1 U	70.1 E	893 E	13	1 U	68 E	671 E	180 E	1 U	**2121**
MW-101B	12/26/03	Dilution	100 U	188 D	100 U	100 U	963 D	100 U	100 U	100 U	696 D	148 D	100 U	**1995**
MW-101B	04/28/04		50 U	226	50 U	59.4	1140	50 U	100 U	61.8	843	174	50 U	**2504**
MW-101B	05/21/05		10 U	200	10 U	50	920	10 U	20 U	47	610	130	10 U	**1957**
MW-101B	01/12/06		5 U	200	5 U	42	890	6.3	10 U	41	570	120	5 U	**1869**
MW-101B	05/08/06		10 U	230	10 U	52	1100	10 U	20 U	50	660	130	1 U	**2222**
MW-101B	01/04/07		10 U	210	10 U	46	950	10 U	20 U	46	620	120	10 U	**1992**
MW-101B	10/07/07		2	200	2	47	790	12	2 U	44	460	110	1 U	**1667**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-101B	05/17/08		50 U	240	50 U	64	960	50 U	100	52	560	130	50 U	**2106**
MW-101B	11/28/08	Dilution	2.4 J	181	1.75 J	36.2	760	7.45	1.35 J	41.1	438	96.3	5 U	**1566**
MW-101B	06/10/09	Dilution	3.1 J	160	1.8 J	31	750	7.1	5 U	36	390	81	5 U	**1460**
MW-101B	11/27/09	Dilution	2.6 J	170	5 U	37	840	8.4	5 U	37	400	81	5 U	**1576**
MW-101B	06/28/10	Dilution	10 U	130	10 U	35	790	9 J	10 U	32	320	70	10 U	**1386**
MW-101B	11/26/10	Dilution	10 U	130	10 U	36	850	10 U	10 U	32	430	77	10 U	**1555**
MW-101B	05/31/11	Dilution	5 U	140	5 U	32	910	6.2	5 U	30	420	63	5 U	**1601**
MW-101B	12/28/11	Dilution	1.7 J	120	0.86 J	26	270	5.5	10 U	25	380	40	2 U	**869**
MW-101B	06/25/12	Dilution	1.9 J	120	5 U	25	47	4.3 J	25 U	24	430	27	5 U	**679**
MW-101B	11/24/12	Dilution	1.4 J	120	2.5 U	26	33	4.1	0.88 J	25	430	26	2.5 U	**666**
MW-101B	06/04/13	Dilution	1.4 J	140	5 U	27	37	4.8 J	7.4 J	24	520	27	5 U	**789**
MW-101B	11/30/13	Dilution	1.6 J	130	5 U	28	32	4.1 J	25 UB	28	490	27	5 U	**741**
MW-101B	06/14/14	Dilution	1.8 J	170	5 U	30	33	5.8	25 UB	30	560	29	5 U	**860**
MW-101B	11/24/14	Dilution	1.9 J	150	5 U	30	26	5.3	25 U	31	530	30	5 U	**804**
MW-101C	10/06/93		100 U	140	100 U	59	210	100	100 U	72	650	190		**1421**
MW-101C	04/20/99		3.5	140	10 U	34	550	10 U	20 U	45	740	140	10 U	**1653**
MW-101C	10/25/99		3 J	110	25 U	31	380	2.5 J	50 U	42	480	130	25 U	**1179**
MW-101C	01/27/00		20 U	110	20 U	28	370	2.8 J	40 U	42	460	120	20 U	**1133**
MW-101C	04/25/00		3.9 J	120	50 U	28 J	420	3.5 J	100 JB	31 J	450	100	50 U	**1256**
MW-101C	07/26/00		3.6	110	20 U	25	390	2.7	40 U	21	390	82	20 U	**1024**
MW-101C	11/13/00		2.6	130	25 U	24	420	2.7	50 U	34	370	100	25 U	**1083**
MW-101C	04/12/01		2.5	100	25 U	27	420	3	50 U	37	450	110	25 U	**1150**
MW-101C	10/30/01		2.9	120	25 U	21	510	11	50 U	32	470	110	25 U	**1277**
MW-101C	04/22/02		3.2	120	25 U	31	570	4.2	50 U	41	490	120	25 U	**1379**
MW-101C	10/10/02		50 U	200	50 U	200	660	50 U	28	150	650	130	1 U	**2018**
MW-101C	04/23/03	Dilution	50 U	125	50 U	35.8 J	626	50 U	100 U	36.7 J	489	121	50 U	**1434**
MW-101C	04/23/03		3	157 E	1 U	44.3 E	750 E	12.1	2 U	42 E	602 E	152 E	1 U	**1762**
MW-101C	12/30/03		3.64	193 E	1 U	57.2 E	782 E	32.5 E	1 U	63.2 E	644 E	175 E	1 U	**1951**
MW-101C	12/30/03	Dilution	50 U	141 D	50 U	42.4 JD	775 D	50 U	50 U	44.7 JD	628 D	142 D	50 U	**1773**
MW-101C	11/26/08	Dilution	2.45 J	157	2.05 J	33.8	682	6.8	1.5 J	27.9	398	86.4	5 U	**1398**
MW-101C	06/10/09	Dilution	2.6 J	120	5 U	22	550	5.8	5 U	24	270	56	5 U	**1050**
MW-101C	11/27/09	Dilution	2.4 J	120	5 U	28	620	5.5	5 U	25	290	63	5 U	**1154**
MW-101C	06/28/10	Dilution	5 U	85	5 U	23	570	5.4	5 U	19	220	44	5 U	**966**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-101C	11/26/10	Dilution	1.9 J	98	1.8 J	24	640	5 U	5 U	20	310	48	5 U	**1144**
MW-101C	05/31/11	Dilution	5 U	110	5 U	25	780	5.4	5 U	21	340	47	5 U	**1328**
MW-101C	12/28/11	Dilution	1.4 J	92	2 U	20	260	4	10 U	18	290	29	2 U	**714**
MW-101C	06/25/12	Dilution	1.4 J	89	2.5 U	17	89	3.3	12 U	16	300	20	2.5 U	**536**
MW-101C	11/30/12	Dilution	1.3 J	99	2.5 U	20	40	3.6	12 U	18	360	20	2.5 U	**562**
MW-101C	11/30/12	Fld Dupe	1.4 J	99	5 U	20	40	3.6 J	25 U	18	360	20	5 U	**562**
MW-101C	06/04/13	Dilution	1.6 J	130	2.5 U	24	40	4.1	7.1 J	22	480	22	2.5 U	**731**
MW-101C	11/30/13	Dilution	5 U	110	5 U	22	30	3.6 J	25 UB	21	400	19	5 U	**606**
MW-101C	06/14/14	Dilution	1.5 J	150	2.5 U	25	32	4.5	12 UB	26	500	20	2.5 U	**759**
MW-101C	11/24/14	Dilution	1.7 J	120	5 U	25	27	4.4 J	25 U	25	430	20	5 U	**653**
MW-101D	10/06/93		50 U	72	50 U	34	130	50	50 U	31	300	96		**713**
MW-101D	04/21/99		2.6	80	5 U	24	230	5 U	10 U	23	300	80	5 U	**740**
MW-101D	01/27/00		1.6 J	42	10 U	14	130	1.5 J	20	18	180	54	10 U	**461**
MW-101D	04/25/00		2.4 JB	70	20 U	23	250	1.9 J	40 JB	23	270	81	20 U	**761**
MW-101D	07/26/00		2.5	60	1.2	14	180	1.1	20 U	2.9	180	33	10 U	**475**
MW-101D	11/16/00		2.2	76	1.3	17	210	1.3	20 U	3.8	180	46	10 U	**538**
MW-101D	04/13/01		2.2	66	10 U	21	250	1.9	20 U	18	250	73	10 U	**682**
MW-101D	10/30/01		2.3	70	20 U	22	260	2	40 U	26	300	80	20 U	**762**
MW-101D	04/30/02		2.5	66	20 U	22	260	2	40 U	20	240	67	20 U	**680**
MW-101D	10/10/02		20 U	100	20 U	94	280	20 U	40 U	20 U	300	58	1 U	**832**
MW-101D	04/23/03		2.17	72.1 E	1 U	28.2 E	323 E	5.34	2 U	24.8	297 E	82.6 E	1 U	**835**
MW-101D	04/23/03	Dilution	20 U	64.7	20 U	23.9	291	20 U	40 U	23	254	73.7	20 U	**730**
MW-101D	04/23/03	Fld Dupe	3	155 E	50 U	44.3 E	744 E	50 U	100 U	35.9 J	603 E	151 E	1 U	**1736**
MW-101D	12/28/03		1.87	47 E	0.88 J	19.8	184 E	8.27	1 U	19.2	202 E	58.3 E	1 U	**541**
MW-101D	12/28/03	Dilution	10 U	41.8 D	10 U	17.6 D	179 D	10 U	10 U	16 D	168 D	51.6 D	10 U	**474**
MW-101D	04/28/04		25 U	68	25 U	22.2	323	25 U	50 U	20.7	249	62.3	25 U	**745**
MW-101D	05/21/05		2	74	1 U	28	330	1 U	2 U	22	230	61	1 U	**747**
MW-101D	01/12/06		2 U	53	2 U	5	85	2 U	4 U	14	190	20	2 U	**367**
MW-101D	06/23/06		10 U	77	10 U	24	410	10 U	20 U	20	220	56	10 U	**807**
MW-101D	01/04/07		5	56	5 U	16	200	5 U	10 U	15	180	46	5 U	**518**
MW-101D	10/07/07		10 U	55	10 U	22	240	10 U	10 U	18	180	50	10 U	**565**
MW-101D	05/17/08		10 U	98	10 U	35	420 E	10 U	18 J	26	250 E	70	10 U	**917**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-101D	05/17/08	Dilution	25 U	81 D	25 U	28 D	380 D	25 U	50 U	25 U	220 D	60 D	25 U	**769**
MW-101D	11/28/08	Dilution	1.46 J	41.6	0.58 J	15	199	1.94 J	0.62 J	16.4	137	39.3	2 U	**453**
MW-101D	06/10/09	Dilution	1.8 J	68	0.86 J	19	340	3.6	2 U	20	180	47	2 U	**680**
MW-101D	11/27/09	Dilution	1.5 J	64	2.5 U	18	290	4.1	2.5 U	16	150	39	2.5 U	**583**
MW-101D	06/28/10	Dilution	2.5 U	44	2.5 U	16	270	3.1	2.5 U	13	110	32	2.5 U	**488**
MW-101D	11/26/10	Dilution	1.4 J	51	1 J	18	320	0.62 J	2.5 U	17	160	38	2.5 U	**607**
MW-101D	05/31/11	Dilution	1.4 J	60	2 U	17	210	2.4	2 U	15	170	31	2 U	**507**
MW-101D	12/28/11		1	42	1 U	13	39	2.1	5 U	12	120	19	1 U	**248**
MW-101D	06/25/12		1.1	47	1 U	14	33	1.8	5 U	12	150	19	1 U	**278**
MW-101D	11/24/12		1	42	1 U	13	27	1.6	5 U	11	140	16	1 U	**252**
MW-101D	06/04/13		1.2	49	1 U	16	20	1.5	5 U	12	180	19	1 U	**299**
MW-101D	11/30/13		0.91 J	29	1 U	11	20	1	5 U	11	110	16	1 U	**199**
MW-101D	06/14/14		0.73 J	44	1 U	12	57	1.8	5 UB	11	86	18	0.19 J	**231**
MW-101D	11/24/14		0.71 J	53	1 U	14	63	2	5 U	9.6	90	15	0.28 J	**248**
MW-102A	09/28/93		2 U	26	2 U	4	32	2	23	2	34	6		**129**
MW-102A	05/20/99		1 U	43	0.25	1.2	54	1.8	2 U	0.6	51	6.3	1 U	**158**
MW-102A	10/25/99		0.15 J	43	5 U	2.5 J	61	1.7 J	10 U	3.1 J	57	15	5 U	**183**
MW-102A	02/16/00		5 U	64	5 U	2.8 J	90	3 J	10 U	5 U	97	14	5 U	**271**
MW-102A	04/25/00		5 U	43	5 U	1.5 J	49	1.4 J	10 JB	5 U	57	7.6	5 U	**170**
MW-102A	04/25/00	Fld Dupe	0.14 J	43	5 U	1.4 J	49	1.3 J	10 JB	5 U	57	7.7	5 U	**170**
MW-102A	07/26/00		10 U	71	10 U	2.7	95	2.5	20 U	10 U	100	16	10 U	**287**
MW-102A	11/16/00		5 U	91	5 U	2.8	110	2.7	10 U	5 U	88	14	5 U	**309**
MW-102A	04/10/01		10 U	91	10 U	4.2	140	4.4	20 U	10 U	120	22	10 U	**382**
MW-102A	10/17/01		10 U	77	10 U	2.3	110	4.1	20 U	10 U	88	16	10 U	**297**
MW-102A	04/30/02		5 U	47	5 U	1.6	65	1.9	10 U	5 U	62	11	5 U	**189**
MW-102A	10/10/02		20 U	130	20 U	20 U	160	20 U	40 U	20 U	140	26	1 U	**456**
MW-102A	04/25/03		1 U	101 E	1 U	4.17	153 E	5.08	2 U	1 U	123 E	25.7 E	1 U	**412**
MW-102A	04/25/03	Dilution	10 U	92.9	10 U	10 U	137	10 U	20 U	10 U	102	22.2	10 U	**354**
MW-102A	12/26/03	Dilution	10 U	118 D	10 U	10 U	156 D	5.56 JD	10 U	10 U	114 D	22.4 D	10 U	**416**
MW-102A	12/26/03		1 U	108 E	1 U	4.14	145 E	5.89	1 U	1 U	111 E	20.1	1 U	**394**
MW-102A	04/28/04		2 U	39	2 U	2 U	34.2	1.45	4 U	2 U	37.3	6.93	2 U	**119**
MW-102A	05/02/05		1 U	19	1 U	1 U	16	0.84	2 U	1 U	19	3.5	1 U	**58**
MW-102A	05/02/05	Fld Dupe	1 U	24	1 U	1 J	21	1.1	2 U	1 U	21	4.3	1 U	**72**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-102A	11/02/05		1 U	71	1 U	1.9	110	5.1	2 U	1 U	57	11	1 U	**256**
MW-102A	06/22/06		1 U	39	1 U	0.98	54	1.9	2 U	1 U	31	6.6	1 U	**133**
MW-102A	11/16/06		1 U	73	1 U	1.8	120	3.3	2 U	1 U	100	15	1 U	**313**
MW-102A	10/08/07		10 U	64	10 U	4	150	5	9	10 U	95	20	10 U	**347**
MW-102A	05/19/08		10 U	68	10 U	10 U	150	10 U	20	10 U	93	18	10 U	**349**
MW-102A	11/26/08		0.18 J	58.1	0.32 J	2.81	137	4.14	1 U	1 U	82.6	17.6	1 U	**303**
MW-102A	06/11/09		0.19 J	66	0.26 J	2.6	150	4.1	1 U	1 U	82	16	1 U	**321**
MW-102A	11/27/09		1 U	96	1 U	3.5	190	5.3	1 U	1 U	89	18	1 U	**402**
MW-102A	06/28/10	Dilution	2 U	80	2 U	2.7	170	5.3	2 U	2 U	62	15	2 U	**335**
MW-102A	11/26/10	Dilution	2 U	99	2 U	3	200	5.3	2 U	2 U	90	20	2 U	**417**
MW-102A	11/26/10	Fld Dupe	2 U	95	2 U	2.7	200	4.9	2 U	2 U	87	19	2 U	**409**
MW-102A	06/01/11		1 U	94	1 U	2.2	190	6	1 U	1 U	74	16	1 U	**382**
MW-102A	12/28/11		1 U	90	1 U	1.9	170	6	5 U	1 U	63	15	1 U	**346**
MW-102A	06/27/12		1 U	79	1 U	1.4	160	5.1	5 U	1 U	52	13	1 U	**311**
MW-102A	11/30/12		1 U	82	1 U	1.6	160	5.7	5 U	1 U	59	14	1 U	**322**
MW-102A	06/10/13		1 U	40	1 U	0.63 J	70	2.6	5 U	0.57 J	19	5.9	1 U	**139**
MW-102A	12/18/13		1 U	58	1 U	0.77 J	100	4	5 U	1 U	27	7	1 U	**197**
MW-102A	06/13/14		1 U	44	1 U	0.46 J	65	2.7	5 UB	1 U	15	4.4	1 U	**132**
MW-102A	11/24/14		1 U	2.5	0.61 J	1 U	3.4	1 U	5 U	1 U	1 U	1 U	1.3	**8**
MW-102B	09/28/93		1 U	1 U	1 U	1 U	1 U	1 U	3	1 U	1 U	1 U		**3**
MW-102B	05/20/99		1 U	0.99	0.63	0.32	2.1	1 U	2 U	1.1	1.4	2.1	1 U	**9**
MW-102B	10/25/99		1 U	0.93 J	0.66 J	0.4 J	2.7	1 U	2 U	2	5.1	3.7	0.14 J	**16**
MW-102B	02/16/00		1 U	0.32 J	0.47 J	1 U	0.28 J	1 U	2 U	1 U	1 U	1 U	1 U	**1**
MW-102B	04/25/00		1 U	0.36 J	0.49 J	1 U	0.48 J	1 U	2 U	1 U	0.2 J	0.09 J	1 U	**2**
MW-102B	07/26/00		1 U	0.62	0.54	1 U	0.54	1 U	2 U	1 U	1 U	1 U	0.19 J	**2**
MW-102B	11/16/00		1 U	0.76	1 U	1 U	0.62	1 U	2 U	1 U	1 U	1 U	0.17 J	**2**
MW-102B	11/16/00	Fld Dupe	1 U	0.74 J	0.6 J	1 U	0.59 J	1 U	2 U	1 U	1 U	1 U	0.16 J	**2**
MW-102B	04/10/01		1 U	0.71	0.61	1 U	0.71	1 U	2 U	1 U	1 U	1 U	0.11 J	**2**
MW-102B	10/17/01		1 U	0.83	1 U	1 U	1.2	1 U	2 U	1 U	1 U	1 U	0.13 J	**2**
MW-102B	04/30/02		1 U	1	0.58	1 U	1.4	0.13	2 U	1 U	1 U	1 U	0.089	**3**
MW-102B	10/10/02		1 U	2	1 U	1 U	2	1 U	0.6	1 U	1 U	1 U	1 U	**5**
MW-102B	04/25/03		1 U	1.35	1 U	1 U	2.27	1 U	2 U	1 U	1 U	1 U	1 U	**4**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-102B	12/26/03		1 U	1.64	0.64 J	1 U	2.9	1 U	1 U	1 U	1 U	1 U	1 U	**5**
MW-102B	04/28/04		1 U	1.73	0.62	1 U	3.2	1 U	2 U	1 U	1 U	1 U	1 U	**6**
MW-102B	05/02/05		1 U	1.6	0.48	1 U	2.4	1 U	2 U	1 U	1 U	1 U	1 U	**4**
MW-102B	11/02/05		1 U	1.9	1 U	1 U	3.5	1 U	2 U	1 U	1 U	1 U	1 U	**5**
MW-102B	06/22/06		1 U	2.3	1 U	1 U	4.3	1 U	2 U	1 U	1 U	1 U	1 U	**7**
MW-102B	11/16/06		1 U	3	1 U	1 U	5	1 U	2 U	1 U	1 U	1 U	1 U	**8**
MW-102B	10/08/07		1 U	3	0.5	1 U	4	1 U	2 U	1 U	1 U	1 U	1 U	**8**
MW-102B	05/19/08		1 U	4	1 U	1 U	6	1 U	2 U	1 U	1 U	1 U	1 U	**10**
MW-102B	11/26/08		1 U	2.8	0.66 J	1 U	5.11	0.28 J	1 U	1 U	1 U	1 U	0.18 J	**9**
MW-102B	06/11/09		1 U	3.2	0.65 J	1 U	5	1 U	1 U	1 U	1 U	1 U	1 U	**9**
MW-102B	11/27/09		1 U	3.5	0.56 J	1 U	5.6	1 U	1 U	1 U	1 U	1 U	1 U	**10**
MW-102B	06/28/10		1 U	3	0.69 J	1 U	4.4	1 U	1 U	1 U	1 U	1 U	1 U	**8**
MW-102B	11/26/10		1 U	2.9	0.67 J	1 U	5	1 U	1 U	1 U	1 U	1 U	1 U	**9**
MW-102B	06/01/11		1 U	2.8	1 U	1 U	4	1 U	1 U	1 U	1 U	1 U	1 U	**7**
MW-102B	12/28/11		1 U	2.8	1 U	1 U	4.1	1 U	5 U	1 U	1 U	1 U	0.32 J	**7**
MW-102B	06/27/12		1 U	2.7	1 U	1 U	3.8	1 U	5 U	1 U	1 U	1 U	0.32 J	**7**
MW-102B	06/27/12	Fld Dupe	1 U	2.7	1 U	1 U	3.9	1 U	5 U	1 U	1 U	1 U	0.31 J	**7**
MW-102B	11/30/12		1 U	2.8	0.52 J	1 U	4.6	1 U	5 U	1 U	1 U	1 U	0.43 J	**8**
MW-102B	06/05/13		1 U	2.7	1 U	1 U	3.5	1 U	5 U	1 U	1 U	1 U	0.52 J	**7**
MW-102B	12/18/13		1 U	60	1 U	0.81 J	110	4.2	5 U	1 U	28	7.4	1 U	**210**
MW-102B	06/13/14		1 U	2.8	0.64 J	1 U	3.5	1 U	5 UB	1 U	1 U	1 U	0.92 J	**8**
MW-102B	11/24/14		1 U	2.6	0.8 J	1 U	3.5	1 U	5 U	1 U	1 U	1 U	1.2	**8**
MW-102C	09/28/93		12 U	160	12 U	68	140	12 U	55	44	160	140		**767**
MW-102C	05/20/99		2.5	180	4	59	390	10 U	20 U	33	170	140	10 U	**979**
MW-102C	10/25/99		3 J	210	25 U	78	460	25 U	50 U	46	250	170	25 U	**1217**
MW-102C	02/16/00		0.66 J	32	0.91 J	12	61 E	0.57 J	0.38 J	5.9	60 E	26	2 U	**199**
MW-102C	02/16/00	Dilution	0.52 DJ	24 D	5 U	9 D	44 D	5 U	10 U	4.4 DJ	44 D	20 D	5 U	**146**
MW-102C	04/25/00		0.91 J	44	5 U	5.2	65	0.96 J	10 JB	0.67 J	60	10	5 U	**197**
MW-102C	07/26/00		0.64	29	0.8	4.5	39	0.41	4 U	0.99	44	8.2	2 U	**128**
MW-102C	11/16/00		0.32	19	2 U	4.5	28	0.26	4 U	1.1	23	8.3	2 U	**84**
MW-102C	04/10/01		0.94	48	5 U	2.6	39	5 U	10 U	0.8	90	5.4	5 U	**187**
MW-102C	10/17/01		0.6	29	4 U	8.9	53	0.39	8 U	3.5	46	17	4 U	**158**
MW-102C	04/30/02		2.1	110	2.4	40	240	3.3	20 U	19	170	78	10 U	**665**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-102C	10/10/02		5 U	56	5 U	54	87	5 U	10 U	4 J	69	20	1 U	**290**
MW-102C	04/25/03		1.16	83.3 E	1.57	33 E	200 E	4	2 U	16.3	143 E	64.8 E	1 U	**547**
MW-102C	04/25/03	Dilution	10 U	48.4	10 U	18.6	112	10 U	20 U	7.94 J	73.2	34.9	10 U	**295**
MW-102C	12/26/03		0.6 J	40.4 E	0.76 J	9.18	69 E	1.04	1 U	1.6	60.2 E	16.3	1 U	**199**
MW-102C	12/26/03	Dilution	4 U	42.6 D	4 U	9.85 D	79.1 D	4 U	4 U	4 U	59 D	16.2 D	4 U	**207**
MW-102C	04/28/04		25 U	105	25 U	38.2	278	25 U	50 U	20.9	136	70.4	25 U	**649**
MW-102C	05/02/05		0.74	69	1.2	0.62	22	1 U	2 U	1.1	110	1.5	1 U	**206**
MW-102C	11/02/05		1 U	3.4	1 U	1.3	7.4	1 U	2 U	1 U	6.4	2.9	1 U	**21**
MW-102C	11/02/05	Fld Dupe	1 U	18	1 U	5.8	46	1 U	2 U	2.5 H	15	9.9	1 U	**97**
MW-102C	06/22/06		1 U	23	1 U	8.4	49	1 U	2 U	4.9	19	15	1 U	**119**
MW-102C	11/16/06		1 U	69	1.3	10	120	0.97 J	2 U	4	70	23	1 U	**298**
MW-102C	10/08/07		0.4	60	1	22	170	2	2 U	10	35	34	1 U	**334**
MW-102C	10/08/07	Fld Dupe	0.5 J	90 D	1	33 D	270 D	4	2 U	16	52 D	51 D	0.6 J	**518**
MW-102C	05/19/08		10 U	66	10 U	26	210	10 U	21	12	74	37	10 U	**446**
MW-102C	11/26/08		0.21 J	18.9	0.33 J	5.75	56.6	0.79 J	1 U	2.66	18.4	9.54	1 U	**113**
MW-102C	06/11/09		0.31 J	36	0.57 J	6.1	99	0.74 J	1 U	0.94 J	23	8.9	1 U	**176**
MW-102C	11/27/09	Dilution	10 U	210	10 U	59	760	6.7 J	10 U	22	94	74	10 U	**1226**
MW-102C	06/28/10	Dilution	5 U	160	5 U	53	740	6.8	5 U	18	89	65	5 U	**1132**
MW-102C	11/26/10	Dilution	10 U	170	3.2 J	51	720	10 U	10 U	21	110	68	10 U	**1143**
MW-102C	06/01/11	Dilution	5 U	200	5 U	50	870	7	5 U	25	90	63	5 U	**1305**
MW-102C	12/28/11	Dilution	0.95 J	160	5 U	40	670	5.6	25 U	17	80	47	5 U	**1021**
MW-102C	06/27/12	Dilution	1.2 J	130	5 U	33	550	4.4 J	25 U	7.3	55	30	5 U	**811**
MW-102C	11/30/12	Dilution	0.36 J	64	0.54 J	15	200	2	10 U	4.2	41	15	2 U	**342**
MW-102C	06/05/13	Dilution	0.7 J	150	2 U	36	360	4	6.2 J	10	84	33	0.8 J	**685**
MW-102C	12/18/13	Fld Dupe	0.65 J	160	1.1 J	37	300	4.4	7.1 J	8.2	77	28	1 J	**624**
MW-102C	12/18/13	Dilution	0.75 J	120	1.1 J	31	270	4	5 UB	7.3	78	24	0.58 J	**537**
MW-102C	06/13/14		1 U	5.3	1 U	0.76 J	6.5	1 U	5 UB	0.4 J	1.2	0.6 J	1 U	**15**
MW-102C	11/24/14		1 U	1	1 U	1 U	1.4	1 U	5 U	1 U	0.26 J	1 U	1 U	**3**
MW-113A	10/08/93		7 U	92	7 U	33	110	7 U	14 U	7 U	140	56		**431**
MW-113A	05/03/99		0.9	34	0.4	10	52	1.2	2 U	1.9	59	24	1 U	**183**
MW-113A	11/10/99		2.3 J	100	10 U	27	160	2.4 J	20	3.2 J	160	69	10 U	**544**
MW-113A	02/15/00		2.1 J	91	10 U	16	160	5.7 J	20 U	2.9 J	160	71	10 U	**509**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-113A	04/24/00		2.1 JB	92	10 U	5.1 J	160	13	20 JB	2.4 J	160	61	10 U	**516**
MW-113A	07/27/00		2.3	86	10 U	4	110	7.5	20 U	10 U	130	22	1 U	**362**
MW-113A	11/16/00		2.3	130	10 U	9.4	200	12	20 U	2.1	170	62	10 U	**588**
MW-113A	04/12/01		2.4	10	10 U	210	210	15	20 U	3.7	200	81	10 U	**732**
MW-113A	10/31/01		2.8	110	10 U	3	240	22	20 U	3.3	200	75	10 U	**656**
MW-113A	04/29/02		2.5	100	10 U	1.5	200	23	20 U	4.5	200	70	10 U	**602**
MW-113A	10/18/02		20 U	190	20 U	240	430	20 U	40 U	20 U	370	140	1 U	**1370**
MW-113A	04/23/03		2.84	139 E	1 U	27.6 E	371 E	18.2	2 U	8.11	306 E	126 E	1 U	**999**
MW-113A	04/23/03	Dilution	25 U	121	25 U	33.9	325	25 U	50 U	25 U	245	101	25 U	**826**
MW-113A	12/28/03		2.93	140 E	1.38	38.3 E	345 E	10.4	1 U	9.72	309 E	124 E	1 U	**981**
MW-113A	12/28/03	Dilution	20 U	109 D	20 U	31.4 D	318 D	20 U	20 U	20 U	232 D	92.9 D	20 U	**783**
MW-113A	04/28/04	Fld Dupe	3.09	123	1.6	35.9	371	37.9 E	2 U	10.3	240	96.8	1 U	**920**
MW-113A	04/28/04		25 U	123	25 U	32.4	360	25 U	50 U	25 U	239	89.1	25 U	**844**
MW-113A	05/21/05		5 U	140	5 U	45	410	5.7	10 U	8.1	260	100	5 U	**969**
MW-113A	10/20/05		2.6	110	1 U	22	330	17	2 U	8	210	82	1 U	**782**
MW-113A	05/08/06		2.3	110	1 U	32	470	9.1	20 U	10	270	93	1 U	**996**
MW-113A	01/04/07		10 U	110	10 U	27	430	10 U	20 U	10	210	10	10 U	**797**
MW-113A	10/08/07		2	150	1	46	480	15	2 U	10	260	110	1 U	**1074**
MW-113A	05/17/08		20 U	160	20 U	54	510 E	20 U	41	20 U	280	130	20 U	**1175**
MW-113A	05/17/08	Dilution	40 U	140 D	40 U	48 D	470 D	40 U	80 U	40 U	250 D	110 D	40 U	**1018**
MW-113A	11/29/08	Dilution	2.2 J	135	1.5 J	7.25	369	40.6	1.7 J	10.5	210	98.6	5 U	**876**
MW-113A	06/11/09	Dilution	2.6 J	110	5 U	21	370	15	5 U	10	180	85	5 U	**794**
MW-113A	11/28/09	Dilution	1.5 J	110	2.5 U	1.7 J	290	44	2.5 U	12	170	84	2.5 U	**713**
MW-113A	06/29/10	Dilution	1.1 J	88	1 J	3.3	240	30	0.85 J	12	130	76	2.5 U	**582**
MW-113A	11/28/10	Dilution	0.95 J	85	0.7 J	17	250	11	2.5 U	12	110	67	2.5 U	**554**
MW-113A	06/01/11		0.96 J	88	1 U	2.4	90	14	1 U	13	120	57	1 U	**385**
MW-113A	12/29/11		1.1	95	1 U	16	50	4.3	5 U	13	130	46	1 U	**355**
MW-113A	06/25/12		1.1	100	1 U	14	48	5.3	5 U	13	140	48	1 U	**369**
MW-113A	11/24/12		1.2	110	1 U	14	43	4.4	5 U	13	140	45	1 U	**371**
MW-113A	06/04/13		1.2	120	1 U	26	40	3.9	5 U	13	160	45	1 U	**409**
MW-113A	11/30/13		1.2	140	1 U	33	37	4.4	5 UB	13	160	51	1 U	**440**
MW-113A	06/14/14		1.3	140	1 U	32	32	4.5	5 UB	14	160	49	1 U	**433**
MW-113A	11/24/14		1.3	140	1 U	18	31	5.2	5 U	11	140	50	1 U	**397**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-113B	10/19/93		2 U	14	2 U	4	12	2 U	3 U	2 U	6	6		**42**
MW-113B	04/29/99		0.54	33	0.56	12	38	0.65	2 U	1.8	17	19	1 U	**123**
MW-113B	10/27/99		0.45 J	33	5 U	8.4	39	0.55 J	10 U	1.3 J	13	20	5 U	**116**
MW-113B	02/15/00		0.65 J	48	5 U	11	62	0.83 J	10 U	1.4 J	27	30	5 U	**181**
MW-113B	04/24/00		0.61 JB	43	5 U	11	56	0.98 J	10 JB	1.2 J	21	26	5 U	**170**
MW-113B	07/27/00		0.71	38	0.6	9.4	49	0.91	10 U	0.89	17	20	5 U	**137**
MW-113B	11/16/00		0.63	55	5 U	11	62	1.3	10 U	1.4	22	27	5 U	**180**
MW-113B	04/12/01		0.56	40	5 U	8.9	53	1	10 U	5 U	17	20	5 U	**140**
MW-113B	10/31/01		0.64	50	5 U	12	67	1.1	10 U	5 U	24	29	5 U	**184**
MW-113B	04/29/02		0.6	39	5 U	9.8	60	0.97	10 U	1.3	19	23	5 U	**154**
MW-113B	10/18/02		10 U	84	10 U	88	120	10 U	5	10 U	39	42	1 U	**378**
MW-113B	04/23/03		1.05	77.3 E	1 U	23.3	143 E	6.06	2 U	3.77	65.8 E	55.8 E	2.2	**378**
MW-113B	04/23/03	Dilution	10 U	58.6	10 U	17.4	115	10 U	20 U	10 U	45.6	41.9	10 U	**279**
MW-113B	12/28/03		0.97 J	71.3 E	1 U	21.4	134 E	4.01	1 U	3.72	53.4 E	52.1 E	1.24	**342**
MW-113B	12/28/03	Dilution	10 U	65.1 D	10 U	19.1 D	129 D	10 U	10 U	10 U	43.1 D	45.9 D	10 U	**302**
MW-113B	04/28/04		10 U	70	10 U	19.8	143	10 U	20 U	10 U	44.9	42.7	10 U	**320**
MW-113B	05/21/05		1 U	64	1 U	19	140	1.8	2 U	2.9	39	39	4.8	**311**
MW-113B	10/20/05		1 U	78	1 U	22	170	1.9	2 U	3.8	45	47	1 U	**368**
MW-113B	05/08/06		1 U	64	1 U	21	140	1.9	2 U	3.6	33	37	9.2	**310**
MW-113B	01/04/07		1 U	61	1 U	20	120	1.7	2 U	3	30	38	1.4	**275**
MW-113B	10/08/07		0.5	56	0.6	17	120	2	2 U	3	21	30	15	**265**
MW-113B	05/17/08		10 U	66	10 U	19	140	10 U	19 J	10 U	25	34	17	**320**
MW-113B	11/29/08		0.71 J	71.3	0.92 J	20.4	169	2.15	1 U	3.49	28.8	41.5	6.2	**344**
MW-113B	06/11/09		0.73 J	71	0.87 J	19	180	2.2	1 U	3.6	29	42	6.9	**355**
MW-113B	11/28/09		0.69 J	77	0.76 J	22	190	2.5	1 U	3.9	31	41	8	**377**
MW-113B	06/29/10	Dilution	2 U	63	2 U	19	150	2.7	2 U	3	19	33	9	**299**
MW-113B	11/28/10	Dilution	2 U	67	0.8 J	19	160	3	2 U	4.2	26	37	8.8	**326**
MW-113B	06/01/11		0.46 J	66	0.61 J	18	140	2.3	1 U	4.1	23	36	11	**301**
MW-113B	12/29/11		0.42 J	59	0.63 J	16	100	2	5 U	3.9	19	30	8.9	**240**
MW-113B	06/25/12		0.48 J	60	1 U	14	98	1.9	5 U	3.6	17	28	9.4	**232**
MW-113B	11/24/12		0.34 J	59	0.46 J	14	78	1.8	5 U	3.7	18	26	7.5	**209**
MW-113B	06/04/13		0.27 J	55	1 U	12	58	1.4	5 U	2.5	12	20	12	**173**
MW-113B	11/30/13		0.3 J	53	0.36 J	12	56	1.4	5 U	2.7	11	21	9.6	**167**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-113B	06/14/14		0.28 J	63	0.42 J	14	52	1.7	5 UB	2.8	13	19	12	**178**
MW-113B	11/24/14		0.4 J	66	0.52 J	15	55	2.2	5 U	2.1	13	22	13	**189**
MW-114A	10/05/93		1 U	2	1 U	4	5	1 U	2 U	1 U	6	2		**19**
MW-114A	04/28/99		5 U	6.7	5 U	46	14	5 U	10 U	1.9 J	250	34	5 U	**353**
MW-114A	10/26/99		0.34 J	7.1 J	25 U	48	11 J	25 U	50 U	25 U	290	47	25 U	**403**
MW-114A	01/31/00		10 U	5 J	10 U	34	6.6 J	10 U	1.5 J	10 U	220	33	10 U	**300**
MW-114A	04/24/00		10 U	4.2 J	10 U	26	5.6 J	10 U	20 JB	10 U	160	24	10 U	**240**
MW-114A	07/27/00		10 U	3.9	10 U	24	5.4	10 U	20 U	10 U	140	22	10 U	**195**
MW-114A	11/13/00		10 U	4.2	10 U	20	4.7	10 U	20 U	10 U	120	19	10 U	**168**
MW-114A	04/12/01		5 U	2.7	5 U	18	3.9	5 U	10 U	5 U	120	20	5 U	**165**
MW-114A	10/31/01		5 U	2.5	5 U	15	3.6	5 U	10 U	5 U	100	18	5 U	**139**
MW-114A	04/25/02		5 U	3.1	5 U	16	4.1	5 U	10 U	5 U	100	22	5 U	**145**
MW-114A	04/25/02	Fld Dupe	5 U	3.1 J	5 U	16	4 J	5 U	10 U	5 U	100	22	5 U	**145**
MW-114A	10/15/02		10 U	10 U	10 U	140	7	10 U	20 U	10 U	170	38	1 U	**355**
MW-114A	04/23/03		1 U	3.28	1 U	13.4	4.09	1 U	2 U	1 U	94.6 E	23.5	1 U	**139**
MW-114A	04/23/03	Dilution	10 U	10 U	10 U	12.9	10 U	10 U	20 U	10 U	80.2	20.8	10 U	**114**
MW-114A	12/26/03		1 U	2.86	1 U	9.96	3.62	1 U	1 U	1 U	73.9 E	16.3	1 U	**107**
MW-114A	12/26/03	Dilution	4 U	2.86 JD	4 U	10.3 D	3.6 JD	4 U	4 U	4 U	70.1 D	15.9 D	4 U	**103**
MW-114A	04/28/04		5 U	3.69	5 U	12	4.25	5 U	10 U	5 U	79.9	20.8	5 U	**121**
MW-114A	05/21/05		1 U	2.5	1 U	5.7	3.3	1 U	2 U	1 U	28	7.9	1 U	**47**
MW-114A	10/20/05		1 U	2.6	1 U	7.2	2.9	1 U	2 U	1 U	39	9.8	1 U	**62**
MW-114A	05/06/06		1 U	3.4	1 U	9.4	3.7	1 U	2 U	1 U	44	12	1 U	**73**
MW-114A	01/04/07		1 U	3.5	1 U	11	3.3	1 U	2 U	1 U	51	9.6	1 U	**78**
MW-114A	10/08/07		1 U	2	1 U	7	2	1 U	2 U	2 U	34	5	1 U	**50**
MW-114A	05/17/08		2 U	2	2 U	5	3	2 U	3 J	2 U	28	4	2 U	**45**
MW-114A	11/29/08		1 U	0.28 J	1 U	1 U	1 U	1 U	1 U	1 U	1.09	1 U	1 U	**1**
MW-114A	06/11/09		0.16 J	1 U	1 U	1 U	1 U	1 U	1 U	1 U	0.9 J	1 U	1 U	**1**
MW-114A	11/28/09		0.46 J	1.9	1 U	3.9	1.3	1 U	1 U	1 U	36	2.7	1 U	**46**
MW-114A	06/25/10		1 U	3.2	1 U	6.6	2.2	1 U	1 U	1 U	70	4.4	1 U	**86**
MW-114A	11/27/10		1 U	2.8	1 U	8.5	2.1	1 U	1 U	1 U	65	4.7	1 U	**83**
MW-114A	06/01/11		1 U	4.2	1 U	10	2.9	1 U	1 U	1 U	85	5.5	1 U	**108**
MW-114A	12/28/11		1 U	3.6	1 U	9.1	2.6	1 U	5 U	0.18 J	65	4.1	1 U	**85**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-114A	06/27/12		0.21 J	4.3	1 U	5.6	3	1 U	5 U	1 U	71	4.2	1 U	**88**
MW-114A	11/24/12		1 U	2.9	1 U	1.6	2.4	0.22 J	5 U	1 U	27	1.8	1 U	**36**
MW-114A	06/07/13		1 U	5.5	1 U	11	4.3	1 U	5 U	1 U	82	4.7	1 U	**108**
MW-114A	12/19/13		1 U	3.1	1 U	5.8	2.7	1 U	5 U	0.19 J	43	2.3	1 U	**57**
MW-114A	06/14/14		1 U	6.3	1 U	5.5	4.8	1 U	5 UB	0.23 J	52	3.1	1 U	**72**
MW-114A	11/24/14		1 U	4.6	1 U	4.9	4.1	1 U	5 U	0.27 J	38	3.1	1 U	**55**
MW-114B	10/04/93		2 U	14	2 U	4	12	2 U	3 U	2 U	6	6		**42**
MW-114B	04/28/99		1 U	0.89	1 U	0.6	3.3	1 U	2 U	1	4	6.2	1 U	**16**
MW-114B	10/26/99		1 U	1	1 U	0.46 J	3.3	1 U	2 U	0.66 J	1.2	8.2	1 U	**15**
MW-114B	01/31/00		1 U	0.81 J	1 U	0.18 J	2.3	1 U	2 U	1 U	1 U	5.7	1 U	**9**
MW-114B	04/24/00		1 U	0.68 J	1 U	0.11 J	1.7	1 U	2 JB	1 U	0.05 J	1.8	1 U	**6**
MW-114B	07/27/00		1 U	1	1 U	0.26	3	1 U	2 U	1 U	1 U	7.9	1 U	**12**
MW-114B	07/27/00	Fld Dupe	1 U	1	1 U	0.26 J	3	1 U	2 U	1 U	1 U	7.5	1 U	**12**
MW-114B	11/13/00		1 U	1.2	1 U	0.13	2.4	1 U	2 U	1 U	1 U	3.5	1 U	**7**
MW-114B	04/12/01		1 U	0.98	1 U	0.26	2.9	1 U	2 U	1 U	1 U	8.2	1 U	**12**
MW-114B	10/31/01		1 U	0.96	1 U	0.13	2.2	1 U	2 U	1 U	1 U	4.8	1 U	**8**
MW-114B	04/25/02		1 U	1.1	1 U	0.29	3	0.04	2 U	1 U	1 U	7.2	1 U	**12**
MW-114B	10/15/02		1 U	2	3	1	3	1 U	0.6	1 U	1 U	9	1 U	**19**
MW-114B	04/23/03		1 U	1.15	1 U	1 U	2.84	1 U	2 U	1 U	1 U	8.8	1 U	**13**
MW-114B	12/26/03		1 U	1.25	1 U	1.07	2.98	1 U	1 U	1 U	1 U	8.91	1 U	**14**
MW-114B	04/28/04		1 U	1.21	1 U	1 U	2.87	1 U	2 U	1 U	1 U	8.82	1 U	**13**
MW-114B	05/21/05		1 U	1.5	1 U	1 U	2.3	1 U	2 U	1 U	1 U	7.6	1 U	**11**
MW-114B	10/20/05		1 U	1.6	1 U	1 U	2.3	1 U	2 U	1 U	1 U	8.8	1 U	**13**
MW-114B	05/06/06		1 U	1 U	1 U	1 U	2.1	1 U	2 U	1 U	1 U	8.7	1 U	**11**
MW-114B	01/04/07		1 U	1.4	1 U	1 U	1.8	1 U	2 U	1 U	1 U	6.7	1 U	**10**
MW-114B	01/04/07	Fld Dupe	1 U	1.6	1 U	1 U	1.8	1 U	2 U	1 U	1 U	6.4	1 U	**10**
MW-114B	10/08/07		1 U	2	1 U	0.5	2	1 U	2 U	1 U	1 U	6	1 U	**11**
MW-114B	05/17/08		1 U	2	1 U	1 U	2	1 U	2 U	1 U	1 U	9	1 U	**13**
MW-114B	12/18/08		1 U	1.6	1 U	0.67 J	2	1 U	1 U	1 U	1 U	6.8	1 U	**11**
MW-114B	06/20/09		1 U	1.8	1 U	0.67 J	2.2	1 U	1 U	1 U	1 U	6.5	1 U	**11**
MW-114B	11/28/09	Fld Dupe	1 U	2.4	1 U	0.93 J	1.9	1 U	1 U	1 U	1 U	6.8	1 U	**12**
MW-114B	11/28/09		1 U	2.2	1 U	1	2	1 U	1 U	1 U	1 U	6.7	1 U	**12**
MW-114B	06/25/10		1 U	2.1	1 U	0.84 J	2	1 U	1 U	1 U	1 U	6.3	1 U	**11**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-114B	06/25/10	Fld Dupe	1 U	2	1 U	0.81 J	1.9	1 U	1 U	1 U	1 U	6.3	1 U	**11**
MW-114B	11/27/10		1 U	1.8	1 U	1	2.3	1 U	1 U	1 U	1 U	7.8	1 U	**13**
MW-114B	06/01/11		1 U	1.6	1 U	1 U	2.1	1 U	1 U	1 U	1 U	7.7	1 U	**11**
MW-114B	06/01/11	Fld Dupe	1 U	1.6	1 U	1 U	2.1	1 U	1 U	1 U	1 U	7.4	1 U	**11**
MW-114B	12/28/11		1 U	1.3	1 U	0.54 J	2.2	1 U	5 U	1 U	1 U	6.7	1 U	**11**
MW-114B	06/28/12		1 U	1.1	1 U	1 U	1.8	1 U	5 U	1 U	1 U	6.5	1 U	**9**
MW-114B	06/28/12	Fld Dupe	1 U	1.1	1 U	0.41 J	1.8	1 U	5 U	1 U	1 U	6.7	1 U	**10**
MW-114B	11/24/12	Fld Dupe	1 U	1.3	1 U	0.38 J	1.8	1 U	5 U	1 U	1 U	5.8	1 U	**9**
MW-114B	11/24/12		1 U	1.3	1 U	0.44 J	1.9	1 U	5 U	1 U	1 U	6.1	1 U	**10**
MW-114B	06/07/13		1 U	1.2	1 U	1 U	1.9	1 U	5 U	1 U	1 U	6.9	1 U	**10**
MW-114B	06/14/14		1 U	1.5	1 U	1 U	1.5	1 U	5 UB	1 U	1 U	4.9	1 U	**8**
MW-114B	06/14/14	Fld Dupe	1 U	1.4	1 U	1 U	1.5	1 U	5 UB	1 U	1 U	4.6	1 U	**8**
MW-114B	11/24/14		1 U	1.4	1 U	1 U	1	1 U	5 U	0.28 J	0.24 J	4	1 U	**7**
MW-117B	10/04/93		0.6	1 U	1 U	1 U	1	1 U	2 U	4	2	5		**13**
MW-117B	04/22/99		0.72	7.3	0.54	14	16	1 U	2 U	3.1	83	21	1 U	**146**
MW-117B	10/18/99		0.58 J	7.7	5 U	14	17	5 U	10	1.3 J	68	17	5 U	**136**
MW-117B	01/26/00		0.36 J	8	5 U	9.5	18	5 U	10	1.9 J	59	22	5 U	**129**
MW-117B	04/17/00		0.39 J	8.1	0.42 J	11	19	2 U	4 JB	1.6 J	49	19	0.07 J	**113**
MW-117B	07/24/00		0.49	6.6	2 U	9.6	15	2 U	4 U	1.7	42	17	2 U	**92**
MW-117B	11/07/00		0.42	10	2 U	11	18	2 U	4 U	1.7	37	19	2 U	**97**
MW-117B	04/09/01		0.37	5.8	2 U	7.3	13	0.25	4 U	1.8	28	17	2 U	**74**
MW-117B	10/15/01		0.35	7.1	2 U	7.5	16	2 U	4 U	1.3	23	16	2 U	**71**
MW-117B	04/16/02		0.3	5.9	0.22	7.3	15	0.2	2 U	1.7	22	16	1 U	**69**
MW-117B	10/07/02		5 U	8	5 U	54	20	5 U	10 U	3	25	16	1 U	**126**
MW-117B	04/22/03		1 U	7.55	1 U	10.4	20.1	0.61 J	2 U	2.31	23.1	18.4	1 U	**82**
MW-117B	12/22/03		0.99 J	5.96	1 U	9.38	18.7	0.53 J	1 U	2.25	21.8	16.9	1 U	**77**
MW-117B	04/28/04		0.73	3.77	1 U	4.76	11.5	1 U	2 U	2	13.5	11.5	1 U	**48**
MW-117B	05/21/05		1 U	4.5	1 U	5.7	13	1 U	2 U	1.6	11	9.4	1 U	**45**
MW-117B	10/19/05		1 U	4.7	1 U	5.6	14	1 U	2 U	1.8	12	9.3	1 U	**47**
MW-117B	06/28/06		1 U	21	1 U	23	70	1 U	2 U	24	56	23	1 U	**217**
MW-117B	11/21/06		1 U	3.6	1 U	4	11	1 U	2 U	2.1	12	11	1 U	**44**
MW-117B	10/06/07		0.4	6	1 U	8	8	1 U	2 U	2	16	12	1 U	**52**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-117B	05/17/08		1 U	8	1 U	11	11	1 U	2 U	3	25 E	16	1 U	**74**
MW-117B	05/17/08	Dilution	2 U	7 D	2 U	10 D	9 D	2 U	4 U	3 D	22 D	14 D	2 U	**65**
MW-117B	11/28/08		0.38 J	7.91	1 U	8.73	8.11	1 U	1 U	4.99	24	15.8	1 U	**70**
MW-117B	06/09/09		0.49 J	11	1 U	12	7.9	1 U	1 U	4.5	31	17	1 U	**84**
MW-117B	11/24/09		0.42 J	8.5	1 U	9	5.1	1 U	1 U	5.3	24	15	1 U	**67**
MW-117B	06/24/10		0.32 J	12	1 U	12	6	1 U	1 U	6.5	37	17	1 U	**91**
MW-117B	11/24/10		0.31 J	11	1 U	8.1	4.6	1 U	1 U	8.4	31	19	1 U	**82**
MW-117B	05/31/11		1 U	4.7	1 U	3.9	2.2	1 U	1 U	7.8	13	10	1 U	**42**
MW-117B	12/22/11		0.29 J	8.7	1 U	4.5	1.8	1 U	5 U	6.7	11	8.7	1 U	**42**
MW-117B	06/26/12		0.3 J	5.9	1 U	2.6	0.77 J	1 U	5 U	5.9	7.8	5.7	1 U	**29**
MW-117B	11/25/12		0.35 J	10	1 U	3	1.1	1 U	5 U	5.7	10	6	1 U	**36**
MW-117B	05/30/13		0.27 J	3	1 U	1.6	0.6 J	1 U	5 U	5.2	4.4	3.7	1 U	**19**
MW-117B	11/29/13		0.39 J	8.4	1 U	3.1	0.9 J	1 U	5 U	5.5	7.4	4.9	1 U	**31**
MW-117B	06/05/14		0.21 J	4	1 U	1.9	0.55 J	1 U	5 U	5.4	5	3.6	1 U	**21**
MW-117B	11/21/14		0.3 J	11	1 U	3.7	0.82 J	1 U	5 U	4.8	7.9	4.4	1 U	**33**
MW-117C	10/04/93		2 U	17	2 U	13	23	2 U	5 U	2 U	50	75		**178**
MW-117C	04/22/99		0.77	54	2.3	44	69	2 U	4 U	6	75	36	0.79 J	**288**
MW-117C	10/18/99		5 U	60	5 U	53	82	5 U	10 U	7.5	94	40	0.96 J	**337**
MW-117C	02/16/00		0.82 J	61	5 U	53	94	0.5 J	0.8 J	9.7	93	41	0.9 J	**355**
MW-117C	04/18/00		0.79 J	54	2.2 J	49	94	0.6 J	10 JB	10	91	39	0.82 J	**351**
MW-117C	07/24/00		1	55	2.4	48	99	1.1	10 U	8.7	89	38	0.63 J	**343**
MW-117C	11/07/00		0.79	69	2.4	50	100	5 U	10 U	8.8	78	34	0.74 J	**344**
MW-117C	04/09/01		0.84	57	2.3	59	120	0.82	10 U	12	99	42	0.72 J	**394**
MW-117C	10/15/01		0.81	48	5 U	45	110	0.44	10 U	11	74	32	0.67 J	**322**
MW-117C	04/16/02		0.75	41	1.6	469	120	0.74	0.3	16	82	34	0.42 J	**766**
MW-117C	10/07/02		20 U	59	20 U	330	150	20 U	32	22	110	42	0.6 J	**746**
MW-117C	04/22/03		0.85 J	43.6 E	1.35	63.6 E	134 E	1.71	2 U	27.1 E	113 E	48 E	0.67 J	**434**
MW-117C	04/22/03	Dilution	10 U	40	10 U	58.2	123	10 U	20 U	23.1	93	44.3	10 U	**382**
MW-117C	12/22/03		0.82 J	39.6 E	1.01	55.8 E	126 E	2.07	1 U	27.5 E	104 E	46.4 E	1 U	**403**
MW-117C	12/22/03	Dilution	10 U	33.1 D	10 U	43.3 D	107 D	10 U	10 U	19.9 D	78.2 D	34.8 D	10 U	**316**
MW-117C	04/28/04		10 U	30.5	10 U	37	97.3	10 U	20 U	20.3	66.4	30.1	10 U	**282**
MW-117C	05/21/05		1 U	28	1 U	34	91	1 U	2 U	22	59	27	1 U	**261**
MW-117C	10/19/05		1 U	25	1 U	29	84	1 U	2 U	20	54	26	1 U	**238**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-117C	05/06/06		1 U	25	1 U	26	91	1 U	2 U	21	50	26	1 U	**239**
MW-117C	11/21/06		1 U	41	1 U	46	140	1 U	2 U	36	100	44	1 U	**407**
MW-117C	10/06/07		0.5	24	0.3	30	88	0.9	2 U	24	60	26	1 U	**254**
MW-117C	05/17/08		5 U	28	5 U	33	99	5 U	10	30	72	30	5 U	**302**
MW-117C	11/28/08		0.55 J	24.1	0.26 J	25.6	85.9	0.31 J	1 U	26.5	57.1	23.1	1 U	**243**
MW-117C	06/09/09		0.51 J	24	0.23 J	25	70	0.33 J	1 U	26	58	23	1 U	**227**
MW-117C	11/24/09		0.48 J	23	1 U	24	57	1 U	1 U	26	51	21	1 U	**202**
MW-117C	06/24/10		0.42 J	24	1 U	23	40	0.24 J	1 U	28	51	20	1 U	**187**
MW-117C	11/24/10		0.38 J	22	1 U	22	34	1 U	1 U	27	53	21	1 U	**179**
MW-117C	05/31/11		0.45 J	25	1 U	21	24	1 U	1 U	27	47	19	1 U	**163**
MW-117C	12/22/11		0.38 J	23	1 U	17	13	1 U	5 U	25	37	17	1 U	**132**
MW-117C	06/26/12		0.4 J	25	1 U	17	14	1 U	5 U	23	37	15	1 U	**131**
MW-117C	11/25/12		0.35 J	29	1 U	17	7.4	1 U	5 U	22	36	14	1 U	**126**
MW-117C	05/30/13		1 U	33	1 U	14	12	1 U	5 U	16	27	10	1 U	**112**
MW-117C	11/29/13		1 U	34	1 U	13	4.7	1 U	5 U	23	23	13	1 U	**111**
MW-117C	06/05/14		0.32 J	38	1 U	13	4.6	0.28 J	5 U	24	26	14	1 U	**120**
MW-117C	11/21/14		0.29 J	39	1 U	13	4.5	1 U	5 U	22	25	12	1 U	**116**
MW-117D	04/22/99		0.74	46	2	50	110	2 U	4 U	17	110	38	2 U	**374**
MW-117D	10/18/99		10 U	39	10 U	44	110	10 U	1.5 J	17	97	35	10 U	**344**
MW-117D	02/17/00		0.8 J	34	1.4 J	41	100	5 U	10 U	19	91	35	0.45 J	**323**
MW-117D	04/18/00		0.63 J	29	1.1 J	35	90	5 U	10 JB	17	82	32	0.38 J	**297**
MW-117D	07/24/00		0.85	27	1.2	36	81	5 U	10 U	16	80	35	5 U	**277**
MW-117D	11/07/00		0.6	37	1	33	87	5 U	10 U	16	71	30	5 U	**276**
MW-117D	04/09/01		0.65	29	5 U	37	88	0.39	10 U	13	80	31	5 U	**279**
MW-117D	10/16/01		0.53	23	5 U	25	75	5 U	10 U	17	57	23	5 U	**221**
MW-117D	04/16/02		0.61	21	5 U	24	72	5 U	10 U	18	58	23	5 U	**217**
MW-117D	10/07/02		10 U	36	10 U	180	100	10 U	18	24	87	29	1 U	**474**
MW-117D	04/22/03		0.64 J	29.8 E	0.7 J	43.1 E	95.8 E	1 U	2 U	6.41	78.7 E	32.4 E	1 U	**288**
MW-117D	04/22/03	Dilution	5 U	28.3	5 U	36.7	83.1	5 U	10 U	4.62 J	64.5	26	5 U	**243**
MW-117D	12/22/03		0.61 J	28.1 E	1 U	30.4 E	102 E	1 U	1 U	30.1 E	84.2 E	31.2 E	1 U	**307**
MW-117D	12/22/03	Dilution	5 U	29 D	5 U	32.8 D	110 D	5 U	5 U	29.6 D	85.1 D	31.2 D	5 U	**318**
MW-117D	04/28/04		5 U	28.6	5 U	37.7	105	5 U	10 U	17.4	75.5	33.2	5 U	**297**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-117D	05/21/05		1 U	20	1 U	24	84	1 U	2 U	21	60	24	1 U	**233**
MW-117D	10/19/05		1 U	24	1 U	21	73	1 U	2 U	24	58	22	1 U	**222**
MW-117D	05/06/06		1 U	23	1 U	17	67	1 U	2 U	22	52	20	1 U	**201**
MW-117D	05/06/06	Fld Dupe	1 U	18	1 U	30	52	1 U	2 U	23	70	33	1 U	**226**
MW-117D	11/21/06		1 U	27	1 U	22	76	2.1	2 U	31	89	32	1 U	**279**
MW-117D	10/06/07		0.4	22	0.3	22	71	1	2 U	15	62	29	1 U	**223**
MW-117D	05/17/08		5 U	24	5 U	24	31	5 U	12	30	62	23	5 U	**206**
MW-117D	11/28/08		0.46 J	23.3	1 U	19.5	23.5	0.27 J	1 U	28.6	58	19.4	1 U	**173**
MW-117D	06/09/09		0.49 J	25	1 U	18	13	1 U	1 U	30	55	20	1 U	**161**
MW-117D	11/24/09		0.49 J	29	1 U	19	11	1 U	1 U	28	49	18	1 U	**154**
MW-117D	06/24/10		0.33 J	28	1 U	16	5.3	0.18 J	1 U	29	46	15	1 U	**140**
MW-117D	11/24/10		0.34 J	30	1 U	16	5.6	1 U	1 U	29	45	17	1 U	**143**
MW-117D	05/31/11		1 U	37	1 U	13	5.4	1 U	1 U	26	39	15	1 U	**135**
MW-117D	12/22/11		0.34 J	38	1 U	10	3.8	1 U	5 U	23	31	13	1 U	**119**
MW-117D	06/26/12		0.41 J	43	1 U	11	2.8	1 U	5 U	22	33	12	1 U	**124**
MW-117D	11/25/12		0.32 J	48	1 U	12	3	1 U	5 U	19	34	11	1 U	**127**
MW-117D	05/30/13		0.31 J	52	1 U	11	2.9	1 U	5 U	17	36	10	1 U	**129**
MW-117D	11/29/13		0.33 J	51	1 U	12	2.9	1 U	5 UB	18	33	9.9	1 U	**127**
MW-117D	06/05/14		0.3 J	45	1 U	10	2.6	1 U	5 U	19	34	10	1 U	**121**
MW-117D	11/22/14		0.28 J	48	1 U	12	2.3	1 U	5 U	18	35	10	1 U	**126**
MW-119	10/11/93		12 U	12 U	12 U	12 U	12 U	12 U	25 U	12 U	12 U	12 U		**0**
MW-119	05/03/99		1 U	1 U	1 U	1 U	0.36	1 U	2 U	0.63	1.8	1	5 U	**4**
MW-119	10/27/99		0.25 J	0.35 J	1 U	0.26 J	1.3	1 U	2 U	1.4	2.5	2	1 U	**8**
MW-119	01/26/00		0.19 J	0.21 J	1 U	1 U	1 U	1 U	2 U	0.18 J	0.75 J	0.2 J	1 U	**2**
MW-119	04/17/00		0.16 J	0.23 J	1 U	1 U	1 U	1 U	2 JB	0.19 J	0.79 J	0.2 J	1 U	**4**
MW-119	07/25/00		0.12	0.26	1 U	1 U	1 U	1 U	2 U	0.22	0.88	0.21	1 U	**2**
MW-119	11/08/00		1 U	0.27	1 U	1 U	1 U	1 U	2 U	0.18	0.72	0.18	1 U	**1**
MW-119	04/10/01		1 U	0.26	1 U	1 U	1 U	1 U	2 U	0.17	0.85	0.19	1 U	**1**
MW-119	10/16/01		0.1	0.29	1 U	1 U	1 U	1 U	2 U	0.15	0.71	0.16	1 U	**1**
MW-119	04/30/02		0.1	0.31	1 U	1 U	1 U	1 U	2 U	0.18	0.95	0.17	1 U	**2**
MW-119	10/17/02		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-119	04/22/03		1.07	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1	1 U	1 U	**2**
MW-119	12/30/03		7.22	0.67 J	1 U	0.54 J	0.59 J	1 U	1 U	1 U	0.72 J	1 U	1 U	**10**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-119	04/28/04		1.67	0.51	1 U	1 U	1 U	1 U	2 U	1 U	0.62	1 U	1 U	**3**
MW-119	05/21/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1.3	1 U	1 U	**1**
MW-119	10/20/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1.3	1 U	1 U	**1**
MW-119	05/06/06		1 U	1.2	1 U	1 U	1 U	1 U	2 U	1 U	1.1	1 U	1 U	**2**
MW-119	01/04/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-119	10/08/07		1 U	1	1 U	1 U	0.4	1 U	2 U	1 U	1	1 U	1 U	**2**
MW-119	05/18/08		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1	1 U	1 U	**1**
MW-119	11/29/08		0.3 J	0.98 J	1 U	1 U	0.54 J	1 U	1 U	1 U	1.29	0.27 J	1 U	**3**
MW-119	06/10/09		0.64 J	1	1 U	1 U	0.66 J	1 U	1 U	1 U	1.2	0.29 J	1 U	**4**
MW-119	11/29/09		0.45 J	1.4	1 U	1 U	0.61 J	1 U	1 U	1 U	1.2	1 U	1 U	**4**
MW-119	06/29/10		1 U	0.92 J	1 U	1 U	1.2	1 U	1 U	1 U	1.1	1 U	1 U	**3**
MW-119	11/27/10		0.46 J	1.1	1 U	1 U	1.1	1 U	1 U	1 U	1.7	0.42 J	1 U	**5**
MW-119	06/03/11		0.32 J	0.97 J	1 U	1 U	0.69 J	1 U	1 U	1 U	1.4	0.37 J	1 U	**4**
MW-119	12/29/11		0.29 J	1	1 U	1 U	0.69 J	1 U	5 U	1 U	1	0.34 J	1 U	**3**
MW-119	06/27/12		0.29 J	0.97 J	1 U	1 U	0.88 J	1 U	5 U	1 U	1.1	1 U	1 U	**3**
MW-119	11/25/12		0.13 J	0.99 J	1 U	1 U	0.8 J	1 U	5 U	1 U	1.2	0.32 J	1 U	**3**
MW-119	05/31/13		1 U	1.3	1 U	1 U	0.97 J	1 U	5 U	1 U	1.3	1 U	1 U	**4**
MW-119	12/01/13		1 U	0.93 J	1 U	1 U	0.61 J	1 U	5 U	1 U	0.94 J	0.35 J	1 U	**3**
MW-119	06/14/14		0.25 J	1.6	1 U	1 U	0.57 J	1 U	5 UB	0.16 J	1.4	0.33 J	1 U	**4**
MW-119	11/22/14		0.29 J	1.4	1 U	1 U	0.47 J	1 U	5 U	1 UB	1.6	0.46 J	1 U	**4**
MW-121	10/15/93		2 U	2 U	2 U	2 U	27	2 U	5 U	4	7	82		**120**
MW-121	04/28/99		5 U	3.4	5 U	6	7.2	5 U	10 U	2.7	3.8	26	5 U	**49**
MW-121	10/26/99	Dilution	2 U	3.2 D	0.67 DJ	6.6 D	6.8 D	0.1 DJ	4 U	2.9 D	4.4 D	29 D	2 U	**54**
MW-121	10/26/99		0.67 J	3.8	0.78 J	8	8.4	0.15 J	2 U	3.4	5.5	33 E	1 U	**64**
MW-121	01/31/00		0.65 J	2.9	2 U	5.5	6.3	0.2 J	0.41 J	2.5	3.4	23	2 U	**45**
MW-121	04/18/00		0.55 J	2.8	0.72 J	3	5.6	0.22 J	2 JB	0.64 J	2.8	11	1 U	**29**
MW-121	07/25/00		0.68	3.5	0.82	4.4	6.8	0.39	2 U	1.8	4.3	20	1 U	**43**
MW-121	11/08/00		0.77	4.6	0.89	8	7	0.22	2 U	2.6	5.1	22	1 U	**51**
MW-121	04/10/01		0.78	3.7	0.82	2	6.7	0.68	2 U	2.3	5.5	22	1 U	**44**
MW-121	10/16/01		0.82	3.8	0.81	3.6	6.5	0.42	2 U	2.4	5.9	19	1 U	**43**
MW-121	04/17/02		0.75	3.8	0.07	3	6.1	0.58	2 U	2.6	6.9	20	0.064 J	**44**
MW-121	10/17/02		5 U	5	5 U	42	7	5 U	2 U	3	9	24	1 U	**90**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-121	04/22/03		0.65 J	4.3	0.55 J	7.28	5.74	1 U	2 U	2.85	7.18	22.6	1 U	**51**
MW-121	12/28/03		1 U	4.76	1 U	5.11	4.61	1 U	1 U	2.74	5.79	20.3	0.68 J	**44**
MW-121	04/28/04		0.52	4.37	1 U	4.58	4.79	1 U	2 U	2.43	5.84	18.8	1 U	**41**
MW-121	05/21/05		1 U	2.2	1 U	3.9	5.2	1 U	2 U	1.9	5.1	18	1 U	**36**
MW-121	05/21/05	Fld Dupe	1 U	2.4	1 U	4.8	5.3	1 U	2 U	2.1	6	20	1 U	**41**
MW-121	10/20/05		1 U	2.9	1 U	3.9	5.9	1 U	2 U	2.1	5.7	20	1 U	**41**
MW-121	05/06/06		1 U	2.5	1 U	3.3	5.3	1 U	2 U	2.3	4.8	22	1 U	**40**
MW-121	01/03/07		1 U	1.4	1 U	1.7	3	1 U	2 U	1.9	3.9	20	1 U	**32**
MW-121	10/07/07		0.7	2	1 U	2	6	0.4	2 U	2	5	22	1 U	**40**
MW-121	05/18/08	Dilution	2 U	2 D	2 U	3 D	6 D	2 U	3 DJ	2 D	5 D	25 D	2 U	**46**
MW-121	05/18/08		1 U	2	1 U	2	7	1 U	2 U	2	6	26 E	1 U	**45**
MW-121	11/29/08		0.56 J	1.36	1 U	1 U	3.42	0.55 J	1 U	1.84	2.67	14.4	1 U	**25**
MW-121	06/11/09		0.65 J	1.9	1 U	1 U	4.8	0.76 J	1 U	2.3	4	23	1 U	**37**
MW-121	11/25/09		0.63 J	2.1	1 U	1.8	4.3	1 U	1 U	2	3.1	20	1 U	**34**
MW-121	06/29/10		1 U	2.9	1 U	1.7	3.7	1 U	1 U	1.5	2	16	1 U	**28**
MW-121	11/25/10		0.6 J	4.6	1 U	2.5	4.3	1 U	1 U	2.1	3.4	22	1 U	**40**
MW-121	06/03/11		0.63 J	9.6	1 U	4.1	4.7	0.42 J	1 U	1.8	4.2	19	1 U	**44**
MW-121	12/29/11		0.75 J	15	1 U	6.9	4.9	0.51 J	5 U	1.8	6.6	18	1 U	**54**
MW-121	06/27/12		0.86 J	21	1 U	5.5	5.1	0.62 J	5 U	1.6	10	19	1 U	**64**
MW-121	11/25/12		0.76 J	23	1 U	3	5.3	0.74 J	5 U	1.5	12	18	1 U	**64**
MW-121	05/31/13		0.84 J	29	1 U	9.9	6.2	0.54 J	5 U	1.6	15	22	1 U	**85**
MW-121	12/01/13		0.74 J	29	1 U	6.6	5.9	0.57 J	5 U	1.6	15	22	1 U	**81**
MW-121	06/04/14		0.82 J	37	1 U	13	7.1	0.71 J	5 U	1.9	22	26	1 U	**109**
MW-121	11/23/14		0.84 J	42	1 U	8.7	6.4	0.92 J	5 U	1.6	20	25	1 U	**105**
MW-124	10/18/93		120 U	150	120 U	410	210		120 U	50	1400	140		**2360**
MW-124	04/28/99		10 U	75	10 U	97	1200	10 U	20 U	47	540	36	3.4 J	**1998**
MW-124	04/28/99	Fld Dupe	10 U	75	10 U	97	1100 D	10 U	20 JBU	47	540 D	36	3.4 J	**1898**
MW-124	10/27/99		50 U	50	50 U	41 J	560	50 U	8.2 J	28 J	280	28 J	6.9 J	**1002**
MW-124	01/31/00		25 U	95	25 U	36	540	25 U	50 U	12 J	190	20 J	44	**937**
MW-124	04/24/00		0.72 J	92	25 U	24 J	440	3.9 J	50 JB	3.8 J	100	14 J	63	**791**
MW-124	07/25/00		20 U	89	20 U	20	330	20 U	40 U	20 U	79	10	60	**588**
MW-124	11/13/00		20 U	110	20 U	20	300	20 U	40 U	2.7	75	12	63	**583**
MW-124	04/12/01		20 U	47	20 U	35	240	2.1	40 U	30	230	24	13 J	**621**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-124	10/29/01		10 U	98	10 U	19	190	1.4	20 U	6.2	110	16	76	**517**
MW-124	04/17/02		20 U	64	20 U	35	370	12	40 U	30	210	26	16 J	**763**
MW-124	04/17/02	Fld Dupe	20 U	65	20 U	41	370	5.7 J	40 U	30	200	20 U	18 J	**730**
MW-124	10/17/02		20 U	92	20 U	230	360	20 U	40 U	35	290	33	21	**1061**
MW-124	04/25/03		1 U	83.4 E	1.32	30 E	226 E	8.35	2 U	13.8	136 E	20.9	62.7 E	**582**
MW-124	04/25/03	Dilution	10 U	71.4	10 U	26.4	213	10 U	20 U	13.5	119	18.9	39.2	**501**
MW-124	12/28/03		1 U	109 E	1.34	22.8	174 E	6.96	1 U	11.2	116 E	19.2	67.2 E	**528**
MW-124	12/28/03	Dilution	10 U	83.2 D	10 U	20.1 D	176 D	10 U	10 U	10.6 D	94.7 D	15.6 D	40 D	**440**
MW-124	04/28/04		40 U	197	40 U	43.6	389	40 U	80 U	34.6	185	26.7	24 J	**900**
MW-124	05/21/05		5 U	340	5 U	37	420	5 U	10 U	8.4	120	18	110	**1053**
MW-124	10/20/05		1 U	250	1 U	25	260	1.5	2 U	6.6	76	15	75 H	**709**
MW-124	05/06/06		1 U	320	1.2	29	370	1.5	2 U	15	120	18	61	**936**
MW-124	01/04/07		10 U	370	10 U	15	250	10 U	20 U	10 U	110	10	10 U	**755**
MW-124	10/07/07		1 U	620	0.7	28	300	4	2 U	8	100	12	120	**1193**
MW-124	05/18/08		40 U	870	40 U	42	320	40 U	80 U	40 U	190	40 U	64	**1486**
MW-124	11/29/08	Dilution	5 U	415	5 U	16.1	144	1.4 J	1.45 J	11.8	90	10.4	32.1	**722**
MW-124	06/10/09	Dilution	1 J	500	5 U	18	150	5 U	5 U	14	100	10	23	**816**
MW-124	11/29/09	Dilution	5 U	510	5 U	22	170	5 U	5 U	16	98	9.4	21	**846**
MW-124	06/29/10	Dilution	5 U	500	5 U	20	220	5 U	1.9 J	14	82	8.6	30	**877**
MW-124	11/27/10	Dilution	5 U	490	5 U	25	280	5 U	5 U	14	95	9.2	30	**943**
MW-124	06/03/11	Dilution	5 U	450	5 U	28	240	5 U	2.4 J	13	120	7.4	23	**884**
MW-124	12/29/11	Dilution	5 U	370	5 U	20	130	5 U	25 U	12	96	5.9	17	**651**
MW-124	06/27/12	Dilution	5 U	420	5 U	17	100	5 U	25 U	9.5	90	5.2	23	**665**
MW-124	11/25/12	Dilution	2 U	330	2 U	9.6	70	0.9 J	1 J	5.2	50	4.3	30	**501**
MW-124	06/04/13	Dilution	2.5 U	350	2.5 U	13	92	2.5 U	5.8 J	10	84	4.9	14	**574**
MW-124	12/01/13	Dilution	2.5 U	280	2.5 U	8.6	82	2.5 U	12 UB	7.4	40	4.1	20	**442**
MW-124	06/14/14	Dilution	2.5 U	480	2.5 U	9.2	120	0.9 J	12 UB	7.8	49	4.3	41	**712**
MW-124	11/23/14	Dilution	2.5 U	420	2.5 U	10	130	1.2 J	12 UB	7.8	41	4.9	31	**646**
MW-130	10/19/93		67 U	26	67 U	10	25		8	67 U	1000	28		**1097**
MW-130	04/28/99		0.19	19	1 U	11	24	1 U	2 U	5.3	670	17	1 U	**746**
MW-130	04/28/99	Fld Dupe	0.17 J	18	1 U	10	23 DJ	1 U	2 U	5.3	670 D	17	1 U	**743**
MW-130	10/28/99		25 U	10 J	25 U	4.9 J	7.8 J	25 U	50 U	25 U	370	8.2 J	25 U	**401**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-130	02/16/00		25 U	11 J	25 U	3.6 J	7.5 J	25 U	50 U	25 U	460	8.5 J	25 U	**491**
MW-130	04/24/00		50 JB	12 J	50 U	3.1 J	7.7 J	50 U	100 JB	50 U	510	8.3 J	50 U	**691**
MW-130	07/27/00		20 U	13	20 U	3.3	7.7	20 U	40 U	20 U	670	8.5	20 U	**703**
MW-130	11/14/00		25 U	12	25 U	4.3	7.2	25 U	50 U	25 U	390	7	25 U	**421**
MW-130	04/12/01		20 U	10	20 U	20 U	5.7	20 U	40 U	20 U	440	6.2	20 U	**462**
MW-130	10/30/01	Fld Dupe	50 U	15 J	50 U	50 U	6.5 J	50 U	100 U	50 U	610	8.1 J	50 U	**640**
MW-130	10/30/01		50 U	14	50	50 U	50 U	50 U	100 U	50 U	660	50 U	50 U	**724**
MW-130	04/30/02		25 U	11	25 U	1.6	5.7	25 U	50 U	0.97	360	5.4	25 U	**385**
MW-130	10/17/02		50 U	50 U	50 U	54	50 U	50 U	43	50 U	840	50 U	1 U	**937**
MW-130	04/25/03		0.1 J	13	1 U	5.33	7.5	0.48 J	2 U	1.37	424 E	5.94	1 U	**458**
MW-130	04/25/03	Dilution	20 U	11.6 J	20 U	20 U	20 U	20 U	40 U	20 U	322	20 U	20 U	**334**
MW-130	04/25/03	Fld Dupe	20 U	11.3 J	1 U	20 U	7.84	0.43 J	40 U	1.37	341	6.15	20 U	**368**
MW-130	12/28/03	Dilution	20 U	10.3 JD	20 U	20 U	20 U	20 U	20 U	20 U	263 D	20 U	20 U	**273**
MW-130	12/28/03		1 U	12.1	1 U	5.65	8.09	1 U	1 U	1.11	320 E	5.46	1 U	**352**
MW-130	04/28/04		10 U	11	10 U	10 U	10.6	10 U	20 U	10 U	157	10 U	10 U	**179**
MW-130	05/21/05		1 U	14	1 U	4	11	1 U	2 U	1 U	210	3.5	1 U	**243**
MW-130	10/20/05		1 U	16	1 U	4.2	14	1 U	2 U	1 U	210	3.6	1 U	**248**
MW-130	05/08/06		1 U	16	1 U	4.1	14	1 U	2 U	1 U	140	3.6	1 U	**178**
MW-130	01/04/07		1 U	20	1 U	4.6	18	1 U	2 U	1 U	160	4.3	1 U	**207**
MW-130	10/07/07		1 U	17	1 U	5	21	0.6	2 U	0.6	170	4	1 U	**218**
MW-130	05/17/08		10 U	22	10 U	10 U	25	10 U	20 U	10 U	200	10 U	10 U	**247**
MW-130	11/29/08	Dilution	2 U	21.9	2 U	4.18	21	0.4 J	0.56 J	0.56 J	198	4.26	2 U	**251**
MW-130	06/11/09	Dilution	0.48 J	26	2 U	4.3	20	2 U	2 U	0.9 J	300	4.3	2 U	**356**
MW-130	11/29/09	Dilution	2 U	31	2 U	5.5	12	2 U	2 U	2 U	320	3.3	2 U	**372**
MW-130	06/29/10	Dilution	10 U	70	10 U	15	17	10 U	2.9 J	10 U	1100	7.6 J	10 U	**1213**
MW-130	11/27/10	Dilution	5 U	29	5 U	8.4	8.3	5 U	5 U	5 U	430	3.6 J	5 U	**479**
MW-130	06/03/11	Dilution	2.5 U	20	2.5 U	5.4	6.5	2.5 U	1 J	2.5 U	250	3.8	2.5 U	**287**
MW-130	12/28/11		1 U	9.7	1 U	2.7	4.1	1 U	5 U	0.68 J	100	2.7	1 U	**120**
MW-130	06/25/12		0.26 J	7.7	1 U	1.9	3	1 U	5 U	0.65 J	68	2.1	1 U	**84**
MW-130	11/24/12		1 U	7.5	1 U	1.7	2.5	1 U	5 U	0.64 J	47	1.9	1 U	**61**
MW-130	06/07/13		1 U	7.6	1 U	1.5	2.2	1 U	5 U	0.7 J	32	1.8	1 U	**46**
MW-130	12/01/13		1 U	8.4	1 U	1.2	2.2	1 U	5 U	0.65 J	16	1.6	1 U	**30**
MW-130	06/14/14		1 U	12	1 U	1.4	2.5	0.29 J	5 UB	0.49 J	13	1.7	1 U	**31**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-130	11/23/14		0.34 J	12	1 U	1.5	2.5	1 U	5 U	1 UB	9.3	1.8	1 U	**27**
MW-133A	10/20/93		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	0.8	1 U		**1**
MW-133A	04/26/99		1 U	1 U	1 U	1 U	0.27	1 U	2 U	0.37	0.95	1.1	1 U	**3**
MW-133A	10/26/99		0.03 J	0.52 J	1 U	0.66 J	1.8	1 U	2 U	1	4.6	4.8	1 U	**13**
MW-133A	02/15/00		1 U	0.08 J	1 U	1 U	0.16 J	1 U	2 U	1 U	0.38 J	1 U	1 U	**1**
MW-133A	04/25/00		1 U	1 U	1 U	1 U	1 U	1 U	2 JB	1 U	0.35 J	1 U	1 U	**2**
MW-133A	07/27/00		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	10 U	**0**
MW-133A	11/16/00		1 U	1 U	1 U	1 U	0.49	1 U	2 U	1 U	0.81	0.11	1 U	**1**
MW-133A	04/10/01		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-133A	10/31/01		1 U	0.41	1 U	0.1	1.2	1 U	2 U	1 U	1	0.19	1 U	**3**
MW-133A	04/29/02		1 U	1 U	1 U	1 U	0.04	1 U	2 U	1 U	0.06	1 U	1 U	**0**
MW-133A	10/16/02		1 U	1	1 U	1 U	4	1 U	0.6	1 U	3	1 U	1 U	**9**
MW-133A	04/25/03		1 U	2.96	1 U	1.05	11.7	1 U	2 U	1 U	5.2	0.98 J	1 U	**22**
MW-133A	12/30/03		1 U	1.92	1 U	0.53 J	6.34	1 U	1 U	1 U	2.51	1 U	1 U	**11**
MW-133A	04/28/04		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-133A	05/02/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-133A	11/02/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-133A	06/22/06		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-133A	11/16/06		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-133A	10/07/07		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**0**
MW-133A	05/17/08		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-133A	11/26/08		1 U	1 U	1 U	1 U	0.26 J	1 U	1 U	1 U	0.32 J	1 U	1 U	**1**
MW-133A	06/20/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**0**
MW-133A	06/20/09	Fld Dupe	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**0**
MW-133A	11/28/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**0**
MW-133A	06/25/10		1 U	1 U	1 U	1 U	0.23 J	1 U	1 U	1 U	0.26 J	1 U	1 U	**0**
MW-133A	11/27/10		1 U	0.21 J	1 U	1 U	0.91 J	1 U	1 U	1 U	0.86 J	1 U	1 U	**2**
MW-133A	11/27/10	Fld Dupe	1 U	1 U	1 U	1 U	0.79 J	1 U	1 U	1 U	0.82 J	1 U	1 U	**2**
MW-133A	06/02/11		1 U	1 U	1 U	1 U	1 U	1 U	0.28 J	1 U	1 U	1 U	1 U	**0**
MW-133A	12/28/11		1 U	1 U	1 U	1 U	0.67 J	1 U	5 U	1 U	0.67 J	1 U	1 U	**1**
MW-133A	06/28/12		1 U	1 U	1 U	1 U	0.4 J	1 U	5 U	1 U	0.3 J	1 U	1 U	**1**
MW-133A	06/07/13		1 U	0.44 J	1 U	1 U	1 U	1 U	5 U	1 U	0.33 J	1 U	1 U	**1**
MW-133A	11/30/13		1 U	1 U	1 U	1 U	0.27 J	1 U	5 UB	1 U	0.39 J	1 U	1 U	**1**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-133A	06/13/14		1 U	1 U	1 U	1 U	1 U	1 U	5 UB	1 U	1 U	1 U	1 U	**0**
MW-133A	11/24/14		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	**0**
MW-133B	10/20/93		100 U	270	100 U	130	810		100 U	160	1200	380		**2950**
MW-133B	04/26/99		10	200	4.6	110	780	7	4 U	110	840	270	2 U	**2332**
MW-133B	10/26/99		7.9 J	170	50 U	67	810	7.1 J	6.8 J	77	630	190	50 U	**1966**
MW-133B	02/15/00		9.3 J	180	50 U	100	840	50 U	100 U	120	730	250	50 U	**2229**
MW-133B	04/25/00		12 J	170	50 U	78	600	50 U	100 JB	76	620	190	50 U	**1846**
MW-133B	07/27/00		12	160	4.1	88	670	10	40 U	94	760	220	20 U	**2018**
MW-133B	11/16/00		11	200	25 U	88	530	9.5	50 U	94	570	230	25 U	**1733**
MW-133B	04/10/01		13	200	50 U	46	660	43	100 U	140	830	300	50 U	**2232**
MW-133B	10/31/01		12	180	50 U	7	510	49	100 U	110	700	250	50 U	**1818**
MW-133B	04/29/02		9.1	150	3.7	25 U	460	54	50 U	99	570	170	25 U	**1516**
MW-133B	10/16/02		50 U	250	50 U	650	820	50 U	31	140	800	290	1 U	**2981**
MW-133B	04/25/03		10.7	183 E	3.97	110 E	728 E	24.5	2 U	151 E	699 E	325 E	1 U	**2235**
MW-133B	04/25/03	Dilution	40 U	158	40 U	40.4	571	41.4	80 U	112	617	237	40 U	**1777**
MW-133B	12/30/03		9.91	162 E	1 U	93 E	562 E	16.3	1 U	122 E	510 E	250 E	1 U	**1725**
MW-133B	12/30/03	Dilution	50 U	151 D	50 U	81.6 D	623 D	50 U	50 U	109 D	577 D	240 D	50 U	**1782**
MW-133B	04/28/04		10 U	161	10 U	106	803	10 U	20 U	111	622	216	100 U	**2019**
MW-133B	05/02/05		5.6	120	5 U	70	630	17	10 U	81	460	160	5 U	**1544**
MW-133B	05/02/05	Fld Dupe	5.7	120	5 U	74	580	13	10 U	87	420	150	5 U	**1450**
MW-133B	11/02/05		8.2	180	5 U	98	930	28	10 U	110	620	220	5 U	**2194**
MW-133B	06/22/06		10 U	110	10 U	54	720	11	20 U	68	430	120	10 U	**1513**
MW-133B	06/22/06	Fld Dupe	10 U	120	10 U	53	710	17	20 U	80	450	140	10 U	**1570**
MW-133B	11/16/06		10 U	160	10 U	10 U	740	78	50 U	85	10 U	170	10 U	**1233**
MW-133B	10/07/07		6	160	3	84	930	38	2 U	110	600	200	1 U	**2131**
MW-133B	05/17/08		40 U	130	40 U	60	900	40 U	80 U	59	440	110	40 U	**1699**
MW-133B	11/26/08		8 J	308	5.4 J	12	1860	193	3.2 J	126	955	208	10 U	**3679**
MW-133B	06/20/09	Dilution	7.3 J	230	4.3 J	19	1400	140	10 U	110	710	170	10 U	**2791**
MW-133B	11/28/09	Dilution	7.8 J	280	20 U	100	2000	84	20 U	110	820	190	20 U	**3592**
MW-133B	06/25/10	Dilution	5.4 J	230	4 J	81	1700	47	20 U	96	680	150	20 U	**2993**
MW-133B	11/27/10	Dilution	20 U	240	20 U	120	1900	11 J	20 U	110	790	180	20 U	**3351**
MW-133B	06/02/11	Dilution	3.8 J	150	2.9 J	56	1200	29	11	70	420	120	10 U	**2063**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-133B	12/28/11	Dilution	4.9 J	180	3.9 J	5.3 J	1100	100	50 U	73	470	100	10 U	**2037**
MW-133B	06/28/12	Dilution	5.2 J	180	10 U	25	1200	60	11 J	65	470	92	10 U	**2108**
MW-133B	11/24/12	Dilution	6 J	160	3.3 J	49	1300	49	50 U	64	420	96	10 U	**2147**
MW-133B	06/07/13	Dilution	2.8 J	130	5 U	45	530	19	4.8 J	61	390	68	5 U	**1251**
MW-133B	11/30/13	Dilution	4 J	190	2.3 J	86	960	21	25 UB	74	490	98	5 U	**1925**
MW-133B	06/13/14	Dilution	4 J	160	1.3 J	58	430	20	25 UB	72	410	74	5 U	**1229**
MW-133B	11/24/14	Dilution	4.4 J	170	5 U	48	160	12	25 U	78	480	68	5 U	**1020**
MW-133C	10/20/93		20 U	76	20 U	75	120		20 U	44	340	170		**825**
MW-133C	04/26/99		8.5	57	2.8	47	100	5 U	10 U	28	200	110	5 U	**553**
MW-133C	10/26/99		7.2 J	49	10 U	40	91	1.1 J	20 U	22	170	93	10 U	**473**
MW-133C	02/15/00		5.4	31	2.3 J	23	32	0.42 J	10 U	2.5 J	110	55	5 U	**262**
MW-133C	04/25/00		4.7 JB	28	10 U	21	28	0.34 J	20 JB	1.2 J	100	48	10 U	**251**
MW-133C	07/27/00		4.9	28	2.2	18	30	5 U	10 U	0.82	91	34	5 U	**209**
MW-133C	07/27/00	Fld Dupe	5.4	31	2.4 J	21	32	0.55 J	10 U	1 J	100	44	5 U	**237**
MW-133C	11/16/00		5.2	35	2.2	22	31	5 U	10 U	1.2	95	47	5 U	**239**
MW-133C	04/10/01		6.2	36	10 U	28	36	10 U	20 U	1.6	130	62	10 U	**300**
MW-133C	10/31/01		5.1	31	5 U	14	31	5 U	10 U	5 U	100	31	5 U	**212**
MW-133C	10/31/01	Fld Dupe	5.3	32	2 J	18	33	5 U	10 U	5 U	100	40	5 U	**230**
MW-133C	04/29/02		5.4	33	1.8	26	45	0.73	0.49	4.5	120	58	5 U	**295**
MW-133C	10/16/02		6	49	10 U	150	51	10 U	6	10 U	140	66	1 U	**468**
MW-133C	10/16/02	Fld Dupe	7	49 D	2 U	180 D	53 D	5	0.9 J	2	150 D	74 D	1 U	**521**
MW-133C	04/25/03		5.34	33.5 E	1.86	29.9 E	42.1 E	1.04	2 U	2.41	137 E	72.2 E	1 U	**325**
MW-133C	04/25/03	Dilution	5.04 J	31.6	10 U	26.5	39.2	10 U	20 U	10 U	113	60.7	10 U	**276**
MW-133C	12/30/03	Dilution	5.64 JD	143 D	10 U	32.5 D	49.5 D	10 U	10 U	10 U	136 D	74.4 D	10 U	**441**
MW-133C	12/30/03		6.43	40.7 E	2.01	36.8 E	55.5 E	0.8 J	1 U	3.02	166 E	83 E	1 U	**394**
MW-133C	04/28/04		5.42	34.7	10 U	29.2	47.2	10 U	20 U	10 U	124	63.7	10 U	**304**
MW-133C	05/02/05		5.7	37	1.8	31	53	0.59	2 U	2.6	130	63	1 U	**325**
MW-133C	11/02/05		6.5	46	5 U	43	70	5 U	10 U	5 U	150	75	5 U	**391**
MW-133C	06/22/06		7.3	44	1 U	42	71	1.3	2 U	4.3	150	78	1 U	**398**
MW-133C	11/16/06		7.7	61	1.9	23	86	3.5	2 U	5.1	220	110	1 U	**518**
MW-133C	10/07/07		7	50	2	51	88	2	2 U	5	170	88	1 U	**463**
MW-133C	05/17/08		8 U	60	8 U	62	120	8 U	16 U	8 U	200 E	100	8 U	**542**
MW-133C	05/17/08	Fld Dupe	7	55 E	2	65 D	110 E	20 U	20 DJ	6	200 D	100 E	20 U	**565**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-133C	05/17/08	Dilution	10 U	57 D	10 U	58 D	110 D	10 U	20 U	10 U	180 D	94 D	10 U	**499**
MW-133C	11/26/08		7.82	53.6	1.92	24.6	96.9	6.93	0.23 J	6.06	182	94.8	1 U	**475**
MW-133C	06/20/09		7.4	59	2	36	110	9.7	1 U	6	190	100	1 U	**520**
MW-133C	11/28/09		7.1	58	1.8	53	110	1.2	1 U	6.2	170	94	1 U	**501**
MW-133C	06/25/10		6.9	54	1.8	50	130	1.3	1 U	8.6	180	89	1 U	**522**
MW-133C	11/27/10		6.1	47	1.8	46	130	0.3 J	1 U	10	180	94	1 U	**515**
MW-133C	06/02/11		6.3	56	1.8	51	180	1.5	0.47 J	16	160	95	1 U	**568**
MW-133C	12/28/11		5.8	50	1.8	41	130	2	5 U	9.7	140	76	1 U	**456**
MW-133C	06/28/12		5.7	51	1.6	40	130	1.7	5 U	6.6	150	81	1 U	**468**
MW-133C	11/24/12		5.3	49	1.6	41	130	1.5	5 U	6.6	140	75	1 U	**450**
MW-133C	06/07/13		5.3	52	1.3	47	130	1.6	5 U	7.5	160	77	1 U	**482**
MW-133C	11/30/13		5.2	52	1.3	46	140	1.4	5 UB	7.5	160	83	1 U	**496**
MW-133C	06/13/14		6.8	68	1.6	53	160	2.1	5 UB	8.5	190	88	1 U	**578**
MW-133C	11/24/14		5.8	58	1.3	47	130	2.2	5 U	6.6	150	83	1 U	**484**
MW-136	10/19/93		5 U	5 U	5 U	5 U	5 U	5 U	10 U	5 U	5 U	5 U		**0**
MW-136	04/29/99		0.37	0.35	1 U	0.88	3.5	1 U	2 U	1.7	8	3.8	1 U	**19**
MW-136	10/28/99		1.5	0.34 J	1 U	0.37 J	1.1	0.03 J	2 U	1.4	16	2.4	1 U	**23**
MW-136	02/15/00		0.74 J	1 U	1 U	1 U	1 U	1 U	2 U	1 U	0.28 J	1 U	1 U	**1**
MW-136	04/25/00		0.57 JB	1 U	1 U	1 U	1 U	1 U	2 JB	1 U	0.31 J	1 U	1 U	**3**
MW-136	07/27/00		0.48	1 U	1 U	1 U	1 U	1 U	2 U	1 U	0.3	1 U	1 U	**1**
MW-136	11/17/00		0.5	1 U	1 U	1 U	1 U	1 U	2 U	1 U	0.29	1 U	1 U	**1**
MW-136	04/10/01		0.45	1 U	1 U	1 U	1 U	1 U	2 U	1 U	0.3	1 U	1 U	**1**
MW-136	10/31/01		0.45	1 U	1 U	1 U	1 U	1 U	2 U	1 U	0.3	1 U	1 U	**1**
MW-136	04/29/02		0.45	1 U	1 U	1 U	1 U	1 U	2 U	0.53	0.3	1 U	1 U	**1**
MW-136	10/18/02		0.6	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**1**
MW-136	04/23/03		0.8 J	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**1**
MW-136	04/28/04		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-136	06/23/06		1.1	1 U	1 U	1 U	1 U	1 U	1.8	1 U	1 U	1 U	1 U	**3**
MW-136	01/05/07		2.5	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**3**
MW-136	10/07/07		1 U	1 U	1 U	1 U	1 U	1 U	0.7	1 U	1 U	1 U	1 U	**1**
MW-136	05/18/08		2	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**2**
MW-136	11/29/08		4.5	1 U	1 U	1 U	0.2 J	1 U	1 U	1 U	1 U	1 U	1 U	**5**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-136	06/11/09		3.1	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	3
MW-136	11/28/09		1.5	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	2
MW-136	06/29/10		0.84 J	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1
MW-136	11/28/10		0.82 J	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1
MW-136	06/01/11		1	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1
MW-136	12/29/11		0.79 J	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	1
MW-136	06/25/12		0.62 J	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	1
MW-136	11/24/12		0.5 J	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	1
MW-136	06/04/13		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-136	11/30/13		0.38 J	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	0
MW-136	06/13/14		0.38 J	1 U	1 U	1 U	1 U	1 U	5 UB	1 U	0.23 J	1 U	1 U	1
MW-136	11/23/14		0.58 J	1 U	1 U	1 U	1 U	1 U	5 UB	1 U	1 U	1 U	1 U	1
MW-200	04/26/99		1 U	1 U	1 U	0.34	0.66	1 U	2 U	0.61	2.2	2.2	1 U	6
MW-200	10/27/99		1 U	1 U	1 U	0.26 J	1.2	1 U	2 U	1.1	1.9	1.8	1 U	6
MW-200	02/15/00		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-200	04/25/00		1 U	1 U	1 U	1 U	1 U	1 U	2 JB	1 U	0.07 J	1 U	1 U	2
MW-200	07/27/00		1 U	1 U	1 U	1 U	0.1	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-200	11/14/00		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-200	04/10/01		1 U	1 U	1 U	1 U	0.17	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-200	10/29/01		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	0.12	1 U	0
MW-200	04/22/02		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-200	10/18/02		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-200	04/25/03		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-200	12/30/03		1 U	1 U	1 U	0.89 J	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1
MW-200	04/28/04		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-200	04/28/04	Fld Dupe	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	0
MW-200	05/21/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1.9	1 U	1 U	2
MW-200	01/12/06		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-200	05/08/06		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-200	01/04/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-200	10/08/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-200	05/18/08		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	0
MW-200	11/29/08		1 U	1 U	1 U	1 U	0.69 J	1 U	1 U	1 U	0.21 J	0.17 J	1 U	1

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-200	06/11/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**0**
MW-200	11/28/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**0**
MW-200	06/29/10		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**0**
MW-200	11/28/10		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**0**
MW-200	05/31/11		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	1 U	**0**
MW-200	12/29/11		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	**0**
MW-200	06/25/12		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	**0**
MW-200	11/24/12		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	**0**
MW-200	06/04/13		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	**0**
MW-200	12/01/13		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	**0**
MW-200	06/14/14		1 U	1 U	1 U	1 U	1 U	1 U	5 UB	1 U	1 U	1 U	1 U	**0**
MW-200	11/23/14		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1 U	1 U	1 U	1 U	**0**
MW-201	02/16/00		5 U	48	5 U	1.1 J	85	5 U	10 U	5 U	4.5 J	8.3	5.6	**153**
MW-201	04/18/00		10 U	120	10 U	1.9 J	87	0.78 J	20 JB	10 U	4.9 J	15	7.2 J	**257**
MW-201	04/18/00	Fld Dupe	0.29 J	130	10 U	2.3 J	93	0.74 J	20 JB	10 U	5.8 J	12	5.8 J	**270**
MW-201	07/25/00		20 U	330	20 U	6.8	220	20 U	40 U	20 U	110	4.5	22	**693**
MW-201	11/13/00		20 U	340	20 U	5.2	180	20 U	40 U	20 U	39	4.9	7.1 J	**576**
MW-201	04/12/01		5 U	43	5 U	1.6	60	0.64	10 U	5 U	12	19	5.8	**142**
MW-201	04/12/01	Fld Dupe	5 U	43	5 U	1.6 J	60	0.64 J	10 U	5 U	12	18	5.5	**141**
MW-201	10/29/01		10 U	150	10 U	3.6	120	10 U	20 U	10 U	55	25	4.8 J	**358**
MW-201	04/30/02		5	5500	250 U	130	2600	250 U	500 U	250 U	1700	13	50 J	**9998**
MW-201	10/03/02		500 U	7100	500 U	480	2200	500 U	1000 U	500 U	970	500 U	28 E	**0778**
MW-201	10/03/02	Fld Dupe	1 U	7700	1 U	420 J	2200	7	2 U	1 U	1000	26 E	50 E	**1403**
MW-201	04/25/03		0.05 J	1410 E	1 U	52.8 E	989 E	20.3	2 U	0.29 J	452 E	28.9 E	108 E	**3061**
MW-201	04/25/03	Dilution	500 U	6350	500 U	500 U	863	500 U	1000 U	500 U	294 J	500 U	500 U	**7507**
MW-201	12/30/03		1 U	1580 E	1 U	15	123 E	1 U	1 U	1 U	175 E	2.99	39.4 E	**1935**
MW-201	12/30/03	Dilution	400 U	6480 D	400 U	400 U	400 U	400 U	400 U	400 U	400 U	400 U	400 U	**6480**
MW-201	12/30/03	Fld Dupe	1 U	6030 D	400 U	400 U	90.9 E	400 U	400 U	400 U	400 U	400 U	38.7 E	**6160**
MW-201	04/28/04		500 U	4150	500 U	500 U	500 U	500 U	1000 U	500 U	500 U	500 U	500 U	**4150**
MW-201	05/21/05		25 U	3500	25 U	25 U	58	25 U	50 U	25 U	26	25 U	25 U	**3584**
MW-201	01/12/06		1 U	230	1 U	1.2	23	1 U	2 U	1 U	8.8	14	1 U	**277**
MW-201	06/28/06		10 U	550	10 U	10 U	16	10 U	20 U	10 U	32	14	10 U	**612**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-201	01/05/07		1 U	80	1 U	1 U	5.1	1 U	2 U	1 U	20	2.8	1 U	**108**
MW-201	10/08/07		1 U	20	1 U	2	2	1 U	2 U	6	7	9	1	**47**
MW-201	05/18/08		1 U	64 E	1 U	2	11	1 U	2 U	1 U	7	10	8	**102**
MW-201	05/18/08	Dilution	4 U	55 D	4 U	4 U	9 D	4 U	8 U	4 U	6 D	9 D	6 D	**85**
MW-201	11/29/08	Dilution	2 J	1460	10 U	10 U	7.1 J	10 U	4.4 J	10 U	14.2	7.7 J	6.2 J	**1502**
MW-201	11/29/08	Fld Dupe	10 U	1580	10 U	10 U	5.5 J	10 U	3.1 J	10 U	12.5	7.1 J	5.6 J	**1614**
MW-201	06/10/09	Dilution	2 J	1200	10 U	10 U	16	10 U	10 U	10 U	10	7.7 J	10 U	**1236**
MW-201	06/10/09	Fld Dupe	10 U	1200	10 U	10 U	9.8 J	10 U	10 U	10 U	7.4 J	5.7 J	10 U	**1223**
MW-201	11/29/09	Dilution	10 U	480	10 U	10 U	6.4 J	10 U	10 U	10 U	37	10 U	10	**533**
MW-201	11/29/09	Fld Dupe	10 U	500	10 U	10 U	5.7 J	10 U	10 U	10 U	36	10 U	9.3 J	**551**
MW-201	06/29/10		1 U	12	1 U	1 U	5	1 U	1 U	0.53 J	4.4	1.1	0.91 J	**24**
MW-201	11/28/10		1 U	2.7	1 U	0.43 J	0.75 J	1 U	1 U	0.93 J	3.4	1.2	1 U	**9**
MW-201	06/03/11		1 U	2.2	1 U	1 U	0.69 J	1 U	1 U	1.3	3.4	0.85 J	1 U	**8**
MW-201	06/03/11	Fld Dupe	1 U	2.2	1 U	1 U	0.63 J	1 U	0.26 J	1.2	3.4	0.87 J	1 U	**9**
MW-201	12/29/11		1 U	3.7	1 U	1 U	3.3	1 U	5 U	1.7	2.4	0.73 J	1 U	**12**
MW-201	12/29/11	Fld Dupe	1 U	3.6	1 U	1 U	3.3	1 U	5 U	1.8	2.4	0.77 J	1 U	**12**
MW-201	06/27/12		1 U	8	1 U	1 U	0.75 J	1 U	5 U	1.9	5.8	0.44 J	1 U	**17**
MW-201	11/25/12		1 U	5	1 U	1 U	1	1 U	5 U	0.85 J	15	0.31 J	1 U	**22**
MW-201	06/05/13		1 U	1.5	1 U	1 U	0.42 J	1 U	5 U	0.73 J	5.6	0.36 J	1 U	**9**
MW-201	12/01/13		1 U	4.8	1 U	0.56 J	1.7	1 U	5 U	2.9	16	1.8	1 U	**28**
MW-201	06/14/14		1 U	2.9	1 U	1 U	0.62 J	1 U	5 UB	1.1	4	0.34 J	1 U	**9**
MW-201	11/23/14		1 U	6.5	1 U	0.83 J	3.2	1 U	5 U	1.7	18	1.4	1 U	**32**
MW-201	11/23/14	Fld Dupe	1 U	6.1	1 U	0.82 J	2.8	1 U	5 U	1.5	18	1.2	1 U	**30**
MW-202	05/20/99		1 U	1 U	1 U	1 U	0.81	1 U	2 U	4.6	2	2.1	1 U	**10**
MW-202	10/28/99		1 U	1 U	1 U	0.18 J	0.68 J	1 U	2 U	5	2.2	2.1	1 U	**10**
MW-202	02/16/00		1 U	1 U	1 U	1 U	1 U	1 U	2 U	3.6	0.77 J	0.5 J	1 U	**5**
MW-202	04/18/00		0.25 J	1 U	1 U	1 U	1 U	1 U	2 JB	3.1	0.65 J	0.55 J	1 U	**7**
MW-202	07/27/00		0.48	1 U	1 U	1 U	1 U	1 U	2 U	3.5	0.72	0.75	1 U	**5**
MW-202	11/13/00		1 U	1 U	1 U	1 U	1 U	1 U	2 U	14	0.11	0.19	1 U	**14**
MW-202	04/12/01		1 U	1 U	1 U	1 U	1 U	1 U	2 U	13	0.08	0.11	1 U	**13**
MW-202	10/29/01		1 U	1 U	1 U	1 U	1 U	1 U	2 U	12	0.06	1 U	1 U	**12**
MW-202	04/30/02		1 U	1 U	1 U	1 U	1 U	1 U	2 U	10	1 U	0.12	1 U	**10**
MW-202	10/17/02		1 U	1 U	1 U	1 U	1 U	1 U	0.5	12	1 U	1 U	1 U	**13**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-202	04/24/03		1 U	1 U	1 U	1 U	1 U	1 U	2 U	2.82	1 U	0.8 J	1 U	**4**
MW-202	12/30/03		1 U	1 U	1 U	0.54 J	1 U	1 U	1 U	2.78	1 U	1.11	1 U	**4**
MW-202	04/28/04		1 U	1 U	1 U	1 U	1 U	1 U	2 U	2.3	1 U	0.68	1 U	**3**
MW-202	05/21/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1.8	1 U	1 U	1 U	**2**
MW-202	10/21/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-202	06/28/06		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1.5	1 U	1 U	1 U	**2**
MW-202	01/05/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	14	1 U	1 U	1 U	**14**
MW-202	10/08/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1	1	0.3	1 U	**2**
MW-202	05/19/08		1 U	1 U	1 U	1 U	1 U	1 U	2 U	4	1 U	1 U	1 U	**4**
MW-202	11/29/08		0.3 J	0.95 J	1 U	1 U	1 U	1 U	1 U	1.26	1.15	0.65 J	1 U	**4**
MW-202	06/11/09		1 U	0.46 J	1 U	1 U	1 U	1 U	1 U	1.2	1	0.6 J	1 U	**3**
MW-202	11/29/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	1.2	1 U	1 U	1 U	**1**
MW-202	06/29/10		1 U	0.7 J	1 U	1 U	1 U	1 U	1 U	1.6	1.3	0.79 J	1 U	**4**
MW-202	11/28/10		1 U	1 U	1 U	1 U	1 U	1 U	1 U	2.1	0.67 J	1 U	1 U	**3**
MW-202	06/03/11		1 U	0.35 J	1 U	1 U	1 U	1 U	0.26 J	1.5	0.45 J	0.39 J	1 U	**3**
MW-202	12/29/11		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1.2	0.22 J	0.28 J	1 U	**2**
MW-202	06/27/12		1 U	0.46 J	1 U	1 U	1 U	1 U	5 U	1.4	0.94 J	1 U	1 U	**3**
MW-202	11/30/12		1 U	0.45 J	1 U	1 U	1 U	1 U	5 U	2.1	1	0.3 J	1 U	**4**
MW-202	06/05/13		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1.7	0.51 J	0.37 J	1 U	**3**
MW-202	12/01/13		1 U	1 U	1 U	1 U	1 U	1 U	5 U	1.1	0.66 J	1 U	1 U	**2**
MW-202	06/14/14		1 U	0.44 J	1 U	1 U	1 U	1 U	5 UB	1.4	0.39 J	0.38 J	1 U	**3**
MW-202	11/24/14		1 U	0.43 J	1 U	1 U	1 U	1 U	5 U	0.97 J	1 U	0.35 J	1 U	**2**
MW-203	05/20/99		1 U	1 U	1 U	1 U	0.67	1 U	2 U	14	0.92	1.2	1 U	**17**
MW-203	10/28/99		0.08 J	0.28 J	1 U	0.42 J	1.5	0.06 J	2 U	15	2.7	2.6	1 U	**23**
MW-203	02/15/00		1 U	1 U	1 U	1 U	0.13 J	1 U	2 U	8.6	0.26 J	0.16 J	1 U	**9**
MW-203	04/18/00		1 U	1 U	1 U	1 U	0.07 J	1 U	2 U	11	0.14 J	0.17 J	1 U	**11**
MW-203	07/27/00		1 U	1 U	1 U	1 U	1 U	1 U	2 U	13	0.2	0.24	1 U	**13**
MW-203	11/13/00		0.82	1 U	1 U	1 U	1 U	1 U	2 U	3.5	0.66	0.81	1 U	**6**
MW-203	04/12/01		1.8	1 U	1 U	1 U	1 U	1 U	2 U	3.2	0.81	0.76	1 U	**7**
MW-203	10/29/01		4.3	0.19	1 U	1 U	1 U	1 U	2 U	3.1	0.76	0.84	1 U	**9**
MW-203	04/30/02		4.1	0.12	1 U	1 U	1 U	1 U	2 U	3	0.69	0.63	1 U	**9**
MW-203	10/17/02		1	1 U	1 U	1 U	1 U	1 U	0.5	3	1 U	0.7	1 U	**5**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-203	04/24/03		1 U	1 U	1 U	1 U	1 U	1 U	2 U	10.2	1 U	1 U	1 U	**10**
MW-203	12/30/03		1 U	1 U	1 U	1 U	1 U	1 U	1 U	8.43	1 U	1 U	1 U	**8**
MW-203	04/28/04		1 U	1 U	1 U	1 U	1 U	1 U	2 U	8.79	1 U	1 U	1 U	**9**
MW-203	05/21/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	9.6	1 U	1 U	1 U	**10**
MW-203	10/21/05		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1 U	1 U	1 U	1 U	**0**
MW-203	06/28/06		1 U	1 U	1 U	1 U	1 U	1 U	2 U	17	1 U	1 U	1 U	**17**
MW-203	01/05/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1.7	1 U	1 U	1 U	**2**
MW-203	10/08/07		1 U	1 U	1 U	1 U	1 U	1 U	2 U	4	1 U	1 U	1 U	**4**
MW-203	05/18/08		1 U	1 U	1 U	1 U	1 U	1 U	2 U	1	1	1 U	1 U	**2**
MW-203	05/18/08	Fld Dupe	1 U	1 U	1 U	1 U	1 U	1 U	2 U	1	1	1 U	1 U	**2**
MW-203	11/29/08		0.15 J	0.45 J	1 U	1 U	1 U	1 U	1 U	3.11	0.19 J	0.33 J	1 U	**4**
MW-203	06/11/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	4.4	1 U	1 U	1 U	**4**
MW-203	11/29/09		1 U	1 U	1 U	1 U	1 U	1 U	1 U	5.4	1 U	1 U	1 U	**5**
MW-203	06/29/10		1 U	1 U	1 U	1 U	1 U	1 U	0.32 J	8.9	1 U	1 U	1 U	**9**
MW-203	11/28/10		1 U	1 U	1 U	1 U	1 U	1 U	1 U	7.3	1 U	1 U	1 U	**7**
MW-203	06/03/11		1 U	1 U	1 U	1 U	1 U	1 U	0.27 J	5.1	1 U	1 U	1 U	**5**
MW-203	12/29/11		1 U	1 U	1 U	1 U	1 U	1 U	5 U	5.1	1 U	0.19 J	1 U	**5**
MW-203	06/28/12		1 U	1 U	1 U	1 U	1 U	1 U	5 U	10	1 U	0.41 J	1 U	**10**
MW-203	11/30/12		1 U	0.19 J	1 U	1 U	1 U	1 U	5 U	11	0.36 J	0.34 J	1 U	**12**
MW-203	06/10/13		1 U	1 U	1 U	1 U	1 U	1 U	5 U	9.5	1 U	1 U	1 U	**10**
MW-203	12/01/13		1 U	1 U	1 U	1 U	1 U	1 U	5 U	5.9	1 U	1 U	1 U	**6**
MW-203	06/14/14		1 U	0.35 J	1 U	1 U	0.21 J	1 U	5 UB	2.6	0.31 J	0.23 J	1 U	**4**
MW-203	11/24/14		1 U	1 U	1 U	1 U	1 U	1 U	5 U	4.1	0.24 J	1 U	1 U	**4**
MW-204	04/23/99		20 U	20 U	20 U	6.2	56	20 U	40 U	20 U	4.7	230	20 U	**297**
MW-204	10/26/99		10 U	5.2 J	4.5 J	8.6 J	51	0.55 J	20 U	2.4 J	5.4 J	230	1.1 J	**309**
MW-204	01/31/00		0.67 J	5 J	5.3 J	8.2 J	41	10 U	2 J	2.4 J	4.2 J	200	0.85 J	**270**
MW-204	04/24/00		0.92 J	4.9 J	5.7 J	9.2 J	44	10 U	20 JB	2 J	4 J	190	1.2 J	**282**
MW-204	07/25/00		1.1	4.4	5.7	6.9	38	10 U	20 U	1.3	3.4	120	10 U	**181**
MW-204	11/08/00		10 U	6.5	6.8	11	37	10 U	20 U	2.4	4	170	10 U	**238**
MW-204	04/12/01		10 U	5	6	11	27	10 U	20 U	2.4	4.5	160	10 U	**216**
MW-204	10/16/01		10 U	5.4	10 U	13	23	10 U	20 U	2.8	4.9	140	10 U	**189**
MW-204	04/17/02		0.77	6.9	10	18	20	10 U	20 U	2.9	6	140	0.041 J	**205**
MW-204	10/03/02		20 U	14	20 U	140	23	20 U	40 U	20 U	20 U	170	1 U	**347**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-204	04/22/03		0.59 J	8.21	9.93	28.4 E	28.6 E	0.61 J	2 U	3.9	9.93	192 E	0.76 J	**283**
MW-204	04/22/03	Dilution	10 U	7.58 J	9.49 J	23.9	26.8	10 U	20 U	10 U	9.28 J	165	10 U	**242**
MW-204	12/28/03		0.58 J	8.14	9.41	26.3 E	28.8 E	1 U	1 U	3.83	11.3	163 E	0.8 J	**252**
MW-204	12/28/03	Dilution	10 U	7.65 JD	8.32 JD	21.8 D	23.7 D	10 U	10 U	10 U	9.1 JD	151 D	10 U	**222**
MW-204	04/28/04		10 U	6.41	8.07	21	20.7	10 U	20 U	10 U	8.96	124	10 U	**189**
MW-204	05/21/05		1 U	6	5.9	22	13	1 U	2 U	2.8	10	96	1 U	**156**
MW-204	10/19/05		1 U	6.2	5.7	20	15	1 U	2 U	2.3	9.1	97	1 U	**155**
MW-204	05/06/06		1 U	5.7	4.4	21	13	1 U	2 U	2.9	10	100	1 U	**157**
MW-204	01/03/07		1 U	6	3.5	22	15	1 U	2 U	3.2	10	100	1 U	**160**
MW-204	10/07/07		0.5	6	3	19	15	0.5	2 U	3	10	85	0.4 J	**142**
MW-204	10/07/07	Fld Dupe	0.5 J	5	3	18	15	0.4 J	2 U	3	9	82 D	1 U	**136**
MW-204	05/18/08		4 U	6	4 U	20	20	4 U	8 U	4 U	9	91	4 U	**146**
MW-204	11/29/08		0.65 J	4.9	2.07	13.6	14.4	0.29 J	1 U	2.64	7.61	74	0.32 J	**120**
MW-204	06/11/09		0.67 J	4.3	1.4	11	14	0.4 J	1 U	2.6	7.2	73	0.31 J	**115**
MW-204	11/25/09		0.65 J	5.8	1.8	14	20	1 U	1 U	2.6	6.2	71	0.56 J	**123**
MW-204	06/29/10		1 U	5.2	1.3	12	18	1 U	1 U	2	4.3	61	1 U	**104**
MW-204	11/25/10		0.54 J	5.3	1.5	11	24	1 U	1 U	2.5	6.4	66	1 U	**117**
MW-204	06/02/11		0.5 J	5.9	1.3	11	26	0.4 J	1 U	2.1	5.9	60	0.25 J	**113**
MW-204	12/29/11		0.55 J	5.3	1.3	10	26	0.52 J	5 U	2	5.6	51	1 U	**102**
MW-204	06/27/12		0.63 J	5.5	1.2	7.1	30	1.3	5 U	1.7	5.8	54	1 U	**107**
MW-204	11/25/12		0.45 J	6	1.2	12	33	0.64 J	5 U	1.8	7.3	51	1 U	**113**
MW-204	05/31/13		0.46 J	6.5	1	12	36	0.5 J	5 U	1.7	7.9	51	1 U	**117**
MW-204	05/31/13	Fld Dupe	0.45 J	6.4	0.97 J	12	36	0.41 J	5 U	1.7	7.8	51	1 U	**117**
MW-204	12/01/13		0.33 J	6.2	0.75 J	12	37	0.47 J	5 U	1.6	6.4	52	1 U	**117**
MW-204	06/04/14		0.3 J	8.6	0.7 J	15	40	0.52 J	5 U	1.9	12	52	0.18 J	**131**
MW-204	11/23/14		0.38 J	9.8	0.94 J	16	40	0.78 J	5 U	1.4	10	51	1 U	**130**
MW-205A	04/22/99		0.88	23	4.4	100	49	5 U	10 U	3.9	570	69	5 U	**820**
MW-205A	10/21/99		1.1 J	23 J	25 U	110	57	25 U	50 U	3.4 J	460	68	25 U	**723**
MW-205A	02/07/00		25 U	22 J	3.5 J	110	56	25 U	50 U	3.6 J	450	68	25 U	**713**
MW-205A	04/18/00		50 U	23 J	50 U	140	61	50 U	100 JB	50 U	540	80	50 U	**944**
MW-205A	07/25/00		20 U	19	3.5	92	50	20 U	40 U	20 U	350	47	20 U	**562**
MW-205A	11/07/00		25 U	27	25 U	120	56	25 U	50 U	25 U	410	66	25 U	**679**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-205A	04/09/01		20 U	23	20 U	130	56	20 U	40 U	4.3	430	68	20 U	**711**
MW-205A	10/16/01		1.1	18	20 U	87	44	20 U	40 U	2.1	240	49	20 U	**441**
MW-205A	04/16/02		1.1	17	20 U	79	43	20 U	40 U	6.7	270	47	20 U	**464**
MW-205A	10/07/02		50 U	50 U	50 U	690	53	50 U	84	110	310	49	1 U	**1296**
MW-205A	04/22/03		0.78 J	21	2.39	122 E	51.2 E	1 U	2 U	7.15	397 E	72.8 E	1 U	**674**
MW-205A	04/22/03	Dilution	25 U	19.8 J	25 U	111	46.6	25 U	50 U	25 U	322	64.3	25 U	**564**
MW-205A	12/22/03		0.69 J	19.7	1.48	95.6 E	52.7 E	1 U	1 U	11.3	308 E	64.3 E	1 U	**554**
MW-205A	12/22/03	Dilution	20 U	15.4 JD	20 U	71.9 D	38.5 D	20 U	20 U	20 U	237 D	47.1 D	20 U	**410**
MW-205A	04/28/04		20 U	15.8	20 U	68.7	39.9	20 U	40 U	20 U	229	43.9	20 U	**397**
MW-205A	05/21/05		1 U	15	1 U	51	43	1 U	2 U	11	130	36	1 U	**286**
MW-205A	10/19/05		1 U	13	1 U	35	38	1 U	2 U	11	89	32	1 U	**218**
MW-205A	05/06/06		1 U	14	1 U	29	37	1 U	2 U	18	81	32	1 U	**211**
MW-205A	11/21/06		1 U	13	1 U	49	47	1 U	2 U	17	160	51	1 U	**337**
MW-205A	10/06/07		0.5	12	0.4	31	39	1 U	2 U	16	75	34	1 U	**208**
MW-205A	05/18/08		4 U	13	4 U	27	48	4 U	8 U	20	73	35	4 U	**216**
MW-205A	11/28/08		0.49 J	11.9	0.29 J	21.3	41.5	1 U	1 U	20.2	59.5	30.8	1 U	**186**
MW-205A	06/09/09		0.45 J	10	0.27 J	19	36	1 U	1 U	19	60	30	1 U	**175**
MW-205A	11/25/09		0.48 J	11	1 U	19	32	1 U	1 U	20	46	27	1 U	**155**
MW-205A	06/24/10		0.35 J	11	1 U	16	25	1 U	1 U	22	41	23	1 U	**138**
MW-205A	11/25/10		0.38 J	13	1 U	16	18	1 U	1 U	23	41	24	1 U	**135**
MW-205A	06/02/11		0.34 J	15	1 U	15	13	1 U	1 U	23	36	22	1 U	**124**
MW-205A	01/08/12		0.31 J	20	1 U	14	7.4	1 U	5 U	24	31	16	1 U	**113**
MW-205A	06/28/12		0.4 J	21	1 U	13	5.7	1 U	5 U	24	30	16	1 U	**110**
MW-205A	12/02/12		0.26 J	20	1 U	11	4.6	1 U	5 U	24	27	15	1 U	**102**
MW-205A	05/31/13		0.26 J	20	1 U	11	5.3	1 U	5 U	23	25	16	1 U	**101**
MW-205A	11/29/13		0.27 J	27	1 U	12	4.4	1 U	5 UB	26	24	15	1 U	**109**
MW-205A	06/05/14		0.3 J	23	1 U	10	4.6	1 U	5 U	25	24	15	1 U	**102**
MW-205A	11/22/14		0.29 J	36	1 U	12	2.7	1 U	5 U	22	27	14	1 U	**114**
MW-205B	04/22/99		0.73	23	3.4	74	47	5 U	10 U	3.5	310	57	5 U	**519**
MW-205B	10/21/99		25 U	23 J	25 U	82	54	25 U	50 U	3.4 J	340	58	25 U	**560**
MW-205B	02/07/00		25 U	24 J	25 U	86	57	25 U	50 U	3.8 J	360	60	25 U	**591**
MW-205B	04/18/00		20 U	26	20 U	90	59	20 U	40 JB	3.8 J	370	65	20 U	**654**
MW-205B	07/25/00		20 U	23	20 U	70	52	20 U	40 U	20 U	270	44	20 U	**459**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-205B	11/07/00		20 U	31	2.9	79	55	20 U	40 U	3.6	270	53	20 U	**495**
MW-205B	04/09/01		20 U	31	20 U	110	68	20 U	40 U	4.5	330	67	20 U	**611**
MW-205B	10/16/01		20 U	21	20 U	73	50	20 U	40 U	5.1	250	45	20 U	**444**
MW-205B	04/16/02		0.82	22	10 U	59	53	1.4	0.7	5.8	220	48	10 U	**411**
MW-205B	10/07/02		50 U	50 U	50 U	470	65	50 U	90	110	310	49	1 U	**1094**
MW-205B	04/22/03		0.75 J	24.2	1.79	92.4 E	59.6 E	1 U	2 U	11.4	303 E	63.8 E	1 U	**557**
MW-205B	04/22/03	Dilution	20 U	23.7	20 U	93.1	57.3	20 U	40 U	10 J	262	60.4	20 U	**507**
MW-205B	12/22/03		0.7 J	21.6	1.36	70.5 E	53.8 E	0.55 J	1 U	13	239 E	52.1 E	1 U	**453**
MW-205B	12/22/03	Dilution	20 U	18.7 JD	20 U	64.9 D	47.1 D	20 U	20 U	10.5 JD	201 D	44.6 D	20 U	**387**
MW-205B	04/28/04		20 U	22.4	20 U	75.5	54.4	20 U	40 U	11.4	233	49.3	20 U	**446**
MW-205B	05/21/05		1 U	17	1 U	43	47	1 U	2 U	13	110	34	1 U	**264**
MW-205B	10/19/05		1 U	17	1 U	32	43	1 U	2 U	14	89	31	1 U	**226**
MW-205B	05/06/06		1 U	18	1 U	26	52	1 U	2 U	23	59	31	1 U	**209**
MW-205B	11/21/06		1 U	18	1 U	39	71	1 U	2 U	23	95	44	1 U	**290**
MW-205B	10/06/07		0.4	15	0.4	30	52	1 U	2 U	18	66	31	1 U	**213**
MW-205B	05/18/08		4 U	16	4 U	30	63	4 U	8 U	22	69	34	4 U	**234**
MW-205B	11/28/08		0.49 J	15	0.38 J	19.9	43.1	1 U	1 U	12.8	79.4	24.6	1 U	**196**
MW-205B	06/09/09		0.49 J	15	0.25 J	21	44	1 U	1 U	18	63	29	1 U	**191**
MW-205B	11/25/09		0.55 J	14	1 U	21	37	1 U	1 U	21	47	27	1 U	**168**
MW-205B	06/24/10		0.38 J	14	0.16 J	17	29	1 U	1 U	22	43	23	1 U	**149**
MW-205B	11/25/10		0.41 J	15	1 U	17	23	1 U	1 U	23	42	24	1 U	**144**
MW-205B	06/02/11		0.38 J	17	1 U	18	21	1 U	1 U	23	39	22	1 U	**140**
MW-205B	01/08/12		0.32 J	20	1 U	14	11	1 U	5 U	23	31	16	1 U	**115**
MW-205B	06/28/12		0.43 J	21	1 U	13	8.2	1 U	5 U	23	30	15	1 U	**111**
MW-205B	12/02/12		0.32 J	20	1 U	10	6	1 U	5 U	16	25	12	1 U	**89**
MW-205B	05/31/13		0.32 J	23	1 U	12	7	1 U	5 U	23	27	15	1 U	**107**
MW-205B	11/29/13		0.26 J	27	1 U	12	5.4	1 U	5 UB	25	24	14	1 U	**108**
MW-205B	06/05/14		0.3 J	30	1 U	11	4.8	1 U	5 U	26	25	14	1 U	**111**
MW-205B	11/22/14		0.3 J	38	1 U	13	4.1	1 U	5 U	23	28	14	1 U	**120**
MW-206A	04/23/99		0.64	8.5	0.75	22	23	2 U	4 U	9.3	100	37	2 U	**201**
MW-206A	10/20/99		10 U	9.8 J	10 U	21	21	10 U	20 U	6.6 J	87	33	10 U	**178**
MW-206A	02/07/00		0.55 J	10	5 U	14	20	5 U	10 U	7	79	25	5 U	**156**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-206A	04/18/00		0.55 J	9.6	5 U	12	20	0.36 J	10 JB	5.2	62	22	5 U	**142**
MW-206A	07/25/00		0.72	9.4	5 U	14	21	5 U	10 U	3.1	66	16	5 U	**130**
MW-206A	11/07/00		5 U	12	5 U	5.9	13	5 U	10 U	0.84	46	7.6	5 U	**85**
MW-206A	04/09/01		0.66	9.7	5 U	13	20	5 U	10 U	4.5	55	22	5 U	**125**
MW-206A	10/16/01		0.49	8.8	2 U	9.9	18	2 U	0.34	3.5	39	18	2 U	**98**
MW-206A	04/16/02		0.39	7.1	2 U	7.1	15	0.39	4 U	3.4	31	16	2 U	**80**
MW-206A	10/08/02		5 U	11	5 U	57	23	5 U	10 U	3	35	18	1 U	**147**
MW-206A	04/21/03		0.87 J	11.8	1 U	11.7	30.3 E	1.05	2 U	3.48	31.1 E	18.1	1 U	**108**
MW-206A	04/21/03	Dilution	2 U	11	2 U	11.1	28.4	2 U	4 U	3.17	26.9	17	2 U	**98**
MW-206A	12/22/03	Dilution	2 U	12.4 D	2 U	11.4 D	33.6 D	1.11 JD	2 U	3.36 D	29.8 D	16.5 D	2 U	**108**
MW-206A	12/22/03		1.04	14.5	1 U	13.9	38.4 E	1.4	1 U	3.99	35.8 E	19	1 U	**128**
MW-206A	04/28/04		1.28	10.7	2 U	11.1	31.6	2 U	4 U	3.65	27.4	15.1	2 U	**101**
MW-206A	05/21/05		1.1	5.6	1 U	6.7	16	1 U	2 U	2.9	17	11	1 U	**60**
MW-206A	10/19/05		1 U	8.1	1 U	8.8	23	1 U	2 U	3.1	19	11	1 U	**73**
MW-206A	05/06/06		1 U	9.2	1 U	9.1	25	1 U	2 U	3.8	23	13	1 U	**83**
MW-206A	11/27/06		1.1	9	1 U	8.2	14	1 U	2 U	4.2	22	14	1 U	**73**
MW-206A	10/06/07		0.6	5	1 U	5	6	1 U	2 U	3	14	9	1 U	**43**
MW-206A	05/18/08		1 U	6	1 U	8	7	1 U	2 U	4	18	11	1 U	**54**
MW-206A	11/28/08		0.28 J	13	0.19 J	7.54	9.43	0.21 J	1 U	1.95	17.9	7.85	1.59	**60**
MW-206A	06/10/09		0.41 J	11	1 U	7.5	7.3	1 U	1 U	2.8	23	9.9	0.97 J	**63**
MW-206A	04/01/10		0.27 J	7.6	1 U	6.8	4.2	1 U	1 U	3.7	18	10	1 U	**51**
MW-206A	06/25/10		0.28 J	8.3	1 U	7.1	4.2	1 U	1 U	3.8	18	9.3	1 U	**51**
MW-206A	11/29/10		0.16 J	13	1 U	4.4	4.5	1 U	1 U	1.5	9.7	4.3	3.6	**41**
MW-206A	06/02/11		0.27 J	12	1 U	6.8	3.8	1 U	0.27 J	3.4	17	9.6	0.55 J	**54**
MW-206A	12/22/11		0.93 J	75	2.2	76	100	1 U	5 U	7.3	52	44	0.92 J	**358**
MW-206A	06/26/12		0.6 J	7.8	1 U	3.7	1.8	1 U	5 U	4.4	11	6.9	1 U	**36**
MW-206A	11/23/12		0.42 J	12	1 U	3.8	2	1 U	5 U	5.5	12	6.2	1 U	**42**
MW-206A	05/30/13		0.38 J	9.9	1 U	3.4	1.7	1 U	5 U	4.9	8.6	5.4	1 U	**34**
MW-206A	11/29/13	Fld Dupe	0.35 J	9.1	1 U	4	1.8	1 U	5 UB	5.7	8.8	5.6	0.21 J	**36**
MW-206A	11/29/13		0.32 J	9.1	1 U	3.9	1.8	1 U	5 UB	5.6	9.1	5.5	0.22 J	**36**
MW-206A	06/05/14		0.51 J	6.7	1 U	2.8	1.2	1 U	5 U	6.2	8.3	5.3	1 U	**31**
MW-206A	11/22/14		0.5 J	7.2	1 U	3	1.2	1 U	5 U	5	6.7	4.5	1 U	**28**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-206B	04/23/99		10 U	5.1	10 U	2.5	59	10 U	20 U	13	4.6	150	10 U	**234**
MW-206B	10/20/99		10 U	9.1 J	10 U	4.9 J	54	10 U	1.3 J	9.6 J	8.4 J	160	10 U	**247**
MW-206B	02/17/00		10 U	13	10 U	8.8 J	36	10 U	20 U	5.8 J	16	150	10 U	**230**
MW-206B	04/18/00		0.62 J	14	10 U	9 J	40	0.28 J	20 JB	5.6 J	16	150	10 U	**256**
MW-206B	07/25/00		0.6	12	5 U	6	36	5 U	10 U	0.98	11	86	5 U	**153**
MW-206B	11/07/00		5 U	17	5 U	8.4	34	5 U	10 U	3.3	14	120	5 U	**197**
MW-206B	04/09/01		0.51	14	5 U	9.1	33	5 U	10 U	2.5	16	110	5 U	**185**
MW-206B	10/16/01		0.62	14	5 U	11	26	5 U	10 U	1.7	20	80	5 U	**153**
MW-206B	04/16/02		0.69	12	5 U	10	23	5 U	10 U	1.5	20	70	5 U	**137**
MW-206B	10/08/02		5 U	22	5 U	76	31	5 U	4	5 U	35	100	1 U	**268**
MW-206B	04/22/03		0.83 J	16.2	0.7 J	16.8	22.1	1 U	2 U	1.35	32.5 E	75.7 E	1 U	**166**
MW-206B	04/22/03	Dilution	5 U	15.1	5 U	15.7	20.5	5 U	10 U	5 U	27.2	68.7	5 U	**147**
MW-206B	12/22/03		0.88 J	17.3	0.71 J	18.2	21.5	1 U	1 U	1.34	34 E	68.8 E	1 U	**163**
MW-206B	12/22/03	Dilution	4 U	14.8 D	4 U	14 D	17.4 D	4 U	4 U	4 U	26.5 D	54.5 D	4 U	**127**
MW-206B	04/28/04		4 U	16	4 U	14.2	19.5	4 U	8 U	4 U	26.3	59.2	4 U	**135**
MW-206B	05/21/05		1 U	16	1 U	13	13	1 U	2 U	1 U	22	33	1 U	**97**
MW-206B	10/19/05		1 U	16	1 U	12	13	1 U	2 U	1 U	22	35	1 U	**98**
MW-206B	05/06/06		1 U	24	1 U	17	15	1 U	2 U	1 U	24	32	1 U	**112**
MW-206B	11/27/06		1 U	47	1.4	31	21	1 U	2 U	1.2	44	45	1 U	**191**
MW-206B	11/27/06	Fld Dupe	1 U	7.1	1 U	5	18	1 U	2 U	1 U	1 U	71	1 U	**101**
MW-206B	10/06/07		0.8	50	1	39	32	1 U	2 U	1	39	28	0.5 J	**191**
MW-206B	05/18/08		4 U	56	4 U	46	50	4 U	8 U	4 U	44	48	4 U	**244**
MW-206B	11/28/08		0.92 J	57.7	1.74	40.9	45.8	0.2 J	1 U	1.71	39.9	35.6	0.72 J	**225**
MW-206B	06/10/09		1	79	2.3	63	70	0.33 J	1 U	3.3	57	37	0.86 J	**314**
MW-206B	04/01/10		0.97 J	77	2.3	77	76	0.57 J	1 U	4.4	58	38	1.2	**335**
MW-206B	06/25/10		1	84	2.4	77	90	0.39 J	1 U	4.9	64	37	1.1	**362**
MW-206B	11/29/10		0.92 J	78	2.3	71	72	0.53 J	1 U	5.5	55	34	1.1	**320**
MW-206B	06/02/11		1.1	91	2.7	83	98	0.39 J	0.27 J	7.2	61	44	1.1	**390**
MW-206B	12/22/11		0.93 J	72	2.2	75	100	1 U	5 U	7.3	50	43	0.96 J	**351**
MW-206B	06/26/12		1	69	2.4	80	130	0.44 J	5 U	10	58	46	0.86 J	**398**
MW-206B	11/23/12		0.86 J	55	2.1	74	130	0.4 J	5 U	14	55	41	0.8 J	**373**
MW-206B	05/30/13		0.79 J	58	2	64	100	1 U	5 U	10	48	36	0.74 J	**320**
MW-206B	11/29/13		0.7 J	51	1.4	69	130	0.37 J	5 U	15	40	35	2.7	**345**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-206B	06/05/14		0.79 J	50	1.5	60	120	0.47 J	5 U	17	44	39	1.6	**334**
MW-206B	11/22/14		0.82 J	44	1.2	60	120	0.36 J	5 U	20	46	38	0.39 J	**331**
MW-206C	04/23/99		1 U	1 U	1 U	0.31	2.7	1 U	2 U	0.41	1.5	4.1	1 U	**9**
MW-206C	10/20/99		1 U	0.18 J	1 U	0.15 J	2.3	1 U	2 U	1 U	0.26 J	4.3	1 U	**7**
MW-206C	02/07/00		1 U	1 U	1 U	1 U	3.5	1 U	2 U	1 U	1 U	5.3	1 U	**9**
MW-206C	04/18/00		1 U	1 U	1 U	1 U	4	1 U	2 JB	1 U	1 U	6	1 U	**12**
MW-206C	07/25/00		1 U	1 U	1 U	1.3	4.8	1 U	2 U	1 U	1 U	3.5	1 U	**10**
MW-206C	11/07/00		1 U	0.14	1 U	0.12	2.3	1 U	2 U	1 U	0.29	3.4	1 U	**6**
MW-206C	11/07/00	Fld Dupe	1 U	0.14 J	1 U	0.12 J	2.3	1 U	2 U	1 U	0.28 J	3.3	1 U	**6**
MW-206C	04/09/01	Fld Dupe	1 U	0.33 J	1 U	0.26 J	4.2	1 U	2 U	0.26 J	0.48 J	6.3	1 U	**12**
MW-206C	04/09/01		1 U	0.36	1 U	0.28	4.3	1 U	2 U	0.25	0.7	6.6	1 U	**12**
MW-206C	10/16/01		1 U	0.24	1 U	0.11	5.9	1 U	2 U	0.2	0.18	7.6	1 U	**14**
MW-206C	04/16/02		1 U	1 U	1 U	0.17	6.9	1 U	2 U	0.06	1 U	14	1 U	**21**
MW-206C	10/08/02		5 U	5 U	5 U	5 U	15	5 U	4	5 U	5 U	30	1 U	**49**
MW-206C	04/22/03		1 U	0.86 J	1 U	0.55 J	14.4	1 U	2 U	1 U	1 U	43 E	1 U	**59**
MW-206C	04/22/03	Dilution	2.5 U	2.5 U	2.5 U	2.5 U	13.2	2.5 U	5 U	2.5 U	2.5 U	39.1	2.5 U	**52**
MW-206C	12/22/03		1 U	1.37	1 U	1.68	16.6	0.61 J	1 U	1 U	1 U	53 E	1 U	**73**
MW-206C	12/22/03	Dilution	4 U	4 U	4 U	4 U	14 D	4 U	4 U	4 U	4 U	44.7 D	4 U	**59**
MW-206C	04/28/04		2 U	1.21	2 U	2 U	14.9	2 U	4 U	2 U	2 U	37.7	2 U	**54**
MW-206C	05/21/05		1 U	1.5	1 U	1.1	9.2	1 U	2 U	1 U	1 U	34	1 U	**46**
MW-206C	10/19/05		1 U	3.8	1 U	2.6	15	1 U	0.1	1 U	1 U	47	1 U	**69**
MW-206C	05/06/06		1 U	5	1 U	3.5	14	1 U	2 U	1 U	1 U	52	1 U	**75**
MW-206C	11/27/06		1 U	6.5	1 U	4.4	17	1 U	2 U	1 U	1 U	85	1 U	**113**
MW-206C	10/06/07		1 U	5	1 U	4	11	1 U	2 U	0.4	1 U	44	1 U	**64**
MW-206C	05/18/08		2 U	5	2 U	4	12	2 U	4 U	2 U	2 U	38	2 U	**59**
MW-206C	11/28/08		1 U	3.11	1 U	2.01	5.23	1 U	1 U	1 U	1 U	19.4	1 U	**30**
MW-206C	06/10/09		1 U	2.7	1 U	1.8	4.8	1 U	1 U	1 U	1 U	16	1 U	**25**
MW-206C	04/01/10		1 U	3.4	1 U	2.7	4.8	1 U	1 U	1 U	1 U	16	1 U	**27**
MW-206C	06/25/10		1 U	5.2	1 U	3.6	6.5	1 U	1 U	1 U	1 U	20	1 U	**35**
MW-206C	11/29/10		1 U	3.9	1 U	3.1	5.1	1 U	1 U	1 U	1 U	16	1 U	**28**
MW-206C	06/02/11		1 U	6	1 U	3.9	6.9	1 U	0.26 J	1 U	1 U	22	1 U	**39**
MW-206C	12/22/11		1 U	6.3	1 U	4.4	7.5	1 U	5 U	0.3 J	1 U	24	1 U	**43**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-206C	06/26/12		1 U	5.8	1 U	3.8	6.1	1 U	5 U	1 U	1 U	19	1 U	**35**
MW-206C	11/23/12		1 U	7.1	1 U	5.1	7.1	1 U	5 U	0.24 J	1 U	19	1 U	**39**
MW-206C	05/30/13		1 U	7.5	1 U	4.9	6.9	1 U	5 U	1 U	1 U	18	1 U	**37**
MW-207	04/23/99		0.39	0.76	2 U	2 U	1.6	2 U	4 U	2.6	2.7	26	2 U	**34**
MW-207	10/27/99		0.59 J	1.3	1 U	0.74 J	5.1	0.06 J	2 U	3.9	5.9	25	1 U	**43**
MW-207	02/17/00		0.54 J	1.1	1 U	0.22 J	1.2	1 U	2 U	2.8	2	22	1 U	**30**
MW-207	04/18/00		0.62 J	1.2	1 U	0.1 J	1.2	0.1 J	2 JB	2.7	2	20	1 U	**30**
MW-207	07/25/00		0.63	1.3	1 U	1 U	1.4	0.16	2 U	2.1	2	17	1 U	**25**
MW-207	11/08/00		0.71	2.1	1 U	0.24	1.4	1 U	2 U	2.3	1.9	16	1 U	**25**
MW-207	04/10/01		0.6	1.5	1 U	1 U	3.2	0.44	2 U	0.51	1.5	11	1 U	**19**
MW-207	10/16/01		0.44	5.3	1 U	0.13	3.4	0.33	2 U	1	4.2	22	1 U	**37**
MW-207	04/17/02		0.36	6.2	2 U	0.26	3.7	0.39	4 U	1.4	5.7	25	1 U	**43**
MW-207	10/08/02		1 U	8	1 U	6	5	1 U	0.8	0.9	5	21	1 U	**47**
MW-207	04/22/03		0.54 J	7.42	1 U	1.8	5.09	1 U	2 U	2.5	8.37	29.3 E	1 U	**55**
MW-207	04/22/03	Dilution	2 U	7.05	2 U	2.13	4.88	2 U	4 U	2.3	7.6	27.8	2 U	**52**
MW-207	12/28/03		0.53 J	6.12	1 U	2.64	4.5	1 U	1 U	2.58	8.64	29.4 E	1 U	**54**
MW-207	12/28/03	Dilution	2 U	5.68 D	2 U	2.18 D	3.78 D	2 U	2 U	2.21 D	7.19 D	25.8 D	2 U	**47**
MW-207	04/28/04		2 U	5.87	2 U	1.85	4.26	2 U	4 U	2.67	8.24	28.1	2 U	**51**
MW-207	05/21/05	Fld Dupe	1 U	4.4	1 U	1.6	3	1 U	2 U	2	5.3	18	1 U	**34**
MW-207	05/21/05		1 U	4.3	1 U	1.7	3	1 U	2 U	2.1	5.4	18	1 U	**35**
MW-207	10/19/05		1 U	4.5	1 U	1 U	2.7	1 U	2 U	1.3	5.7	17	1 U	**31**
MW-207	05/06/06		1 U	5.2	1 U	1.8	3.3	1 U	2 U	2	6.7	19	1 U	**38**
MW-207	11/27/06		1 U	5.7	1 U	1.1	3.1	1 U	2 U	2.6	9.3	24	1 U	**46**
MW-207	10/07/07		0.4	4	1 U	0.7	3	1 U	1 U	2	7	15	1 U	**32**
MW-207	05/18/08		1 U	4	1 U	2	3	1 U	2 U	2	7	15	1 U	**33**
MW-207	11/29/08		0.36 J	2.97	1 U	1 U	1.89	0.27 J	1 U	1.98	5.58	10.8	1 U	**24**
MW-207	06/10/09		0.31 J	2.4	1 U	0.65 J	1.8	1 U	1 U	2.1	4.6	9.9	1 U	**22**
MW-207	11/25/09		1 U	1.6	1 U	0.6 J	1.2	1 U	1 U	2.2	3.5	7.4	1 U	**17**
MW-207	06/24/10		0.18 J	1.3	1 U	0.52 J	1	1 U	1 U	1.9	2.8	5.6	1 U	**13**
MW-207	11/25/10		0.22 J	1.3	1 U	0.72 J	1.3	1 U	1 U	2.2	3	6	1 U	**15**
MW-207	06/02/11		1 U	1.5	1 U	0.6 J	1.2	1 U	0.3 J	1.6	2.8	5.2	1 U	**13**
MW-207	12/29/11		0.19 J	1.5	1 U	0.57 J	1.4	1 U	5 U	1.7	2.6	4.4	1 U	**12**
MW-207	06/26/12		0.27 J	1.4	1 U	0.4 J	1.2	1 U	5 U	1.3	2.2	3.9	1 U	**11**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Well ID	Date	Sample Type	CFM	1,1-DCA	1,2-DCA	1,1-DCE	c1,2-DCE	t1,2-DCE	MC	PCE	1,1,1-TCA	TCE	VC	Total VOCs
		MCL	NA	NA	5	7	70	100	5	5	200	5	2	
MW-207	11/30/12		0.22 J	1.4	1 U	0.53 J	1.2	1 U	5 U	1.4	2.3	4	1 U	**11**
MW-207	05/31/13		1 U	1.8	1 U	0.5 J	1.4	1 U	5 U	1.4	2.4	4.5	1 U	**12**
MW-207	12/01/13		1 U	1.3	1 U	0.35 J	1.2	1 U	5 U	1.4	1.8	3.7	1 U	**10**
MW-207	06/04/14		0.29 J	1.7	1 U	0.64 J	1.3	1 U	5 U	1.5	2.7	4.5	1 U	**13**
MW-207	11/23/14		0.28 J	1.8	1 U	0.58 J	1.2	1 U	5 U	1.4	2.3	4	1 U	**12**

Table 2: Southeast Rockford NPL Site
Cumulative Ground Water Analytical Results

Results reported in micrograms per liter (µg/l)

Highlighted results equal or exceed the Maximum Contaminant Level (MCL), where applicable

CFM	Chloroform
1,1-DCA	1,1-Dichloroethane
1,2-DCA	1,2-Dichloroethane
1,1-DCE	1,1-Dichloroethene
c1,2-DCE	cis- 1,2-Dichloroethene
t1,2-DCE	trans-1,2-Dichloroethene
MC	Methylene Chloride
PCE	Tetrachloroethene
1,1,1-TCA	1,1,1-Trichloroethane
TCE	Trichloroethene
VC	Vinyl Chloride
Total VOCs	Sum of Total Volatile Organic Compound Concentrations

B	Concentration is less than the reporting limit but greater than the instrument detection limit.
D	Reported concentration is based on an analysis requiring a secondary detection limit.
E	The associated value exceeds the calibration range.
J	The reported concentration is estimated.
U	Analyte was not detected at or above the reporting limit.

Sample Type reported as undiluted, investigative sample unless stated otherwise

Fld Dupe	Field Duplicate

Table 3: Southeast Rockford NPL Site
Ground Water Elevations

Station Identification	Measurement Date	Water Level (ft TOC)	Groundwater Elevation (ft amsl)	Total Depth (ft TOC)	Comments
MW-16	11/24/14	24.10	703.94	62.36	**** Well repaired - well level from new TOC
MW-47	11/23/14	41.40	694.26	54.49	
MW-101A	11/24/14	45.12	720.50	90.35	Field Duplicate (FD-2) Collected
MW-101B	11/24/14	45.83	720.79	153.74	
MW-101C	11/24/14	45.72	720.76	174.89	
MW-101D	11/24/14	47.82	717.14	212.72	
MW-102A	11/24/14	17.22	771.21	37.69	
MW-102B	11/24/14	37.10	751.51	100.50	
MW-102C	11/24/14	37.43	752.44	187.42	
MW-113A	11/24/14	56.92	709.62	104.50	
MW-113B	11/24/14	57.55	709.10	155.26	
MW-114A	11/24/14	32.74	694.15	97.48	
MW-114B	11/24/14	28.73	698.69	222.58	Well repaired - measurements taken from new TOC
MW-117B	11/21/14	5.45	690.81	89.50	
MW-117C	11/21/14	4.38	691.73	158.31	1 bolt hole stripped
MW-117D	11/22/14	4.18	691.92	200.20	
MW-119	11/22/14	25.92	693.05	62.41	
MW-121	11/23/14	23.27	693.71	67.55	
MW-124	11/23/14	35.88	695.42	102.76	
MW-130	11/23/14	24.93	703.02	38.17	
MW-133A	11/24/14	33.00	747.18	37.85	STATIC WATER LEVEL AT TOP OF PUMP
MW-133B	11/24/14	28.14	752.19	61.49	
MW-133C	11/24/14	23.74	756.55	98.49	
MW-136	11/23/14	35.27	799.50	44.33	
MW-200	11/23/14	51.29	708.87	89.93	
MW-201	11/23/14	30.75	698.28	50.15	Field Duplicate collected = FD-1
MW-202	11/24/14	29.94	699.68	50.01	
MW-203	11/24/14	29.44	699.65	49.35	well pump was removed by unknown. Pumped utilizing a QED sample pro portable pump with teflon liner & tubing.
MW-204	11/23/14	26.39	690.82	88.96	
MW-205A	11/22/14	2.53	690.80	110.27	
MW-205B	11/22/14	2.47	690.75	150.05	
MW-206A	11/22/14	4.16	689.54	90.24	
MW-206B	11/22/14	2.46	690.80	129.94	
MW-206C		0.00	693.06	251.31	Inaccessible well - did not sample
MW-207	11/23/14	34.16	690.01	90.81	

ft amsl Feet above mean sea level
ft TOC Feet from Top of Casing

Table 4 - Southeast Rockford Contamination Site
Groundwater Monitoring Network

Well ID	Easting	Northing	TOC Elevation (ft amsl)[1]	Ground Surface Elevation (ft amsl)[1]	Casing Stickup (ft)[2]	Total Depth (ft TOC)[2]	Screen Top (ft bgs)	Screen Bottom (ft bgs)	Screen Length (ft)	Casing (in)	Casing Material	Aquifer screened	Location Description	Comments
MW-16	2593475.34	2030401.25	727.91	728.00	-0.09	62.36	42.70	47.70	5.00	2		unconsolidated	East of Kinsey Street, north of drain canal	flush mount; measured 01/05/15
MW-47	2588765.03	2028342.66	735.66	733.70	-0.63	54.49	48.00	53.00	5.00	2	SS	unconsolidated	Brooke Rd. 1/2 Block West of Kishwaukee Intersection.	
MW-101A	2598084.40	2029683.41	765.62	764.10	1.45	90.35	78.00	88.00	10.00	2	SS	unconsolidated	Northeast corner of Laude and 24th Street	
MW-101B	2598093.32	2029682.50	766.62	764.10	2.16	153.74	140.10	150.10	10.00	2	SS	bedrock		
MW-101C	2598076.01	2029675.69	766.48	764.00	1.12	174.89	162.00	172.00	10.00	2	SS	bedrock		
MW-101D	2598066.94	2029682.19	764.96	763.90	0.89	212.72	202.80	212.80	10.00	2	SS	bedrock		
MW-102A	2599371.95	2029982.56	788.43	786.50	-0.47	37.69	25.00	35.00	10.00	2	SS	unconsolidated	South of RR tracks, east of Laude Street (Owens-Corning Property)	flush mount ~2005
MW-102B	2599380.00	2029990.00	788.61	786.60	-0.68	100.50	88.00	98.00	10.00	2	SS	unconsolidated		
MW-102C	2599388.00	2029999.00	789.87	787.70	-0.43	187.42	174.30	184.30	10.00	2	SS	bedrock		
MW-113A	2596096.44	2029869.64	766.54	767.00	-1.06	104.50	90.00	105.00	15.00	2	SS	bedrock	West of Willis and 18th Street	
MW-113B	2596088.18	2029873.56	766.65	766.40	-0.43	155.26	145.00	155.00	10.00	2	SS	bedrock		
MW-114A	2593333.10	2030016.18	726.89	724.90	2.45	97.48	85.00	95.00	10.00	2	SS	unconsolidated	Corner of Willis and Kinsey Street	casing slightly bent
MW-114B	2593338.00	2030023.51	725.02	725.20	-0.18	222.58	210.00	220.00	10.00	2	SS	sandstone		flush mount; measured 01/05/15
MW-117B	2586515.64	2028092.93	696.26	696.40	-0.45	89.50	79.50	89.50	10.00	2	SS	unconsolidated	Brooke Rd meridian. West of Grant Park Blvd.	
MW-117C	2586522.28	2028099.95	696.11	696.40	-0.63	158.31	149.50	159.50	10.00	2	SS	unconsolidated		
MW-117D	2586502.42	2028081.65	696.10	696.40	-0.30	200.00	190.50	200.50	10.00	2	SS			TOS from well completion
MW-119	2589374.24	2027137.22	718.97	716.50	3.25	62.41	49.50	59.50	10.00	2	SS	unconsolidated	Corner of Sawyer and South 4th Street	
MW-121	2587523.45	2030898.78	716.98	714.50	2.53	67.55	54.50	64.50	10.00	2	SS	unconsolidated	Corner of Harrison Ave. and Olsen Street	
MW-124	2590224.67	2030300.32	731.30	729.00	2.17	102.76	95.00	100.00	5.00	2	SS	unconsolidated	South of Park Court, west of railroad track	
MW-130	2594440.11	2030701.27	727.95	728.00	-0.30	38.17	27.50	37.50	10.00	2	SS	unconsolidated	Corner of Alton Ave. and Sewell Street	
MW-133A	2600083.74	2028900.38	780.18	777.60	2.30	37.85	25.00	35.00	10.00	2	SS	unconsolidated	West end of Balsam Lane	
MW-133B	2600084.59	2028906.98	780.33	777.50	2.51	61.49	48.00	58.00	10.00	2	SS	unconsolidated		
MW-133C	2600090.11	2028901.64	780.29	777.70	2.37	98.49	86.00	96.00	10.00	2	SS	bedrock		
MW-136	2603572.26	2027821.67	834.77	834.90	-0.42	44.33	40.00	45.00	5.00	2	SS	bedrock	North end of New England Drive	
MW-200	2595998.62	2027199.13	760.16	759.01	1.15	89.93	78.00	88.00	10.00	2	SS		Southeast corner of 17th Street and Sawyer	
MW-201	2591771.57	2031653.69	729.03	729.35	-0.32	50.15	40.00	50.00	10.00	2	SS		Northeast Corner of Rockford Products Parking lot on the East side of 9th St, North of Harrision Ave.	flush mount
MW-202	2592985.38	2032213.06	729.62	729.94	-0.32	50.01	40.00	50.00	10.00	2	SS		West of 11th Street, South of Harrison Ave./23rd Street (Abe Pekarsky property, parking lot)	flush mount
MW-203	2592993.40	2032079.04	729.09	729.67	-0.58	49.35	40.00	50.00	10.00	2	SS		West of 11th Street, South of Harrison Ave./23rd Street (Abe Pekarsky property, parking lot)	flush mount
MW 204	2585435.61	2029789.39	717.21	717.21	-0.39	88.96	80.00	90.00	10.00	2	SS		South end of Falund Street	
MW-205A	2585564.99	2027820.78	693.33	693.67	-0.34	110.27	100.50	110.50	10.00	2	SS		North of Brooke Road, east of Rock River	
MW-205B	2585567.66	2027827.74	693.22	693.70	-0.48	150.05	140.50	150.50	10.00	2	SS			
MW-206A	2585871.82	2026940.34	693.70	694.06	-0.36	90.24	80.00	90.00	10.00	2	SS		Between River Blvd. and the Rock River	
MW-206B	2585856.13	2026938.65	693.26	693.71	-0.45	129.94	120.00	130.00	10.00	2	SS			
MW-206C	2585860.69	2026940.21	693.06	693.61	-0.55	251.31	240.00	250.00	10.00	2	SS			
MW-207	2587190.96	2026478.18	724.17	724.47	-0.30	90.81	80.00	90.00	10.00	2	SS		Corner of Martin Road & Grant Park Blvd.	

[1] Checked against Table 3.1 of 1998 NES work Plan

[2] From June 2009 field report

IEPA keys

From NES well completion forms

calculated TOC elevation, from ground surface and stickup

calculated ground surface elevation, from TOC and stickup

adjusted to reflect 01/05/15 TOC measurement

Appendix A

APPENDIX A

Ground Water Monitoring

Data Validation Summary
Laboratory Data Sheets

Data Quality Control Criteria Review Summary

SDG Number: 1411479 **Project Number:** 1016-2

Site: SE Rockford, 32nd Event

Contractor Lab: TriMatrix (Grand Rapids, MI)

Validator: Brian LaFlamme **Validation Date:** 16 Jan 15

Sample Matrix: Water **Sample Date:** 11/21/14 – 11/24/14

Analytical Methods: EPA SW-846 Method 8260B

Sample Designations:

MW-16	**MW-102C**	**MW-119**	**MW-200**	**MW-206B**
MW-47	**MW-113A**	**MW-121**	**MW-201**	**MW-207**
MW-101A	**MW-113B**	**MW-124**	**MW-202**	
MW-101B	**MW-114A**	**MW-130**	**MW-203**	**FD-1 (field duplicate of MW-201)**
MW-101C	**MW-114B**	**MW-133A**	**MW-204**	**FD-2 (field duplicate of MW-101A)**
MW-101D	**MW-117B**	**MW-133B**	**MW-205A**	**Trip Blank TML3399**
MW-102A	**MW-117C**	**MW-133C**	**MW-205B**	
MW-102B	**MW-117D**	**MW-136**	**MW-206A**	

The analytical data were reviewed in accordance with the analytical methods, SW-846 validation guidelines, and the Environmental Protections Agency (EPA) Contract Laboratory Program (CLP) National Functional Guidelines. The review included comparing quality control (QC) values provided on the laboratory QC forms to method QC criteria. Review of the raw data was not performed.

Quality Control Summary

QC Review Item	VOA
Completeness	X
Case Narrative	X
Chain of Custody (COC) Forms	X
Sample Preservation	X
Holding Times	X
Laboratory Blank Results	1
System Monitoring Compounds (Surrogate) Results	X
Matrix Spike/Matrix Duplicate (MS/MSD) Results	X
Laboratory Control Sample (LCS) Results	X
Method Specific Quality Control (QC) Results *	2
System Performance	X
Field Quality Control Results #	3
Other	X

X Acceptable, no qualification necessary NR Not required
See validation summary comment NA Not applicable
*) The reviewer has indicated in the comments, if necessary, the method specific QC results included in the data package that were reviewed.
#) Field QC may include field duplicates, trip blanks, rinse blanks, field blanks, and equipment blank samples as required by project specific criteria.

Data for the above samples are:

- ☐ Acceptable for use
- ☒ Acceptable for use as qualified
- ☐ Unacceptable for use

Is action required by the Project Manager?

Yes ☐ No ☒

Data Validation Summary Comments:

1. **Laboratory Blank Result** – Acetone (6.7 J µg/l) and Tetrachloroethene (0.25 J µg/l) were detected in the method blank for QC batch 1413767 and QC batch 1413689, respectively. Carbon disulfide (0.31 J µg/l) was detected in the method blank for QC batch 1413809. Carbon disulfide was not detected in any of the investigative samples. Therefore, qualification was not necessary. The affected samples and the data validation qualifier results are shown in the following table.

Sample Identification	Parameter	Reported Result	Data Validation Result
FD2	Acetone	15 J	100UB
MW101A		14 J	100UB
MW101B		14 J	100UB
MW101C		15 J	100UB
MW133B		14 J	100UB
MW-119	Tetrachloroethene	0.28 J	1UB
MW-130		0.56 J	1UB
MW-47		0.36 J	1UB

2. **Method Specific Quality Control (QC) Results** - The corresponding CCV for this analytical batch had a recovery exceeding the upper control limit of the method for chloromethane. Chloromethane was not detected in any of the investigative samples. Therefore, qualification was not necessary.

3. **Field Quality Control Samples** – Methylene Chloride (0.58 J µg/l) was detected in the trip blank. The affected samples and the data validation qualifier results are shown in the following table.

Sample Identification	Parameter	Reported Result	Data Validation Result
MW-124	Methylene Chloride	1.8 J	12UB
MW-136		0.39 J	5UB

The relative percent difference (RPD) is not necessarily calculated if both the primary and duplicate results are not five times greater than the reporting limit. However, the RPD between the investigative and duplicate samples was less than or equal to 33% when comparing detected concentrations. Qualification is not necessary.

OVERALL ASSESSMENT OF DATA

The TriMatrix Work Order Report # 1411479 is 100 percent complete. The data usability is based on EPA's guidance documents. No problems were identified with reported data and analytical performance was within specified limits. The data are acceptable and meet the project's data quality objectives.

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW16**	Sampled:	11/24/14 11:47
Lab Sample ID:	**1411479-30**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/05/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/05/14 15:56 By: DLV
QC Batch:	1413767	Analytical Batch:	4L05035

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	**0.62J**	1.0	0.14
74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	**45**	1.0	0.13
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.17
75-35-4	1,1-Dichloroethene	**8.6**	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	**12**	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	**1.1**	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	5.0U	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By

Date 1/16/15

Continued on next page

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW16**	Sampled:	11/24/14 11:47
Lab Sample ID:	**1411479-30**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/05/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/05/14 15:56 By: DLV
QC Batch:	1413767	Analytical Batch:	4L05035

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
127-18-4	Tetrachloroethene	**4.2**	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	**50**	1.0	0.080
79-00-5	1,1,2-Trichloroethane	**0.54J**	1.0	0.11
79-01-6	Trichloroethene	**17**	1.0	0.10
75-01-4	Vinyl Chloride	1.0U	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*107*	*85-118*
1,2-Dichloroethane-d4	*102*	*87-122*
Toluene-d8	*99*	*85-113*
4-Bromofluorobenzene	*95*	*82-110*

VALIDATED

Reviewed By

Date 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW47**	Sampled:	11/23/14 09:34
Lab Sample ID:	**1411479-09**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/04/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/04/14 14:33 By: DLV
QC Batch:	1413689	Analytical Batch:	4L04033

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	1.0U	1.0	0.14
*74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	**0.23J**	1.0	0.13
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.17
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	1.0U	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	5.0U	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By

Date 1/16/15

Continued on next page

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7462 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**		
Project:	SE Rockford, Il Site	Description:	Laboratory Services		
Client Sample ID:	**MW47**	Sampled:	11/23/14 09:34		
Lab Sample ID:	**1411479-09**	Sampled By:	Patrick Egan		
Matrix:	Water	Received:	11/26/14 09:30		
Unit:	ug/L	Prepared:	12/04/14 07:00	By:	DLV
Dilution Factor:	1	Analyzed:	12/04/14 14:33	By:	DLV
QC Batch:	1413689	Analytical Batch:	4L04033		

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
*127-18-4	Tetrachloroethene	**0.36J**	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	1.0U	1.0	0.080
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.11
79-01-6	Trichloroethene	1.0U	1.0	0.10
75-01-4	Vinyl Chloride	1.0U	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*101*	*85-118*
1,2-Dichloroethane-d4	*101*	*87-122*
Toluene-d8	*98*	*85-113*
4-Bromofluorobenzene	*95*	*82-110*

VALIDATED

Reviewed By [signature]

Date 1/16/15

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7462 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW101A**	Sampled:	11/24/14 14:20
Lab Sample ID:	**1411479-33**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/05/14 07:00 By: DLV
Dilution Factor:	5	Analyzed:	12/05/14 18:18 By: DLV
QC Batch:	1413767	Analytical Batch:	4L05035

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
*67-64-1	Acetone	**14J**	100	7.8
71-43-2	Benzene	5.0U	5.0	1.0
74-97-5	Bromochloromethane	5.0U	5.0	0.74
75-27-4	Bromodichloromethane	5.0U	5.0	0.65
75-25-2	Bromoform	5.0U	5.0	0.92
74-83-9	Bromomethane	5.0U	5.0	1.1
75-15-0	Carbon Disulfide	25U	25	0.52
56-23-5	Carbon Tetrachloride	5.0U	5.0	0.78
108-90-7	Chlorobenzene	5.0U	5.0	1.0
75-00-3	Chloroethane	5.0U	5.0	1.2
67-66-3	Chloroform	**3.6J**	5.0	0.69
74-87-3	Chloromethane	5.0U	5.0	1.3
96-12-8	1,2-Dibromo-3-chloropropane	5.0U	5.0	1.4
124-48-1	Dibromochloromethane	5.0U	5.0	0.52
106-93-4	1,2-Dibromoethane	5.0U	5.0	0.56
95-50-1	1,2-Dichlorobenzene	5.0U	5.0	1.0
541-73-1	1,3-Dichlorobenzene	5.0U	5.0	0.51
106-46-7	1,4-Dichlorobenzene	5.0U	5.0	1.0
75-34-3	1,1-Dichloroethane	**270**	5.0	0.63
107-06-2	1,2-Dichloroethane	5.0U	5.0	0.87
75-35-4	1,1-Dichloroethene	**64**	5.0	1.1
156-59-2	cis-1,2-Dichloroethene	**520**	5.0	0.67
156-60-5	trans-1,2-Dichloroethene	**25**	5.0	1.3
78-87-5	1,2-Dichloropropane	5.0U	5.0	0.73
10061-01-5	cis-1,3-Dichloropropene	5.0U	5.0	0.68
10061-02-6	trans-1,3-Dichloropropene	5.0U	5.0	1.0
100-41-4	Ethylbenzene	5.0U	5.0	1.0
591-78-6	2-Hexanone	25U	25	1.7
75-09-2	Methylene Chloride	25U	25	1.7
78-93-3	2-Butanone (MEK)	25U	25	2.6
108-10-1	4-Methyl-2-pentanone (MIBK)	25U	25	2.0

VALIDATED

Reviewed By

Date 1/16/15

Continued on next page

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**		
Project:	SE Rockford, Il Site	Description:	Laboratory Services		
Client Sample ID:	**MW101A**	Sampled:	11/24/14 14:20		
Lab Sample ID:	**1411479-33**	Sampled By:	Patrick Egan		
Matrix:	Water	Received:	11/26/14 09:30		
Unit:	ug/L	Prepared:	12/05/14 07:00	By:	DLV
Dilution Factor:	5	Analyzed:	12/05/14 18:18	By:	DLV
QC Batch:	1413767	Analytical Batch:	4L05035		

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	5.0U	5.0	0.56
79-34-5	1,1,2,2-Tetrachloroethane	5.0U	5.0	0.70
127-18-4	Tetrachloroethene	**71**	5.0	0.67
108-88-3	Toluene	5.0U	5.0	1.0
71-55-6	1,1,1-Trichloroethane	**670**	5.0	0.40
79-00-5	1,1,2-Trichloroethane	**1.9J**	5.0	0.57
79-01-6	Trichloroethene	**150**	5.0	0.52
75-01-4	Vinyl Chloride	5.0U	5.0	0.80
1330-20-7	Xylene (Total)	15U	15	1.7

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*109*	*85-118*
1,2-Dichloroethane-d4	*102*	*87-122*
Toluene-d8	*100*	*85-113*
4-Bromofluorobenzene	*94*	*82-110*

VALIDATED

Reviewed By _____

Date 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**FD2**	Sampled:	11/24/14 14:22
Lab Sample ID:	**1411479-34** MW-101A field duplicate	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/05/14 07:00 By: DLV
Dilution Factor:	5	Analyzed:	12/05/14 18:47 By: DLV
QC Batch:	1413767	Analytical Batch:	4L05035

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
*67-64-1	Acetone	**15J**	100	7.8
71-43-2	Benzene	5.0U	5.0	1.0
74-97-5	Bromochloromethane	5.0U	5.0	0.74
75-27-4	Bromodichloromethane	5.0U	5.0	0.65
75-25-2	Bromoform	5.0U	5.0	0.92
74-83-9	Bromomethane	5.0U	5.0	1.1
75-15-0	Carbon Disulfide	25U	25	0.52
56-23-5	Carbon Tetrachloride	5.0U	5.0	0.78
108-90-7	Chlorobenzene	5.0U	5.0	1.0
75-00-3	Chloroethane	5.0U	5.0	1.2
67-66-3	Chloroform	**3.5J**	5.0	0.69
74-87-3	Chloromethane	5.0U	5.0	1.3
96-12-8	1,2-Dibromo-3-chloropropane	5.0U	5.0	1.4
124-48-1	Dibromochloromethane	5.0U	5.0	0.52
106-93-4	1,2-Dibromoethane	5.0U	5.0	0.56
95-50-1	1,2-Dichlorobenzene	5.0U	5.0	1.0
541-73-1	1,3-Dichlorobenzene	5.0U	5.0	0.51
106-46-7	1,4-Dichlorobenzene	5.0U	5.0	1.0
75-34-3	1,1-Dichloroethane	**270**	5.0	0.63
107-06-2	1,2-Dichloroethane	5.0U	5.0	0.87
75-35-4	1,1-Dichloroethene	**50**	5.0	1.1
156-59-2	cis-1,2-Dichloroethene	**510**	5.0	0.67
156-60-5	trans-1,2-Dichloroethene	**35**	5.0	1.3
78-87-5	1,2-Dichloropropane	5.0U	5.0	0.73
10061-01-5	cis-1,3-Dichloropropene	5.0U	5.0	0.68
10061-02-6	trans-1,3-Dichloropropene	5.0U	5.0	1.0
100-41-4	Ethylbenzene	5.0U	5.0	1.0
591-78-6	2-Hexanone	25U	25	1.7
75-09-2	Methylene Chloride	25U	25	1.7
78-93-3	2-Butanone (MEK)	25U	25	2.6
108-10-1	4-Methyl-2-pentanone (MIBK)	25U	25	2.0

VALIDATED

Reviewed By

Date 1/16/15

Continued on next page

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**FD2**	Sampled:	11/24/14 14:22
Lab Sample ID:	**1411479-34** MW-101A field duplicate	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/05/14 07:00 By: DLV
Dilution Factor:	5	Analyzed:	12/05/14 18:47 By: DLV
QC Batch:	1413767	Analytical Batch:	4L05035

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	5.0U	5.0	0.56
79-34-5	1,1,2,2-Tetrachloroethane	5.0U	5.0	0.70
127-18-4	Tetrachloroethene	**71**	5.0	0.67
108-88-3	Toluene	5.0U	5.0	1.0
71-55-6	1,1,1-Trichloroethane	**670**	5.0	0.40
79-00-5	1,1,2-Trichloroethane	**1.9J**	5.0	0.57
79-01-6	Trichloroethene	**150**	5.0	0.52
75-01-4	Vinyl Chloride	5.0U	5.0	0.80
1330-20-7	Xylene (Total)	15U	15	1.7

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*108*	*85-118*
1,2-Dichloroethane-d4	*102*	*87-122*
Toluene-d8	*100*	*85-113*
4-Bromofluorobenzene	*94*	*82-110*

VALIDATED

Reviewed By _____

Date 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE ▲ Grand Rapids, MI 49512 ▲ 616.975.4500 ▲ Fax 616.942.7463 ▲ www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW101B**	Sampled:	11/24/14 13:53
Lab Sample ID:	**1411479-32**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/05/14 07:00 By: DLV
Dilution Factor:	5	Analyzed:	12/05/14 17:50 By: DLV
QC Batch:	1413767	Analytical Batch:	4L05035

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
*67-64-1	Acetone	**14J**	100	7.8
71-43-2	Benzene	5.0U	5.0	1.0
74-97-5	Bromochloromethane	5.0U	5.0	0.74
75-27-4	Bromodichloromethane	5.0U	5.0	0.65
75-25-2	Bromoform	5.0U	5.0	0.92
74-83-9	Bromomethane	5.0U	5.0	1.1
75-15-0	Carbon Disulfide	25U	25	0.52
56-23-5	Carbon Tetrachloride	5.0U	5.0	0.78
108-90-7	Chlorobenzene	5.0U	5.0	1.0
75-00-3	Chloroethane	5.0U	5.0	1.2
67-66-3	Chloroform	**1.9J**	5.0	0.69
74-87-3	Chloromethane	5.0U	5.0	1.3
96-12-8	1,2-Dibromo-3-chloropropane	5.0U	5.0	1.4
124-48-1	Dibromochloromethane	5.0U	5.0	0.52
106-93-4	1,2-Dibromoethane	5.0U	5.0	0.56
95-50-1	1,2-Dichlorobenzene	5.0U	5.0	1.0
541-73-1	1,3-Dichlorobenzene	5.0U	5.0	0.51
106-46-7	1,4-Dichlorobenzene	5.0U	5.0	1.0
75-34-3	1,1-Dichloroethane	**150**	5.0	0.63
107-06-2	1,2-Dichloroethane	5.0U	5.0	0.87
75-35-4	1,1-Dichloroethene	**30**	5.0	1.1
156-59-2	cis-1,2-Dichloroethene	**26**	5.0	0.67
156-60-5	trans-1,2-Dichloroethene	**5.3**	5.0	1.3
78-87-5	1,2-Dichloropropane	5.0U	5.0	0.73
10061-01-5	cis-1,3-Dichloropropene	5.0U	5.0	0.68
10061-02-6	trans-1,3-Dichloropropene	5.0U	5.0	1.0
100-41-4	Ethylbenzene	5.0U	5.0	1.0
591-78-6	2-Hexanone	25U	25	1.7
75-09-2	Methylene Chloride	25U	25	1.7
78-93-3	2-Butanone (MEK)	25U	25	2.6
108-10-1	4-Methyl-2-pentanone (MIBK)	25U	25	2.0

VALIDATED

Reviewed By

Date 1/16/15

Continued on next page

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**		
Project:	SE Rockford, Il Site	Description:	Laboratory Services		
Client Sample ID:	**MW101B**	Sampled:	11/24/14 13:53		
Lab Sample ID:	**1411479-32**	Sampled By:	Patrick Egan		
Matrix:	Water	Received:	11/26/14 09:30		
Unit:	ug/L	Prepared:	12/05/14 07:00	By:	DLV
Dilution Factor:	5	Analyzed:	12/05/14 17:50	By:	DLV
QC Batch:	1413767	Analytical Batch:	4L05035		

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	5.0U	5.0	0.56
79-34-5	1,1,2,2-Tetrachloroethane	5.0U	5.0	0.70
127-18-4	Tetrachloroethene	**31**	5.0	0.67
108-88-3	Toluene	5.0U	5.0	1.0
71-55-6	1,1,1-Trichloroethane	**530**	5.0	0.40
79-00-5	1,1,2-Trichloroethane	5.0U	5.0	0.57
79-01-6	Trichloroethene	**30**	5.0	0.52
75-01-4	Vinyl Chloride	5.0U	5.0	0.80
1330-20-7	Xylene (Total)	15U	15	1.7

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*108*	*85-118*
1,2-Dichloroethane-d4	*102*	*87-122*
Toluene-d8	*99*	*85-113*
4-Bromofluorobenzene	*95*	*82-110*

VALIDATED

Reviewed By _____

Date 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7462 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**	
Project:	SE Rockford, Il Site	Description:	Laboratory Services	
Client Sample ID:	**MW101C**	Sampled:	11/24/14 15:18	
Lab Sample ID:	**1411479-36**	Sampled By:	Patrick Egan	
Matrix:	Water	Received:	11/26/14 09:30	
Unit:	ug/L	Prepared:	12/05/14 07:00	By: DLV
Dilution Factor:	5	Analyzed:	12/05/14 19:15	By: DLV
QC Batch:	1413767	Analytical Batch:	4L05035	

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
*67-64-1	Acetone	**15J**	100	7.8
71-43-2	Benzene	5.0U	5.0	1.0
74-97-5	Bromochloromethane	5.0U	5.0	0.74
75-27-4	Bromodichloromethane	5.0U	5.0	0.65
75-25-2	Bromoform	5.0U	5.0	0.92
74-83-9	Bromomethane	5.0U	5.0	1.1
75-15-0	Carbon Disulfide	25U	25	0.52
56-23-5	Carbon Tetrachloride	5.0U	5.0	0.78
108-90-7	Chlorobenzene	5.0U	5.0	1.0
75-00-3	Chloroethane	5.0U	5.0	1.2
67-66-3	Chloroform	**1.7J**	5.0	0.69
74-87-3	Chloromethane	5.0U	5.0	1.3
96-12-8	1,2-Dibromo-3-chloropropane	5.0U	5.0	1.4
124-48-1	Dibromochloromethane	5.0U	5.0	0.52
106-93-4	1,2-Dibromoethane	5.0U	5.0	0.56
95-50-1	1,2-Dichlorobenzene	5.0U	5.0	1.0
541-73-1	1,3-Dichlorobenzene	5.0U	5.0	0.51
106-46-7	1,4-Dichlorobenzene	5.0U	5.0	1.0
75-34-3	1,1-Dichloroethane	**120**	5.0	0.63
107-06-2	1,2-Dichloroethane	5.0U	5.0	0.87
75-35-4	1,1-Dichloroethene	**25**	5.0	1.1
156-59-2	cis-1,2-Dichloroethene	**27**	5.0	0.67
156-60-5	trans-1,2-Dichloroethene	**4.4J**	5.0	1.3
78-87-5	1,2-Dichloropropane	5.0U	5.0	0.73
10061-01-5	cis-1,3-Dichloropropene	5.0U	5.0	0.68
10061-02-6	trans-1,3-Dichloropropene	5.0U	5.0	1.0
100-41-4	Ethylbenzene	5.0U	5.0	1.0
591-78-6	2-Hexanone	25U	25	1.7
75-09-2	Methylene Chloride	25U	25	1.7
78-93-3	2-Butanone (MEK)	25U	25	2.6
108-10-1	4-Methyl-2-pentanone (MIBK)	25U	25	2.0

VALIDATED

Reviewed By [signature]

Date 1/16/15

Continued on next page

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc
Individual sample results relate only to the sample tested.

5550 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW101C**	Sampled:	11/24/14 15:18
Lab Sample ID:	**1411479-36**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/05/14 07:00 By: DLV
Dilution Factor:	5	Analyzed:	12/05/14 19:15 By: DLV
QC Batch:	1413767	Analytical Batch:	4L05035

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	5.0U	5.0	0.56
79-34-5	1,1,2,2-Tetrachloroethane	5.0U	5.0	0.70
127-18-4	Tetrachloroethene	**25**	5.0	0.67
108-88-3	Toluene	5.0U	5.0	1.0
71-55-6	1,1,1-Trichloroethane	**430**	5.0	0.40
79-00-5	1,1,2-Trichloroethane	5.0U	5.0	0.57
79-01-6	Trichloroethene	**20**	5.0	0.52
75-01-4	Vinyl Chloride	5.0U	5.0	0.80
1330-20-7	Xylene (Total)	15U	15	1.7

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*109*	*85-118*
1,2-Dichloroethane-d4	*102*	*87-122*
Toluene-d8	*100*	*85-113*
4-Bromofluorobenzene	*95*	*82-110*

VALIDATED

Reviewed By _____

Date 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**	
Project:	SE Rockford, Il Site	Description:	Laboratory Services	
Client Sample ID:	**MW101D**	Sampled:	11/24/14 14:57	
Lab Sample ID:	**1411479-35**	Sampled By:	Patrick Egan	
Matrix:	Water	Received:	11/26/14 09:30	
Unit:	ug/L	Prepared:	12/05/14 07:00	By: DLV
Dilution Factor:	1	Analyzed:	12/05/14 16:53	By: DLV
QC Batch:	1413767	Analytical Batch:	4L05035	

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	**0.71J**	1.0	0.14
74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	**53**	1.0	0.13
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.17
75-35-4	1,1-Dichloroethene	**14**	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	**63**	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	**2.0**	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	5.0U	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By

Date 1/16/15

Continued on next page

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW101D**	Sampled:	11/24/14 14:57
Lab Sample ID:	**1411479-35**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/05/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/05/14 16:53 By: DLV
QC Batch:	1413767	Analytical Batch:	4L05035

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
127-18-4	Tetrachloroethene	**9.6**	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	**90**	1.0	0.080
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.11
79-01-6	Trichloroethene	**15**	1.0	0.10
75-01-4	Vinyl Chloride	**0.28J**	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*108*	*85-118*
1,2-Dichloroethane-d4	*101*	*87-122*
Toluene-d8	*100*	*85-113*
4-Bromofluorobenzene	*96*	*82-110*

VALIDATED

Reviewed By

Date 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5568 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.247.7462 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**		
Project:	SE Rockford, Il Site	Description:	Laboratory Services		
Client Sample ID:	**MW102A**	Sampled:	11/24/14 09:20		
Lab Sample ID:	**1411479-23**	Sampled By:	Patrick Egan		
Matrix:	Water	Received:	11/26/14 09:30		
Unit:	ug/L	Prepared:	12/05/14 07:00	By:	DLV
Dilution Factor:	1	Analyzed:	12/05/14 13:15	By:	DLV
QC Batch:	1413809	Analytical Batch:	4L08003		

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	1.0U	1.0	0.14
*74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	**2.5**	1.0	0.13
107-06-2	1,2-Dichloroethane	**0.61J**	1.0	0.17
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	**3.4**	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	5.0U	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By

Date 1/16/15

Continued on next page

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW102A**	Sampled:	11/24/14 09:20
Lab Sample ID:	**1411479-23**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/05/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/05/14 13:15 By: DLV
QC Batch:	1413809	Analytical Batch:	4L08003

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
127-18-4	Tetrachloroethene	1.0U	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	1.0U	1.0	0.080
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.11
79-01-6	Trichloroethene	1.0U	1.0	0.10
75-01-4	Vinyl Chloride	**1.3**	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*103*	*85-118*
1,2-Dichloroethane-d4	*100*	*87-122*
Toluene-d8	*101*	*85-113*
4-Bromofluorobenzene	*91*	*82-110*

VALIDATED

Reviewed By _____

Date 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7162 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**		
Project:	SE Rockford, Il Site	Description:	Laboratory Services		
Client Sample ID:	**MW102B**	Sampled:	11/24/14 08:55		
Lab Sample ID:	**1411479-22**	Sampled By:	Patrick Egan		
Matrix:	Water	Received:	11/26/14 09:30		
Unit:	ug/L	Prepared:	12/05/14 07:00	By:	DLV
Dilution Factor:	1	Analyzed:	12/05/14 12:49	By:	DLV
QC Batch:	1413809	Analytical Batch:	4L08003		

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	1.0U	1.0	0.14
*74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	**2.6**	1.0	0.13
107-06-2	1,2-Dichloroethane	**0.80J**	1.0	0.17
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	**3.5**	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	5.0U	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By

Date 1/16/15

Continued on next page

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**		
Project:	SE Rockford, Il Site	Description:	Laboratory Services		
Client Sample ID:	**MW102B**	Sampled:	11/24/14 08:55		
Lab Sample ID:	**1411479-22**	Sampled By:	Patrick Egan		
Matrix:	Water	Received:	11/26/14 09:30		
Unit:	ug/L	Prepared:	12/05/14 07:00	By:	DLV
Dilution Factor:	1	Analyzed:	12/05/14 12:49	By:	DLV
QC Batch:	1413809	Analytical Batch:	4L08003		

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
127-18-4	Tetrachloroethene	1.0U	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	1.0U	1.0	0.080
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.11
79-01-6	Trichloroethene	1.0U	1.0	0.10
75-01-4	Vinyl Chloride	**1.2**	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*101*	*85-118*
1,2-Dichloroethane-d4	*103*	*87-122*
Toluene-d8	*101*	*85-113*
4-Bromofluorobenzene	*94*	*82-110*

VALIDATED

Reviewed By _____

Date 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7162 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**	
Project:	SE Rockford, Il Site	Description:	Laboratory Services	
Client Sample ID:	**MW102C**	Sampled:	11/24/14 08:28	
Lab Sample ID:	**1411479-21**	Sampled By:	Patrick Egan	
Matrix:	Water	Received:	11/26/14 09:30	
Unit:	ug/L	Prepared:	12/05/14 07:00	By: DLV
Dilution Factor:	1	Analyzed:	12/05/14 15:27	By: DLV
QC Batch:	1413767	Analytical Batch:	4L05035	

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	1.0U	1.0	0.14
74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	**1.0**	1.0	0.13
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.17
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	**1.4**	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	5.0U	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By: [signature]

Date: 1/16/15

Continued on next page

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW102C**	Sampled:	11/24/14 08:28
Lab Sample ID:	**1411479-21**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/05/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/05/14 15:27 By: DLV
QC Batch:	1413767	Analytical Batch:	4L05035

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
127-18-4	Tetrachloroethene	1.0U	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	**0.26J**	1.0	0.080
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.11
79-01-6	Trichloroethene	1.0U	1.0	0.10
75-01-4	Vinyl Chloride	1.0U	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*101*	*85-118*
1,2-Dichloroethane-d4	*101*	*87-122*
Toluene-d8	*99*	*85-113*
4-Bromofluorobenzene	*95*	*82-110*

VALIDATED

Reviewed By: [signature]

Date: 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5550 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7462 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW113A**	Sampled:	11/24/14 13:19
Lab Sample ID:	**1411479-28**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/05/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/05/14 15:01 By: DLV
QC Batch:	1413809	Analytical Batch:	4L08003

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	**1.3**	1.0	0.14
*74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	**140**	1.0	0.13
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.17
75-35-4	1,1-Dichloroethene	**18**	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	**31**	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	**5.2**	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	5.0U	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By

Date 1/16/15

Continued on next page

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax: 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**		
Project:	SE Rockford, Il Site	Description:	Laboratory Services		
Client Sample ID:	**MW113A**	Sampled:	11/24/14 13:19		
Lab Sample ID:	**1411479-28**	Sampled By:	Patrick Egan		
Matrix:	Water	Received:	11/26/14 09:30		
Unit:	ug/L	Prepared:	12/05/14 07:00	By:	DLV
Dilution Factor:	1	Analyzed:	12/05/14 15:01	By:	DLV
QC Batch:	1413809	Analytical Batch:	4L08003		

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
127-18-4	Tetrachloroethene	**11**	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	**140**	1.0	0.080
79-00-5	1,1,2-Trichloroethane	**0.96J**	1.0	0.11
79-01-6	Trichloroethene	**50**	1.0	0.10
75-01-4	Vinyl Chloride	1.0U	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*103*	*85-118*
1,2-Dichloroethane-d4	*98*	*87-122*
Toluene-d8	*99*	*85-113*
4-Bromofluorobenzene	*91*	*82-110*

VALIDATED

Reviewed By _____

Date 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW113B**	Sampled:	11/24/14 12:50
Lab Sample ID:	**1411479-27**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/05/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/05/14 14:34 By: DLV
QC Batch:	1413809	Analytical Batch:	4L08003

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	**0.40J**	1.0	0.14
*74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	**66**	1.0	0.13
107-06-2	1,2-Dichloroethane	**0.52J**	1.0	0.17
75-35-4	1,1-Dichloroethene	**15**	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	**55**	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	**2.2**	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	5.0U	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By

Date 1/16/15

Continued on next page

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7462 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW113B**	Sampled:	11/24/14 12:50
Lab Sample ID:	**1411479-27**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/05/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/05/14 14:34 By: DLV
QC Batch:	1413809	Analytical Batch:	4L08003

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
127-18-4	Tetrachloroethene	**2.1**	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	**13**	1.0	0.080
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.11
79-01-6	Trichloroethene	**22**	1.0	0.10
75-01-4	Vinyl Chloride	**13**	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*101*	*85-118*
1,2-Dichloroethane-d4	*97*	*87-122*
Toluene-d8	*99*	*85-113*
4-Bromofluorobenzene	*94*	*82-110*

VALIDATED

Reviewed By: [signature]

Date: 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW114A**	Sampled:	11/24/14 11:22
Lab Sample ID:	**1411479-29**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/05/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/05/14 15:27 By: DLV
QC Batch:	1413809	Analytical Batch:	4L08003

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	1.0U	1.0	0.14
*74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	**4.6**	1.0	0.13
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.17
75-35-4	1,1-Dichloroethene	**4.9**	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	**4.1**	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	5.0U	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By

Date 1/16/15

Continued on next page

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW114A**	Sampled:	11/24/14 11:22
Lab Sample ID:	**1411479-29**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/05/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/05/14 15:27 By: DLV
QC Batch:	1413809	Analytical Batch:	4L08003

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
127-18-4	Tetrachloroethene	**0.27J**	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	**38**	1.0	0.080
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.11
79-01-6	Trichloroethene	**3.1**	1.0	0.10
75-01-4	Vinyl Chloride	1.0U	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*104*	*85-118*
1,2-Dichloroethane-d4	*101*	*87-122*
Toluene-d8	*101*	*85-113*
4-Bromofluorobenzene	*93*	*82-110*

VALIDATED

Reviewed By

Date 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5550 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.947.7462 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW114B**	Sampled:	11/24/14 12:16
Lab Sample ID:	**1411479-31**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/05/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/05/14 16:24 By: DLV
QC Batch:	1413767	Analytical Batch:	4L05035

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	1.0U	1.0	0.14
74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	**1.4**	1.0	0.13
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.17
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	**1.0**	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	5.0U	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By

Date 1/16/15

Continued on next page

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5550 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**		
Project:	SE Rockford, Il Site	Description:	Laboratory Services		
Client Sample ID:	**MW114B**	Sampled:	11/24/14 12:16		
Lab Sample ID:	**1411479-31**	Sampled By:	Patrick Egan		
Matrix:	Water	Received:	11/26/14 09:30		
Unit:	ug/L	Prepared:	12/05/14 07:00	By:	DLV
Dilution Factor:	1	Analyzed:	12/05/14 16:24	By:	DLV
QC Batch:	1413767	Analytical Batch:	4L05035		

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
127-18-4	Tetrachloroethene	**0.28J**	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	**0.24J**	1.0	0.080
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.11
79-01-6	Trichloroethene	**4.0**	1.0	0.10
75-01-4	Vinyl Chloride	1.0U	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*102*	*85-118*
1,2-Dichloroethane-d4	*102*	*87-122*
Toluene-d8	*100*	*85-113*
4-Bromofluorobenzene	*95*	*82-110*

VALIDATED

Reviewed By: [signature]

Date: 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW117B**	Sampled:	11/21/14 12:15
Lab Sample ID:	**1411479-01**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/03/14 09:00 By: DLV
Dilution Factor:	1	Analyzed:	12/03/14 17:46 By: DLV
QC Batch:	1413656	Analytical Batch:	4L04002

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	**0.30J**	1.0	0.14
74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	**11**	1.0	0.13
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.17
75-35-4	1,1-Dichloroethene	**3.7**	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	**0.82J**	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	5.0U	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By: [signature]

Date: 1/6/15

Continued on next page

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW117B**	Sampled:	11/21/14 12:15
Lab Sample ID:	**1411479-01**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/03/14 09:00 By: DLV
Dilution Factor:	1	Analyzed:	12/03/14 17:46 By: DLV
QC Batch:	1413656	Analytical Batch:	4L04002

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
127-18-4	Tetrachloroethene	**4.8**	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	**7.9**	1.0	0.080
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.11
79-01-6	Trichloroethene	**4.4**	1.0	0.10
75-01-4	Vinyl Chloride	1.0U	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*108*	*85-118*
1,2-Dichloroethane-d4	*103*	*87-122*
Toluene-d8	*102*	*85-113*
4-Bromofluorobenzene	*97*	*82-110*

VALIDATED

Reviewed By: [signature]

Date: 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW117C**	Sampled:	11/21/14 12:43
Lab Sample ID:	**1411479-02**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/03/14 09:00 By: DLV
Dilution Factor:	1	Analyzed:	12/03/14 18:15 By: DLV
QC Batch:	1413656	Analytical Batch:	4L04002

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	**0.29J**	1.0	0.14
74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	**39**	1.0	0.13
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.17
75-35-4	1,1-Dichloroethene	**13**	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	**4.5**	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	5.0U	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By

Date 1/16/15

Continued on next page

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7162 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW117C**	Sampled:	11/21/14 12:43
Lab Sample ID:	**1411479-02**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/03/14 09:00 By: DLV
Dilution Factor:	1	Analyzed:	12/03/14 18:15 By: DLV
QC Batch:	1413656	Analytical Batch:	4L04002

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
127-18-4	Tetrachloroethene	**22**	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	**25**	1.0	0.080
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.11
79-01-6	Trichloroethene	**12**	1.0	0.10
75-01-4	Vinyl Chloride	1.0U	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	*% Recovery*	*Control Limits*
Dibromofluoromethane	*111*	*85-118*
1,2-Dichloroethane-d4	*105*	*87-122*
Toluene-d8	*103*	*85-113*
4-Bromofluorobenzene	*98*	*82-110*

VALIDATED

Reviewed By [signature]

Date 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**		
Project:	SE Rockford, Il Site	Description:	Laboratory Services		
Client Sample ID:	**MW117D**	Sampled:	11/22/14 11:27		
Lab Sample ID:	**1411479-03**	Sampled By:	Patrick Egan		
Matrix:	Water	Received:	11/26/14 09:30		
Unit:	ug/L	Prepared:	12/03/14 09:00	By:	DLV
Dilution Factor:	1	Analyzed:	12/03/14 18:43	By:	DLV
QC Batch:	1413656	Analytical Batch:	4L04002		

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	**0.28J**	1.0	0.14
74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	**48**	1.0	0.13
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.17
75-35-4	1,1-Dichloroethene	**12**	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	**2.3**	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	5.0U	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By

Date 1/16/15

Continued on next page

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7462 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**		
Project:	SE Rockford, Il Site	Description:	Laboratory Services		
Client Sample ID:	**MW117D**	Sampled:	11/22/14 11:27		
Lab Sample ID:	**1411479-03**	Sampled By:	Patrick Egan		
Matrix:	Water	Received:	11/26/14 09:30		
Unit:	ug/L	Prepared:	12/03/14 09:00	By:	DLV
Dilution Factor:	1	Analyzed:	12/03/14 18:43	By:	DLV
QC Batch:	1413656	Analytical Batch:	4L04002		

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
127-18-4	Tetrachloroethene	**18**	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	**35**	1.0	0.080
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.11
79-01-6	Trichloroethene	**10**	1.0	0.10
75-01-4	Vinyl Chloride	1.0U	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*112*	*85-118*
1,2-Dichloroethane-d4	*105*	*87-122*
Toluene-d8	*103*	*85-113*
4-Bromofluorobenzene	*98*	*82-110*

VALIDATED

Reviewed By

Date 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7167 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW119**	Sampled:	11/22/14 14:16
Lab Sample ID:	**1411479-08**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/04/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/04/14 14:07 By: DLV
QC Batch:	1413689	Analytical Batch:	4L04033

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	**0.29J**	1.0	0.14
*74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	**1.4**	1.0	0.13
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.17
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	**0.47J**	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	5.0U	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By _____

Date 1/16/15

Continued on next page

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW119**	Sampled:	11/22/14 14:16
Lab Sample ID:	**1411479-08**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/04/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/04/14 14:07 By: DLV
QC Batch:	1413689	Analytical Batch:	4L04033

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
*127-18-4	Tetrachloroethene	**0.28J**	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	**1.6**	1.0	0.080
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.11
79-01-6	Trichloroethene	**0.46J**	1.0	0.10
75-01-4	Vinyl Chloride	1.0U	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*104*	*85-118*
1,2-Dichloroethane-d4	*102*	*87-122*
Toluene-d8	*102*	*85-113*
4-Bromofluorobenzene	*93*	*82-110*

VALIDATED

Reviewed By [signature]

Date 1/16/15

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW121**	Sampled:	11/23/14 14:25
Lab Sample ID:	**1411479-14**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/04/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/04/14 16:45 By: DLV
QC Batch:	1413689	Analytical Batch:	4L04033

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	**0.84J**	1.0	0.14
*74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	**42**	1.0	0.13
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.17
75-35-4	1,1-Dichloroethene	**8.7**	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	**6.4**	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	**0.92J**	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	5.0U	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By: [signature]

Date: 1/16/15

Continued on next page

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7162 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW121**	Sampled:	11/23/14 14:25
Lab Sample ID:	**1411479-14**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/04/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/04/14 16:45 By: DLV
QC Batch:	1413689	Analytical Batch:	4L04033

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
127-18-4	Tetrachloroethene	**1.6**	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	**20**	1.0	0.080
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.11
79-01-6	Trichloroethene	**25**	1.0	0.10
75-01-4	Vinyl Chloride	1.0U	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*103*	*85-118*
1,2-Dichloroethane-d4	*97*	*87-122*
Toluene-d8	*99*	*85-113*
4-Bromofluorobenzene	*93*	*82-110*

VALIDATED

Reviewed By: [signature]

Date: 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5568 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW124**	Sampled:	11/23/14 15:05
Lab Sample ID:	**1411479-15**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/04/14 07:00 By: DLV
Dilution Factor:	2.5	Analyzed:	12/04/14 17:12 By: DLV
QC Batch:	1413689	Analytical Batch:	4L04033

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	50U	50	3.9
71-43-2	Benzene	2.5U	2.5	0.50
74-97-5	Bromochloromethane	2.5U	2.5	0.37
75-27-4	Bromodichloromethane	2.5U	2.5	0.32
75-25-2	Bromoform	2.5U	2.5	0.46
74-83-9	Bromomethane	2.5U	2.5	0.54
75-15-0	Carbon Disulfide	12U	12	0.26
56-23-5	Carbon Tetrachloride	2.5U	2.5	0.39
108-90-7	Chlorobenzene	2.5U	2.5	0.50
75-00-3	Chloroethane	**22**	2.5	0.58
67-66-3	Chloroform	2.5U	2.5	0.34
*74-87-3	Chloromethane	2.5U	2.5	0.66
96-12-8	1,2-Dibromo-3-chloropropane	2.5U	2.5	0.70
124-48-1	Dibromochloromethane	2.5U	2.5	0.26
106-93-4	1,2-Dibromoethane	2.5U	2.5	0.28
95-50-1	1,2-Dichlorobenzene	2.5U	2.5	0.50
541-73-1	1,3-Dichlorobenzene	2.5U	2.5	0.26
106-46-7	1,4-Dichlorobenzene	2.5U	2.5	0.50
75-34-3	1,1-Dichloroethane	**420**	2.5	0.32
107-06-2	1,2-Dichloroethane	2.5U	2.5	0.44
75-35-4	1,1-Dichloroethene	**10**	2.5	0.56
156-59-2	cis-1,2-Dichloroethene	**130**	2.5	0.34
156-60-5	trans-1,2-Dichloroethene	**1.2J**	2.5	0.67
78-87-5	1,2-Dichloropropane	2.5U	2.5	0.36
10061-01-5	cis-1,3-Dichloropropene	2.5U	2.5	0.34
10061-02-6	trans-1,3-Dichloropropene	2.5U	2.5	0.50
100-41-4	Ethylbenzene	2.5U	2.5	0.50
591-78-6	2-Hexanone	12U	12	0.87
75-09-2	Methylene Chloride	**1.8J**	12	0.86
78-93-3	2-Butanone (MEK)	12U	12	1.3
108-10-1	4-Methyl-2-pentanone (MIBK)	12U	12	1.0

VALIDATED

Reviewed By [signature]

Date 1/16/15

Continued on next page

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**		
Project:	SE Rockford, Il Site	Description:	Laboratory Services		
Client Sample ID:	**MW124**	Sampled:	11/23/14 15:05		
Lab Sample ID:	**1411479-15**	Sampled By:	Patrick Egan		
Matrix:	Water	Received:	11/26/14 09:30		
Unit:	ug/L	Prepared:	12/04/14 07:00	By:	DLV
Dilution Factor:	2.5	Analyzed:	12/04/14 17:12	By:	DLV
QC Batch:	1413689	Analytical Batch:	4L04033		

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	2.5U	2.5	0.28
79-34-5	1,1,2,2-Tetrachloroethane	2.5U	2.5	0.35
127-18-4	Tetrachloroethene	**7.8**	2.5	0.34
108-88-3	Toluene	2.5U	2.5	0.50
71-55-6	1,1,1-Trichloroethane	**41**	2.5	0.20
79-00-5	1,1,2-Trichloroethane	2.5U	2.5	0.28
79-01-6	Trichloroethene	**4.9**	2.5	0.26
75-01-4	Vinyl Chloride	**31**	2.5	0.40
1330-20-7	Xylene (Total)	7.5U	7.5	0.85

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*100*	*85-118*
1,2-Dichloroethane-d4	*99*	*87-122*
Toluene-d8	*100*	*85-113*
4-Bromofluorobenzene	*93*	*82-110*

VALIDATED

Reviewed By [signature]

Date 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW130**	Sampled:	11/23/14 15:36
Lab Sample ID:	**1411479-16**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/04/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/04/14 17:38 By: DLV
QC Batch:	1413689	Analytical Batch:	4L04033

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	**0.34J**	1.0	0.14
*74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	**12**	1.0	0.13
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.17
75-35-4	1,1-Dichloroethene	**1.5**	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	**2.5**	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	5.0U	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By

Date 1/16/15

Continued on next page

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlab.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**		
Project:	SE Rockford, Il Site	Description:	Laboratory Services		
Client Sample ID:	**MW130**	Sampled:	11/23/14 15:36		
Lab Sample ID:	**1411479-16**	Sampled By:	Patrick Egan		
Matrix:	Water	Received:	11/26/14 09:30		
Unit:	ug/L	Prepared:	12/04/14 07:00	By:	DLV
Dilution Factor:	1	Analyzed:	12/04/14 17:38	By:	DLV
QC Batch:	1413689	Analytical Batch:	4L04033		

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
*127-18-4	Tetrachloroethene	**0.56J**	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	**9.3**	1.0	0.080
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.11
79-01-6	Trichloroethene	**1.8**	1.0	0.10
75-01-4	Vinyl Chloride	1.0U	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*103*	*85-118*
1,2-Dichloroethane-d4	*100*	*87-122*
Toluene-d8	*102*	*85-113*
4-Bromofluorobenzene	*94*	*82-110*

VALIDATED

Reviewed By [signature]

Date 1/16/15

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW133A**	Sampled:	11/24/14 09:42
Lab Sample ID:	**1411479-24**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/05/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/05/14 13:42 By: DLV
QC Batch:	1413809	Analytical Batch:	4L08003

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	1.0U	1.0	0.14
*74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	1.0U	1.0	0.13
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.17
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	1.0U	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	5.0U	5.0	0.35
78-93-3	2-Butanone (MEK)	**2.3J**	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By

Date 1/16/15

Continued on next page

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5559 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7462 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW133A**	Sampled:	11/24/14 09:42
Lab Sample ID:	**1411479-24**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/05/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/05/14 13:42 By: DLV
QC Batch:	1413809	Analytical Batch:	4L08003

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
127-18-4	Tetrachloroethene	1.0U	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	1.0U	1.0	0.080
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.11
79-01-6	Trichloroethene	1.0U	1.0	0.10
75-01-4	Vinyl Chloride	1.0U	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	*% Recovery*	*Control Limits*
Dibromofluoromethane	*104*	*85-118*
1,2-Dichloroethane-d4	*100*	*87-122*
Toluene-d8	*101*	*85-113*
4-Bromofluorobenzene	*92*	*82-110*

VALIDATED

Reviewed By

Date 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5550 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7462 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**	
Project:	SE Rockford, Il Site	Description:	Laboratory Services	
Client Sample ID:	**MW133B**	Sampled:	11/24/14 10:12	
Lab Sample ID:	**1411479-25**	Sampled By:	Patrick Egan	
Matrix:	Water	Received:	11/26/14 09:30	
Unit:	ug/L	Prepared:	12/05/14 07:00	By: DLV
Dilution Factor:	5	Analyzed:	12/05/14 17:21	By: DLV
QC Batch:	1413767	Analytical Batch:	4L05035	

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
*67-64-1	Acetone	**14J**	100	7.8
71-43-2	Benzene	5.0U	5.0	1.0
74-97-5	Bromochloromethane	5.0U	5.0	0.74
75-27-4	Bromodichloromethane	5.0U	5.0	0.65
75-25-2	Bromoform	5.0U	5.0	0.92
74-83-9	Bromomethane	5.0U	5.0	1.1
75-15-0	Carbon Disulfide	25U	25	0.52
56-23-5	Carbon Tetrachloride	5.0U	5.0	0.78
108-90-7	Chlorobenzene	5.0U	5.0	1.0
75-00-3	Chloroethane	5.0U	5.0	1.2
67-66-3	Chloroform	**4.4J**	5.0	0.69
74-87-3	Chloromethane	5.0U	5.0	1.3
96-12-8	1,2-Dibromo-3-chloropropane	5.0U	5.0	1.4
124-48-1	Dibromochloromethane	5.0U	5.0	0.52
106-93-4	1,2-Dibromoethane	5.0U	5.0	0.56
95-50-1	1,2-Dichlorobenzene	5.0U	5.0	1.0
541-73-1	1,3-Dichlorobenzene	5.0U	5.0	0.51
106-46-7	1,4-Dichlorobenzene	5.0U	5.0	1.0
75-34-3	1,1-Dichloroethane	**170**	5.0	0.63
107-06-2	1,2-Dichloroethane	5.0U	5.0	0.87
75-35-4	1,1-Dichloroethene	**48**	5.0	1.1
156-59-2	cis-1,2-Dichloroethene	**160**	5.0	0.67
156-60-5	trans-1,2-Dichloroethene	**12**	5.0	1.3
78-87-5	1,2-Dichloropropane	5.0U	5.0	0.73
10061-01-5	cis-1,3-Dichloropropene	5.0U	5.0	0.68
10061-02-6	trans-1,3-Dichloropropene	5.0U	5.0	1.0
100-41-4	Ethylbenzene	5.0U	5.0	1.0
591-78-6	2-Hexanone	25U	25	1.7
75-09-2	Methylene Chloride	25U	25	1.7
78-93-3	2-Butanone (MEK)	25U	25	2.6
108-10-1	4-Methyl-2-pentanone (MIBK)	25U	25	2.0

VALIDATED

Reviewed By

Date 1/16/15

Continued on next page

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**		
Project:	SE Rockford, Il Site	Description:	Laboratory Services		
Client Sample ID:	**MW133B**	Sampled:	11/24/14 10:12		
Lab Sample ID:	**1411479-25**	Sampled By:	Patrick Egan		
Matrix:	Water	Received:	11/26/14 09:30		
Unit:	ug/L	Prepared:	12/05/14 07:00	By:	DLV
Dilution Factor:	5	Analyzed:	12/05/14 17:21	By:	DLV
QC Batch:	1413767	Analytical Batch:	4L05035		

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	5.0U	5.0	0.56
79-34-5	1,1,2,2-Tetrachloroethane	5.0U	5.0	0.70
127-18-4	Tetrachloroethene	**78**	5.0	0.67
108-88-3	Toluene	5.0U	5.0	1.0
71-55-6	1,1,1-Trichloroethane	**480**	5.0	0.40
79-00-5	1,1,2-Trichloroethane	**2.0J**	5.0	0.57
79-01-6	Trichloroethene	**68**	5.0	0.52
75-01-4	Vinyl Chloride	5.0U	5.0	0.80
1330-20-7	Xylene (Total)	15U	15	1.7

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*107*	*85-118*
1,2-Dichloroethane-d4	*101*	*87-122*
Toluene-d8	*99*	*85-113*
4-Bromofluorobenzene	*94*	*82-110*

VALIDATED

Reviewed By [signature]

Date 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW133C**	Sampled:	11/24/14 10:39
Lab Sample ID:	**1411479-26**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/05/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/05/14 14:08 By: DLV
QC Batch:	1413809	Analytical Batch:	4L08003

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	**5.8**	1.0	0.14
*74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	**58**	1.0	0.13
107-06-2	1,2-Dichloroethane	**1.3**	1.0	0.17
75-35-4	1,1-Dichloroethene	**47**	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	**130**	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	**2.2**	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	5.0U	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By: [signature]

Date: 1/16/15

Continued on next page

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7162 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**		
Project:	SE Rockford, Il Site	Description:	Laboratory Services		
Client Sample ID:	**MW133C**	Sampled:	11/24/14 10:39		
Lab Sample ID:	**1411479-26**	Sampled By:	Patrick Egan		
Matrix:	Water	Received:	11/26/14 09:30		
Unit:	ug/L	Prepared:	12/05/14 07:00	By:	DLV
Dilution Factor:	1	Analyzed:	12/05/14 14:08	By:	DLV
QC Batch:	1413809	Analytical Batch:	4L08003		

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
127-18-4	Tetrachloroethene	**6.6**	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	**150**	1.0	0.080
79-00-5	1,1,2-Trichloroethane	**1.3**	1.0	0.11
79-01-6	Trichloroethene	**83**	1.0	0.10
75-01-4	Vinyl Chloride	1.0U	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*105*	*85-118*
1,2-Dichloroethane-d4	*99*	*87-122*
Toluene-d8	*100*	*85-113*
4-Bromofluorobenzene	*95*	*82-110*

VALIDATED

Reviewed By: [signature]

Date: 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW136**	Sampled:	11/23/14 16:44
Lab Sample ID:	**1411479-18**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/05/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/05/14 11:04 By: DLV
QC Batch:	1413809	Analytical Batch:	4L08003

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	**0.58J**	1.0	0.14
*74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	1.0U	1.0	0.13
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.17
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	1.0U	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	**0.39J**	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By

Date 1/16/15

Continued on next page

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5568 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**	
Project:	SE Rockford, Il Site	Description:	Laboratory Services	
Client Sample ID:	**MW136**	Sampled:	11/23/14 16:44	
Lab Sample ID:	**1411479-18**	Sampled By:	Patrick Egan	
Matrix:	Water	Received:	11/26/14 09:30	
Unit:	ug/L	Prepared:	12/05/14 07:00	By: DLV
Dilution Factor:	1	Analyzed:	12/05/14 11:04	By: DLV
QC Batch:	1413809	Analytical Batch:	4L08003	

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
127-18-4	Tetrachloroethene	1.0U	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	1.0U	1.0	0.080
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.11
79-01-6	Trichloroethene	1.0U	1.0	0.10
75-01-4	Vinyl Chloride	1.0U	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	*% Recovery*	*Control Limits*
Dibromofluoromethane	*104*	*85-118*
1,2-Dichloroethane-d4	*97*	*87-122*
Toluene-d8	*99*	*85-113*
4-Bromofluorobenzene	*94*	*82-110*

VALIDATED

Reviewed By _____

Date 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW200**	Sampled:	11/23/14 16:16
Lab Sample ID:	**1411479-17**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/05/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/05/14 10:38 By: DLV
QC Batch:	1413809	Analytical Batch:	4L08003

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	1.0U	1.0	0.14
*74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	1.0U	1.0	0.13
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.17
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	1.0U	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	5.0U	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By [signature]

Date 1/16/15

Continued on next page

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7462 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW200**	Sampled:	11/23/14 16:16
Lab Sample ID:	**1411479-17**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/05/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/05/14 10:38 By: DLV
QC Batch:	1413809	Analytical Batch:	4L08003

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
127-18-4	Tetrachloroethene	1.0U	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	1.0U	1.0	0.080
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.11
79-01-6	Trichloroethene	1.0U	1.0	0.10
75-01-4	Vinyl Chloride	1.0U	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	*% Recovery*	*Control Limits*
Dibromofluoromethane	*100*	*85-118*
1,2-Dichloroethane-d4	*98*	*87-122*
Toluene-d8	*99*	*85-113*
4-Bromofluorobenzene	*94*	*82-110*

VALIDATED

Reviewed By _____

Date 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Ct. SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW201**	Sampled:	11/23/14 13:47
Lab Sample ID:	**1411479-12**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/04/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/04/14 15:53 By: DLV
QC Batch:	1413689	Analytical Batch:	4L04033

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	1.0U	1.0	0.14
*74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	**6.5**	1.0	0.13
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.17
75-35-4	1,1-Dichloroethene	**0.83J**	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	**3.2**	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	5.0U	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By

Date 1/16/15

Continued on next page

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW201**	Sampled:	11/23/14 13:47
Lab Sample ID:	**1411479-12**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/04/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/04/14 15:53 By: DLV
QC Batch:	1413689	Analytical Batch:	4L04033

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
127-18-4	Tetrachloroethene	**1.7**	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	**18**	1.0	0.080
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.11
79-01-6	Trichloroethene	**1.4**	1.0	0.10
75-01-4	Vinyl Chloride	1.0U	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*102*	*85-118*
1,2-Dichloroethane-d4	*101*	*87-122*
Toluene-d8	*99*	*85-113*
4-Bromofluorobenzene	*94*	*82-110*

VALIDATED

Reviewed By _____

Date 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**FD1**	Sampled:	11/23/14 13:50
Lab Sample ID:	**1411479-13** MW-201 Field duplicate	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/04/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/04/14 16:19 By: DLV
QC Batch:	1413689	Analytical Batch:	4L04033

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	1.0U	1.0	0.14
*74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	**6.1**	1.0	0.13
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.17
75-35-4	1,1-Dichloroethene	**0.82J**	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	**2.8**	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	5.0U	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By

Date 1/16/15

Continued on next page

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7462 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**FD1**	Sampled:	11/23/14 13:50
Lab Sample ID:	**1411479-13** MW-201 field duplicate	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/04/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/04/14 16:19 By: DLV
QC Batch:	1413689	Analytical Batch:	4L04033

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
127-18-4	Tetrachloroethene	**1.5**	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	**18**	1.0	0.080
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.11
79-01-6	Trichloroethene	**1.2**	1.0	0.10
75-01-4	Vinyl Chloride	1.0U	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*102*	*85-118*
1,2-Dichloroethane-d4	*99*	*87-122*
Toluene-d8	*99*	*85-113*
4-Bromofluorobenzene	*94*	*82-110*

VALIDATED

Reviewed By _____

Date 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7462 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW202**	Sampled:	11/24/14 07:53
Lab Sample ID:	**1411479-20**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/05/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/05/14 11:57 By: DLV
QC Batch:	1413809	Analytical Batch:	4L08003

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	1.0U	1.0	0.14
*74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	**0.43J**	1.0	0.13
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.17
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	1.0U	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	5.0U	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By

Date 1/16/15

Continued on next page

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW202**	Sampled:	11/24/14 07:53
Lab Sample ID:	**1411479-20**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/05/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/05/14 11:57 By: DLV
QC Batch:	1413809	Analytical Batch:	4L08003

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
127-18-4	Tetrachloroethene	**0.97J**	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	1.0U	1.0	0.080
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.11
79-01-6	Trichloroethene	**0.35J**	1.0	0.10
75-01-4	Vinyl Chloride	1.0U	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*103*	*85-118*
1,2-Dichloroethane-d4	*100*	*87-122*
Toluene-d8	*102*	*85-113*
4-Bromofluorobenzene	*95*	*82-110*

VALIDATED

Reviewed By: [signature]

Date: 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW203**	Sampled:	11/24/14 07:26
Lab Sample ID:	**1411479-19**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/05/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/05/14 11:30 By: DLV
QC Batch:	1413809	Analytical Batch:	4L08003

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	1.0U	1.0	0.14
*74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	1.0U	1.0	0.13
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.17
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	1.0U	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	5.0U	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By

Date 1/16/15

Continued on next page

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax: 616.947.7462 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW203**	Sampled:	11/24/14 07:26
Lab Sample ID:	**1411479-19**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/05/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/05/14 11:30 By: DLV
QC Batch:	1413809	Analytical Batch:	4L08003

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
127-18-4	Tetrachloroethene	**4.1**	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	**0.24J**	1.0	0.080
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.11
79-01-6	Trichloroethene	1.0U	1.0	0.10
75-01-4	Vinyl Chloride	1.0U	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*105*	*85-118*
1,2-Dichloroethane-d4	*98*	*87-122*
Toluene-d8	*101*	*85-113*
4-Bromofluorobenzene	*94*	*82-110*

VALIDATED

Reviewed By _____

Date 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5568 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7167 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW204**	Sampled:	11/23/14 11:41
Lab Sample ID:	**1411479-11**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/04/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/04/14 15:26 By: DLV
QC Batch:	1413689	Analytical Batch:	4L04033

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	**0.38J**	1.0	0.14
*74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	**9.8**	1.0	0.13
107-06-2	1,2-Dichloroethane	**0.94J**	1.0	0.17
75-35-4	1,1-Dichloroethene	**16**	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	**40**	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	**0.78J**	1.0	0.27
78-87-5	1,2-Dichloropropane	**0.71J**	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	5.0U	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By

Date 1/16/15

Continued on next page

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**		
Project:	SE Rockford, Il Site	Description:	Laboratory Services		
Client Sample ID:	**MW204**	Sampled:	11/23/14 11:41		
Lab Sample ID:	**1411479-11**	Sampled By:	Patrick Egan		
Matrix:	Water	Received:	11/26/14 09:30		
Unit:	ug/L	Prepared:	12/04/14 07:00	By:	DLV
Dilution Factor:	1	Analyzed:	12/04/14 15:26	By:	DLV
QC Batch:	1413689	Analytical Batch:	4L04033		

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
*127-18-4	Tetrachloroethene	**1.4**	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	**10**	1.0	0.080
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.11
79-01-6	Trichloroethene	**51**	1.0	0.10
75-01-4	Vinyl Chloride	1.0U	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*104*	*85-118*
1,2-Dichloroethane-d4	*101*	*87-122*
Toluene-d8	*100*	*85-113*
4-Bromofluorobenzene	*95*	*82-110*

VALIDATED

Reviewed By [signature]

Date 1/16/15

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**	
Project:	SE Rockford, Il Site	Description:	Laboratory Services	
Client Sample ID:	**MW205A**	Sampled:	11/22/14 11:58	
Lab Sample ID:	**1411479-04**	Sampled By:	Patrick Egan	
Matrix:	Water	Received:	11/26/14 09:30	
Unit:	ug/L	Prepared:	12/03/14 09:00	By: DLV
Dilution Factor:	1	Analyzed:	12/03/14 19:12	By: DLV
QC Batch:	1413656	Analytical Batch:	4L04002	

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	**0.29J**	1.0	0.14
74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	**36**	1.0	0.13
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.17
75-35-4	1,1-Dichloroethene	**12**	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	**2.7**	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	5.0U	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By: [signature]

Date: 1/16/15

Continued on next page

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**		
Project:	SE Rockford, Il Site	Description:	Laboratory Services		
Client Sample ID:	**MW205A**	Sampled:	11/22/14 11:58		
Lab Sample ID:	**1411479-04**	Sampled By:	Patrick Egan		
Matrix:	Water	Received:	11/26/14 09:30		
Unit:	ug/L	Prepared:	12/03/14 09:00	By:	DLV
Dilution Factor:	1	Analyzed:	12/03/14 19:12	By:	DLV
QC Batch:	1413656	Analytical Batch:	4L04002		

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
127-18-4	Tetrachloroethene	**22**	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	**27**	1.0	0.080
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.11
79-01-6	Trichloroethene	**14**	1.0	0.10
75-01-4	Vinyl Chloride	1.0U	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*111*	*85-118*
1,2-Dichloroethane-d4	*106*	*87-122*
Toluene-d8	*104*	*85-113*
4-Bromofluorobenzene	*98*	*82-110*

VALIDATED

Reviewed By _____

Date 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7462 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**	
Project:	SE Rockford, Il Site	Description:	Laboratory Services	
Client Sample ID:	**MW205B**	Sampled:	11/22/14 12:20	
Lab Sample ID:	**1411479-05**	Sampled By:	Patrick Egan	
Matrix:	Water	Received:	11/26/14 09:30	
Unit:	ug/L	Prepared:	12/03/14 09:00	By: DLV
Dilution Factor:	1	Analyzed:	12/03/14 19:40	By: DLV
QC Batch:	1413656	Analytical Batch:	4L04002	

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	**0.30J**	1.0	0.14
74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	**38**	1.0	0.13
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.17
75-35-4	1,1-Dichloroethene	**13**	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	**4.1**	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	5.0U	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By: [signature]

Date: 1/16/15

Continued on next page

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW205B**	Sampled:	11/22/14 12:20
Lab Sample ID:	**1411479-05**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/03/14 09:00 By: DLV
Dilution Factor:	1	Analyzed:	12/03/14 19:40 By: DLV
QC Batch:	1413656	Analytical Batch:	4L04002

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
127-18-4	Tetrachloroethene	**23**	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	**28**	1.0	0.080
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.11
79-01-6	Trichloroethene	**14**	1.0	0.10
75-01-4	Vinyl Chloride	1.0U	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*111*	*85-118*
1,2-Dichloroethane-d4	*107*	*87-122*
Toluene-d8	*103*	*85-113*
4-Bromofluorobenzene	*97*	*82-110*

VALIDATED

Reviewed By [signature]

Date 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7162 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW206A**	Sampled:	11/22/14 13:26
Lab Sample ID:	**1411479-07**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/04/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/04/14 13:41 By: DLV
QC Batch:	1413689	Analytical Batch:	4L04033

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	**0.50J**	1.0	0.14
*74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	**7.2**	1.0	0.13
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.17
75-35-4	1,1-Dichloroethene	**3.0**	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	**1.2**	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	5.0U	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By [signature]

Date 1/16/15

Continued on next page

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7462 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**	
Project:	SE Rockford, Il Site	Description:	Laboratory Services	
Client Sample ID:	**MW206A**	Sampled:	11/22/14 13:26	
Lab Sample ID:	**1411479-07**	Sampled By:	Patrick Egan	
Matrix:	Water	Received:	11/26/14 09:30	
Unit:	ug/L	Prepared:	12/04/14 07:00	By: DLV
Dilution Factor:	1	Analyzed:	12/04/14 13:41	By: DLV
QC Batch:	1413689	Analytical Batch:	4L04033	

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
127-18-4	Tetrachloroethene	**5.0**	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	**6.7**	1.0	0.080
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.11
79-01-6	Trichloroethene	**4.5**	1.0	0.10
75-01-4	Vinyl Chloride	1.0U	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*103*	*85-118*
1,2-Dichloroethane-d4	*96*	*87-122*
Toluene-d8	*100*	*85-113*
4-Bromofluorobenzene	*94*	*82-110*

VALIDATED

Reviewed By [signature]

Date 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7162 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW206B**	Sampled:	11/22/14 12:49
Lab Sample ID:	**1411479-06**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/03/14 09:00 By: DLV
Dilution Factor:	1	Analyzed:	12/03/14 20:09 By: DLV
QC Batch:	1413656	Analytical Batch:	4L04002

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	**0.82J**	1.0	0.14
74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	**44**	1.0	0.13
107-06-2	1,2-Dichloroethane	**1.2**	1.0	0.17
75-35-4	1,1-Dichloroethene	**60**	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	**120**	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	**0.36J**	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	5.0U	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By

Date 1/16/15

Continued on next page

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5550 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW206B**	Sampled:	11/22/14 12:49
Lab Sample ID:	**1411479-06**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/03/14 09:00 By: DLV
Dilution Factor:	1	Analyzed:	12/03/14 20:09 By: DLV
QC Batch:	1413656	Analytical Batch:	4L04002

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
127-18-4	Tetrachloroethene	**20**	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	**46**	1.0	0.080
79-00-5	1,1,2-Trichloroethane	**3.1**	1.0	0.11
79-01-6	Trichloroethene	**38**	1.0	0.10
75-01-4	Vinyl Chloride	**0.39J**	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*112*	*85-118*
1,2-Dichloroethane-d4	*105*	*87-122*
Toluene-d8	*103*	*85-113*
4-Bromofluorobenzene	*97*	*82-110*

VALIDATED

Reviewed By [signature]

Date 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7462 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**MW207**	Sampled:	11/23/14 10:15
Lab Sample ID:	**1411479-10**	Sampled By:	Patrick Egan
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/04/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/04/14 15:00 By: DLV
QC Batch:	1413689	Analytical Batch:	4L04033

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	**0.28J**	1.0	0.14
*74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	**1.8**	1.0	0.13
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.17
75-35-4	1,1-Dichloroethene	**0.58J**	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	**1.2**	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	5.0U	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By

Date 1/16/15

Continued on next page

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**		
Project:	SE Rockford, Il Site	Description:	Laboratory Services		
Client Sample ID:	**MW207**	Sampled:	11/23/14 10:15		
Lab Sample ID:	**1411479-10**	Sampled By:	Patrick Egan		
Matrix:	Water	Received:	11/26/14 09:30		
Unit:	ug/L	Prepared:	12/04/14 07:00	By:	DLV
Dilution Factor:	1	Analyzed:	12/04/14 15:00	By:	DLV
QC Batch:	1413689	Analytical Batch:	4L04033		

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
*127-18-4	Tetrachloroethene	**1.4**	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	**2.3**	1.0	0.080
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.11
79-01-6	Trichloroethene	**4.0**	1.0	0.10
75-01-4	Vinyl Chloride	1.0U	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*102*	*85-118*
1,2-Dichloroethane-d4	*100*	*87-122*
Toluene-d8	*100*	*85-113*
4-Bromofluorobenzene	*94*	*82-110*

VALIDATED

Reviewed By

Date 1/16/15

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7162 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**
Project:	SE Rockford, Il Site	Description:	Laboratory Services
Client Sample ID:	**Trip Blank TML3399**	Sampled:	11/24/14 00:00
Lab Sample ID:	**1411479-37**	Sampled By:	TML
Matrix:	Water	Received:	11/26/14 09:30
Unit:	ug/L	Prepared:	12/05/14 07:00 By: DLV
Dilution Factor:	1	Analyzed:	12/05/14 10:11 By: DLV
QC Batch:	1413809	Analytical Batch:	4L08003

Volatile Organic Compounds by EPA Method 8260B

CAS Number	Analyte	Analytical Result	RL	MDL
67-64-1	Acetone	20U	20	1.6
71-43-2	Benzene	1.0U	1.0	0.20
74-97-5	Bromochloromethane	1.0U	1.0	0.15
75-27-4	Bromodichloromethane	1.0U	1.0	0.13
75-25-2	Bromoform	1.0U	1.0	0.18
74-83-9	Bromomethane	1.0U	1.0	0.22
75-15-0	Carbon Disulfide	5.0U	5.0	0.10
56-23-5	Carbon Tetrachloride	1.0U	1.0	0.16
108-90-7	Chlorobenzene	1.0U	1.0	0.20
75-00-3	Chloroethane	1.0U	1.0	0.23
67-66-3	Chloroform	1.0U	1.0	0.14
*74-87-3	Chloromethane	1.0U	1.0	0.26
96-12-8	1,2-Dibromo-3-chloropropane	1.0U	1.0	0.28
124-48-1	Dibromochloromethane	1.0U	1.0	0.10
106-93-4	1,2-Dibromoethane	1.0U	1.0	0.11
95-50-1	1,2-Dichlorobenzene	1.0U	1.0	0.20
541-73-1	1,3-Dichlorobenzene	1.0U	1.0	0.10
106-46-7	1,4-Dichlorobenzene	1.0U	1.0	0.20
75-34-3	1,1-Dichloroethane	1.0U	1.0	0.13
107-06-2	1,2-Dichloroethane	1.0U	1.0	0.17
75-35-4	1,1-Dichloroethene	1.0U	1.0	0.22
156-59-2	cis-1,2-Dichloroethene	1.0U	1.0	0.13
156-60-5	trans-1,2-Dichloroethene	1.0U	1.0	0.27
78-87-5	1,2-Dichloropropane	1.0U	1.0	0.15
10061-01-5	cis-1,3-Dichloropropene	1.0U	1.0	0.14
10061-02-6	trans-1,3-Dichloropropene	1.0U	1.0	0.20
100-41-4	Ethylbenzene	1.0U	1.0	0.20
591-78-6	2-Hexanone	5.0U	5.0	0.35
75-09-2	Methylene Chloride	**0.58J**	5.0	0.35
78-93-3	2-Butanone (MEK)	5.0U	5.0	0.52
108-10-1	4-Methyl-2-pentanone (MIBK)	5.0U	5.0	0.41

VALIDATED

Reviewed By

Date 1/16/15

Continued on next page

*See Statement of Data Qualifications

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7462 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

ANALYTICAL REPORT

Client:	**Nationwide Environmental Services, Inc.**	Work Order:	**1411479**		
Project:	SE Rockford, Il Site	Description:	Laboratory Services		
Client Sample ID:	**Trip Blank TML3399**	Sampled:	11/24/14 00:00		
Lab Sample ID:	**1411479-37**	Sampled By:	TML		
Matrix:	Water	Received:	11/26/14 09:30		
Unit:	ug/L	Prepared:	12/05/14 07:00	By:	DLV
Dilution Factor:	1	Analyzed:	12/05/14 10:11	By:	DLV
QC Batch:	1413809	Analytical Batch:	4L08003		

Volatile Organic Compounds by EPA Method 8260B (Continued)

CAS Number	Analyte	Analytical Result	RL	MDL
100-42-5	Styrene	1.0U	1.0	0.11
79-34-5	1,1,2,2-Tetrachloroethane	1.0U	1.0	0.14
127-18-4	Tetrachloroethene	1.0U	1.0	0.13
108-88-3	Toluene	1.0U	1.0	0.20
71-55-6	1,1,1-Trichloroethane	1.0U	1.0	0.080
79-00-5	1,1,2-Trichloroethane	1.0U	1.0	0.11
79-01-6	Trichloroethene	1.0U	1.0	0.10
75-01-4	Vinyl Chloride	1.0U	1.0	0.16
1330-20-7	Xylene (Total)	3.0U	3.0	0.34

Surrogates:	***% Recovery***	***Control Limits***
Dibromofluoromethane	*104*	*85-118*
1,2-Dichloroethane-d4	*101*	*87-122*
Toluene-d8	*101*	*85-113*
4-Bromofluorobenzene	*94*	*82-110*

VALIDATED

Reviewed By: [signature]

Date: 1/16/15

This report shall not be reproduced, except in full, without written authorization of TriMatrix Laboratories, Inc.
Individual sample results relate only to the sample tested.

5560 Corporate Exchange Court SE • Grand Rapids, MI 49512 • 616.975.4500 • Fax 616.942.7463 • www.trimatrixlabs.com

TRIMATRIX LABORATORIES

5560 Corporate Exchange Court SE
Grand Rapids, MI 49512
Phone (616) 975-4500 Fax (616) 942-7463
www.trimatrixlabs.com

Chain of Custody Record

COC No. 150035

Pg. 1 of 4

For Lab Use Only
Cart: —
VOA Rack/Tray: Box 317678
Receipt Log No.: 2110
Project Chemist:
Work Order No.: 1411419

Client Name: Nationwide Env. Svcs
Address: 14818 6th Ave Ste 5A
City, State Zip: Golden CO
Phone/Fax:
Email: 303 232 2134

Project Name: SE Rock
Client Project No. / P.O. No.:
Invoice To: ☐ Client ☐ Other (comments)
Contact/Report To: B Cafiamme

Analyses Requested: Hg per list

PRESERVATIVES
A NONE pH~7
B HNO_3 pH<2
C H_2SO_4 pH<2
D 1+1 HCl pH<2
E NaOH pH>12
F ZnAc/NaOH pH>9
G MeOH
H Other (note below)

Schedule	Matrix Code	Sample Number	Field Sample ID	Cooler ID	Sample Date	Sample Time	COMP	GRAB	Matrix	Number of Containers Submitted	Total	Sample Comments
		01	1 MW117B	Tm 2548	11/21	1215		X	GW	3	3	
		02	2 MW117C		11/21	1243		X	GW	3	3	
		03	3 MW117D		11/22	1127		X	GW	3	3	
		04	4 MW205A		11/22	1158		X	GW	3	3	
		05	5 MW205B		11/22	1220		X	GW	3	3	
		06	6 MW206B		11/22	1249		X	GW	3	3	
		07	7 MW206A		11/22	1326		X	GW	3	3	
		08	8 MW119		11/22	1416		X	GW	3	3	
		09	9 MW47		11/23	934		X	GW	3	3	
		10	10 MW207		11/23	1015		X	GW	3	3	

Sampled By (print): Patrick Egan
Sampler's Signature: [signature]
Company: AEG

How Shipped? Hand ___ Carrier Fedex
Tracking No. 7119 7983 3699

Comments: All Samples Kept in Secure Location @ 4°C

1. Relinquished By	Date	Time	2. Relinquished By	Date	Time	3. Relinquished By	Date	Time
[signature]	11/24/14	1930				[signature]	11/20/14	0930
1. Received By	Date	Time	2. Received By	Date	Time	3. Received for Lab By	Date	Time

WHITE COPY - REPORT YELLOW COPY - LABORATORY PINK COPY - FIELD

1016-2.D.3.7

TRIMATRIX LABORATORIES

5560 Corporate Exchange Court SE
Grand Rapids, MI 49512
Phone (616) 975-4500 Fax (616) 942-7463
www.trimatrixlabs.com

Chain of Custody Record

COC No. 150036

Pg. 2 of 4

For Lab Use Only
Cart:
VOA Rack/Tray:
Receipt Log No. 2110
Project Chemist:
Work Order No. 1411479

Client Name: Nationwide Env Svcs
Address: 14818 6th Ave Ste 5A
City, State Zip: Golden CO
Phone/Fax: 303 232 2134
Email:

Project Name: SE Rock
Client Project No. / P.O. No.:
Invoice To: ☐ Client ☐ Other (comments)
Contact/Report To: B Lohmann

Analyses Requested: VOC per Test

Preservatives: A NONE pH~7; B HNO_3 pH<2; C H_2SO_4 pH<2; D 1+1 HCl pH<2; E NaOH pH>12; F ZnAc/NaOH pH>9; G MeOH; H Other (note below)

Container Type (corresponds to Container Packing List)

Schedule	Matrix Code	Sample Number	Field Sample ID	Cooler ID	Sample Date	Sample Time	COMP	GRAB	Matrix	Number of Containers Submitted	Total	Sample Comments
		11	1 MW204	Tm 2548	11/23	1141		x	GW	3	3	
		12	2 MW201		11/23	1347		x	GW	3	3	
		13	3 FD1		11/23	1350		x	GW	3	3	
		14	4 MW121		11/23	1425		x	GW	3	3	
		15	5 MW124		11/23	1505		x	GW	3	3	
		16	6 MW130		11/23	1536		x	GW	3	3	
		17	7 MW200		11/23	1616		x	GW	3	3	
		18	8 MW136		11/23	1644		x	GW	3	3	
		19	9 MW203		11/24	726		x	GW	3	3	
		20	10 MW202		11/24	753		x	GW	3	3	

Sampler By (print): Patrick Egan
Sampler's Signature:
Company: AEE

How Shipped? Hand ___ Carrier Fedex
Tracking No. 771979833699

1. Relinquished By: Date 11/24/14 Time 1930
1. Received By: Date Time

Comments: All Samples Kept in Secure Location @ 4°C

2. Relinquished By: Date Time
2. Received By: Date Time

3. Relinquished By: Date Time
3. Received By: Date 11/24/14 Time 0930

WHITE COPY - REPORT YELLOW COPY - LABORATORY PINK COPY - FIELD

TRIMATRIX LABORATORIES

5560 Corporate Exchange Court SE
Grand Rapids, MI 49512
Phone (616) 975-4500 Fax (616) 942-7463
www.trimatrixlabs.com

Chain of Custody Record

COC No. 150037

Pg. 3 of 4

Analyses Requested

For Lab Use Only		
Cart		
VOA Rack/Tray	Client Name: Nationwide Env Svcs	Project Name: SE Rock
Receipt Log No. 2110	Address: 14818 6th Ave Ste 5A	Client Project No. / P.O. No.
Project Chemist	City, State Zip: Golden CO	Invoice To: ☐ Client ☐ Other (comments)
Work Order No. 1411479	Phone/Fax: Email 303 232 2134	Contact/Report To: B LaHamme

D VOC per list

Container Type (corresponds to Container Packing List)

⇦ PRESERVATIVES
A NONE pH~7
B HNO_3 pH<2
C H_2SO_4 pH<2
D 1+1 HCl pH<2
E NaOH pH>12
F ZnAc/NaOH pH>9
G MeOH
H Other (note below)

Schedule	Matrix Code	Sample Number	Field Sample ID	Cooler ID	Sample Date	Sample Time	COMP	GRAB	Matrix	Number of Containers Submitted	Total	Sample Comments
		21	1 MW102C	Tm 3399	11/24	828		X	GW	3	3	
		22	2 MW102B		11/24	855		X	GW	3	3	
		23	3 MW102A		11/24	920		X	GW	3	3	
		24	4 MW133A		11/24	942		X	GW	3	3	
		25	5 MW133B		11/24	1012		X	GW	3	3	
		26	6 MW133C		11/24	1039		X	GW	3	3	
		27	7 MW113B		11/24	1250		X	GW	3	3	
		28	8 MW113A		11/24	1319		X	GW	3	3	
		29	9 MW114A		11/24	1122		X	GW	3	3	
		30	10 MW16		11/24	1147		X	GW	3	3	

Sampled By (print): Patrick Egan
Sampler's Signature: [signature]
Company: AEE

How Shipped? Hand ___ Carrier Fedex
Tracking No. 7719 9984 9448

Comments: All samples kept in secure location at 4°C

1. Relinquished By	Date	Time	2. Relinquished By	Date	Time	3. Relinquished By	Date	Time
[signature]	11/24/14	1930						

1. Received By	Date	Time	2. Received By	Date	Time	3. Received For Lab By	Date	Time
						[signature]	11/26/14	0930

WHITE COPY - REPORT YELLOW COPY - LABORATORY PINK COPY - FIELD

TRIMATRIX LABORATORIES

5560 Corporate Exchange Court SE
Grand Rapids, MI 49512
Phone (616) 975-4500 Fax (616) 942-7463
www.trimatrixlabs.com

Chain of Custody Record

COC No. 150038

Pg 4 of 4

For Lab Use Only
Cart
VOA Rack/Tray
Receipt Log No. 2110
Project Chemist
Work Order No. 1411479

Client Name: Nationwide Env Svcs
Address: 14818 6th Ave Ste 5A
City, State Zip: Golden CO
Phone/Fax
Email: 303 232 2134

Project Name: SE Rock
Client Project No. / P.O. No.
Invoice To: ☐ Client ☐ Other (comments)
Contact/Report To: B. LaHamme

Analyses Requested: Voc per List

Container Type (corresponds to Container Packing List)

PRESERVATIVES
A NONE pH~7
B HNO_3 pH<2
C H_2SO_4 pH<2
D 1+1 HCl pH<2
E NaOH pH>12
F ZnAc/NaOH pH>9
G MeOH
H Other (note below)

Schedule	Matrix Code	Sample Number	Field Sample ID	Cooler ID	Sample Date	Sample Time	COMP	GRAB	Matrix	Number of Containers Submitted	Total	Sample Comments
		31	1 MW 114B	Tm 3399	11/24	1216		x	GW	3	3	
		32	2 MW 101B		11/24	1353		x	GW	3	3	
		33	3 MW 101A		11/24	1420		x	GW	3	3	
		34	4 FD2		11/24	1422		x	GW	3	3	
		35	5 MW 101D		11/24	1457		x	GW	3	3	
		36	6 MW 101C		11/24	1518		x	GW	3	3	
		37	7 Trip Blank									
			8									
			9									
			10									

Sampled By (print): Patrick Egan
Sampler's Signature: [signature]
Company: AEE

How Shipped? Hand ___ Carrier: Fedex
Tracking No.: 7719 7849 9448

Comments: All Samples Kept in Secure Location at 4°C

1. Relinquished By	Date	Time	2. Relinquished By	Date	Time	3. Relinquished By	Date	Time
[signature]	11/24	1930						
1. Received By	Date	Time	2. Received By	Date	Time	3. Received For Lab By	Date	Time
						[signature]	11/26/14	0930

WHITE COPY - REPORT YELLOW COPY - LABORATORY PINK COPY - FIELD

APPENDIX B

Ground Water Monitoring

Field Data Sheets

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW16
Casing Stickup (Ft.)	-0.28	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	24-Nov-14
Total Well Depth (Ft.) TOC	62.36	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	24.1	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	38.26	Field Analysis Equip	YSI 556 MSP	Sampling Period	FALL 2014		

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
11:25							0	24.1	Static
11:31	7.3	1.63	11.87	30.3	1.16		380		Start Time
11:35	7.29	1.55	11.93	32.7	1.153		380		reddish brown
11:38	7.27	1.57	12.04	36	1.142		380	24.21	clear
11:41	7.28	1.55	12.02	38.1	1.134		380		clear
11:44	7.28	1.53	11.97	40	1.124		380	24.23	clear
11:47	7.28	1.56	11.98	41.8	1.117	25	380		clear
MINUTES							TOTAL LITERS		
16.0	0.00	0.64%	-0.33%	3.70	-1.52%		6.08		

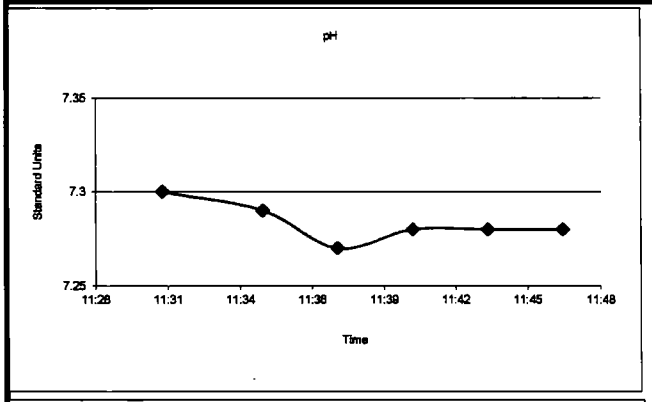

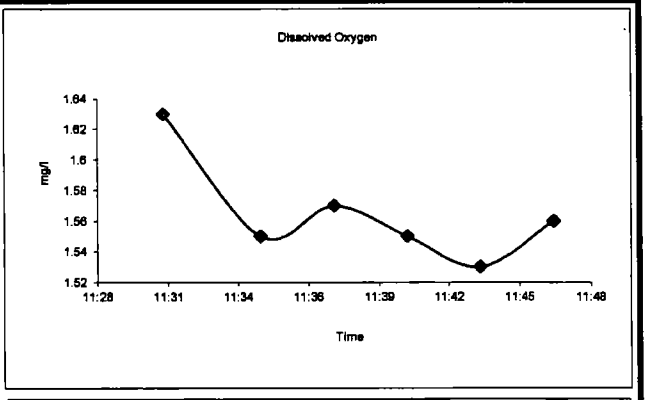

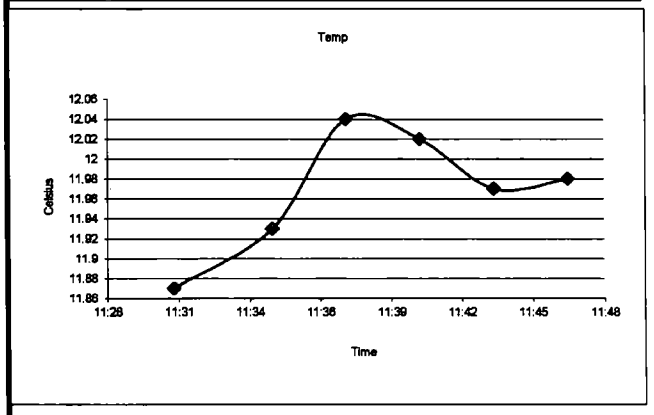

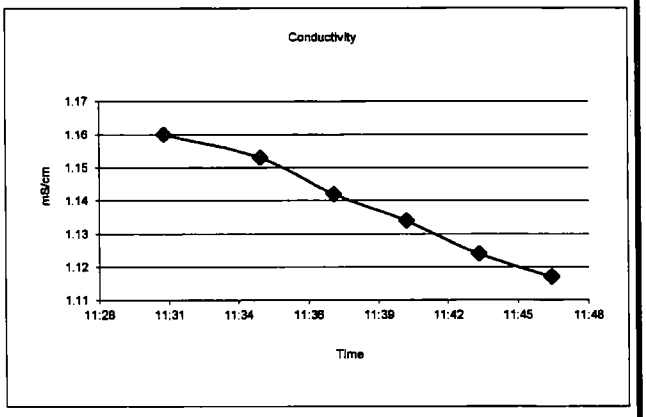

Remarks: (well condition, maintenance, etc...)

**** Well repaired - well level from new TOC

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (Inch)	2	**Pump Inlet** (Ft.) TOC	52	**Lab Analysis**	VOCs (SW-846 8260)	**Well ID:**	**MW 47**
Casing Stickup (Ft.)	-0.63	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	**Sample Date**	23-Nov-14
Total Well Depth (Ft.) TOC	54.49	**Purge Equip**	QED Air Diaphragm	**Sample Type**	Grab (Groundwater)	**Sampled by:**	Patrick Egan
Static Water Level (Ft.) TOC	41.4	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	**Site Visitors:**	None
Water Thickness (Ft.)	13.09	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	FALL 2014		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HH:MM	Standard Units	mg/l	°C	mV	mS/cm	FTU	mL/min	(Ft.) TOC	
9:04							0	41.40	Start Time
9:17	7.39	6.05	12.22	37.7	1.098		390		brown
9:21	7.39	6.16	12.24	37.6	1.097		390	41.51	brown
9:24	7.38	6.11	12.23	38.2	1.096		390		clear
9:28	7.38	6.1	12.25	38.2	1.096		390	41.52	clear
9:31	7.38	6.09	12.23	38.6	1.096		390		clear
9:34	7.39	6.05	12.22	38.6	1.094	57	390		clear
MINUTES						**TOTAL LITERS**			
17.0	0.01	-0.83%	-0.25%	0.40	-0.18%		**6.63**		

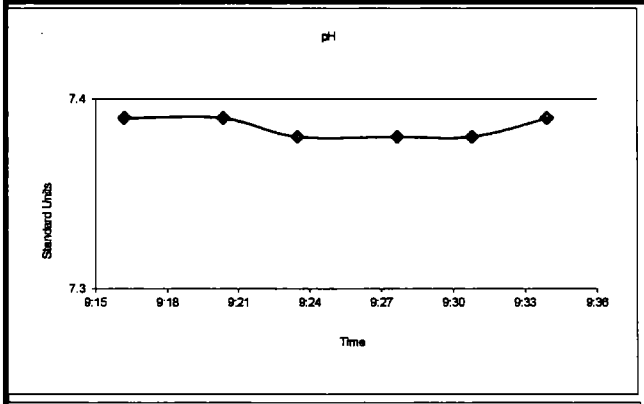

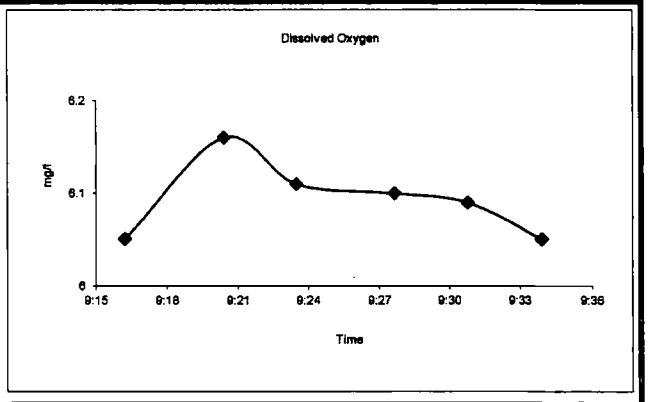

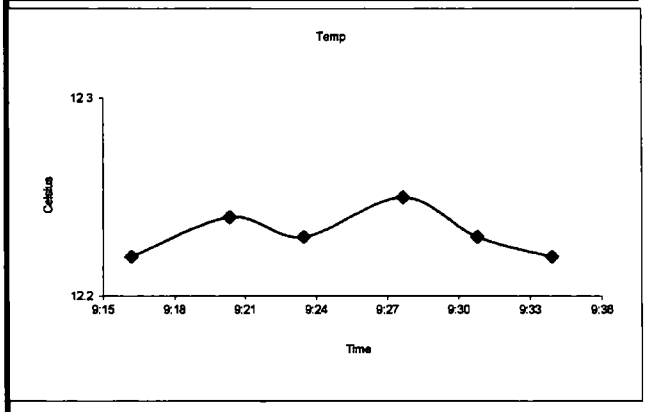

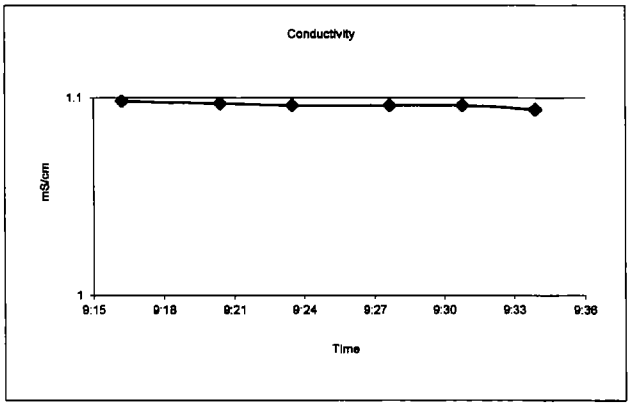

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	88	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 101A
Casing Stickup (Ft.)	1.45	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	24-Nov-14
Total Well Depth (Ft.) TOC	90.35	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	45.12	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	45.23	Field Analysis Equip	YSI 556 MSP	Sampling Period	FALL 2014		

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
14:00							0	45.12	Static
14:08	7.18	0.27	10.44	62.3	1.044		450		Start Time
14:11	7.18	0.28	10.51	61.8	1.043		450	45.12	clear
14:14	7.18	0.3	10.46	61.6	1.045		450		clear
14:17	7.18	0.3	10.46	61.4	1.043		450	45.12	clear
14:20	7.18	0.31	10.49	61.2	1.043	36	450		clear
MINUTES							TOTAL LITERS		
12.0	0.00	3.23%	0.29%	-0.40	-0.19%		5.40		

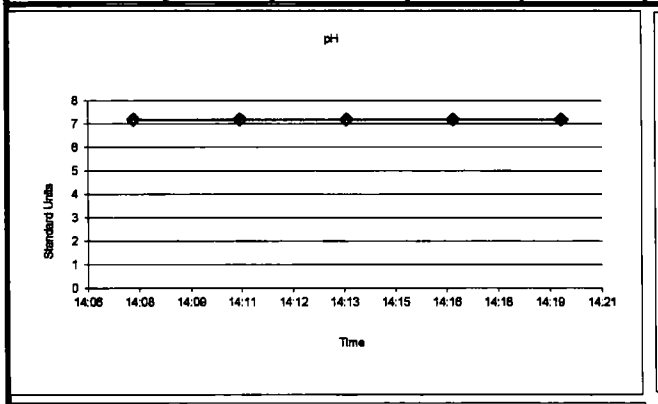

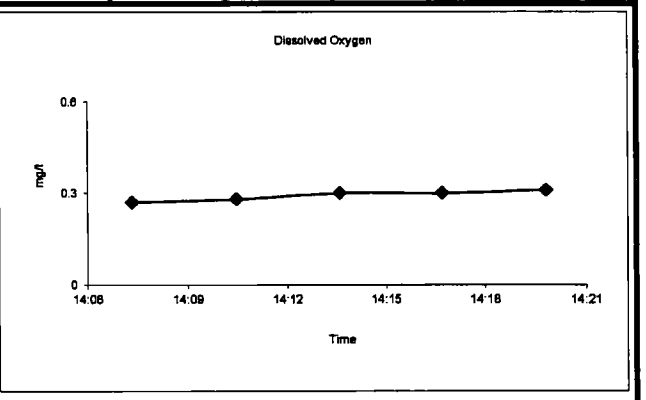

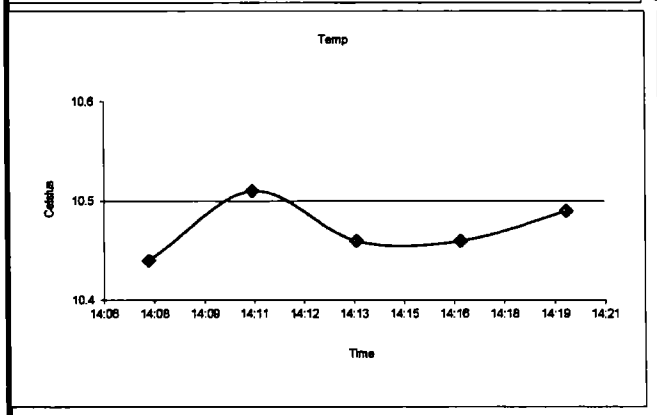

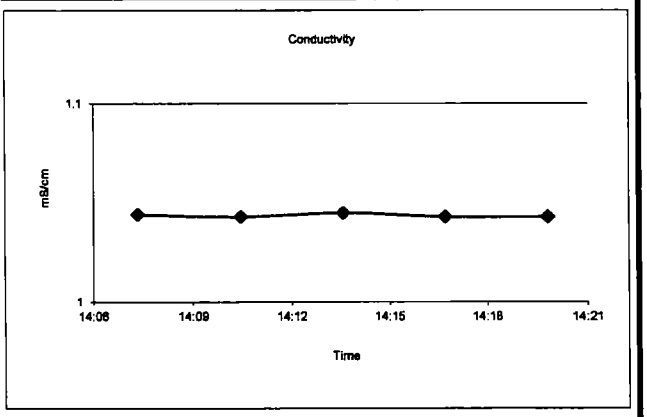

Remarks: (well condition, maintenance, etc...)
Field Duplicate (FD-2) Collected

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	151	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 101B
Casing Stickup (Ft.)	2.16	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	24-Nov-14
Total Well Depth (Ft.) TOC	153.74	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	45.83	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	107.91	Field Analysis Equip	YSI 556 MSP	Sampling Period	FALL 2014		

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
13:30							0	45.83	Static
13:41	7.3	0.27	10.51	60.6	0.979		470		clear
13:44	7.29	0.32	10.59	61.4	0.978		470	45.85	clear
13:47	7.28	0.33	10.6	62.2	0.978		470		clear
13:50	7.27	0.39	10.54	62.9	0.979		470	45.87	clear
13:53	7.27	0.36	10.6	63.8	0.977	20	470		clear
MINUTES							TOTAL LITERS		
12.0	-0.01	8.33%	0.00%	1.60	-0.10%		5.64		

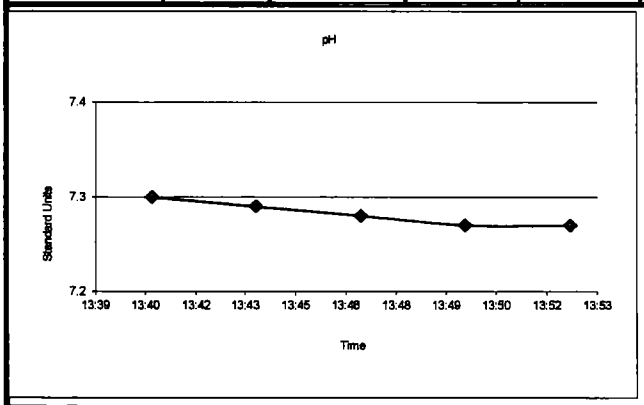

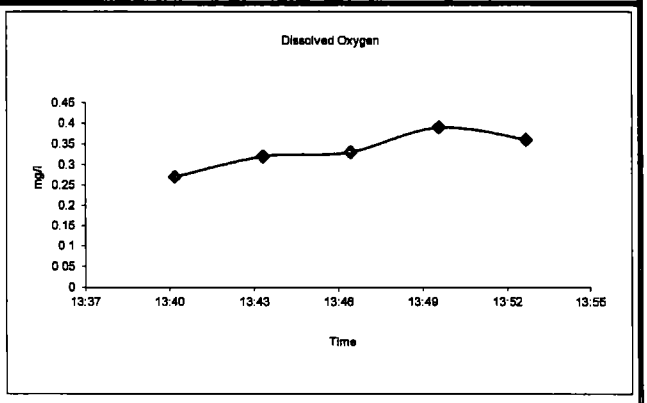

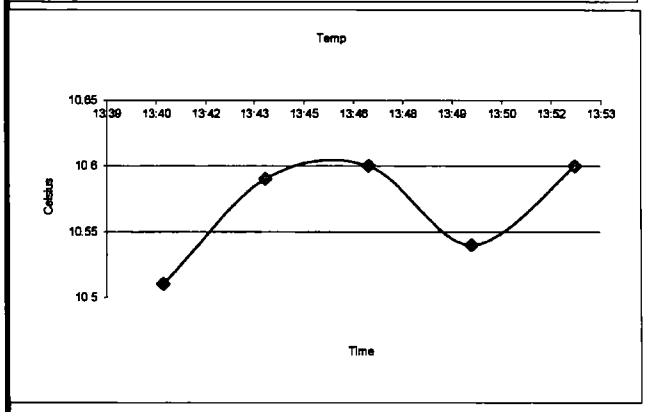

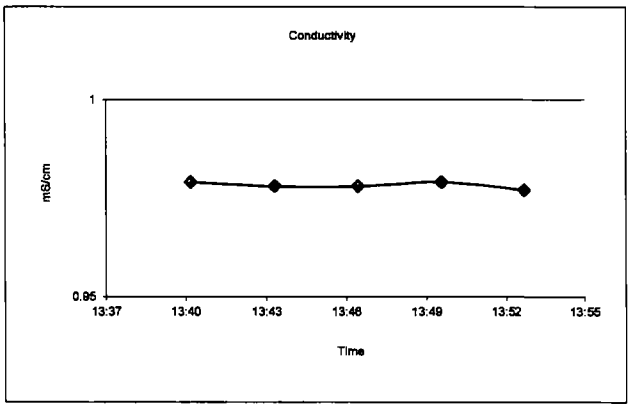

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	172	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 101C
Casing Stickup (Ft.)	1.12	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	24-Nov-14
Total Well Depth (Ft.) TOC	174.89	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	45.72	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	129.17	Field Analysis Equip	YSI 556 MSP	Sampling Period	FALL 2014		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HH:MM	Standard Units	mg/l	°C	mV	mS/cm	FTU	mL/min	(Ft.) TOC	
14:59							0	45.72	Static
15:04	7.2	1.26	10.32	24.6	0.975		450		Start Time
15:07	7.19	1.22	10.38	28.2	0.974		450	45.75	clear
15:10	7.19	1.21	10.33	31.6	0.975		450		clear
15:13	7.18	1.21	10.35	34.5	0.975		450	45.75	clear
15:18	7.18	1.21	10.32	37	0.975	22	450		clear
MINUTES							TOTAL LITERS		
14.0	-0.01	0.00%	-0.10%	5.40	0.00%		6.30		

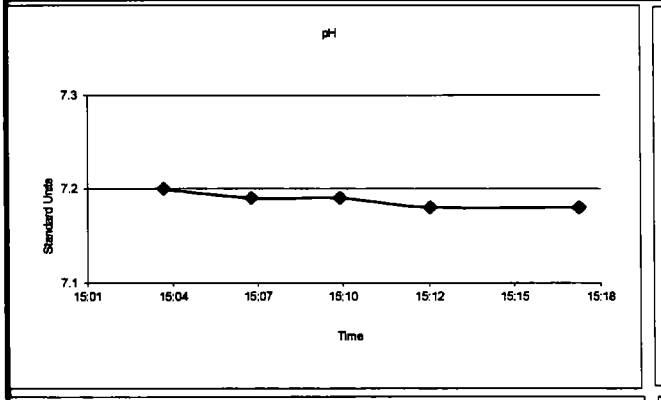

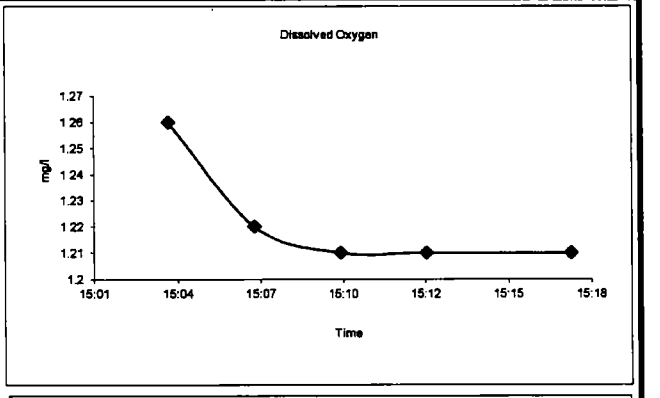

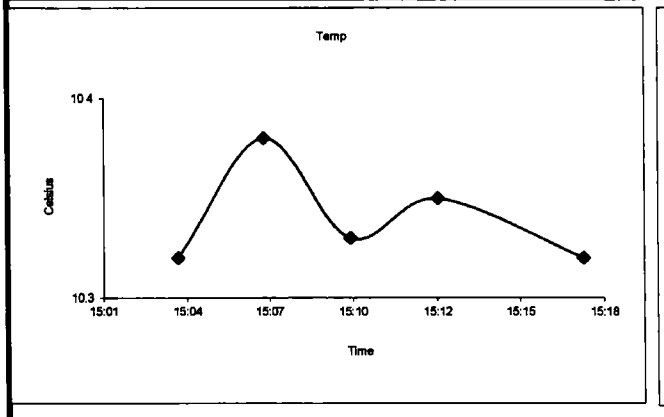

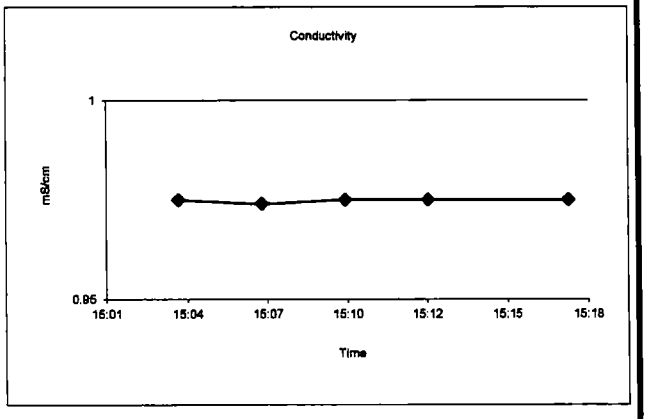

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	172	**Lab Analysis**	VOCs (SW-846 8260)	Well ID:	**MW 101D**
Casing Stickup (Ft.)	0.89	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	24-Nov-14
Total Well Depth (Ft.) TOC	212.72	**Purge Equip**	QED Air Diaphragm	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	47.82	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	164.9	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	FALL 2014		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HH:MM	Standard Units	mg/l	°C	mV	mS/cm	FTU	mL/min	(Ft.) TOC	
14:25							0	47.82	Static
14:40	6.41	0.64	10.46	-12.1	1.409		500		Start Time
14:45	6.37	0.69	10.37	-12.9	1.544		500		cloudy
14:48	6.37	0.69	10.35	-12.7	1.612		500	47.84	clear
14:52	6.39	0.66	10.38	-14	1.613		500		clear
14:57	6.4	0.66	10.37	-14.2	1.619	31	500	47.85	clear
MINUTES							**TOTAL LITERS**		
17.0	0.03	-4.55%	0.19%	-1.50	0.43%		**8.50**		

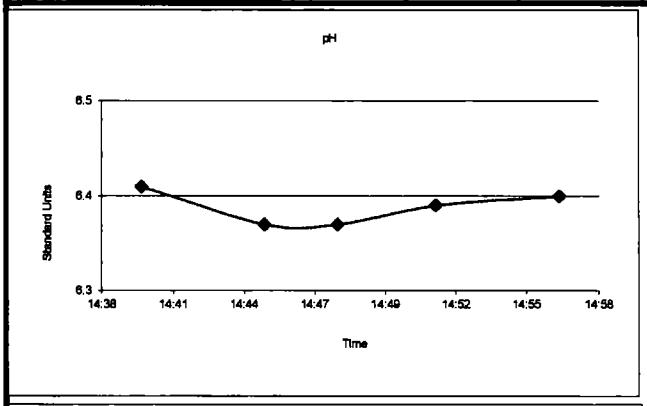

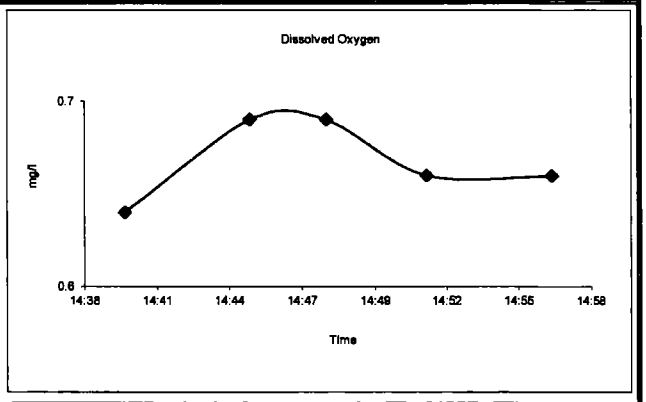

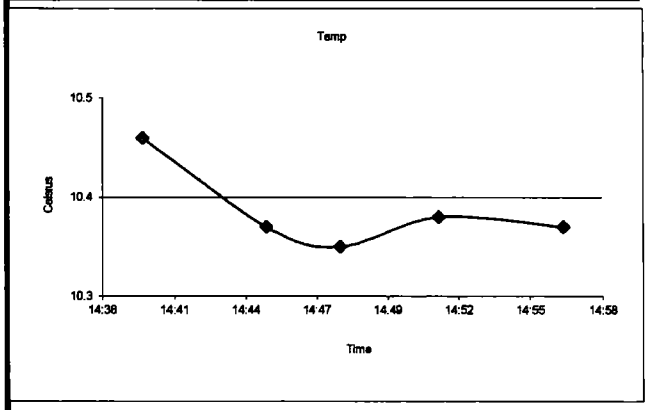

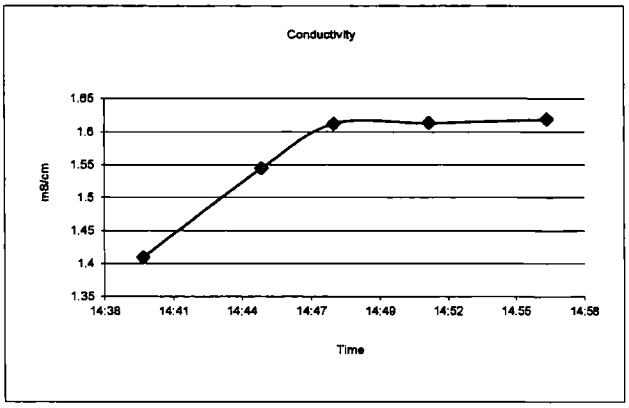

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	35	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 102A
Casing Stickup (Ft.)	-0.47	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	24-Nov-14
Total Well Depth (Ft.) TOC	37.69	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	17.22	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	20.47	Field Analysis Equip	YSI 556 MSP	Sampling Period	FALL 2014		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HH:MM	Standard Units	mg/l	°C	mV	mS/cm	FTU	mL/min	(Ft.) TOC	
8:57							0	17.22	Static
9:08	7.29	0.31	10.16	-76.4	0.873		380		Start Time
9:11	7.29	0.32	9.74	-76.8	0.874		380	17.38	brown cloudy
9:14	7.29	0.33	9.11	-77.4	0.875		380		brown cloudy
9:17	7.29	0.34	9.12	-77.4	0.875		380	17.38	cloudy
9:20	7.3	0.35	9.16	-77.2	0.878	60	380		clear
MINUTES							TOTAL LITERS		
12.0	0.01	5.71%	0.55%	0.20	0.34%		4.56		

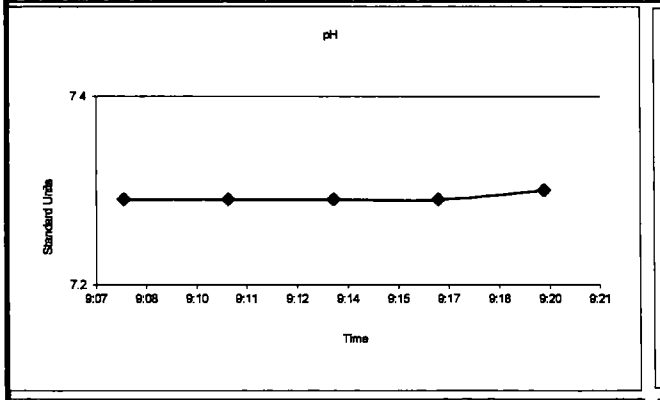

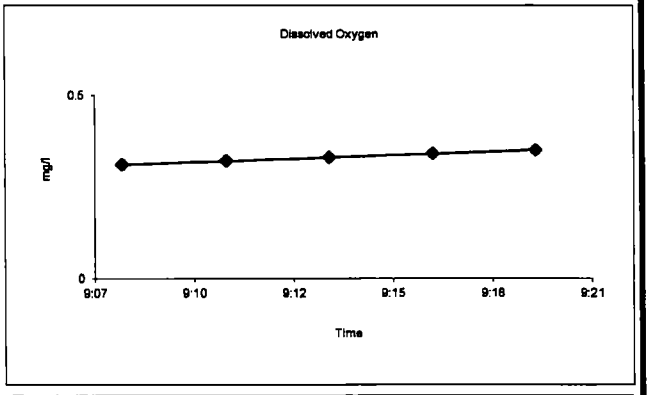

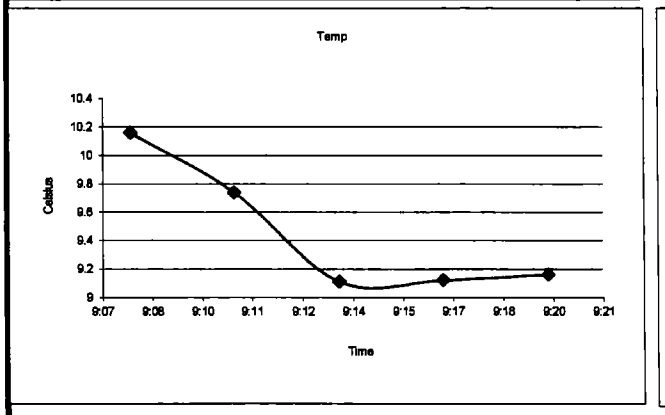

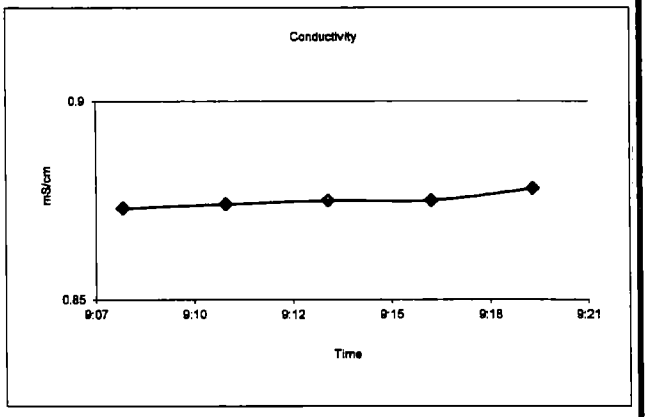

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	98	**Lab Analysis**	VOCs (SW-846 8260)	Well ID:	**MW 102B**
Casing Stickup (Ft.)	-0.68	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	Sample Date	24-Nov-14
Total Well Depth (Ft.) TOC	100.5	**Purge Equip**	QED Air Diaphragm	**Sample Type**	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	37.1	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	63.4	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	FALL 2014		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HH:MM	Standard Units	mg/l	°C	mV	mS/cm	FTU	mL/min	(Ft.) TOC	
8:35							0	37.10	Static
8:43	7.29	1.22	10.66	-64.9	0.855		400		reddish brown color
8:46	7.28	0.66	10.65	-68.6	0.86		400	37.25	reddish brown color
8:49	7.27	0.45	10.5	-71.7	0.865		400		reddish brown color
8:52	7.28	0.42	10.59	-74.6	0.867		400	37.26	cloudy
8:55	7.28	0.41	10.6	-77	0.868	88	400		clear
MINUTES						**TOTAL LITERS**			
12.0	0.01	-9.76%	0.94%	-5.30	0.35%		**4.80**		

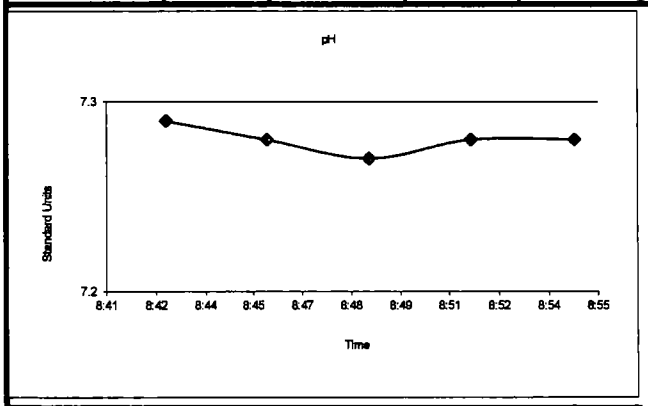

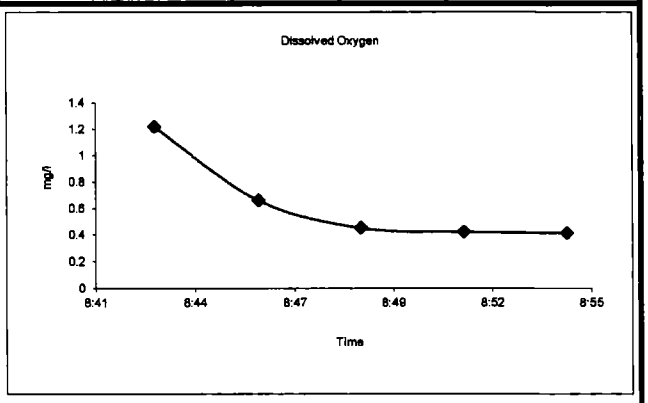

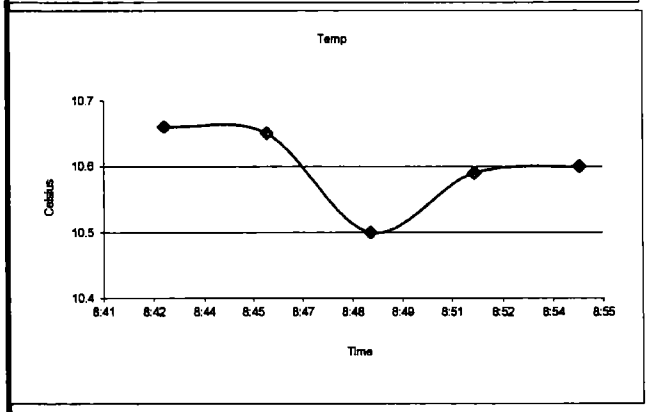

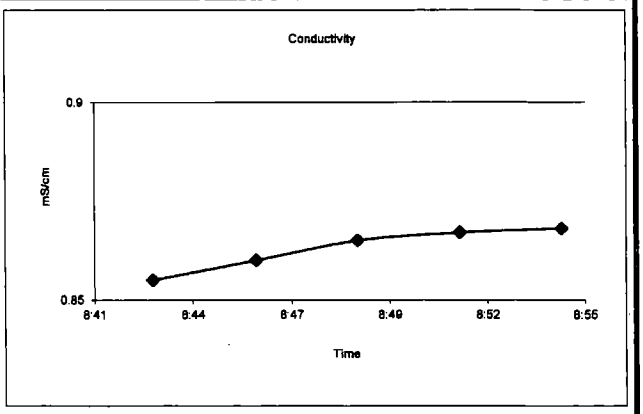

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	185	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 102C
Casing Stickup (Ft.)	-0.43	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	24-Nov-14
Total Well Depth (Ft.) TOC	187.42	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	37.43	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	149.99	Field Analysis Equip	YSI 556 MSP	Sampling Period	FALL 2014		

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
8:05							0	37.43	Static
8:13	7.43	0.38	10.35	-131.9	0.737		450		Start Time
8:16	7.44	0.38	10.34	-136.1	0.745		450	37.48	black silty
8:19	7.44	0.36	10.4	-138.1	0.745		450		black silty
8:22	7.44	0.37	10.34	-139.9	0.741		450	37.50	black silty
8:25	7.43	0.35	10.2	-141.6	0.74		450		cloudy
8:28	7.43	0.35	10.26	-145.1	0.731	90	450		cloudy
MINUTES							TOTAL LITERS		
15.0	-0.01	-5.71%	-0.78%	-5.20	-1.37%		6.75		

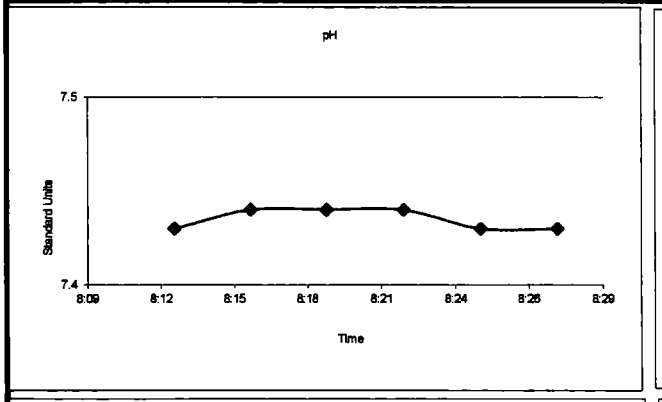

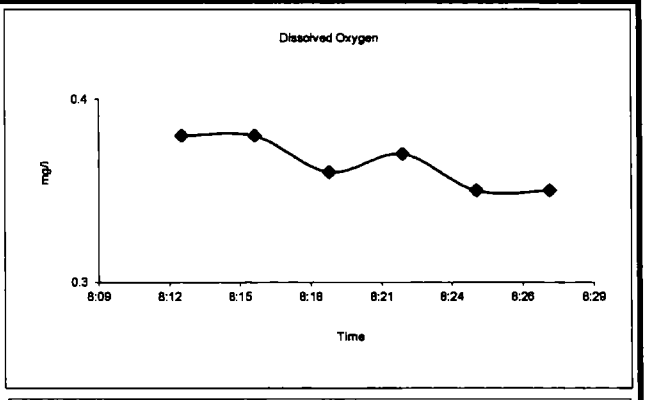

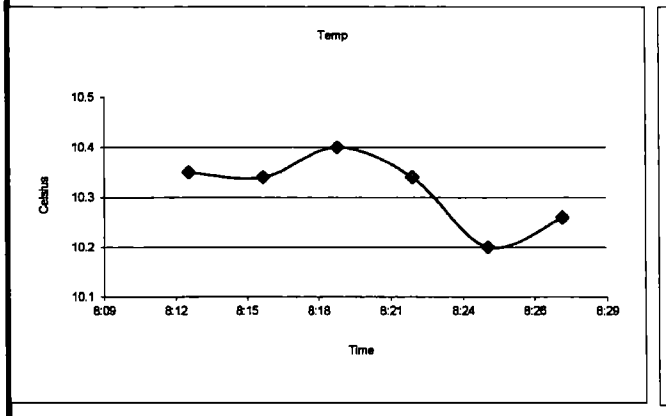

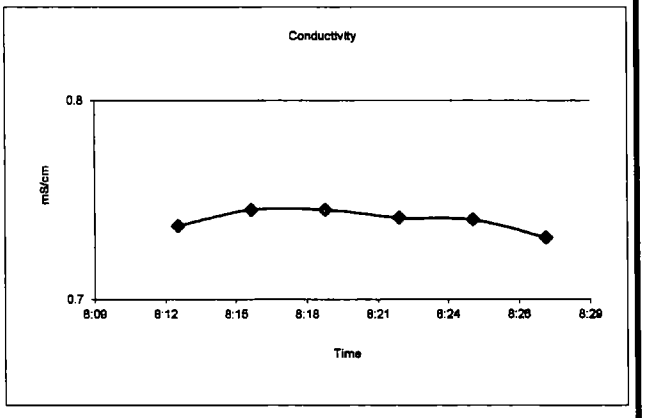

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	102	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 113A
Casing Stickup (Ft.)	-1.06	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	24-Nov-14
Total Well Depth (Ft.) TOC	104.5	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	56.92	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	47.58	Field Analysis Equip	YSI 556 MSP	Sampling Period	FALL 2014		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HH:MM	Standard Units	mg/l	°C	mV	mS/cm	FTU	mL/min	(Ft.) TOC	
12:53							0	56.92	Static
13:03	7.23	0.9	11.27	20.5	1.096		390		Start Time
13:07	7.23	0.87	11.24	19.1	1.096		390	56.96	brown & cloudy
13:10	7.23	0.86	11.26	17.3	1.096		390		cloudy
13:13	7.23	0.88	11.31	15	1.094		390		cloudy
13:16	7.23	0.89	11.32	13.9	1.095		390	56.96	clear
13:19	7.23	0.85	11.32	13.1	1.094	65	390		clear
MINUTES						TOTAL LITERS			
16.0	0.00	-3.53%	0.09%	-1.90	0.00%		6.24		

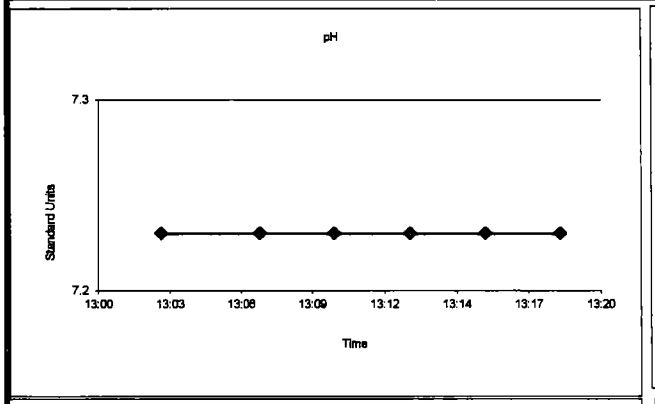

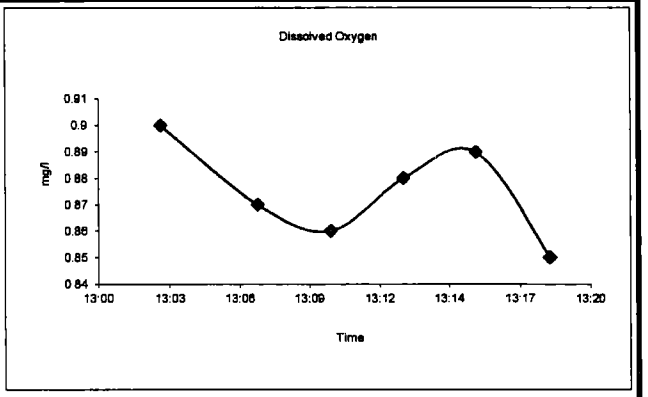

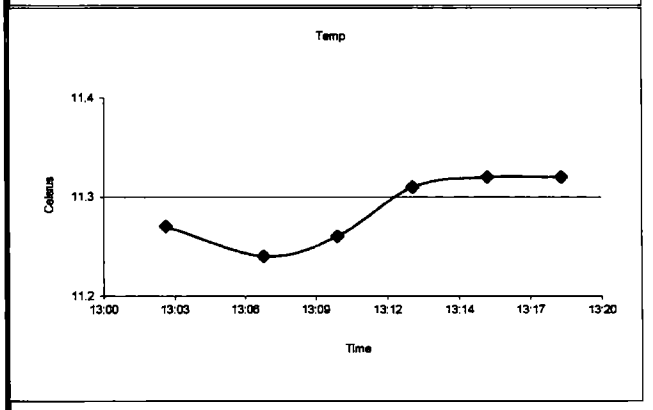

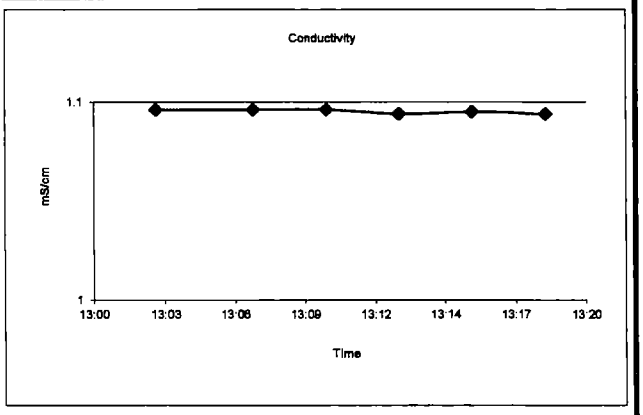

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	153	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 113B
Casing Stickup (Ft.)	-0.43	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	24-Nov-14
Total Well Depth (Ft.) TOC	155.26	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	57.55	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	97.71	Field Analysis Equip	YSI 556 MSP	Sampling Period	FALL 2014		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HH:MM	Standard Units	mg/l	°C	mV	mS/cm	FTU	mL/min	(Ft.) TOC	
12:27							0	57.55	Static
12:34	7.39	0.23	11.32	-109.9	0.881		400		Start Time
12:37	7.4	0.23	11.36	-108.3	0.88		400		cloudy white
12:40	7.39	0.22	11.37	-108.7	0.88		400	57.70	cloudy
12:43	7.39	0.23	11.36	-110.1	0.88		400		clear
12:47	7.39	0.23	11.27	-109.7	0.88		400	57.70	clear
12:50	7.36	0.23	11.33	-109.7	0.879	88	400		clear
MINUTES							TOTAL LITERS		
16.0	-0.03	0.00%	-0.26%	0.40	-0.11%		6.40		

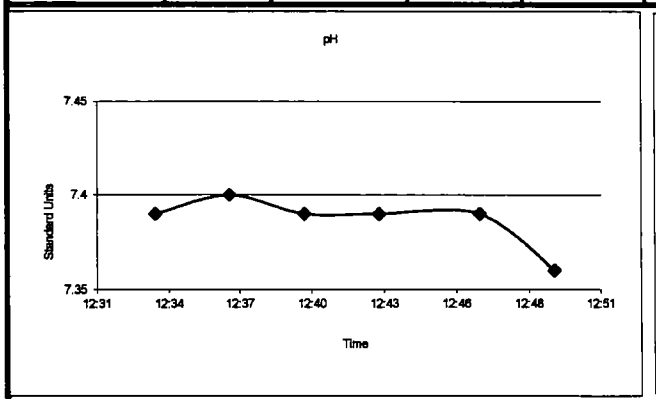

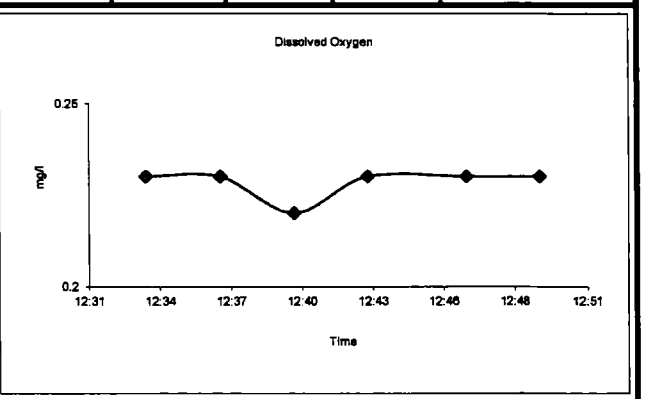

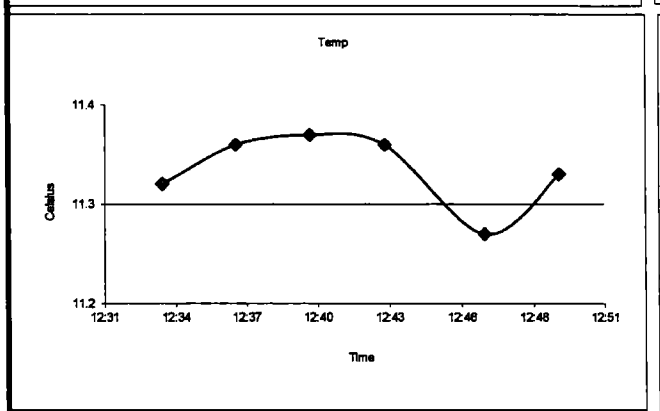

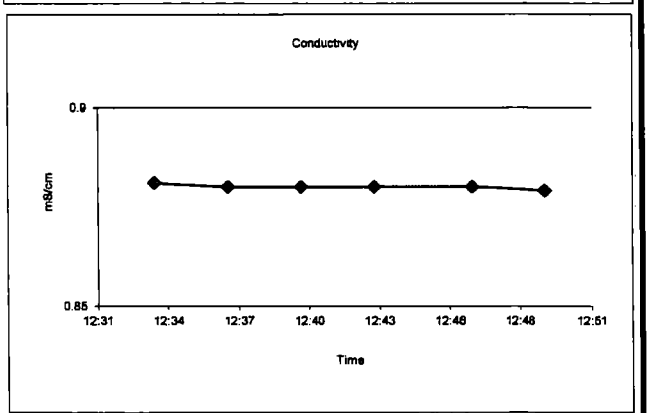

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	95	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 114A
Casing Stickup (Ft.)	2.45	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	24-Nov-14
Total Well Depth (Ft.) TOC	97.48	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	32.74	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	64.74	Field Analysis Equip	YSI 556 MSP	Sampling Period	FALL 2014		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HH:MM	Standard Units	mg/l	°C	mV	mS/cm	NTU	mL/min	(Ft.) TOC	
10:50							0	32.74	Static
11:02	7.41	2.61	11.96	-6.9	1.529		380		Start Time
11:07	7.4	2.55	11.81	-5.6	1.518		380		clear
11:12	7.39	2.5	11.8	-4.3	1.504		380	32.77	clear
11:16	7.39	2.49	11.9	-2.8	1.489		380		clear
11:19	7.38	2.5	11.9	-1.5	1.479		380	32.79	clear
11:22	7.37	2.5	11.94	-0.2	1.479	56	380		clear
MINUTES							TOTAL LITERS		
20.0	-0.02	0.40%	0.34%	2.60	-0.68%		7.60		

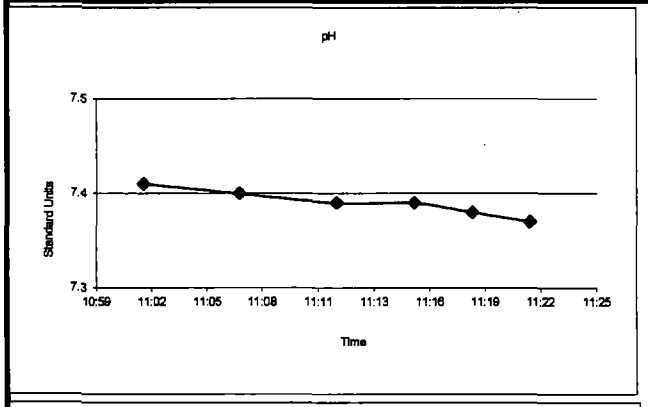

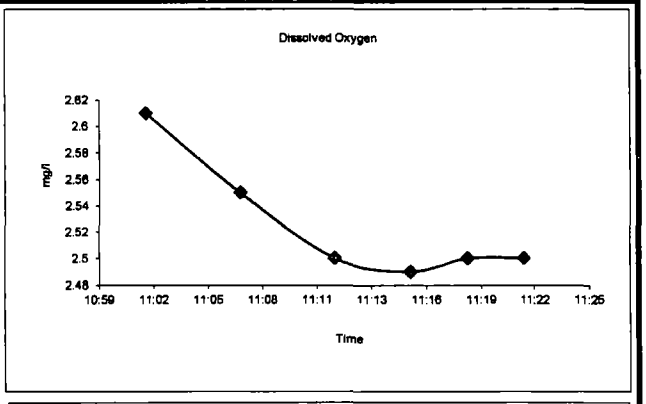

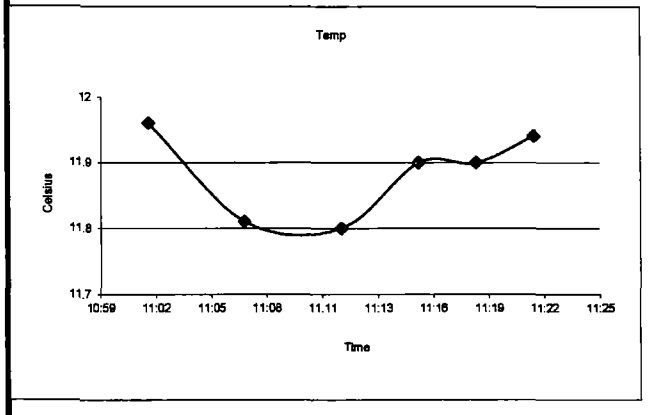

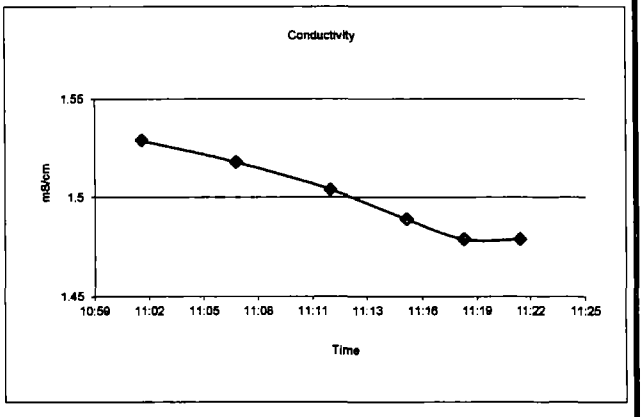

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	220	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 114B
Casing Stickup (Ft.)	-0.24	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	24-Nov-14
Total Well Depth (Ft.) TOC	222.58	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	28.73	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	193.85	Field Analysis Equip	YSI 556 MSP	Sampling Period	FALL 2014		

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
11:50								28.73	
12:01	8.24	4.57	11.69	44.5	1.004		500		cloudy
12:04	8.3	4.79	11.58	44.1	1.001		500	28.75	cloudy
12:07	8.37	5.04	11.63	42.6	0.994		500		clear
12:10	8.4	5.14	11.61	43.5	0.986		500	28.75	clear
12:13	8.44	5.23	11.6	45.3	0.965		500		clear
12:16	8.44	5.19	11.65	44.2	0.964	19	500		clear
MINUTES						TOTAL LITERS			
15.0	0.04	0.96%	0.34%	0.70	-2.28%		7.50		

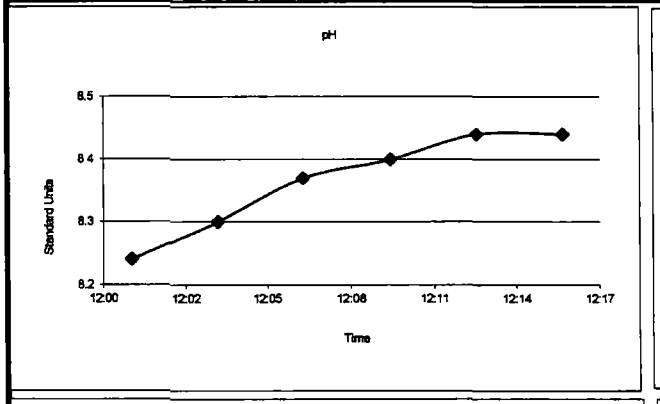

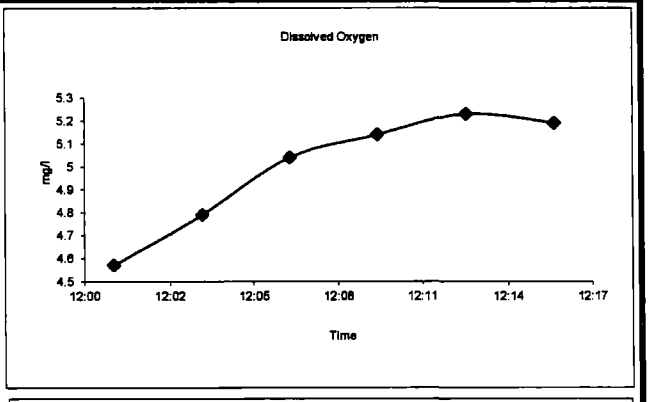

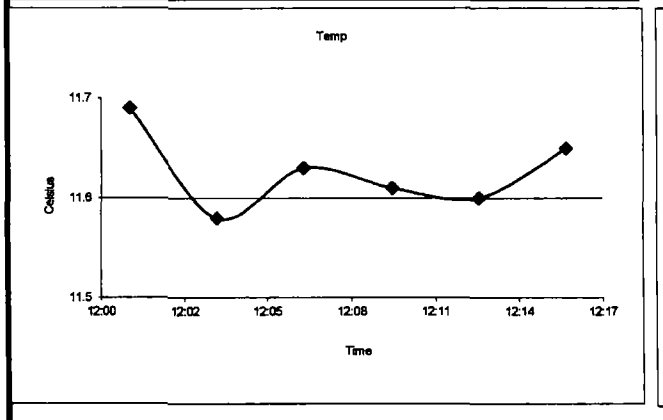

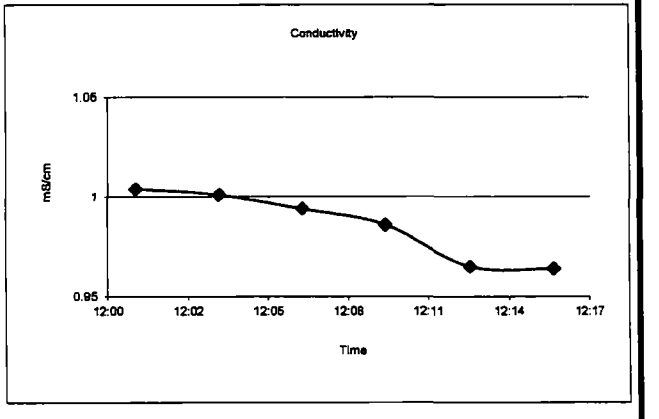

Remarks: (well condition, maintenance, etc...)

Well repaired - measurements taken from new TOC

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	87	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 117B
Casing Stickup (Ft.)	-0.45	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	21-Nov-14
Total Well Depth (Ft.) TOC	89.5	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	5.45	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	84.05	Field Analysis Equip	YSI 556 MPS	Sampling Period	FALL 2014		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HH:MM	Standard Units	mg/l	°C	mV	mS/cm	FTU	mL/min	(Ft.) TOC	
11:51							0	5.45	Static
12:03	7.17	1.77	12.92	133.1	1.002		450		Start Time
12:06	7.18	1.72	12.91	130.5	1.003		450		clear
12:09	7.18	1.7	12.91	130.4	1.003		450	5.45	clear
12:12	7.18	1.71	12.91	130.1	1.003		450		clear
12:15	7.19	1.71	12.91	128.9	1.003	28	450	5.45	clear
MINUTES							TOTAL LITERS		
12.0	0.01	0.58%	0.00%	-1.50	0.00%		5.40		

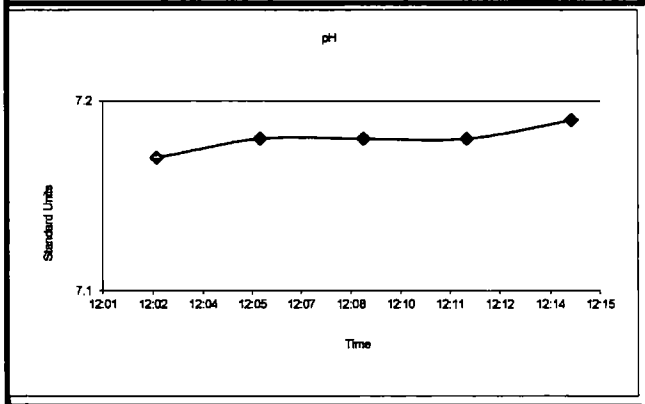

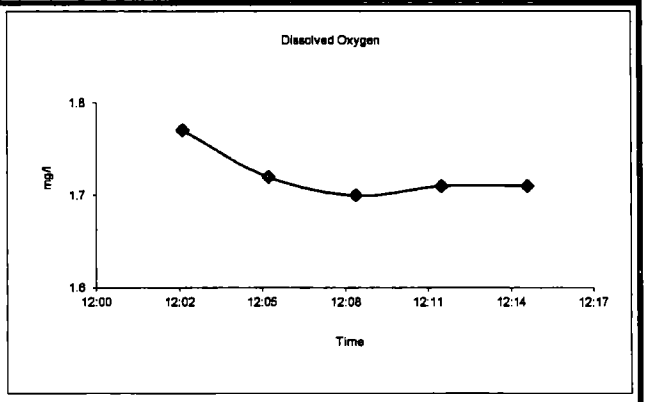

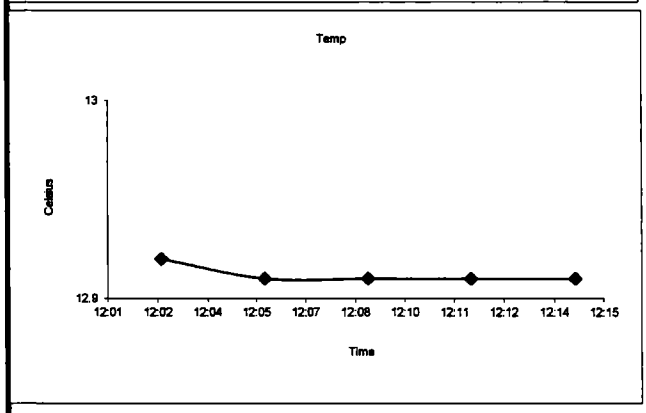

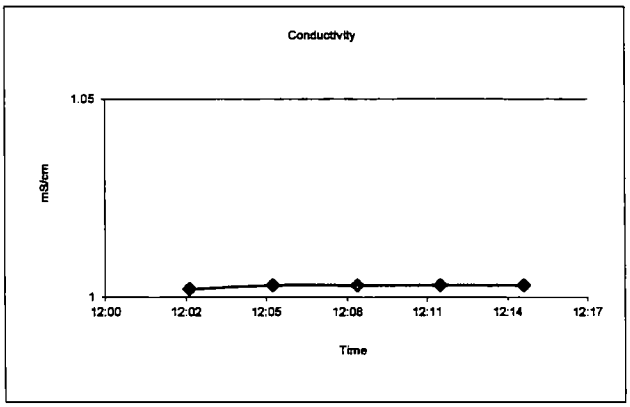

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	156	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 117C
Casing Stickup (Ft.)	-0.63	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	21-Nov-14
Total Well Depth (Ft.) TOC	158.31	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	4.38	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	153.93	Field Analysis Equip	YSI556 MPS	Sampling Period	FALL 2014		

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
12:18							0	4.38	Static
12:29	7.33	1.14	11.99	78.9	1.107		370		Start Time
12:34	7.31	1.1	11.98	62.2	1.106		370	4.39	clear
12:37	7.31	1.1	11.98	53.4	1.106		370		clear
12:40	7.32	1.1	11.98	52.2	1.104		370	4.39	clear
12:43	7.31	1.08	11.97	55.7	1.103	25	370		clear
MINUTES							TOTAL LITERS		
14.0	0.00	-1.85%	-0.08%	2.30	-0.27%		5.18		

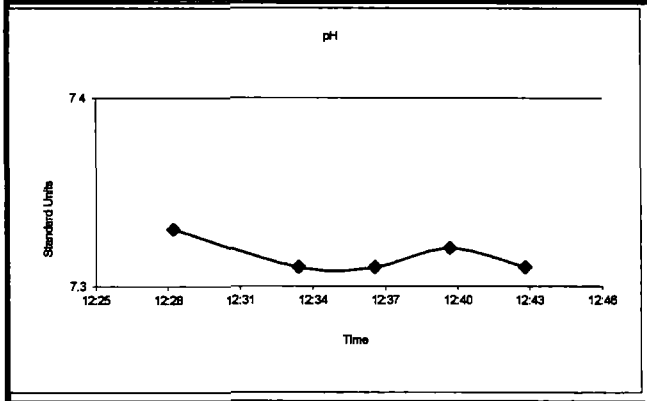

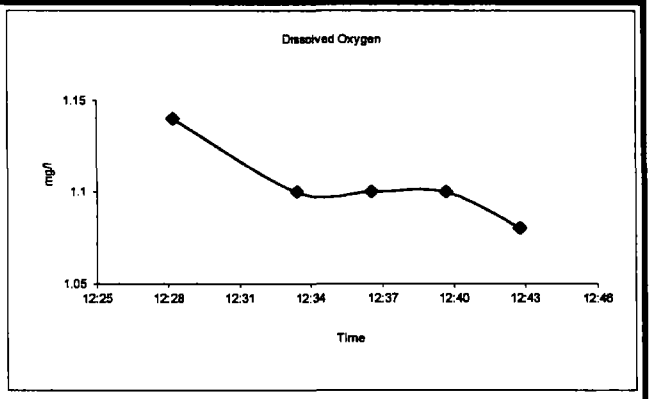

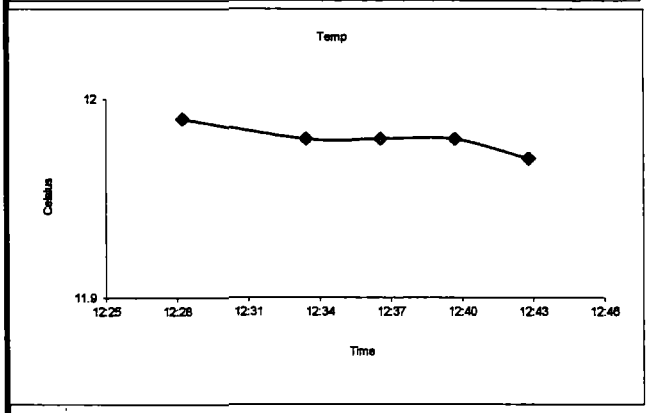

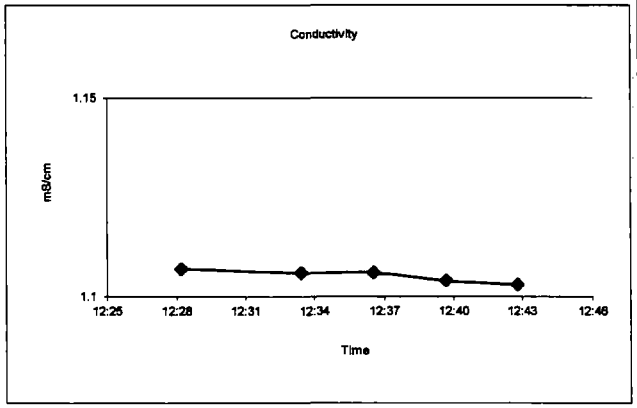

Remarks: (well condition, maintenance, etc...)

1 bolt hole stripped

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	198	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 117D
Casing Stickup (Ft.)	-0.3	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	22-Nov-14
Total Well Depth (Ft.) TOC	200.2	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	4.18	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	196.02	Field Analysis Equip	YSI556 MPS	Sampling Period	FALL 2014		

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
11:02							0	4.18	Static
11:10	7.11	1.61	12.48	154.9	1.243		500		Start Time
11:13	7.11	1.71	12.52	149.1	1.243		500		clear
11:17	7.11	1.71	12.49	144.6	1.243		500	4.18	clear
11:20	7.11	1.72	12.52	139.5	1.243		500		clear
11:23	7.11	1.73	12.49	135.6	1.243		500		clear
11:27	7.11	1.76	12.52	131	1.243	12	500	4.18	clear
MINUTES							TOTAL LITERS		
17.0	0.00	2.27%	0.00%	-8.50	0.00%		8.50		

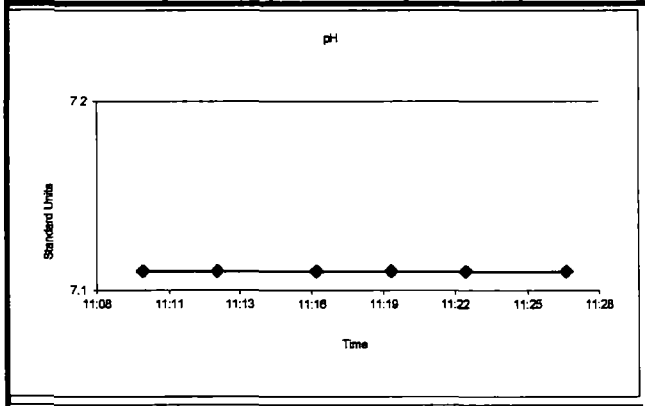

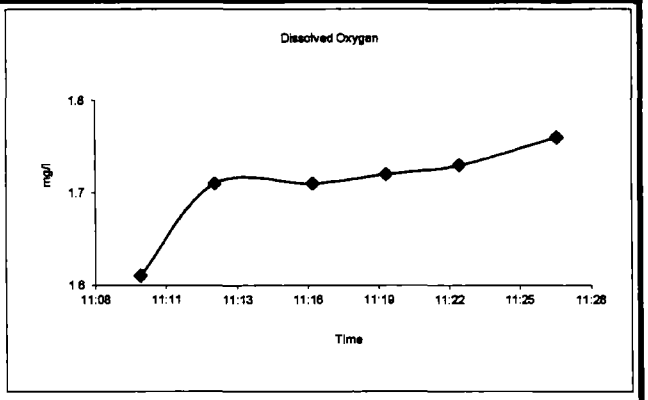

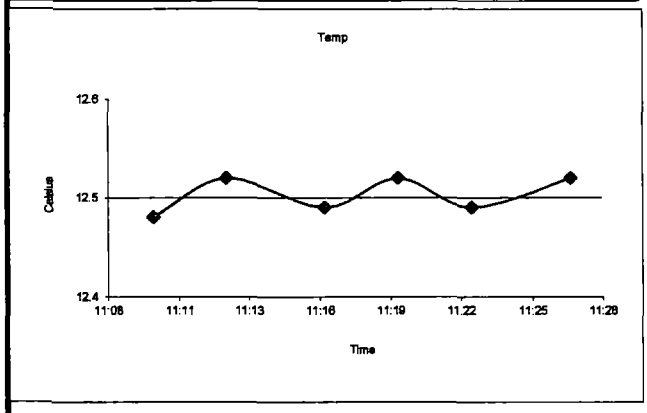

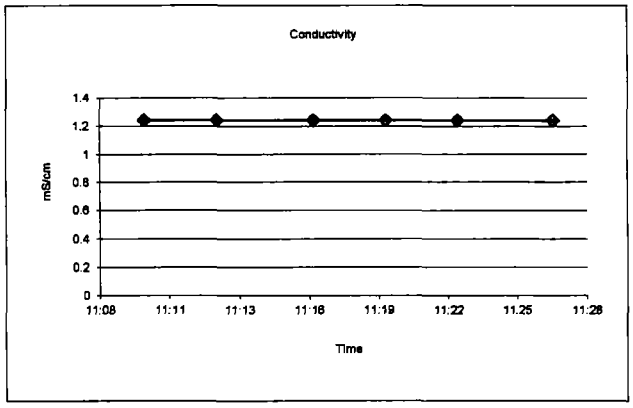

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	60	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 119
Casing Stickup (Ft.)	3.25	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	22-Nov-14
Total Well Depth (Ft.) TOC	62.41	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	25.92	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	36.49	Field Analysis Equip	YSI 556 MSP	Sampling Period	FALL 2014		

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
13:48							0	25.92	Static
14:01	7.25	2.65	11.97	141.8	1.241		300		Start Time
14:08	7.25	2.63	11.99	141.7	1.24		300	25.98	clear
14:10	7.25	2.58	11.99	141.8	1.239		300		clear
14:13	7.25	2.57	11.98	141.6	1.239		300	26.05	clear
14:16	7.25	2.56	11.98	141.7	1.238	49	300		clear
MINUTES							TOTAL LITERS		
15.0	0.00	-0.78%	-0.08%	-0.10	-0.08%		4.50		

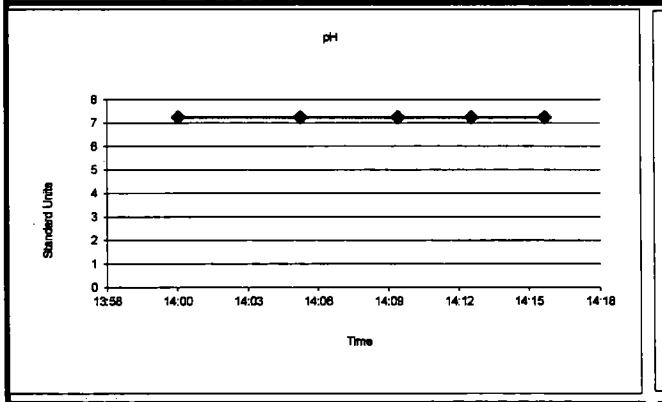

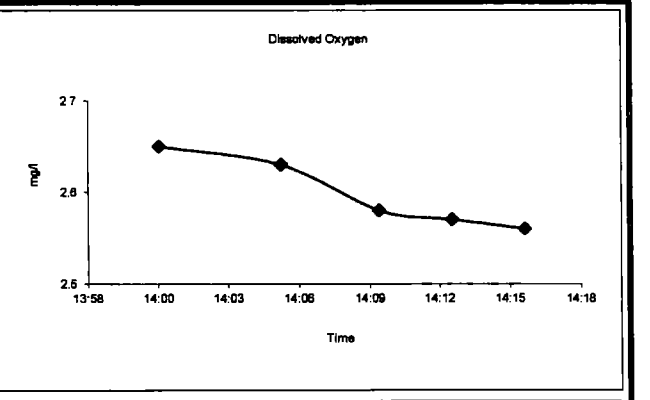

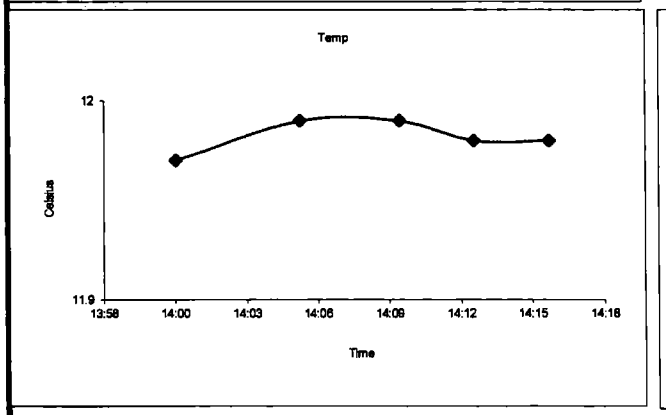

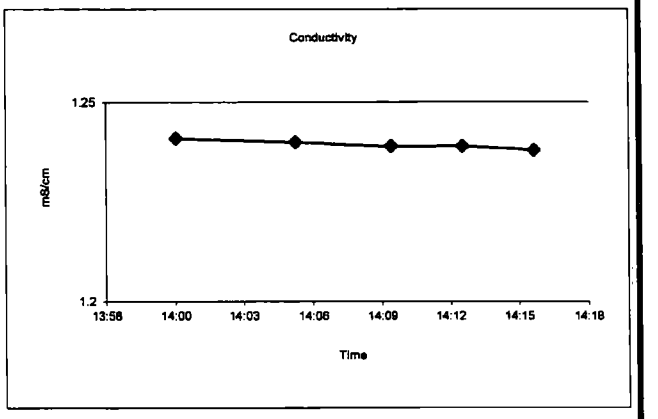

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	65	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 121
Casing Stickup (Ft.)	2.53	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	23-Nov-14
Total Well Depth (Ft.) TOC	67.55	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	23.27	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	44.28	Field Analysis Equip	YSI556 MSP	Sampling Period	FALL 2014		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HH:MM	Standard Units	mg/l	°C	mV	mS/cm	FTU	mL/min	(Ft.) TOC	
13:58							0	23.27	Start Time
14:10	7.19	1.73	13.03	69.2	1.289		400		cloudy
14:13	7.19	1.74	13.04	67.7	1.287		400	23.31	clear
14:16	7.19	1.71	13.04	66.3	1.286		400		clear
14:19	7.19	1.71	13.03	64.9	1.286		400	23.33	clear
14:22	7.19	1.73	13.02	63.9	1.287		400		clear
14:25	7.19	1.71	13.04	63.3	1.288	45	400		clear
MINUTES							TOTAL LITERS		
15.0	0.00	0.00%	0.08%	-1.60	0.16%		6.00		

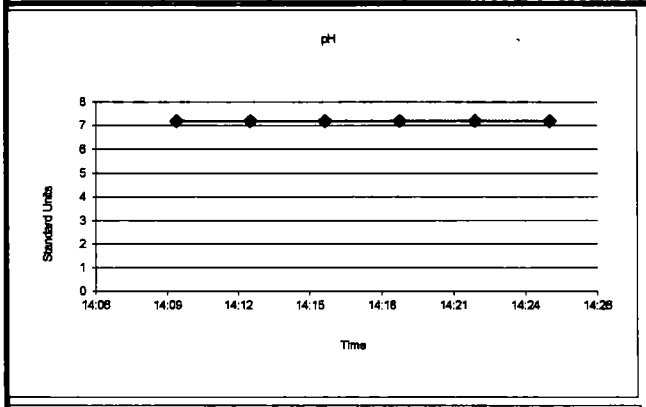

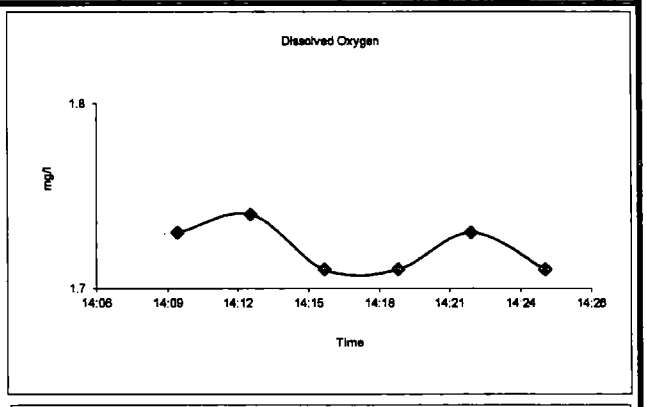

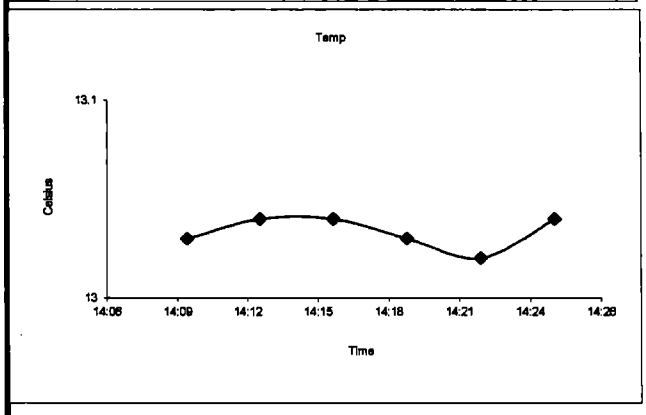

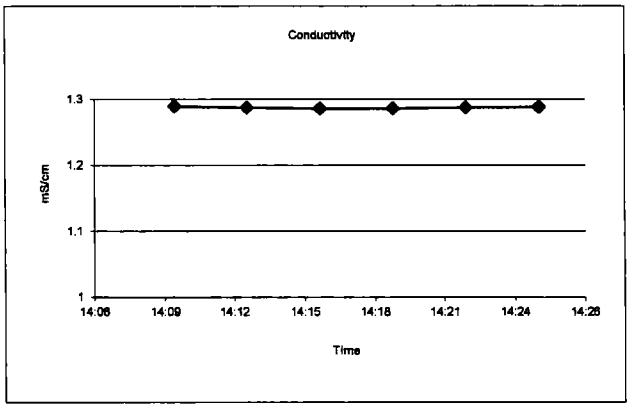

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	100	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 124
Casing Stickup (Ft.)	2.17	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	23-Nov-14
Total Well Depth (Ft.) TOC	102.76	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	35.88	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	66.88	Field Analysis Equip	YSI 556 MSP	Sampling Period	FALL 2014		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HH:MM	Standard Units	mg/l	°C	mV	mS/cm	FTU	mL/min	(Ft.) TOC	
14:38							0	35.88	Start Time
14:48	7.18	0.26	13.1	-105.2	1.352		400		cloudy
14:52	7.17	0.28	13.09	-104.4	1.355		400	35.96	cloudy
14:55	7.17	0.36	13.09	-106.1	1.358		400		clear
14:58	7.17	0.32	13.08	-101.5	1.36		400	35.99	clear
15:02	7.17	0.34	13.06	-100.1	1.363		400		clear
15:05	7.17	0.34	13.05	-100.8	1.365	30	400		clear
MINUTES							TOTAL LITERS		
17.0	0.00	5.88%	-0.23%	0.70	0.37%		6.80		

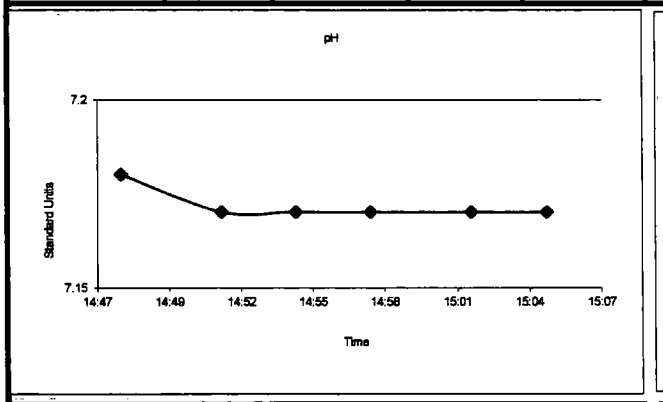

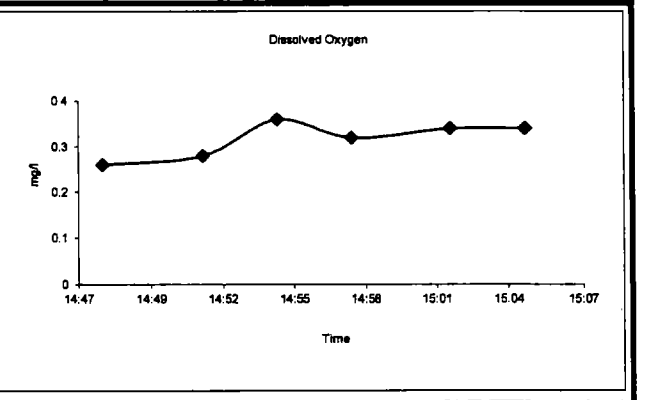

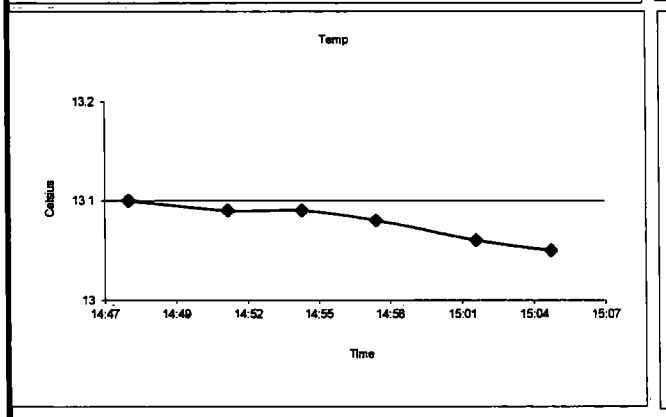

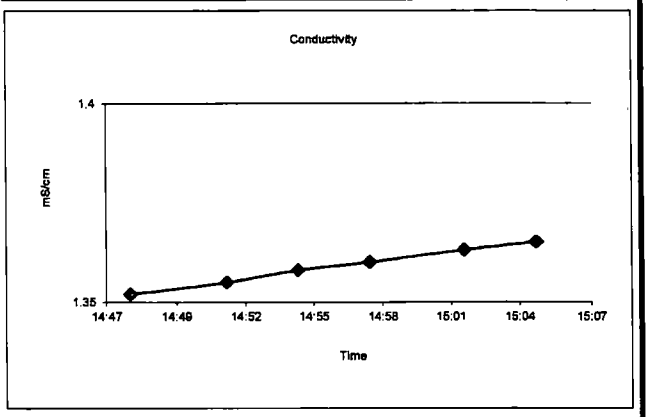

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	36	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 130
Casing Stickup (Ft.)	-0.3	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	23-Nov-14
Total Well Depth (Ft.) TOC	38.17	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	24.93	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	13.24	Field Analysis Equip	YSI 556 MSP	Sampling Period	FALL 2014		

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
15:13							0	24.93	Start Time
15:21	7.09	2.22	12.48	16.8	1.26		380		cloudy
15:24	7.1	2.25	12.48	18.8	1.26		380	25.11	clear
15:27	7.1	2.85	12.46	20.7	1.261		380		clear
15:30	7.1	2.32	12.47	22.1	1.261		380		clear
15:33	7.11	2.37	12.48	23.6	1.261		380	25.13	clear
15:36	7.11	2.4	12.49	24.6	1.261	28	380		clear
MINUTES						TOTAL LITERS			
15.0	0.01	3.33%	0.16%	2.50	0.00%		5.70		

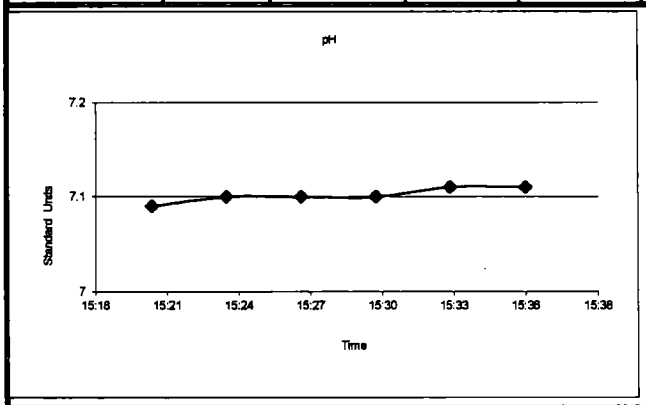

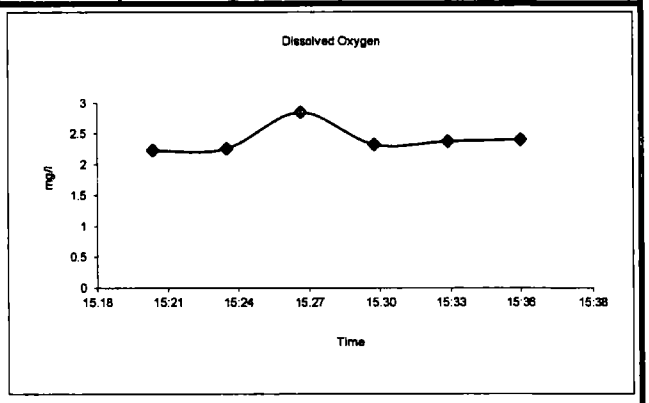

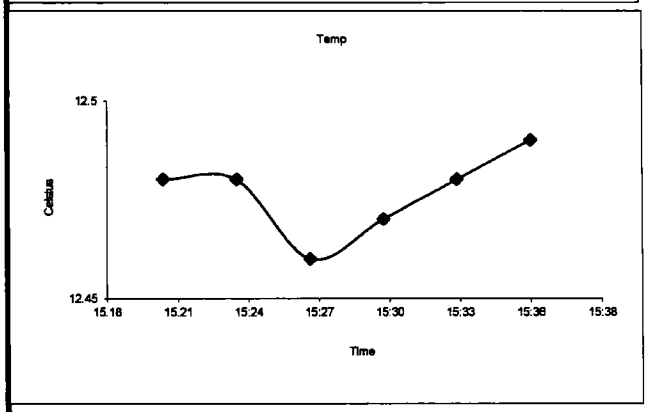

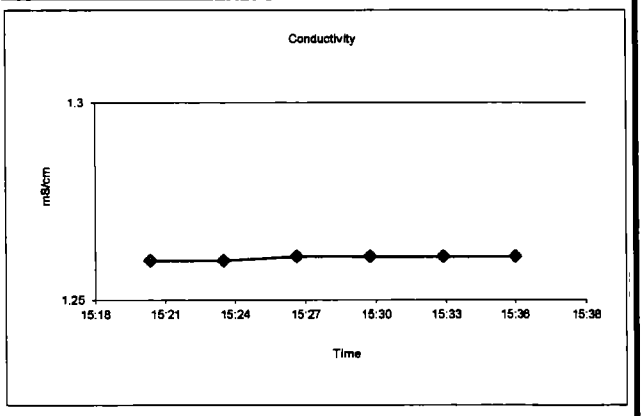

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	35	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 133A
Casing Stickup (Ft.)	2.3	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	24-Nov-14
Total Well Depth (Ft.) TOC	37.85	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	33	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	4.85	Field Analysis Equip	YSI 556 MSP	Sampling Period	FALL 2014		

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
9:25							0	33.00	Static
9:30	6.89	0.56	10.62	-72.9	0.668		400		Start Time
9:33	6.91	0.45	10.61	-76.8	0.67		400		brown cloudy
9:36	6.92	0.42	10.59	-79.8	0.672		400	33.00	cloudy
9:39	6.93	0.39	10.55	-81.5	0.675		400		clear
9:42	6.94	0.41	10.52	-82.8	0.677	20	400	33.00	clear
MINUTES							TOTAL LITERS		
12.0	0.02	-2.44%	-0.67%	-3.00	0.74%		4.80		

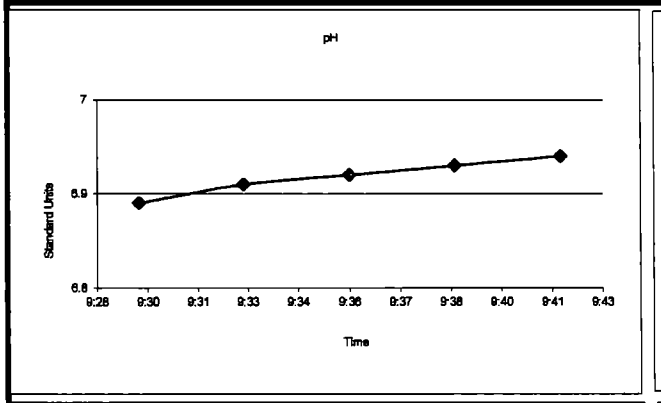

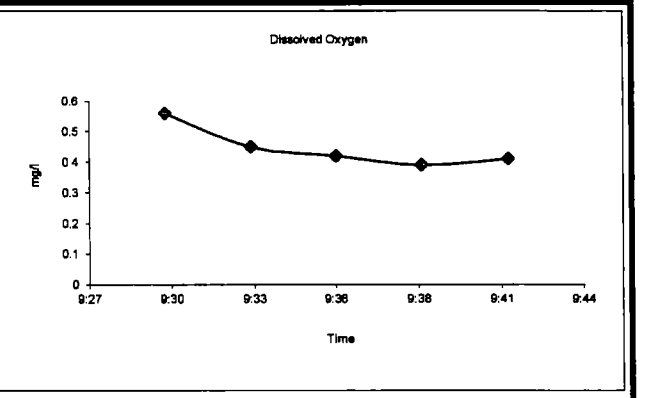

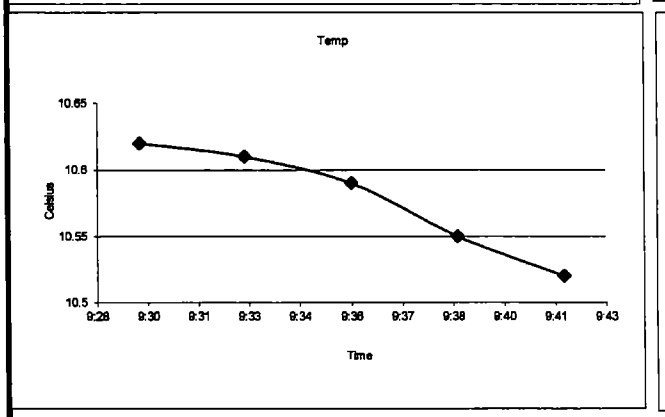

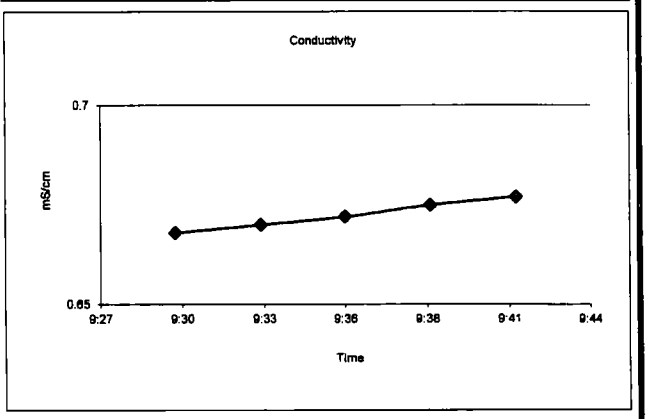

Remarks: (well condition, maintenance, etc...)
STATIC WATER LEVEL AT TOP OF PUMP

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (Inch)	2	Pump Inlet (Ft.) TOC	59	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 133B
Casing Stickup (Ft.)	2.51	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	24-Nov-14
Total Well Depth (Ft.) TOC	61.49	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	28.14	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	33.35	Field Analysis Equip	YAI 556 MSP	Sampling Period	FALL 2014		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HH:MM	Standard Units	mg/l	°C	mV	mS/cm	NTU	mL/min	(Ft.) TOC	
9:45							0	28.14	Static
9:58	7.23	2.91	10.42	-22.4	1.024		440		slightly cloudy
10:03	7.2	2.76	10.48	-12.1	1.043		440	28.30	slightly cloudy
10:06	7.17	2.56	10.49	-6.4	1.056		440		slightly cloudy
10:09	7.16	2.45	10.48	-3.3	1.064		440	28.31	clear
10:12	7.16	2.4	10.43	-0.8	1.062	41	440		clear
MINUTES							TOTAL LITERS		
14.0	-0.01	-6.67%	-0.58%	5.60	0.56%		6.16		

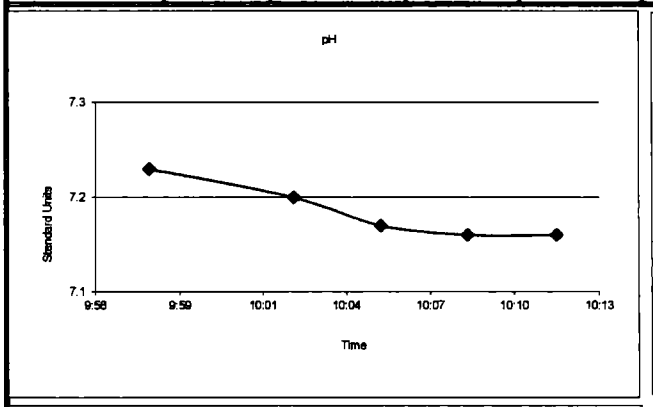

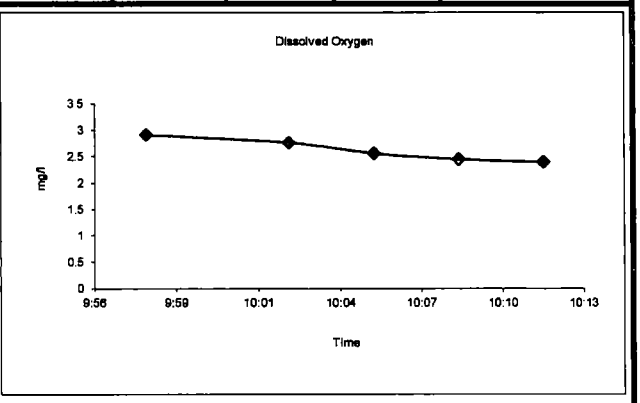

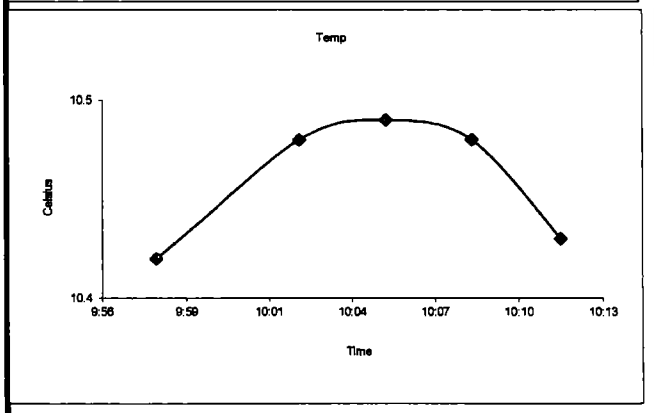

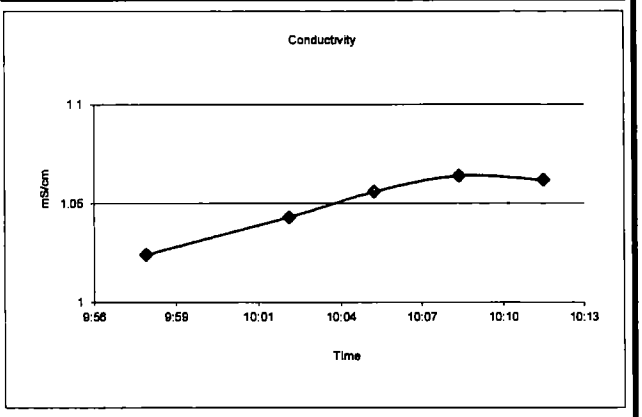

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	96	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 133C
Casing Stickup (Ft.)	2.37	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	24-Nov-14
Total Well Depth (Ft.) TOC	98.49	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	23.74	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	74.75	Field Analysis Equip	YSI 556 MSP	Sampling Period	FALL 2014		

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
10:16							0	23.74	Static
10:26	7.2	1.91	10.05	12.6	0.916		500		Start Time
10:30	7.24	1.49	10.17	16.5	0.87		500	23.76	clear
10:33	7.27	1.54	10.27	15.5	0.8		500		clear
10:36	7.31	1.58	10.21	13.9	0.771		500	23.76	clear
10:39	7.31	1.51	10.16	15.4	0.773	35	500		clear
MINUTES						TOTAL LITERS			
13.0	0.04	-1.99%	-1.08%	-0.10	-3.49%		6.50		

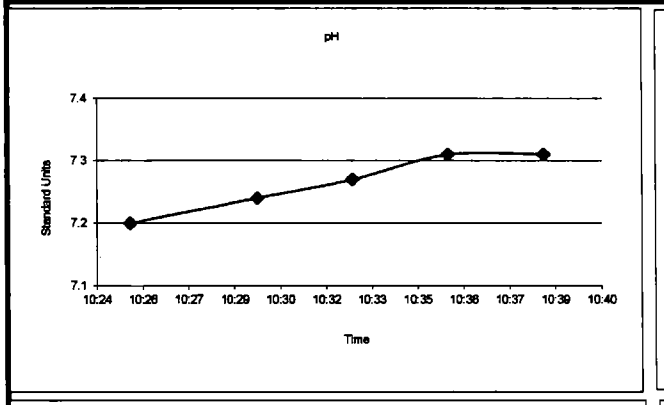

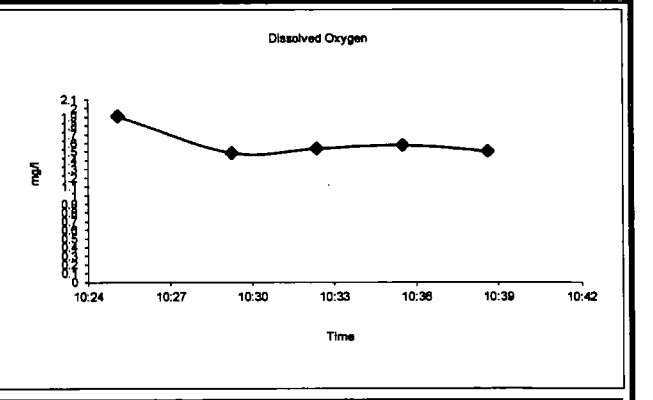

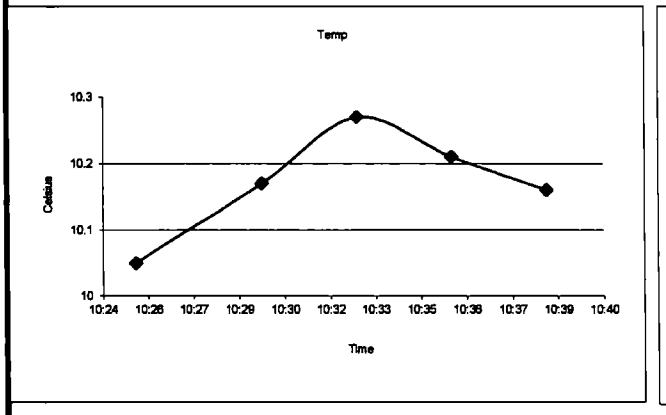

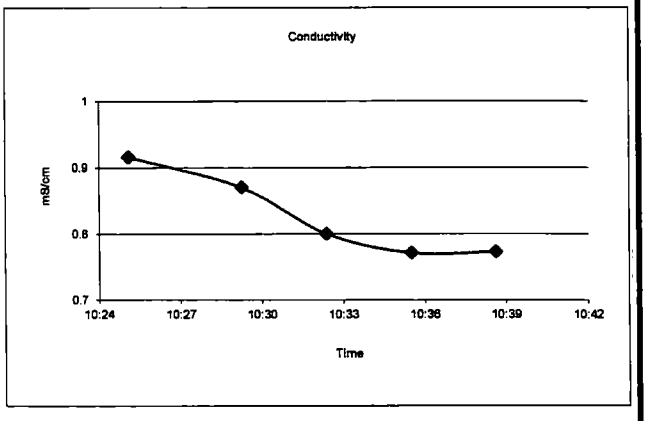

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	42	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 136
Casing Stickup (Ft.)	-0.42	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	23-Nov-14
Total Well Depth (Ft.) TOC	44.33	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	35.27	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	9.06	Field Analysis Equip	YSI 556 MSP	Sampling Period	FALL2014		

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
16:25							0	35.27	Static
16:29	7.06	4.29	11.68	85.6	1.329		350		Start Time
16:32	7.06	4.34	11.65	86.6	1.33		350	35.38	clear
16:35	7.06	4.37	11.67	87.3	1.33		350		clear
16:38	7.06	4.42	11.66	88.4	1.331		350	35.40	clear
16:41	7.05	4.39	11.65	89.4	1.332		350		clear
16:44	7.05	4.43	11.67	90.2	1.333	38	350		clear
MINUTES						TOTAL LITERS			
15.0	-0.01	0.23%	0.09%	1.80	0.15%		5.25		

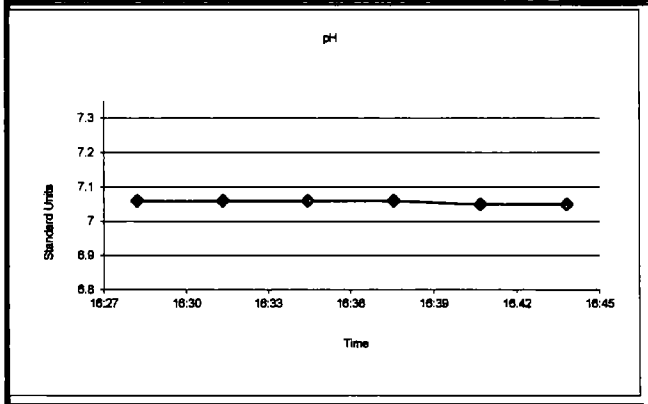

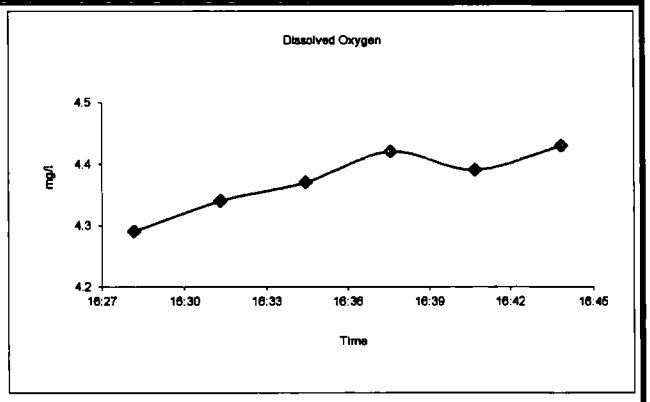

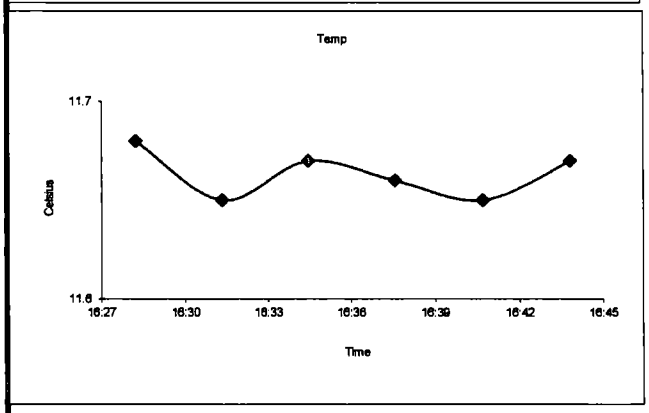

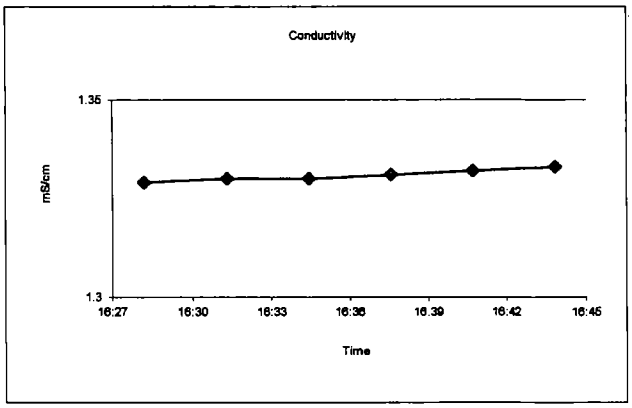

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (Inch)	2	Pump Inlet (Ft.) TOC	87	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 200
Casing Stickup (Ft.)	1.15	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	23-Nov-14
Total Well Depth (Ft.) TOC	89.93	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	51.29	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	38.64	Field Analysis Equip	YSI 556 MSP	Sampling Period	FALL 2014		

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
15:51							0	51.29	Static
16:00	7.16	3	12.02	23.7	1.122		380		Start Time
16:03	7.17	3.07	12.03	24.2	1.121		380	51.36	cloudy
16:06	7.18	3.12	12.04	24.9	1.119		380		cloudy
16:10	7.18	3.15	12.05	24.8	1.119		380		slightly cloudy
16:13	7.19	3.14	12.05	25.5	1.118		380	51.35	slightly cloudy
16:16	7.19	3.14	12.01	25.6	1.119	75	380		slightly cloudy
MINUTES						TOTAL LITERS			
16.0	0.01	-0.32%	-0.33%	0.80	0.00%		6.08		

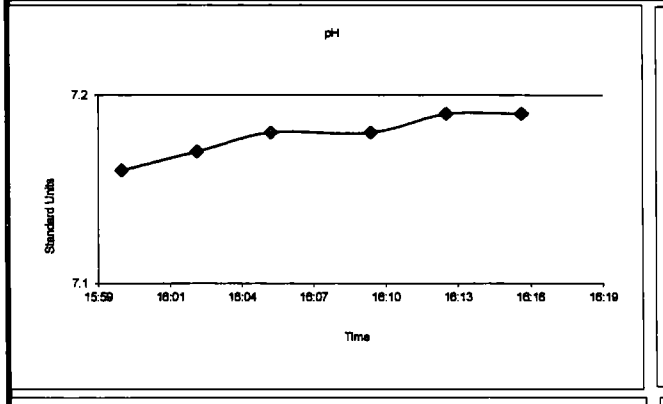

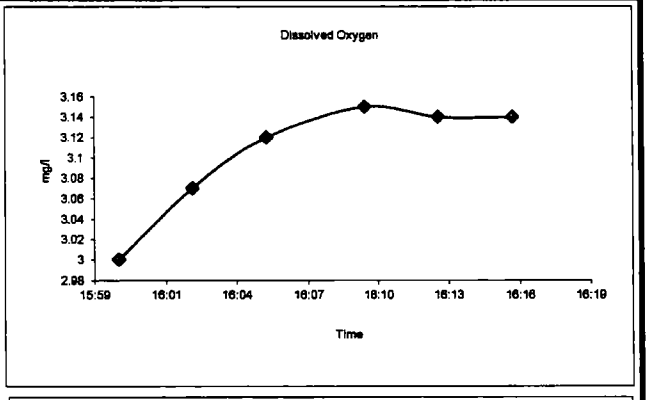

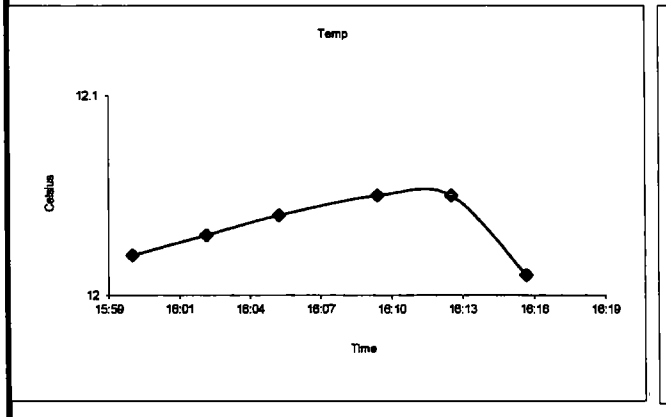

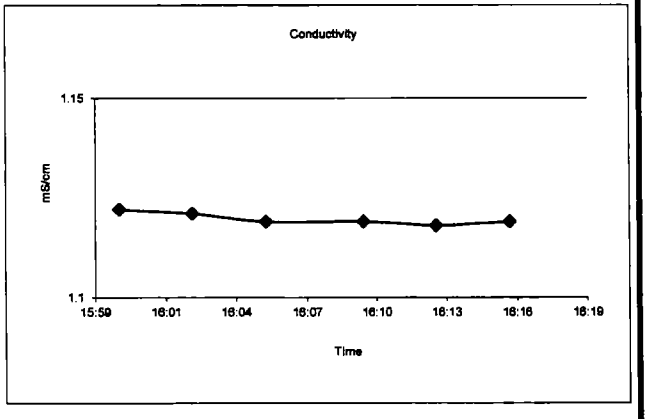

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	48	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 201
Casing Stickup (Ft.)	-0.32	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	23-Nov-14
Total Well Depth (Ft.) TOC	50.15	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	30.75	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	19.4	Field Analysis Equip	YSI 556 MSP	Sampling Period	FALL 2014		

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
13:15							0	30.75	Start Time
13:33	7.46	9.84	14.26	253.2	1.3		400		cloudy
13:36	7.46	9.95	14.27	254.2	1.299		400	30.82	clear
13:37	7.46	9.91	14.29	254.4	1.297		400		clear
13:40	7.46	9.89	14.26	255.1	1.297		400	30.83	clear
13:43	7.46	10.01	14.28	255.9	1.296		400		clear
13:47	7.46	9.86	14.27	256.4	1.295	29	400		clear
MINUTES							TOTAL LITERS		
14.0	0.00	-0.30%	0.07%	1.30	-0.15%		5.60		

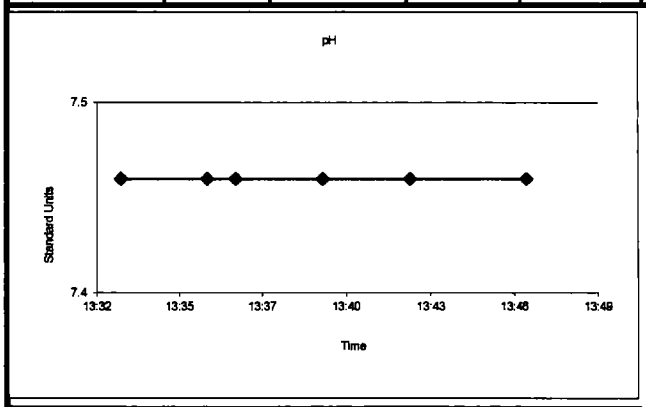

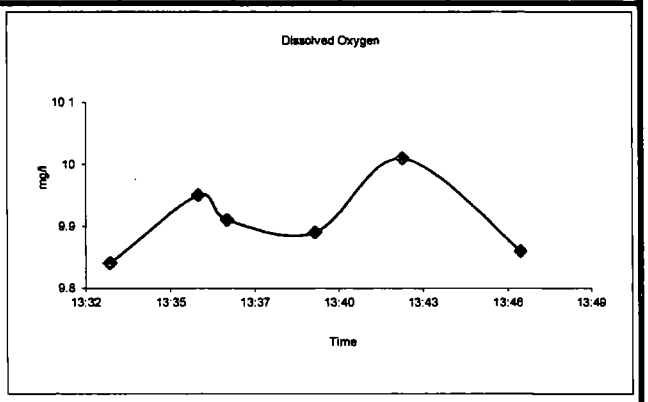

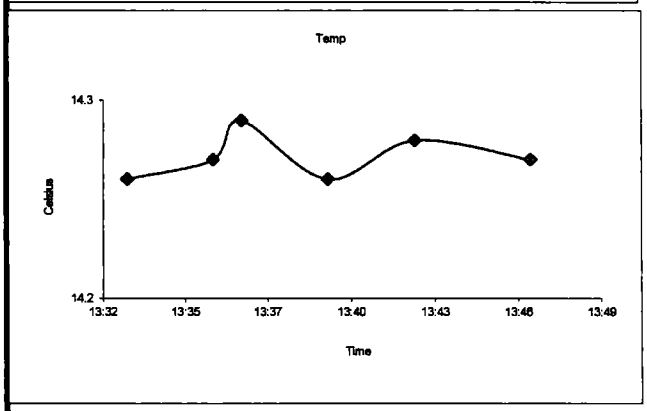

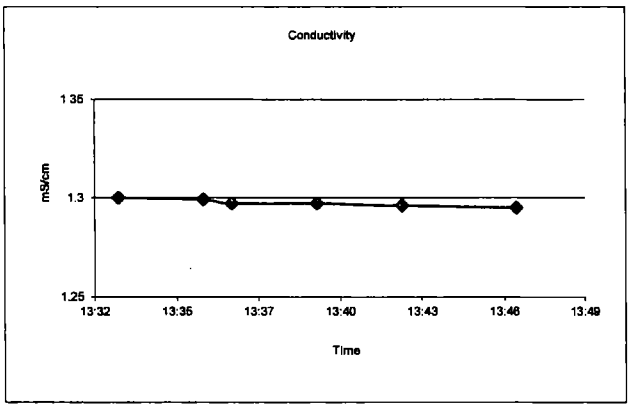

Remarks: (well condition, maintenance, etc...)
Field Duplicate collected = FD-1

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	48	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 202
Casing Stickup (Ft.)	-0.32	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	24-Nov-14
Total Well Depth (Ft.) TOC	50.01	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	29.94	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	20.07	Field Analysis Equip	YSI 556 MSP	Sampling Period	FALL 2014		

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
7:31							0	29.94	Start Time
7:40	7.11	0.66	14.1	92.3	1.205		320		cloudy
7:44	7.11	0.68	14.14	92.9	1.203		320	30.12	clear
7:47	7.11	0.69	14.13	93.4	1.203		320		clear
7:50	7.11	0.71	14.05	94.1	1.204		320	30.14	clear
7:53	7.11	0.72	14.08	94.2	1.201	44	320		clear
MINUTES						TOTAL LITERS			
13.0	0.00	4.17%	-0.36%	0.80	-0.17%		4.16		

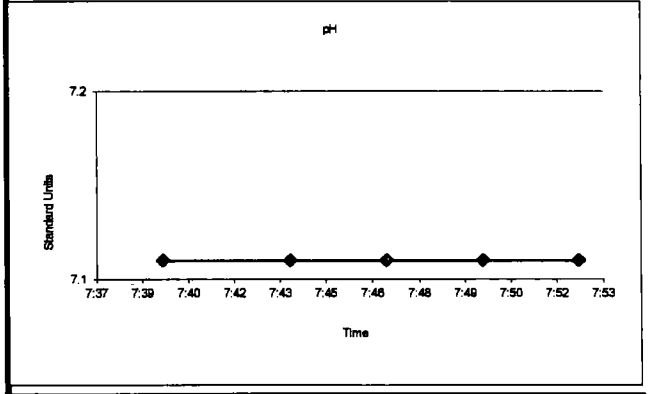

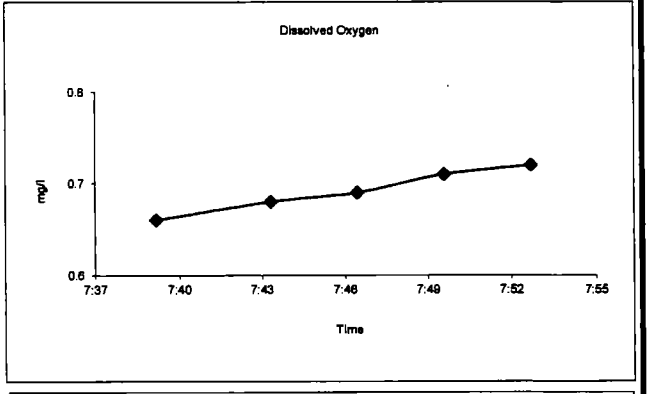

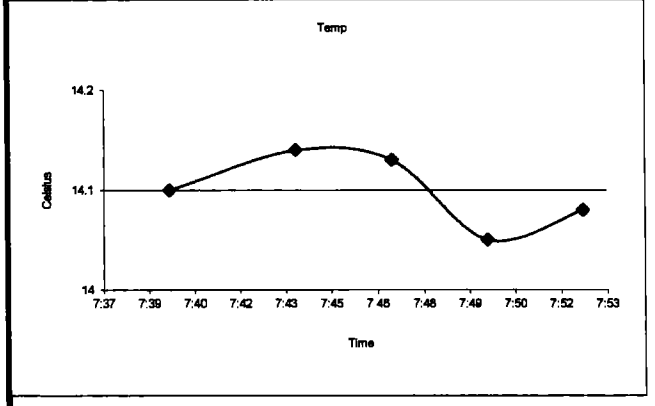

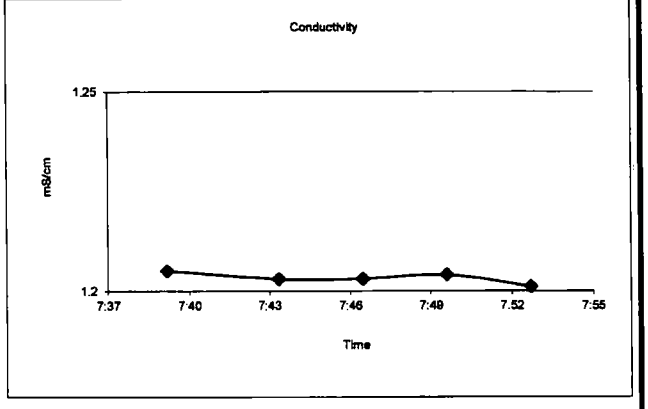

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (Inch)	2	Pump Inlet (Ft.) TOC	47	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 203
Casing Stickup (Ft.)	-0.58	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	24-Nov-14
Total Well Depth (Ft.) TOC	49.35	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	29.44	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	19.91	Field Analysis Equip	YSI 556 MSP	Sampling Period	FALL2014		

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
7:03							0	29.44	Start Time
7:13	7.15	4.72	14.31	77.8	0.974		300		cloudy
7:16	7.08	4.08	14.22	71.2	0.977		300	29.50	cloudy
7:20	7.05	3.4	14.23	70.1	0.978		300		clear
7:23	7.04	3.39	14.21	70.3	0.979		300	29.52	clear
7:26	7.05	3.3	14.21	71	0.979	41	300		clear
MINUTES							TOTAL LITERS		
13.0	0.00	-3.03%	-0.14%	0.90	0.10%		3.90		

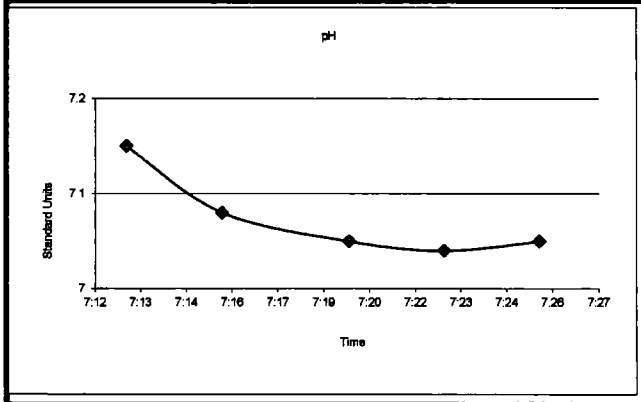

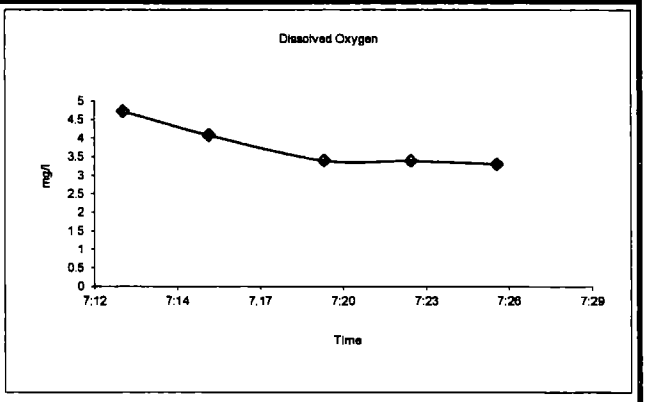

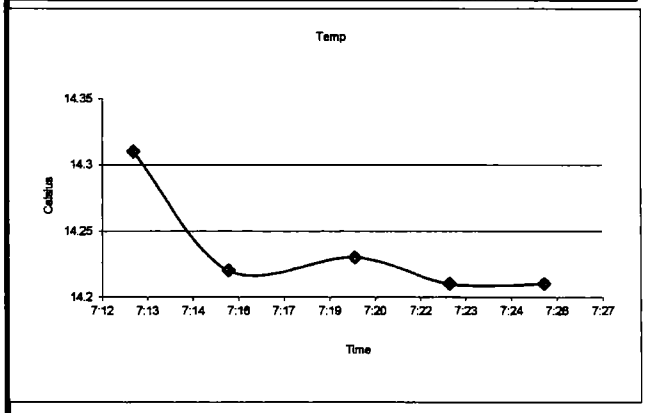

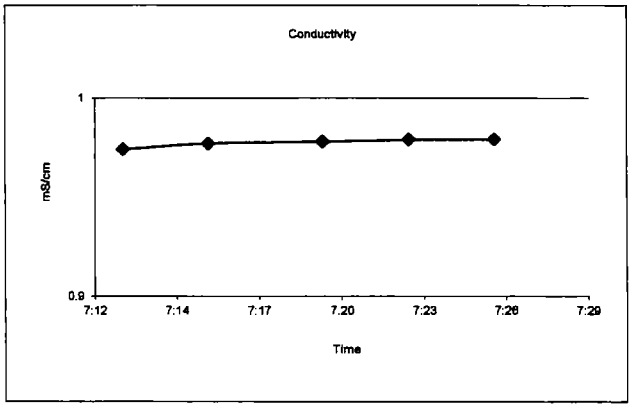

Remarks: (well condition, maintenance, etc...)

well pump was removed by unknown. Pumped utilizing a QED sample pro portable pump with teflon liner & tubing.

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (Inch)	2	Pump Inlet (Ft.) TOC	86	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 204
Casing Stickup (Ft.)	-0.39	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	23-Nov-14
Total Well Depth (Ft.) TOC	88.96	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	26.39	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	62.57	Field Analysis Equip	YSI 556 MPS	Sampling Period	FALL 2014		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HH:MM	Standard Units	mg/l	°C	mV	mS/cm	FTU	mL/min	(Ft.) TOC	
11:15							0	26.39	Static
11:28	7.2	0.3	13.1	120.2	1.067		420		slightly cloudy
11:32	7.2	0.3	13.11	120.3	1.067		420	26.43	slightly cloudy
11:36	7.2	0.32	13.12	120.4	1.067		420		slightly cloudy
11:38	7.2	0.33	13.11	120.7	1.067		420	26.43	clear
11:41	7.2	0.35	13.10	120.8	1.067	91	420		clear
MINUTES							TOTAL LITERS		
13.0	0.00	8.57%	-0.15%	0.40	0.00%		5.46		

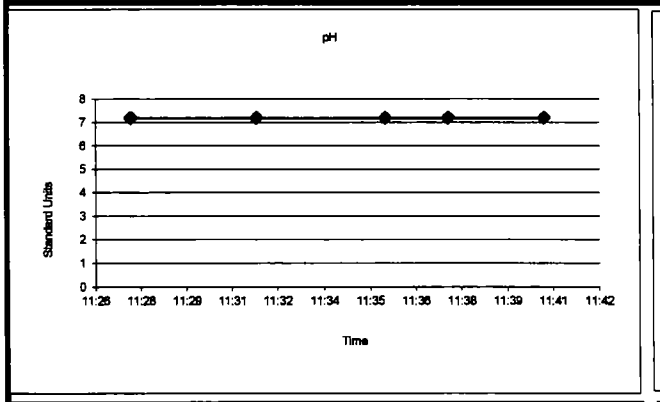

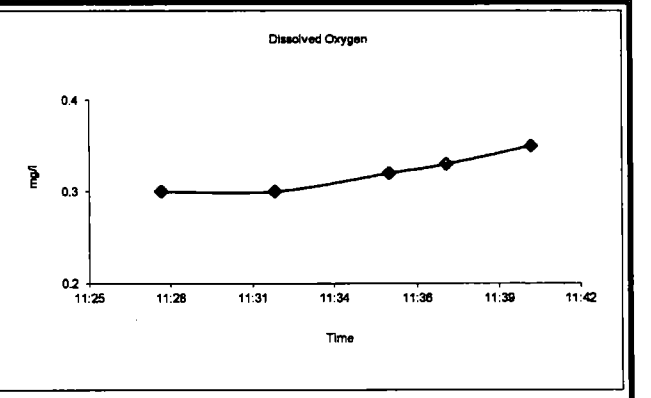

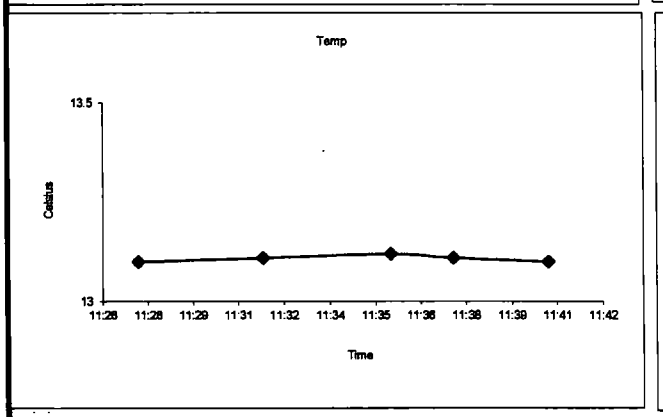

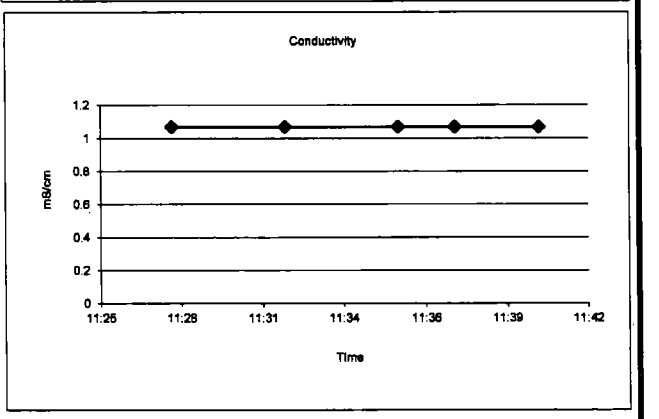

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	**Pump Inlet** (Ft.) TOC	108	**Lab Analysis**	VOCs (SW-846 8260)	**Well ID:**	**MW 205A**
Casing Stickup (Ft.)	-0.34	**Purge Method**	Low Flow Micro Purge	**Container**	40 mL VOA Vial	**Sample Date**	22-Nov-14
Total Well Depth (Ft.) TOC	110.27	**Purge Equip**	QED Air Diaphragm	**Sample Type**	Grab (Groundwater)	**Sampled by:**	Patrick Egan
Static Water Level (Ft.) TOC	2.53	**Field Analysis Method**	Flow Thru Analysis - 250 mL	**Preservation**	HCl / Ice	**Site Visitors:**	None
Water Thickness (Ft.)	107.74	**Field Analysis Equip**	YSI 556 MSP	**Sampling Period**	FALL 2014		

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
11:35							0	2.53	Static
11:43	7.18	0.46	12.95	155.8	1.202		500		clear
11:46	7.18	0.45	12.93	155.6	1.204		500	2.53	clear
11:49	7.18	0.45	12.94	155.3	1.204		500		clear
11:52	7.17	0.44	12.93	155.1	1.205		500		clear
11:55	7.17	0.46	12.93	154.9	1.206		500	2.53	clear
11:58	7.19	0.46	12.95	154.7	1.205	22	500		clear
MINUTES							**TOTAL LITERS**		
15.0	0.02	4.35%	0.15%	-0.40	0.00%		**7.50**		

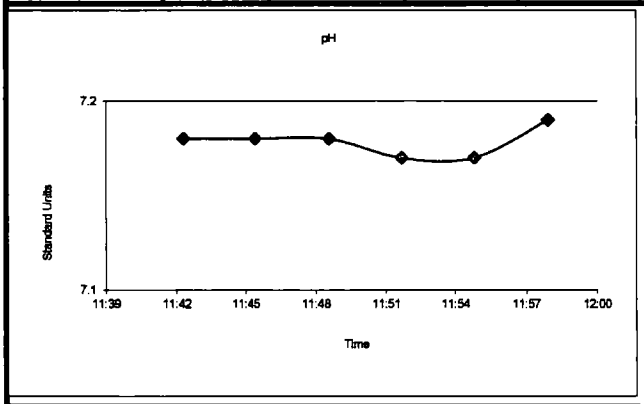

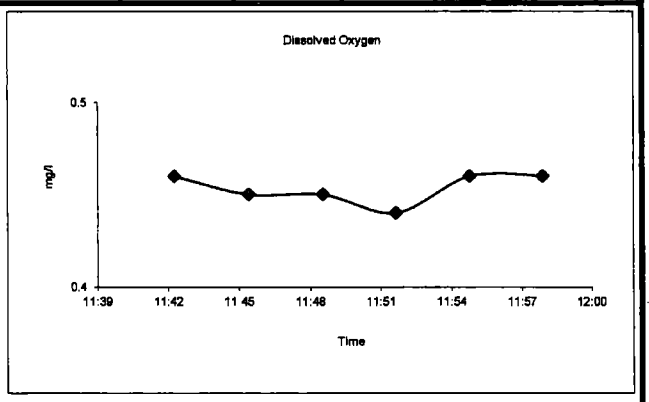

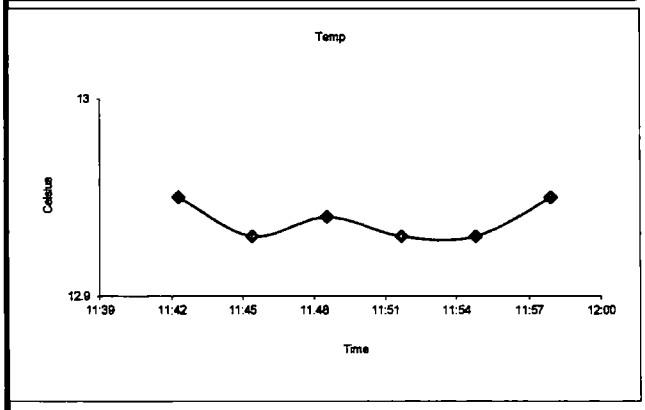

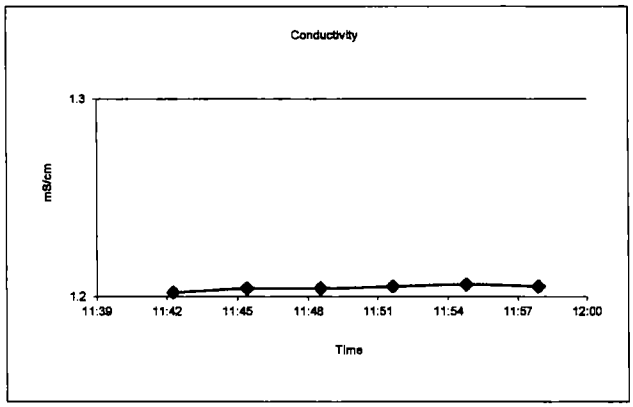

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	148	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 205B
Casing Stickup (Ft.)	-0.48	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	22-Nov-14
Total Well Depth (Ft.) TOC	150.05	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	2.47	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	147.58	Field Analysis Equip	YSI 556 MSP	Sampling Period	FALL 2014		

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
12:01							0	2.47	Static
12:04	7.17	0.41	12.97	153.3	1.198		480	2.47	clear
12:09	7.17	0.39	12.97	152.9	1.198		480		clear
12:13	7.17	0.43	12.97	152.5	1.198		480		clear
12:16	7.17	0.39	12.96	152	1.198		480	2.47	clear
12:20	7.17	0.42	12.97	151.4	1.198	20	480		clear
MINUTES							TOTAL LITERS		
16.0	0.00	-2.38%	0.00%	-1.10	0.00%		7.68		

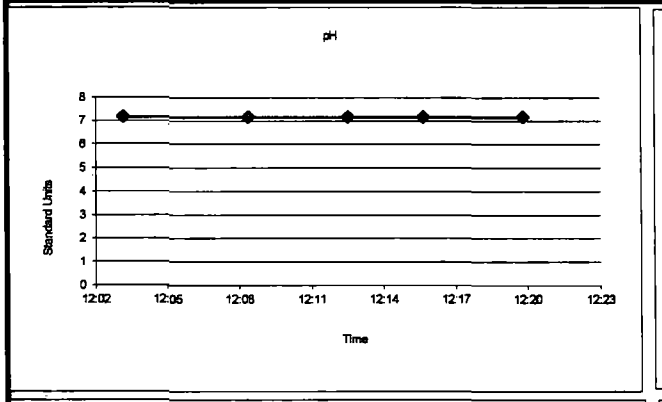

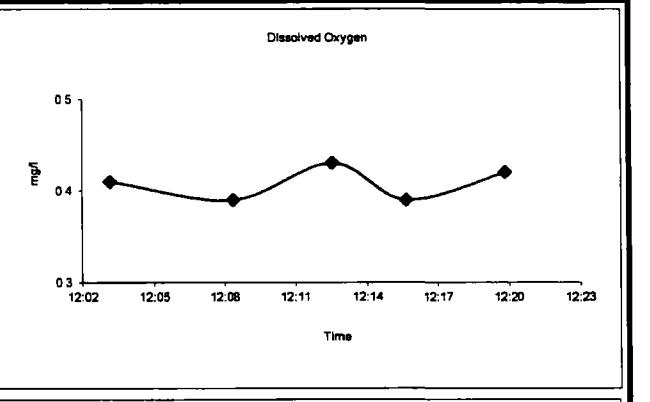

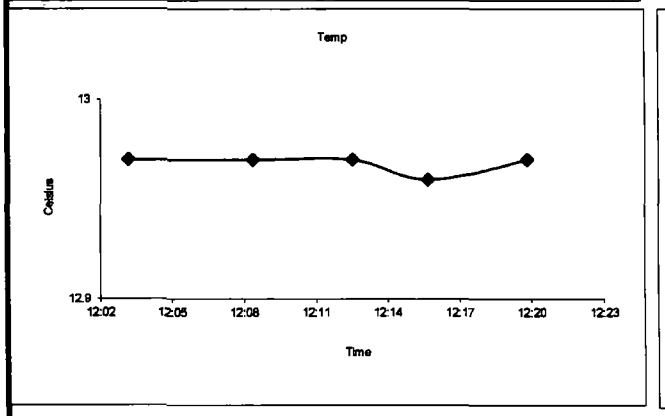

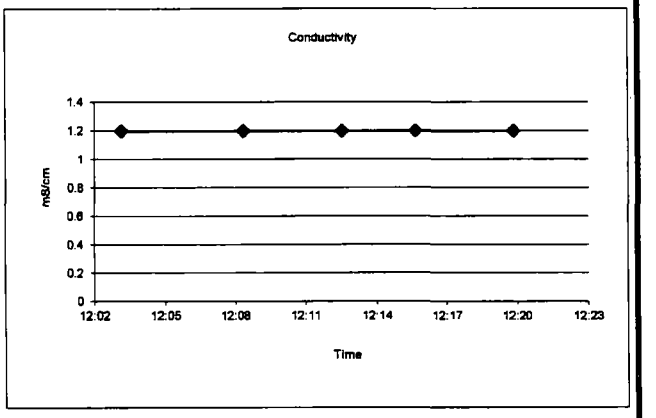

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	88	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 206A
Casing Stickup (Ft.)	-0.36	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	22-Nov-14
Total Well Depth (Ft.) TOC	90.24	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	4.16	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	86.08	Field Analysis Equip	YSI 556 MSP	Sampling Period	FALL 2014		

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
12:58							0	4.16	Static
13:12	7.33	1.26	12.43	133	0.856		450		Start Time
13:16	7.33	1.3	12.39	132.6	0.857		450	4.19	cloudy
13:19	7.33	1.27	12.42	132	0.856		450		cloudy
13:22	7.33	1.25	12.42	131.6	0.857		450	4.20	cloudy
13:26	7.33	1.26	12.42	131.2	0.856	49	450		clear
MINUTES							TOTAL LITERS		
14.0	0.00	-0.79%	0.00%	-0.80	0.00%		6.30		

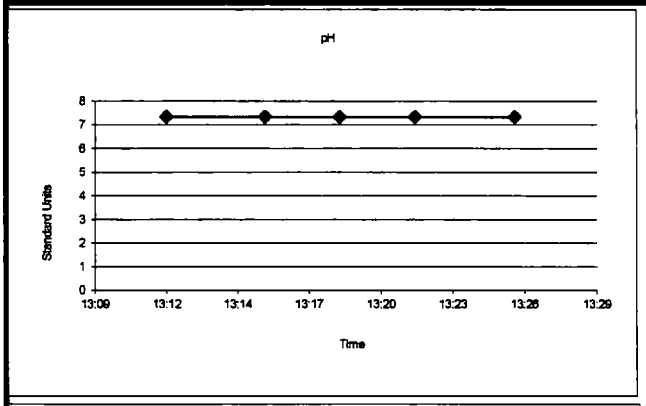

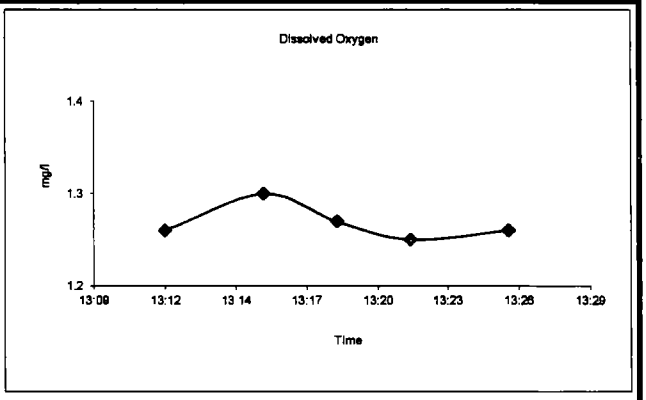

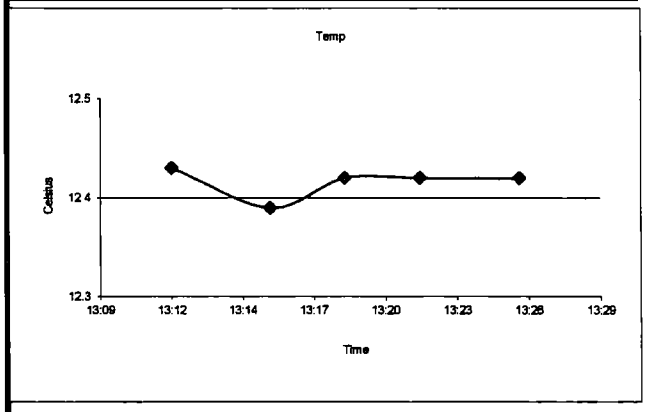

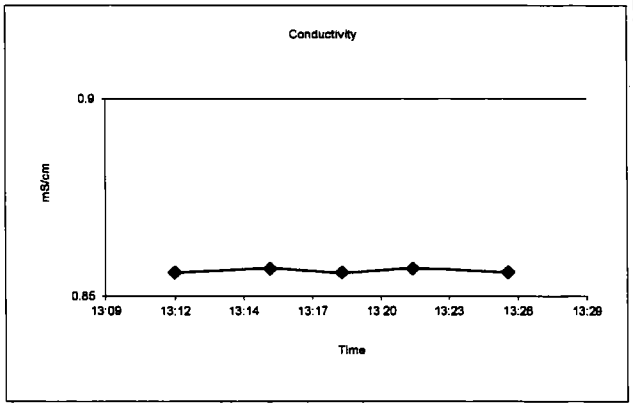

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	127	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 206B
Casing Stickup (Ft.)	-0.45	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	22-Nov-14
Total Well Depth (Ft.) TOC	129.94	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	2.46	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	127.48	Field Analysis Equip	YSI 556 MSP	Sampling Period	FALL 2014		

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
12:24							0	2.46	Static
12:32	7.23	0.45	12.45	153.3	1.035		500		Start Time
12:36	7.22	0.55	12.45	153.1	1.035		500		clear
12:40	7.22	0.43	12.44	152.8	1.035		500	2.46	clear
12:43	7.22	0.41	12.44	152.7	1.035		500		clear
12:46	7.22	0.42	12.44	152.4	1.035		500		clear
12:49	7.22	0.42	12.41	152.3	1.035	18	500	2.46	clear
MINUTES							TOTAL LITERS		
17.0	0.00	2.38%	-0.24%	-0.40	0.00%		8.50		

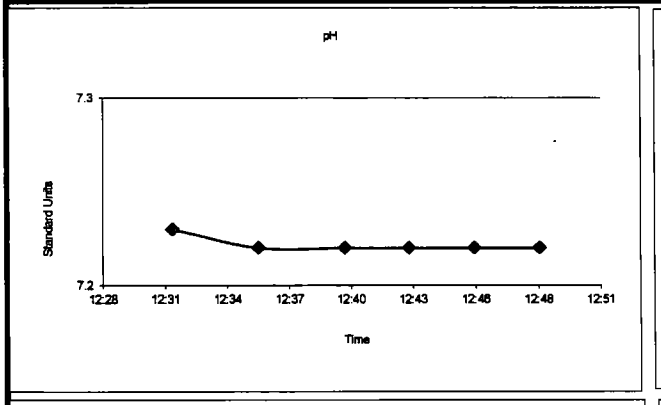

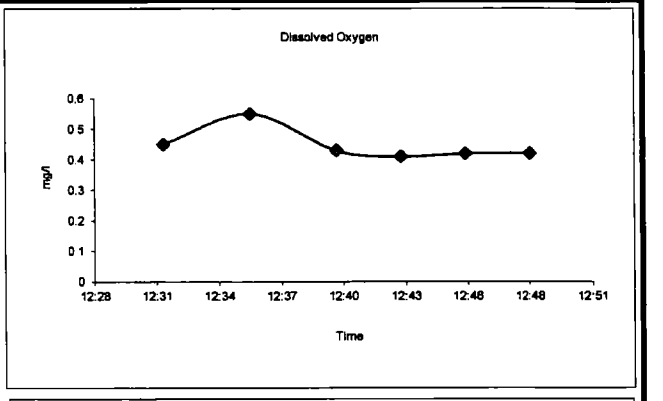

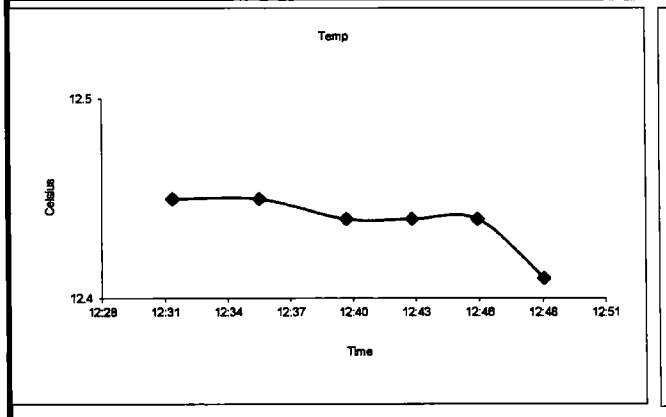

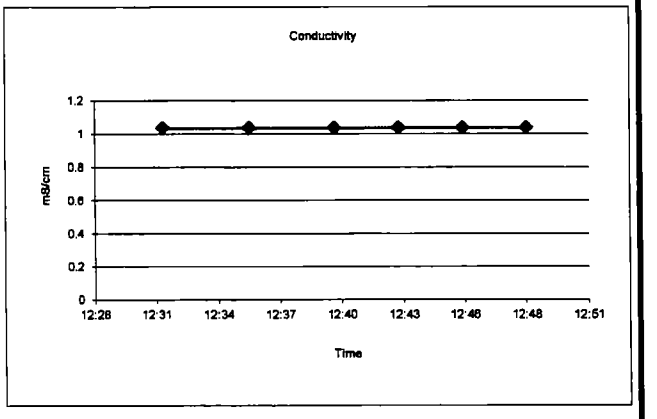

Remarks: (well condition, maintenance, etc...)

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (Inch)	2	Pump Inlet (Ft.) TOC	249	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 206C
Casing Stickup (Ft.)	-0.55	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	
Total Well Depth (Ft.) TOC	251.31	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC		Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	251.31	Field Analysis Equip	YSI 556 MSP	Sampling Period	FALL 2014		

FIELD PURGE MONITORING

Time	pH	DO	Temp	ORP	SpCond	TURB	Flow Rate	Well Level	Annotation
HH:MM	Standard Units	mg/l	°C	mV	mS/cm	FTU	mL/min	(Ft.) TOC	
0.0	0.00	0.00%	0.00%	0.00	0.00%		0.00		

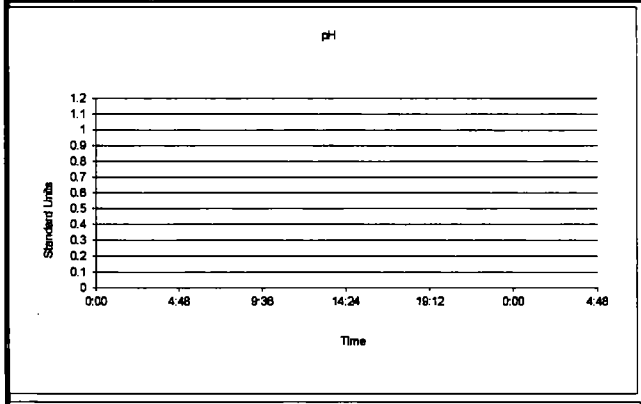

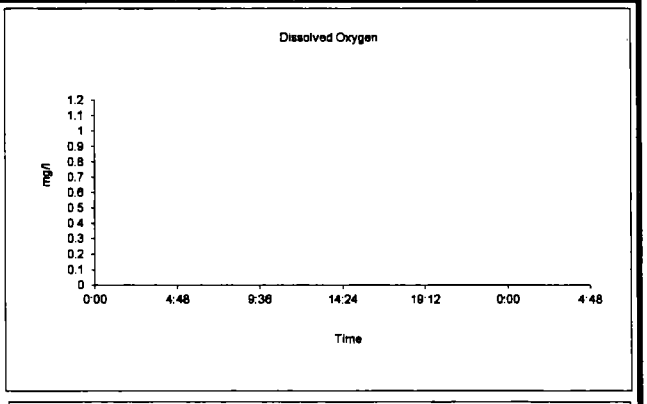

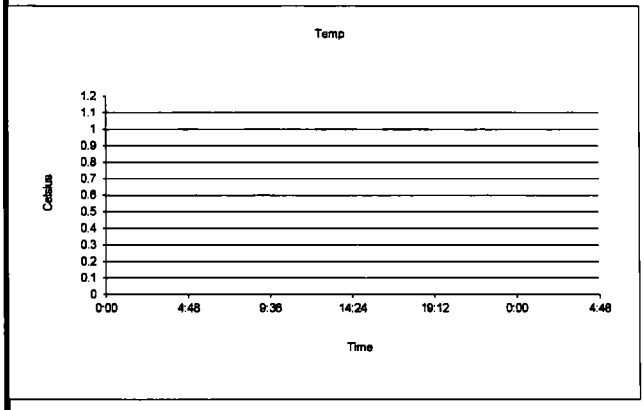

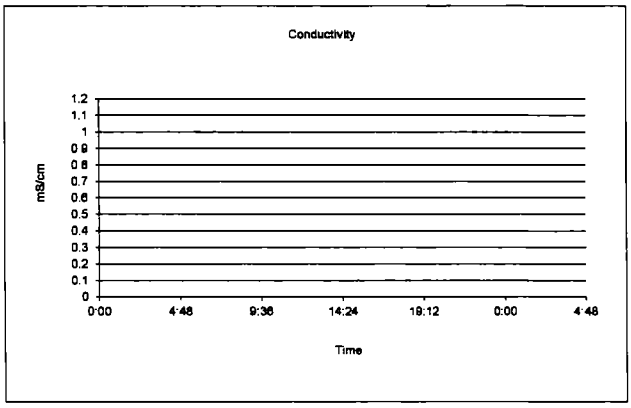

Remarks: (well condition, maintenance, etc...)

Inaccessible well - did not sample

SE Rockford Superfund Site Ground Water Sampling - Field Report

Casing Diameter (inch)	2	Pump Inlet (Ft.) TOC	88	Lab Analysis	VOCs (SW-846 8260)	Well ID:	MW 207
Casing Stickup (Ft.)	-0.3	Purge Method	Low Flow Micro Purge	Container	40 mL VOA Vial	Sample Date	23-Nov-14
Total Well Depth (Ft.) TOC	90.81	Purge Equip	QED Air Diaphragm	Sample Type	Grab (Groundwater)	Sampled by:	Patrick Egan
Static Water Level (Ft.) TOC	34.16	Field Analysis Method	Flow Thru Analysis - 250 mL	Preservation	HCl / Ice	Site Visitors:	None
Water Thickness (Ft.)	56.65	Field Analysis Equip	YSI 556 MSP	Sampling Period	FALL 2014		

FIELD PURGE MONITORING

Time HH:MM	pH Standard Units	DO mg/l	Temp °C	ORP mV	SpCond mS/cm	TURB FTU	Flow Rate mL/min	Well Level (Ft.) TOC	Annotation
9:50							0	34.16	Static
10:02	7.19	4.45	12.15	70.3	1.249		420		reddish brown cloudy
10:05	7.19	4.45	12.15	70.7	1.249		420	34.22	reddish brown cloudy
10:08	7.19	4.47	12.14	71.2	1.249		420		clear
10:11	7.19	4.44	12.14	71.6	1.249		420	34.23	clear
10:15	7.19	4.43	12.14	72	1.249	77	420		clear
MINUTES							TOTAL LITERS		
13.0	0.00	-0.90%	0.00%	0.80	0.00%		5.46		

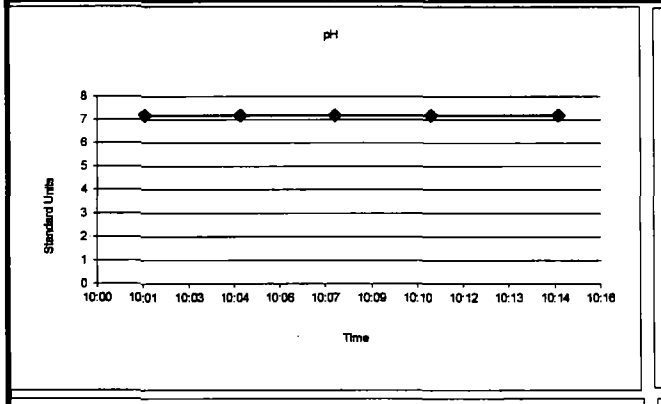

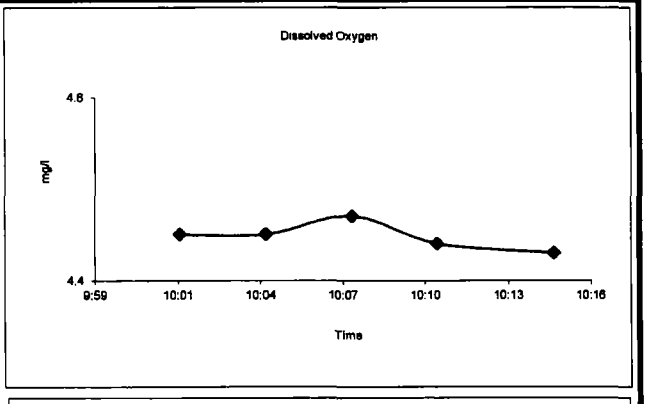

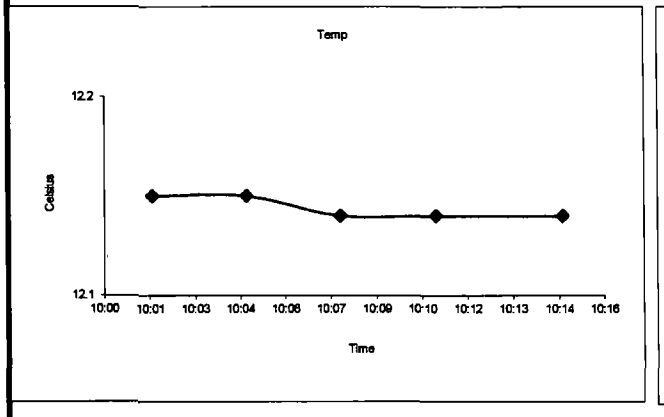

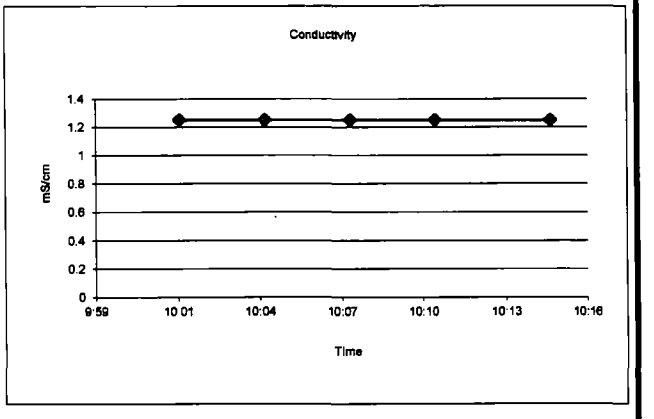

Remarks: (well condition, maintenance, etc...)
