PRELIMINARY ACM CLEANUP SCHEDULE AT MINILLAS NORTH TOWER (REV 2.0)

ID	Task Name	Calendar Days	Start	Finish	Predecess
1	**Cleanup Works**	**0**	**Mon 8/20/12**	**Thu 10/25/12**	
2	**General**	**10**	**Mon 8/20/12**	**Wed 8/29/12**	
3	1000 Submit Work Plan for EPA Approval	0	Mon 8/20/12	Mon 8/20/12	
4	1010 Work Plan EPA Approval	2	Mon 8/20/12	Tue 8/21/12	3
5	1030 Permits & Contracts Issuance	4	Wed 8/22/12	Sat 8/25/12	4
6	1040 Signing Asbestos Contractors (or subcontractors)	0	Sun 8/26/12	Sun 8/26/12	5
7	1050 Contractors Mobilization	0	Mon 8/27/12	Mon 8/27/12	6
8	**1055 Site Control & Decon Unit Installation**	**0**	**Tue 8/28/12**	**Tue 8/28/12**	**7**
9	Ground Floor Isolation, critical barriers, equipment decon & waste-load out construction, placement and testing of the required number of negative air machines/equipment	0	Wed 8/29/12	Wed 8/29/12	
10	1060 Order to Proceed	0	Wed 8/29/12	Wed 8/29/12	8
11	**Work area: South Elevator Shaft and Cabins (Cars)-See Appendix III**	**8**	**Sat 8/25/12**	**Mon 9/3/12**	
12	1065 Confirm the sealing integrity of the south elevators doors (as applicable)	0	Sat 8/25/12	Sat 8/25/12	
13	1066 Placement and testing of the required number of negative air machines/equipment	0	Sat 8/25/12	Sat 8/25/12	12
14	**1067 Cleanup Activities**	**4**	**Sat 8/25/12**	**Tue 8/28/12**	**13**
15	Interior and exterior elevators Cabins (cars) cleanup	1	Sat 8/25/12	Sat 8/25/12	
16	Cleanup of Elevator Shaft walls and pit basin	1	Sun 8/26/12	Sun 8/26/12	
17	Clearance Sampling of the three south cars	1	Mon 8/27/12	Mon 8/27/12	
18	Clearance Sampling of the three south cars	1	Tue 8/28/12	Tue 8/28/12	
19	1068 Final Clearance Sampling	0	Wed 8/29/12	Wed 8/29/12	14
20	1069 EPA Review of Clearance & Results	5	Thu 8/30/12	Mon 9/3/12	19
21	**Work area: Air conditioning system supply and return ducts -See Appendix II**	**10**	**Wed 8/29/12**	**Fri 9/7/12**	
22	1070 Placement and testing of the required number of negative air machines/equipment	0	Wed 8/29/12	Wed 8/29/12	
23	1071 Clean up the supply and return duct from Levels 17 to 9 and then from Levels 8 to Promenade (ground level has independently A/C units to be cleaned as well)	2	Wed 8/29/12	Thu 8/30/12	
24	1072 Block air transfer grilles for each floor through the installation of critical barriers	0	Fri 8/31/12	Fri 8/31/12	
25	1073 Clearance Sampling of the ducts	0	Sat 9/1/12	Sat 9/1/12	
26	1074 Isolation and Seal until receiving clearance sample results	0	Sun 9/2/12	Sun 9/2/12	
27	1075 EPA Review of Clearances and results	5	Mon 9/3/12	Fri 9/7/12	
28					
29	**Work area: Elevator machine (mechanical) room-See Appendix II**	**7**	**Wed 8/29/12**	**Wed 9/5/12**	
30	**1080 Installation of temporary containment isolation barriers/decontamination unit/waste load-out unit**	**0**	**Wed 8/29/12**	**Wed 8/29/12**	
31	Installation of Decontamination unit at entrance of the work area	0	Wed 8/29/12	Wed 8/29/12	
32	Placement, as applicable, of Critical Barriers	0	Wed 8/29/12	Wed 8/29/12	
33	Placement and testing of the required number of negative air machines/equipment	0	Wed 8/29/12	Wed 8/29/12	
34	Installation of Equipment Decontamination and Bag-out unit per work area, as applicable	0	Wed 8/29/12	Wed 8/29/12	
35	1085 Cleanup Activities	4	Wed 8/29/12	Sat 9/1/12	30
36	1090 Final Clearance Sampling	0	Thu 8/30/12	Thu 8/30/12	35
37	1100 EPA's Review of Clearance & Results	0	Fri 8/31/12	Fri 8/31/12	36
38	1110 Isolation & Seal after clearance criteria acceptance	5	Sat 9/1/12	Wed 9/5/12	37
39	**Work area: 17th Level-See Appendix II**	**10**	**Fri 8/31/12**	**Mon 9/10/12**	
40	**1120 Installation of temporary containment isolation barriers/decontamination unit/waste load-out unit**	**0**	**Fri 8/31/12**	**Fri 8/31/12**	
41	Installation of Decontamination unit at entrance of the work area	0	Fri 8/31/12	Fri 8/31/12	
42	Placement, as applicable, of Critical Barriers	0	Fri 8/31/12	Fri 8/31/12	
43	Placement and testing of the required number of negative air machines/equipment	0	Fri 8/31/12	Fri 8/31/12	
44	Installation of Equipment Decontamination and Bag-out unit per work area, as applicable	0	Fri 8/31/12	Fri 8/31/12	
45	1130 Cleanup Activities	4	Fri 8/31/12	Mon 9/3/12	40
46	1140 Final Clearance Sampling	0	Tue 9/4/12	Tue 9/4/12	45
47	1150 EPA's Review of Clearance & Results	0	Wed 9/5/12	Wed 9/5/12	46
48	1160 Isolation & Seal after clearance criteria acceptance	5	Thu 9/6/12	Mon 9/10/12	47
49					
50	**Work area: 16th Level-See Appendix II**	**11**	**Tue 9/4/12**	**Fri 9/14/12**	
51	**1170 Installation of temporary containment isolation barriers/decontamination unit/waste load-out unit**	**0**	Tue 9/4/12	Tue 9/4/12	
52	Installation of Decontamination unit at entrance of the work area	**0**	Tue 9/4/12	Tue 9/4/12	
53	Placement, as applicable, of Critical Barriers	**0**	Tue 9/4/12	Tue 9/4/12	
54	Placement and testing of the required number of negative air machines/equipment	**0**	Tue 9/4/12	Tue 9/4/12	
55	Installation of Equipment Decontamination and Bag-out unit per work area, as applicable	**0**	Tue 9/4/12	Tue 9/4/12	
56	Re-confirmation Assessment of Ceiling Stucco condition and response action further determination	**0**	Tue 9/4/12	Tue 9/4/12	
57	1180 Cleanup Activities	4	Tue 9/4/12	Fri 9/7/12	51
58	1190 Final Clearance Sampling	1	Sat 9/8/12	Sat 9/8/12	57
59	1200 EPA's Review of Clearance & Results	0	Sun 9/9/12	Sun 9/9/12	58
60	1210 Isolation & Seal after clearance criteria acceptance	5	Mon 9/10/12	Fri 9/14/12	59
61					
62	**Work area: 15th Level-See Appendix II**	**11**	**Sat 9/8/12**	**Tue 9/18/12**	
63	**1220 Installation of temporary containment isolation barriers/decontamination unit/waste load-out unit**	**1**	**Sat 9/8/12**	**Sat 9/8/12**	
64	Installation of Decontamination unit at entrance of the work area	**0**	Sat 9/8/12	Sat 9/8/12	
65	Placement, as applicable, of Critical Barriers	**0**	Sat 9/8/12	Sat 9/8/12	

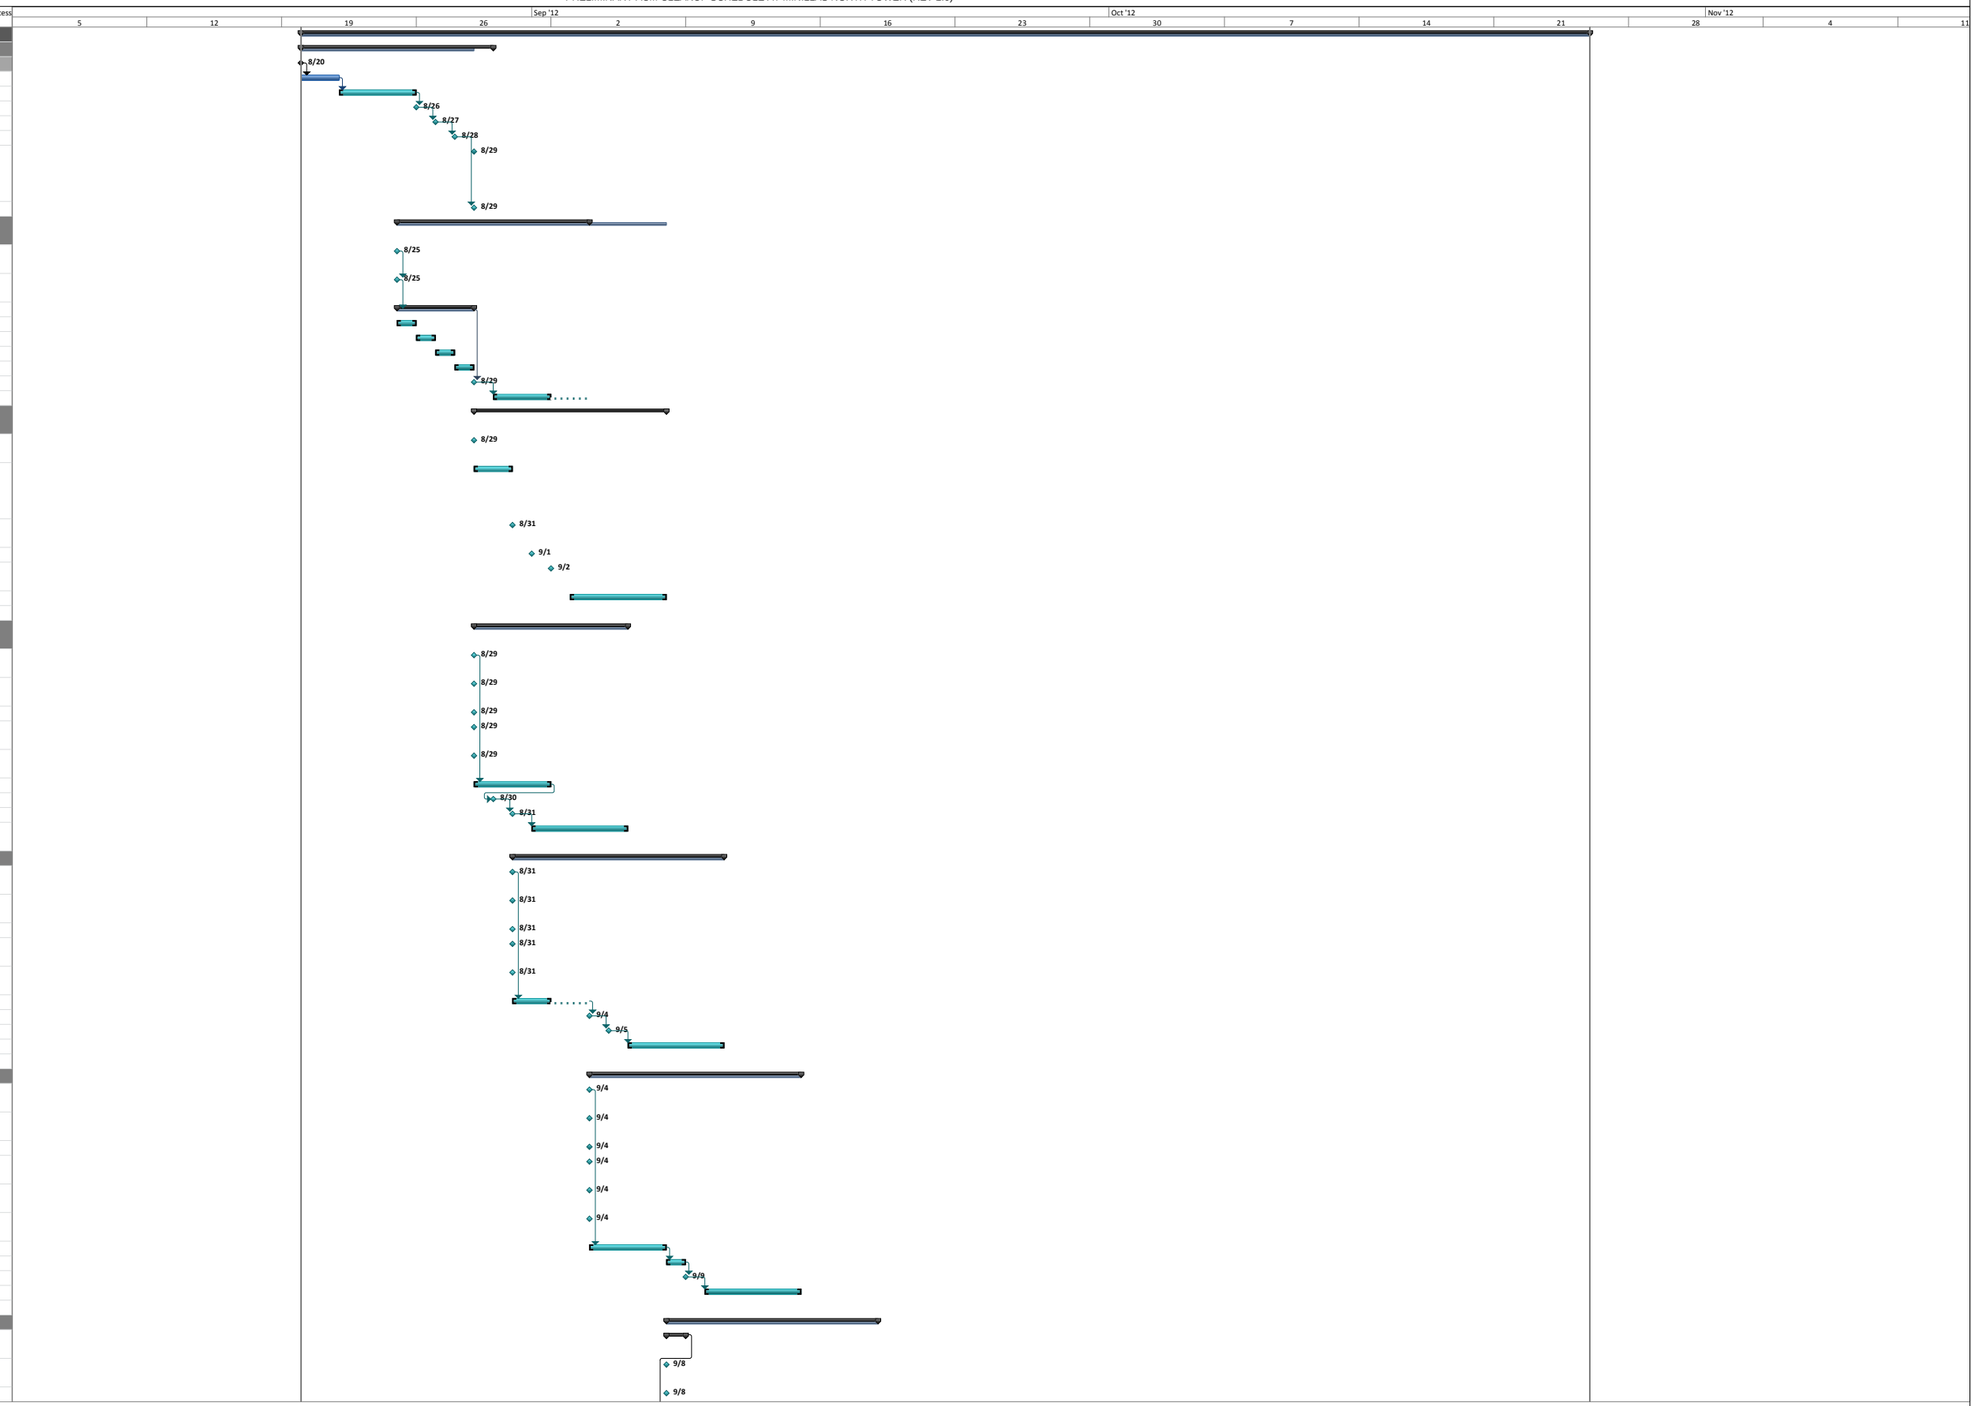

Project: Preliminary ACM Cleanup Schedule for Minillas North Tower
Note: The start date is August 14, 2012 or as approved.

(REV 2.0) Date: Mon 8/20/12

Task | Split | Milestone | Summary | Project Summary | External Tasks | External Milestone | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | Deadline | Progress

"The given *Calendar days* are only for guidance purposes, are estimated, subject to change and subject to the availability of the contractors".

PRELIMINARY ACM CLEANUP SCHEDULE AT MINILLAS NORTH TOWER (REV 2.0)

ID	Task Name	Calendar Days	Start	Finish	Predecess
66	Placement and testing of the required number of negative air machines/equipment	0	Sat 9/8/12	Sat 9/8/12	
67	Installation of Equipment Decontamination and Bag-out unit per work area, as applicable	0	Sat 9/8/12	Sat 9/8/12	
68	1230 Cleanup Activities	4	Sat 9/8/12	Tue 9/11/12	63
69	1240 Final Clearance Sampling	0	Wed 9/12/12	Wed 9/12/12	68
70	1250 EPA's Review of Clearance & Results	0	Thu 9/13/12	Thu 9/13/12	69
71	1260 Isolation & Seal after clearance criteria acceptance	5	Fri 9/14/12	Tue 9/18/12	70
72					
73	**Work area: 14th Level-See Appendix II**	**11**	**Wed 9/12/12**	**Sat 9/22/12**	
74	**1270 Installation of temporary containment isolation barriers/decontamination unit/waste load-out unit**	**0**	**Wed 9/12/12**	**Wed 9/12/12**	
75	Installation of Decontamination unit at entrance of the work area	0	Wed 9/12/12	Wed 9/12/12	
76	Placement, as applicable, of Critical Barriers	0	Wed 9/12/12	Wed 9/12/12	
77	Placement and testing of the required number of negative air machines/equipment	0	Wed 9/12/12	Wed 9/12/12	
78	Installation of Equipment Decontamination and Bag-out unit per work area, as applicable	0	Wed 9/12/12	Wed 9/12/12	
79	1280 Cleanup Activities	4	Wed 9/12/12	Sat 9/15/12	74
80	1290 Final Clearance Sampling	0	Sun 9/16/12	Sun 9/16/12	79
81	1310 EPA Review of Clearance & Results	5	Tue 9/18/12	Sat 9/22/12	82
82	1300 Isolation & Seal after clearance criteria acceptance	0	Mon 9/17/12	Mon 9/17/12	80
83					
84	**Work area: 13th Level-See Appendix II**	**11**	**Sun 9/16/12**	**Wed 9/26/12**	
85	**1320 Installation of temporary containment isolation barriers/decontamination unit/waste load-out unit**	**0**	**Sun 9/16/12**	**Sun 9/16/12**	
86	Installation of Decontamination unit at entrance of the work area	0	Sun 9/16/12	Sun 9/16/12	
87	Placement, as applicable, of Critical Barriers	0	Sun 9/16/12	Sun 9/16/12	
88	Placement and testing of the required number of negative air machines/equipment	0	Sun 9/16/12	Sun 9/16/12	
89	Installation of Equipment Decontamination and Bag-out unit per work area, as applicable	0	Sun 9/16/12	Sun 9/16/12	
90	1330 Cleanup Activities	4	Sun 9/16/12	Wed 9/19/12	85
91	1340 Final Clearance Sampling	0	Thu 9/20/12	Thu 9/20/12	90
92	1350 EPA's Review of Clearance & Results	0	Fri 9/21/12	Fri 9/21/12	91
93	1360 Isolation & Seal after clearance criteria acceptance	5	Sat 9/22/12	Wed 9/26/12	92
94					
95	**Work area: 12th Level-See Appendix II**	**11**	**Thu 9/20/12**	**Sun 9/30/12**	
96	**1370 Installation of temporary containment isolation barriers/decontamination unit/waste load-out unit**	**0**	**Thu 9/20/12**	**Thu 9/20/12**	
97	Installation of Decontamination unit at entrance of the work area	0	Thu 9/20/12	Thu 9/20/12	
98	Placement, as applicable, of Critical Barriers	0	Thu 9/20/12	Thu 9/20/12	
99	Placement and testing of the required number of negative air machines/equipment	0	Thu 9/20/12	Thu 9/20/12	
100	Installation of Equipment Decontamination and Bag-out unit per work area, as applicable	0	Thu 9/20/12	Thu 9/20/12	
101	Re-confirmation Assessment of Ceiling Stucco condition and response action further determination	0	Thu 9/20/12	Thu 9/20/12	
102	1380 Cleanup Activities	4	Thu 9/20/12	Sun 9/23/12	96
103	1390 Final Clearance Sampling	0	Mon 9/24/12	Mon 9/24/12	102
104	1400 EPA's Review of Clearance & Results	0	Tue 9/25/12	Tue 9/25/12	103
105	1410 Isolation & Seal after clearance criteria acceptance	5	Wed 9/26/12	Sun 9/30/12	104
106					
107	**Work area: 11th Level-See Appendix II**	**11**	**Mon 9/24/12**	**Thu 10/4/12**	
108	**1420 Installation of temporary containment isolation barriers/decontamination unit/waste load-out unit**	**0**	**Mon 9/24/12**	**Mon 9/24/12**	
109	Installation of Decontamination unit at entrance of the work area	0	Mon 9/24/12	Mon 9/24/12	
110	Placement, as applicable, of Critical Barriers	0	Mon 9/24/12	Mon 9/24/12	
111	Placement and testing of the required number of negative air machines/equipment	0	Mon 9/24/12	Mon 9/24/12	
112	Installation of Equipment Decontamination and Bag-out unit per work area, as applicable	0	Mon 9/24/12	Mon 9/24/12	
113	Re-confirmation Assessment of Ceiling Stucco condition and response action further determination	0	Mon 9/24/12	Mon 9/24/12	
114	1430 Cleanup Activities	4	Mon 9/24/12	Thu 9/27/12	108
115	1440 Final Clearance Sampling	0	Fri 9/28/12	Fri 9/28/12	114
116	1460 EPA Review of Clearance & Results	5	Sun 9/30/12	Thu 10/4/12	117
117	1450 Isolation & Seal after clearance criteria acceptance	0	Sat 9/29/12	Sat 9/29/12	115
118					
119	**Work area: 10th Level-See Appendix II**	**11**	**Fri 9/28/12**	**Mon 10/8/12**	
120	**1470 Installation of temporary containment isolation barriers/decontamination unit/waste load-out unit**	**0**	**Fri 9/28/12**	**Fri 9/28/12**	
121	Installation of Decontamination unit at entrance of the work area	0	Fri 9/28/12	Fri 9/28/12	
122	Placement, as applicable, of Critical Barriers	0	Fri 9/28/12	Fri 9/28/12	
123	Placement and testing of the required number of negative air machines/equipment	0	Fri 9/28/12	Fri 9/28/12	
124	Installation of Equipment Decontamination and Bag-out unit per work area, as applicable	0	Fri 9/28/12	Fri 9/28/12	
125	Re-confirmation Assessment of Ceiling Stucco condition and response action further determination	0	Fri 9/28/12	Fri 9/28/12	
126	1480 Cleaning & Decontamination Activities	4	Fri 9/28/12	Mon 10/1/12	120
127	1490 Final Clearance Sampling	1	Tue 10/2/12	Tue 10/2/12	126
128	1500 Isolation & Seal Floors	1	Wed 10/3/12	Wed 10/3/12	127
129	1510 EPA Review of Clearance & Results	5	Thu 10/4/12	Mon 10/8/12	128
130					
131	**Work area: 9th Level-See Appendix II**	**11**	**Tue 10/2/12**	**Fri 10/12/12**	
132	**1520 Installation of temporary containment isolation barriers/decontamination unit/waste load-out unit**	**1**	**Tue 10/2/12**	**Tue 10/2/12**	
133	Installation of Decontamination unit at entrance of the work area	0	Tue 10/2/12	Tue 10/2/12	

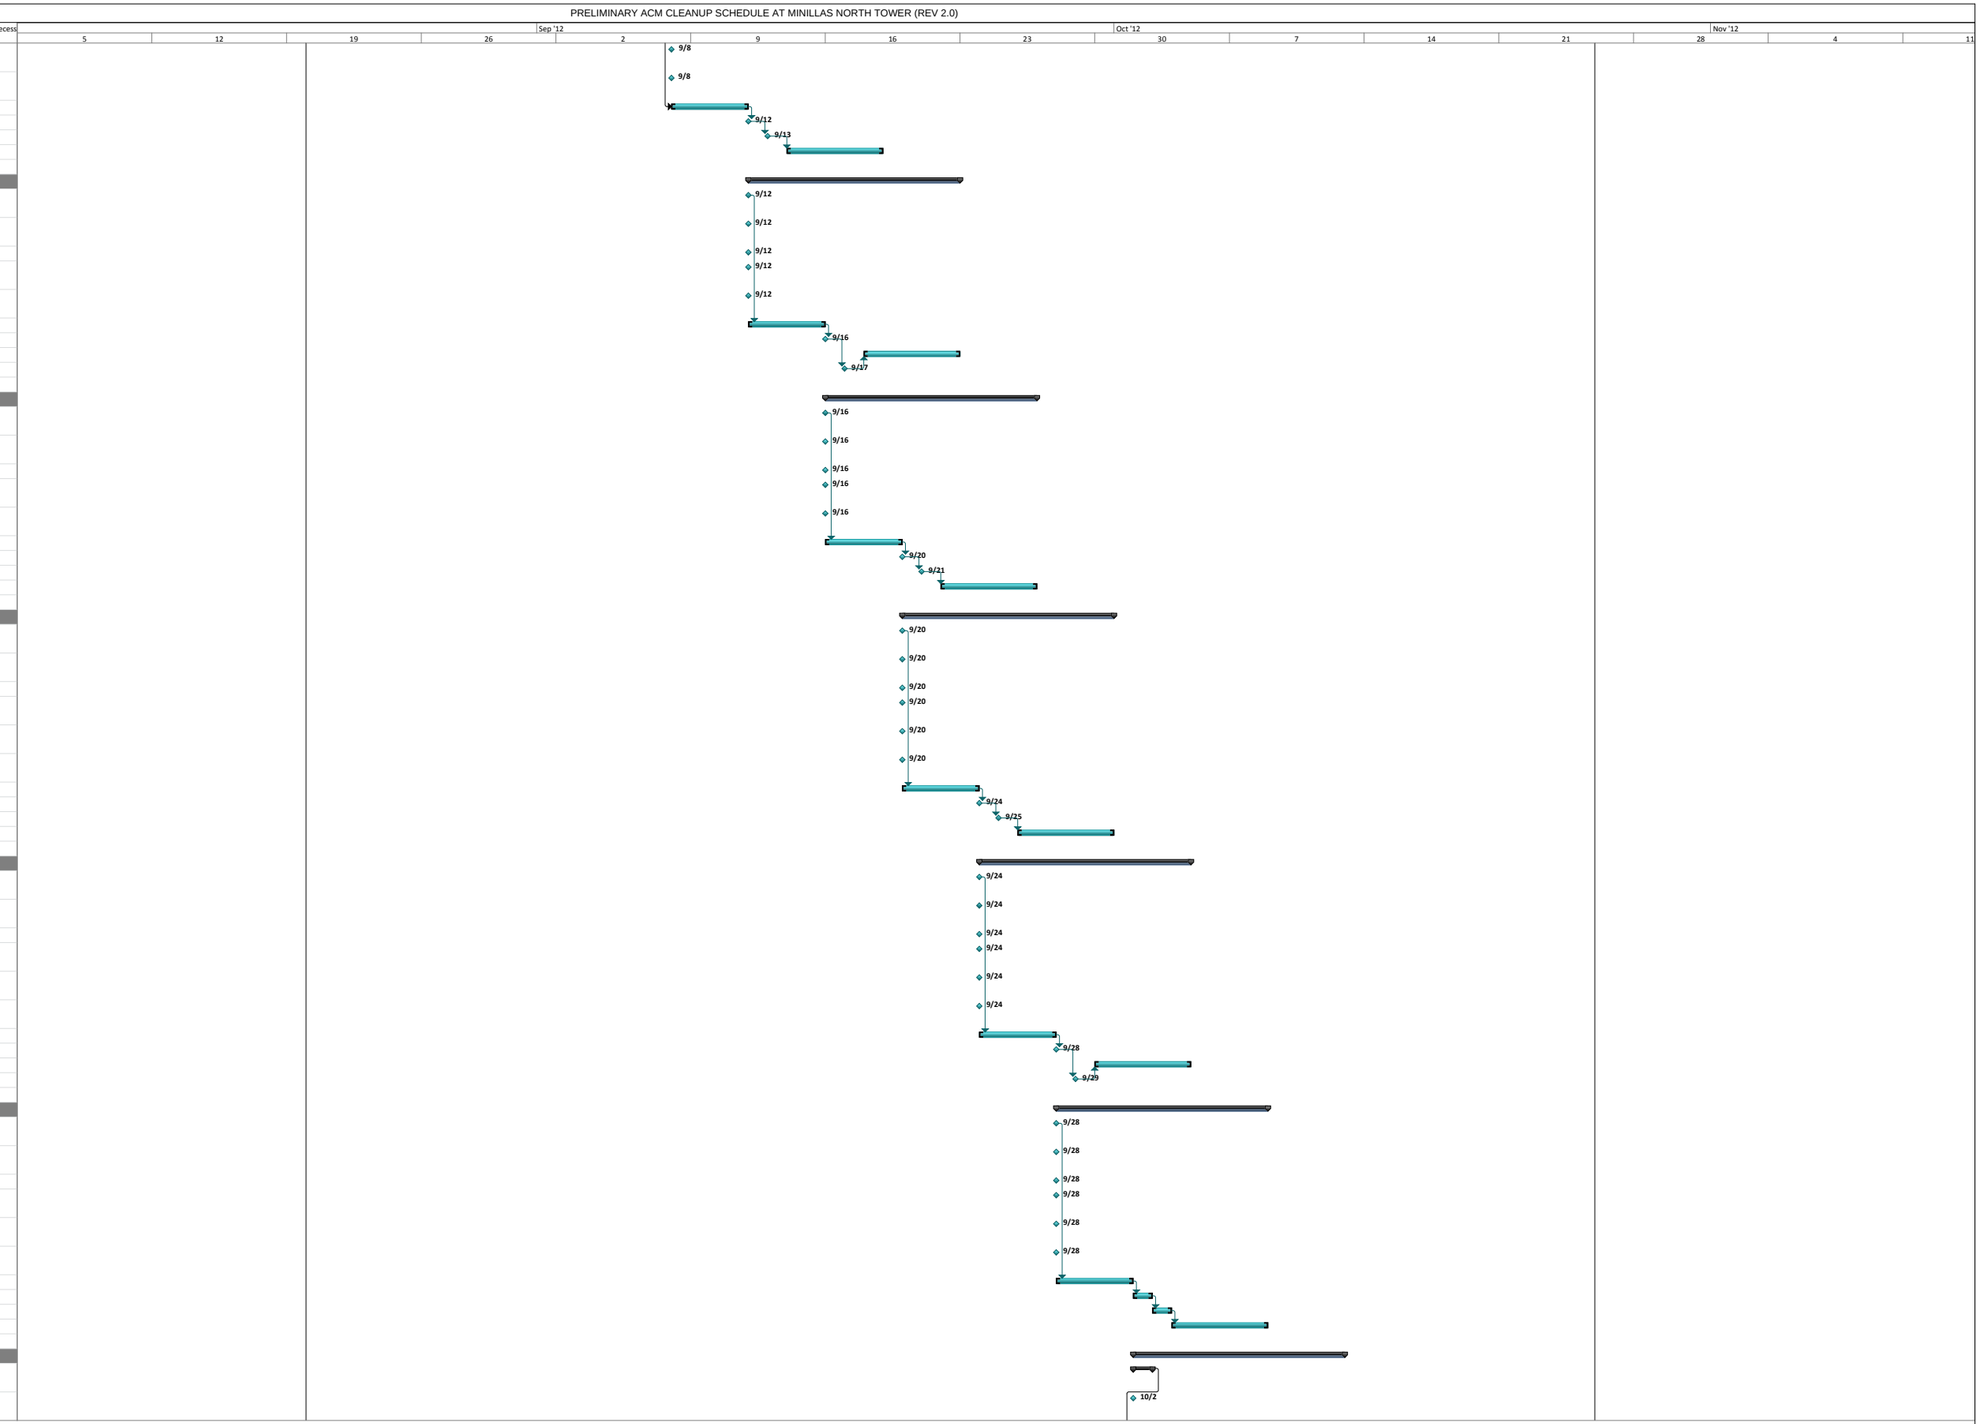

Project: Preliminary ACM Cleanup Schedule for Minillas North Tower
Note: The start date is August 14, 2012 or as approved.

(REV 2.0) Date: Mon 8/20/12

Task | Split | Milestone | Summary | Project Summary | External Tasks | External Milestone | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | Deadline | Progress

"The given *Calendar days* are only for guidance purposes, are estimated, subject to change and subject to the availability of the contractors".

PRELIMINARY ACM CLEANUP SCHEDULE AT MINILLAS NORTH TOWER (REV 2.0)

ID	Task Name	Calendar Days	Start	Finish	Predecess
134	Placement, as applicable, of Critical Barriers	0	Tue 10/2/12	Tue 10/2/12	
135	Placement and testing of the required number of negative air machines/equipment	0	Tue 10/2/12	Tue 10/2/12	
136	Installation of Equipment Decontamination and Bag-out unit per work area, as applicable	0	Tue 10/2/12	Tue 10/2/12	
137	1530 Cleanup Activities	4	Tue 10/2/12	Fri 10/5/12	132
138	1540 Final Clearance Sampling	1	Sat 10/6/12	Sat 10/6/12	137
139	1550 EPA's Review of Clearance & Results	1	Sun 10/7/12	Sun 10/7/12	138
140	1560 Isolation & Seal after clearance criteria acceptance	5	Mon 10/8/12	Fri 10/12/12	139
141					
142	**Work area: Promenade (P) Level-See Appendix II**	**11**	**Fri 8/31/12**	**Mon 9/10/12**	
143	**1570 Installation of temporary containment isolation barriers/decontamination unit/waste load-out unit**	**1**	**Fri 8/31/12**	**Fri 8/31/12**	
144	Installation of Decontamination unit at entrance of the work area	0	Fri 8/31/12	Fri 8/31/12	
145	Placement, as applicable, of Critical Barriers	0	Fri 8/31/12	Fri 8/31/12	
146	Placement and testing of the required number of negative air machines/equipment	0	Fri 8/31/12	Fri 8/31/12	
147	Installation of Equipment Decontamination and Bag-out unit per work area, as applicable	0	Fri 8/31/12	Fri 8/31/12	
148	1580 Cleanup Activities	4	Fri 8/31/12	Mon 9/3/12	143
149	1590 Final Clearance Sampling	1	Tue 9/4/12	Tue 9/4/12	148
150	1600 EPA's Review of Clearance & Results	5	Wed 9/5/12	Sun 9/9/12	149
151	1610 Isolation & Seal after clearance criteria acceptance	1	Mon 9/10/12	Mon 9/10/12	150
152					
153	**Work area: 2nd Level-See Appendix II**	**11**	**Tue 9/4/12**	**Fri 9/14/12**	
154	**1620 Installation of temporary containment isolation barriers/decontamination unit/waste load-out unit**	**0**	**Tue 9/4/12**	**Tue 9/4/12**	
155	Installation of Decontamination unit at entrance of the work area	0	Tue 9/4/12	Tue 9/4/12	
156	Placement, as applicable, of Critical Barriers	0	Tue 9/4/12	Tue 9/4/12	
157	Placement and testing of the required number of negative air machines/equipment	0	Tue 9/4/12	Tue 9/4/12	
158	Installation of Equipment Decontamination and Bag-out unit per work area, as applicable	0	Tue 9/4/12	Tue 9/4/12	
159	Re-confirmation Assessment of Ceiling Stucco condition and response action further determination	0	Tue 9/4/12	Tue 9/4/12	
160	1630 Cleanup Activities	4	Tue 9/4/12	Fri 9/7/12	154
161	1640 Final Clearance Sampling	0	Sat 9/8/12	Sat 9/8/12	160
162	1650 EPA's Review of Clearance & Results	5	Sun 9/9/12	Thu 9/13/12	161
163	1660 Isolation & Seal after clearance criteria acceptance	1	Fri 9/14/12	Fri 9/14/12	162
164					
165	**Work area: 3rd Level-See Appendix II**	**11**	**Sat 9/8/12**	**Tue 9/18/12**	
166	**1670 Installation of temporary containment isolation barriers/decontamination unit/waste load-out unit**	**0**	**Sat 9/8/12**	**Sat 9/8/12**	
167	Installation of Decontamination unit at entrance of the work area	0	Sat 9/8/12	Sat 9/8/12	
168	Placement, as applicable, of Critical Barriers	0	Sat 9/8/12	Sat 9/8/12	
169	Placement and testing of the required number of negative air machines/equipment	0	Sat 9/8/12	Sat 9/8/12	
170	Installation of Equipment Decontamination and Bag-out unit per work area, as applicable	0	Sat 9/8/12	Sat 9/8/12	
171	1680 Cleanup Activities	4	Sat 9/8/12	Tue 9/11/12	166
172	1690 Final Clearance Sampling	0	Wed 9/12/12	Wed 9/12/12	171
173	1700 EPA's Review of Clearance & Results	5	Thu 9/13/12	Mon 9/17/12	172
174	1710 Isolation & Seal after clearance criteria acceptance	1	Tue 9/18/12	Tue 9/18/12	173
175					
176	**Work area: 4th Level-See Appendix II**	**11**	**Wed 9/12/12**	**Sat 9/22/12**	
177	**1720 Installation of temporary containment isolation barriers/decontamination unit/waste load-out unit**	**0**	**Wed 9/12/12**	**Wed 9/12/12**	
178	Installation of Decontamination unit at entrance of the work area	0	Wed 9/12/12	Wed 9/12/12	
179	Placement, as applicable, of Critical Barriers	0	Wed 9/12/12	Wed 9/12/12	
180	Placement and testing of the required number of negative air machines/equipment	0	Wed 9/12/12	Wed 9/12/12	
181	Installation of Equipment Decontamination and Bag-out unit per work area, as applicable	0	Wed 9/12/12	Wed 9/12/12	
182	Re-confirmation Assessment of Ceiling Stucco condition and response action further determination	0	Wed 9/12/12	Wed 9/12/12	
183	1730 Cleanup Activities	4	Wed 9/12/12	Sat 9/15/12	177
184	1740 Final Clearance Sampling	0	Sun 9/16/12	Sun 9/16/12	183
185	1750 EPA Review of Clearance & Results	5	Mon 9/17/12	Fri 9/21/12	186
186	1760 Isolation & Seal after clearance criteria acceptance	0	Sat 9/22/12	Sat 9/22/12	184
187					
188	**Work area: 5th Level-See Appendix II**	**11**	**Sun 9/16/12**	**Wed 9/26/12**	
189	**1770 Installation of temporary containment isolation barriers/decontamination unit/waste load-out unit**	**0**	**Sun 9/16/12**	**Sun 9/16/12**	
190	Installation of Decontamination unit at entrance of the work area	0	Sun 9/16/12	Sun 9/16/12	
191	Placement, as applicable, of Critical Barriers	0	Sun 9/16/12	Sun 9/16/12	
192	Placement and testing of the required number of negative air machines/equipment	0	Sun 9/16/12	Sun 9/16/12	
193	Installation of Equipment Decontamination and Bag-out unit per work area, as applicable	0	Sun 9/16/12	Sun 9/16/12	
194	Re-confirmation Assessment of Ceiling Stucco condition and response action further determination	0	Sun 9/16/12	Sun 9/16/12	
195	1780 Cleanup Activities	4	Sun 9/16/12	Wed 9/19/12	189
196	1790 Final Clearance Sampling	0	Thu 9/20/12	Thu 9/20/12	195
197	1800 EPA's Review of Clearance & Results	5	Fri 9/21/12	Tue 9/25/12	196
198	1810 Isolation & Seal after clearance criteria acceptance	1	Wed 9/26/12	Wed 9/26/12	197
199					
200	**Work area: 6th Level-See Appendix II**	**11**	**Thu 9/20/12**	**Sun 9/30/12**	
201	**1820 Installation of temporary containment isolation barriers/decontamination unit/waste load-out unit**	**0**	**Thu 9/20/12**	**Thu 9/20/12**	

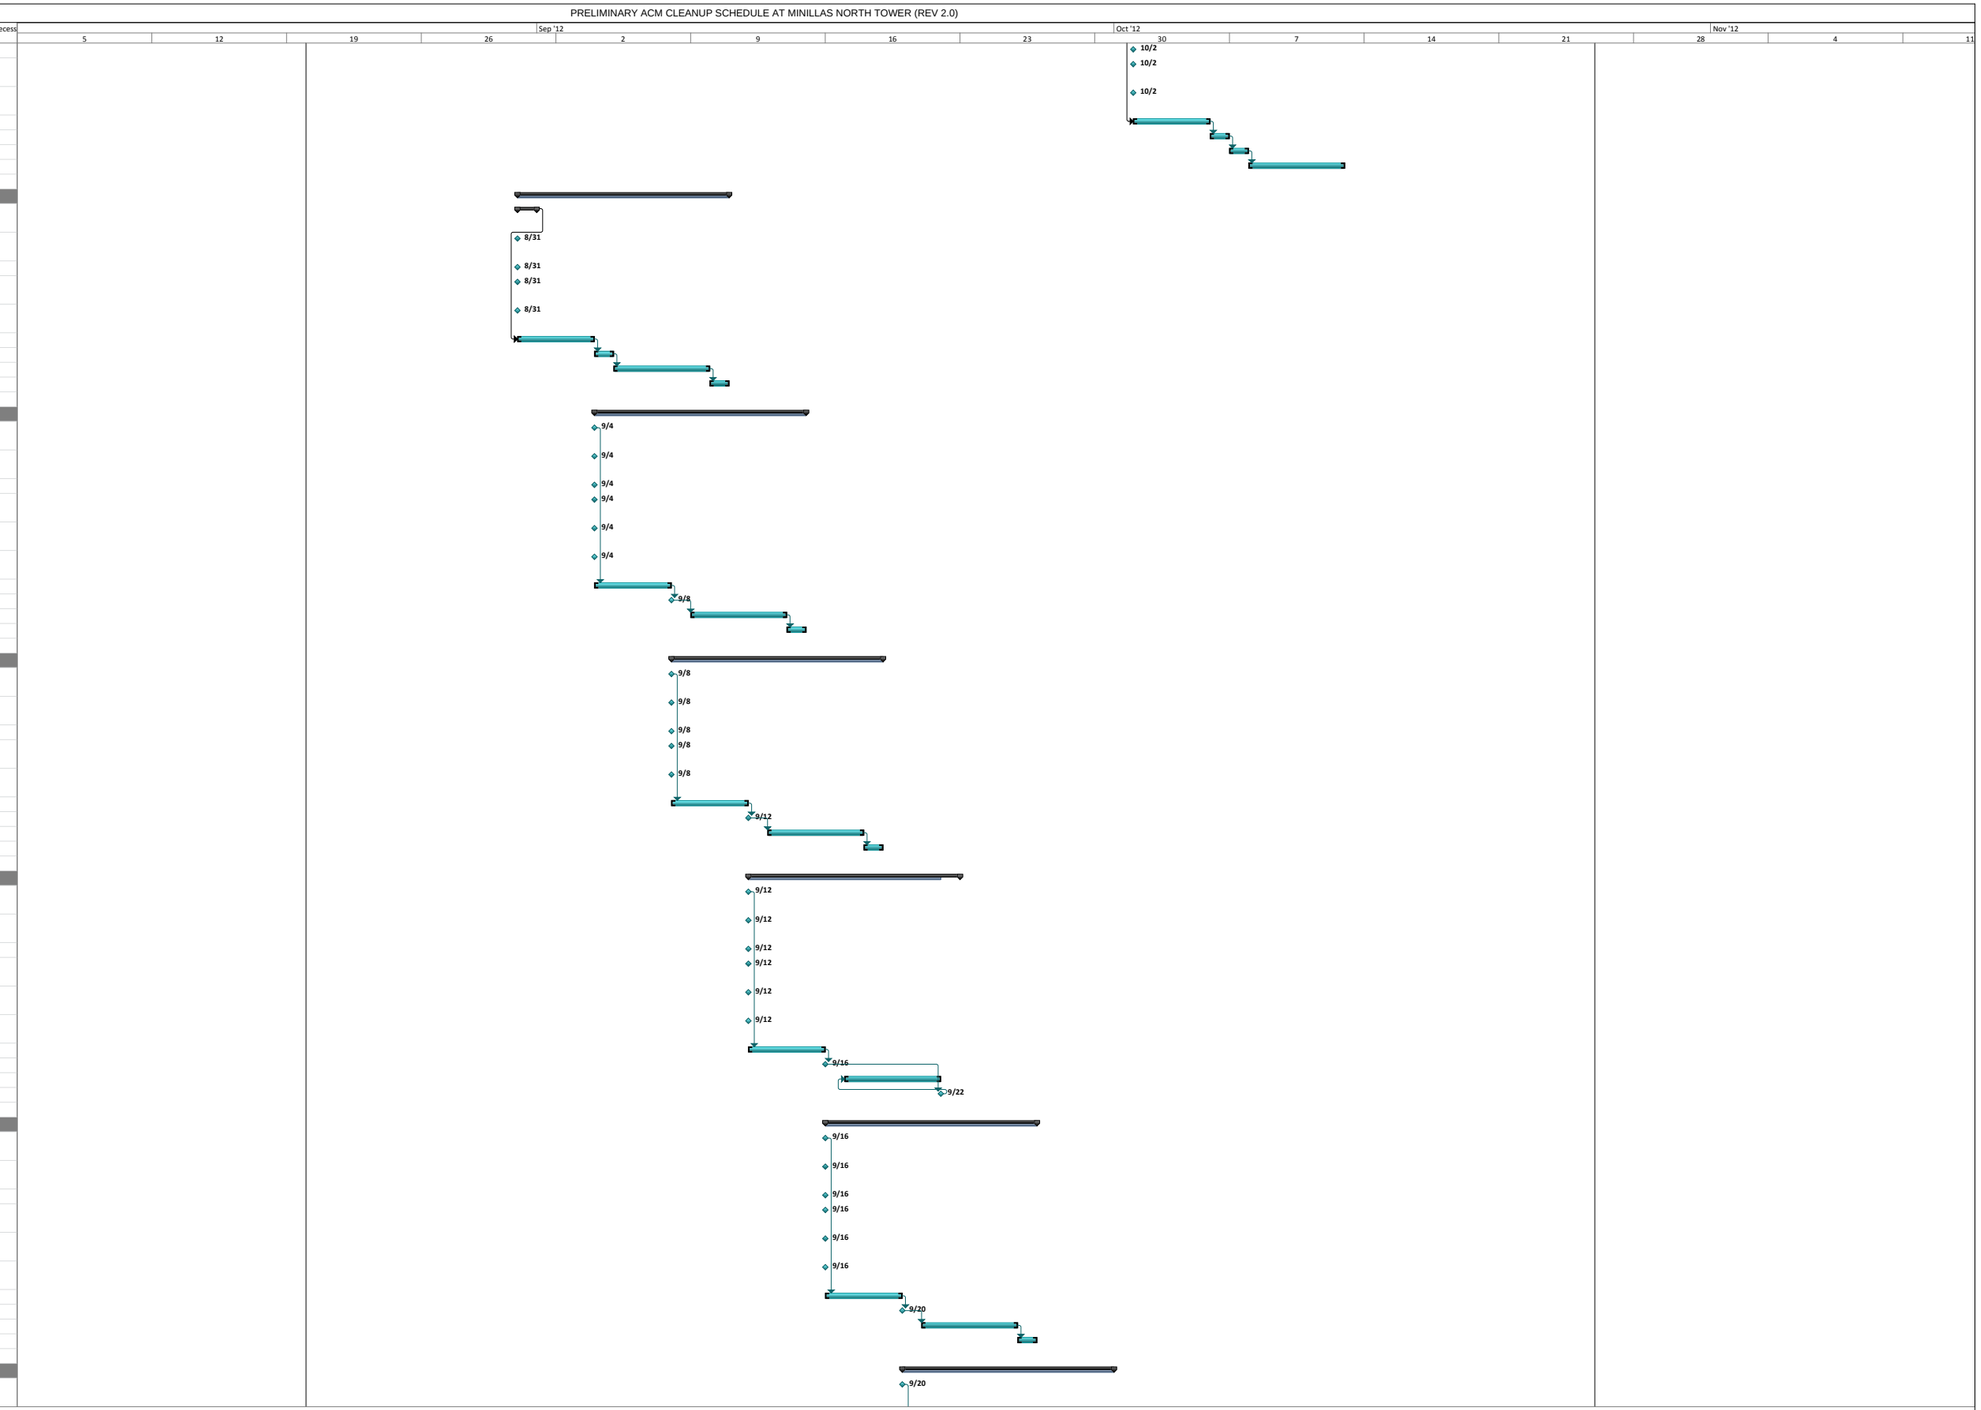

Project: Preliminary ACM Cleanup Schedule for Minillas North Tower
Note: The start date is August 14, 2012 or as approved.

(REV 2.0) Date: Mon 8/20/12

Task | Split | Milestone | Summary | Project Summary | External Tasks | External Milestone | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | Deadline | Progress

"The given *Calendar days* are only for guidance purposes, are estimated, subject to change and subject to the availability of the contractors".

PRELIMINARY ACM CLEANUP SCHEDULE AT MINILLAS NORTH TOWER (REV 2.0)

ID	Task Name	Calendar Days	Start	Finish	Predecess
202	Installation of Decontamination unit at entrance of the work area	0	Thu 9/20/12	Thu 9/20/12	
203	Placement, as applicable, of Critical Barriers	0	Thu 9/20/12	Thu 9/20/12	
204	Placement and testing of the required number of negative air machines/equipment	0	Thu 9/20/12	Thu 9/20/12	
205	Installation of Equipment Decontamination and Bag-out unit per work area, as applicable	0	Thu 9/20/12	Thu 9/20/12	
206	Re-confirmation Assessment of Ceiling Stucco condition and response action further determination	0	Thu 9/20/12	Thu 9/20/12	
207	1830 Cleanup Activities	4	Thu 9/20/12	Sun 9/23/12	201
208	1840 Final Clearance Sampling	0	Mon 9/24/12	Mon 9/24/12	207
209	1850 EPA's Review of Clearance & Results	5	Tue 9/25/12	Sat 9/29/12	
210	1860 Isolation & Seal after clearance criteria acceptance	1	Sun 9/30/12	Sun 9/30/12	209
211					
212	**Work area: 7th Level-See Appendix II**	**11**	**Mon 9/24/12**	**Thu 10/4/12**	
213	**1870 Installation of temporary containment isolation barriers/decontamination unit/waste load-out unit**	**0**	**Mon 9/24/12**	**Mon 9/24/12**	
214	Installation of Decontamination unit at entrance of the work area	1	Mon 9/24/12	Mon 9/24/12	
215	Placement, as applicable, of Critical Barriers	1	Mon 9/24/12	Mon 9/24/12	
216	Placement and testing of the required number of negative air machines/equipment	1	Mon 9/24/12	Mon 9/24/12	
217	Installation of Equipment Decontamination and Bag-out unit per work area, as applicable	1	Mon 9/24/12	Mon 9/24/12	
218	1880 Cleanup Activities	4	Mon 9/24/12	Thu 9/27/12	213
219	1890 Final Clearance Sampling	0	Fri 9/28/12	Fri 9/28/12	218
220	1900 EPA's Review of Clearance & Results	5	Sat 9/29/12	Wed 10/3/12	219
221	1910 Isolation & Seal after clearance criteria acceptance	1	Thu 10/4/12	Thu 10/4/12	220
222					
223	**Work area: 8th Level-See Appendix II**	**11**	**Fri 9/28/12**	**Mon 10/8/12**	
224	**1920 Installation of temporary containment isolation barriers/decontamination unit/waste load-out unit**	**0**	**Fri 9/28/12**	**Fri 9/28/12**	
225	Installation of Decontamination unit at entrance of the work area	0	Fri 9/28/12	Fri 9/28/12	
226	Placement, as applicable, of Critical Barriers	0	Fri 9/28/12	Fri 9/28/12	
227	Placement and testing of the required number of negative air machines/equipment	0	Fri 9/28/12	Fri 9/28/12	
228	Installation of Equipment Decontamination and Bag-out unit per work area, as applicable	0	Fri 9/28/12	Fri 9/28/12	
229	1930 Cleanup Activities	4	Fri 9/28/12	Mon 10/1/12	224
230	1940 Final Clearance Sampling	0	Tue 10/2/12	Tue 10/2/12	229
231	1950 EPA's Review of Clearance & Results	5	Wed 10/3/12	Sun 10/7/12	230
232	1960 Isolation & Seal after clearance criteria acceptance	1	Mon 10/8/12	Mon 10/8/12	231
233					
234	**Work area: North and South Emergency Stairways-See Appendix II**	**11**	**Tue 10/2/12**	**Fri 10/12/12**	
235	1970 Placement, as applicable, of Critical Barriers	1	Tue 10/2/12	Tue 10/2/12	
236	1975 Placement and testing of the required number of negative air machines/equipment	1	Tue 10/2/12	Tue 10/2/12	
237	1980 Cleanup Activities	4	Tue 10/2/12	Fri 10/5/12	
238	1985 Final Clearance Sampling	1	Sat 10/6/12	Sat 10/6/12	
239	1990 EPA's Review of Clearance & Results	5	Sun 10/7/12	Thu 10/11/12	
240	2010 Isolation & Seal after clearance criteria acceptance	1	Fri 10/12/12	Fri 10/12/12	
241	**Work area: North Elevator Shaft and Cabins (Cars)-See Appendix III**	**11**	**Sat 10/6/12**	**Tue 10/16/12**	
242	2020 Confirm the sealing integrity of the north elevators doors	1	Sat 10/6/12	Sat 10/6/12	
243	2025 Placement and testing of the required number of negative air machines/equipment	1	Sat 10/6/12	Sat 10/6/12	
244	2030 Interior and exterior elevators Cabins (cars) cleanup	2	Sat 10/6/12	Sun 10/7/12	
245	2035 Cleanup of Elevator Shaft walls and pit basin	2	Mon 10/8/12	Tue 10/9/12	
246	2040 Clearance Sampling of the three north cars	1	Wed 10/10/12	Wed 10/10/12	
247	2045 Isolation and Seal until receiving clearance sample results	1	Thu 10/11/12	Thu 10/11/12	
248	2050 EPA Review of Clearance & Results	5	Fri 10/12/12	Tue 10/16/12	
249	**Work area: Re-cleaning and re-clearance of south Elevator Shaft and Cabins (Cars)-See Appendix III**	**11**	**Thu 10/11/12**	**Sun 10/21/12**	
250	2060 Confirm the sealing integrity of the south elevators doors	1	Thu 10/11/12	Thu 10/11/12	
251	2070 Placement and testing of the required number of negative air machines/equipment	1	Thu 10/11/12	Thu 10/11/12	
252	2080 Interior and exterior elevators Cabins (cars) cleanup	4	Thu 10/11/12	Sun 10/14/12	
253	2090 Clearance Sampling of the two south cars	1	Mon 10/15/12	Mon 10/15/12	
254	2100 Isolation and Seal until receiving clearance sample results	1	Tue 10/16/12	Tue 10/16/12	
255	2110 EPA Review of Clearance & Results	5	Wed 10/17/12	Sun 10/21/12	
256	**Ground Floor**	**0**	**Mon 10/15/12**	**Thu 10/25/12**	
257	2120 Re-revise the integrity, as applicable, of Critical Barriers	1	Mon 10/15/12	Mon 10/15/12	
258	2130 Re-testing of the required number of negative air machines/equipment	1	Mon 10/15/12	Mon 10/15/12	
259	2140 Re-confirmation Assessment of Ceiling Stucco condition and response action further determination	1	Mon 10/15/12	Mon 10/15/12	
260	2150 Cleanup Activities	4	Mon 10/15/12	Thu 10/18/12	
261	2160 Final Clearance Sampling	1	Fri 10/19/12	Fri 10/19/12	
262	2170 EPA's Review of Clearance & Results	5	Sat 10/20/12	Wed 10/24/12	
263	2180 Isolation & Seal after clearance criteria acceptance	1	Thu 10/25/12	Thu 10/25/12	

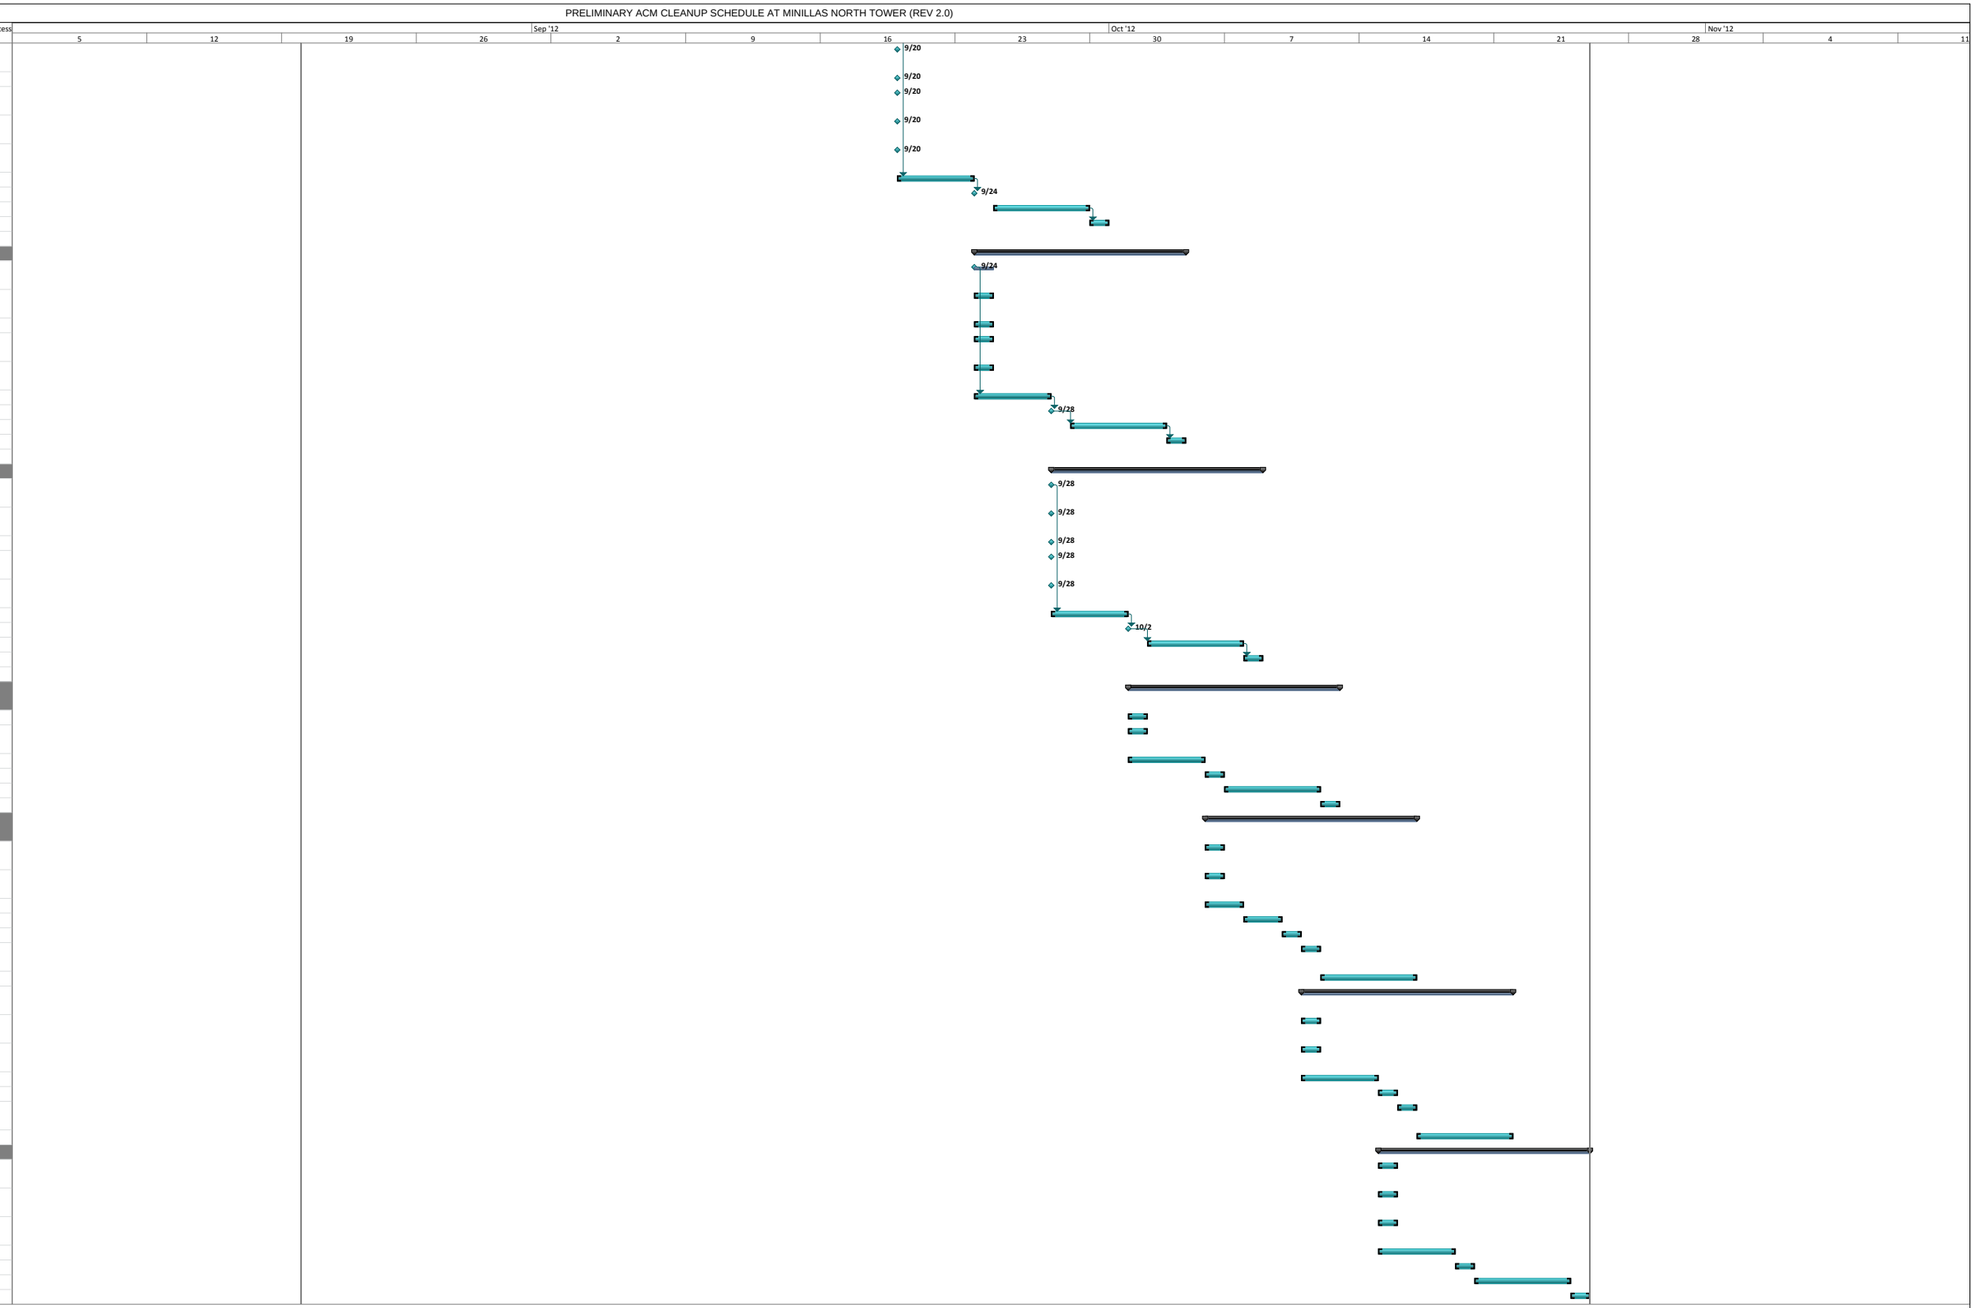

Project: Preliminary ACM Cleanup Schedule for Minillas North Tower
Note: The start date is August 14, 2012 or as approved.

(REV 2.0) Date: Mon 8/20/12

Task | Split | Milestone | Summary | Project Summary | External Tasks | External Milestone | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | Deadline | Progress

"The given *Calendar days* are only for guidance purposes, are estimated, subject to change and subject to the availability of the contractors".
