Project Manager: Charles Huang
Superintendent: Dave Harper

Tue 3/15/05

# Harbor Gateway/ Lot 8 Development

| ID | Task Name | Duration | Start | Finish | Predecessors |
|---|---|---|---|---|---|
| 1 | **Jobsite Construction** | 183 days | Mon 1/17/05 | Mon 10/3/05 | |
| 2 | | | | | |
| 3 | "Shell" building (146,826 sf) | 156 days | Mon 1/17/05 | Wed 8/24/05 | |
| 4 | Earthwork | 43 days | Mon 1/17/05 | Wed 3/16/05 | |
| 5 | Construct Bldg pad | 13 days | Mon 1/17/05 | Wed 2/2/05 | |
| 6 | Certify building pad from City | 5 days | Thu 2/3/05 | Wed 2/9/05 | 5 |
| 7 | Site rough grade | 3 days | Mon 2/7/05 | Wed 2/9/05 | 6FF |
| 8 | Construct temp fire access road | 3 days | Mon 3/14/05 | Wed 3/16/05 | 47 |
| 9 | Site Utilities | 40 days | Thu 2/10/05 | Wed 4/6/05 | |
| 10 | Sewer line | 5 days | Thu 2/10/05 | Wed 2/16/05 | 6 |
| 11 | Storm drain | 10 days | Tue 2/15/05 | Mon 2/28/05 | 10FS-2 days |
| 12 | Water line | 4 days | Tue 3/1/05 | Fri 3/4/05 | 11,10 |
| 13 | Fire main | 18 days | Mon 3/14/05 | Wed 4/6/05 | 12 |
| 14 | Fire main | 15 days | Mon 3/14/05 | Fri 4/1/05 | 10,47 |
| 15 | Test and flush | 3 days | Mon 4/4/05 | Wed 4/6/05 | 14 |
| 16 | Electrical & tele UG | 5 days | Tue 3/1/05 | Mon 3/7/05 | 10,11 |
| 17 | Install tele & electrical vaults | 3 days | Wed 3/30/05 | Fri 4/1/05 | 42 |
| 18 | Underslab utilities | 90 days | Wed 2/16/05 | Wed 6/22/05 | |
| 19 | Sewer piping | 4 days | Wed 2/16/05 | Mon 2/21/05 | 6FS-1 day,24SS+4 days |
| 20 | Electrical | 3 days | Mon 6/20/05 | Wed 6/22/05 | 97SS+2 days |
| 21 | Interior footings | 60 days | Tue 2/1/05 | Mon 4/25/05 | |
| 22 | Footings w/o gas barrier | 8 days | Tue 2/1/05 | Thu 2/10/05 | |
| 23 | Dig/Rebar | 3 days | Tue 2/1/05 | Thu 2/3/05 | 5FS-2 days |
| 24 | Place concrete | 1 day | Thu 2/10/05 | Thu 2/10/05 | 6 |
| 25 | Footings in mezz. areas with gas barrier | 7 days | Fri 4/15/05 | Mon 4/25/05 | |
| 26 | Dig footings | 2 days | Fri 4/15/05 | Mon 4/18/05 | 37 |
| 27 | Barrier under footings | 3 days | Tue 4/19/05 | Thu 4/21/05 | 26SS+2 days |
| 28 | Rebar | 3 days | Wed 4/20/05 | Fri 4/22/05 | 27FS-2 days |
| 29 | Place concrete | 1 day | Mon 4/25/05 | Mon 4/25/05 | 28 |
| 30 | NE pad - environmental below SOG | 13 days | Thu 3/10/05 | Mon 3/28/05 | |
| 31 | Drill wells | 2 days | Thu 3/10/05 | Fri 3/11/05 | 35FS+5 days |
| 32 | Begin underground piping | 2 days | Mon 3/14/05 | Tue 3/15/05 | 31 |
| 33 | Complete underground piping | 9 days | Wed 3/16/05 | Mon 3/28/05 | 32 |
| 34 | Environmental infrastructure below SOG | 46 days | Thu 2/10/05 | Thu 4/14/05 | |
| 35 | Drill wells | 15 days | Thu 2/10/05 | Wed 3/2/05 compl 3/10 | 6 |
| 36 | Begin underground piping ok c/slab | ~~15 days~~ | ~~Thu 3/3/05~~ | ~~Wed 3/23/05~~ | 35 |
| 37 | Complete underground piping ok c/slab | 15 days | Thu 3/24/05 ok | Thu 4/14/05 ok to compl | 36 |
| 38 | Perimeter Footings | 8 days | Mon 3/28/05 | Wed 4/6/05 | |
| 39 | Layout & excavation | 3 days | Mon 3/28/05 | Wed 3/30/05 | 48FS+4 days |
| 40 | Rebar | 3 days | Thu 3/31/05 | Mon 4/4/05 | 39 |
| 41 | Pour | 2 days | Tue 4/5/05 | Wed 4/6/05 | 40 |

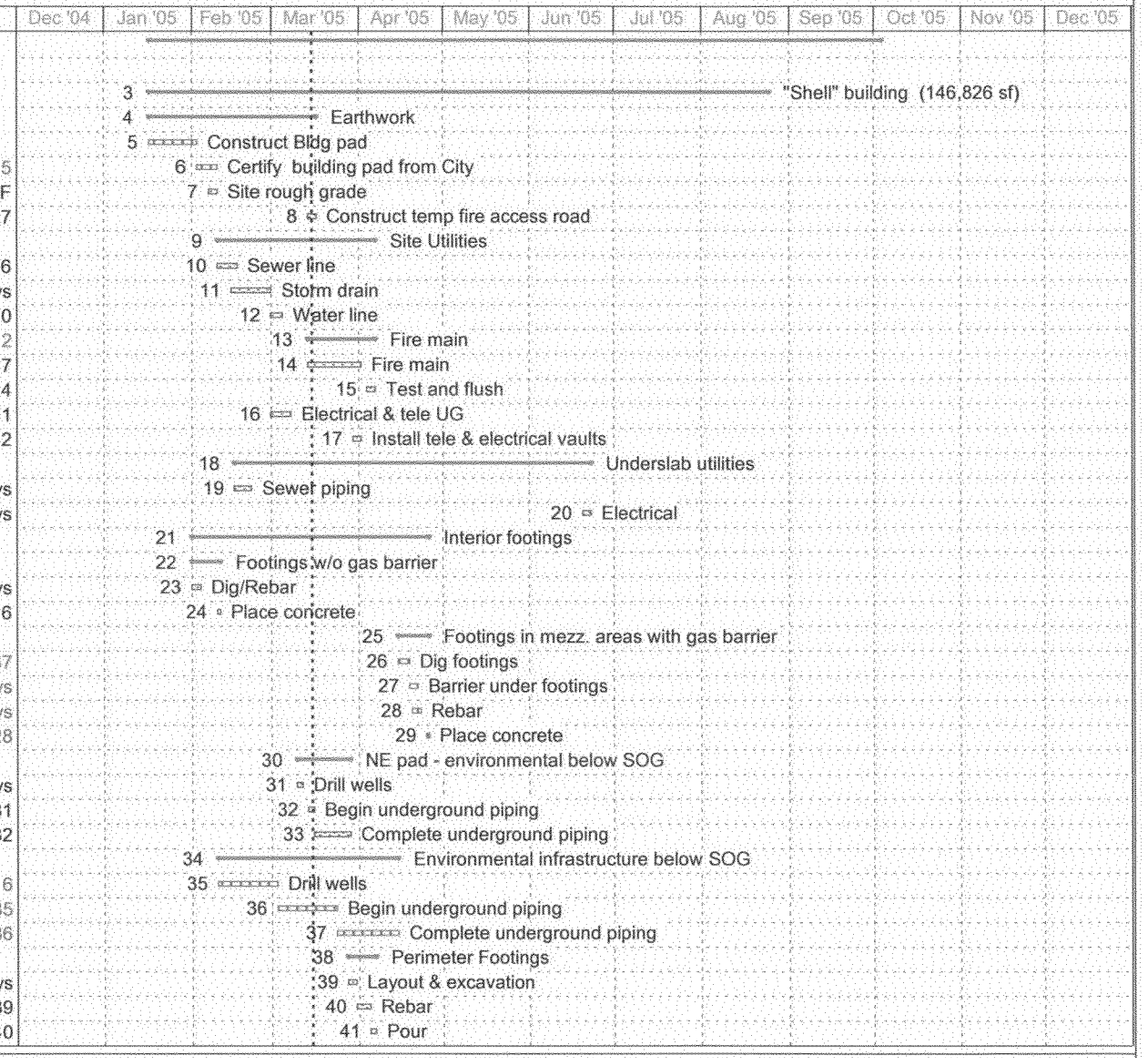


Schedule File: BoeingRealtyOwner3-4-05.mpp

Task | Critical Task | Progress | Milestone | Summary | Rolled Up Task | Rolled Up Critical Task | Rolled Up Milestone | Rolled Up Progress | Split | External Tasks | Project Summary | External Milestone | Deadline



MILLIE and SEVERSON

BOE-C6-0094053

Project Manager: Charles Huang
Superintendent: Dave Harper

Tue 3/15/05

# Harbor Gateway/ Lot 8 Development

| ID | Task Name | Duration | Start | Finish | Predecessors |
|---|---|---|---|---|---|
| 42 | Site wall footings | 6 days | Tue 3/22/05 | Tue 3/29/05 | |
| 43 | Dig footings / place rebar | 4 days | Tue 3/22/05 | Fri 3/25/05 | 48 |
| 44 | Place concrete | 2 days | Mon 3/28/05 | Tue 3/29/05 | 43 |
| 45 | Slab on Grade | 62 days | Fri 2/11/05 | Mon 5/9/05 | |
| 46 | Complete SOG in west area w/o UG pip | 27 days | Fri 2/11/05 | Mon 3/21/05 | |
| 47 | Set-up and pour slab | 21 days | Fri 2/11/05 | Fri 3/11/05 | 24 |
| 48 | Slab cure | 6 days | Mon 3/14/05 | Mon 3/21/05 | 47 |
| 49 | Complete SOG at NE | 12 days | Tue 3/29/05 | Wed 4/13/05 | |
| 50 | Fine grade | 2 days | Tue 3/29/05 | Wed 3/30/05 | 33 |
| 51 | Place rebar / concrete | 5 days | Thu 3/31/05 | Wed 4/6/05 | 50 |
| 52 | Slab cure | 5 days | Thu 4/7/05 | Wed 4/13/05 | 51 |
| 53 | Complete SOG over underground piping | 17 days | Fri 4/15/05 | Mon 5/9/05 | |
| 54 | Fine grade / install gas barrier | 5 days | Fri 4/15/05 | Thu 4/21/05 | 37 |
| 55 | Place rebar / concrete | 5 days | Tue 4/26/05 | Mon 5/2/05 | 29,37,54 |
| 56 | Slab cure | 5 days | Tue 5/3/05 | Mon 5/9/05 | 55 |
| 57 | Precast panels | 51 days | Fri 3/18/05 | Fri 5/27/05 | |
| 58 | Site tilt-panels | 12 days | Fri 3/18/05 | Mon 4/4/05 | |
| 59 | Cast and pour panels | 5 days | Fri 3/18/05 | Thu 3/24/05 | 48FS-2 days |
| 60 | Cure site panels | 5 days | Fri 3/25/05 | Thu 3/31/05 | 59 |
| 61 | 3/30 Erect site panels | 2 days | Fri 4/1/05 | Mon 4/4/05 | MOVE UP 60 |
| 62 | 1st group of panels | 18 days | Fri 3/18/05 | Tue 4/12/05 | |
| 63 | Layout & form | 8 days | Fri 3/18/05 | Tue 3/29/05 | 48FS-2 days |
| 64 | Rebar & embeds | 4 days | Wed 3/30/05 | Mon 4/4/05 | 63 |
| 65 | Pour panels | 1 day | Tue 4/5/05 | Tue 4/5/05 | 64 |
| 66 | Panel cure | 5 days | Wed 4/6/05 | Tue 4/12/05 | 65 |
| 67 | 2nd group of panels | 18 days | Fri 3/25/05 | Tue 4/19/05 | |
| 68 | Layout & form | 8 days | Fri 3/25/05 | Tue 4/5/05 | 63FS-3 days |
| 69 | Rebar & embeds | 4 days | Wed 4/6/05 | Mon 4/11/05 | 68,64 |
| 70 | Pour panels | 1 day | Tue 4/12/05 | Tue 4/12/05 | 69 |
| 71 | Panel cure | 5 days | Wed 4/13/05 | Tue 4/19/05 | 70 |
| 72 | Panels over underground piping | 32 days | Thu 4/14/05 | Fri 5/27/05 | |
| 73 | 3rd group of panels(NE) | 14 days | Thu 4/14/05 | Tue 5/3/05 | |
| 74 | Layout & form | 5 days | Thu 4/14/05 | Wed 4/20/05 | 52 |
| 75 | Rebar & embeds | 3 days | Thu 4/21/05 | Mon 4/25/05 | 74 |
| 76 | Pour panels | 1 day | Tue 4/26/05 | Tue 4/26/05 | 75 |
| 77 | Panel cure | 5 days | Wed 4/27/05 | Tue 5/3/05 | 76 |
| 78 | 4th group of panels | 14 days | Tue 5/10/05 | Fri 5/27/05 | |
| 79 | Layout & form | 5 days | Tue 5/10/05 | Mon 5/16/05 | 56 |
| 80 | Rebar & embeds | 3 days | Tue 5/17/05 | Thu 5/19/05 | 79 |
| 81 | Pour panels | 1 day | Fri 5/20/05 | Fri 5/20/05 | 80 |
| 82 | Panel cure | 5 days | Mon 5/23/05 | Fri 5/27/05 | 81 |

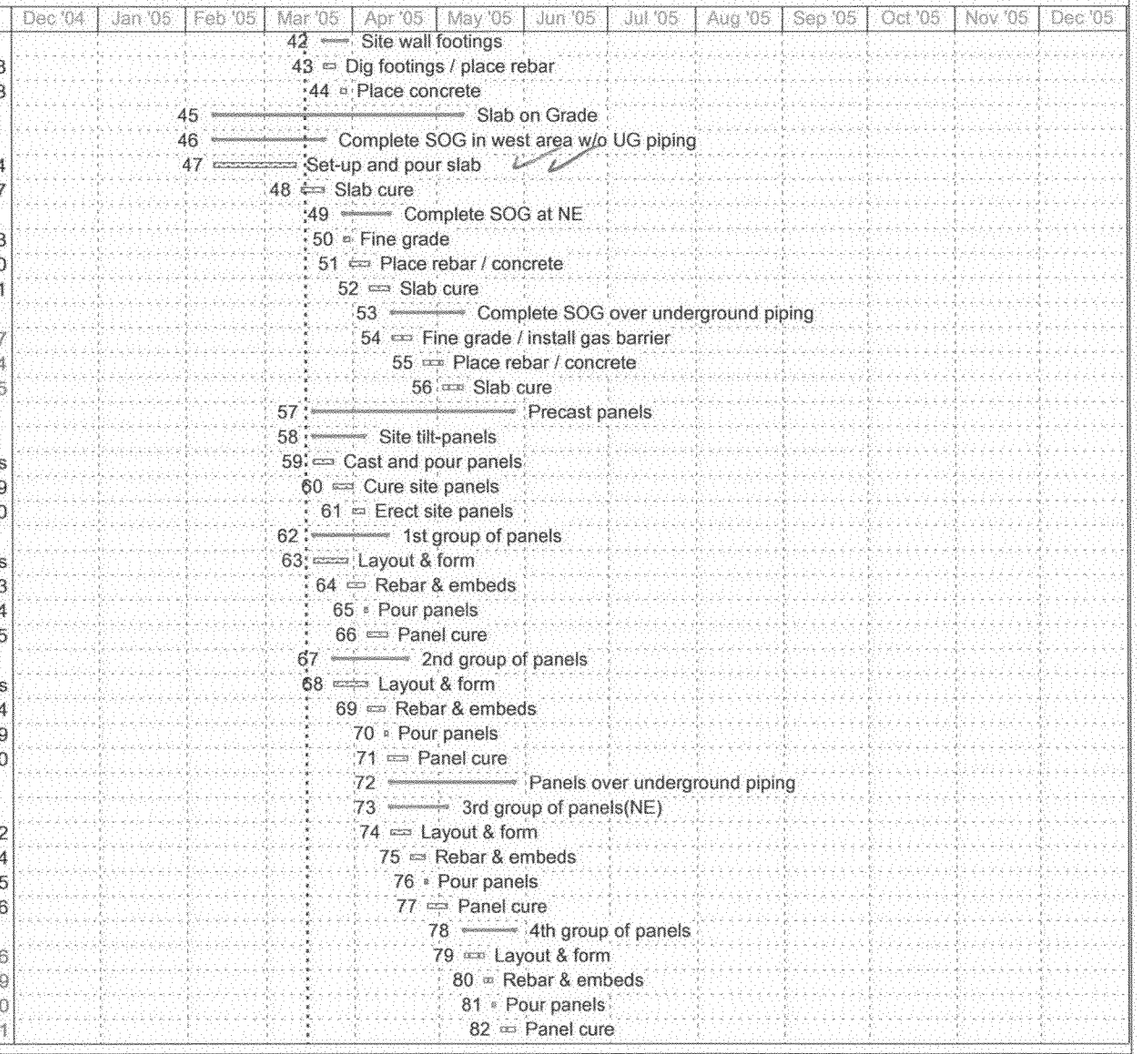


Schedule File: BoeingRealtyOwner3-4-05.mpp

Task | Critical Task | Progress | Milestone | Summary | Rolled Up Task | Rolled Up Critical Task | Rolled Up Milestone | Rolled Up Progress | Split | External Tasks | Project Summary | External Milestone | Deadline



MILLIE and SEVERSON

BOE-C6-0094054

Project Manager: Charles Huang
Superintendent: Dave Harper

Tue 3/15/05

# Harbor Gateway/ Lot 8 Development

| ID | Task Name | Duration | Start | Finish | Predecessors |
|---|---|---|---|---|---|
| 83 | Erect panels | 4 days | Wed 5/25/05 | Tue 5/31/05 | 66,71,82FS-3 days |
| 84 | Weld panels | 5 days | Wed 6/1/05 | Tue 6/7/05 | 83 |
| 85 | Erect columns | 2 days | Wed 6/1/05 | Thu 6/2/05 | 83 |
| 86 | Panelized roof structure | 12 days | Fri 6/3/05 | Mon 6/20/05 | 83,85,8 |
| 87 | Roof Assembly | 20 days | Tue 6/21/05 | Tue 7/19/05 | |
| 88 | Wood curbs / mechanical platforms | 5 days | Tue 6/21/05 | Mon 6/27/05 | 86 |
| 89 | Roof drains & scuppers | 3 days | Tue 6/21/05 | Thu 6/23/05 | 88SS |
| 90 | Lead flashings | 2 days | Tue 6/21/05 | Wed 6/22/05 | 86 |
| 91 | Pre Roof Inspection | 1 day | Tue 6/28/05 | Tue 6/28/05 | 88,89,90 |
| 92 | Roofing | 11 days | Wed 6/29/05 | Thu 7/14/05 | 88,91 |
| 93 | Skylights/smoke hatches | 3 days | Fri 7/15/05 | Tue 7/19/05 | 88,92 |
| 94 | Remove braces | 13 days | Thu 6/16/05 | Tue 7/5/05 | |
| 95 | Pour strip | 13 days | Thu 6/16/05 | Tue 7/5/05 | |
| 96 | Office areas | 7 days | Thu 6/16/05 | Fri 6/24/05 | |
| 97 | Place conduit | 1 day | Thu 6/16/05 | Thu 6/16/05 | 83,86FS-3 days |
| 98 | Backfill | 2 days | Fri 6/17/05 | Mon 6/20/05 | 83,97 |
| 99 | Rebar | 2 days | Tue 6/21/05 | Wed 6/22/05 | 98FF+2 days |
| 100 | Place concrete | 2 days | Thu 6/23/05 | Fri 6/24/05 | 99 |
| 101 | Other areas | 12 days | Fri 6/17/05 | Tue 7/5/05 | |
| 102 | Place conduit | 3 days | Fri 6/17/05 | Tue 6/21/05 | 97 |
| 103 | Backfill | 4 days | Wed 6/22/05 | Mon 6/27/05 | 102 |
| 104 | Rebar | 3 days | Mon 6/27/05 | Wed 6/29/05 | 103FF+2 days |
| 105 | Place concrete | 3 days | Thu 6/30/05 | Tue 7/5/05 | 104 |
| 106 | Mezzanine (5,964 sf) | 15 days | Fri 6/10/05 | Thu 6/30/05 | |
| 107 | Erect steel (cols and beams) | 2 days | Mon 6/13/05 | Tue 6/14/05 | 86FS-6 days |
| 108 | Frame shear walls | 5 days | Fri 6/10/05 | Thu 6/16/05 | 107FS-3 days |
| 109 | Plywood shear walls | 2 days | Wed 6/15/05 | Thu 6/16/05 | 108FS-2 days |
| 110 | Beams / trusses | 5 days | Fri 6/17/05 | Thu 6/23/05 | 109 |
| 111 | Plywood / nailing / inspection | 5 days | Fri 6/24/05 | Thu 6/30/05 | 110 |
| 112 | Frame stairs & guard rails | 3 days | Wed 6/15/05 | Fri 6/17/05 | 109FS-2 days |
| 113 | Warehouse finishes | 36 days | Mon 6/13/05 | Tue 8/2/05 | |
| 114 | A.F.S. system | 25 days | Mon 6/13/05 | Mon 7/18/05 | 86FS-6 days |
| 115 | Emergency building lights | 4 days | Fri 7/8/05 | Wed 7/13/05 | 114FS-7 days |
| 116 | Sectional and overhead doors | 5 days | Mon 7/11/05 | Fri 7/15/05 | 105FS+3 days |
| 117 | Painting | 10 days | Mon 7/18/05 | Fri 7/29/05 | 118FF+2 days,116 |
| 118 | Doors & Hardware | 3 days | Mon 7/11/05 | Wed 7/13/05 | 114FS-6 days |
| 119 | Clean & seal floors | 2 days | Mon 8/1/05 | Tue 8/2/05 | 114,115,117,118,116 |
| 120 | Exterior Finishes | 42 days | Wed 6/15/05 | Fri 8/12/05 | |
| 121 | Frame canopies | 3 days | Tue 6/21/05 | Thu 6/23/05 | 86 |
| 122 | Window system | 42 days | Wed 6/15/05 | Fri 8/12/05 | |
| 123 | Site fab of window metal | 15 days | Wed 6/15/05 | Wed 7/6/05 | 86FS-4 days |

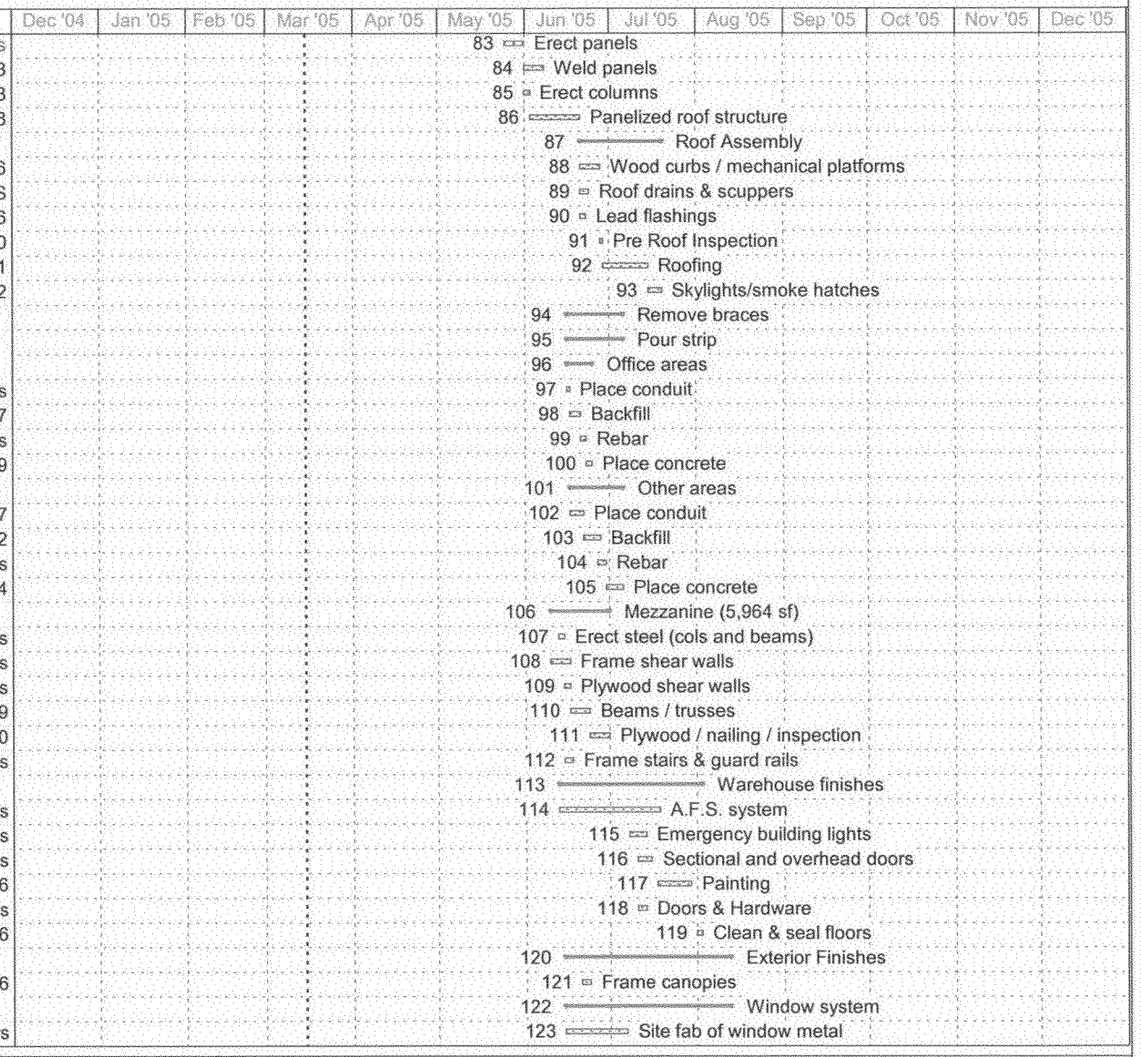


Schedule File: BoeingRealtyOwner3-4-05.mpp

Task | Critical Task | Progress | Milestone | Summary | Rolled Up Task | Rolled Up Critical Task | Rolled Up Milestone | Rolled Up Progress | Split | External Tasks | Project Summary | External Milestone | Deadline



MILLIE and SEVERSON

BOE-C6-0094055

Project Manager: Charles Huang
Superintendent: Dave Harper

Tue 3/15/05

# Harbor Gateway/ Lot 8 Development

| ID | Task Name | Duration | Start | Finish | Predecessors |
|---|---|---|---|---|---|
| 124 | Layout | 1 day | Tue 6/21/05 | Tue 6/21/05 | 86 |
| 125 | Install aluminum framing | 15 days | Mon 7/11/05 | Fri 7/29/05 | 100,92FS-4 days,123FS-5 days |
| 126 | Install glass & caulk | 10 days | Mon 8/1/05 | Fri 8/12/05 | 125 |
| 127 | Install glass entry doors | 3 days | Tue 8/9/05 | Thu 8/11/05 | 125,126FS-4 days |
| 128 | Canopy metal panels | 4 days | Mon 8/1/05 | Thu 8/4/05 | 121,92,125 |
| 129 | Patch panels | 8 days | Tue 6/21/05 | Thu 6/30/05 | 86 |
| 130 | Caulk panel joints | 5 days | Fri 7/1/05 | Fri 7/8/05 | 129 |
| 131 | Wash down and paint exterior | 10 days | Mon 8/1/05 | Fri 8/12/05 | 125,129,130,128FS-4 days |
| 132 | Electrical Service | 36 days | Wed 7/6/05 | Wed 8/24/05 | |
| 133 | Set Switchgear | 15 days | Wed 7/6/05 | Tue 7/26/05 | 105 |
| 134 | S.C.Edison Hook-up | 2 days | Tue 8/23/05 | Wed 8/24/05 | 133,118,167 |
| 135 | | | | | |
| 136 | Sitework | 82 days | Wed 6/1/05 | Mon 9/26/05 | |
| 137 | Structural backfill against panels / fine grade | 5 days | Wed 6/1/05 | Tue 6/7/05 | 83 |
| 138 | Site work phase I - north, south and west | 27 days | Wed 6/8/05 | Fri 7/15/05 | 137 |
| 139 | survey | 2 days | Wed 6/8/05 | Thu 6/9/05 | 137 |
| 140 | Cut curb grades | 3 days | Fri 6/10/05 | Tue 6/14/05 | 139 |
| 141 | Demo for new driveway approach | 1 day | Wed 6/15/05 | Wed 6/15/05 | 140 |
| 142 | Concrete curb wall, new driveway appro | 7 days | Tue 6/14/05 | Wed 6/22/05 | 140FS-1 day |
| 143 | Landscape irrigations/ sleeves | 12 days | Wed 6/15/05 | Thu 6/30/05 | 140 |
| 144 | Survey for AC paving | 1 day | Thu 6/23/05 | Thu 6/23/05 | 142 |
| 145 | Grade for AC paving | 2 days | Fri 6/24/05 | Mon 6/27/05 | 142,144 |
| 146 | Base, AC paving, street patch | 3 days | Tue 6/28/05 | Thu 6/30/05 | 145 |
| 147 | Chain link fencing | 5 days | Fri 7/1/05 | Fri 7/8/05 | 146 |
| 148 | Pavement markings | 1 day | Mon 7/11/05 | Mon 7/11/05 | 147 |
| 149 | Landscaping | 10 days | Fri 7/1/05 | Fri 7/15/05 | 143 |
| 150 | Layout curbs for environmental infrastructu | 1 day | Wed 6/8/05 | Wed 6/8/05 | 137 |
| 151 | Environmental infrastructure | 40 days | Thu 6/9/05 | Thu 8/4/05 | 150 |
| 152 | Area 1 (south) | 25 days | Thu 6/9/05 | Thu 7/14/05 | |
| 153 | Drill wells | 10 days | Thu 6/9/05 | Wed 6/22/05 | 150 |
| 154 | Piping / vaults | 15 days | Thu 6/23/05 | Thu 7/14/05 | 153 |
| 155 | Area 2 (middle) | 25 days | Thu 6/23/05 | Thu 7/28/05 | |
| 156 | Drill wells | 10 days | Thu 6/23/05 | Thu 7/7/05 | 153 |
| 157 | Piping / vaults | 15 days | Fri 7/8/05 | Thu 7/28/05 | 156 |
| 158 | Area 3 (north) | 20 days | Fri 7/8/05 | Thu 8/4/05 | |
| 159 | Drill wells | 10 days | Fri 7/8/05 | Thu 7/21/05 | 156 |
| 160 | Piping / vaults | 10 days | Fri 7/22/05 | Thu 8/4/05 | 152,159 |
| 161 | Underground Utilities at West | 4 days | Fri 8/5/05 | Wed 8/10/05 | 160 |
| 162 | Survey for curbs and paving | 1 day | Thu 8/11/05 | Thu 8/11/05 | 161 |
| 163 | Fine grade | 2 days | Fri 8/12/05 | Mon 8/15/05 | 162 |
| 164 | Grade @ curbs, apron, demo driveway | 3 days | Tue 8/16/05 | Thu 8/18/05 | 163 |

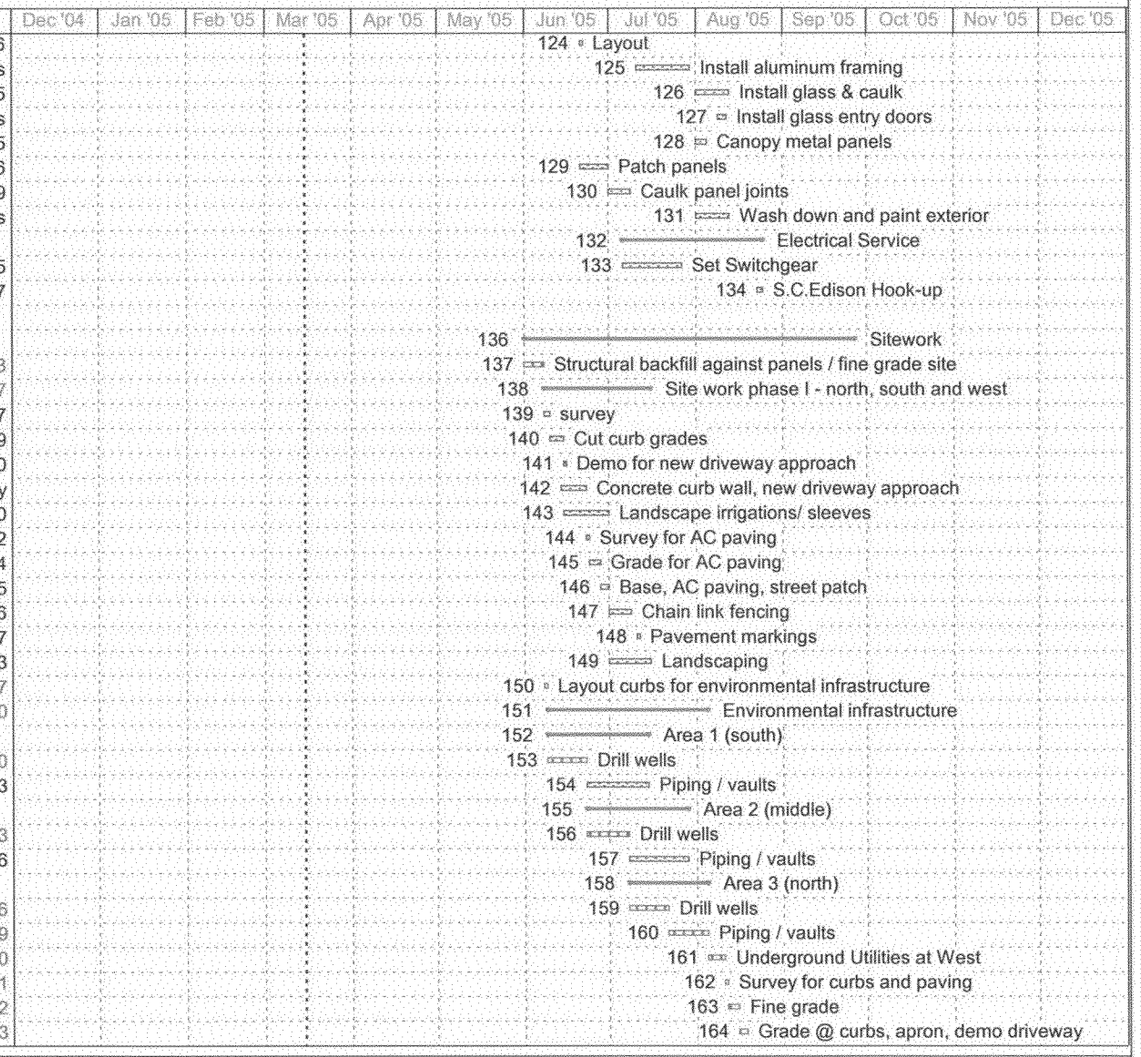


Schedule File: BoeingRealtyOwner3-4-05.mpp

Task | Critical Task | Progress | Milestone | Summary | Rolled Up Task | Rolled Up Critical Task | Rolled Up Milestone | Rolled Up Progress | Split | External Tasks | Project Summary | External Milestone | Deadline



MILLIE and SEVERSON

BOE-C6-0094056

Project Manager: Charles Huang
Superintendent: Dave Harper

Tue 3/15/05

# Harbor Gateway/ Lot 8 Development

| ID | Task Name | Duration | Start | Finish | Predecessors |
|---|---|---|---|---|---|
| 165 | Backfill curbs & finegrade @ ac paving | 3 days | Tue 8/30/05 | Thu 9/1/05 | 172 |
| 166 | Site Electrical | 23 days | Fri 8/19/05 | Wed 9/21/05 | |
| 167 | Set Edison transformers | 2 days | Fri 8/19/05 | Mon 8/22/05 | 164,133 |
| 168 | Install conduits | 8 days | Tue 8/30/05 | Fri 9/9/05 | 172 |
| 169 | Pour light pole bases | 5 days | Fri 9/2/05 | Fri 9/9/05 | 168SS+3 days |
| 170 | Install parking lot lights | 3 days | Mon 9/19/05 | Wed 9/21/05 | 169,175 |
| 171 | Site Concrete & asphalt | 20 days | Fri 8/19/05 | Fri 9/16/05 | |
| 172 | Curbs, walls, gutters, and driveways | 7 days | Fri 8/19/05 | Mon 8/29/05 | 164 |
| 173 | Entry walkways | 5 days | Tue 8/30/05 | Tue 9/6/05 | 172 |
| 174 | Base and concrete paving | 6 days | Fri 9/2/05 | Mon 9/12/05 | 165,172 |
| 175 | Base & ac paving | 4 days | Tue 9/13/05 | Fri 9/16/05 | 165,172,174 |
| 176 | Chain link fencing | 5 days | Fri 9/2/05 | Fri 9/9/05 | |
| 177 | Install fencing | 5 days | Fri 9/2/05 | Fri 9/9/05 | 165 |
| 178 | Pavement markings | 2 days | Tue 9/20/05 | Wed 9/21/05 | 175FS+1 day |
| 179 | Irrigation system | 5 days | Wed 9/14/05 | Tue 9/20/05 | 74FS-3 days,175FS-3 days,172 |
| 180 | Landscaping | 6 days | Mon 9/19/05 | Mon 9/26/05 | 179FS-2 days |
| 181 | | | | | |
| 182 | Interior finishes | 34 days | Fri 7/1/05 | Thu 8/18/05 | |
| 183 | Underground plumbing | 6 days | Fri 7/1/05 | Mon 7/11/05 | 109FS-2 days,111 |
| 184 | 1st floor | 30 days | Fri 7/8/05 | Thu 8/18/05 | |
| 185 | Overhead rough in | 8 days | Fri 7/8/05 | Tue 7/19/05 | |
| 186 | Ductwork/Elec/Plbg overhd | 8 days | Fri 7/8/05 | Tue 7/19/05 | 183FS-2 days,109FS-2 days |
| 187 | AFS overhead | 3 days | Wed 7/13/05 | Fri 7/15/05 | 186FS-5 days |
| 188 | Metal Studs & Drywall | 15 days | Fri 7/15/05 | Thu 8/4/05 | |
| 189 | Frame walls & clgs | 7 days | Fri 7/15/05 | Mon 7/25/05 | 186FS-3 days,187FS-3 days |
| 190 | Elec & plbg rough in | 5 days | Fri 7/22/05 | Thu 7/28/05 | 189FS-2 days |
| 191 | Insulation 1st fl | 1 day | Wed 7/27/05 | Wed 7/27/05 | 190FS-2 days |
| 192 | Drywall 1st fl | 4 days | Mon 7/25/05 | Thu 7/28/05 | 191FS-3 days |
| 193 | Taping 1st flr | 7 days | Wed 7/27/05 | Thu 8/4/05 | 192FS-2 days |
| 194 | Finishes | 13 days | Tue 8/2/05 | Thu 8/18/05 | |
| 195 | Paint prime coats 1st fl | 2 days | Thu 8/4/05 | Fri 8/5/05 | 193FS-1 day |
| 196 | Acoustical ceiling 1st fl | 9 days | Thu 8/4/05 | Tue 8/16/05 | |
| 197 | T bar grid | 4 days | Thu 8/4/05 | Tue 8/9/05 | 195FS-2 days |
| 198 | Lights and grilles | 5 days | Fri 8/5/05 | Thu 8/11/05 | 197FS-3 days |
| 199 | Acoustic tile | 4 days | Thu 8/11/05 | Tue 8/16/05 | 198FS-1 day |
| 200 | Toilet rooms | 10 days | Tue 8/2/05 | Mon 8/15/05 | |
| 201 | Paint prime coat | 1 day | Tue 8/2/05 | Tue 8/2/05 | 193FS-3 days |
| 202 | Ceramic tile | 7 days | Tue 8/2/05 | Wed 8/10/05 | 193FS-3 days,201FS-3 days |
| 203 | Plumbing fixtures | 3 days | Thu 8/11/05 | Mon 8/15/05 | 202 |
| 204 | Partitions & acc. | 2 days | Fri 8/12/05 | Mon 8/15/05 | 203FS-2 days |
| 205 | Install frames/doors/hdw | 3 days | Thu 8/11/05 | Mon 8/15/05 | 195SS+4 days,198SS+4 days |

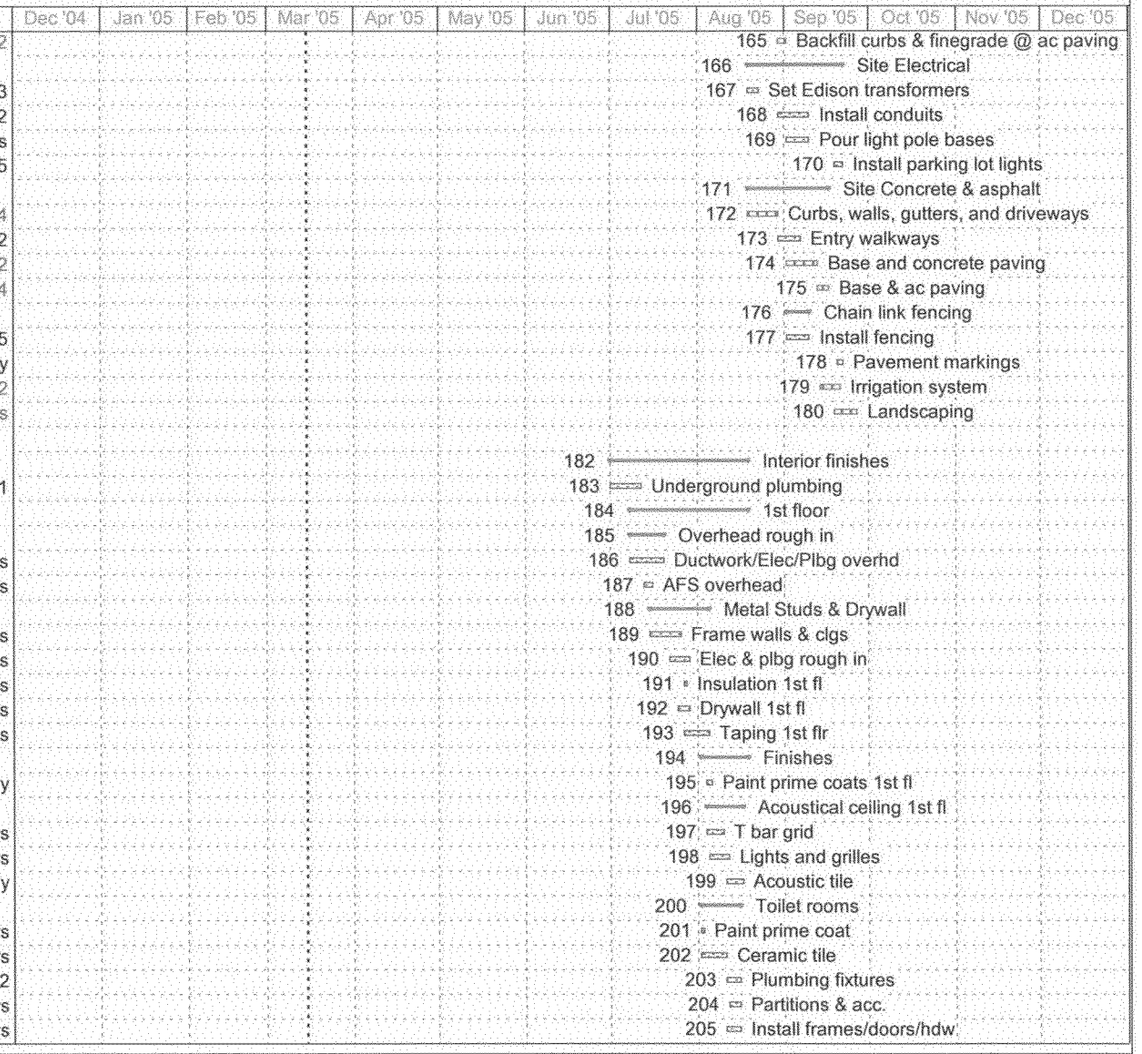


Schedule File: BoeingRealtyOwner3-4-05.mpp

Task | Critical Task | Progress | Milestone | Summary | Rolled Up Task | Rolled Up Critical Task | Rolled Up Milestone | Rolled Up Progress | Split | External Tasks | Project Summary | External Milestone | Deadline



MILLIE and SEVERSON

BOE-C6-0094057

Project Manager: Charles Huang
Superintendent: Dave Harper

Tue 3/15/05

# Harbor Gateway/ Lot 8 Development

| ID | Task Name | Duration | Start | Finish | Predecessors |
|---|---|---|---|---|---|
| 206 | Flooring | 2 days | Thu 8/11/05 | Fri 8/12/05 | ys,198FS-3 days,205FS-3 days |
| 207 | Install interior glass | 1 day | Fri 8/12/05 | Fri 8/12/05 | 205FS-2 days |
| 208 | Install cabinets | 2 days | Tue 8/9/05 | Wed 8/10/05 | 195FS-1 day,197FS-1 day |
| 209 | Paint finish coats | 5 days | Fri 8/12/05 | Thu 8/18/05 | 205FS-2 days,206FS-2 days |
| 210 | MEP Finishes | 7 days | Wed 8/10/05 | Thu 8/18/05 | |
| 211 | Plbg @ cabinets 1st fl | 1 day | Wed 8/10/05 | Wed 8/10/05 | 208FS-1 day |
| 212 | Electrical 1st fl | 3 days | Tue 8/16/05 | Thu 8/18/05 | ys,208FS-3 days,209FS-3 days |
| 213 | | | | | |
| 214 | Building finals | 5 days | Tue 9/27/05 | Mon 10/3/05 | |
| 215 | Final Inspections | 5 days | Tue 9/27/05 | Mon 10/3/05 | 211,212,180,119,131 |

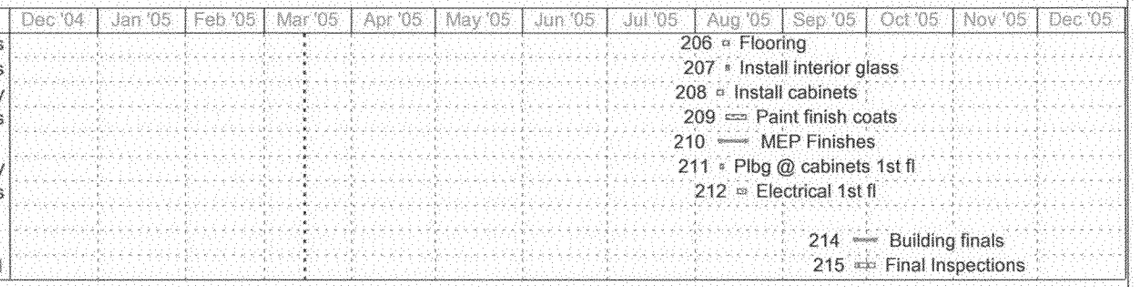


Schedule File:
BoeingRealtyOwner3-4-05.mpp

Task | Critical Task | Progress | Milestone | Summary | Rolled Up Task | Rolled Up Critical Task | Rolled Up Milestone | Rolled Up Progress | Split | External Tasks | Project Summary | External Milestone | Deadline



MILLIE and SEVERSON

BOE-C6-0094058
