Event: NOI-WORKOVER
Event End: 5/13/2010 00:00
Sec. Reason:
End Status:
Well Classification: DEVELOPMENT - CLASS II

OCCIDENTAL OF ELK HILLS INC

342-3G

Ground Level: 1,031.0ft
Datum: Original KB @ 1,041.00ft (default)
API No.: 0402929021

Wellbore: ORIGINAL HOLE
PBMD: 6,487.0ft
Btm TMD: 7,636.0ft
Spud Date: 6/1/1949 00:00
BH Coord X: 6,147,708.71uss ft
BH Coord Y: 2,285,619.33uss ft

Casing Shoes (ft)	Schematic (5/13/2010)	Openings Top/Btm/Type/Status

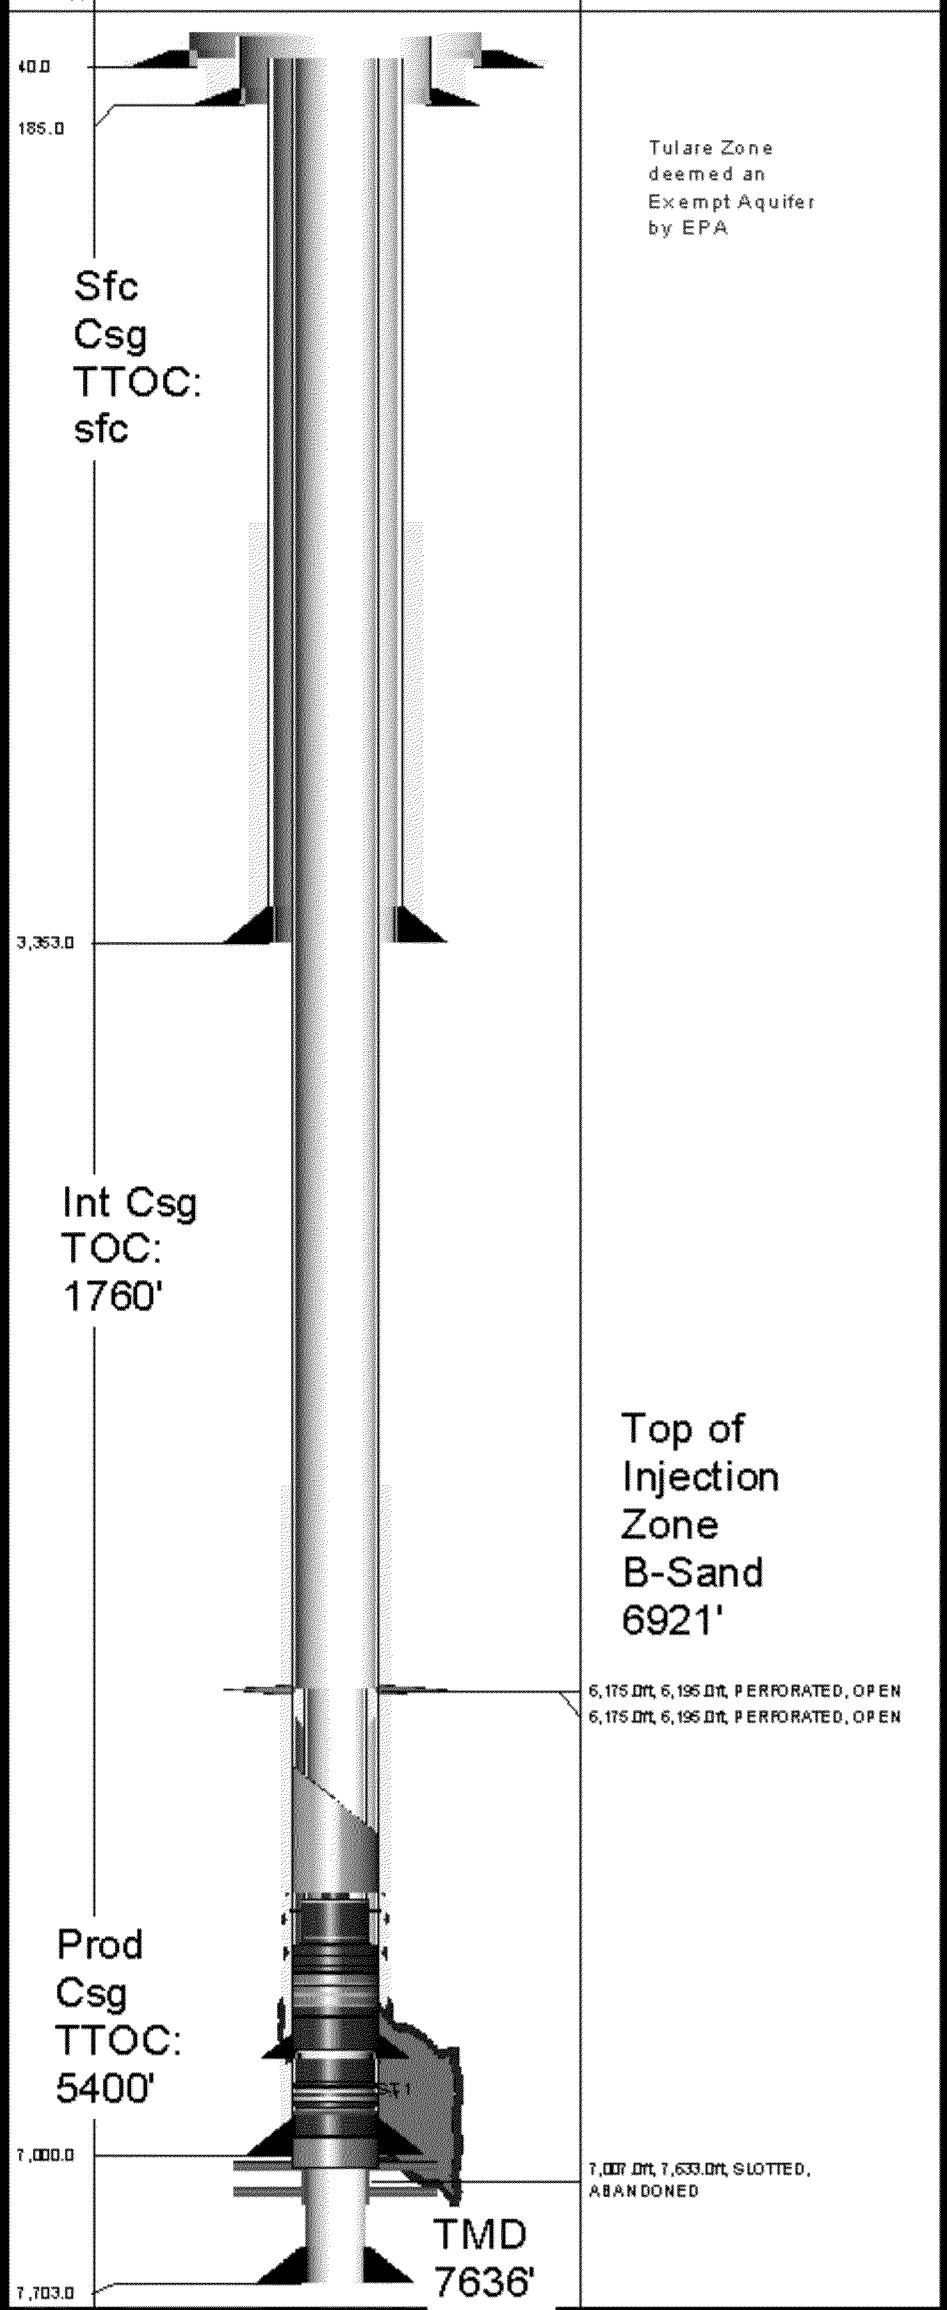

TUBING STRING Report Date: 12/10/2004 00:00

Component	Top MD (ft)	Btm MD (ft)
TH-DBB	10.0	11.0
FATNIP	11.0	11.7
TBGJNT	11.7	5,302.7
AC	5,302.7	5,305.0
TBGJNT	5,305.0	5,399.1
XO	5,399.1	5,400.3
TBGJNT	5,400.3	6,871.3
STNIP	6,871.3	6,872.3
TBGJNT	6,872.3	6,903.3
STCOLL	6,903.3	6,903.7

PLUG BACK Report Date: 5/17/2002 00:00

Component	Top MD (ft)	Btm MD (ft)
WHIPST	6,470.0	6,487.0
BP-PRM	6,487.0	6,490.0
CR-PRM	6,490.0	6,493.0
CEMENT	6,493.0	7,470.0

ROD STRING Report Date: 11/10/2007 00:00

Component	Top MD (ft)	Btm MD (ft)
POLROD	0.0	30.0
PNYROD	30.0	42.0
ROD	42.0	582.0
R-4PER	582.0	1,602.0
ROD	1,602.0	4,062.0
ROD	4,062.0	6,822.0
RSTBAR	6,822.0	6,826.0
INSPUMP	6,826.0	6,850.0

CONDUCTOR CASING Report Date: 5/17/1949 00:00

Item	OD (in)	Grade	Wt. (ppf)	Top MD (ft)	Btm MD (ft)
CASING JOINT(S)	26.000			10.0	40.0

SURFACE CASING Report Date: 6/2/1949 00:00

Item	OD (in)	Grade	Wt. (ppf)	Top MD (ft)	Btm MD (ft)
CASING JOINT(S)	16.000	H-40	65.00	10.0	185.0

INTERMEDIATE CASING Report Date: 6/9/1949 00:00

Item	OD (in)	Grade	Wt. (ppf)	Top MD (ft)	Btm MD (ft)
CASING JOINT(S)	10.750	J-55	45.50	10.0	72.0
CASING JOINT(S)	10.750	J-55	40.50	72.0	2,202.0
CASING JOINT(S)	10.750	J-55	45.50	2,202.0	3,353.0

PRODUCTION CASING Report Date: 7/10/1949 00:00

Item	OD (in)	Grade	Wt. (ppf)	Top MD (ft)	Btm MD (ft)
CASING JOINT(S)	7.000	N-80	26.00	10.0	75.8
CASING JOINT(S)	7.000	N-80	23.00	75.8	5,287.7
CASING JOINT(S)	7.000	N-80	26.00	5,287.7	7,000.0

LINER Report Date: 7/31/1949 00:00

Item	OD (in)	Grade	Wt. (ppf)	Top MD (ft)	Btm MD (ft)
CASING JOINT(S)	5.500	J-55	17.00	6,961.0	7,077.0
SLOTTED LINER	5.500		17.00	7,077.0	7,703.0

Well: 342-3G S/T/R: 3G/31S/24E

CASING CEMENT DETAIL

Sfc Csg. Cmt Vol: 400 sx
Hole Size: 22"
Casing Size: 16"
Top Job: No
Rtns to Sfc: No
TTOC: Sfc

Interm Csg. Cmt Vol: 900 sx
Hole Size: 15"
Casing Size: 10.75"
Top Job: No
Rtns to Sfc: No
TOC: 1760' (Per Thermometric Survey)

Prod. Csg. Cmt Vol: 400 sx
Hole Size: 9.625"
Casing Size: 7"
Top Job: No
Rtns to Sfc: No
TOC: 5400' (Per Thermometric Survey)

Liner Cmt Vol: Landed
Hole Size: 6.125"
Casing Size: 5.5"
Top Job:
Rtns to Sfc:
TTOC:

Top of Formation:
B-Sand 6921'

Volume Behind Pipe:
1.3 Yield Assumed
Theoretical Calculations (TTOC)
