Event: WELL MAINT - RIGLESS
Event End: 12/28/2010 00:00
Sec. Reason:
End Status:
Well Classification: INJECTION

OCCIDENTAL OF ELK HILLS INC

352-2G

Ground Level: 845.0ft
Datum: ORIGINAL KB @ 862.00ft (default)
API No.: 0402968290

Wellbore: ORIGINAL HOLE
PBMD: 7,997.0ft
Btm TMD: 8,050.0ft
Spud Date: 1/27/1983 00:00
BH Coord X: 6,153,569.34uss ft
BH Coord Y: 2,285,692.79uss ft

Casing Shoes (ft) | Schematic (12/28/2010) | Openings Top/Btm/Type/Status

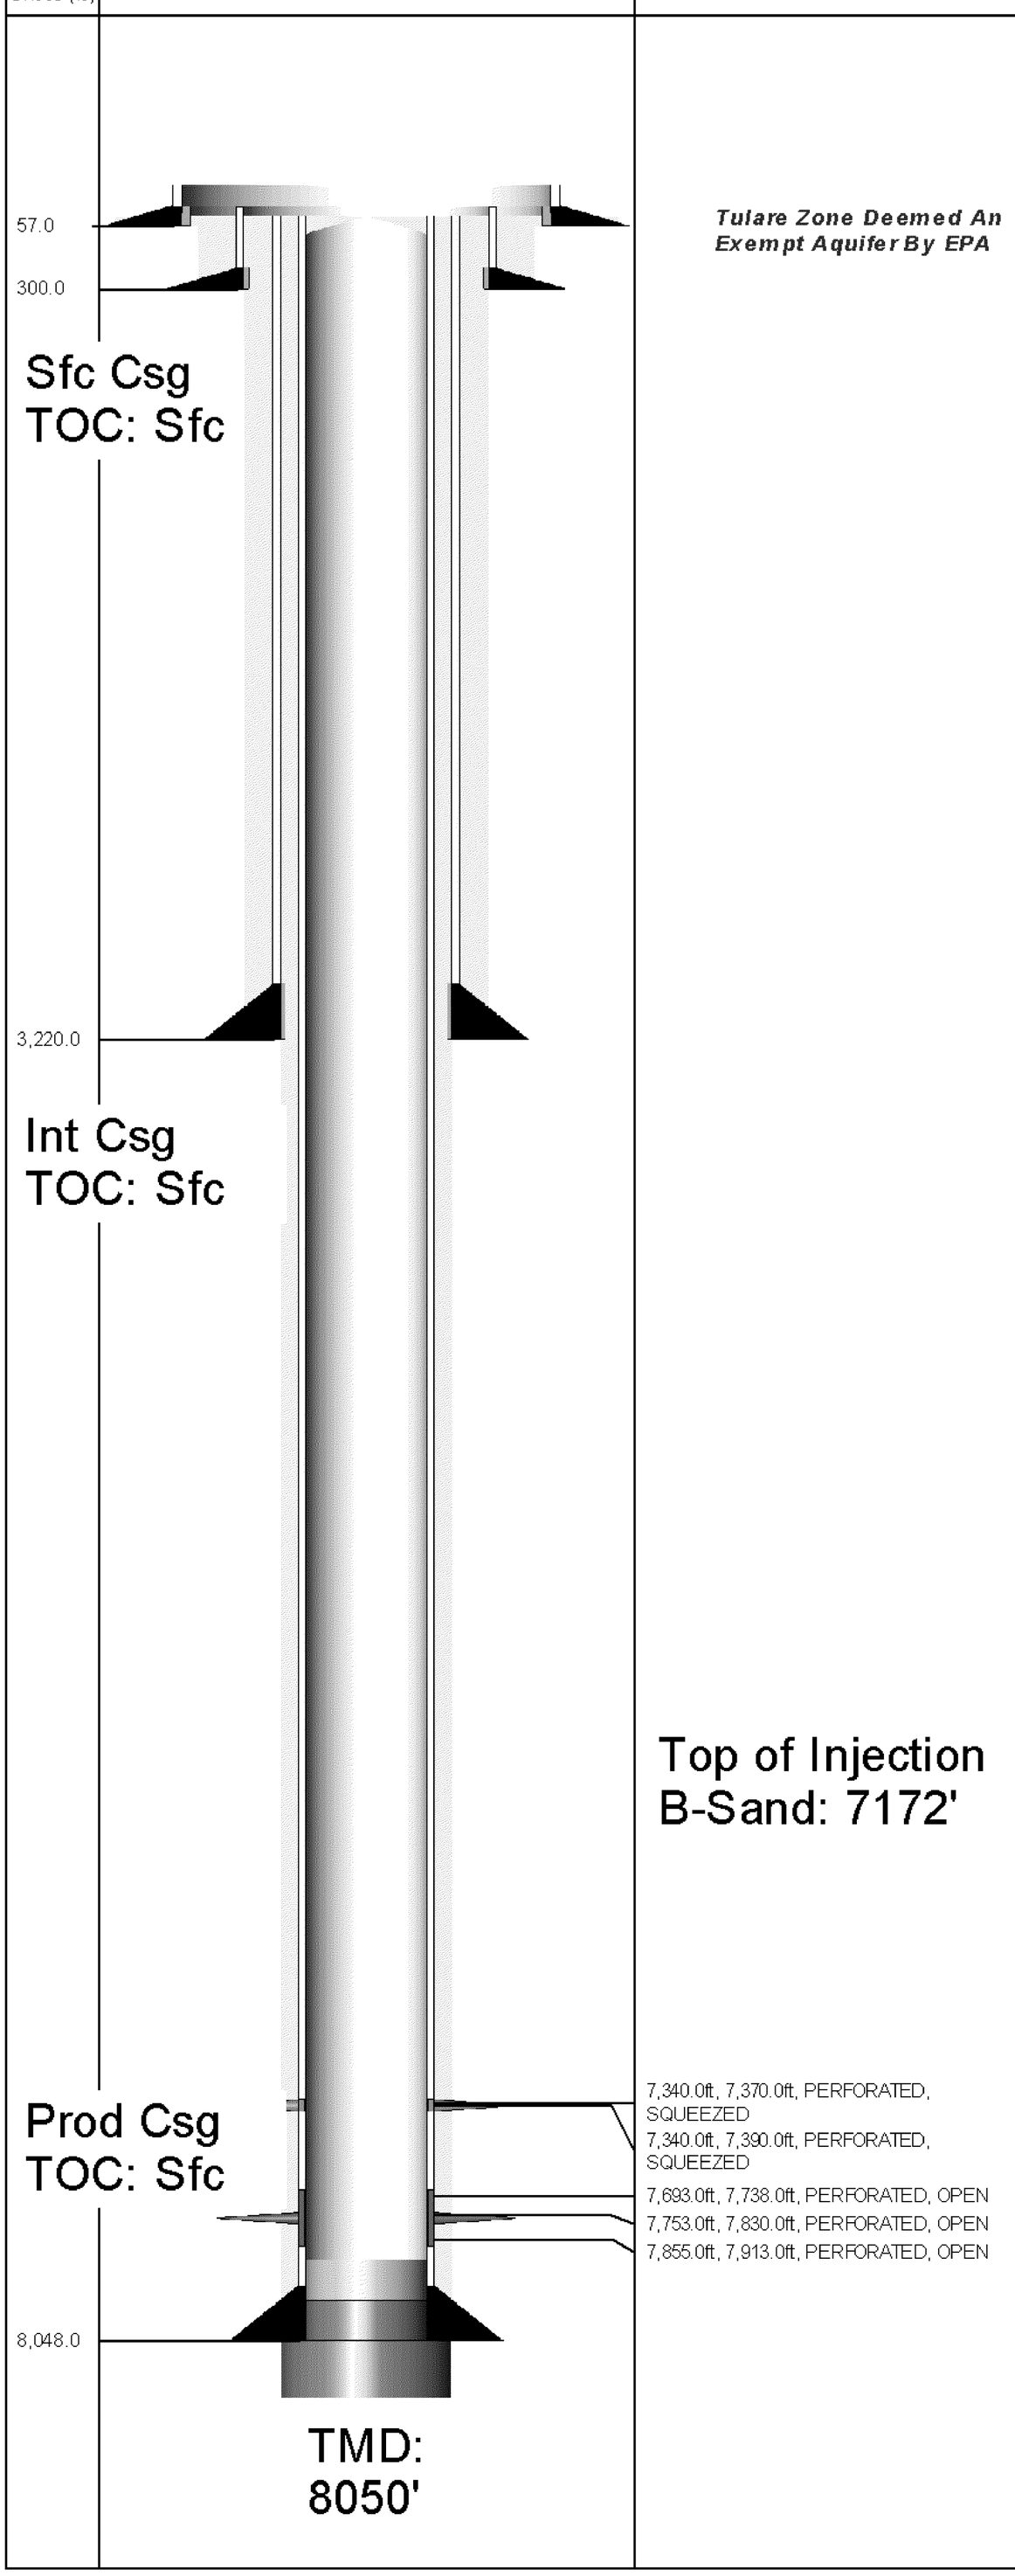

TUBING STRING — Report Date: 7/24/1984 00:00

Component	Top MD (ft)	Btm MD (ft)
TH-SGL	17.0	17.6
TBGJNT	17.6	7,630.7
PKR-S	7,630.7	7,637.5
PUPJNT	7,637.5	7,647.6
NOGO-O	7,647.6	7,648.9
PUPJNT	7,648.9	7,655.0
BELCOL	7,655.0	7,655.4

PLUG BACK — Report Date: 2/18/2004 00:00

Component	Top MD (ft)	Btm MD (ft)
FILL	7,964.0	7,997.0

PLUG BACK — Report Date: 4/29/2005 00:00

Component	Top MD (ft)	Btm MD (ft)
FILL	7,966.0	7,997.0

PLUG BACK — Report Date: 8/22/1983 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,997.0	8,048.0

PLUG BACK — Report Date: 2/15/1983 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	8,048.0	8,050.0

CONDUCTOR CASING — Report Date: 1/21/1983 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	20.000			17.0	57.0

SURFACE CASING — Report Date: 1/27/1983 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	13.375	H-40	48.00	17.0	298.7
GUIDE SHOE	13.375			298.7	300.0

INTERMEDIATE CASING — Report Date: 1/31/1983 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	9.625	K-55	40.00	17.0	3,218.7
GUIDE SHOE	9.625			3,218.7	3,220.0

PRODUCTION CASING — Report Date: 2/15/1983 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	7.000	N-80	26.00	17.0	86.6
CASING JOINT(S)	7.000	K-55	23.00	86.6	5,022.8
CASING JOINT(S)	7.000	K-55	26.00	5,022.8	6,629.1
FLAG JOINT	7.000	K-55	23.00	6,629.1	6,649.9
CASING JOINT(S)	7.000	N-80	26.00	6,649.9	7,996.8
FLOAT COLLAR	7.000	N-80		7,996.8	7,998.6
CASING JOINT(S)	7.000	N-80	26.00	7,998.6	8,045.7
FLOAT SHOE	7.000			8,045.7	8,048.0

Well: 352-2G S/T/R: 2G/31S/24E

CASING CEMENT DETAIL
- - -
Sfc Csg. Cmt Vol: 415 cf
Hole Size: 17-1/2"
Casing Size: 13-3/8"
Top Job: NO
Rtns to Sfc: YES (45 cf)
TOC: NA
- - -

Interm Csg. Cmt Vol: 1530 cf
Hole Size: 12-1/4"
Casing Size: 9-5/8"
Top Job: NO
Rtns to Sfc: YES (40 cf)
TOC: NA
- - -

Prod. Csg. Cmt Vol: 2125 cf
Hole Size: 8-3/4"
Casing Size: 7"
Top Job: NO
Rtns to Sfc: YES (10 cf)
TOC: NA
- - -

Liner Cmt Vol: None
Hole Size:
Casing Size:
Top Job:
Rtns to Sfc:
TTOC:
- - -

Top of Formation:
B-Sand: 7172'

- - -

Volume Behind Pipe:
1.15 Yield Assumed
Theoretical Calculations (TTOC)
DWN April 2011
