Event: DEV DRILLING
Event End: 2/9/2001 00:00
Sec. Reason:
End Status: DRILLED
Well Classification: DEVELOPMENT

OCCIDENTAL OF ELK HILLS INC

321H-3G

Ground Level: 962.0ft
Datum: ORIGINAL KB @ 979.00ft (default)
API No.: 0402979893

Wellbore: ORIGINAL HOLE
PBMD: 6625.0ft
Btm TMD: 7,640.0ft
Spud Date: 7/30/1987 00:00
BH Coord X: 6,146,431.00uss ft
BH Coord Y: 2,286,523.00uss ft

Casing Shoes (ft) | Schematic (2/9/2001) | Openings Top/Btm/Type/Status

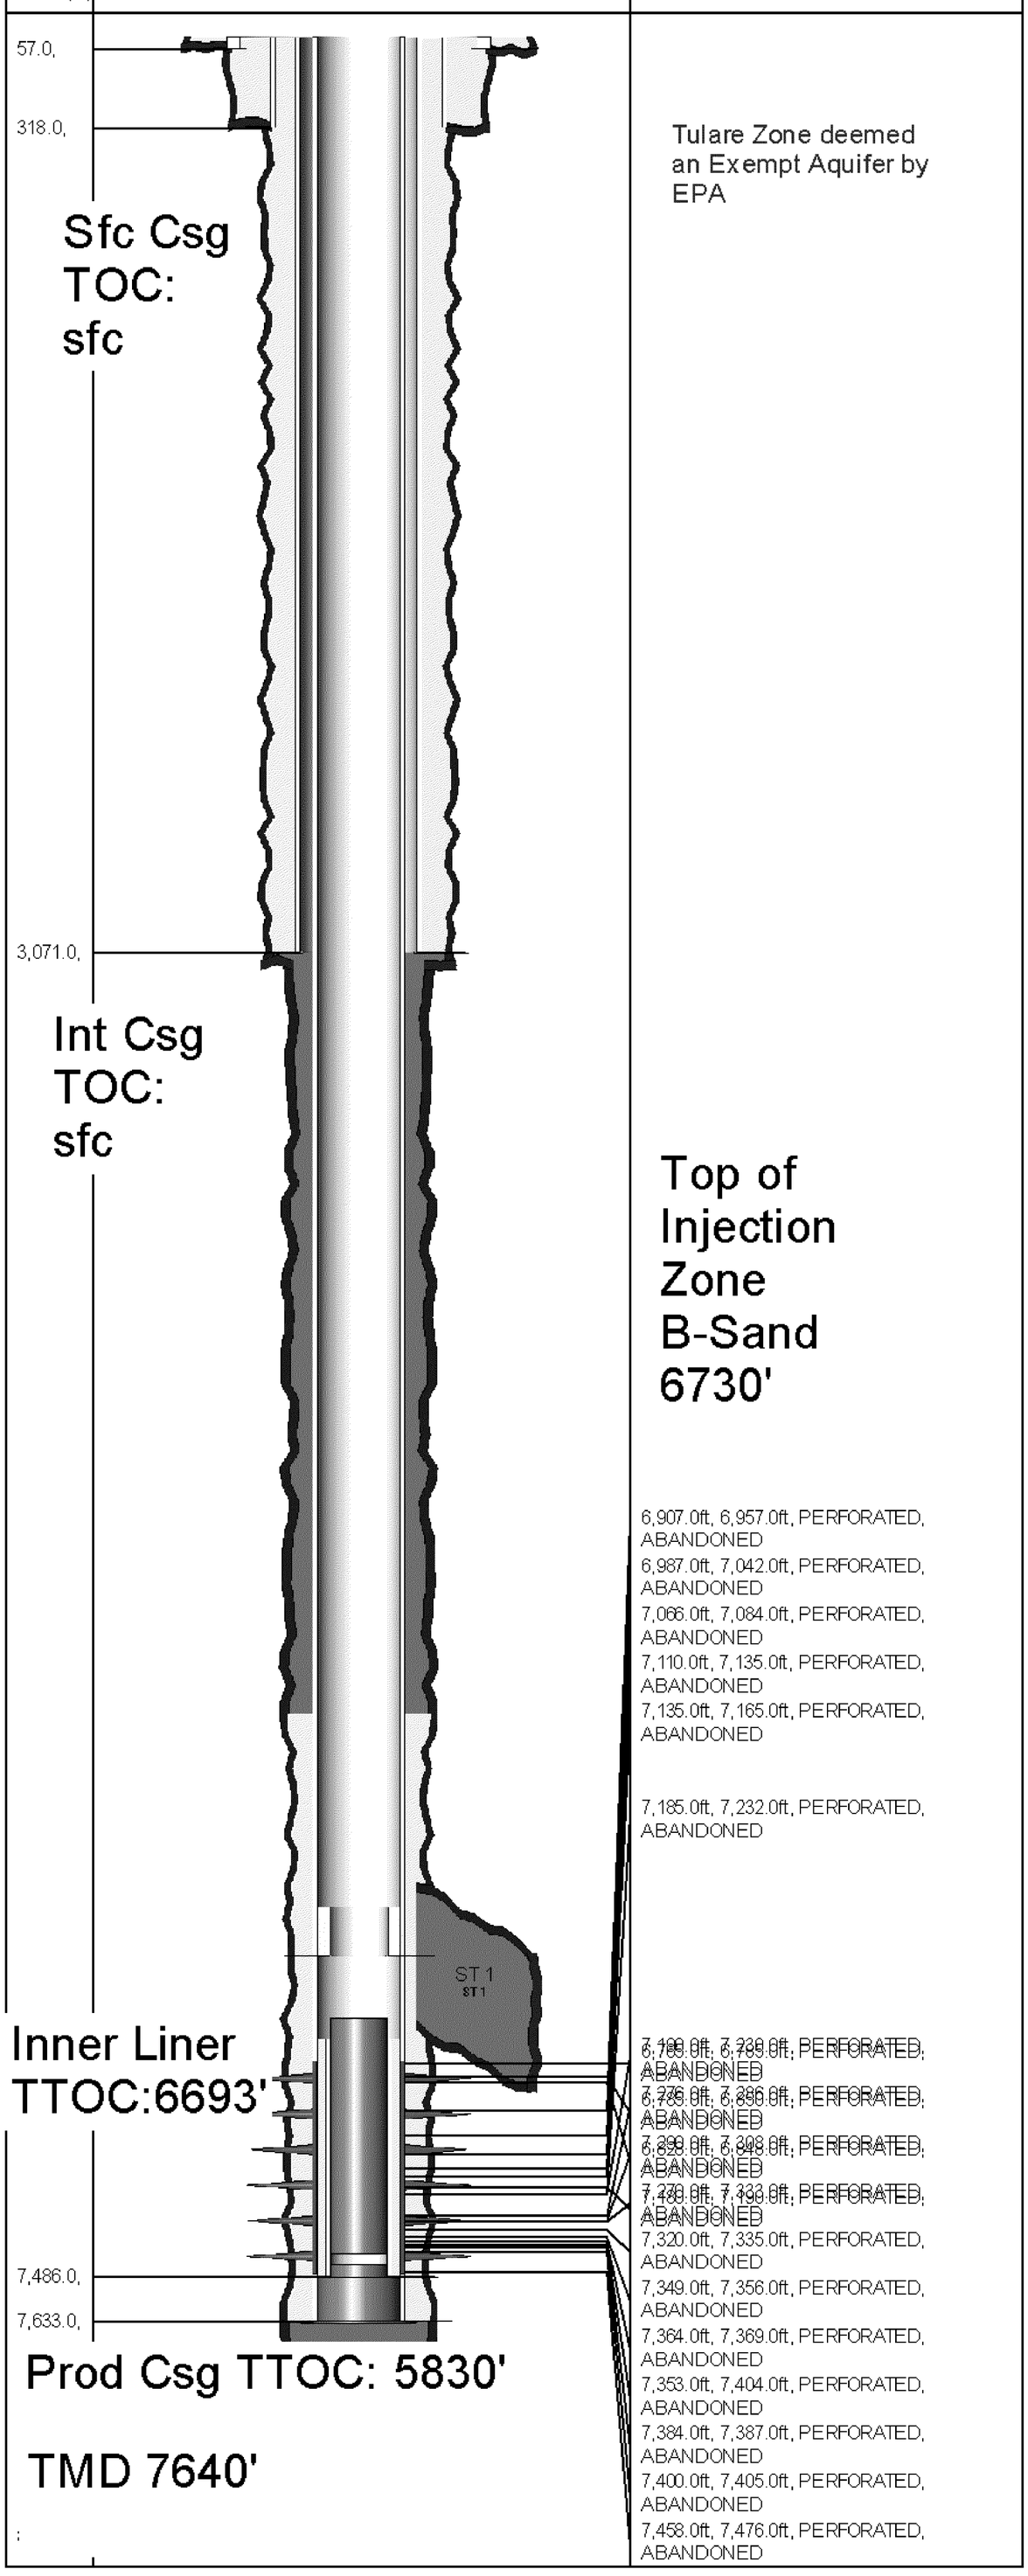

PLUG BACK Report Date: 9/12/2000 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	6,625.0	7,407.0

PLUG BACK Report Date: 9/9/1998 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,445.0	7,486.0

PLUG BACK Report Date: 9/8/1998 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,486.0	7,488.0

PLUG BACK Report Date: 9/7/1998 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,488.0	7,524.0

PLUG BACK Report Date: 9/24/1987 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,524.0	7,633.0

PLUG BACK Report Date: 8/21/1987 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,633.0	7,640.0

ROD STRING Report Date: 11/1/2000 00:00

Component	Top MD (ft)	Btm MD (ft)
POLROD	13.0	43.0
PNYROD	43.0	49.0
PNYROD	49.0	69.0
ROD	69.0	6,309.0
INSPMP	6,309.0	

CONDUCTOR CASING Report Date: 7/15/1987 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	20.000			17.0	57.0

SURFACE CASING Report Date: 8/1/1987 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	13.375	H-40	48.00	21.0	318.0

INTERMEDIATE CASING Report Date: 8/7/1987 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	9.625	K-55	40.00	19.0	3,071.0

PRODUCTION CASING Report Date: 8/21/1987 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	7.000	N-80	26.00	17.0	55.0
CASING JOINT(S)	7.000	K-55	23.00	55.0	5,130.0
CASING JOINT(S)	7.000	K-55	26.00	5,130.0	7,118.0
CASING JOINT(S)	7.000	N-80	26.00	7,118.0	7,633.0

INNER LINER Report Date: 9/8/1998 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	5.000	P-110	18.00	6,693.0	7,486.0

Well: 321H-3G S/T/R: 3G/31S/24E

CASING CEMENT DETAIL
- - -

Cond Csg. Cmt Vol: Unknown amount
Hole Size: 22" (Est.)
Casing Size: 20"
Top Job: Unknown
Rtns to Sfc: Yes (22 cfl)
TOC: Surface
- - -

Sfc Csg. Cmt Vol: 400 cf
Hole Size: 17.5"
Casing Size: 13.375"
Top Job: No
Rtns to Sfc: Yes (20 cf)
TOC: Surface
- - -

Interm Csg. Cmt Vol: 1330 cf
Hole Size: 12.25"
Casing Size: 9.625"
Top Job: No
Rtns to Sfc: Yes (120 cf)
TOC: Surface
- - -

Prod. Csg. Cmt Vol: 1300 cf
Hole Size: 8.75"
Casing Size: 7"
Top Job: No
Rtns to Sfc: No
TTOC: 5830'
- - -

Liner Cmt Vol: 77 cf
Hole Size: 6.28" (7" Casing ID)
Casing Size: 5"
Top Job: No
Rtns to Sfc: No
TTOC: 6693 '
- - -

Top of Formation:
B-Sand 6730'

- - -

Volume Behind Pipe:
1.18 Yield Assumed
Theoretical Calculations (TTOC)
