OCCIDENTAL OF ELK HILLS INC

325-35S

Event: WELL MAINT - RIGLESS
Event End:
Sec. Reason:
End Status:
Well Classification: DEVELOPMENT

Ground Level: 743.0ft
Datum: ORIGINAL KB @ 760.00ft (default)
API No.: 0402981460

Wellbore: ORIGINAL HOLE
PBMD: 7,347.0ft
Btm TMD: 8,555.0ft
Spud Date: 11/21/1987 00:01
BH Coord X: 6,151,891.82uss ft
BH Coord Y: 2,289,051.19uss ft

Casing Shoes (ft) | Schematic (9/13/2011) | Openings Top/Btm/Type/Status

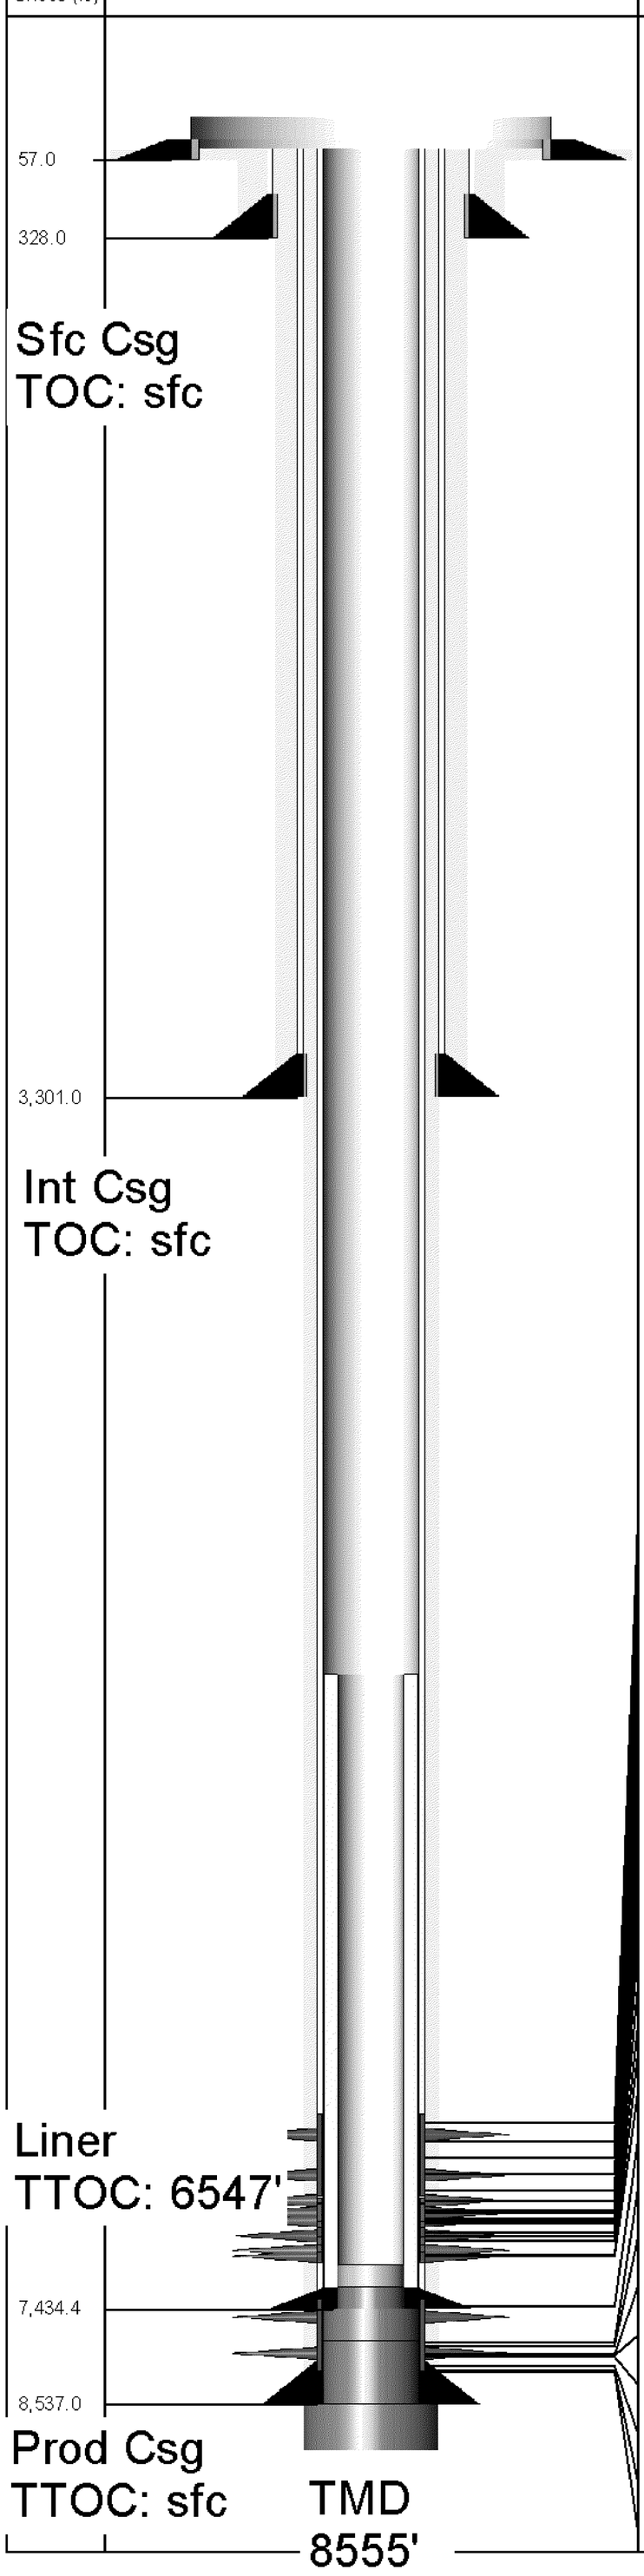

Tulare Zone Deemed An Exempt Aquifer By EPA

Top of Injection Zone
B-Sand: 6631'

6,820.0ft, 6,874.0ft, PERFORATED, ABANDONED
6,894.0ft, 6,930.0ft, PERFORATED, ABANDONED
6,950.0ft, 6,990.0ft, PERFORATED, ABANDONED
7,012.0ft, 7,038.0ft, PERFORATED, ABANDONED
7,060.0ft, 7,100.0ft, PERFORATED, ABANDONED
7,110.0ft, 7,125.0ft, PERFORATED, OPEN
7,130.1ft, 7,170.0ft, PERFORATED, OPEN
7,130.0ft, 7,190.0ft, PERFORATED, ABANDONED
7,175.0ft, 7,186.0ft, PERFORATED, OPEN
7,186.0ft, 7,190.0ft, PERFORATED, OPEN
7,190.0ft, 7,204.0ft, PERFORATED, OPEN
7,209.0ft, 7,244.0ft, PERFORATED, OPEN
7,210.0ft, 7,270.0ft, PERFORATED, ABANDONED
7,250.0ft, 7,260.0ft, PERFORATED, OPEN
7,276.0ft, 7,330.0ft, PERFORATED, OPEN
7,295.0ft, 7,325.0ft, PERFORATED, ABANDONED
7,395.0ft, 7,435.0ft, PERFORATED, ABANDONED
7,450.0ft, 7,490.0ft, PERFORATED, ABANDONED
7,550.0ft, 7,620.0ft, PERFORATED, ABANDONED
7,868.0ft, 7,880.0ft, PERFORATED, ABANDONED
7,890.0ft, 7,920.0ft, PERFORATED, ABANDONED
7,948.0ft, 7,956.0ft, PERFORATED, ABANDONED
8,253.0ft, 8,262.0ft, PERFORATED, ABANDONED
8,385.0ft, 8,395.0ft, PERFORATED, ABANDONED
8,410.0ft, 8,443.0ft, PERFORATED, ABANDONED

TUBING STRING — Report Date: 8/19/2002 00:00

Component	Top MD (ft)	Btm MD (ft)
TH-SGL	17.0	17.6
FATNIP	17.6	18.9
TBGJNT	18.9	6,399.8
XO	6,399.8	6,400.9
TBGJNT	6,400.9	6,620.9
ON-OFF	6,620.9	6,622.0
PKR-S	6,622.0	6,626.0
PUPJNT	6,626.0	6,632.1
PNIP-O	6,632.1	6,633.5
WLREG	6,633.5	6,633.9

PLUG BACK — Report Date: 11/3/2003 00:00

Component	Top MD (ft)	Btm MD (ft)
FILL	7,340.0	7,347.0

PLUG BACK — Report Date: 2/26/2002 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,347.0	7,434.4

PLUG BACK — Report Date: 2/18/2002 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,434.4	7,440.0

PLUG BACK — Report Date: 2/7/2002 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	7,440.0	8,480.0

PLUG BACK — Report Date: 9/14/1998 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	8,480.0	8,537.0

PLUG BACK — Report Date: 1/11/1988 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	8,537.0	8,555.0

CONDUCTOR CASING — Report Date: 11/1/1987 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	26.000			17.0	57.0

SURFACE CASING — Report Date: 11/21/1987 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	13.375	H-40	48.00	17.0	328.0

INTERMEDIATE CASING — Report Date: 11/26/1987 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	9.625	K-55	40.00	17.0	3,301.0

PRODUCTION CASING — Report Date: 1/11/1988 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	7.000	N-80	29.00	17.0	285.8
CASING JOINT(S)	7.000	K-55	23.00	285.8	4,271.6
CASING JOINT(S)	7.000	K-55	26.00	4,271.6	6,430.6
CASING JOINT(S)	7.000	N-80	29.00	6,430.6	6,598.5
FLAG JOINT	7.000	N-80	29.00	6,598.5	6,620.4
CASING JOINT(S)	7.000	N-80	29.00	6,620.4	8,448.2
FLOAT COLLAR	7.000	N-80	29.00	8,448.2	8,450.2
CASING JOINT(S)	7.000	N-80	29.00	8,450.2	8,534.3
GUIDE SHOE	7.000	N-80	29.00	8,534.3	8,537.0

INNER LINER — Report Date: 2/18/2002 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
LINER HANGER PACKER	5.572	P-110	18.00	6,477.0	6,495.8
CROSSOVER	5.500	P-110	18.00	6,495.8	6,498.6
LINER HANGER	5.971	P-110	18.00	6,498.6	6,504.7
CASING JOINT(S)	5.000	P-110	18.00	6,504.7	7,340.8
FLOAT COLLAR	5.572	P-110	18.00	7,340.8	7,342.3
CASING JOINT(S)	5.000	P-110	18.00	7,342.3	7,386.8
FLOAT COLLAR	5.570	P-110	18.00	7,386.8	7,388.3
CASING JOINT(S)	5.000	P-110	18.00	7,388.3	7,432.6
GUIDE SHOE	5.572	P-110	18.00	7,432.6	7,434.4

Well: 325-35S S/T/R: 35S/30S/24E

CASING CEMENT DETAIL
- - -
Sfc Csg. Cmt Vol: 500 cf
Hole Size: 17-1/2"
Casing Size: 13-3/8"
Top Job: NO
Rtns to Sfc: YES (75 cf)
TOC: sfc
- - -

Interm Csg. Cmt Vol: 1580 cf
Hole Size: 12-1/4"
Casing Size: 9-5/8"
Top Job: NO
Rtns to Sfc: YES (35 cf)
TOC: sfc
- - -

Prod. Csg. Cmt Vol: 1700 cf
Hole Size: 8-3/4"
Casing Size: 7"
Top Job: NO
Rtns to Sfc: NO
TTOC: Surface
- - -

Liner Cmt Vol: 104 cf
Hole Size: 6.184" (7" Csg ID)
Casing Size: 5"
Top Job: NO
Rtns to Sfc: NO
TTOC: 6547'
- - -

Top of Formation:
B-Sand: 6631'

- - -

Volume Behind Pipe:
1.3 and 1.18 Yield Assumed
Theoretical Calculations (TTOC)
DWN April 2011
