OCCIDENTAL OF ELK HILLS INC

361XH-2G

Event: WELL MAINT - RIG
Event End:
Sec. Reason:
End Status:
Well Classification: DEVELOPMENT - CLASS II

Ground Level: 871.7ft
Datum: Original KB @ 894.70ft (default)
API No.: 0403025976

Wellbore: ORIGINAL HOLE
PBMD: 9,365.0ft
Btm TMD: 9,423.0ft
Spud Date: 10/24/2004 00:00
BH Coord X: 6,156,358.39uss ft
BH Coord Y: 2,288,147.19uss ft

Casing Shoes (ft) | Schematic (4/28/2012) | Openings Top/Btm/Type/Status

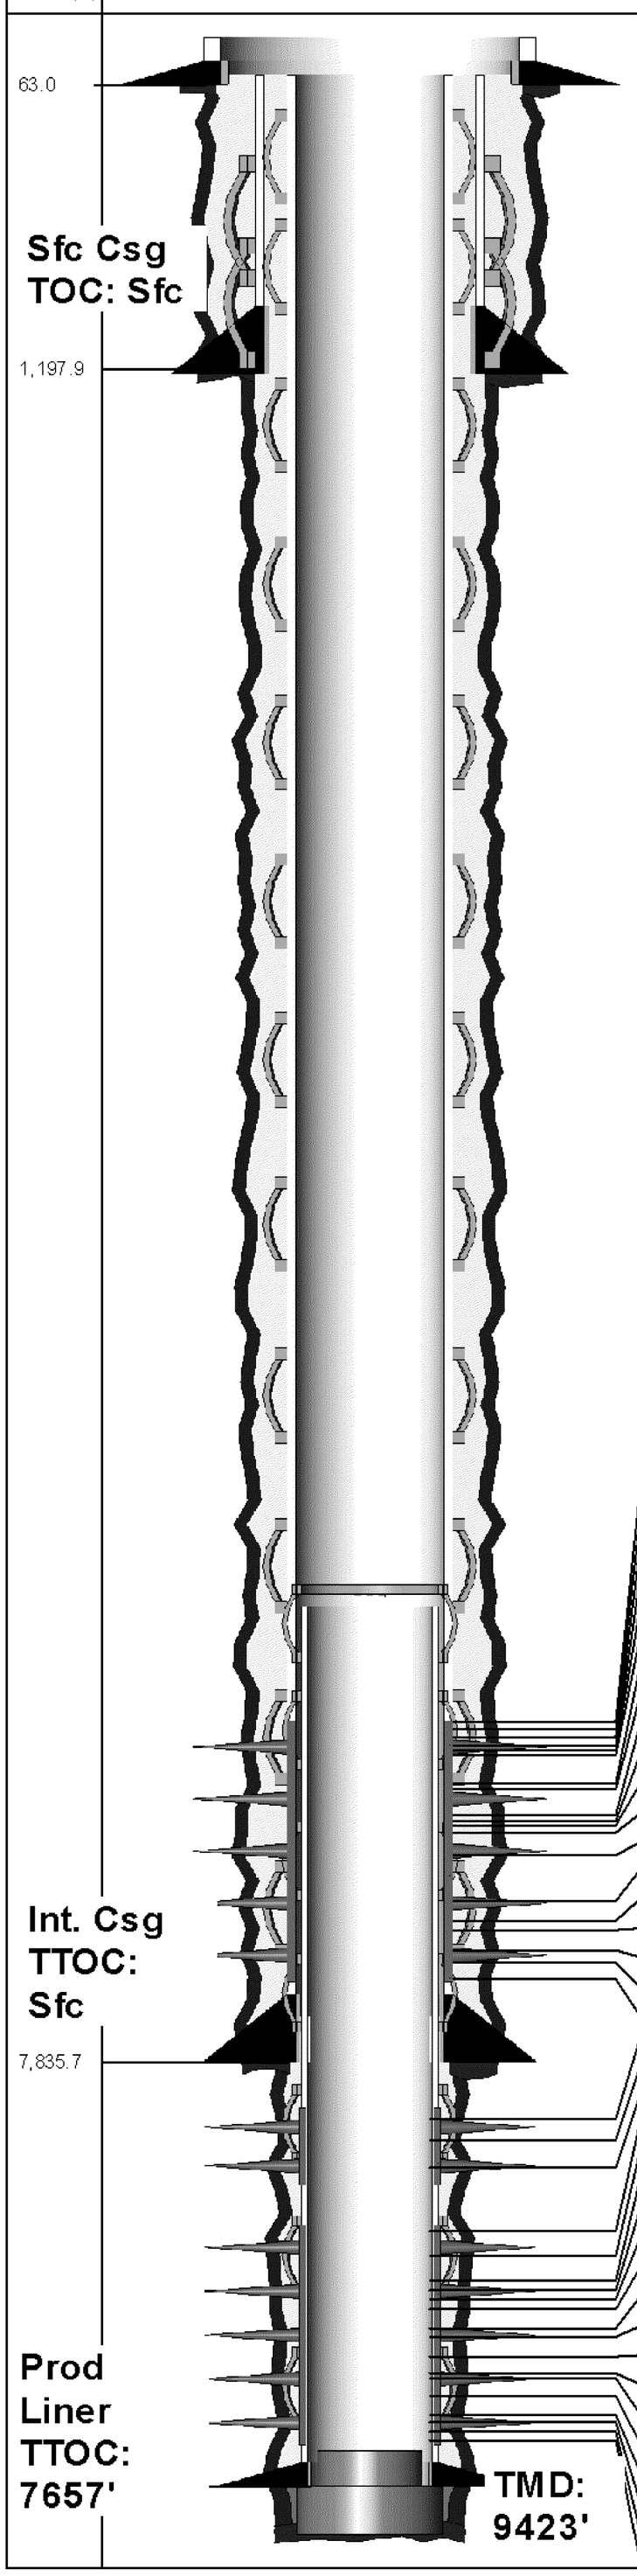

Wellbore Status: Active Producer

NO USDW PRESENT

Top of Injection Zone: B-Sand 7469'

6,494.0ft, 6,501.0ft, PERFORATED, OPEN
6,520.0ft, 6,530.0ft, PERFORATED, OPEN
6,552.0ft, 6,560.0ft, PERFORATED, OPEN
6,588.0ft, 6,592.0ft, PERFORATED, OPEN
6,605.0ft, 6,615.0ft, PERFORATED, OPEN
6,625.0ft, 6,630.0ft, PERFORATED, OPEN
6,735.0ft, 6,740.0ft, PERFORATED, OPEN
6,753.0ft, 6,770.0ft, PERFORATED, OPEN
6,848.0ft, 6,876.0ft, PERFORATED, OPEN
6,882.0ft, 6,894.0ft, PERFORATED, OPEN
6,900.0ft, 6,906.0ft, PERFORATED, OPEN
6,926.0ft, 6,938.0ft, PERFORATED, OPEN
7,016.0ft, 7,026.0ft, PERFORATED, OPEN
7,190.0ft, 7,212.0ft, PERFORATED, OPEN
7,268.0ft, 7,290.0ft, PERFORATED, OPEN
7,304.0ft, 7,326.0ft, PERFORATED, OPEN
7,386.0ft, 7,402.0ft, PERFORATED, OPEN
7,434.0ft, 7,454.0ft, PERFORATED, OPEN
7,496.0ft, 7,518.0ft, PERFORATED, OPEN
8,015.0ft, 8,100.0ft, PERFORATED, OPEN
8,120.0ft, 8,162.0ft, PERFORATED, OPEN
8,180.0ft, 8,320.0ft, PERFORATED, OPEN
8,478.0ft, 8,520.0ft, PERFORATED, OPEN
8,575.0ft, 8,616.0ft, PERFORATED, OPEN
8,685.0ft, 8,698.0ft, PERFORATED, OPEN
8,724.0ft, 8,740.0ft, PERFORATED, OPEN
8,740.0ft, 8,792.0ft, PERFORATED, OPEN
8,800.0ft, 8,812.0ft, PERFORATED, OPEN
8,872.0ft, 8,890.0ft, PERFORATED, OPEN
8,890.0ft, 8,940.0ft, PERFORATED, OPEN
8,940.0ft, 9,045.0ft, PERFORATED, OPEN
9,045.0ft, 9,070.0ft, PERFORATED, OPEN
9,070.0ft, 9,085.0ft, PERFORATED, OPEN
9,136.0ft, 9,159.0ft, PERFORATED, OPEN
9,214.0ft, 9,227.0ft, PERFORATED, OPEN
9,242.0ft, 9,258.0ft, PERFORATED, OPEN
9,283.0ft, 9,292.0ft, PERFORATED, OPEN
9,303.0ft, 9,340.0ft, PERFORATED, OPEN

PLUG BACK Report Date: 11/11/2004 00:00

Component	Top MD (ft)	Btm MD (ft)
CEMENT	9,365.0	9,388.0
CEMENT	9,388.0	9,423.0

ROD STRING Report Date: 8/5/2011 00:00

Component	Top MD (ft)	Btm MD (ft)
POLRDL	0.0	36.0
PNYROD	36.0	44.0
ROD	44.0	74.0
COROD	74.0	1,233.0
COROD	1,233.0	2,943.0
COROD	2,943.0	7,713.0
RSTBAR	7,713.0	7,717.0
ON-OFF	7,717.0	7,718.0
RSTBAR	7,718.0	7,722.0
INSPMP	7,722.0	7,746.0

CONDUCTOR CASING Report Date: 10/11/2004 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	14.000			23.0	63.0

SURFACE CASING Report Date: 10/25/2004 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
CASING JOINT(S)	9.625	K-55	36.00	23.0	1,159.9
	9.625			1,159.9	1,159.9
CASING JOINT(S)	9.625	K-55	36.00	1,159.9	1,196.8
GUIDE SHOE	9.625			1,196.8	1,198.0

INTERMEDIATE CASING Report Date: 11/4/2004 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
LINER HANGER	7.000	N-80	26.00	23.0	24.0
PUP JOINT	7.000	N-80	26.00	24.0	27.4
PUP JOINT	7.000	N-80	26.00	27.4	48.9
CASING JOINT(S)	7.000	N-80	26.00	48.9	7,461.0
CROSSOVER	7.000	N-80	26.00	7,461.0	7,496.0
CASING JOINT(S)	7.000	N-80	26.00	7,496.0	7,747.1
FLOAT COLLAR	7.000	N-80	26.00	7,747.1	7,748.7
CASING JOINT(S)	7.000	N-80	26.00	7,748.7	7,834.0
FLOAT SHOE	7.000	N-80	26.00	7,834.0	7,835.7

LINER Report Date: 11/10/2004 00:00

Item	OD (in)	Grade	Wt. (ppf)	TopMD (ft)	BtmMD (ft)
TIE BACK RECEPTACLE	5.750	N-80		7,657.0	7,663.0
	6.000			7,663.0	7,664.4
PACKER (SINGLE)	6.000			7,664.4	7,667.0
SEALBORE EXTENSION	5.250	N-80		7,667.0	7,671.9
TIE BACK RECEPTACLE	5.750			7,671.9	7,677.9
	5.705			7,677.9	7,685.0
LINER HANGER	6.000			7,685.0	7,692.1
CASING JOINT(S)	5.000	N-80	15.00	7,692.1	9,333.4
LANDING COLLAR	5.000	N-80	15.00	9,333.4	9,335.7
FLOAT COLLAR	5.000	N-80	15.00	9,335.7	9,338.1
CASING JOINT(S)	5.000	N-80	15.00	9,338.1	9,385.1
FLOAT SHOE	5.000	N-80	15.00	9,385.1	9,388.0

Well: 361XH-2G S/T/R: 2G/31S/24E

CASING CEMENT DETAIL
- - -

Sfc Csg. Cmt Vol: 758 cf
Hole Size: 12.25"
Casing Size: 9.625"
Top Job: No
Rtns to Sfc: Yes (112 cf)
TOC: Sfc
- - -

Interm Csg. Cmt Vol: 2065 cf
Hole Size: 8.75"
Casing Size: 7"
Top Job: No
Rtns to Sfc: No
TTOC: Sfc
- - -

Prod. Csg. Cmt Vol:
Hole Size:
Casing Size:
Top Job:
Rtns to Sfc:
TTOC:
- - -

Liner Cmt Vol: 252 cf
Hole Size: 6.125"
Casing Size: 5"
Top Job:
Rtns to Sfc:
TTOC: 7657' (TOL)
- - -

Top of Injection Zone:
B-Sand 7469'
- - -

Volume Behind Pipe:
1.18 Yield Assumed
Theoretical Calculations (TTOC)
Apr 2012
