Message

From: Wayne Miller [Miller.Wayne@azdeq.gov]
Sent: 7/7/2016 8:22:20 PM
To: d'Almeida, Carolyn K. [dAlmeida.Carolyn@epa.gov]
Subject: 2016-7-7- wafb - ST12 - thanks - groundwater plume contours over time-

Thank you.

From: d'Almeida, Carolyn K. [mailto:dAlmeida.Carolyn@epa.gov]
Sent: Thursday, July 07, 2016 11:19 AM
To: Davis, Eva <Davis.Eva@epa.gov>; Dan Pope <DPope@css-dynamac.com>; Wayne Miller <Miller.Wayne@azdeq.gov>
Cc: Henning, Loren <Henning.Loren@epa.gov>; Butler, Thomas <Butler.Thomas@epa.gov>; Levine, Herb <Levine.Herb@epa.gov>; Brasaemle, Karla <KBrasaemle@TechLawInc.com>; ARohrbaugh@TechLawInc.com
Subject: 2016-7-7- wafb - ST12 groundwater plume contours over time- cda epa

This figure below is from the 2013 ROD amendment - note the extent of the 5000 ppb contour line

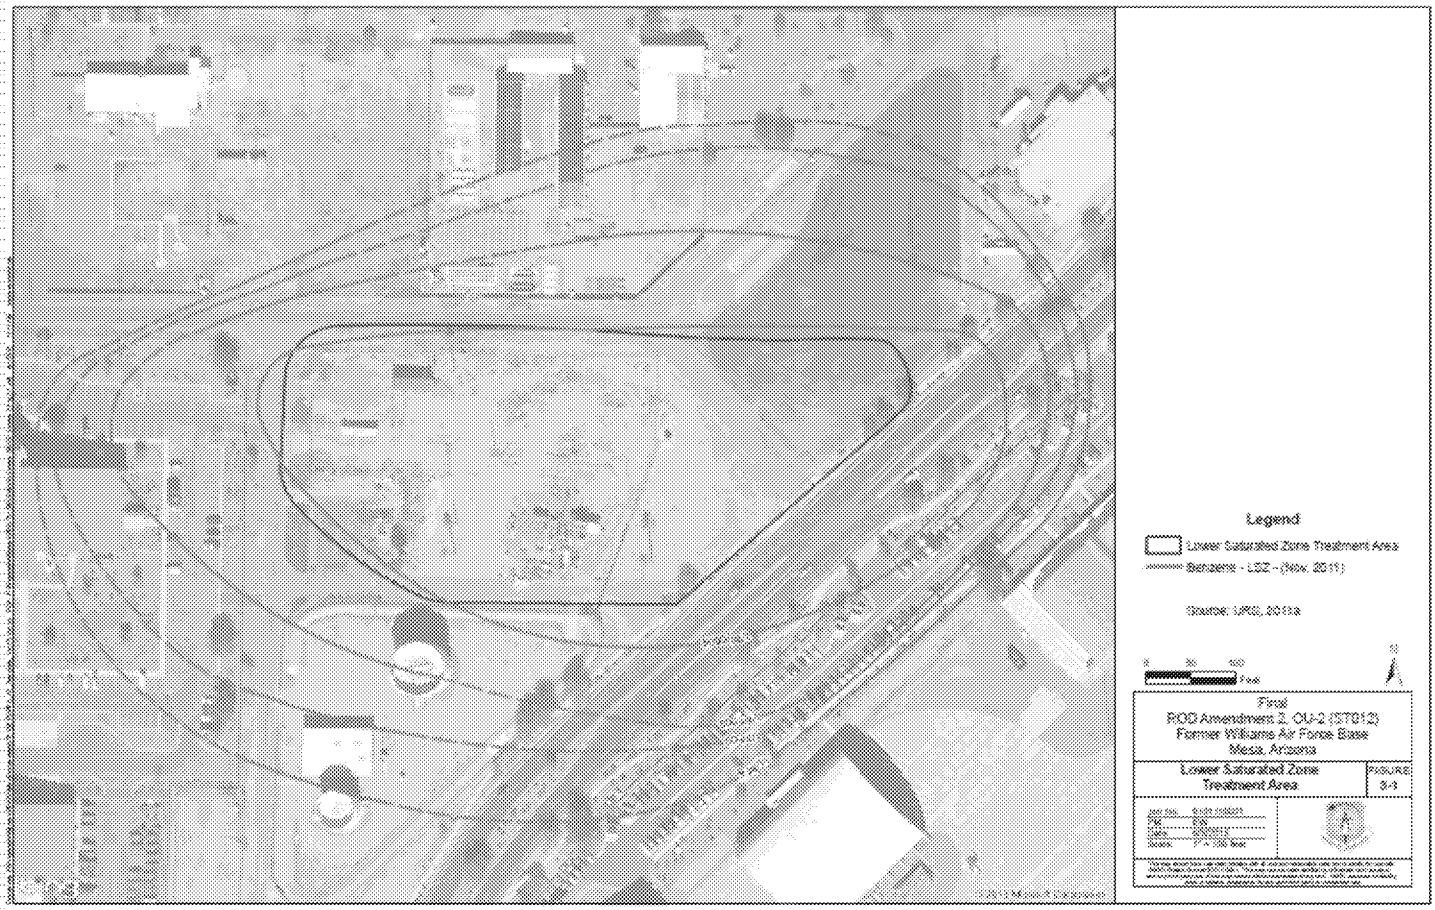

From the RDRA workplan: Note concentrations over 10,000 ppb present – believe this refers to soil cores, not dissolved in groundwater

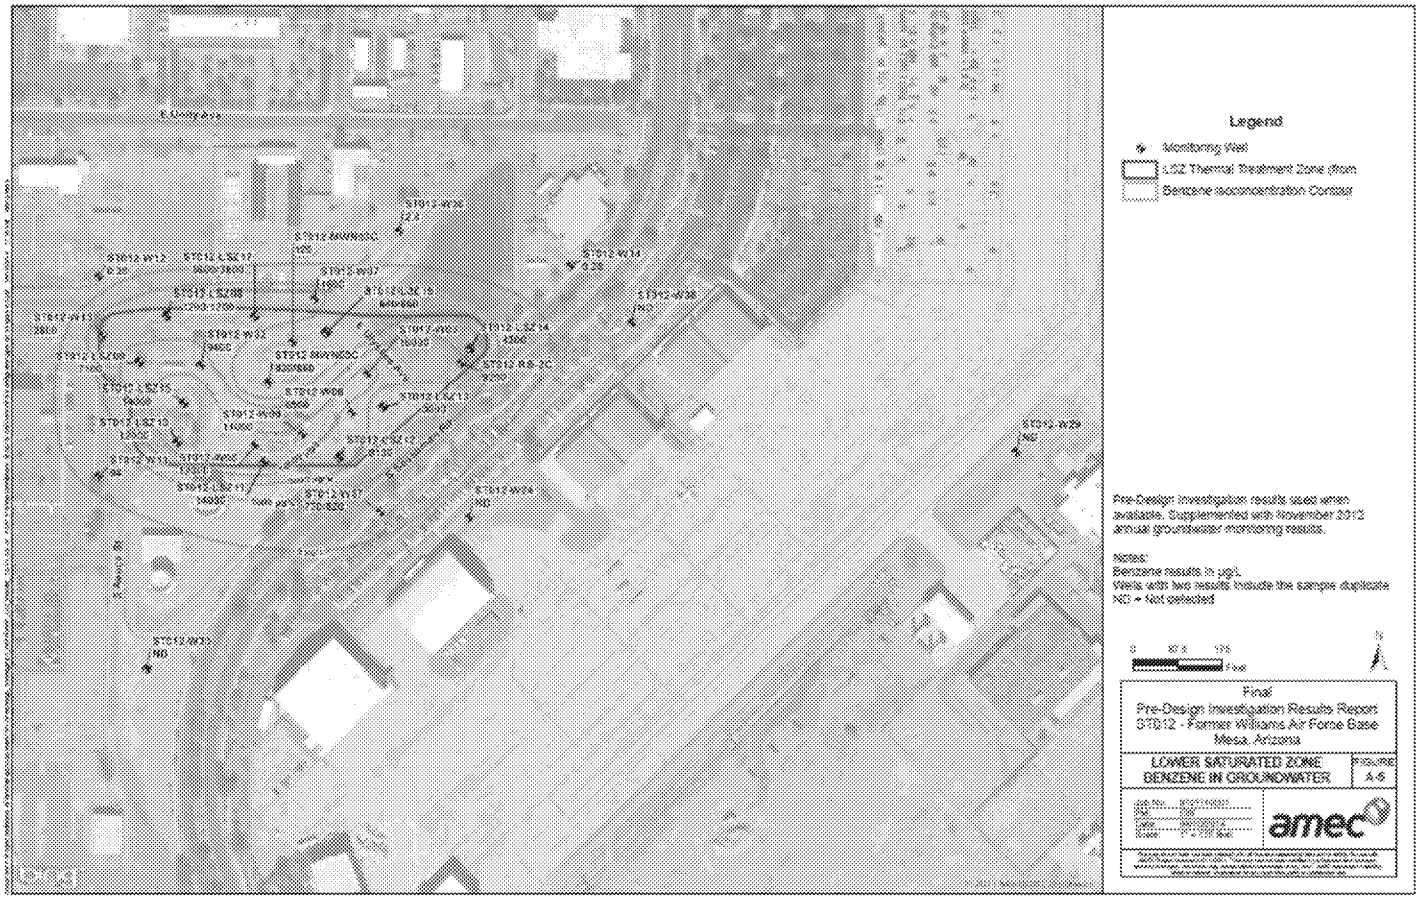

Here is Upper Water bearing zone contours; basis of design for SEE in the Upper Water Bearing Zone

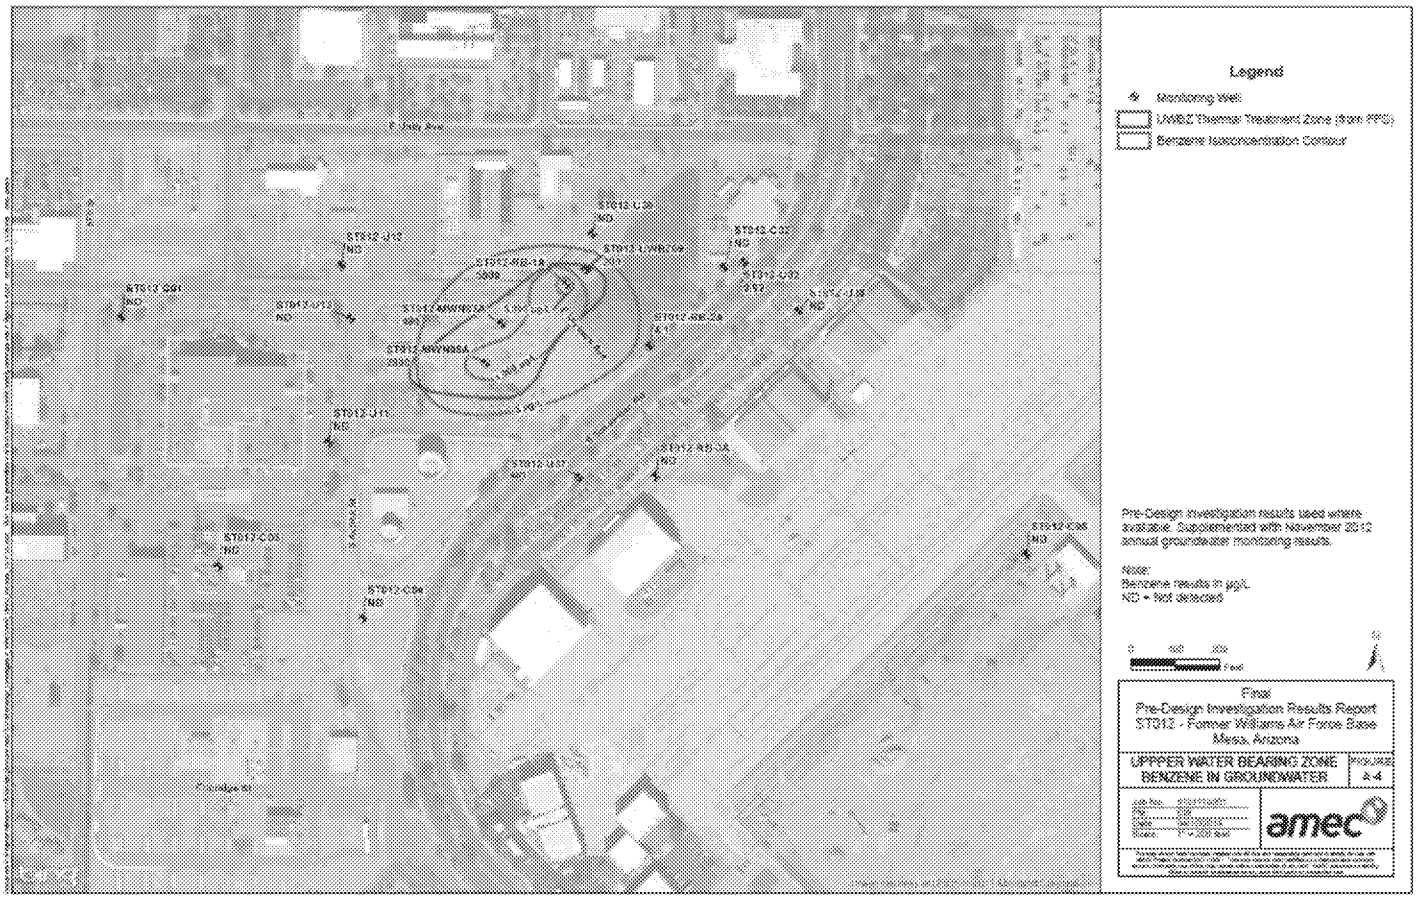

2014 Annual groundwater monitoring report – November 2014 1 month after initiation of SEE - note where 5000 ppb benzene concentration was is now 1000 ppb benzene concentration. Where did all of the benzene go ? Is it volatilizing?

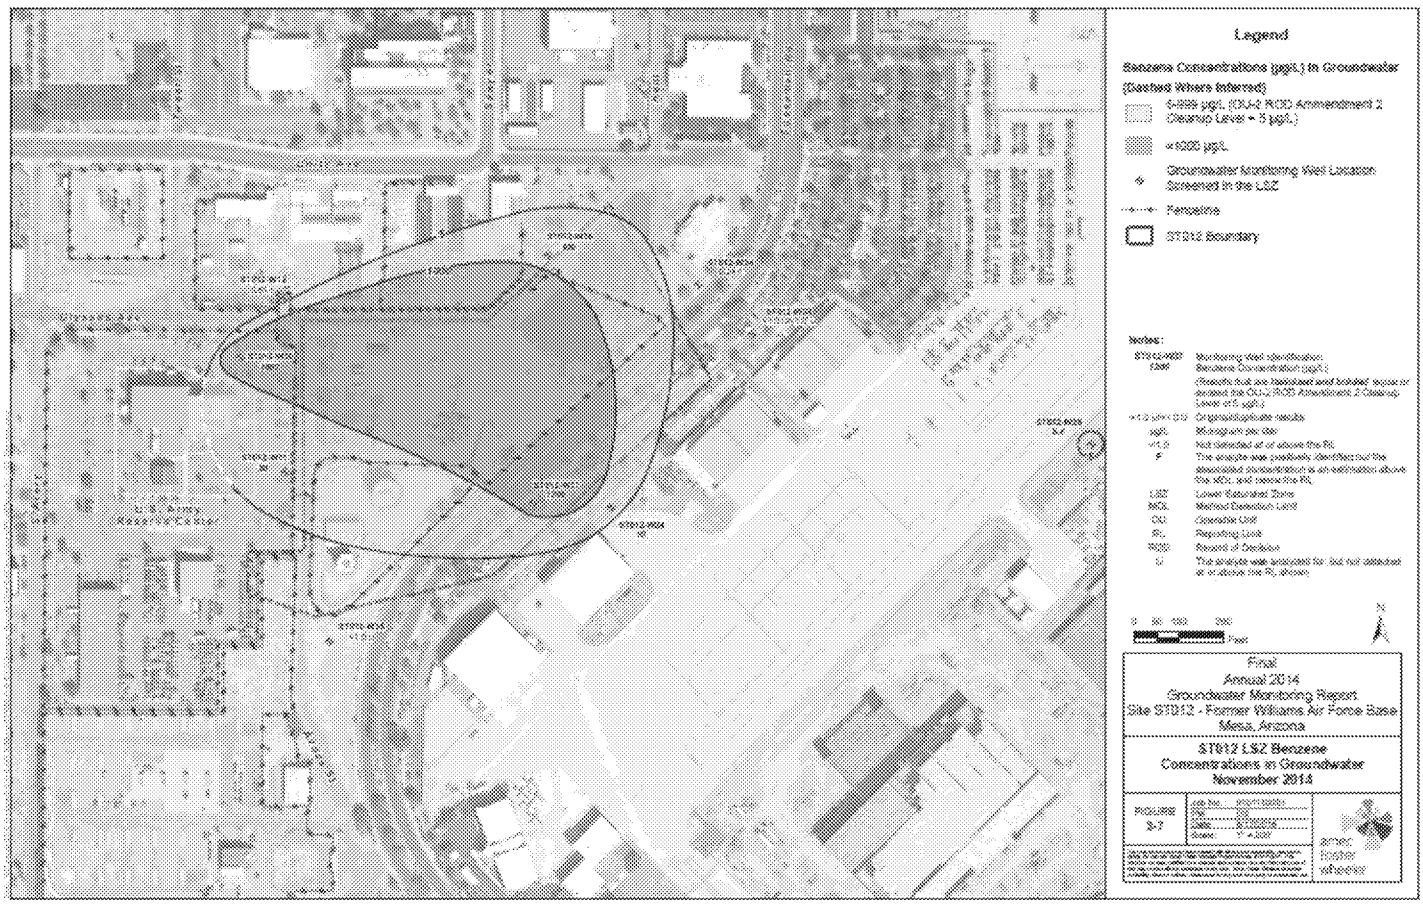

Presented at the June 2016 BCT meeting : 5000 ppb contour is very small area of the site as of Jan 2008 AF has always described the plume as "stable": Did it spread just with the rising water table, or was this an underrepresentation of the actual site conditons? This is dissolved phase benzene before TEE Pilot operation began:

LSZ Benzene Concentrations Jan 2008

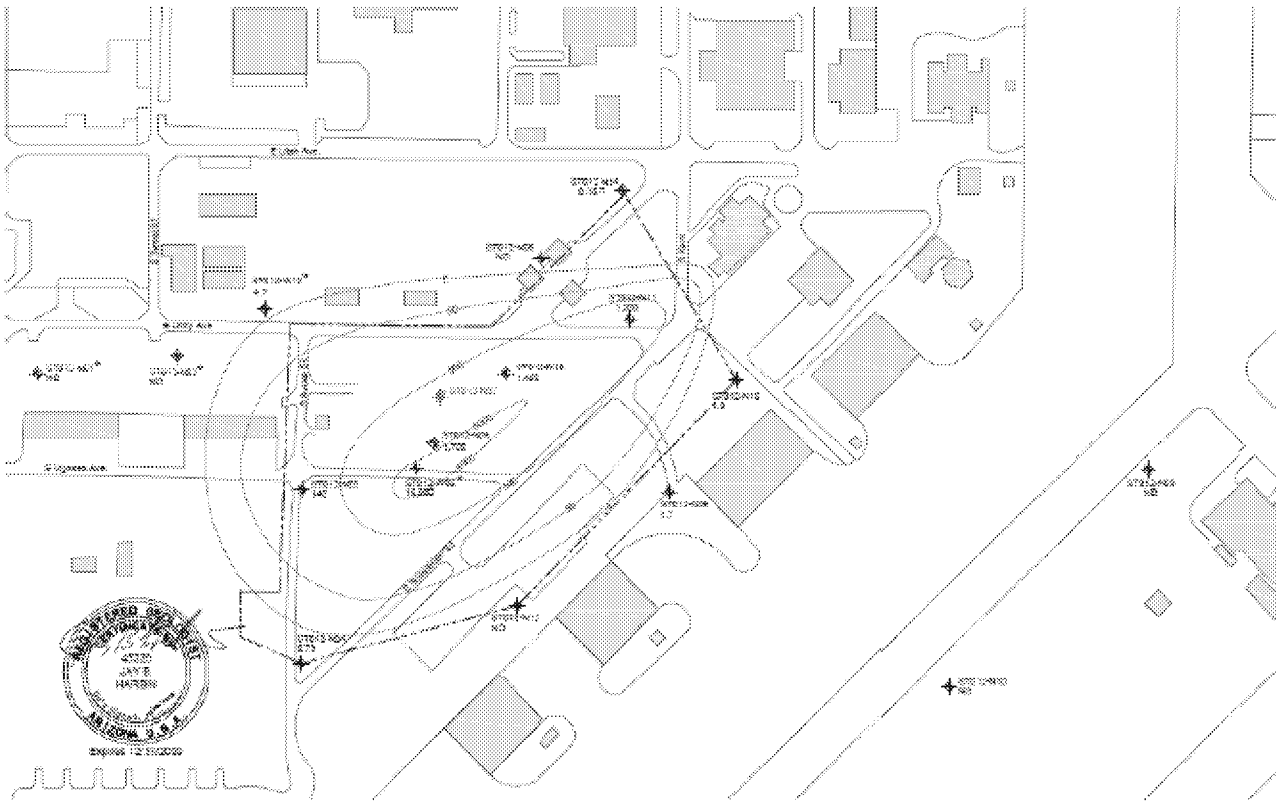

Pilot operation schedule:

Step 1: Pre Steam Groundwater/NAPL Extraction 8/11/08 - 10/28/08

Step 2: Mass Transfer Testing (LSZ) 8/26 – 10/27/08; (UWBZ) 8/28 – 8/23/09

Step 3: Steam injection (LSZ) 10/28/-1/26/08; (UWBZ) 11/10 – 2/17 2009

Step 4: Co Steam/Air Injection (LSZ) 1/26 -3/23/09 (UWBZ) 2/17 – 4/8/09 2009

Step 4: Air/ Water Injection (LSZ) 3/24- 5/20/09 (UWBZ) 4/8 -5/20/09

---

11 Weeks of pre- steam pump and treat & mass transfer tests
17 Weeks of steam injection 13 weeks in LSZ, 14 weeks in UWBZ
10 Weeks of steam and air, 8 weeks in LSZ, 7 weeks in UWBZ
10 weeks of cooling and flooding

As of Nov 2008 – beginning of steam injection for TEE pilot:

LSZ Benzene Concentrations Nov 2008

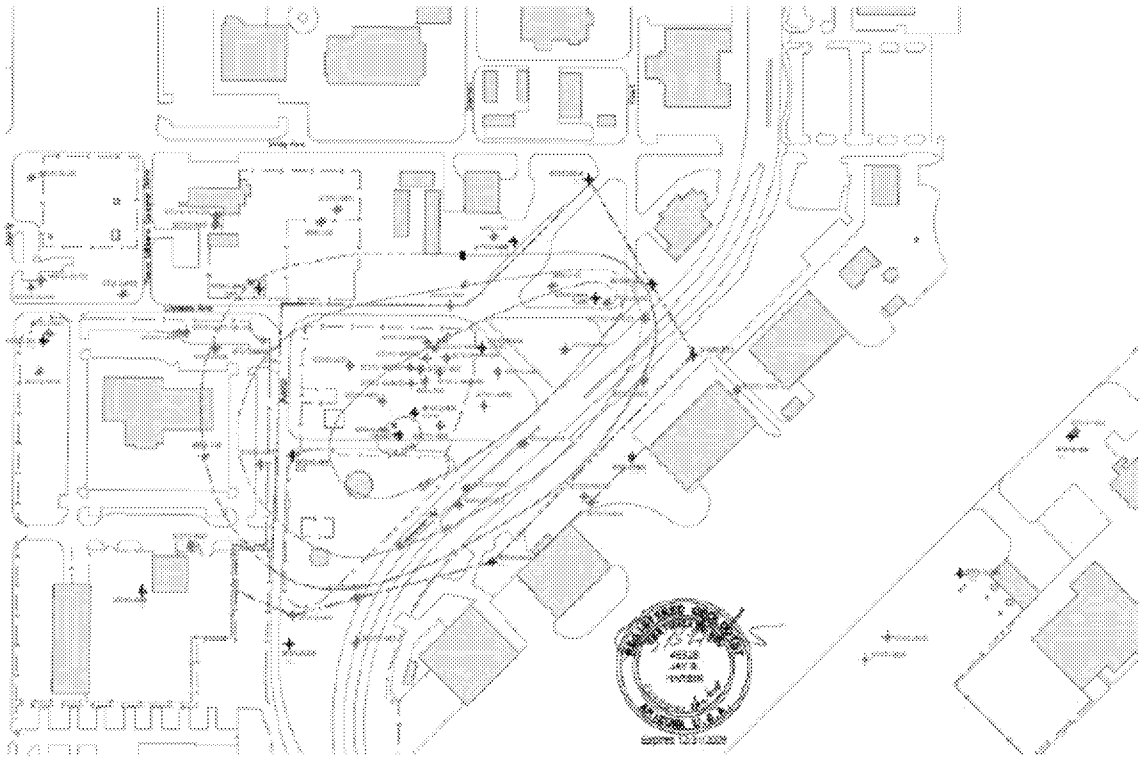

This is the beginning of steam injection into the LSZ just after startup of TEE pilot – note dramatic change in contours

LSZ Benzene Concentrations Nov 2009

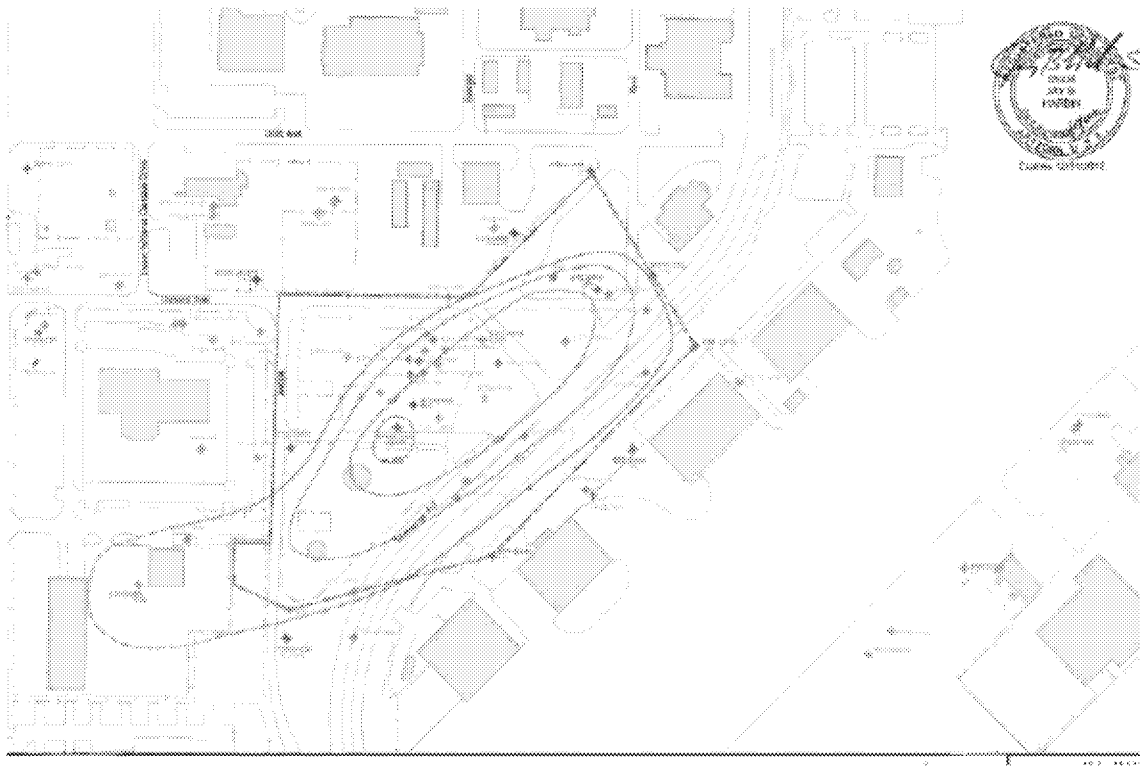

After TEE Pilot: Loss of containment was a concern during TEE because extraction pumps kept going down and werent repaired/replaced while pilot was operating; steam injection operating without full containment.

LSZ Benzene Concentrations Nov 2010

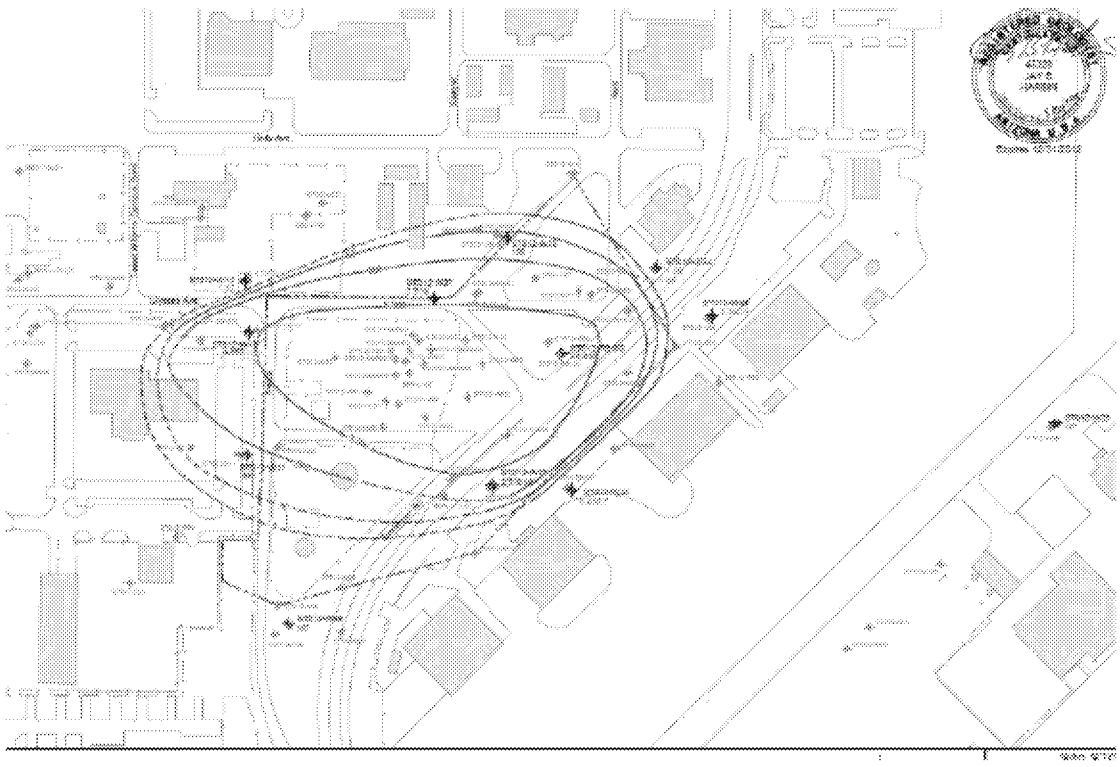

Plume continues to spread – water table now up in highly transmissve cobble zone

LSZ Benzene Concentrations Nov 2011

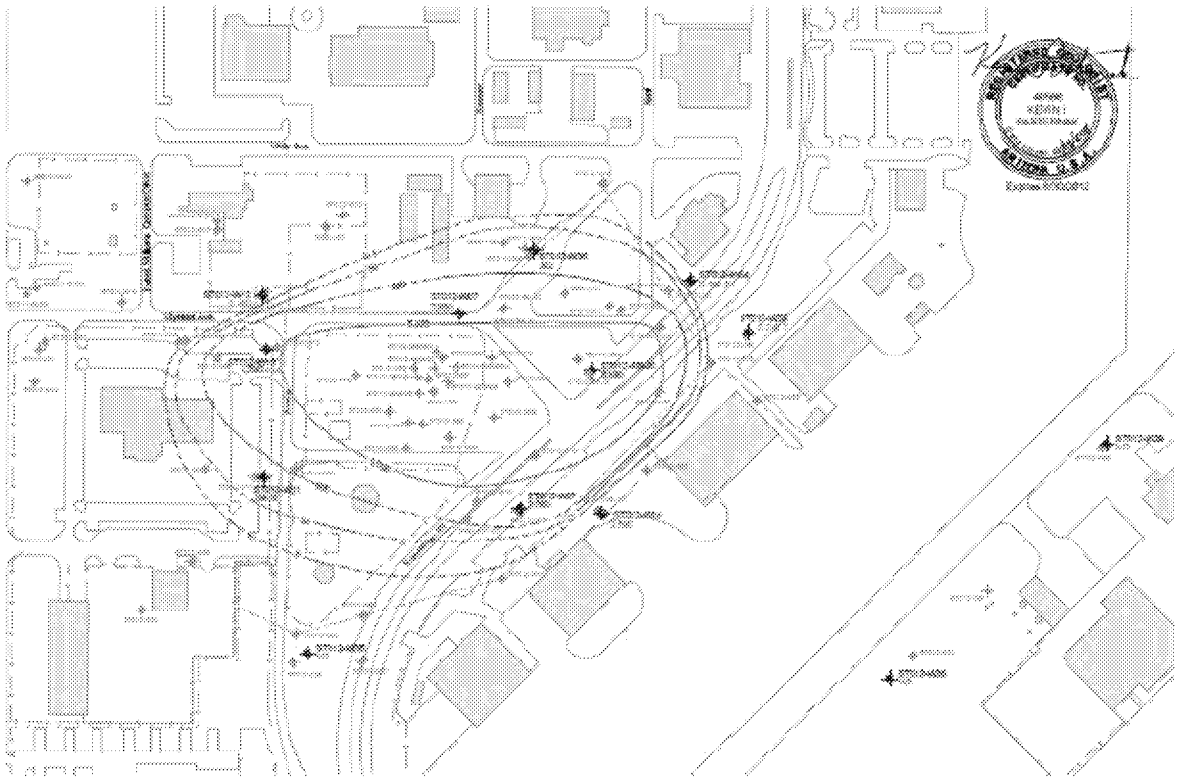

This appears to indicate that the dissolved phase benzene may have moved east of the area treated by SEE, before SEE system was designed. At this time AF was pumping TEE pilot wells for containment:

LSZ Benzene Concentrations Nov 2012

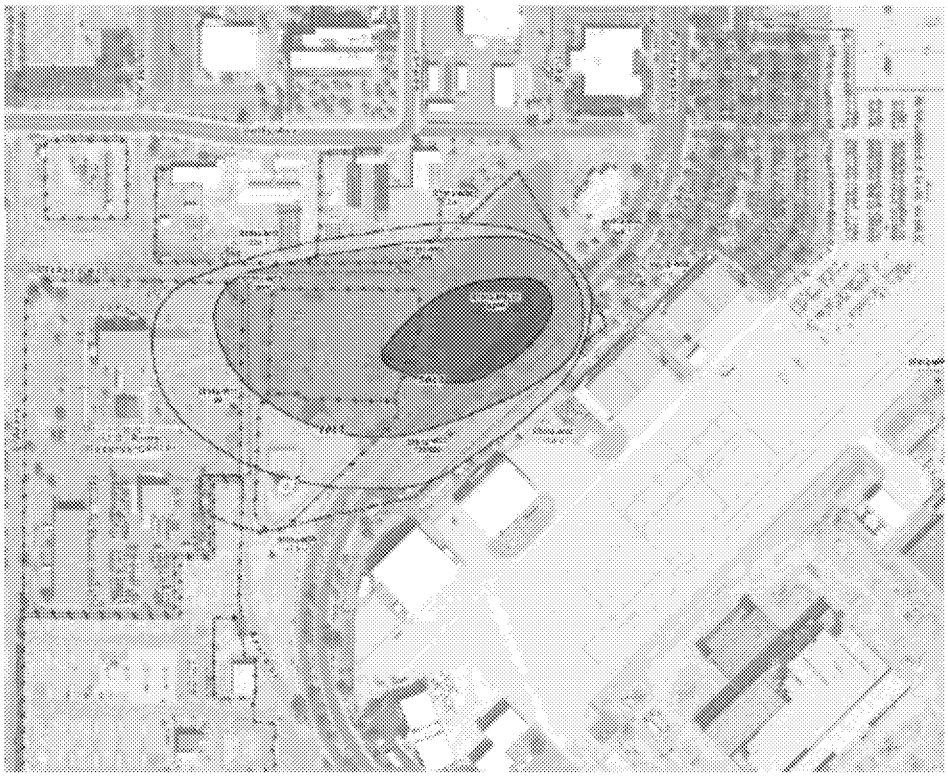

Dissolved phase Benzene as of RODA Signature: These contours are inconsistent with the figure from the RODA (first figure a the top of the page): The 5000 ppb contour below is shown in dark pink Why is dissolved phase plume smaller?

LSZ Benzene Concentrations Nov 2013

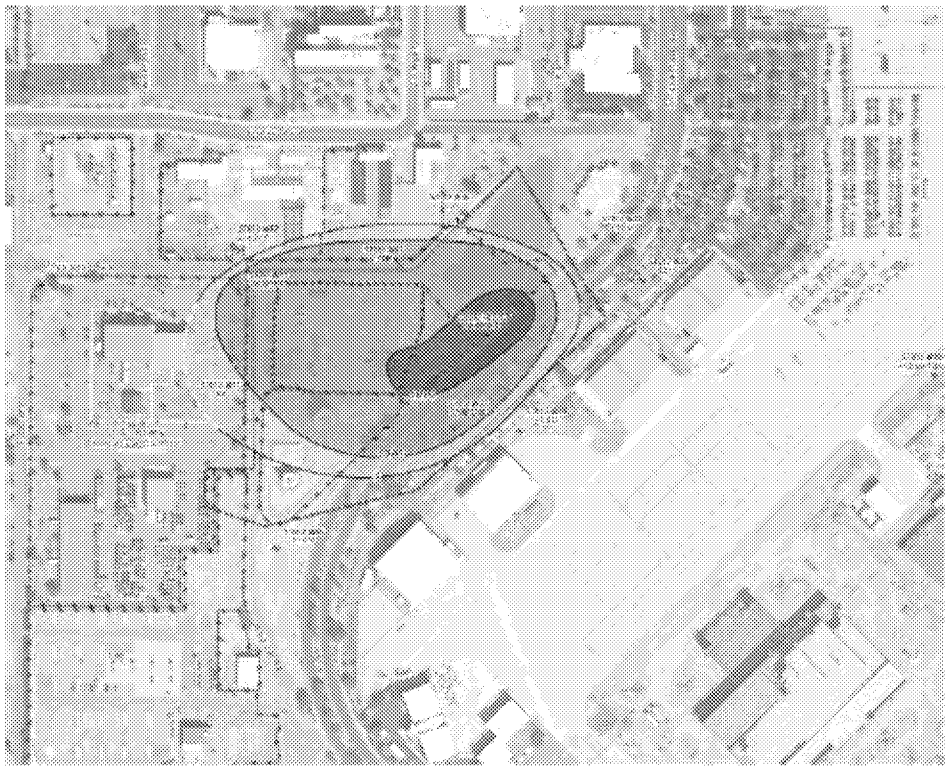

About 6 weeks after startup of SEE, site not even at steam temps yet dark pink is 1000 ppb contour line. Where did 5000 ppb contour line go?

LSZ Benzene Concentrations Nov 2014

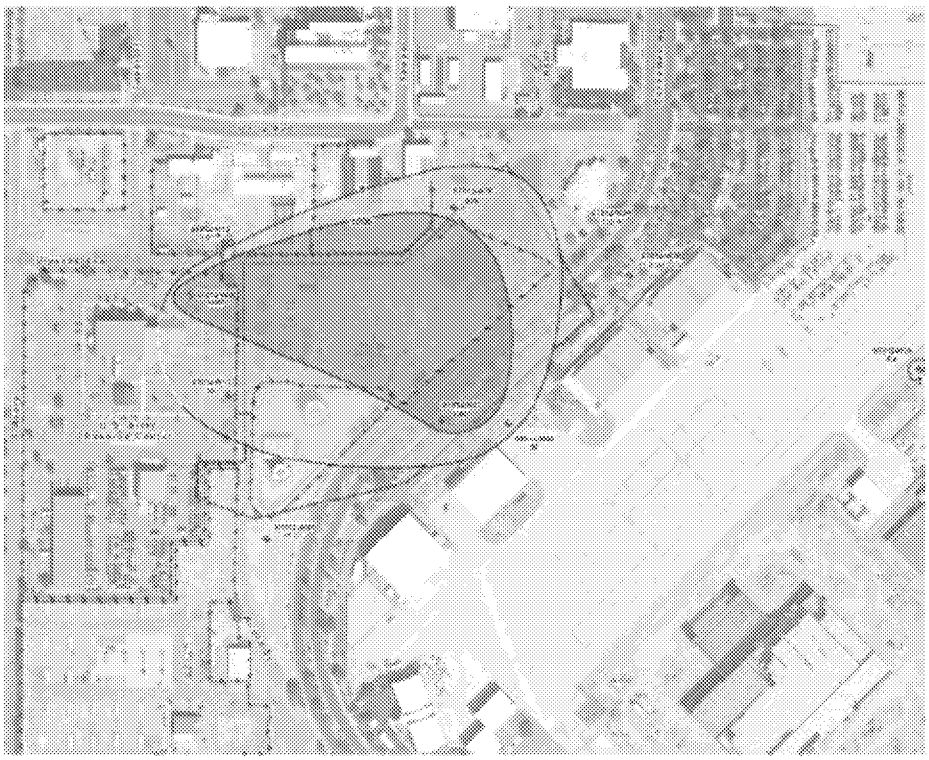

Why have dissolved benzene concentrations moved north during SEE operations ? Is this representation realistic when there is LNAPL documented as present in wells outside of these contours?

LSZ Benzene Concentrations Nov 2015

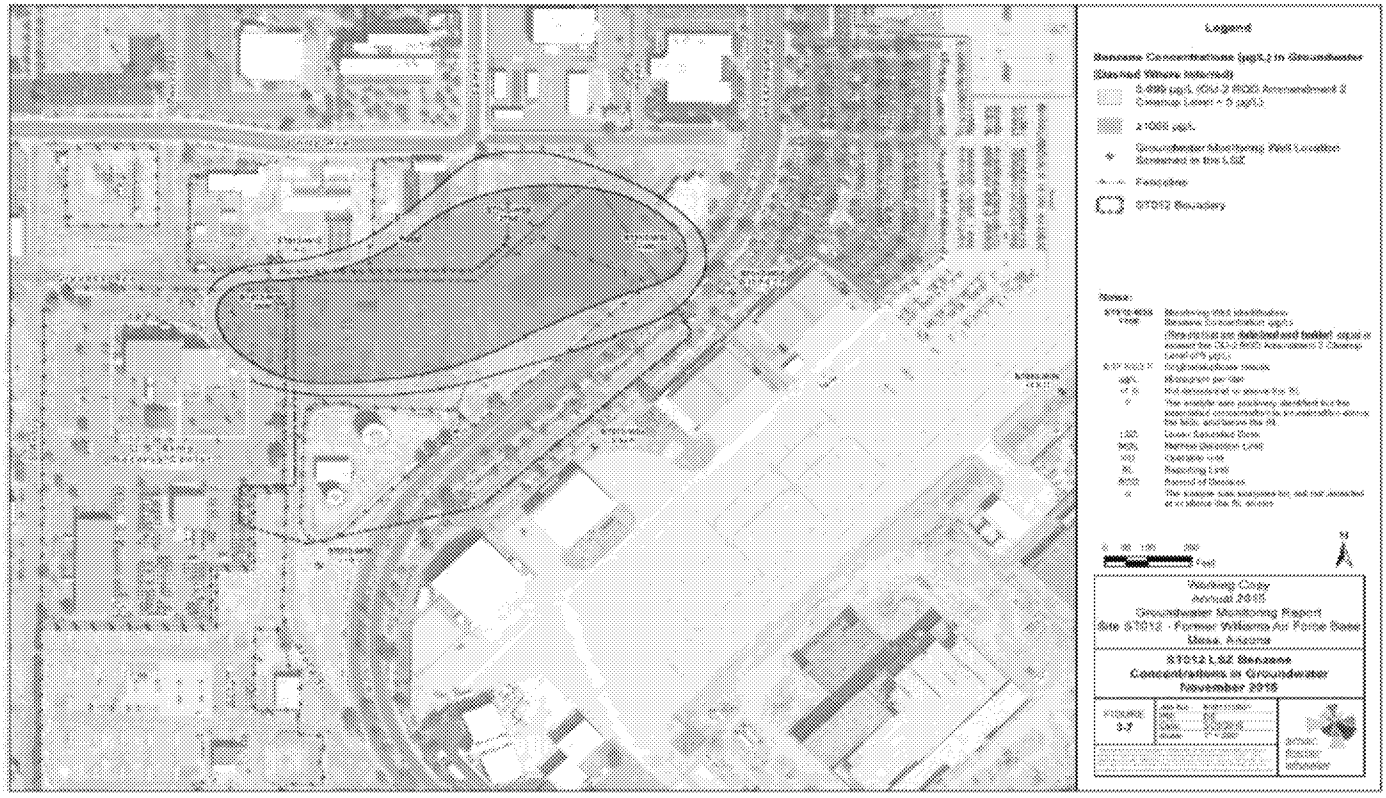

Conclusions / Questions

1) LNAPL and dissolved phase plumes are not stable, but probably moving.
2) Do these figures accurately reflect actual conditions?
3) Focus has been on the LSZ rather than the UWBZ and cobble zone, where contaminants are most likely to be mobilized off site – why isn't Amec presenting the UWBZ/ Cobble Zone data?
4) Could LNAPLor dissolved phase BTEX have been mobilized upward from the LSZ into the UWBZ/ Cobble Zone during thermal treatment?
5) Benzene concentrations between different figures range from over 10000 ppb to less than 5 ppb within the same locations over time, even in areas that were not directly treated with steam. Does this make sense?
6) Why isnt AF/Amec willing to characterize baseline conditions (extent of LNAPL and, benzene concentrations in soil cores post SEE) before initiating EBR?
7) Without knowing baseline conditions, how can milestones be established for meeting the RAO of achieving MCLs within 20 years?
8) If milestones for meeting RAOs cannot be established; do we have grounds already for declaring remedy failure?

Carolyn d'Almeida
Remedial Project Manager
Federal Facilites Branch (SFD 8-1)
US EPA Region 9
(415) 972-3150

"Because a waste is a terrible thing to mind..."

NOTICE: This e-mail (and any attachments) may contain PRIVILEGED OR CONFIDENTIAL information and is intended only for the use of the specific individual(s) to whom it is addressed. It may contain information that is privileged and confidential under state and federal law. This information may be used or disclosed only in accordance with law, and you may be subject to penalties under law for improper use or further disclosure of the information in this e-mail and its attachments. If you have received this e-mail in error, please immediately notify the person named above by reply e-mail, and then delete the original e-mail. Thank you.
