9685 Research Drive
Irvine, CA 92618

949.727.9336 PHONE
949.727.7311 FAX

www.trcsolutions.com

June 7, 2016

Ms. Maryam Tasnif-Abassi
Department of Toxic Substances Control
5796 Corporate Avenue
Cypress, California 90630

SITE: FORMER AGRICULTURAL PARK
7020 CREST AVENUE
RIVERSIDE, CALIFORNIA

RE: SOIL SAMPLING AND EXCAVATION WORK PLAN

Dear Ms. Tasnif-Abassi:

This Work Plan is provided to describe upcoming activities that will be conducted at the former Riverside Agricultural Park located at 7020 Crest Avenue in Riverside, California. Based on soil sampling efforts conducted in November 2015, as documented in the *Former Riverside Agricultural Park Soil Sampling Report* dated January 6, 2016, it was determined that surface soil with polychlorinated biphenyl (PCB) concentrations above the cleanup goal of 0.22 milligrams per kilogram (mg/kg) was present at select locations. A description of previous remediation activities and planned future work activities are presented in this Work Plan.

Phase I Activities - 2009

The scope of the first phase of soil removal was to excavate, remove, and properly dispose of soils containing PCB concentrations in excess of 50 mg/kg from locations determined by previous Site investigation efforts. In addition, soil samples were collected from select locations and analyzed for dioxins, furans and metals.

The remedial excavation alternative selected for the project included the removal, transportation, and proper disposal of PCB and metals-impacted soil. Between April and July 2009, Friends of the Riverside Airport LLC (FRA) removed soil containing PCB concentrations above 50 mg/kg. All remedial excavation activities were completed in July 2009. Excavation areas were concluded only after all confirmation samples from the excavation sidewalls and bottoms returned laboratory data results that verified the remaining soil was <50 mg/kg for PCBs.

All excavated soil with PCB concentrations at or above 50 mg/kg was transported offsite to the Waste Management, Incorporated, Kettleman Hills facility in Kettleman City, California. Soil containing PCB concentrations above 50 mg/kg at locations identified during previous Site

characterization efforts has been removed, transported offsite, and disposed of properly. A total of ~8,666 tons of PCB- and /or metals-impacted soil were transported offsite for disposal. Additional items removed from the site include brush debris (green waste), PCB-contaminated concrete, sewer pipe, and utility poles.

A total of 31 soil samples were analyzed for dioxin/furan congeners. Of the samples analyzed, 13 contained 2,3,7,8-TCDD Equivalent concentrations in excess of the health-based screening level for residential land-use (i.e., 4.5 picograms per gram [pg/g] or 4.5E-6 mg/kg). This health-based screening level represents the USEPA Regional Screening Level (RSL) established by Region IX (USEPA, 2008). The samples that contained the highest concentrations of 2,3,7,8-TCDD Eq. are TP-30E (4,817.7), TP-30S (8,372.8), and TP-30W (300.7). These three samples are co-located with PCB-impacted soil. Six additional samples exceeded the health-based screening level (B-67, TP-29, S-22+20E, TP-30N, TP-30B, and TP-103). These nine samples are co-located with PCB-impacted areas, and were removed during Phase 2 mass grading activities.

Phase II Activities – 2013/2014

The scope of the second phase of soil removal was to excavate, remove, and properly dispose of soils containing PCB concentrations in excess of 0.22 mg/kg from locations determined by previous site investigation efforts. In addition, soil samples were collected from select locations and analyzed for dioxins, furans and metals.

Between July 2013 and January 2014, FRA removed soil containing PCB concentrations above 0.22 mg/kg. Excavation areas were concluded only after all confirmation samples from the excavation sidewalls and bottoms returned laboratory data results that verified the remaining soil was <0.22 mg/kg for PCBs.

PCB-impacted soil (165,226.64 tons) generated during excavation activities was characterized as a non-hazardous waste and transported to the Waste Management, Inc. Azusa Land Reclamation facility in Azusa, California, for recycling. Additional materials that were removed from the Site included clean soil (30,782 tons), concrete (4,481.37 tons), green waste (422.26 tons), and asbestos-cement pipe (50.82 tons).

Thirteen dioxin/furan-impacted locations identified during Phase 1 activities were addressed by conducting additional excavation and confirmation sampling. Of the 50 confirmation samples collected, 17 were above the health-based screening level (4.5 pg/g). Consequently, additional soil was removed from these locations and more confirmation samples were collected. This procedure was repeated until all final confirmation sample results were below 4.5 pg/g.

Planned Remediation Activities for 2016

Work activities will begin following approval of this work plan by DTSC and EPA and are anticipated to take place over a two to three month period. The work will be conducted based on four distinct types of areas or phases as described below:

- Cut Lots - lots where soil was removed to achieve the final grade in Tract 28987;
- Fill Lots - lots where soil was imported and compacted to achieve the final grade in Tract 28987;
- Outside Areas - areas outside of the planned Phase I housing development; and
- Final Lot Sampling - final confirmation soil sampling of all lots in Tract 28987 (Phase I) housing development.

Soil sampling and removal activities for each of these areas will proceed in the following manner:

Cut Lots

- Collect step-out soil samples in four directions at 25 feet and 50 feet from sample location exceeding PCB cleanup goal. Collect samples prior to soil removal. See Figure 1 for proposed sample locations.
- Remove soil around sample location exceeding cleanup goal to 1 foot deep and out to step-out sample limits (minimum 50 foot by 50 foot square excavation). Do not excavate within 2 feet of existing concrete curbs and gutters or driveway aprons on Jurupa Avenue, Clemente Court, and Drysdale Street. Leave curbs, gutters, and driveway aprons in place.
- Collect one bottom sample per 1,000 square feet with a minimum of three samples per removal area.
- Continue step-out sampling an additional 10 feet until results are below cleanup goal (0.22 mg/kg).
- Dispose of excavated soil offsite.

Fill Lots

- Collect step-out soil samples in four directions at 60 feet from sample location exceeding PCB cleanup goal. Collect samples prior to soil removal. See Figure 2 for proposed sample locations.
- Remove soil around sample location exceeding cleanup goal to 1 foot deep and out to step-out sample limits (minimum 120 foot by 120 foot square excavation). Do not excavate within 2 feet of existing concrete curbs and gutters or driveway aprons on Jurupa Avenue, Clemente Court, and Drysdale Street. Leave curbs, gutters, and driveway aprons in place.

- Collect one bottom sample per 1,000 square feet with a minimum of three samples per removal area.
- Continue step-out sampling an additional 10 feet until results are below cleanup goal.
- Dispose of excavated soil offsite.

Outside Areas

- Re-sample the outside areas on a 62.5 foot grid. If a historic result is within 2 feet of the grid point and is below the cleanup goal then no sample required. See Figure 3 for proposed sample locations.
- Collect step-out soil samples in four directions at 25 and 50 feet from sample location exceeding PCB cleanup goal. Collect samples prior to soil removal.
- Remove soil around sample location exceeding cleanup goal to 1 foot deep and out to step-out sample limits (minimum 50 foot by 50 foot square excavation).
- Collect one bottom sample per 1,000 square feet with a minimum of three samples per removal area.
- Continue step-out sampling an additional 10 feet until results are below cleanup goal.
- Dispose of excavated soil offsite.
- Note: a minimum of 5 feet of clean fill will be imported and placed over all lots included in the future Phase II development area which is still in the planning phase.

Tract 28987 Final Lot Sampling - See Figure 4 for proposed sample locations.

- For small lots, as defined in Table 1, collect 6 samples per lot (2 front yard, 2 side yard, and 2 back yard. Soil samples will not be collected in the location of a planned house.
- For large lots, as defined in Table 1, collect 8 samples per lot (2 front yard, 4 side yard, and 2 back yard. Soil samples will not be collected in the location of a planned house.
- For cut lots, collect only surface samples (0-6 inches).
- For fill lots, collect surface samples, two foot deep samples, and for fill 8 feet or deeper, 50% of the depth of the fill (not including concrete fill material).
- For all lots, if any result exceeds the cleanup goal, remove soil in the area 2 feet deep and laterally to adjacent sample location meeting the cleanup goal, then resample.
- Continue removing and sampling until results are below cleanup goal.
- Dispose of excavated soil offsite.

Backfilling

Excavations created during these additional remediation activities will be backfilled and compacted. The import soil will come from a stockpile located south of Jurupa Avenue near the intersection of Jurupa Avenue and Van Buren Boulevard approximately 0.4 mile east of the site. This stockpile has been previously tested and meets the DTSC criteria for import fill soil. However, the soil will be resampled in accordance with DTSC import sampling criteria (12 samples for the first 5,000 cubic yards, then 1 sample for every 1,000 cubic yards thereafter) and the analytical results will be provided to DTSC for approval prior to beginning backfill activities.

Underground Utility Excavation

Excavated soil from underground utility excavations in street areas for water, sewer, storm drain, telephone, gas, electric, and cable television will be stockpiled, tested, and then disposed of offsite at one of the soil disposal facilities listed below. The utility trenches will be backfilled with clean imported material. This work will be conducted after receipt of the certificate of completion from DTSC.

Offsite Soil Disposal

- The proposed soil disposal facilities for soil containing PCBs below 50 mg/kg include the following:
    - Waste Management, Incorporated (WMI) facility at 2801 Madera Road, Simi Valley, California.
    - WMI Azusa Land Reclamation facility at 1211 W. Gladstone Street, Azusa, California.
    - WMI El Sobrante Landfill at 10910 Dawson Canyon Road, Corona, California.
- The proposed soil disposal facility for soil containing PCBs at or above 50 mg/kg is the Waste Management facility at 35251 Old Skyline Road, Kettleman City, California.
- Proposed haul route maps are provided as Figures 5 and 6.

Laboratory Analysis

The soil samples collected during confirmation sampling will be analyzed for PCBs using EPA Method 8082 with extraction by the Soxhlet method. The contract laboratory for this sampling effort will be Test America in Irvine, California. Chain of custody protocol will be followed for all samples. The chain of custody form accompanies the samples from the sampling locality to the laboratory, providing a continuous record of possession prior to analysis.

Air Monitoring

Air monitoring will be performed during soil excavation activities according to Appendix E (Workplan for Air Monitoring) of the Frey Environmental *Revised Response Plan* dated June 19, 2006, and the TRC *Air Monitoring Plan Addendum* dated June 7, 2016 (Appendix A).

Cleanup Goal

In accordance with the Response Plan that was approved by DTSC in 2006, all known PCBs found above the original cleanup level of 0.22 mg/kg in the November 2015 sampling event will be removed during this remediation. The 0.22 mg/kg used throughout the project is a conservative cleanup goal and lower than the level of 1 mg/kg, which EPA and DTSC considers health protective in a residential setting and falls within both agencies' acceptable risk range.

Confirmation samples will be collected during and after soil removal to ensure that the site is suitable for residential development, including sampling of each residential lot with up to eight sample locations. While it is possible that individual residual concentrations above 0.22 mg/kg may be found after the cleanup, the site will still be safe for residential use if the 95% upper confidence limit (UCL) concentrations for individual lots meet the cleanup goal of 0.22 mg/kg. A post-remediation risk evaluation will be developed in such cases for approval by DTSC.

Soil sampling results for samples collected after the initial drafting of this work plan are provided in Appendix B.

Reporting

Following the completion of excavation activities, a summary report will be prepared.

- The report will include findings, tabulated laboratory results, sample location figures, and copies of manifests.
- A post-removal health risk analysis will be included in the report.

General

TRC will provide field oversight of excavation activities and will perform confirmation soil sampling.

A site-specific health and safety plan will be prepared by TRC and will be available at the site for use by TRC personnel and agency representatives.

The sampling requirements described in this Work Plan can be modified in the field by the DTSC or EPA if necessary to meet project objectives.

If you have any comments, please contact David Lennon at (949) 341-7458.

Sincerely,

David Lennon
Principal Consultant

Ross Surrency, PG
Senior Project Geologist

Attachments: Figure 1 - Proposed Soil Sample Locations for Cut Lots
Figure 2 - Proposed Soil Sample Locations for Fill Lots
Figure 3 - Proposed Soil Sample Locations for Outside Areas
Figure 4 - Proposed Soil Sample Locations for Final Lot Sampling
Figure 5 - Soil Transportation Route to Van Buren Boulevard
Figure 6 - Soil Transportation Route from Van Buren Boulevard to Highway 60
Table 1 - Individual Lot Information
Appendix A – Air Monitoring Plan Addendum
Appendix B – Soil Sampling Memorandum (with laboratory data provided on a CD)

cc: Sara Ziff, EPA (electronic copy)
Katherine Baylor, EPA (electronic copy)
Greg Neal, DTSC (electronic copy)

LEGEND

- Proposed Soil Sample Locations
- 1732 0.18 — PCB Sample Location (Total PCBs < 0.22 mg/kg)
- 1731 131 — PCB Sample Location (Total PCBs ≥ 0.22 mg/kg)
- Cut Lots (39 total)
- Fill Lots (70 total)



NOTES:

PCB concentrations shown represent the highest value from the two different laboratory extraction methods (Soxhlet and Method 3545).

N

REV	DATE	BY	APP	DESCRIPTION	DATE	CHECKED	DATE
				DRAFT - ISSUED FOR REVIEW			
03/21/2016					12/17/15	R.S.	12/17/15
DESIGNED	DATE	DRAWN BY	DATE				
R.S.	12/17/15	R.M.C.	12/17/15				

TRC
□□5 RESEAR□□ DRIVE
IRVINE□CALIFORNIA □□□

PROJECT: □□□□□□□□□□□□□□□□
FACILITY: FORMER AGRICULTURAL PAR□
□□□□□REST AVENUE
RIVERSIDE□CALIFORNIA

TITLE:
PROPOSED SOIL SAMPLE LO□ATIONS FOR □UT LOTS

FILE NAME: FRA RIVERSIDE-SP-REV2015.dwg
REVISION: □
DATE: 03/21/2016
Page 1 of 4
SHEET: 1

LEGEND

- Proposed Soil Sample Locations
- 1732 0.18 PCB Sample Location (Total PCBs < 0.22 mg/kg)
- 1731 131 PCB Sample Location (Total PCBs ≥ 0.22 mg/kg)
- Cut Lots (39 total)
- Fill Lots (70 total)



NOTES:

PCB concentrations shown represent the highest value from the two different laboratory extraction methods (Soxhlet and Method 3545).

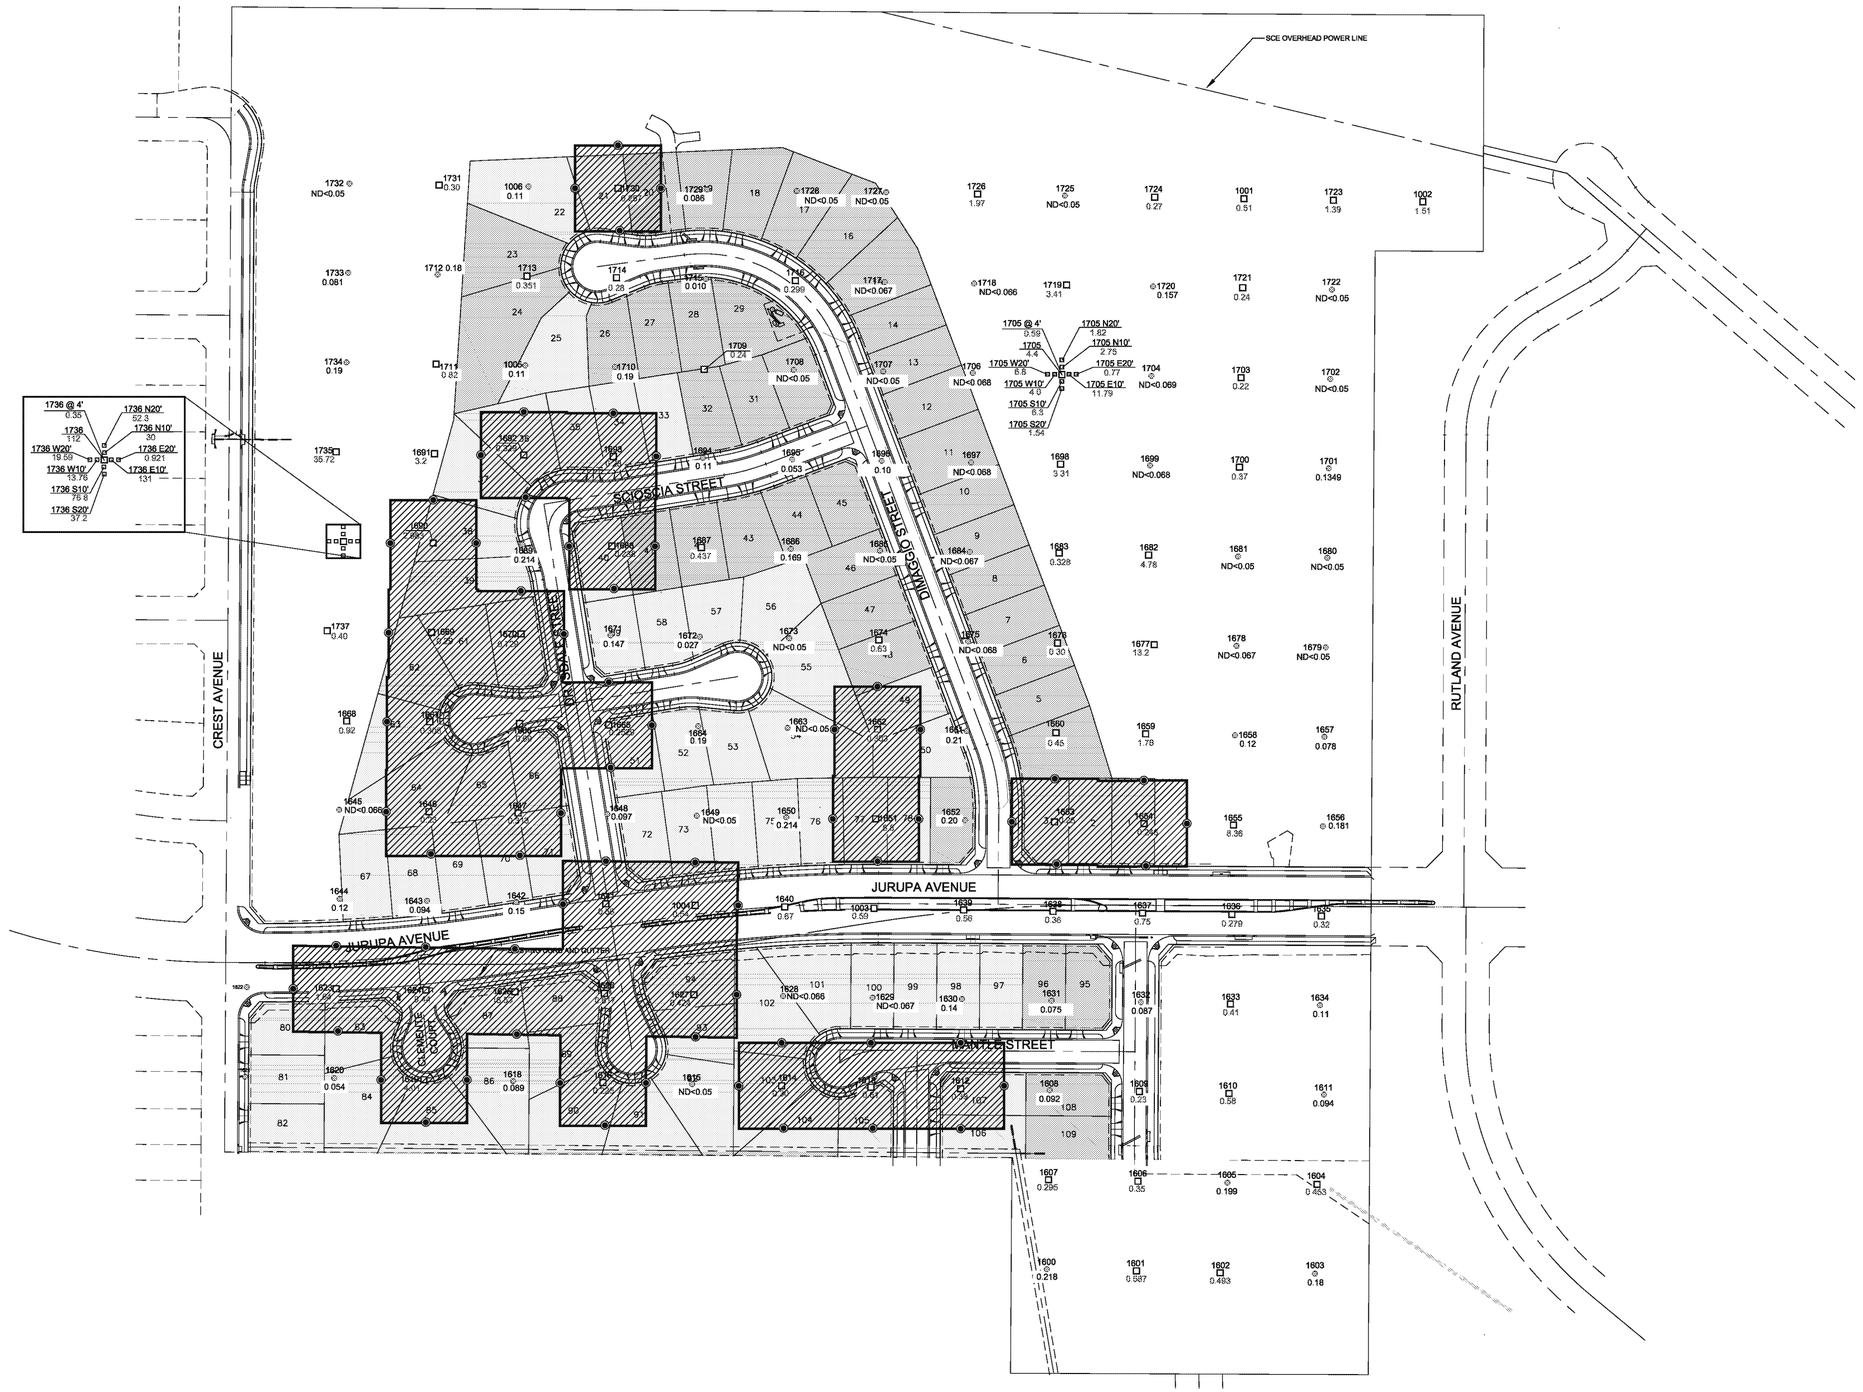

N

SCALE (FEET)
0 100 200
1" = 100'

DRAFT- ISSUED FOR REVIEW

REV	DATE	BY	APP	DESCRIPTION
	03/21/2016			

DESIGNED	DATE	DRAWN BY	DATE	CHECKED	DATE
R.S.	12/17/15	R.M.C.	12/17/15	R.S.	12/17/15

TRC
5 RESEARCH DRIVE
IRVINE, CALIFORNIA

PROJECT:
FACILITY: FORMER AGRICULTURAL PARK
CREST AVENUE
RIVERSIDE, CALIFORNIA

TITLE:
PROPOSED SOIL SAMPLE LOCATIONS FOR FILL LOTS

FILE NAME: FRA RIVERSIDE-SP-REV2016.dwg
REVISION:
SHEET: 2
DATE: 03/21/2016
Page 2 of 4

L:\Graphics\Projects\Ivanhoe\Riverside-FRA\CADD\FRA RIVERSIDE-SP-Phase-rev.dwg Mar 21, 2016 - 11:02am rcollins

LEGEND

- Proposed Soil Sample Locations (New 62.5 Grid)
- 1732 0.18 PCB Sample Location (Total PCBs < 0.22 mg/kg)
- 1731 131 PCB Sample Location (Total PCBs ≥ 0.22 mg/kg)
- Cut Lots (39 total)
- Fill Lots (70 total)

50' 50' INITIAL EXCAVATION AREA

NOTES:

PCB concentrations shown represent the highest value from the two different laboratory extraction methods (Soxhlet and Method 3545).

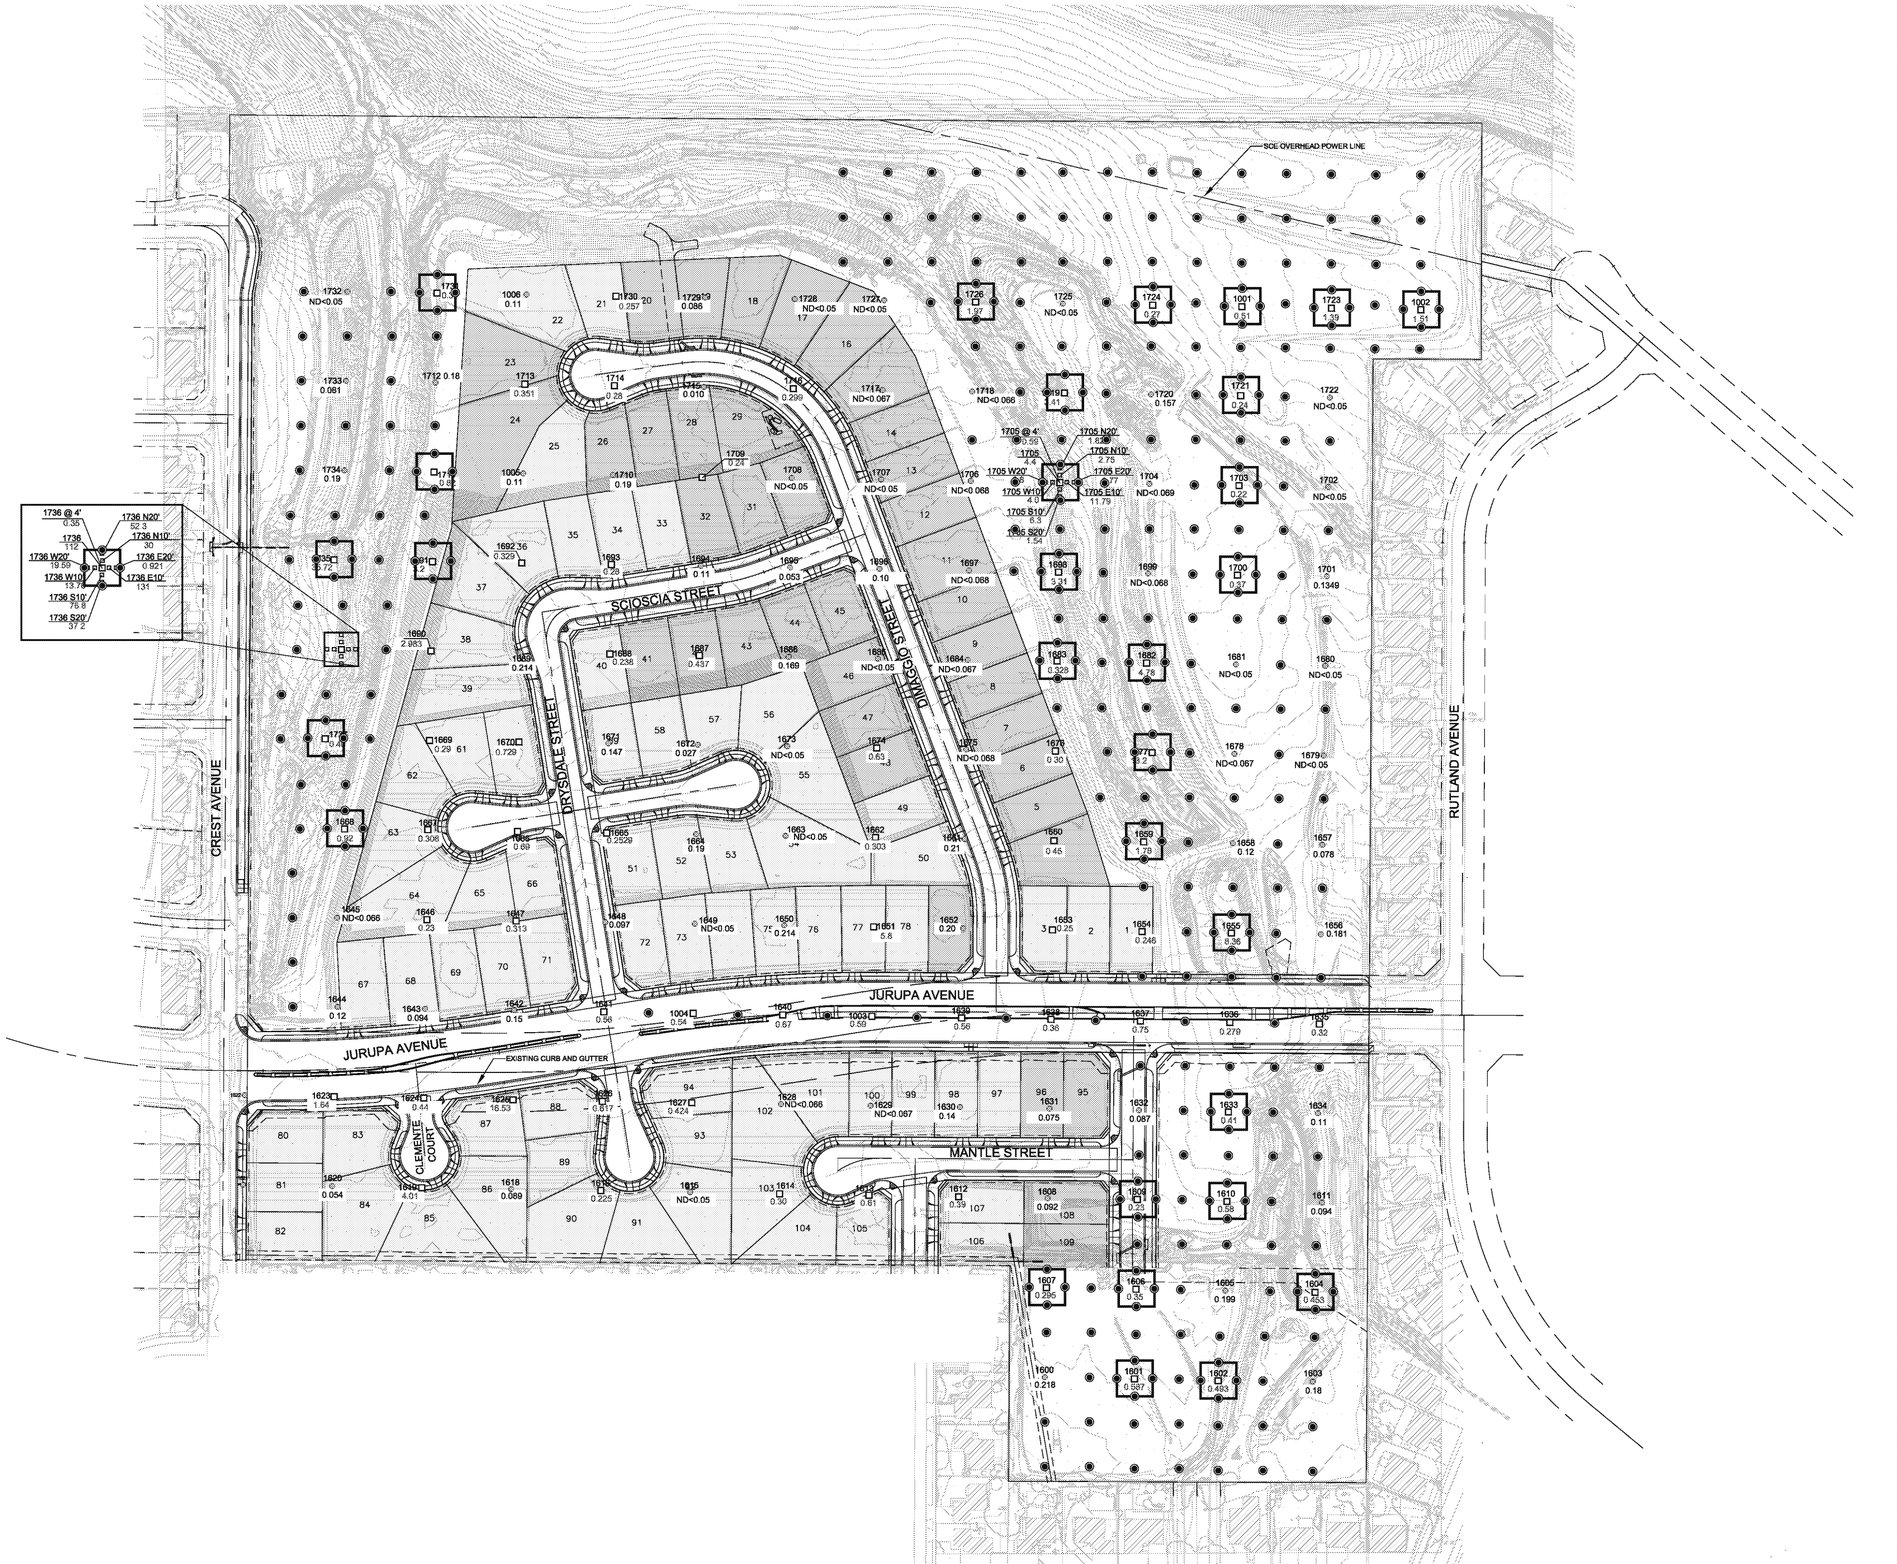

N

REV	DATE	BY	APP	DESCRIPTION
03/21/2016				DRAFT - ISSUED FOR REVIEW

DESIGNED	DATE	DRAWN BY	DATE	CHECKED	DATE
R.S.	12/17/15	R.M.C.	12/17/15	R.S.	12/17/15

TRC
5 RESEARCH DRIVE
IRVINE, CALIFORNIA

PROJECT:
FACILITY: FORMER AGRICULTURAL PARK
CREST AVENUE
RIVERSIDE, CALIFORNIA

TITLE: PROPOSED SOIL SAMPLE LOCATIONS FOR OUTSIDE AREAS

FILE NAME: FRA RIVERSIDE-SP-REV2016.dwg
REVISION:
DATE: 03/21/2016
Page 3 of 4
SHEET: 3

L:\Graphics\Projects\ByName\Riverside-FRA\CADD\FRA RIVERSIDE-SP-Phase-rev.dwg Mar 21, 2016 - 11:03am rcollins

ED_005263_00003397-00010

LEGEND

● Proposed Soil Sample Locations

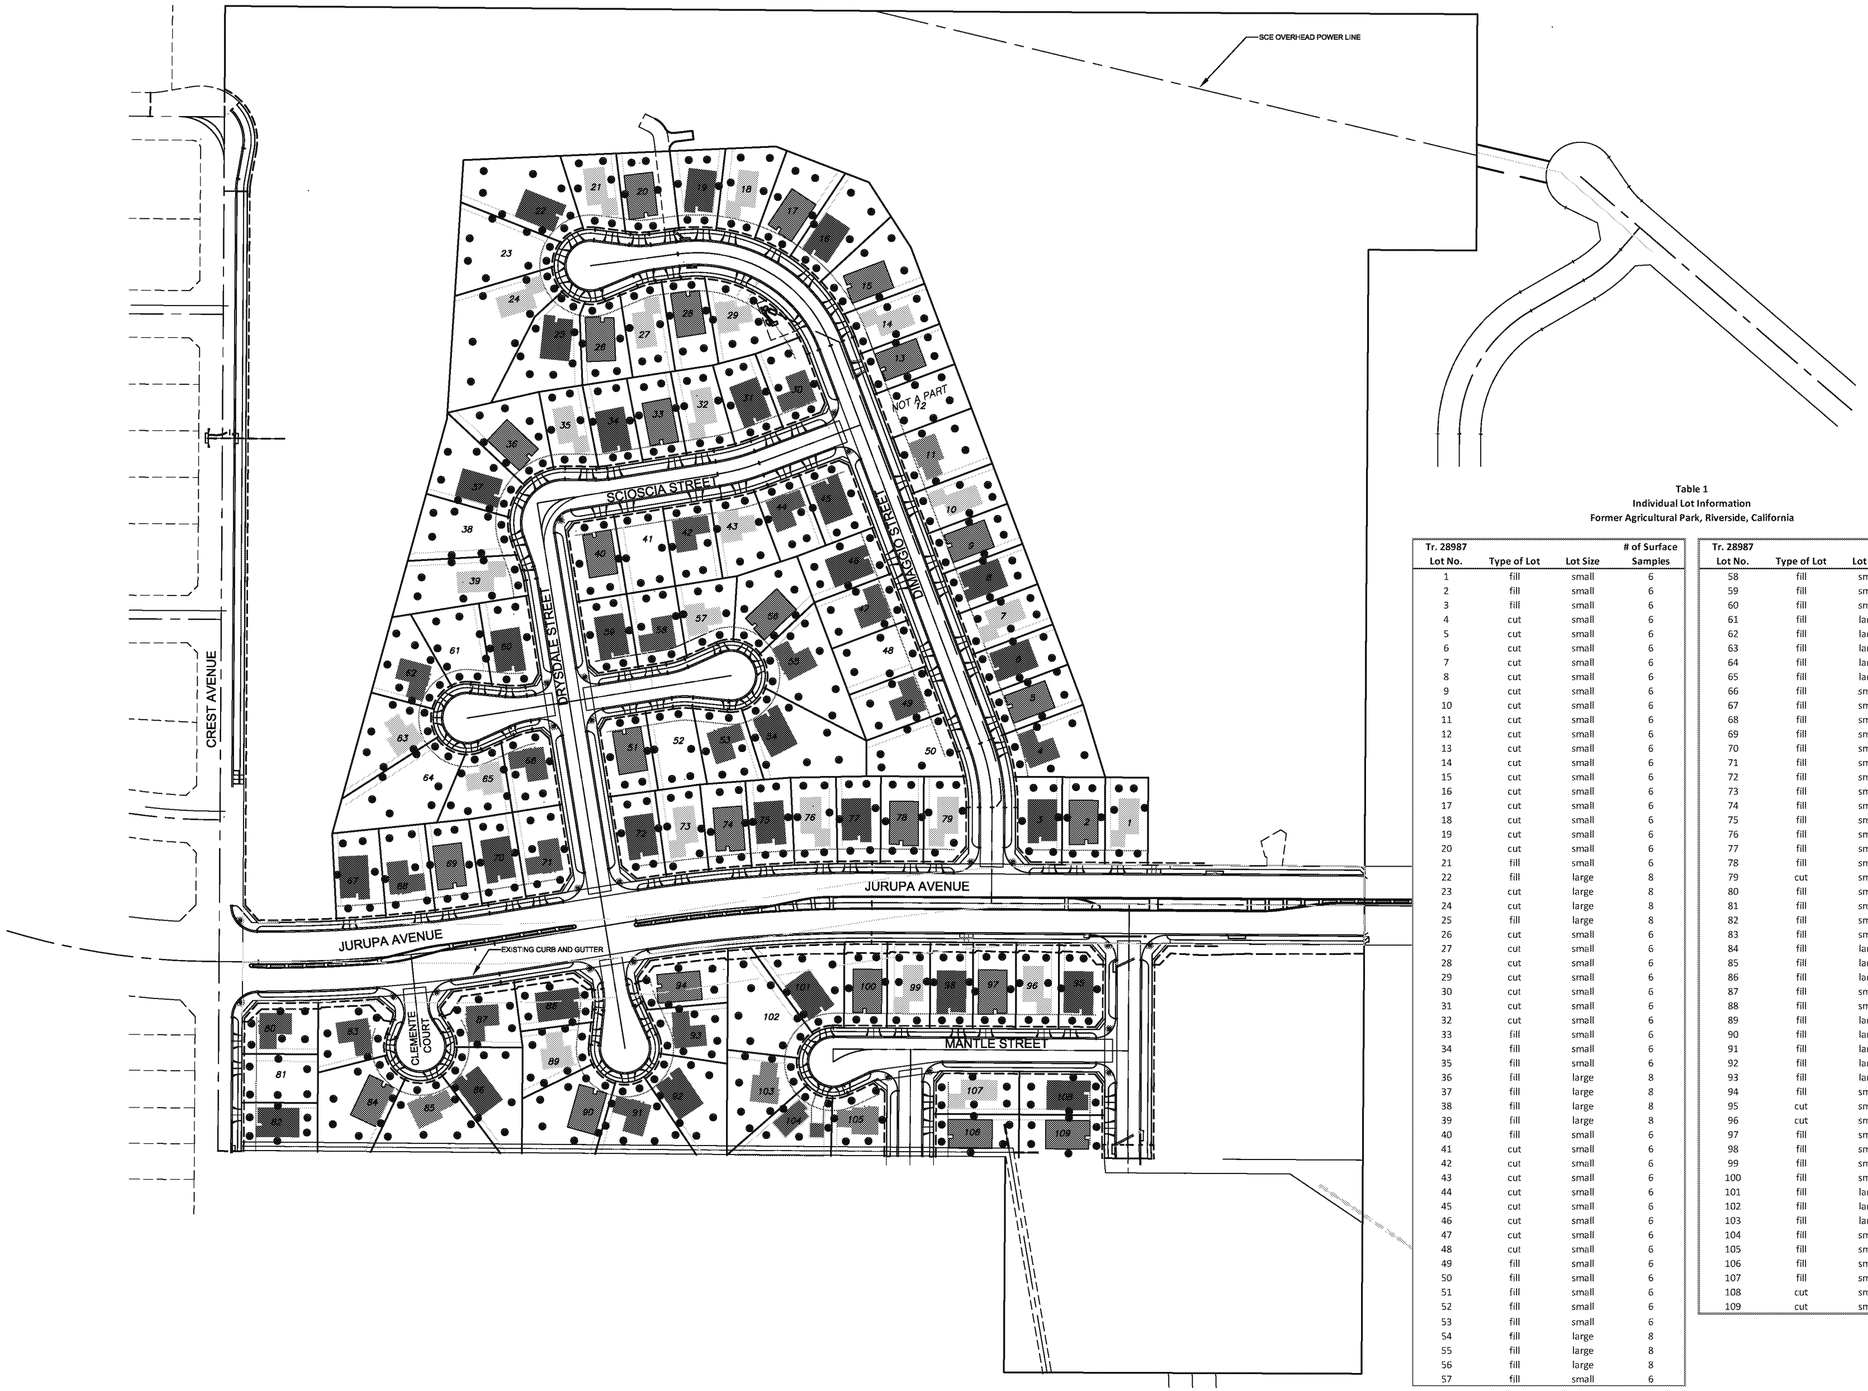

Table 1
Individual Lot Information
Former Agricultural Park, Riverside, California

Tr. 28987 Lot No.	Type of Lot	Lot Size	# of Surface Samples
1	fill	small	6
2	fill	small	6
3	fill	small	6
4	cut	small	6
5	cut	small	6
6	cut	small	6
7	cut	small	6
8	cut	small	6
9	cut	small	6
10	cut	small	6
11	cut	small	6
12	cut	small	6
13	cut	small	6
14	cut	small	6
15	cut	small	6
16	cut	small	6
17	cut	small	6
18	cut	small	6
19	cut	small	6
20	cut	small	6
21	fill	small	6
22	fill	large	8
23	cut	large	8
24	cut	large	8
25	fill	large	8
26	cut	small	6
27	cut	small	6
28	cut	small	6
29	cut	small	6
30	cut	small	6
31	cut	small	6
32	cut	small	6
33	fill	small	6
34	fill	small	6
35	fill	small	6
36	fill	large	8
37	fill	large	8
38	fill	large	8
39	fill	large	8
40	fill	small	6
41	cut	small	6
42	cut	small	6
43	cut	small	6
44	cut	small	6
45	cut	small	6
46	cut	small	6
47	cut	small	6
48	cut	small	6
49	fill	small	6
50	fill	small	6
51	fill	small	6
52	fill	small	6
53	fill	small	6
54	fill	large	8
55	fill	large	8
56	fill	large	8
57	fill	small	6

Tr. 28987 Lot No.	Type of Lot	Lot Size	# of Surface Samples
58	fill	small	6
59	fill	small	6
60	fill	small	6
61	fill	large	8
62	fill	large	8
63	fill	large	8
64	fill	large	8
65	fill	large	8
66	fill	small	6
67	fill	small	6
68	fill	small	6
69	fill	small	6
70	fill	small	6
71	fill	small	6
72	fill	small	6
73	fill	small	6
74	fill	small	6
75	fill	small	6
76	fill	small	6
77	fill	small	6
78	fill	small	6
79	cut	small	6
80	fill	small	6
81	fill	small	6
82	fill	small	6
83	fill	small	6
84	fill	large	8
85	fill	large	8
86	fill	large	8
87	fill	small	6
88	fill	small	6
89	fill	large	8
90	fill	large	8
91	fill	large	8
92	fill	large	8
93	fill	large	8
94	fill	small	6
95	cut	small	6
96	cut	small	6
97	fill	small	6
98	fill	small	6
99	fill	small	6
100	fill	small	6
101	fill	large	8
102	fill	large	8
103	fill	large	8
104	fill	small	6
105	fill	small	6
106	fill	small	6
107	fill	small	6
108	cut	small	6
109	cut	small	6

N

REV	DATE	BY	APP	DESCRIPTION	DATE	CHECKED	DATE
				DRAFT - ISSUED FOR REVIEW			
DES'GNED	03/21/2016	DATE	DRAWN BY	DATE	CHECKED	DATE	
R.S.		12/17/15	R.M.C.	12/17/15	R.S.	12/17/15	

TRC
□□15 RESEAR□□DRIVE
IRVINE□CALIFORNIA □□□

PROJECT: □□□□□□□□□□□□□□□□
FACILITY: FORMER AGRI□ULTURAL PAR□
□□□□□REST AVENUE
RIVERSIDE□CALIFORNIA

TITLE:
PROPOSED SOIL SAMPLE LO□ATIONS FOR FINAL LOT SAMPLING

FILE NAME: FRA RIVERSIDE-SP-REV2016.dwg
REV'S ON: □
DATE: 03/21/2016
Page 4 of 4
SHEET: 4

\\Graphics\Projects\Hamel\Riverside-FRA\CADD\FRA RIVERSIDE-SP-Phase - rev.dwg, Mar 21, 2016 - 11:04am rcollins

MS=1:1 L:\Graphics\ProjectsbyName\Riverside-FRA\CADD\FRA_Routes-6-2016.dwg Jun 07, 2016 - 2:25pm rcollins

LEGEND

Soil Transportation Route

SCALE (FEET)

0 500

NOTE:

Map provided by Google Earth Professional, dated 2/9/2016.

TRC

PROJECT: 167991

FACILITY:

FRIENDS OF THE RIVERSIDE AIRPORT, LLC
7020 CREST AVENUE
RIVERSIDE, CALIFORNIA

SOIL TRANSPORTATION ROUTE TO VAN BUREN BOULEVARD

FIGURE 5

MS=1:1 L:\Graphics\ProjectsByName\Riverside-FRA\CADD\FRA_Routes.dwg Feb 10, 2016 - 1:42pm rcollins

LEGEND

Soil Transportation Route

SCALE (FEET)

0 4,000

NOTE:

Map provided by Google Earth Professional, dated 6/7/12.

TRC

PROJECT: 167991

FACILITY:

FRIENDS OF THE RIVERSIDE AIRPORT, LLC
7020 CREST AVENUE
RIVERSIDE, CALIFORNIA

SOIL TRANSPORTATION ROUTE FROM VAN BUREN BOULEVARD TO HIGHWAY 60

FIGURE 6

Table 1
Individual Lot Information
Former Agricultural Park, Riverside, California

Tr. 28987 Lot No.	Type of Lot	Lot Size	# of Surface Samples
1	fill	small	6
2	fill	small	6
3	fill	small	6
4	cut	small	6
5	cut	small	6
6	cut	small	6
7	cut	small	6
8	cut	small	6
9	cut	small	6
10	cut	small	6
11	cut	small	6
12	cut	small	6
13	cut	small	6
14	cut	small	6
15	cut	small	6
16	cut	small	6
17	cut	small	6
18	cut	small	6
19	cut	small	6
20	cut	small	6
21	fill	small	6
22	fill	large	8
23	cut	large	8
24	cut	large	8
25	fill	large	8
26	cut	small	6
27	cut	small	6
28	cut	small	6
29	cut	small	6
30	cut	small	6
31	cut	small	6
32	cut	small	6
33	fill	small	6
34	fill	small	6
35	fill	small	6
36	fill	large	8
37	fill	large	8
38	fill	large	8
39	fill	large	8
40	fill	small	6
41	cut	small	6
42	cut	small	6
43	cut	small	6
44	cut	small	6
45	cut	small	6
46	cut	small	6
47	cut	small	6
48	cut	small	6
49	fill	small	6
50	fill	small	6
51	fill	small	6
52	fill	small	6
53	fill	small	6
54	fill	large	8
55	fill	large	8
56	fill	large	8
57	fill	small	6

Tr. 28987 Lot No.	Type of Lot	Lot Size	# of Surface Samples
58	fill	small	6
59	fill	small	6
60	fill	small	6
61	fill	large	8
62	fill	large	8
63	fill	large	8
64	fill	large	8
65	fill	large	8
66	fill	small	6
67	fill	small	6
68	fill	small	6
69	fill	small	6
70	fill	small	6
71	fill	small	6
72	fill	small	6
73	fill	small	6
74	fill	small	6
75	fill	small	6
76	fill	small	6
77	fill	small	6
78	fill	small	6
79	cut	small	6
80	fill	small	6
81	fill	small	6
82	fill	small	6
83	fill	small	6
84	fill	large	8
85	fill	large	8
86	fill	large	8
87	fill	small	6
88	fill	small	6
89	fill	large	8
90	fill	large	8
91	fill	large	8
92	fill	large	8
93	fill	large	8
94	fill	small	6
95	cut	small	6
96	cut	small	6
97	fill	small	6
98	fill	small	6
99	fill	small	6
100	fill	small	6
101	fill	large	8
102	fill	large	8
103	fill	large	8
104	fill	small	6
105	fill	small	6
106	fill	small	6
107	fill	small	6
108	cut	small	6
109	cut	small	6

APPENDIX A

AIR MONITORING PLAN ADDENDUM

9685 Research Drive
Irvine, CA 92618

949.727.9336 PHONE
949.727.7311 FAX

www.trcsolutions.com

June 7, 2016

Ms. Maryam Tasnif-Abassi
Department of Toxic Substances Control
5796 Corporate Avenue
Cypress, California 90630

SITE: FORMER AGRICULTURAL PARK
7020 CREST AVENUE
RIVERSIDE, CALIFORNIA

RE: AIR MONITORING PLAN ADDENDUM

Dear Ms. Tasnif-Abassi:

This document is intended to serve as an addendum to the *Workplan for Air Monitoring* provided as Appendix E in the Frey Environmental *Revised Response Plan – Excavation of Soils Containing PCBs* dated June 19, 2006. This addendum describes proposed methods to conduct upcoming air monitoring during soil removal efforts at the former Riverside Agricultural Park located at 7020 Crest Avenue in Riverside, California. Based on soil sampling efforts conducted in November 2015, as documented in the *Former Riverside Agricultural Park Soil Sampling Report* dated January 6, 2016, it was determined that surface soil with polychlorinated biphenyl (PCB) concentrations above the cleanup goal of 0.22 milligrams per kilogram (mg/kg) was present at select locations.

In 2009, Phase I of the remediation effort was conducted including excavation, removal, and proper disposal of soils containing PCB concentrations in excess of 50 mg/kg from locations determined by previous Site investigation efforts. In addition, soil samples were collected from select locations and analyzed for dioxins, furans and metals. All excavated soil with PCB concentrations at or above 50 mg/kg was transported offsite to the Waste Management, Incorporated, Kettleman Hills facility in Kettleman City, California. Soil containing PCB concentrations above 50 mg/kg at locations identified during previous Site characterization efforts has been removed, transported offsite, and disposed of properly. A total of ~8,666 tons of PCB- and /or metals-impacted soil were transported offsite for disposal. Additional items removed from the site include brush debris (green waste), PCB-contaminated concrete, sewer pipe, and utility poles.

In 2013/2014, Phase II of the removal effort was conducted including the excavation, removal, and disposal of soils containing PCB concentrations in excess of 0.22 mg/kg from locations

determined by previous site investigation efforts. In addition, soil samples were collected from select locations and analyzed for dioxins, furans and metals. PCB-impacted soil (165,226.64 tons) generated during excavation activities was characterized as a non-hazardous waste and transported to the Waste Management, Inc. Azusa Land Reclamation facility in Azusa, California, for recycling. Additional materials that were removed from the Site included clean soil (30,782 tons), concrete (4,481.37 tons), green waste (422.26 tons), and asbestos-cement pipe (50.82 tons).

Phase III work activities began on March 22, 2016 following approval of the *Soil Sampling and Excavation Work Plan* (TRC, 2016) by DTSC and EPA and are ongoing. The work is being conducted based on four distinct types of areas or phases as described below:

- Cut Lots - lots where soil was removed to achieve the final grade in Tract 28987;
- Fill Lots - lots where soil was imported and compacted to achieve the final grade in Tract 28987;
- Outside Areas - areas outside of the planned Phase I housing development; and
- Final Lot Sampling - final confirmation soil sampling of all lots in Tract 28987 (first phase of housing development).

Please refer to the *Soil Sampling and Excavation Work Plan* (TRC, 2016) for details regarding the sampling and excavation efforts planned for each area.

Background

Construction activities, including excavation and soil loading, are capable of generating soil-derived dust. Suspension and dispersion of dust containing PCBs can be transported to nearby receptors where exposures may potentially occur. While the specific dust mitigation measures to be implemented during excavation and soil loading are intended to reduce the potential for dust generation, a program of measurement and verification is required to address the following objectives:

- Evaluate the influence of excavation activities on downwind dust concentrations,
- Identify the need for additional mitigation measures and/or work stoppage based on the dust levels observed, and
- Confirm that the concentrations of PCBs in air are below levels that are protective of public health.

Measurement of PCB concentrations in air requires the use of air sampling equipment and subsequent laboratory analysis. While air sampling approaches provide reliable measurements for presence of PCBs in air, the typical turnaround time for receipt of laboratory analytical data ranges from several days to weeks. Consequently, standard air sampling approaches may not identify an exceedance of a health-based concentration until days or weeks after the fact. In consideration of this limitation, the proposed air monitoring program is designed to provide both the efficacy of dust mitigation measures and to confirm that the work activities are performed in a manner that is protective of public health.

Real-time particulate monitoring provides more instantaneous feedback regarding the efficacy of the dust mitigation measures, but does not provide a direct measurement of the PCB concentration in air. Thus, the establishment of a health-based dust concentration limit (DCL) which is measureable by real-time air monitoring equipment is critical to preventing public exposures. The results of the particulate monitoring provide advance notice when dust levels at the project fenceline approach or exceed the DCL. This allows for prompt action to address and mitigate the condition such as increasing the frequency or volume of water applied to the work area or under extreme conditions, work stoppage. Development of a health-protective DCL is an essential element of the real-time particulate monitoring program. Additional details regarding the methodology utilized to establish a health-based DCL are provided in the following section.

Health-Based Dust Concentration Limit Determination

Derivation of the health-based DCL assumes that the concentration of PCBs in dust is proportional to PCB concentration detected in soil. The equation that describes the calculation of the health-based DCL is provided below:

$$DCL = REL_{PCB} / [C_{PCB} \ x \ CF]$$

Where:

DCL = Health-Based Dust Concentration Limit ($\mu g/m^3$)
REL_{PCB} = Health-Based Reference Exposure Level for PCBs in Air ($\mu g/m^3$)
C_{PCB} = Maximum Concentration of PCBs in Soil (mg/kg)
CF = Correction Factor (1E-6 kg soil/mg soil)

Based on the laboratory analytical results of soil samples collected at the Site, the maximum PCB concentration remaining is 500 mg/kg (Sample O2289-W25 at 0.5 fbg). In order to calculate the health-based DCL, a value representing the health-based reference exposure level for PCBs in air is required. Since the anticipated project duration is on the order of months as opposed to years, a chronic, non-cancer endpoint reference exposure level is a conservative and health-protective value to use for this analysis. The United States Environmental Protection Agency (USEPA) definition of a chronic exposure is one that occurs over a period of 7 years or longer. A summary of potentially applicable health-based reference exposure levels for PCBs in air in a residential setting is provided below:

Reference Exposure Level ($\mu g/m^3$)	Basis for REL Value	Source of REL
7.3E-2	Chronic, Non-Cancer Endpoint (Original Value from Frey, 2006)	EPA Preliminary Remediation Goals, unspeciated mixture of PCBs (USEPA, 2004)
8.0E-2	Chronic, Non-Cancer Endpoint	Human Health Risk Assessment Note 3 Table, DTSC-modified Screening Level Reference

Reference Exposure Level ($\mu g/m^3$)	Basis for REL Value	Source of REL
		Concentration for Aroclor 1254 (DTSC, 2016)
7.0E-2	Chronic, Non-Cancer Endpoint (route-to-route extrapolation from Oral Reference Dose [2E-5 mg/kg-day])	Integrated Risk Information System Oral Reference Dose for Aroclor 1254; extrapolated to Reference Concentration in air (USEPA, 2015)
1.2E-1	Sub-Chronic, Non-Cancer Endpoint (route-to-route extrapolation from Oral Minimum Risk Level [3E-5 mg/kg-day])	Intermediate (15 to 364 days) Oral Minimum Risk Level for PCBs (Aroclor 1254); extrapolated to Reference Concentration in air (ATSDR, 2000)

Notes:

DTSC, 2016. California Department of Toxic Substances Control. Human and Ecological Risk Office. Human Health Risk Assessment Note 3 Tables. Reference Concentration and Residential Air Screening Level for High Risk PCBs (e.g., Aroclor 1254).

USEPA, 2004. United States Environmental Protection Agency. Region 9 Preliminary Remediation Goal Table, Air-H20, Non-Cancer Endpoint for Unspeciated Mixture of PCBs, High Risk (e.g., Aroclor 1254). October.

USEPA, 2015. United States Environmental Protection Agency. Integrated Risk Information System. Reference Exposure Level Extrapolated from Oral Reference Dose for Aroclor 1254 of 2E-5 mg/kg-day based on body weight of 70 kg and 20 m^3/day inhalation rate for residential exposure.

ATSDR, 2000. Agency for Toxic Substances and Disease Registry. Toxicological Profile for Polychlorinated Biphenyls (PCBs). November.

The potentially applicable reference exposure levels for intermediate to chronic, non-cancer effects range from 0.07 to 0.12 $\mu g/m^3$. These values are consistent with the reference exposure level utilized in the original dust action level calculation (Frey, 2006). For the purpose of calculating an updated DCL for Phase III remediation activities, the reference exposure level of 0.07 $\mu g/m^3$ was selected to derive the health-based DCL.

Table 1 provides an overview of the health-based DCL calculation and associated assumptions and references. Based on the current maximum PCB concentration detected in soil and the reference exposure level, the calculated health-based DCL for Phase III activities is approximately 140 $\mu g/m^3$. Dust levels below this value would not result in PCB concentrations in air above the reference exposure level of 0.07 $\mu g/m^3$. The calculated health-based DCL is considered very conservative as it was derived based on a chronic (7 years or longer) reference exposure level and

the maximum PCB concentration detected in soil, even though the anticipated project duration is only several months and the average PCB concentration would have been a more realistic representation of PCB levels that could be carried by dust during the cleanup.

Since the health-based DCL is higher than the 50 $\mu g/m^3$ PM_{10} concentration limit described in SCAQMD Rule 403 (as the difference between upwind and downwind samples) for fugitive dust controls, this lower value will represent the dust action level for the Phase III activities.

Monitoring for dioxins/furans was contemplated in the 2006 Response Plan. However, at the established dust action level (50 μg/m3) for the Phase III cleanup, the maximum predicted concentration of dioxins in air using the maximum detected concentration in soil (4.5E-6 mg/kg after Phase II cleanup) would be 2E-13 mg/m^3 (see the equation above). This value is well below the Community Action Level of 7E-9 mg/m3, and thus dioxin/furan sampling is not needed.

It should be noted that upon completion of additional sampling that is currently underway, the health-based DCL calculation will be re-evaluated based on the maximum PCB concentration in soil. If the resulting health-based DCL is determined to be lower than 50 $\mu g/m^3$, the lower value will be used as the dust action level during Phase III activities.

Proposed Air Monitoring Activities to be Performed During Phase III

Air monitoring will be performed during earth moving activities during Phase III of the remedial effort. Air monitoring activities will include wind monitoring, particulate monitoring for dust, and monitoring for PCB concentrations in air.

Wind Monitoring

Wind speed and direction will be monitored with a Davis Vantage Pro 2 weather station. The weather station is battery operated and will continuously record wind speed and direction during excavation activities. Analog data will be transmitted from the wind speed and direction sensors to a data logger which will be downloaded at the end of each week.

Particulate Monitoring

Air monitoring for particulates (PM_{10}) will be conducted using Met One Instruments E-BAM portable beta attenuation monitors which are Federal Equivalent Method (FEM)-approved monitors. The monitors will be operated continuously during periods of soil disturbance on days where earth moving operations occur (maximum of 8 hours per day). One upwind monitor and two downwind monitors will be placed at the perimeter of the property to provide continuous monitoring of particulate matter. Field calibration checks will be performed on a weekly basis using a BGI deltaCal® air flow calibrator.

As previously described, the health-based DCL is approximately 140 $\mu g/m^3$. Since the SCAQMD Rule 403 PM_{10} concentration is lower than the health-based value, a value of 50 $\mu g/m^3$ is selected as the dust action level for Phase III activities. This action level is measured as the difference between the upwind and downwind monitors over a one-hour period. In the event that the

difference between the upwind and downwind monitoring is greater than 50 $\mu g/m^3$, additional dust mitigation corrective measures will be implemented. Potential corrective measures to be considered range from increasing the water application rate and/or frequency, to the suspension of work activities. In addition to continuous logging by the E-BAM units, a TRC technician will hand record hourly dust concentrations on a field data sheet to determine if additional dust mitigation corrective measures are warranted.

It should be noted that the dust action level of 50 $\mu g/m^3$ is protective of public health with regard to potential exposures to PCBs in air during Phase III cleanup, as it is more stringent than the conservative health-based DCL of 140 $\mu g/m^3$ as discussed above. By way of comparison, the dust action level utilized during Phase I and Phase II activities was 7 $\mu g/m^3$ (Frey, 2006). The lower dust action level utilized during Phase I and II activities reflected the higher concentrations of PCBs in soil that existed at the time the Phase I work was performed. The higher dust action level for Phase III activities is reflective of the significant reduction in the maximum PCB concentrations in soil that were present during the Phase I and Phase II soil removal efforts conducted in 2009 and 2013/2014.

PCB Air Monitoring

Monitoring for PCBs in air will be performed in accordance with EPA Method TO-10A. Air pumps capable of moving 1 to 5 liters per minute (L/min) of air will be fitted with sorbent tube polyurethane foam (PUF) sampling devices. The pumps will be placed adjacent to each of the downwind E-BAM monitors and will be operated during earth moving activities (maximum of 8 hours per day). A minimum of two samples per day will be collected on days when earth moving activities are occurring. The samples will be sent to EMSL Analytical in Cinnaminson, New Jersey for laboratory analysis for PCBs. The results of the PCB monitoring will be compared to the intermediate to chronic PCB reference exposure levels of 0.07 to 0.12 $\mu g/m^3$ to confirm that concentrations of PCBs in air are below levels that are protective of public health.

In summary, this Air Monitoring Plan Addendum is intended to supplement the original Air Monitoring Plan that was used for Phase I and Phase II activities (Frey, 2006). In recognition that the current maximum concentration of PCBs in soil is at least an order of magnitude lower than the concentrations that were present prior to the completed removal activities, the health-based DCL was re-evaluated. The results of the analysis indicate that, based on the current maximum concentration of PCBs in soil, the health-based DCL is higher than the SCAQMD Rule 403 PM_{10} concentration (50 $\mu g/m^3$). Consequently, the dust action level to be utilized during Phase III activities is 50 $\mu g/m^3$.

Following completion of the additional soil sampling that is currently underway, the health-based DCL will be re-evaluated to consider the maximum PCB concentration in soil. The lower of the SCAQMD Rule 403 PM_{10} concentration (50 $\mu g/m^3$) or the health-based DCL will be used to evaluate the effectiveness of the dust mitigation measures and trigger implementation of additional dust mitigation corrective measures.

A minimum of two downwind air samples will be collected over a period of up to 8 hours during each day that excavation, loading or earth-moving activities occur. The results of the downwind air sampling will be compared to the intermediate to chronic PCB reference exposure levels of 0.07 to 0.12 $\mu g/m^3$ to confirm that concentrations of PCBs in air are below levels that are protective of public health. The air monitoring and sampling results will be reviewed on a daily basis to confirm the adequacy of the dust mitigation measures employed during Phase III activities.

If you have any comments, please contact David Lennon at (949) 341-7458.

Sincerely,

David Lennon
Principal Consultant

Ross Surrency, PG
Senior Project Geologist

Attachments:

Table 1 – Calculation of Health-Based Dust Concentration Limit (DCL) for PCBs

cc: Jason Low SCAQMD (electronic copy)
Katherine Baylor, EPA (electronic copy)
Greg Neal, DTSC (electronic copy)

Table 1
Calculation of Health-Based Dust Concentration Limit for PCBs
Phase III Air Monitoring Plan Addendum
Former Agricultural Park
Riverside, California

Equation

Health-Based Dust Concentration Limit = REL/ ($C_{soil\ max}$ x CF)

Symbol and Description	Units	Value
REL = Chronic, Non-Cancer Reference Concentration (EPA, 2015)	$\mu g/m^3$	0.07
$C_{PCB\ max}$ = Maximum Concentration of PCBs in soil[1]	mg/kg	500
$C_{PCB\ max}$ = Maximum Concentration of PCBs in soil[1]	$\mu g/kg$	500,000
CF = Correction factor	kg soil/mg soil	1.00E-06
Health-Based Dust Concentration Limit	mg dust/m^3 air	0.14
Health-Based Dust Concentration Limit	μg dust/m^3 air	140

Notes:

REL = Reference Exposure Level for PCBs in Air

EPA, 2015. Integrated Risk Information System. Reference Exposure Level Extrapolated from Chronic Oral Reference Dose for Aroclor 1254 of 2E-5 mg/kg-day based on body weight of 70 kg and 20 m^3/day inhalation rate for residential exposure.Levels for Residential Air.

[1] Maximum PCB concentration in soil (500 mg/kg) in Sample O2289-W25 at 0.5 fbg (4/25/16)

Health-Based Dust Concentration Limit represents the lowest concentration of dust in air that would not result in an exposure above the REL at the FRA Ag Park Fenceline.

$\mu g/kg$ = micrograms per kilogram
mg/kg = milligrams per kilogram
$\mu g/m^3$ = micrograms per cubic meter of air
mg/m^3 = milligrams per cubic meter of air

APPENDIX B

SOIL SAMPLING RESULTS MEMORANDUM

9685 Research Drive
Irvine, CA 92618

949.727.9336 PHONE
949.727.7311 FAX

www.trcsolutions.com

June 7, 2016

Ms. Maryam Tasnif-Abassi
Department of Toxic Substances Control
5796 Corporate Avenue
Cypress, California 90630

SITE: FORMER AGRICULTURAL PARK
7020 CREST AVENUE
RIVERSIDE, CALIFORNIA

RE: SOIL SAMPLING RESULTS

Dear Ms. Tasnif-Abassi:

This deliverable is provided to update the DTSC with soil sample results for the former Riverside Agricultural Park located at 7020 Crest Avenue in Riverside, California. Work activities began on March 22, 2016 following work plan approval by the DTSC and EPA.

The following documents are provided on the enclosed Compact Disc:

- Data summary tables for the Cut Lots, Fill Lots, and Outside Areas;
- A figure of soil sample locations; and
- Official laboratory reports.

If you have any comments, please contact David Lennon at (949) 341-7458.

Sincerely,

David Lennon
Principal Consultant

Ross Surrency, PG
Senior Project Geologist

Enclosure

cc: Greg Neal, DTSC (electronic copy)

Table 1
PCB Confirmation Sample Results
Cut Lots
Former Agricultural Park, Riverside, California

Cut Lot Samples					Step Out & Retest					Step Out & Retest					Step Out & Retest					Step Out & Retest				
Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action
C1635-N25	0.5	3/22/2016	0.31	Excavate to 50 ft. point																				
C1635-N50	0.5	3/22/2016	0.035	NFA																				
C1635-E25	0.5	3/22/2016	0.023J	NFA																				
C1635-E50	0.5	3/22/2016	ND	NFA																				
C1635-S25	0.5	3/22/2016	0.11	NFA																				
C1635-S50	0.5	3/22/2016	0.11	NFA																				
C1635-W25	0.5	3/22/2016	0.16	NFA																				
C1635-W50	0.5	3/22/2016	0.33	Excavate																				
C1636-N25	0.5	3/22/2016	0.27	Excavate to 50 ft. point																				
C1636-N50	0.5	3/22/2016	0.22	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2088 at same locatior																			
C1636-E25	0.5	3/22/2016	0.12	NFA																				
C1636-E50	0.5	3/22/2016	0.16	NFA																				
C1636-S25	0.5	3/22/2016	0.087	NFA																				
C1636-S50	0.5	3/22/2016	0.11	NFA																				
C1636-W25	0.5	3/22/2016	0.20	NFA																				
C1636-W50	0.5	3/22/2016	0.22	Excavate																				
C1637-N25	0.5	3/22/2016	0.24	Excavate to 50 ft. point																				
C1637-N50	0.5	3/22/2016	0.17	NFA																				
C1637-E25	0.5	3/22/2016	0.27	Excavate to 50 ft. point																				
C1637-E50	0.5	3/22/2016	0.23	Excavate																				
C1637-S25	0.5	3/22/2016	0.099	NFA																				
C1637-S50	0.5	3/22/2016	0.085	NFA																				
C1637-W25	0.5	3/22/2016	0.22	Excavate to 50 ft. point																				
C1637-W50	0.5	3/22/2016	0.30	Excavate																				
C1638-N25	0.5	3/22/2016	0.21	NFA																				
C1638-N50	0.5	3/22/2016	0.16	NFA																				
C1638-E25	0.5	3/22/2016	0.30	Excavate to 50 ft. point																				
C1638-E50	0.5	3/22/2016	0.41	Excavate																				
C1638-S25	0.5	3/22/2016	0.036	NFA																				
C1638-S50	0.5	3/22/2016	0.12	NFA																				
C1638-W25	0.5	3/22/2016	0.33	Excavate to 50 ft. point																				
C1638-W50	0.5	3/22/2016	0.31	Excavate																				
C1639-N25	0.5	3/23/2016	0.44	Excavate to 50 ft. point																				
C1639-N50	0.5	3/23/2016	0.0099J	NFA																				
C1639-E25	0.5	3/23/2016	0.29	Excavate to 50 ft. point																				
C1639-E50	0.5	3/23/2016	0.41	Excavate																				
C1639-S25	0.5	3/23/2016	0.08	NFA																				
C1639-S50	0.5	3/23/2016	0.011J	NFA																				
C1639-W25	0.5	3/23/2016	0.41	Excavate to 50 ft. point																				
C1639-W50	0.5	3/23/2016	0.40	Excavate																				
C1003-N25	0.5	3/23/2016	0.17	NFA																				
C1003-N50	0.5	3/23/2016	0.15	NFA																				
C1003-E25	0.5	3/23/2016	0.30	Excavate to 50 ft. point																				
C1003-E50	0.5	3/23/2016	0.58	Excavate																				
C1003-S25	0.5	3/23/2016	0.12	NFA																				
C1003-S50	0.5	3/23/2016	0.028J	NFA																				
C1003-W25	0.5	3/23/2016	0.43	Excavate to 50 ft. point																				
C1003-W50	0.5	3/23/2016	0.63	Excavate																				
C1640-N25	0.5	3/23/2016	0.10	NFA																				
C1640-N50	0.5	3/23/2016	0.17	NFA																				
C1640-E25	0.5	3/23/2016	0.32	Excavate to 50 ft. point																				
C1640-E50	0.5	3/23/2016	0.26	Excavate																				
C1640-S25	0.5	3/23/2016	0.13	NFA																				
C1640-S50	0.5	3/23/2016	0.10	NFA																				
C1640-W25	0.5	3/23/2016	0.28	Excavate to 50 ft. point																				
C1640-W50	0.5	3/23/2016	0.071	NFA																				
C1660-N25	0.5	3/23/2016	ND	NFA																				
C1660-N50	0.5	3/23/2016	ND	NFA																				
C1660-E25	0.5	3/23/2016	0.17	NFA																				
C1660-E50	0.5	3/23/2016	0.92	Step out 10 ft. and retest	C1660-E60	0.5	4/21/2016	2.4	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O1659-W45 at same locatior														
C1660-S25	0.5	3/23/2016	0.30	Excavate to 50 ft. point																				
C1660-S50	0.5	3/23/2016	0.0092J	NFA																				
C1660-W25	0.5	3/23/2016	0.0085J	NFA																				
C1660-W50	0.5	3/23/2016	0.0099J	NFA																				
C1676-N25	0.5	3/23/2016	0.037	NFA																				
C1676-N50	0.5	3/23/2016	0.011J	NFA																				
C1676-E25	0.5	3/23/2016	0.14	NFA																				
C1676-E50	0.5	3/23/2016	0.35	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2225 at same locatior																			
C1676-S25	0.5	3/23/2016	ND	NFA																				
C1676-S50	0.5	3/23/2016	0.14	NFA																				
C1676-W25	0.5	3/23/2016	ND	NFA																				
C1676-W50	0.5	3/23/2016	ND	NFA																				
C1674-N25	0.5	3/23/2016	ND	NFA																				
C1674-N50	0.5	3/23/2016	0.154	NFA																				
C1674-E25	0.5	3/23/2016	0.036	NFA																				
C1674-E50	0.5	3/23/2016	0.207	NFA																				
C1674-S25	0.5	3/23/2016	0.19	NFA																				
C1674-S50	0.5	3/23/2016	0.259	Step out 10 ft. and retest	No step-out sample collected due to presence of sample F1662-N60 at same locatior																			
C1674-W25	0.5	3/23/2016	0.088	NFA																				
C1674-W50	0.5	3/23/2016	0.092J	NFA																				
C1687-N25	0.5	3/23/2016	0.036	NFA																				
C1687-N50	0.5	3/23/2016	0.26	Step out 10 ft. and retest	C1687-N60	0.5	4/11/2016	ND	NFA															
C1687-E25	0.5	3/23/2016	0.253	Excavate to 50 ft. point																				
C1687-E50	0.5	3/23/2016	ND	NFA																				
C1687-S25	0.5	3/23/2016	0.332	Excavate to 50 ft. point																				
C1687-S50	0.5	3/23/2016	0.41	Step out 10 ft. and retest	C1687-S60	0.5	4/11/2016	ND	NFA															
C1687-W25	0.5	3/23/2016	2.16	Excavate to 50 ft. point																				
C1687-W50	0.5	3/23/2016	0.594	Step out 10 ft. and retest	C1687-W60	0.5	4/21/2016	0.34	Step out 10 ft. and retest	No step-out sample collected due to presence of sample F1688-E60 at same locatior														
C1716-N25	0.5	3/24/2016	ND	NFA																				
C1716-N50	0.5	3/24/2016	ND	NFA																				
C1716-E25	0.5	3/24/2016	ND	NFA																				
C1716-E50	0.5	3/24/2016	ND	NFA																				
C1716-S25	0.5	3/24/2016	ND	NFA																				

Table 1
PCB Confirmation Sample Results
Cut Lots
Former Agricultural Park, Riverside, California

Cut Lot Samples					Step Out & Retest					Step Out & Retest					Step Out & Retest					Step Out & Retest				
Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action
C1716-S50	0.5	3/24/2016	ND	NFA																				
C1716-W25	0.5	3/24/2016	0.073	NFA																				
C1716-W50	0.5	3/24/2016	ND	NFA																				
C1714-N25	0.5	3/24/2016	0.015J	NFA																				
C1714-N50	0.5	3/24/2016	0.025J	NFA																				
C1714-E25	0.5	3/24/2016	ND	NFA																				
C1714-E50	0.5	3/24/2016	ND	NFA																				
C1714-S25	0.5	3/24/2016	ND	NFA																				
C1714-S50	0.5	3/24/2016	0.11	NFA																				
C1714-W25	0.5	3/24/2016	0.18	NFA																				
C1714-W45	0.5	3/24/2016	0.068	NFA																				
C1713-N25	0.5	3/24/2016	0.10	NFA																				
C1713-N50	0.5	3/24/2016	0.15	NFA																				
C1713-E25	0.5	3/24/2016	0.012J	NFA																				
C1713-E50	0.5	3/24/2016	0.068	NFA																				
C1713-S25	0.5	3/24/2016	0.099	NFA																				
C1713-S50	0.5	3/24/2016	0.086	NFA																				
C1713-W25	0.5	3/24/2016	0.067	NFA																				
C1713-W50	0.5	3/24/2016	0.12	NFA																				
C1709-N25	0.5	3/24/2016	ND	NFA																				
C1709-N50	0.5	3/24/2016	0.014J	NFA																				
C1709-E25	0.5	3/24/2016	0.27	Excavate to 50 ft. point																				
C1709-E50	0.5	3/24/2016	ND	NFA																				
C1709-S25	0.5	3/25/2016	1.0	Excavate to 50 ft. point																				
C1709-S50	0.5	3/25/2016	0.62	Step out 10 ft. and retest	C1709-S60	0.5	4/11/2016	0.43	Step out 10 ft. and retest	C1709-S70	0.5	4/25/2016	0.38	Step out 10 ft. and retest	C1709-S80	0.5	5/3/2016	0.40	Step out 10 ft. and retest	C1709-S90	0.5	5/12/2016	0.37	No step-out sample collected due to presence of sample C1694 in same vicinity.
C1709-W25	0.5	3/25/2016	0.95	Excavate to 50 ft. point																				
C1709-W50	0.5	3/25/2016	0.57	Step out 10 ft. and retest	C1709-W60	0.5	4/11/2016	0.1195J	NFA															

Notes:
NFA = No further action. Result is <0.22 mg/kg.
mg/kg = milligrams per kilogram
fbg = feet below grade

Table 2
PCB Confirmation Sample Results
Fill Lots
Former Agricultural Park, Riverside, California

Fill Lot Samples					Step Out & Retest					Step Out & Retest					Step Out & Retest					Step Out & Retest				
Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action
F1612-N60	0.5	3/25/2016	0.083	NFA																				
F1612-E60	0.5	3/25/2016	0.052	NFA																				
F1612-S60	0.5	3/25/2016	0.078	NFA																				
F1613-N60	0.5	3/25/2016	0.041	NFA																				
F1613-S60	0.5	3/25/2016	0.37	Step out 10 ft. and retest	F1613-S70	0.5	4/12/2016	0.509	Step out 10 ft. and retest	F1613-S80	0.5	4/27/2016	0.43	Step out 10 ft. and retest	Unable to step out any further due to south fenceline.									
F1614-S60	0.5	3/25/2016	0.23	Step out 10 ft. and retest	F1614-S70	0.5	4/12/2016	1.54	Step out 10 ft. and retest	F1614-S80	0.5	4/27/2016	0.65	Step out 10 ft. and retest	Unable to step out any further due to south fenceline.									
F1614-N60	0.5	3/25/2016	0.15	NFA																				
F1614-W60	0.5	3/25/2016	0.13	NFA																				
F1616-E60	0.5	3/25/2016	0.22	Step out 10 ft. and retest	F1616-E70	0.5	4/12/2016	0.065	NFA															
F1616-S60	0.5	3/25/2016	0.063	NFA																				
F1616-W60	0.5	3/25/2016	0.041	NFA																				
F1627-S60	0.5	3/25/2016	0.098	NFA																				
F1627-E60	0.5	3/25/2016	0.0080J	NFA																				
F1625-S60	0.5	3/25/2016	0.14	NFA																				
F1619-E60	0.5	3/25/2016	0.080	NFA																				
F1619-W60	0.5	3/25/2016	0.010J	NFA																				
F1619-S60	0.5	3/25/2016	0.027J	NFA																				
F1623-S60	0.5	3/25/2016	0.20	NFA																				
F1623-W60	0.5	3/25/2016	0.89	Step out 10 ft. and retest	F1623-W70	0.5	4/11/2016	0.62	Step out 10 ft. and retest	F1623-W80	0.5	4/27/2016	0.55	Step out 10 ft. and retest	F1623-W90	0.5	5/10/2016	0.30	Step out 10 ft. and retest	F1623-W100	0.5	5/20/2016	0.19	NFA
F1623-N60	0.5	3/25/2016	0.46	Step out 10 ft. and retest	F1623-N70	0.5	4/11/2016	0.296	Step out 10 ft. and retest	F1623-N78	0.5	4/27/2016	0.25	Step out 10 ft. and retest	F1623-N90	0.5	5/10/2016	0.38	Step out 10 ft. and retest	F1623-N100	0.5	5/20/2016	0.070	NFA
F1624-N52	0.5	3/28/2016	0.212	NFA																				
F1625-N60	0.5	3/28/2016	0.301	Step out 10 ft. and retest	F1625-N70	0.5	4/11/2016	0.143J	NFA															
F1641-W60	0.5	3/28/2016	0.47	Step out 10 ft. and retest	F1641-W70	0.5	4/11/2016	0.31	Step out 10 ft. and retest	F1641-W80	0.5	4/27/2016	0.43	Step out 10 ft. and retest	F1641-W90	0.5	5/10/2016	0.47	Step out 10 ft. and retest	F1641-W100	0.5	5/20/2016	0.20	NFA
F1641-N60	0.5	3/28/2016	0.42	Step out 10 ft. and retest	F1641-N70	0.5	4/11/2016	0.186J	NFA															
F1004-N60	0.5	3/28/2016	0.091	NFA																				
F1004-E60	0.5	3/28/2016	0.53	Step out 10 ft. and retest																				
F1647-E60	0.5	3/28/2016	0.043	NFA																				
F1647-S60	0.5	3/28/2016	0.104	NFA																				
F1646-S60	0.5	3/28/2016	0.253	Step out 10 ft. and retest	F1646-S70	0.5	4/11/2016	0.877	Step out 10 ft. and retest	F1646-S80	0.5	4/27/2016	0.43	Step out 10 ft. and retest	F1646-S90	0.5	5/10/2016	0.35	Step out 10 ft. and retest	F1646-S100	0.5	5/20/2016	0.17	NFA
F1646-W60	0.5	3/28/2016	0.132J	NFA																				
F1667-W60	0.5	3/28/2016	0.692	Step out 10 ft. and retest	F1667-W70	0.5	4/11/2016	0.208J	NFA															
F1669-W60	0.5	3/28/2016	0.071	NFA																				
F1690-W60	0.5	3/28/2016	[illegible]	Step out 10 ft. and retest	F1690-W70	0.5	4/11/2016	0.52	Step out 10 ft. and retest	F1690-W80	0.5	4/27/2016	0.32	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2289 in same vicinity.									
F1670-N60	0.5	3/28/2016	0.145J	NFA																				
F1690-N60	0.5	3/28/2016	0.487	Step out 10 ft. and retest	F1690-N70	0.5	4/11/2016	0.024J	NFA															
F1690-E60	0.5	3/28/2016	0.239	Step out 10 ft. and retest	F1690-E70	0.5	4/11/2016	0.233	Step out 10 ft. and retest	F1690-E80	0.5	4/27/2016	0.24	Step out 10 ft. and retest	F1690-E90	0.5	5/10/2016	0.66	Step out 10 ft. and retest	F1690-E100	0.5	5/20/2016	0.12	NFA
F1670-E60	0.5	3/28/2016	1.38	Step out 10 ft. and retest	F1670-E70	0.5	4/11/2016	1.1	Step out 10 ft. and retest	F1670-E80	0.5	4/27/2016	0.19	NFA										
F1665-N60	0.5	3/28/2016	2.61	Step out 10 ft. and retest	F1665-N70	0.5	4/11/2016	0.26	Step out 10 ft. and retest	F1665-N80	0.5	4/27/2016	0.48	Step out 10 ft. and retest	F1665-N90	0.5	5/10/2016	0.042	NFA					
F1665-E60	0.5	3/28/2016	ND	NFA																				
F1665-S60	0.5	3/28/2016	0.036	NFA																				
F1651-S60	0.5	3/28/2016	2.0	Step out 10 ft. and retest																				
F1651-W60	0.5	3/28/2016	0.16	NFA																				
F1651-E60	0.5	3/28/2016	0.52	Step out 10 ft. and retest	F1651-E70	0.5	4/12/2016	0.071	NFA															
F1662-W60	0.5	3/28/2016	0.025J	NFA																				
F1662-E60	0.5	3/28/2016	0.50	Step out 10 ft. and retest	F1662-E70	0.5	4/12/2016	0.343	Step out 10 ft. and retest	F1662-E80	0.5	4/27/2016	1.0	Step out 10 ft. and retest	F1662-E90	0.5	5/10/2016	0.43	Step out 10 ft. and retest	F1662-E100	0.5	5/20/2016	0.26	No step-out sample collected due to presence of sample F1661 in same vicinity.
F1662-N60	0.5	3/28/2016	0.48	Step out 10 ft. and retest																				
F1654-S60	0.5	3/28/2016	0.038	NFA																				
F1654-E60	0.5	3/28/2016	0.92	Step out 10 ft. and retest																				
F1654-N60	0.5	3/28/2016	0.038	NFA																				
F1653-N60	0.5	3/28/2016	0.056	NFA																				
F1653-W60	0.5	3/28/2016	0.43	Step out 10 ft. and retest	F1653-W70	0.5	4/12/2016	0.965	Step out 10 ft. and retest	F1653-W80	0.5	4/27/2016	0.21	NFA										
F1653-S60	0.5	3/28/2016	0.11	NFA																				
F1693-E60	0.5	3/29/2016	0.232	Step out 10 ft. and retest	F1693-E70	0.5	4/11/2016	0.093	NFA															
F1693-N60	0.5	3/29/2016	0.185J	NFA																				
F1692-N60	0.5	3/29/2016	0.257	Step out 10 ft. and retest	F1692-N70	0.5	4/11/2016	0.054	NFA															
F1692-W60	0.5	3/29/2016	0.294	Step out 10 ft. and retest	F1692-W70	0.5	4/11/2016	0.60	Step out 10 ft. and retest	F1692-W80	0.5	4/27/2016	0.055	NFA										
F1688-E60	0.5	3/29/2016	0.72	Step out 10 ft. and retest	F1688-E70	0.5	4/11/2016	0.36	Step out 10 ft. and retest	No step-out sample collected due to presence of sample C1687-W60 at same location.														
F1688-S60	0.5	3/29/2016	0.78	Step out 10 ft. and retest	F1688-S70	0.5	4/11/2016	0.019J	NFA															
F1688-W60	0.5	3/29/2016	0.079	NFA																				
F1730-N60	0.5	3/29/2016	6.7	Step out 10 ft. and retest	F1730-N70	0.5	4/11/2016	0.187J	NFA															
F1730-E60	0.5	3/29/2016	0.984	Step out 10 ft. and retest	F1730-E70	0.5	4/11/2016	0.213J	NFA															
F1730-W60	0.5	3/29/2016	0.288	Step out 10 ft. and retest	F1730-W70	0.5	4/11/2016	0.40	Step out 10 ft. and retest	F1730-W80	0.5	4/27/2016	2.0	Step out 10 ft. and retest	F1730-W90	0.5	5/10/2016	1.5	Step out 10 ft. and retest	F1730-W100	0.5	5/20/2016	1.1	No step-out sample collected due to presence of sample F1006 in same vicinity.
F1730-S60	0.5	3/29/2016	0.415	Step out 10 ft. and retest	No step-out sample collected due to presence of sample C1714-N50 in same vicinity.																			

Notes:
NFA = No further action. Result is <0.22 mg/kg.
mg/kg = milligrams per kilogram
fbg = feet below grade

Table 3
PCB Confirmation Sample Results
Outside Areas
Former Agricultural Park, Riverside, California

Outside Area Samples					Step Out & Retest					Step Out & Retest					Step Out & Retest					Step Out & Retest					Step Out & Retest
Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID
O1601-S25	0.5	3/29/2016	0.51	Step out 10 ft. and retest	O1601-S35	0.5	4/12/2016	0.162J	NFA																
O1601-E25	0.5	3/29/2016	0.047	NFA																					
O1601-N25	0.5	3/29/2016	0.88	Step out 10 ft. and retest	O1601-N35	0.5	4/12/2016	0.817	Step out 10 ft. and retest	O1601-N45	0.5	4/27/2016	0.15	NFA											
O1601-W25	0.5	3/29/2016	0.28	Step out 10 ft. and retest	O1601-W35	0.5	4/12/2016	0.334	Step out 10 ft. and retest	O1601-W45	0.5	4/27/2016	4.3	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2070 in same vicinity										
O1607-W25	0.5	3/29/2016	ND	NFA																					
O1607-S25	0.5	3/29/2016	0.40	Step out 10 ft. and retest	O1607-S35	0.5	4/12/2016	0.533	Step out 10 ft. and retest	O1607-S45	0.5	4/27/2016	0.95	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2061 in same vicinity										
O1607-N25	0.5	3/29/2016	0.15	NFA																					
O1607-E25	0.5	3/29/2016	0.11	NFA																					
O1606-S25	0.5	3/29/2016	0.12	NFA																					
O1606-W25	0.5	3/29/2016	0.086	NFA																					
O1606-E25	0.5	3/29/2016	0.053	NFA																					
O1606-N25	0.5	3/29/2016	0.12	NFA																					
O1609-S25	0.5	3/29/2016	0.32	Step out 10 ft. and retest	O1609-S35	0.5	4/12/2016	0.180J	NFA																
O1609-E25	0.5	3/29/2016	0.19	NFA																					
O1609-W25	0.5	3/29/2016	ND	NFA																					
O1609-N25	0.5	3/29/2016	0.17	NFA																					
O1602-N25	0.5	3/29/2016	0.20	NFA																					
O1602-W25	0.5	3/29/2016	0.20	NFA																					
O1602-S25	0.5	3/29/2016	0.13	NFA																					
O1602-E25	0.5	3/29/2016	0.037	NFA																					
O1610-S25	0.5	3/29/2016	0.162	NFA																					
O1610-N25	0.5	3/29/2016	0.212	NFA																					
O1610-W25	0.5	3/29/2016	0.153	NFA																					
O1610-E25	0.5	3/29/2016	0.15	NFA																					
O2008	0.5	3/30/2016	0.034	NFA																					
O2009	0.5	3/30/2016	0.27	Step out 25 ft. in 4 directions and retest	O2009-E25	0.5	4/13/2016	0.13	NFA																
					O2009-W25	0.5	4/13/2016	0.17	NFA																
					Could not step out south due to fence																				
					Could not step out north due to a rock pile.																				
O2010	0.5	3/30/2016	0.15	NFA																					
O2012	--	--	--	Not sampled due to rock pile.																					
O2013	0.5	3/30/2016	0.11	NFA																					
O2011	0.5	3/30/2016	0.11	NFA																					
O2014	0.5	3/30/2016	0.14	NFA																					
O2016	0.5	3/30/2016	0.061	NFA																					
O2017	0.5	3/30/2016	0.11	NFA																					
O1604-S25	0.5	3/30/2016	0.14	NFA																					
O1604-W25	0.5	3/30/2016	0.090	NFA																					
O1604-E25	0.5	3/30/2016	0.026J	NFA																					
O1604-N25	0.5	3/30/2016	0.15	NFA																					
O2085	0.5	3/30/2016	0.12	NFA																					
O2084	0.5	3/30/2016	0.72	Step out 25 ft. in 4 directions and retest	O2084-N25	0.5	4/13/2016	0.060	NFA																
					O2084-E25	0.5	4/13/2016	0.38	Step out 10 ft. and retest	O2084-E35	0.5	4/27/2016	0.16	NFA											
					O2084-S25	0.5	4/13/2016	0.25	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O1602-N25 at same locatior															
					O2084-W25	0.5	4/13/2016	0.13	NFA																
O2080	0.5	3/30/2016	0.24	Step out 25 ft. in 4 directions and retest	O2080-N25	0.5	4/13/2016	0.31	Step out 10 ft. and retest	O2080-N35	0.5	4/27/2016	0.26	Step out 10 ft. and retest	O2080-N45	0.5	5/11/2016	0.057	NFA						
					O2080-E25	0.5	4/13/2016	0.17	NFA																
					O2080-S25	0.5	4/13/2016	0.57	Step out 10 ft. and retest	O2080-S35	0.5	4/27/2016	0.013 J	NFA											
					O2080-W25	0.5	4/13/2016	0.045	NFA																
O2079	0.5	3/30/2016	0.21	NFA																					
O2049	0.5	3/30/2016	0.145	NFA																					
O2022	0.5	3/30/2016	ND	NFA																					
O2050	0.5	3/30/2016	0.689	Step out 25 ft. in 4 directions and retest	O2050-N25	0.5	4/13/2016	ND	NFA																
					O2050-E25	0.5	4/13/2016	0.40	Step out 10 ft. and retest	O2050-E35	0.5	4/27/2016	0.51	Step out 10 ft. and retest	O2050-E45	0.5	5/11/2016	0.36	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2049 in same vicinity					
					O2050-S25	0.5	4/13/2016	0.57	Step out 10 ft. and retest	O2050-S35	0.5	4/27/2016	0.13	NFA											
					O2050-W25	0.5	4/13/2016	1.7	Step out 10 ft. and retest	O2050-W35	0.5	4/27/2016	0.74	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O1606-E25 in same vicinity										
O2078	0.5	3/30/2016	0.245	Step out 25 ft. in 4 directions and retest	O2078-N25	0.5	4/13/2016	0.082	NFA																
					O2078-E25	0.5	4/13/2016	0.072	NFA																
					O2078-S25	0.5	4/13/2016	0.17	NFA																
					O2078-W25	0.5	4/13/2016	0.15	NFA																
O2051	0.5	3/30/2016	0.033	NFA																					
O2063	0.5	3/30/2016	ND	NFA																					
O2064	0.5	3/30/2016	0.031	NFA																					
O2065	0.5	3/30/2016	0.50	Step out 25 ft. in 4 directions and retest	O2065-N25	0.5	4/13/2016	0.052	NFA																
					O2065-E25	0.5	4/13/2016	0.13	NFA																
					O2065-S15	0.5	4/13/2016	0.20	NFA																
					O2065-W25	0.5	4/13/2016	0.183J	NFA																
O2066	0.5	3/30/2016	0.031J	NFA																					
O2067	0.5	3/30/2016	0.058	NFA																					
O2068	0.5	3/30/2016	0.581	Step out 25 ft. in 4 directions and retest	O2068-E25	0.5	4/13/2016	0.20	NFA																
					O2068-S25	0.5	4/13/2016	0.079	NFA																
					O2068-W25	0.5	4/13/2016	0.099	NFA																
					No north step-out sample collected due to presence of sample O1601-S25 at same locatior																				
O2069	0.5	3/30/2016	0.32	Step out 25 ft. in 4 directions and retest	O2069-N25	0.5	4/13/2016	0.216J	NFA																
					O2069-E25	0.5	4/13/2016	0.17	NFA																
					O2069-S25	0.5	4/13/2016	0.29	Step out 10 ft. and retest	O2069-S35	0.5	4/27/2016	0.072	NFA											
					O2069-W25	0.5	4/13/2016	ND	NFA																
O2062	0.5	3/30/2016	ND	NFA																					
O2070	0.5	3/30/2016	0.483	Step out 25 ft. in 4 directions and retest	O2070-N25	0.5	4/13/2016	0.15	NFA																
					O2070-W25	0.5	4/13/2016	ND	NFA																
					O2070-S25	0.5	4/13/2016	0.22	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2069-N25 at same location															
					No east step-out sample collected due to presence of sample O1601-W25 at same locatior																				
O2061	0.5	3/30/2016	1.56	Step out 25 ft. in 4 directions and retest	O2061-E25	0.5	4/13/2016	ND	NFA																
					O2061-S25	0.5	4/13/2016	ND	NFA																
					O2061-W25	0.5	4/13/2016	ND	NFA																
					No north step-out sample collected due to presence of sample O1607-S25 at same locatior																				
O2076	0.5	3/30/2016	0.203	NFA																					
O2075	0.5	3/30/2016	0.136	NFA																					
O2056	0.5	3/30/2016	0.023J	NFA																					
O2052	0.5	3/30/2016	0.383	Step out 25 ft. in 4 directions and retest	O2052-W25	0.5	4/14/2016	0.32	Step out 10 ft. and retest	O2052-W35	0.5	4/27/2016	0.19	NFA											
					O2052-S25	0.5	4/14/2016	0.0942J	NFA																
					O2052-E25	0.5	4/14/2016	0.10	NFA																
					No north step-out sample collected due to presence of sample O1609-S25 at same locatior																				
O2041	0.5	3/30/2016	0.299	Step out 25 ft. in 4 directions and retest	O2041-N25	0.5	4/14/2016	0.13	NFA																
					O2041-W25	0.5	4/14/2016	0.019J	NFA																
					O2041-S25	0.5	4/14/2016	0.064	NFA																
					O2041-E25	0.5	4/14/2016	0.24	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O1610-W25 at same location															
O2048	0.5	3/30/2016	0.072	NFA																					
O2035	0.5	3/30/2016	0.266	Step out 25 ft. in 4 directions and retest	O2035-S25	0.5	4/14/2016	0.082	NFA																
					O2035-E25	0.5	4/14/2016	0.23	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2046-W25 at same location															

Table 3
PCB Confirmation Sample Results
Outside Areas
Former Agricultural Park, Riverside, California

Outside Area Samples					Step Out & Retest					Step Out & Retest					Step Out & Retest					Step Out & Retest					Step Out & Retest
Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID
					O2035-N12	0.5	4/14/2016	0.048	NFA																
					O2035-W25	0.5	4/14/2016	0.35	Step out 10 ft. and retest	O2035-W35	0.5	4/27/2016	0.29	Step out 10 ft. and retest	O2035-W45	0.5	5/11/2016	0.27	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2036 in same vicinity					
O2036	0.5	3/30/2016	0.196	NFA																					
O2046	0.5	3/30/2016	0.274	Step out 25 ft. in 4 directions and retest	O2046-N25	0.5	4/13/2016	0.18	NFA																
					O2046-E25	0.5	4/13/2016	0.036	NFA																
					O2046-S25	0.5	4/13/2016	0.14	NFA																
					O2046-W25	0.5	4/13/2016	1.5	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2035-E25 in same vicinity															
O2047	0.5	3/30/2016	0.182	NFA																					
O2032	0.5	3/30/2016	0.177	NFA																					
O2033	0.5	3/30/2016	0.131	NFA																					
O2034	0.5	3/30/2016	0.407	Step out 25 ft. in 4 directions and retest	O2034-N21	0.5	4/14/2016	0.42	Step out 10 ft. and retest	Not sampled due to sand stockpile.															
					O2034-W25	0.5	4/14/2016	0.12	NFA																
					O2034-S10	0.5	4/14/2016	0.36	Step out 10 ft. and retest	Not sampled due to rock stockpile															
					O2034-E25	0.5	4/14/2016	0.18	NFA																
O2031	0.5	3/30/2016	0.77	Step out 25 ft. in 4 directions and retest	O2031-W25	0.5	4/14/2016	0.34	Step out 10 ft. and retest	O2031-W35	0.5	4/28/2016	0.52	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2032 in same vicinity										
					O2031-S25	0.5	4/14/2016	0.049	NFA																
					O2031-E25	0.5	4/14/2016	0.33	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2025-W25 at same location															
					No north step-out sample collected due to presence of sample O1636-S50 at same location																				
O2025	0.5	3/30/2016	0.22	Step out 25 ft. in 4 directions and retest	O2025-S25	0.5	4/14/2016	0.40	Step out 10 ft. and retest	O2025-S35	0.5	4/28/2016	0.065	NFA											
					O2025-E25	0.5	4/14/2016	0.15	NFA																
					O2025-W25	0.5	4/14/2016	0.23	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2031-E25 in same vicinity															
					O2025-N25	0.5	4/14/2016	0.18	NFA																
O2024	0.5	3/30/2016	0.11	NFA																					
O2026	0.5	3/30/2016	0.082	NFA																					
O2023	0.5	3/31/2016	0.023J	NFA																					
O2006	0.5	3/31/2016	0.14	NFA																					
O2007	0.5	3/31/2016	0.17	NFA																					
O2005	0.5	3/31/2016	0.24	Step out 25 ft. to north and south and retest	O2005-S25	0.5	4/14/2016	0.16	NFA																
					O2005-N25	0.5	4/14/2016	0.33	Step out 10 ft. and retest	O2005-N35	0.5	4/28/2016	0.60	Step out 10 ft. and retest	O2005-N45	0.5	5/11/2016	0.57	Step out 10 ft. and retest	O2005-N55	0.5	5/20/2016	0.24	Step out 10 ft. and retest	No step-out sample collected due to presence of sample F1654-S60 in same vicinity.
O2004	0.5	3/31/2016	0.31	Step out 25 ft. to north and south and retest	O2004-S25	0.5	4/14/2016	0.079	NFA																
					O2004-N25	0.5	4/14/2016	0.24	Step out 10 ft. and retest	O2004-N35	0.5	4/28/2016	0.90	Step out 10 ft. and retest	O2004-N45	0.5	5/11/2016	0.39	Step out 10 ft. and retest	No step-out sample collected due to presence of concrete					
O2003	0.5	3/31/2016	0.50	Step out 25 ft. to north and south and retest	O2003-S25	0.5	4/14/2016	0.11	NFA																
					O2003-N25	0.5	4/14/2016	0.33	Step out 10 ft. and retest	O2003-N35	0.5	4/28/2016	0.20	NFA											
O2002	0.5	3/31/2016	0.58	Step out 25 ft. to north and south and retest	O2002-S25	0.5	4/14/2016	0.20	NFA																
					O2002-N25	0.5	4/14/2016	0.33	Step out 10 ft. and retest	O2002-N35	0.5	4/28/2016	0.13	NFA											
O2000	0.5	3/31/2016	0.27	Step out 25 ft. to north and south and retest	O2000-N25	0.5	4/14/2016	0.403	Step out 10 ft. and retest	O2000-N35	0.5	4/28/2016	0.20	NFA											
					O2000-S25	0.5	4/14/2016	0.37	Step out 10 ft. and retest	O2000-S35	0.5	4/28/2016	[illegible]	Step out 10 ft. and retest	O2000-S45	0.5	5/11/2016	1.0	Step out 10 ft. and retest	O2000-S55	0.5	5/20/2016			
O2087	0.5	3/31/2016	0.25	Step out 25 ft. in 4 directions and retest	O2087-W25	0.5	4/14/2016	0.43	Step out 10 ft. and retest	O2087-W35	0.5	4/28/2016	0.25	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2088 in same vicinity										
					O2087-E25	0.5	4/14/2016	0.098	NFA																
					O2087-N25	0.5	4/14/2016	ND	NFA																
					O2087-S25	0.5	4/14/2016	0.23	Step out 10 ft. and retest	O2087-S35	0.5	4/28/2016	0.023 J	NFA											
O2086	0.5	3/31/2016	0.064	NFA																					
O2088	0.5	3/31/2016	0.18	NFA																					
O2089	0.5	3/31/2016	0.16	NFA																					
O2123	0.5	3/31/2016	ND	NFA																					
O2124	0.5	3/31/2016	ND	NFA																					
O2120	0.5	3/31/2016	0.073	NFA																					
O2125	0.5	3/31/2016	0.081	NFA																					
O2128	0.5	3/31/2016	0.14	NFA																					
O2177	0.5	3/31/2016	ND	NFA																					
O2126	0.5	3/31/2016	0.15	NFA																					
O1633-S25	0.5	3/31/2016	0.48	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2046-N25 at same location																				
O1633-E25	0.5	3/31/2016	0.19	NFA																					
O1633-W25	0.5	3/31/2016	0.14	NFA																					
O1633-N25	0.5	3/31/2016	0.44	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2031-S25 at same location																				
O2097	0.5	3/31/2016	0.60	Step out 25 ft. in 4 directions and retest	O2097-E25	0.5	4/15/2016	0.47	Step out 10 ft. and retest	O2097-E35	0.5	4/28/2016	0.25	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2127 in same vicinity										
					O2097-N25	0.5	4/15/2016	1.7	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2096-S25 at same location															
					O2097-S25	0.5	4/15/2016	1.9	Step out 10 ft. and retest	O2097-S35	0.5	4/28/2016	1.0	Step out 10 ft. and retest	O2097-S45	0.5	5/11/2016	1.7	Step out 10 ft. and retest	O2097-S55	0.5	5/20/2016	1.9	Step out 10 ft. and retest	No step-out sample collected due to presence of sample F1654-E60 in same vicinity.
					O2097-W25	0.5	4/15/2016	0.59	Step out 10 ft. and retest	O2097-W35	0.5	4/28/2016	0.17	NFA											
O1655-E25	0.5	3/31/2016	0.20	NFA																					
O1655-S25	0.5	3/31/2016	1.1	Step out 10 ft. and retest	O1655-S35	0.5	4/15/2016	0.98	Step out 10 ft. and retest	O1655-S45	0.5	4/28/2016	0.62	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2088 in same vicinity										
O1655-W25	0.5	3/31/2016	1.4	Step out 10 ft. and retest	O1655-W35	0.5	4/15/2016	0.20	NFA																
O1655-N25	0.5	3/31/2016	0.37	Step out 10 ft. and retest	O1655-N35	0.5	4/15/2016	0.48	Step out 10 ft. and retest	O1655-N45	0.5	4/28/2016	0.19	NFA											
O2103	0.5	3/31/2016	ND	NFA																					
O2127	0.5	3/31/2016	1.2	Step out 25 ft. in 4 directions and retest	O2127-N25	0.5	4/15/2016	7.5	Step out 10 ft. and retest	O2127-N35	0.5	4/28/2016	0.55	Step out 10 ft. and retest	O2127-N45	0.5	5/11/2016	0.38	Step out 10 ft. and retest	O2127-N55	0.5	5/20/2016	0.074	NFA	
					O2127-E25	0.5	4/15/2016	4.2	Step out 10 ft. and retest	O2127-E35	0.5	4/28/2016	0.075	NFA											
O2104	0.5	3/31/2016	0.039	NFA																					
O2105	0.5	3/31/2016	ND	NFA																					
O2106	0.5	3/31/2016	0.079	NFA																					
O2119	0.5	3/31/2016	ND	NFA																					
O2121	0.5	3/31/2016	ND	NFA																					
O2122	0.5	3/31/2016	0.21	NFA																					
O2096	0.5	3/31/2016	1.4	Step out 25 ft. in 4 directions and retest	O2096-E25	0.5	4/15/2016	1.8	Step out 10 ft. and retest	O2096-E35	0.5	4/28/2016	0.26	Step out 10 ft. and retest	O2096-E45	0.5	5/11/2016	0.26	Step out 10 ft. and retest	O2096-E55	0.5	5/20/2016	0.097	NFA	
					O2096-S25	0.5	4/15/2016	0.57	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2097-N25 at same location															
					O2096-N25	0.5	4/15/2016	0.16	NFA																
					O2096-W25	0.5	4/15/2016	2.0	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O1659-E35 at same location															
O1659-W25	0.5	3/31/2016	0.59	Step out 10 ft. and retest	O1659-W35	0.5	4/15/2016	0.35	Step out 10 ft. and retest	O1659-W45	0.5	4/28/2016	0.36	Step out 10 ft. and retest	No step-out sample collected due to presence of sample C1660-E60 in same vicinity										
O1659-S25	0.5	3/31/2016	0.58	Step out 10 ft. and retest	O1659-S35	0.5	4/15/2016	0.20	NFA																
O1659-N25	0.5	3/31/2016	ND	NFA																					
O1659-E25	0.5	3/31/2016	0.90	Step out 10 ft. and retest	O1659-E35	0.5	4/15/2016	0.36	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2096-N25 at same location															
O2171	0.5	3/31/2016	0.041	NFA																					
O2170	0.5	3/31/2016	0.016J	NFA																					
O2225	0.5	3/31/2016	4.02	Step out 25 ft. in 4 directions and retest	O2225-E25	0.5	4/15/2016	0.47	Step out 10 ft. and retest	O2225-E35	0.5	4/28/2016	1.9	Step out 10 ft. and retest	O2225-E45	0.5	5/11/2016	1.2	Step out 10 ft. and retest	O2225-E55	0.5	5/20/2016	0.65	Step out 10 ft. and retest	No step-out sample collected due to presence of sample C1677-W25 in same vicinity.
					O2225-N25	0.5	4/15/2016	0.14	NFA																
					O2225-S25	0.5	4/15/2016	0.32	Step out 10 ft. and retest	O2225-S35	0.5	4/28/2016	0.16	NFA											
O1700-S25	0.5	4/1/2016	ND	NFA																					
O1700-E25	0.5	4/1/2016	ND	NFA																					
O1700-W25	0.5	4/1/2016	ND	NFA																					
O1700-N25	0.5	4/1/2016	ND	NFA																					
O2117	0.5	4/1/2016	ND	NFA																					
O2116	0.5	4/1/2016	ND	NFA																					
O2107	0.5	4/1/2016	0.016J	NFA																					
O2115	0.5	4/1/2016	ND	NFA																					
O2131	0.5	4/1/2016	0.27	Step out 25 ft. in 4 directions and retest	O2131-N25	0.5	4/19/2016	0.089	NFA																

Table 3
PCB Confirmation Sample Results
Outside Areas
Former Agricultural Park, Riverside, California

Outside Area Samples					Step Out & Retest					Step Out & Retest					Step Out & Retest					Step Out & Retest					Step Out & Retest
Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID
					O2131-E25	0.5	4/19/2016	0.067	NFA																
					O2131-S25	0.5	4/19/2016	0.66	Step out 10 ft. and retest	O2131-S35	0.5	5/3/2016	0.383	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2130 in same vicinity										
					O2131-W25	0.5	4/19/2016	ND	NFA																
O2130	0.5	4/1/2016	ND	NFA																					
O2129	0.5	4/1/2016	--	Container broke during shipping. Retest	O2129	0.5	4/13/2016	0.25	Step out 25 ft. in 4 directions and retest	O2129-N25	0.5	4/28/2016	0.065	NFA											
O2118	0.5	4/1/2016	ND	NFA						O2129-E25	0.5	4/28/2016	ND	NFA											
O2110	0.5	4/1/2016	ND	NFA						O2129-W25	0.5	4/28/2016	0.025 J	NFA											
O2109	0.5	4/1/2016	ND	NFA						O2129-S25	0.5	4/28/2016	0.18	NFA											
O2108	0.5	4/1/2016	ND	NFA																					
O2132	0.5	4/1/2016	ND	NFA																					
O1703-W25	0.5	4/1/2016	0.013J	NFA																					
O1703-N25	0.5	4/1/2016	0.031J	NFA																					
O1703-E25	0.5	4/1/2016	0.023J	NFA																					
O1703-S25	0.5	4/1/2016	0.022J	NFA																					
O2133	0.5	4/1/2016	0.26	Step out 25 ft. in 4 directions and retest	O2133-N25	0.5	4/19/2016	0.053	NFA																
					O2133-E25	0.5	4/19/2016	0.25	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2167 at same location															
					O2133-S25	0.5	4/19/2016	0.10	NFA																
					O2133-W25	0.5	4/19/2016	ND	NFA																
O2164	0.5	4/1/2016	0.01J	NFA																					
O2134	0.5	4/1/2016	0.34	Step out 25 ft. in 4 directions and retest	O2134-N25	0.5	4/19/2016	0.11	NFA																
					O2134-E25	0.5	4/19/2016	0.077	NFA																
					O2134-S25	0.5	4/19/2016	0.11	NFA																
					O2134-W25	0.5	4/19/2016	0.13	NFA																
O2135	0.5	4/1/2016	--	Container broke during shipping. Retest	O2135	0.5	4/13/2016	0.047	NFA																
O2169	0.5	4/1/2016	ND	NFA																					
O1721-N25	0.5	4/1/2016	0.05	NFA																					
O1721-W25	0.5	4/1/2016	0.059	NFA																					
O1721-E25	0.5	4/1/2016	0.089	NFA																					
O1721-S25	0.5	4/1/2016	0.081	NFA																					
O2161	0.5	4/1/2016	0.016J	NFA																					
O2163	0.5	4/1/2016	0.048	NFA																					
O2162	0.5	4/1/2016	0.0086J	NFA																					
O1001-S25	0.5	4/1/2016	0.068	NFA																					
O1001-E25	0.5	4/1/2016	0.17	NFA																					
O1001-W25	0.5	4/1/2016	0.94	Step out 10 ft. and retest	O1001-W35	0.5	4/15/2016	0.57	Step out 10 ft. and retest	O1001-W45	0.5	4/29/2016	1.2	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2137 in same vicinity										
O1001-N25	0.5	4/1/2016	0.32	Step out 10 ft. and retest	O1001-N35	0.5	4/15/2016	0.54	Step out 10 ft. and retest	O1001-N42	0.5	4/29/2016	0.111J	NFA											
O2156	0.5	4/1/2016	ND	NFA																					
O2155	0.5	4/1/2016	ND	NFA																					
O2154	0.5	4/1/2016	ND	NFA																					
O2153	0.5	4/1/2016	ND	NFA																					
O2136	0.5	4/1/2016	0.38	Step out 25 ft. in 4 directions and retest	O2136-N25	0.5	4/19/2016	0.61	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2137-S25 at same location															
					O2136-E25	0.5	4/19/2016	0.028J	NFA																
					O2136-S25	0.5	4/19/2016	0.11	NFA																
					O2136-W25	0.5	4/19/2016	0.10	NFA																
O2137	0.5	4/1/2016	0.35	Step out 25 ft. in 4 directions and retest	O2137-N25	0.5	4/19/2016	0.78	Step out 10 ft. and retest	O2137-N35	0.5	4/29/2016	0.20	NFA											
					O2137-S25	0.5	4/19/2016	0.33	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2136-N25 at same location															
					O2137-W25	0.5	4/19/2016	0.62	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O1724-E25 at same location															
					No east step-out sample collected due to presence of sample O1001-W35 at same location																				
O2142	0.5	4/1/2016	0.12	NFA																					
O2152	0.5	4/1/2016	ND	NFA																					
O1724-S25	0.5	4/1/2016	0.29	Step out 10 ft. and retest	O1724-S35	0.5	4/19/2016	0.051	NFA																
O1724-E25	0.5	4/1/2016	0.12	NFA																					
O2186	0.5	4/1/2016	0.13	NFA																					
O1724-N25	0.5	4/1/2016	0.12	NFA																					
O1724-W25	0.5	4/1/2016	0.12	NFA																					
O1723-N25	0.5	4/1/2016	--	Container broke during shipping. Retest	O1723-N25	0.5	4/13/2016	0.81	Step out 10 ft. and retest	O1723-N35	0.5	4/29/2016	0.083	NFA											
O1723-W25	0.5	4/1/2016	0.14	NFA																					
O1723-S25	0.5	4/1/2016	0.11	NFA																					
O1723-E25	0.5	4/1/2016	0.028J	NFA																					
O1002-W25	0.5	4/4/2016	0.48	Step out 10 ft. and retest	O1002-W35	0.5	4/15/2016	0.52	Step out 10 ft. and retest	O1002-W45	0.5	4/29/2016	0.59	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2147 in same vicinity										
O1002-N25	0.5	4/4/2016	0.41	Step out 10 ft. and retest	O1002-N35	0.5	4/15/2016	0.14	NFA																
O1002-S25	0.5	4/4/2016	0.62	Step out 10 ft. and retest	O1002-S35	0.5	4/15/2016	0.31	Step out 10 ft. and retest	O1002-S45	0.5	4/29/2016	ND	NFA											
O1002-E25	0.5	4/4/2016	0.66	Step out 10 ft. and retest	O1002-E35	0.5	4/15/2016	0.52	Step out 10 ft. and retest	O1002-E45	0.5	4/29/2016	0.33	Step out 10 ft. and retest	O1002-E55	0.5	5/20/2016	0.32	Step out 10 ft. and retest	No step-out sample collected due to presence of property fence line					
O2197	0.5	4/4/2016	0.17	NFA																					
O2147	0.5	4/4/2016	0.44	Step out 25 ft. in 4 directions and retest	O2147-N25	0.5	4/15/2016	0.23	Step out 10 ft. and retest	O2147-N35	0.5	4/29/2016	0.14	NFA											
					O2147-W25	0.5	4/15/2016	0.50	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O1723-E25 at same location															
					O2147-S25	0.5	4/15/2016	0.64	Step out 10 ft. and retest	O2147-S35	0.5	4/29/2016	2.7	Step out 10 ft. and retest	O2147-S45	0.5	5/20/2016	ND	NFA						
O2196	0.5	4/4/2016	0.11	NFA																					
O2193		--	--	Not sampled due to rock pile.																					
O2194		--	--	Not sampled due to rock pile.																					
O2195	0.5	4/4/2016	0.089	NFA																					
O2198	0.5	4/4/2016	0.21	NFA																					
O2199	0.5	4/4/2016	ND	NFA																					
O2201	0.5	4/4/2016	ND	NFA																					
O2200	0.5	4/4/2016	ND	NFA																					
O2202	0.5	4/4/2016	ND	NFA																					
O2203	0.5	4/4/2016	ND	NFA																					
O2205	0.5	4/4/2016	ND	NFA																					
O2204	0.5	4/4/2016	ND	NFA																					
O2207	0.5	4/4/2016	ND	NFA																					
O2206	0.5	4/4/2016	ND	NFA																					
O2208	0.5	4/4/2016	ND	NFA																					
O2209	0.5	4/4/2016	ND	NFA																					
O2211	0.5	4/4/2016	ND	NFA																					
O2210	0.5	4/4/2016	ND	NFA																					
O2212	0.5	4/4/2016	ND	NFA																					
O2213		--	--	Not sampled due to rock pile.																					
O2251	0.5	4/4/2016	ND	NFA																					
O2191	0.5	4/4/2016	0.18	NFA																					
O2214	0.5	4/4/2016	0.11	NFA																					
O2250	0.5	4/4/2016	0.14	NFA																					
O2269	0.5	4/4/2016	0.058	NFA																					
O2249	0.5	4/4/2016	0.017J	NFA																					
O2252		--	--	Not sampled due to rock pile.																					
O2253	0.5	4/4/2016	ND	NFA																					
O2254	0.5	4/4/2016	ND	NFA																					
O2255	0.5	4/4/2016	ND	NFA																					
O2256	0.5	4/4/2016	1.0	Step out 25 ft. in 4 directions and retest	O2256-N25	0.5	4/18/2016	ND	NFA																
					O2256-E25	0.5	4/18/2016	0.019J	NFA																
					O2256-W25	0.5	4/18/2016	0.23	Step out 10 ft. and retest	O2256-W35	0.5	4/29/2016	1.3	Step out 10 ft. and retest	O2256-W45	0.5	5/20/2016	2.3	Step out 20 ft. and retest						
					O2256-S25	0.5	4/18/2016	ND	NFA																

Table 3
PCB Confirmation Sample Results
Outside Areas
Former Agricultural Park, Riverside, California

Outside Area Samples					Step Out & Retest					Step Out & Retest					Step Out & Retest					Step Out & Retest					Step Out & Retest
Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID
O2259	0.5	4/4/2016	0.024J	NFA																					
O2268	0.5	4/4/2016	0.42	Step out 25 ft. in 4 directions and retest	O2268-N25	0.5	4/18/2016	0.16	NFA																
					O2268-E25	0.5	4/18/2016	0.20	NFA																
					O2268-S25	0.5	4/18/2016	1.8	Step out 10 ft. and retest	O2268-S35	0.5	4/29/2016	0.80	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2500-N45 in same vicinity										
					O2268-W25	0.5	4/18/2016	0.83	Step out 10 ft. and retest	O2268-W35	0.5	4/29/2016	0.060	NFA											
O2258	0.5	4/4/2016	0.41	Step out 25 ft. in 4 directions and retest	O2258-N25	0.5	4/18/2016	0.022J	NFA																
					O2258-W25	0.5	4/18/2016	0.45	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2257-E25 at same location															
					O2258-E25	0.5	4/18/2016	1.6	Step out 10 ft. and retest	O2258-E35	0.5	4/29/2016	1.0	Step out 10 ft. and retest	O2258-E45	0.5	5/20/2016	0.93	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2259 in same vicinity					
					O2258-S25	0.5	4/18/2016	0.33	Step out 10 ft. and retest	O2258-S35	0.5	4/29/2016	0.16	NFA											
O2257	0.5	4/4/2016	0.33	Step out 25 ft. in 4 directions and retest	O2257-N25	0.5	4/18/2016	0.026J	NFA																
					O2257-E25	0.5	4/18/2016	0.55	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2258-W25 at same location															
					O2257-S25	0.5	4/18/2016	1.1	Step out 10 ft. and retest	O2257-S35	0.5	4/29/2016	0.017J	NFA											
					O2257-W25	0.5	4/18/2016	0.022J	NFA																
O2261	0.5	4/4/2016	0.11	NFA																					
O2262	0.5	4/4/2016	ND	NFA																					
O2260	0.5	4/4/2016	0.073	NFA																					
O2263	0.5	4/4/2016	0.90	Step out 25 ft. in 4 directions and retest	O2263-N25	0.5	4/18/2016	0.14	NFA																
					O2263-S25	0.5	4/18/2016	ND	NFA																
					O2263-W25	0.5	4/18/2016	ND	NFA																
O1726-E25	0.5	4/4/2016	1.5	Step out 10 ft. and retest	O1726-N35	0.5	4/18/2016	0.79	Step out 10 ft. and retest	O1726-N45	0.5	4/29/2016	0.23	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2500-W35 in same vicinity										
O1726-N25	0.5	4/4/2016	0.38	Step out 10 ft. and retest	O1726-E35	0.5	4/18/2016	5.7	Step out 10 ft. and retest	O1726-E45	0.5	4/29/2016	4.7	Step out 10 ft. and retest	O1726-E55	0.5	5/20/2016	0.28	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2271 in same vicinity					
O1726-S25	0.5	4/4/2016	0.21	NFA																					
O1726-W25	0.5	4/4/2016	0.031	NFA																					
O1677-E25	0.5	4/5/2016	0.26	Step out 10 ft. and retest	O1677-E35	0.5	4/19/2016	ND	NFA																
O1677-N25	0.5	4/5/2016	0.346	Step out 10 ft. and retest	O1677-N35	0.5	4/19/2016	0.11	NFA																
O1677-S25	0.5	4/5/2016	35.3	Step out 10 ft. and retest	O1677-S35	0.5	4/19/2016	2.6	Step out 10 ft. and retest	O1677-S45	0.5	5/3/2016	3.9	Step out 10 ft. and retest	O1677-S55	0.5	5/12/2016	1.2	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2171 in same vicinity					
O1677-W25	0.5	4/5/2016	0.92	Step out 10 ft. and retest	O1677-W35	0.5	4/19/2016	0.73	Step out 10 ft. and retest	O1677-W45	0.5	5/3/2016	1.1	Step out 10 ft. and retest	O1677-W55	0.5	5/12/2016	2.3	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2225 in same vicinity					
O2223	0.5	4/5/2016	0.029J	NFA																					
O1683-N25	0.5	4/5/2016	0.224	Step out 10 ft. and retest	O1683-N35	0.5	4/19/2016	1.1	Step out 10 ft. and retest	O1683-N45	0.5	4/29/2016	0.16	NFA											
O1683-E25	0.5	4/5/2016	3.78	Step out 10 ft. and retest	O1683-E35	0.5	4/19/2016	0.044	NFA																
O1683-S25	0.5	4/5/2016	0.213J	NFA																					
O1683-W25	0.5	4/5/2016	0.209J	NFA																					
O2226	0.5	4/5/2016	0.167J	NFA																					
O2224	0.5	4/5/2016	13.86	Step out 25 ft. in 4 directions and retest	O2224-N25	0.5	4/19/2016	0.65	Step out 10 ft. and retest	O2224-N35	0.5	4/29/2016	0.15	NFA											
					O2224-E25	0.5	4/19/2016	0.18	NFA																
					O2224-S25	0.5	4/19/2016	0.93	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2225-N25 at same location															
					O2224-W25	0.5	4/19/2016	6.0	Step out 10 ft. and retest	O2224-W35	0.5	4/29/2016	0.42	Step out 10 ft. and retest	O2224-W45	0.5	5/20/2016	1.4	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2226 in same vicinity					
O2231	0.5	4/5/2016	0.259	Step out 25 ft. in 4 directions and retest	O2231-N25	0.5	4/19/2016	0.18	NFA																
					O2231-E25	0.5	4/19/2016	ND	NFA																
					O2231-W25	0.5	4/19/2016	ND	NFA																
					No south step-out sample collected due to presence of sample O1683-N35 at same location																				
O2232	0.5	4/5/2016	ND	NFA																					
O1698-N25	0.5	4/5/2016	0.089J	NFA																					
O1698-E25	0.5	4/5/2016	0.997	Step out 10 ft. and retest	O1698-E35	0.5	4/19/2016	1.6	Step out 10 ft. and retest	O1698-E45	0.5	4/29/2016	0.21	Step out 10 ft. and retest	O1698-E55	0.5	5/20/2016	2.6	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2221 in same vicinity					
O1698-S25	0.5	4/5/2016	0.165J	NFA																					
O1698-W25	0.5	4/5/2016	0.042	NFA																					
O2222	0.5	4/5/2016	1.177	Step out 25 ft. in 4 directions and retest	O2222-N25	0.5	4/19/2016	0.12	NFA																
					O2222-E25	0.5	4/19/2016	0.036	NFA																
					O2222-S25	0.5	4/19/2016	2.6	Step out 10 ft. and retest	O2222-S35	0.5	4/29/2016	2.7	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2223 in same vicinity										
					O2222-W25	0.5	4/19/2016	0.069	NFA																
O2221	0.5	4/5/2016	0.209J	NFA																					
O2238	0.5	4/5/2016	0.012J	NFA																					
O2237	0.5	4/5/2016	0.48	Step out 25 ft. in 4 directions and retest	O2237-E25	0.5	4/19/2016	0.98	Step out 10 ft. and retest	O2237-E35	0.5	4/29/2016	0.79	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2220-N25 in same vicinity										
					O2237-S25	0.5	4/19/2016	0.046	NFA																
					O2237-W25	0.5	4/19/2016	0.23	Step out 10 ft. and retest	O2237-W35	0.5	4/29/2016	0.90	Step out 10 ft. and retest	O2237-W45	0.5	5/20/2016	ND	NFA						
					No north step-out sample collected due to presence of sample O1705-S25 at same location																				
O2239	0.5	4/5/2016	2.67	Step out 25 ft. in 4 directions and retest	O2239-N25	0.5	4/19/2016	ND	NFA																
					O2239-E25	0.5	4/19/2016	0.022J	NFA																
					O2239-S25	0.5	4/19/2016	ND	NFA																
					O2239-W25	0.5	4/19/2016	ND	NFA																
O1705-N25	0.5	4/5/2016	0.47	Step out 10 ft. and retest	O1705-N35	0.5	4/20/2016	5.1	Step out 10 ft. and retest	O1705-N45	0.5	4/29/2016	2.2	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2243 in same vicinity										
O1705-E25	0.5	4/5/2016	0.94	Step out 10 ft. and retest	O1705-E35	0.5	4/20/2016	8.0	Step out 10 ft. and retest	O1705-E45	0.5	5/20/2016	18	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2219 in same vicinity										
O1705-S25	0.5	4/5/2016	0.53	Step out 10 ft. and retest	O1705-S35	0.5	4/20/2016	0.46	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2237 at same location															
O1705-W25	0.5	4/5/2016	2.2	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2239-E25 at same location																				
O2275	0.5	4/5/2016	1.3	Step out 25 ft. in 4 directions and retest	O2275-N25	0.5	4/20/2016	0.054	NFA																
					O2275-E25	0.5	4/20/2016	ND	NFA																
					O2275-S25	0.5	4/20/2016	ND	NFA																
					O2275-W25	0.5	4/20/2016	ND	NFA																
O2276	0.5	4/5/2016	ND	NFA																					
O2273	0.5	4/5/2016	12	Step out 25 ft. in 4 directions and retest	O2273-N25	0.5	4/20/2016	0.36	Step out 10 ft. and retest	O2273-N35	0.5	4/29/2016	0.14	NFA											
					O2273-E25	0.5	4/20/2016	0.35	Step out 10 ft. and retest	O2273-E35	0.5	4/29/2016	0.81	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O1719-W25 in same vicinity										
					O2273-S25	0.5	4/20/2016	0.17	NFA																
					O2273-W25	0.5	4/20/2016	4.1	Step out 10 ft. and retest	O2273-W35	0.5	4/29/2016	ND	NFA											
O2274	0.5	4/5/2016	0.14	NFA																					
O2183	0.5	4/5/2016	0.19	NFA																					
O1682-N25	0.5	4/5/2016	0.040	NFA																					
O1682-E25	0.5	4/5/2016	0.102J	NFA																					
O1682-S25	0.5	4/5/2016	0.247	Step out 10 ft. and retest	O1682-S35	0.5	5/2/2016	0.035	NFA																
O1682-W25	0.5	4/5/2016	6.72	Step out 10 ft. and retest	O1682-W35	0.5	5/2/2016	1.3	Step out 10 ft. and retest																
O2178	0.5	4/5/2016	0.022J	NFA																					
O2184	0.5	4/5/2016	ND	NFA																					
O2220	0.5	4/5/2016	7.5	Step out 25 ft. in 4 directions and retest	O2220-N25	0.5	4/20/2016	11	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2219-S25 at same location															
					O2220-E25	0.5	4/20/2016	0.58	Step out 10 ft. and retest	O2220-E35	0.5	5/2/2016	0.53	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2184 in same vicinity										
					O2220-S25	0.5	4/20/2016	2.4	Step out 10 ft. and retest	O2220-S35	0.5	5/2/2016	5.5	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2221 in same vicinity										
					O2220-W25	0.5	4/20/2016	1.5	Step out 10 ft. and retest	O2220-W35	0.5	5/2/2016	0.78	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2237-S25 in same vicinity										
O2219	0.5	4/5/2016	37	Step out 25 ft. in 4 directions and retest	O2219-N25	0.5	4/20/2016	11	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2218-S25 at same location															
					O2219-E25	0.5	4/20/2016	0.061	NFA																
					O2218-S25	0.5	4/20/2016	3.3	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2219-N25 at same location															
					No west step-out sample collected due to presence of sample O1705-E25 at same location																				
O2218	0.5	4/5/2016	3.0	Step out 25 ft. in 4 directions and retest	O2218-N25	0.5	4/20/2016	1.3	Step out 10 ft. and retest	O2218-N35	0.5	5/2/2016	0.81	Step out 10 ft. and retest	Not able to step out due to a rock pile.										
					O2218-E25	0.5	4/20/2016	0.039	NFA																
					O2218-S25	0.5	4/20/2016	8.7	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2219-N25 at same location															
					O2218-W25	0.5	4/20/2016	8.4	Step out 10 ft. and retest	O2218-W35	0.5	5/2/2016	3.2	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2243 in same vicinity										
O2243	0.5	4/5/2016	0.046	NFA																					
O2185	0.5	4/5/2016	1.31	Step out 25 ft. in 4 directions and retest	O2185-N25	0.5	4/21/2016	0.11	NFA																
					O2185-E25	0.5	4/21/2016	0.032 J	NFA																
					O2185-S25	0.5	4/21/2016	0.40	Step out 10 ft. and retest	O2185-S35	0.5	5/2/2016	0.41	Step out 10 ft. and retest	O2185-S45	0.5	5/11/2016	0.35	Step out 10 ft. and retest	O2185-S55	0.5	5/23/2016	ND	NFA	
					O2185-W25	0.5	4/21/2016	ND	NFA																
O2217	0.5	4/5/2016	0.090	NFA																					
O2216	0.5	4/5/2016	ND	NFA																					
O2215	0.5	4/5/2016	ND	NFA																					

Table 3
PCB Confirmation Sample Results
Outside Areas
Former Agricultural Park, Riverside, California

Outside Area Samples					Step Out & Retest					Step Out & Retest					Step Out & Retest					Step Out & Retest					Step Out & Retest
Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID
O1719-E25	0.5	4/6/2016	1.9	Step out 10 ft. and retest	Could not step out due to a concrete debris pile.																			
O1719-N25	0.5	4/6/2016	0.69	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2248-S25 at same location																			
O1719-S25	0.5	4/6/2016	0.011J	NFA																				
O1719-W25	0.5	4/6/2016	3.6	Step out 10 ft. and retest	O1719-W35	0.5	5/2/2016	1.5	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2273-E25 in same vicinity														
O2248	0.5	4/6/2016	1.9	Step out 25 ft. in 4 directions and retest	O2248-N25	0.5	4/20/2016	0.029J	NFA															
					O2248-E25	0.5	4/20/2016	1.8	Step out 10 ft. and retest	O2248-E35	0.5	5/2/2016	0.16	NFA										
					O2248-S25	0.5	4/20/2016	0.62	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O1719-N25 at same location														
					O2248-W25	0.5	4/20/2016	0.024J	NFA															
O2272	0.5	4/6/2016	0.80	Step out 25 ft. in 4 directions and retest	O2272-N25	0.5	4/21/2016	1.0	Step out 10 ft. and retest	O2272-N35	0.5	5/3/2016	0.86	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2271 in same vicinity									
					O2272-E25	0.5	4/21/2016	ND	NFA															
					O2272-S25	0.5	4/21/2016	4.3	Step out 10 ft. and retest	O2272-S35	0.5	5/3/2016	1.2	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2273-E35 in same vicinity									
					O2272-W25	0.5	4/21/2016	0.99	Step out 10 ft. and retest	O2272-W35	0.5	5/3/2016	1.2	Step out 10 ft. and retest	O2272-W45	0.5	5/12/2016	0.13	NFA					
O2271	0.5	4/6/2016	0.046	NFA																				
O2270	0.5	4/6/2016	0.064	NFA																				
O2500	0.5	4/6/2016	5.7	Step out 25 ft. in 4 directions and retest	O2500-N25	0.5	4/25/2016	1.1	Step out 10 ft. and retest	O2500-N35	0.5	5/3/2016	1.4	Step out 10 ft. and retest	O2500-N45	0.5	5/12/2016	0.23	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2268-S35 in same vicinity				
					O2500-E25	0.5	4/25/2016	0.37	Step out 10 ft. and retest	O2500-E35	0.5	5/3/2016	7.9	Step out 10 ft. and retest	O2500-E45	0.5	5/12/2016	2.0	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2270 in same vicinity				
					O2500-S25	0.5	4/25/2016	30	Step out 10 ft. and retest	O2500-S35	0.5	5/3/2016	3.5	Step out 10 ft. and retest	O2500-S45	0.5	5/12/2016	2.1	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O1726-N35 in same vicinity				
					O2500-W25	0.5	4/25/2016	6.2	Step out 10 ft. and retest	O2500-W35	0.5	5/3/2016	0.38	Step out 10 ft. and retest	O2500-W45	0.5	5/12/2016	12	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2260 in same vicinity				
O2277	0.5	4/6/2016	0.11	NFA																				
O2278	0.5	4/6/2016	0.040	NFA																				
O2279	0.5	4/6/2016	ND	NFA																				
O2280	0.5	4/6/2016	ND	NFA																				
O2281	0.5	4/6/2016	ND	NFA																				
O1668-S25	0.5	4/6/2016	0.015J	NFA																				
O1668-N25	0.5	4/6/2016	0.32	Step out 10 ft. and retest	O1668-N35	0.5	4/21/2016	0.40	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2286-S25 at same location														
O1668-W25	0.5	4/6/2016	2.86	Step out 10 ft. and retest	O1668-W35	0.5	4/21/2016	0.038	NFA															
O1668-E25	0.5	4/6/2016	0.251	Step out 10 ft. and retest	O1668-E35	0.5	4/21/2016	0.011 J	NFA															
O2286	0.5	4/6/2016	0.53	Step out 25 ft. in 4 directions and retest	O2286-N25	0.5	4/21/2016	5.6	Step out 10 ft. and retest	O2286-N35	0.5	5/3/2016	3.9	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O1737-E25 in same vicinity									
					O2286-E25	0.5	4/21/2016	0.31	Step out 10 ft. and retest	O2286-E35	0.5	5/3/2016	0.043	NFA										
					O2286-S25	0.5	4/21/2016	0.33	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O1668-N35 at same location														
					O2286-W25	0.5	4/21/2016	0.10	NFA															
O2306	0.5	4/6/2016	6.92	Step out 25 ft. in 4 directions and retest	O2306-N25	0.5	4/21/2016	4.9	Step out 10 ft. and retest	O2306-N35	0.5	5/3/2016	2.9	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O1737-W35 in same vicinity									
					O2306-E25	0.5	4/21/2016	ND	NFA															
					O2306-S25	0.5	4/21/2016	17	Step out 10 ft. and retest	O2306-S35	0.5	5/3/2016	ND	NFA										
					O2306-W25	0.5	4/21/2016	0.056	NFA															
O2287	0.5	4/6/2016	0.31	Step out 25 ft. in 4 directions and retest	O2287-N25	0.5	4/21/2016	0.055	NFA															
					O2287-S25	0.5	4/21/2016	0.58	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2286-E25 at same location														
					O2287-W25	0.5	4/21/2016	0.75	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O1737-E25 at same location														
					No east step-out sample collected due to presence of sample F1669-W60 at same location																			
O1737-E25	0.5	4/6/2016	ND	NFA																				
O1737-S25	0.5	4/6/2016	ND	NFA																				
O1737-N25	0.5	4/6/2016	0.013J	NFA																				
O1737-W25	0.5	4/6/2016	2.6	Step out 10 ft. and retest	O1737-W35	0.5	4/21/2016	1.2	Step out 10 ft. and retest	O1737-W45	0.5	5/3/2016	0.72	Step out 10 ft. and retest	O1737-W55	0.5	5/12/2016	0.29	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2307 in same vicinity				
O2307	0.5	4/6/2016	0.058	NFA																				
O2312	0.5	4/6/2016	0.18	NFA																				
O2311	0.5	4/6/2016	1.3	Step out 25 ft. in 4 directions and retest	O2311-N25	0.5	4/21/2016	2.6	Step out 10 ft. and retest	O2311-N35	0.5	5/3/2016	3.2	Step out 10 ft. and retest	O2311-N45	0.5	5/12/2016	3.2	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O1736-S20 in same vicinity				
					O2311-E25	0.5	4/21/2016	4.3	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2288-W25 at same location														
					O2311-S25	0.5	4/21/2016	0.012 J	NFA															
					O2311-W25	0.5	4/21/2016	ND	NFA															
O2314	0.5	4/6/2016	15	Step out 25 ft. in 4 directions and retest	O2314-N25	0.5	4/22/2016	18	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2322-S25 in same vicinity														
					O2314-E25	0.5	4/22/2016	0.60	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2318-W25 in same vicinity														
					O2314-S25	0.5	4/22/2016	8.1	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2313-N25 in same vicinity														
					O2314-W25	0.5	4/22/2016	1.4	Step out 10 ft. and retest	O2314-W35	0.5	5/10/2016	0.039	NFA										
O2313	0.5	4/6/2016	0.24	Step out 25 ft. in 4 directions and retest	O2313-N25	0.5	4/21/2016	1.6	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2314-S25 in same vicinity														
					O2313-E25	0.5	4/21/2016	1.8	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O1716-W20 in same vicinity														
					O2313-S25	0.5	4/21/2016	0.85	Step out 10 ft. and retest	O2313-S35	0.5	5/10/2016	0.45	Step out 10 ft. and retest	O2313-S45	0.5	5/23/2016	0.72	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2312 in same vicinity				
					O2313-W25	0.5	4/21/2016	0.064	NFA	O2313-W35	0.5	5/10/2016	0.25	Step out 10 ft. and retest	O2313-W45	0.5	5/23/2016	ND	NFA					
O2318	0.5	4/6/2016	14	Step out 25 ft. in 4 directions and retest	O2318-N25	0.5	4/22/2016	19	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O1735-S35 in same vicinity														
					O2318-E25	0.5	4/22/2016	0.047	NFA															
					O2318-S25	0.5	4/22/2016	8.3	Step out 10 ft. and retest	No step-out sample collected due to presence of DTSC sample B4-N20 in same vicinity														
					O2318-W25	0.5	4/22/2016	20	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2314-E35 in same vicinity														
O1735-W25	0.5	4/6/2016	0.12	NFA																				
O1735-S25	0.5	4/6/2016	4.2	Step out 10 ft. and retest	O1735-S35	0.5	4/22/2016	2.2	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2318-N25 in same vicinity														
O1735-N20	0.5	4/6/2016	0.096	NFA																				
O1735-E25	0.5	4/6/2016	0.99	Step out 10 ft. and retest	O1735-E35	0.5	4/22/2016	25	Step out 10 ft. and retest	O1735-E45	0.5	5/10/2016	1.6	Step out 10 ft. and retest	O1735-E55	0.5	5/23/2016	0.21	NFA					
O2502	0.5	4/7/2016	2.36	Step out 25 ft. in 4 directions and retest	O2502-E25	0.5	4/22/2016	2.0	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O1711-W25 in same vicinity														
					O2502-N25	0.5	4/22/2016	ND	NFA															
					O2502-S25	0.5	4/22/2016	0.035	NFA															
					O2502-W25	0.5	4/22/2016	1.3	Step out 10 ft. and retest	O2502-W35	0.5	5/10/2016	0.076	NFA										
O2503	0.5	4/7/2016	1.091	Step out 25 ft. in 4 directions and retest	O2503-N25	0.5	4/22/2016	ND	NFA															
					O2503-E25	0.5	4/22/2016	19	Step out 10 ft. and retest	O2503-E35	0.5	5/10/2016	12	Step out 10 ft. and retest	O2503-E45	0.5	5/23/2016	3.4	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O1712 in same vicinity				
					O2503-S25	0.5	4/22/2016	0.18	NFA															
					O2503-W25	0.5	4/22/2016	[redacted]	Step out 10 ft. and retest	O2503-W35	0.5	5/10/2016	ND	NFA										
O2504	0.5	4/7/2016	0.231	Step out 25 ft. in 4 directions and retest	O2504-N25	0.5	4/22/2016	0.66	Step out 10 ft. and retest	O2504-N35	0.5	5/10/2016	8.7	Step out 10 ft. and retest	O2504-N45	0.5	5/23/2016	4.2	Step out 20 ft. and retest					
					O2504-E25	0.5	4/22/2016	0.43	Step out 10 ft. and retest	O2504-E35	0.5	5/10/2016	0.080	NFA										
					O2504-S25	0.5	4/22/2016	0.32	Step out 10 ft. and retest	O2504-S35	0.5	5/10/2016	0.014J	NFA										
					O2504-W25	0.5	4/22/2016	2.4	Step out 10 ft. and retest	O2504-W35	0.5	5/10/2016	ND	NFA										
O2505	0.5	4/7/2016	27.4	Step out 25 ft. in 4 directions and retest	O2505-E25	0.5	4/18/2016	5.8	Step out 10 ft. and retest	O2505-E35	0.5	5/2/2016	[redacted]	Step out 10 ft. and retest	O2505-E45	0.5	5/11/2016	1.1	Step out 10 ft. and retest	O2505-E55	0.5	5/23/2016	3.3	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2295 in same vicinity.
					O2505-S25	0.5	4/18/2016	0.031J	NFA															
					O2505-N25	0.5	4/18/2016	2.9	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2505-S25 at same location														
					O2505-W25	0.5	4/18/2016	13	Step out 10 ft. and retest	O2505-W35	0.5	5/2/2016	0.24	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2324 in same vicinity									
O2288	0.5	4/7/2016	0.39	Step out 25 ft. in 4 directions and retest	O2288-N25	0.5	4/25/2016	[redacted]	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2289-S25 in same vicinity														
					O2288-E25	0.5	4/25/2016	0.13	NFA															
					O2288-S25	0.5	4/25/2016	0.53	NFA															
					O2288-W25	0.5	4/25/2016	[redacted]	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2311-E25 in same vicinity														
O2289	0.5	4/7/2016	21.1	Step out 25 ft. in 4 directions and retest	O2289-W25	0.5	4/22/2016	[redacted]	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O1736-E20 in same vicinity														
					O2289-E25	0.5	4/22/2016	0.19	NFA															
					O2289-S25	0.5	4/22/2016	7.0	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2288-N25 in same vicinity														
O2290	0.5	4/7/2016	44.3	Step out 25 ft. in 4 directions and retest	O2290-N25	0.5	4/22/2016	16	Step out 10 ft. and retest	O2290-N35	0.5	5/10/2016	0.33	Step out 10 ft. and retest	O2290-N45	0.5	5/23/2016	31	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2506 in same vicinity				
					O2290-E25	0.5	4/22/2016	0.92	Step out 10 ft. and retest	O2290-E35	0.5	5/10/2016	0.13	NFA										
					O2290-S25	0.5	4/22/2016	0.49	Step out 10 ft. and retest	No step-out sample collected due to presence of sample F1690-W80 in same vicinity														
					O2290-W25	0.5	4/22/2016	2.5	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2318-E25 in same vicinity														
O2506	0.5	4/7/2016	0.119J	NFA																				
O1691-N25	0.5	4/7/2016	0.025J	NFA																				
O1691-S25	0.5	4/7/2016	0.57	Step out 10 ft. and retest	O1691-S35	0.5	4/25/2016	0.98	Step out 10 ft. and retest	O1691-S45	0.5	5/10/2016	0.35	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O1690-N60 in same vicinity									
O1691-E25	0.5	4/7/2016	0.047	NFA																				
O1691-W25	0.5	4/7/2016	1.6	Step out 10 ft. and retest	O1691-W35	0.5	4/25/2016	2.6	Step out 10 ft. and retest	O1691-W45	0.5	5/10/2016	24	Step out 10 ft. and retest	O1691-W55	0.5	5/23/2016	25	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2506 in same vicinity				
O1711-N25	0.5	4/7/2016	0.16	NFA																				
O1711-E25	0.5	4/7/2016	0.019J	NFA																				

Table 3
PCB Confirmation Sample Results
Outside Areas
Former Agricultural Park, Riverside, California

Outside Area Samples					Step Out & Retest					Step Out & Retest					Step Out & Retest					Step Out & Retest					Step Out & Retest
Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID	Sample Depth (fbg)	Date Collected	PCBs (mg/kg)	Action	Sample ID
O1711-S25	0.5	4/7/2016	0.017J	NFA																					
O1711-W25	0.5	4/7/2016	0.96	Step out 10 ft. and retest	O1711-W35	0.5	4/25/2016	0.49	Step out 10 ft. and retest	O1711-W45	0.5	5/10/2016	10	Step out 10 ft. and retest	O1711-W55	0.5	5/23/2016	0.16	NFA						
O2295	0.5	4/7/2016	0.054	NFA																					
O2300	0.5	4/7/2016	0.22	Step out 25 ft. in 4 directions and retest	O2300-N25	0.5	4/25/2016	1.078	Step out 10 ft. and retest	O2300-N35	0.5	5/10/2016	1.1	Step out 10 ft. and retest	O2300-N45	0.5	5/23/2016	0.24	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O1712 in same vicinity					
					O2300-E25	0.5	4/25/2016	1.366	Step out 10 ft. and retest	O2300-E35	0.5	5/10/2016	3.9	Step out 10 ft. and retest	O2300-E45	0.5	5/23/2016	0.083	NFA						
					O2300-W25	0.5	4/25/2016	9.8	Step out 10 ft. and retest	O2300-W35	0.5	5/10/2016	1.6	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2501-E25 in same vicinity										
					No south step-out sample collected due to presence of sample O1711-N25 at same location																				
O2301	0.5	4/7/2016	0.10	NFA																					
O1731-N25	0.5	4/7/2016	0.18	NFA																					
O1731-E25	0.5	4/7/2016	0.14	NFA																					
O1731-S25	0.5	4/7/2016	0.41	Step out 10 ft. and retest	O1731-S35	0.5	4/25/2016	0.37	Step out 10 ft. and retest	O1731-S45	0.5	5/12/2016	0.21	NFA											
O1731-W25	0.5	4/7/2016	0.012J	NFA																					
O2322	0.5	4/7/2016	9.89	Step out 25 ft. in 4 directions and retest	O2322-N25	0.5	4/25/2016	2.2	Step out 10 ft. and retest	O2322-N35	0.5	5/12/2016	0.76	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2323 in same vicinity										
					O2322-E25	0.5	4/25/2016	5.9	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O1735-W25 in same vicinity															
					O2322-S25	0.5	4/25/2016	5.52	Step out 10 ft. and retest	O2322-S35	0.5	5/12/2016	8.4	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2314-N25 in same vicinity										
					O2322-W25	0.5	4/25/2016	0.25	Step out 10 ft. and retest	O2322-W35	0.5	5/12/2016	0.17	NFA											
O2323	0.5	4/7/2016	0.137J	NFA																					
O2325	0.5	4/7/2016	ND	NFA																					
O2326	0.5	4/7/2016	0.010J	NFA																					
O2327	0.5	4/7/2016	ND	NFA																					
O2328	0.5	4/7/2016	ND	NFA																					
O2329	0.5	4/7/2016	ND	NFA																					
O2330	0.5	4/7/2016	0.169J	NFA																					
O2331	0.5	4/7/2016	8.0	Step out 25 ft. in 4 directions and retest	O2331-N25	0.5	4/25/2016	21	Step out 10 ft. and retest	O2331-N35	0.5	5/12/2016	[illegible]	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2504-S25 in same vicinity										
					O2331-E25	0.5	4/25/2016	4.9	Step out 10 ft. and retest	O2331-E35	0.5	5/12/2016	0.72	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2301 in same vicinity										
					O2331-S25	0.5	4/25/2016	7.3	Step out 10 ft. and retest	O2331-S35	0.5	5/12/2016	4.8	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2503-N25 in same vicinity										
					O2331-W25	0.5	4/25/2016	0.66	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2330 in same vicinity															
O2332	0.5	4/7/2016	ND	NFA																					
O2324	0.5	4/7/2016	3.9	Step out 25 ft. in 4 directions and retest	O2324-N25	0.5	4/25/2016	0.018J	NFA																
					O2324-S25	0.5	4/25/2016	3.1	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O1735-N20 in same vicinity															
					O2324-W25	0.5	4/25/2016	0.049	NFA																
					No east step-out sample collected due to presence of sample O2505-W25 at same locatior																				
O2501	0.5	4/7/2016	1.44	Step out 25 ft. in 4 directions and retest	O2501-N25	0.5	4/18/2016	2.8	Step out 10 ft. and retest	O2501-N35	0.5	5/2/2016	0.88	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2503-S25 in same vicinity										
					O2501-E25	0.5	4/18/2016	7.4	Step out 10 ft. and retest	O2501-E35	0.5	5/2/2016	0.14	NFA											
					O2501-S25	0.5	4/18/2016	0.45	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2502-N25 at same location															
					O2501-W25	0.5	4/18/2016	43	Step out 10 ft. and retest	O2501-W35	0.5	5/2/2016	1.9	Step out 10 ft. and retest	No step-out sample collected due to presence of sample O2332 in same vicinity										

Notes: NFA = No further action. Result is <0.22 mg/kg.
mg/kg = milligrams per kilogram
fbg = feet below grade

LEGEND

1732 0.18 PCB Sample Location (Total PCBs < 0.22 mg/kg)

1731 131 PCB Sample Location (Total PCBs ≥ 0.22 mg/kg)

Cut Lots (39 total)

Fill Lots (70 total)

Outside Area Samples 2016



Cut Lot Samples 2016



Fill Lot Samples 2016



NOTES:

PCB concentrations shown represent the highest value from the two different laboratory extraction methods (Soxhlet and Method 3545).

REV	DATE	BY	APP	DESCRIPTION	DATE
	04/12/2016			DRAFT - ISSUED FOR REVIEW	

DESIGNED	DATE	DRAWN BY	DATE	CHECKED	DATE
R.S.	12/17/15	R.M.C.	12/17/15	R.S.	12/17/15

TRC
5 RESEARCH DRIVE
IRVINE, CALIFORNIA

PROJECT:

FACILITY: FORMER AGRICULTURAL PARK
REST AVENUE
RIVERSIDE, CALIFORNIA

TITLE: SOIL SAMPLE LOCATIONS

REVISION:

SHEET: 5

FILE NAME: FRA RIVERSIDE-SP-REV2016.dwg

DATE: 04/12/2016

Page 3 of 4

L:\Graphics\Projects\by\Name\Riverside-FRA\CADD\FRA RIVERSIDE-SP-Phase-rev2.dwg May 31, 2016 - 3:29pm rcollins
