# Gorge Dam Project Schedule_10222021

| ID | % Complete | Task Mode | Task Name | Duration | Start | Finish |
|---|---|---|---|---|---|---|
| 1 | 56% | | **Gorge Dam Remedial Design** | **1489 days** | **Fri 7/20/18** | **Tue 8/16/22** |
| 2 | 78% | | **Task NB - Proposal Task** | **1139 days** | **Fri 7/20/18** | **Tue 8/31/21** |
| 38 | 61% | | **Task 1 - Project Planning and Management** | **1389 days** | **Tue 9/11/18** | **Thu 6/30/22** |
| 55 | 1% | | **Task 2 - Community Involvement** | **946 days** | **Fri 5/31/19** | **Fri 12/31/21** |
| 57 | 92% | | **Task 3 - Field Investigation/Data Acquisition** | **798 days** | **Wed 9/25/19** | **Tue 11/30/21** |
| 58 | ✓ 100% | | **Amendment 1 Field Work** | **577 days** | **Wed 9/25/19** | **Fri 4/23/21** |
| 73 | ✓ 100% | | **Amendment 3 Field Work** | **200 days** | **Tue 9/15/20** | **Fri 4/2/21** |
| 77 | ✓ 100% | | **Amendment 4 Field Work** | **109 days** | **Mon 3/15/21** | **Thu 7/1/21** |
| 83 | 71% | | **Amendment 5 Field Work** | **114 days** | **Mon 8/9/21** | **Tue 11/30/21** |
| 84 | 71% | | **Power Plant Area Forensic Engineering Investigation** | **114 days** | **Mon 8/9/21** | **Tue 11/30/21** |
| 85 | ✓ 100% | | EPA Funding Received | 0 days | Mon 8/9/21 | Mon 8/9/21 |
| 86 | ✓ 100% | | EPA Approval of Amendment 5 | 0 days | Tue 8/31/21 | Tue 8/31/21 |
| 87 | 90% | | City of Akron Access Agreement (EPA Task) | 40 days | Mon 8/9/21 | Fri 9/17/21 |
| 88 | 91% | | **Subcontractor Procurement** | **39 days** | **Tue 8/17/21** | **Fri 9/24/21** |
| 95 | 53% | | **Pre-Mobilization and Mobilization Tasks** | **49 days** | **Tue 8/17/21** | **Mon 10/4/21** |
| 128 | 44% | | **Amendment 5 Field Work** | **72 days** | **Mon 9/20/21** | **Tue 11/30/21** |
| 129 | ✓ 100% | | **Mobilization 1** | **19 days** | **Mon 9/20/21** | **Fri 10/8/21** |
| 135 | 10% | | **Mobilization 2** | **43 days** | **Tue 10/19/21** | **Tue 11/30/21** |
| 136 | ✓ 100% | | Third Party Utility Locate | 1 day | Tue 10/19/21 | Tue 10/19/21 |
| 137 | ✓ 100% | | Mat and Aggregate Placement | 3 days | Wed 10/20/21 | Fri 10/22/21 |
| 138 | 0% | | Geotech Drilling | 10 days | Mon 10/25/21 | Wed 11/3/21 |
| 139 | 0% | | Break | 4 days | Thu 11/4/21 | Sun 11/7/21 |
| 140 | 0% | | Geotech Drilling | 17 days | Mon 11/8/21 | Wed 11/24/21 |
| 141 | 0% | | Parallel Seismic Testing | 5 days | Mon 11/15/21 | Fri 11/19/21 |
| 142 | 0% | | Mat Removal & Borehole Abandonment | 2 days | Mon 11/29/21 | Tue 11/30/21 |
| 143 | 84% | | **Task 4 - Sample Analysis** | **808 days** | **Sat 11/16/19** | **Mon 1/31/22** |
| 144 | ✓ 100% | | **Amendment 1 Geotechnical and Analytical Testing** | **63 days** | **Sat 11/16/19** | **Fri 1/17/20** |
| 149 | ✓ 100% | | **Amendment 1 Sediment Bench Scale Testing** | **62 days** | **Mon 12/9/19** | **Sat 2/8/20** |
| 156 | ✓ 100% | | **Amendment 4 Analytical Testing** | **19 days** | **Thu 6/24/21** | **Mon 7/12/21** |
| 158 | ✓ 100% | | **Amendment 4 Geotechnical Testing** | **102 days** | **Fri 7/9/21** | **Mon 10/18/21** |
| 161 | 0% | | **Amendment 5 Geotechnical Testing** | **66 days** | **Sat 11/27/21** | **Mon 1/31/22** |
| 162 | 0% | | Laboratory Analysis | 52 days | Sat 11/27/21 | Mon 1/17/22 |
| 163 | 0% | | Reporting | 14 days | Tue 1/18/22 | Mon 1/31/22 |
| 164 | 85% | | **Task 5 - Analytical Support and Data Validation** | **614 days** | **Mon 1/20/20** | **Fri 9/24/21** |
| 165 | ✓ 100% | | **Amendment 1** | **82 days** | **Mon 1/20/20** | **Fri 4/10/20** |
| 169 | 68% | | **Amendment 4** | **74 days** | **Tue 7/13/21** | **Fri 9/24/21** |
| 170 | ✓ 100% | | Data Validation | 32 days | Tue 7/13/21 | Fri 8/13/21 |
| 171 | 43% | | Prepare Data Validation Report | 40 days | Mon 8/16/21 | Fri 9/24/21 |
| 172 | 84% | | **Task 6 - Data Evaluation** | **848 days** | **Mon 11/18/19** | **Mon 3/14/22** |
| 173 | ✓ 100% | | **Electronic Data Deliverable** | **126 days** | **Sat 12/7/19** | **Fri 4/10/20** |
| 176 | ✓ 100% | | **Amendment 2 Data Summary Report** | **173 days** | **Mon 11/18/19** | **Fri 5/8/20** |
| 185 | 0% | | **Amendment 4 Data Evaluation** | **22 days** | **Mon 10/25/21** | **Mon 11/15/21** |
| 186 | 0% | | Field Data Summary Report | 22 days | Mon 10/25/21 | Mon 11/15/21 |
| 187 | 0% | | **Amendment 5 Data Evaluation** | **42 days** | **Tue 2/1/22** | **Mon 3/14/22** |
| 188 | 0% | | Data Useability | 5 days | Tue 2/1/22 | Sat 2/5/22 |
| 189 | 0% | | Field Data Summary Report | 42 days | Tue 2/1/22 | Mon 3/14/22 |
| 190 | ✓ 100% | | **Task 7 - Preliminary Design** | **198 days** | **Thu 2/13/20** | **Fri 8/28/20** |
| 220 | 8% | | **Task 8 - Pre-Final/Final Design** | **563 days** | **Wed 1/6/21** | **Fri 7/22/22** |
| 221 | 9% | | **Pre-Final Design** | **514 days** | **Wed 1/6/21** | **Fri 6/3/22** |
| 222 | 21% | | **Prepare 90% Sediment Remediation Design** | **454 days** | **Wed 1/6/21** | **Mon 4/4/22** |
| 223 | ✓ 100% | | Front Street Bridge Evaluation | 73 days | Wed 1/6/21 | Fri 3/19/21 |
| 224 | 0% | | First Energy Bulkhead Wall Evaluation | 44 days | Mon 11/22/21 | Tue 1/4/22 |
| 225 | 0% | | Preparation of Prefinal Design Drawings | 62 days | Wed 1/5/22 | Mon 3/7/22 |
| 226 | 0% | | Preparation of Prefinal Design Specification Packages | 62 days | Wed 1/5/22 | Mon 3/7/22 |
| 227 | 0% | | Update Basis of Design Report | 62 days | Wed 1/5/22 | Mon 3/7/22 |
| 228 | 0% | | Prefinal Cost Estimates | 18 days | Fri 2/18/22 | Mon 3/7/22 |
| 229 | 0% | | **Internal CH2M Review** | **28 days** | **Tue 3/8/22** | **Mon 4/4/22** |
| 230 | 0% | | Design Manager Approval of Prefinal Design Drawings | 2 days | Tue 3/8/22 | Wed 3/9/22 |
| 231 | 0% | | Design Manager Approval of Prefinal Design Specification Packages | 2 days | Tue 3/8/22 | Wed 3/9/22 |
| 232 | 0% | | Senior Review of Prefinal Design Drawings and Specificatic | 8 days | Thu 3/10/22 | Thu 3/17/22 |
| 233 | 0% | | Senior Review Comment Adjudication | 9 days | Mon 3/21/22 | Tue 3/29/22 |
| 234 | 0% | | Incorporate Comments and Finalize Documents | 6 days | Wed 3/30/22 | Mon 4/4/22 |
| 235 | 0% | | **Prepare 90% Disposal Area Design** | **113 days** | **Mon 12/27/21** | **Mon 4/18/22** |
| 236 | 0% | | Preparation of Prefinal Design Drawings | 85 days | Mon 12/27/21 | Mon 3/21/22 |
| 237 | 0% | | Preparation of Prefinal Design Specification Packages | 85 days | Mon 12/27/21 | Mon 3/21/22 |
| 238 | 0% | | Ground Improvements Design | 85 days | Mon 12/27/21 | Mon 3/21/22 |
| 239 | 0% | | Update Basis of Design Report | 85 days | Mon 12/27/21 | Mon 3/21/22 |
| 240 | 0% | | Prefinal Cost Estimates | 18 days | Fri 3/4/22 | Mon 3/21/22 |
| 241 | 0% | | **Internal CH2M Review** | **28 days** | **Tue 3/22/22** | **Mon 4/18/22** |
| 242 | 0% | | Design Manager Approval of Prefinal Design Drawings | 2 days | Tue 3/22/22 | Wed 3/23/22 |
| 243 | 0% | | Design Manager Approval of Prefinal Design Specification Packages | 2 days | Tue 3/22/22 | Wed 3/23/22 |
| 244 | 0% | | Senior Review of Prefinal Design Drawings and Specificatic | 8 days | Thu 3/24/22 | Thu 3/31/22 |
| 245 | 0% | | Senior Review Comment Adjudication | 9 days | Mon 4/4/22 | Tue 4/12/22 |
| 246 | 0% | | Incorporate Comments and Finalize Documents | 6 days | Wed 4/13/22 | Mon 4/18/22 |
| 247 | 0% | | Submit 90% Designs | 0 days | Mon 4/18/22 | Mon 4/18/22 |
| 248 | 0% | | EPA and Partners Review | 35 days | Tue 4/19/22 | Mon 5/23/22 |
| 249 | 0% | | Design Review Meeting | 1 day | Wed 4/27/22 | Wed 4/27/22 |
| 250 | 0% | | Prepare RTC on 90% Designs | 11 days | Tue 5/24/22 | Fri 6/3/22 |
| 251 | 0% | | **Final Design** | **47 days** | **Mon 6/6/22** | **Fri 7/22/22** |
| 252 | 0% | | **Prepare 100% Sediment Remedation Design** | **47 days** | **Mon 6/6/22** | **Fri 7/22/22** |
| 253 | 0% | | Preparation of Final Design Drawings | 19 days | Mon 6/6/22 | Fri 6/24/22 |
| 254 | 0% | | Preparation of Final Design Specification Packages | 19 days | Mon 6/6/22 | Fri 6/24/22 |
| 255 | 0% | | Update Basis of Design Report | 19 days | Mon 6/6/22 | Fri 6/24/22 |
| 256 | 0% | | **Internal CH2M Review** | **26 days** | **Mon 6/27/22** | **Fri 7/22/22** |
| 257 | 0% | | Design Manager Approval of Final Design Drawings | 3 days | Mon 6/27/22 | Wed 6/29/22 |
| 258 | 0% | | Design Manager Approval of Final Design Specification Package | 3 days | Mon 6/27/22 | Wed 6/29/22 |
| 259 | 0% | | Senior Review of Prefinal Design Drawings and Specificatic | 8 days | Thu 6/30/22 | Thu 7/7/22 |
| 260 | 0% | | Senior Review Comment Adjudication | 8 days | Fri 7/8/22 | Fri 7/15/22 |
| 261 | 0% | | Incorporate Comments and Finalize Documents | 5 days | Mon 7/18/22 | Fri 7/22/22 |
| 262 | 0% | | **Prepare 100% Disposal Area Design** | **40 days** | **Mon 6/6/22** | **Fri 7/15/22** |
| 263 | 0% | | Preparation of Final Design Drawings | 19 days | Mon 6/6/22 | Fri 6/24/22 |
| 264 | 0% | | Preparation of Final Design Specification Packages | 19 days | Mon 6/6/22 | Fri 6/24/22 |
| 265 | 0% | | Update Basis of Design Report | 19 days | Mon 6/6/22 | Fri 6/24/22 |
| 266 | 0% | | **Internal CH2M Review** | **19 days** | **Mon 6/27/22** | **Fri 7/15/22** |
| 267 | 0% | | Design Manager Approval of Final Design Drawings | 2 days | Mon 6/27/22 | Tue 6/28/22 |
| 268 | 0% | | Design Manager Approval of Final Design Specification Package | 2 days | Mon 6/27/22 | Tue 6/28/22 |
| 269 | 0% | | Senior Review of Prefinal Design Drawings and Specificatic | 5 days | Wed 6/29/22 | Sun 7/3/22 |
| 270 | 0% | | Senior Review Comment Adjudication | 5 days | Mon 7/4/22 | Fri 7/8/22 |
| 271 | 0% | | Incorporate Comments and Finalize Documents | 5 days | Mon 7/11/22 | Fri 7/15/22 |
| 272 | 0% | | Submit 100% Designs | 0 days | Fri 7/22/22 | Fri 7/22/22 |
| 273 | 0% | | **Task 9 - Prepare/Submit Permit Applications, Licenses, Access Agreements, and Certifications** | **116 days** | **Tue 3/22/22** | **Fri 7/15/22** |
| 274 | 0% | | Prepare Applications | 28 days | Tue 3/22/22 | Mon 4/18/22 |
| 275 | 0% | | Submit Draft Applications w/ 90% design | 0 days | Mon 4/18/22 | Mon 4/18/22 |
| 276 | 0% | | EPA and Partners Review | 35 days | Tue 4/19/22 | Mon 5/23/22 |
| 277 | 0% | | Respond to Comments | 53 days | Tue 5/24/22 | Fri 7/15/22 |
| 278 | 0% | | Submit Final Applications w/ 100% design | 0 days | Fri 7/15/22 | Fri 7/15/22 |
| 279 | 0% | | **Task 11 - Task Order Closeout** | **30 days** | **Mon 7/18/22** | **Tue 8/16/22** |
| 282 | 0% | | **Task 12 - Design Support** | **61 days** | **Mon 10/25/21** | **Fri 12/24/21** |
| 283 | 0% | | Geotechnical Issues – Ground Conditions | 33 days | Mon 10/25/21 | Fri 11/26/21 |
| 284 | 0% | | Geotechnical Issues – Utility Evaluations | 26 days | Mon 11/29/21 | Fri 12/24/21 |

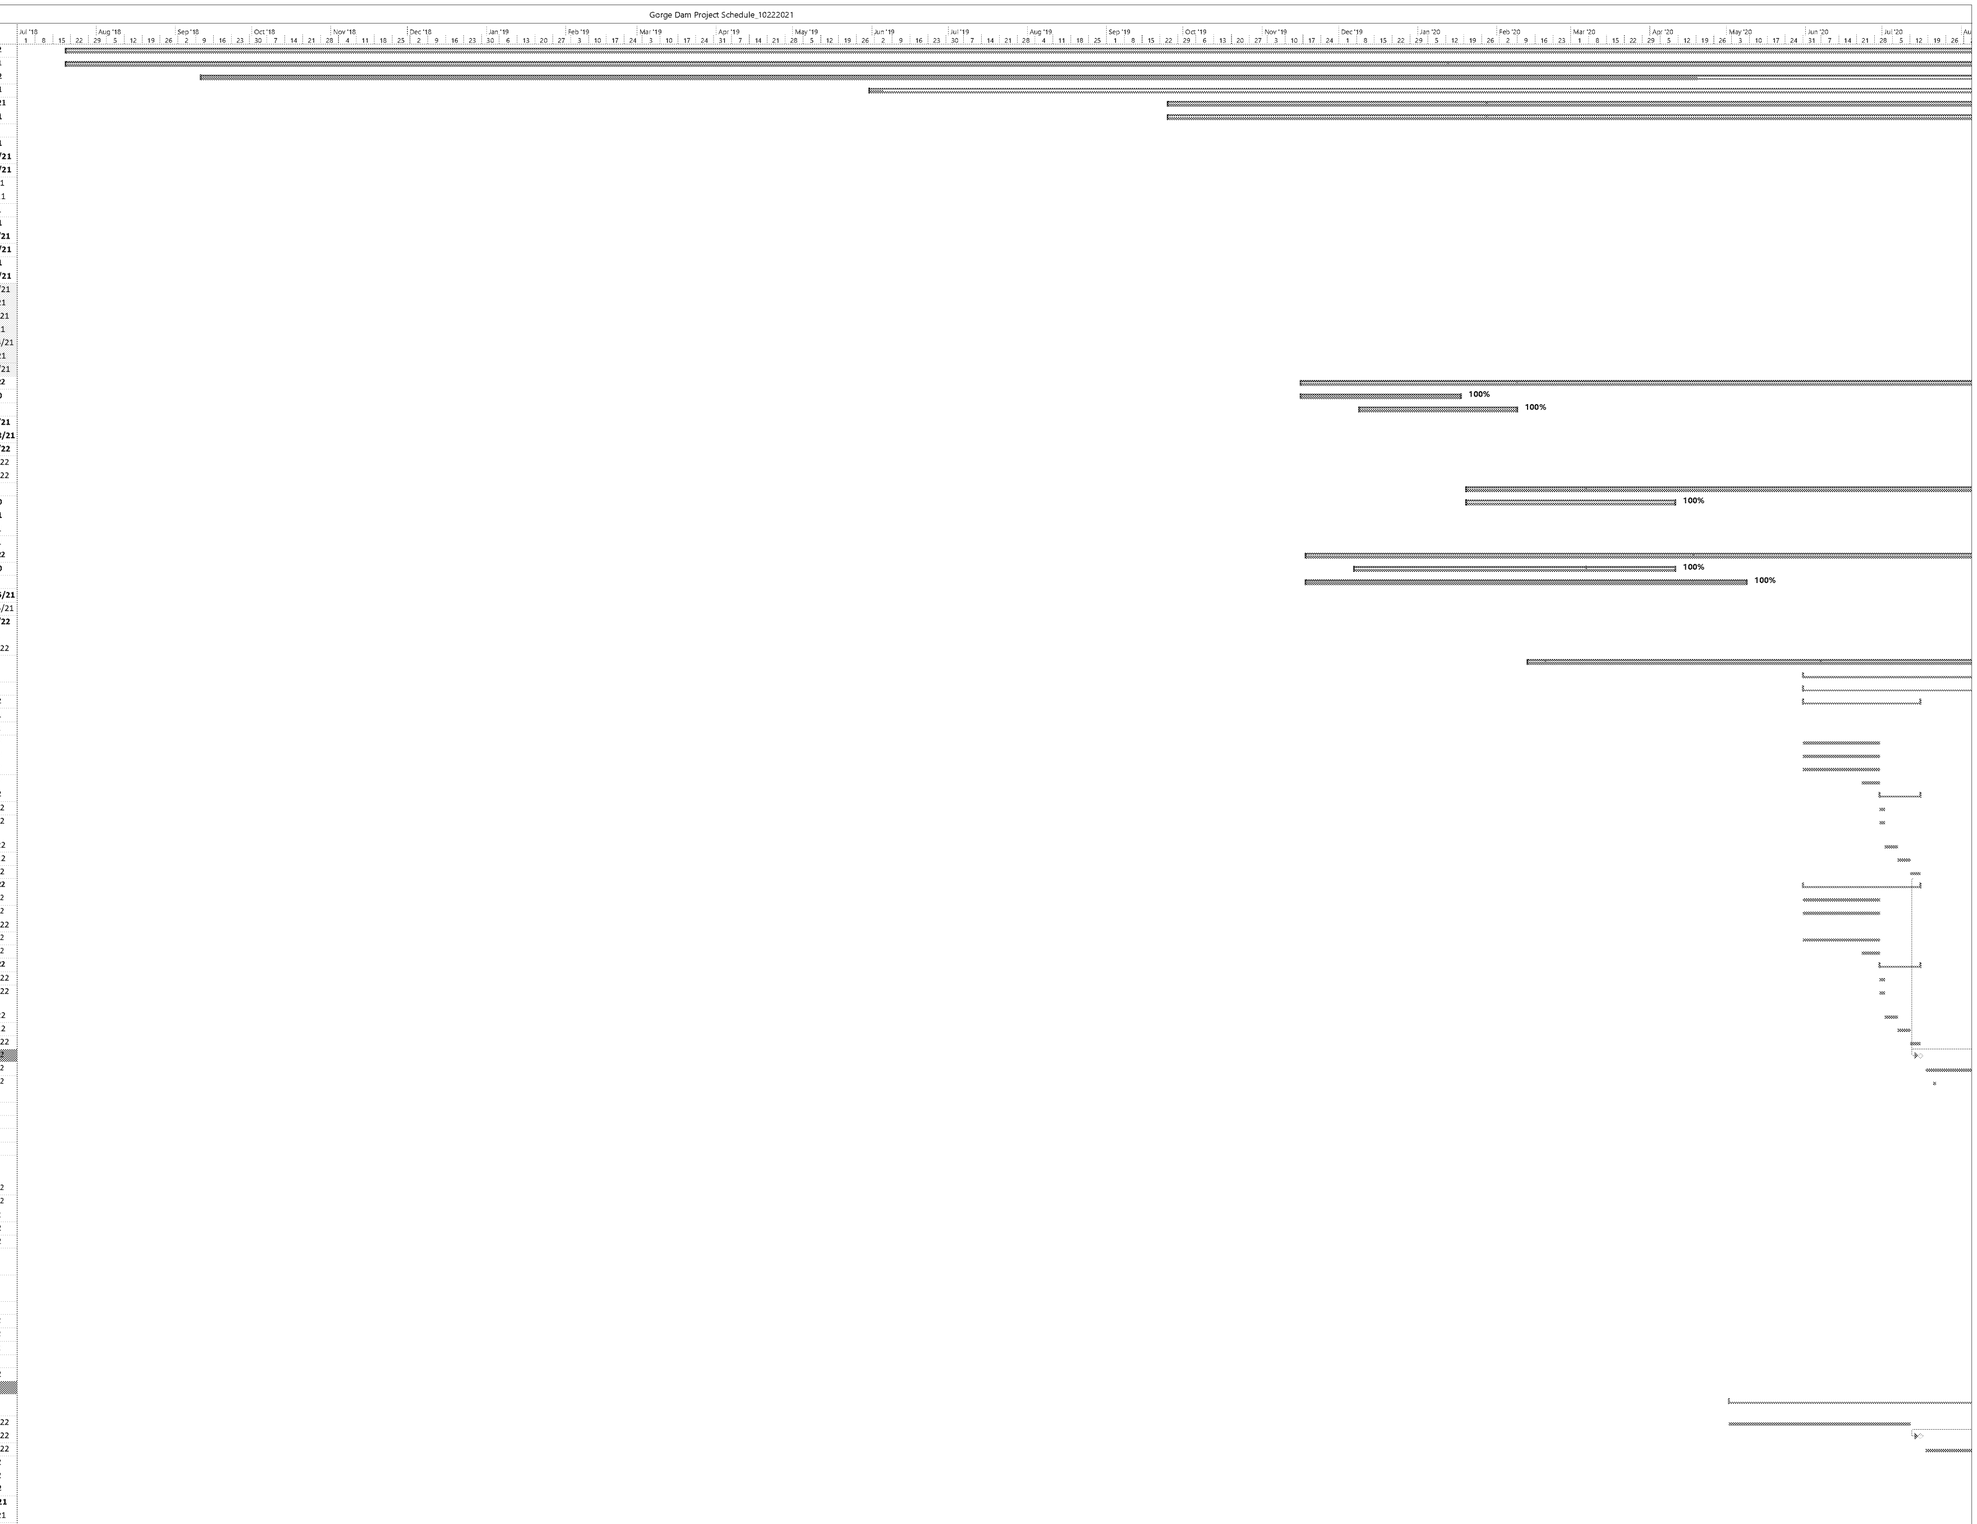

Gorge Dam Project Schedule_10222021

| ID | % Complete | Task Name | Duration | Start | Finish |
|---|---|---|---|---|---|
| 1 | 56% | **Gorge Dam Remedial Design** | **1489 days** | **Fri 7/20/18** | **Tue 8/16/22** |
| 2 | 78% | **Task NB - Proposal Task** | **1139 days** | **Fri 7/20/18** | **Tue 8/31/21** |
| 38 | 61% | **Task 1 - Project Planning and Management** | **1389 days** | **Tue 9/11/18** | **Thu 6/30/22** |
| 55 | 1% | **Task 2 - Community Involvement** | **946 days** | **Fri 5/31/19** | **Fri 12/31/21** |
| 57 | 92% | **Task 3 - Field Investigation/Data Acquisition** | **798 days** | **Wed 9/25/19** | **Tue 11/30/21** |
| 58 | 100% | **Amendment 1 Field Work** | **577 days** | **Wed 9/25/19** | **Fri 4/23/21** |
| 73 | 100% | **Amendment 3 Field Work** | **200 days** | **Tue 9/15/20** | **Fri 4/2/21** |
| 77 | 100% | **Amendment 4 Field Work** | **109 days** | **Mon 3/15/21** | **Thu 7/1/21** |
| 83 | 71% | **Amendment 5 Field Work** | **114 days** | **Mon 8/9/21** | **Tue 11/30/21** |
| 84 | 71% | **Power Plant Area Forensic Engineering Investigation** | **114 days** | **Mon 8/9/21** | **Tue 11/30/21** |
| 85 | 100% | EPA Funding Received | 0 days | Mon 8/9/21 | Mon 8/9/21 |
| 86 | 100% | EPA Approval of Amendment 5 | 0 days | Tue 8/31/21 | Tue 8/31/21 |
| 87 | 90% | City of Akron Access Agreement (EPA Task) | 40 days | Mon 8/9/21 | Fri 9/17/21 |
| 88 | 91% | **Subcontractor Procurement** | **39 days** | **Tue 8/17/21** | **Fri 9/24/21** |
| 95 | 53% | **Pre-Mobilization and Mobilization Tasks** | **49 days** | **Tue 8/17/21** | **Mon 10/4/21** |
| 128 | 44% | **Amendment 5 Field Work** | **72 days** | **Mon 9/20/21** | **Tue 11/30/21** |
| 129 | 100% | **Mobilization 1** | **19 days** | **Mon 9/20/21** | **Fri 10/8/21** |
| 135 | 10% | **Mobilization 2** | **43 days** | **Tue 10/19/21** | **Tue 11/30/21** |
| 136 | 100% | Third Party Utility Locate | 1 day | Tue 10/19/21 | Tue 10/19/21 |
| 137 | 100% | Mat and Aggregate Placement | 3 days | Wed 10/20/21 | Fri 10/22/21 |
| 138 | 0% | Geotech Drilling | 10 days | Mon 10/25/21 | Wed 11/3/21 |
| 139 | 0% | Break | 4 days | Thu 11/4/21 | Sun 11/7/21 |
| 140 | 0% | Geotech Drilling | 17 days | Mon 11/8/21 | Wed 11/24/21 |
| 141 | 0% | Parallel Seismic Testing | 5 days | Mon 11/15/21 | Fri 11/19/21 |
| 142 | 0% | Mat Removal & Borehole Abandonment | 2 days | Mon 11/29/21 | Tue 11/30/21 |
| 143 | 84% | **Task 4 - Sample Analysis** | **808 days** | **Sat 11/16/19** | **Mon 1/31/22** |
| 144 | 100% | **Amendment 1 Geotechnical and Analytical Testing** | **63 days** | **Sat 11/16/19** | **Fri 1/17/20** |
| 149 | 100% | **Amendment 1 Sediment Bench Scale Testing** | **62 days** | **Mon 12/9/19** | **Sat 2/8/20** |
| 156 | 100% | **Amendment 4 Analytical Testing** | **19 days** | **Thu 6/24/21** | **Mon 7/12/21** |
| 158 | 100% | **Amendment 4 Geotechnical Testing** | **102 days** | **Fri 7/9/21** | **Mon 10/18/21** |
| 161 | 0% | **Amendment 5 Geotechnical Testing** | **66 days** | **Sat 11/27/21** | **Mon 1/31/22** |
| 162 | 0% | Laboratory Analysis | 52 days | Sat 11/27/21 | Mon 1/17/22 |
| 163 | 0% | Reporting | 14 days | Tue 1/18/22 | Mon 1/31/22 |
| 164 | 85% | **Task 5 - Analytical Support and Data Validation** | **614 days** | **Mon 1/20/20** | **Fri 9/24/21** |
| 165 | 100% | **Amendment 1** | **82 days** | **Mon 1/20/20** | **Fri 4/10/20** |
| 169 | 68% | **Amendment 4** | **74 days** | **Tue 7/13/21** | **Fri 9/24/21** |
| 170 | 100% | Data Validation | 32 days | Tue 7/13/21 | Fri 8/13/21 |
| 171 | 43% | Prepare Data Validation Report | 40 days | Mon 8/16/21 | Fri 9/24/21 |
| 172 | 84% | **Task 6 - Data Evaluation** | **848 days** | **Mon 11/18/19** | **Mon 3/14/22** |
| 173 | 100% | **Electronic Data Deliverable** | **126 days** | **Sat 12/7/19** | **Fri 4/10/20** |
| 176 | 100% | **Amendment 2 Data Summary Report** | **173 days** | **Mon 11/18/21** | **Fri 5/8/20** |
| 185 | 0% | **Amendment 4 Data Evaluation** | **22 days** | **Mon 10/25/21** | **Mon 11/15/21** |
| 186 | 0% | Field Data Summary Report | 22 days | Mon 10/25/21 | Mon 11/15/21 |
| 187 | 0% | **Amendment 5 Data Evaluation** | **42 days** | **Tue 2/1/22** | **Mon 3/14/22** |
| 188 | 0% | Data Useability | 5 days | Tue 2/1/22 | Sat 2/5/22 |
| 189 | 0% | Field Data Summary Report | 42 days | Tue 2/1/22 | Mon 3/14/22 |
| 190 | 100% | **Task 7 - Preliminary Design** | **198 days** | **Thu 2/13/20** | **Fri 8/28/20** |
| 220 | 8% | **Task 8 - Pre-Final/Final Design** | **563 days** | **Wed 1/6/21** | **Fri 7/22/22** |
| 221 | 9% | **Pre-Final Design** | **514 days** | **Wed 1/6/21** | **Fri 6/3/22** |
| 222 | 21% | **Prepare 90% Sediment Remediation Design** | **454 days** | **Wed 1/6/21** | **Mon 4/4/22** |
| 223 | 100% | Front Street Bridge Evaluation | 73 days | Wed 1/6/21 | Fri 3/19/21 |
| 224 | 0% | First Energy Bulkhead Wall Evaluation | 44 days | Mon 11/22/21 | Tue 1/4/22 |
| 225 | 0% | Preparation of Prefinal Design Drawings | 62 days | Wed 1/5/22 | Mon 3/7/22 |
| 226 | 0% | Preparation of Prefinal Design Specification Packages | 62 days | Wed 1/5/22 | Mon 3/7/22 |
| 227 | 0% | Upcate Basis of Design Report | 62 days | Wed 1/5/22 | Mon 3/7/22 |
| 228 | 0% | Prefinal Cost Estimates | 18 days | Fri 2/18/22 | Mon 3/7/22 |
| 229 | 0% | **Internal CH2M Review** | **28 days** | **Tue 3/8/22** | **Mon 4/4/22** |
| 230 | 0% | Design Manager Approval of Prefinal Design Drawings | 2 days | Tue 3/8/22 | Wed 3/9/22 |
| 231 | 0% | Design Manager Approval of Prefinal Design Specification Packages | 2 days | Tue 3/8/22 | Wed 3/9/22 |
| 232 | 0% | Senior Review of Prefinal Design Drawings and Specificatic | 8 days | Thu 3/10/22 | Thu 3/17/22 |
| 233 | 0% | Senior Review Comment Adjudication | 9 days | Mon 3/21/22 | Tue 3/29/22 |
| 234 | 0% | Incorporate Comments and Finalize Documents | 6 days | Wed 3/30/22 | Mon 4/4/22 |
| 235 | 0% | **Prepare 90% Disposal Area Design** | **113 days** | **Mon 12/27/21** | **Mon 4/18/22** |
| 236 | 0% | Preparation of Prefinal Design Drawings | 85 days | Mon 12/27/21 | Mon 3/21/22 |
| 237 | 0% | Preparation of Prefinal Design Specification Packages | 85 days | Mon 12/27/21 | Mon 3/21/22 |
| 238 | 0% | Ground Improvements Design | 85 days | Mon 12/27/21 | Mon 3/21/22 |
| 239 | 0% | Upcate Basis of Design Report | 85 days | Mon 12/27/21 | Mon 3/21/22 |
| 240 | 0% | Prefinal Cost Estimates | 18 days | Fri 3/4/22 | Mon 3/21/22 |
| 241 | 0% | **Internal CH2M Review** | **28 days** | **Tue 3/22/22** | **Mon 4/18/22** |
| 242 | 0% | Design Manager Approval of Prefinal Design Drawings | 2 days | Tue 3/22/22 | Wed 3/23/22 |
| 243 | 0% | Design Manager Approval of Prefinal Design Specification Packages | 2 days | Tue 3/22/22 | Wed 3/23/22 |
| 244 | 0% | Senior Review of Prefinal Design Drawings and Specificatic | 8 days | Thu 3/24/22 | Thu 3/31/22 |
| 245 | 0% | Senior Review Comment Adjudication | 9 days | Mon 4/4/22 | Tue 4/12/22 |
| 246 | 0% | Incorporate Comments and Finalize Documents | 6 days | Wed 4/13/22 | Mon 4/18/22 |
| 247 | 0% | Submit 90% Designs | 0 days | Mon 4/18/22 | Mon 4/18/22 |
| 248 | 0% | EPA and Partners Review | 35 days | Tue 4/19/22 | Mon 5/23/22 |
| 249 | 0% | Design Review Meeting | 1 day | Wed 4/27/22 | Wed 4/27/22 |
| 250 | 0% | Prepare RTC on 90% Designs | 11 days | Tue 5/24/22 | Fri 6/3/22 |
| 251 | 0% | **Final Design** | **47 days** | **Mon 6/6/22** | **Fri 7/22/22** |
| 252 | 0% | **Prepare 100% Sediment Remedation Design** | **47 days** | **Mon 6/6/22** | **Fri 7/22/22** |
| 253 | 0% | Preparation of Final Design Drawings | 19 days | Mon 6/6/22 | Fri 6/24/22 |
| 254 | 0% | Preparation of Final Design Specification Packages | 19 days | Mon 6/6/22 | Fri 6/24/22 |
| 255 | 0% | Upcate Basis of Design Report | 19 days | Mon 6/6/22 | Fri 6/24/22 |
| 256 | 0% | **Internal CH2M Review** | **26 days** | **Mon 6/27/22** | **Fri 7/22/22** |
| 257 | 0% | Design Manager Approval of Final Design Drawings | 3 days | Mon 6/27/22 | Wed 6/29/22 |
| 258 | 0% | Design Manager Approval of Final Design Specification Package | 3 days | Mon 6/27/22 | Wed 6/29/22 |
| 259 | 0% | Senior Review of Prefinal Design Drawings and Specificatic | 8 days | Thu 6/30/22 | Thu 7/7/22 |
| 260 | 0% | Senior Review Comment Adjudication | 8 days | Fri 7/8/22 | Fri 7/15/22 |
| 261 | 0% | Incorporate Comments and Finalize Documents | 5 days | Mon 7/18/22 | Fri 7/22/22 |
| 262 | 0% | **Prepare 100% Disposal Area Design** | **40 days** | **Mon 6/6/22** | **Fri 7/15/22** |
| 263 | 0% | Preparation of Final Design Drawings | 19 days | Mon 6/6/22 | Fri 6/24/22 |
| 264 | 0% | Preparation of Final Design Specification Packages | 19 days | Mon 6/6/22 | Fri 6/24/22 |
| 265 | 0% | Upcate Basis of Design Report | 19 days | Mon 6/6/22 | Fri 6/24/22 |
| 266 | 0% | **Internal CH2M Review** | **19 days** | **Mon 6/27/22** | **Fri 7/15/22** |
| 267 | 0% | Design Manager Approval of Final Design Drawings | 2 days | Mon 6/27/22 | Tue 6/28/22 |
| 268 | 0% | Design Manager Approval of Final Design Specification Package | 2 days | Mon 6/27/22 | Tue 6/28/22 |
| 269 | 0% | Senior Review of Prefinal Design Drawings and Specificatic | 5 days | Wed 6/29/22 | Sun 7/3/22 |
| 270 | 0% | Senior Review Comment Adjudication | 5 days | Mon 7/4/22 | Fri 7/8/22 |
| 271 | 0% | Incorporate Comments and Finalize Documents | 5 days | Mon 7/11/22 | Fri 7/15/22 |
| 272 | 0% | Submit 100% Designs | 0 days | Fri 7/22/22 | Fri 7/22/22 |
| 273 | 0% | **Task 9 - Prepare/Submit Permit Applications, Licenses, Access Agreements, and Certifications** | **116 days** | **Tue 3/22/22** | **Fri 7/15/22** |
| 274 | 0% | Prepare Applications | 28 days | Tue 3/22/22 | Mon 4/18/22 |
| 275 | 0% | Submit Draft Applications w/ 90% design | 0 days | Mon 4/18/22 | Mon 4/18/22 |
| 276 | 0% | EPA and Partners Review | 35 days | Tue 4/19/22 | Mon 5/23/22 |
| 277 | 0% | Respond to Comments | 53 days | Tue 5/24/22 | Fri 7/15/22 |
| 278 | 0% | Submit Final Applications w/ 100% design | 0 days | Fri 7/15/22 | Fri 7/15/22 |
| 279 | 0% | **Task 11 - Task Order Closeout** | **30 days** | **Mon 7/18/22** | **Tue 8/16/22** |
| 282 | 0% | **Task 12 - Design Support** | **61 days** | **Mon 10/25/21** | **Fri 12/24/21** |
| 283 | 0% | Geotechnical Issues – Ground Conditions | 33 days | Mon 10/25/21 | Fri 11/26/21 |
| 284 | 0% | Geotechnical Issues – Utility Evaluations | 26 days | Mon 11/29/21 | Fri 12/24/21 |

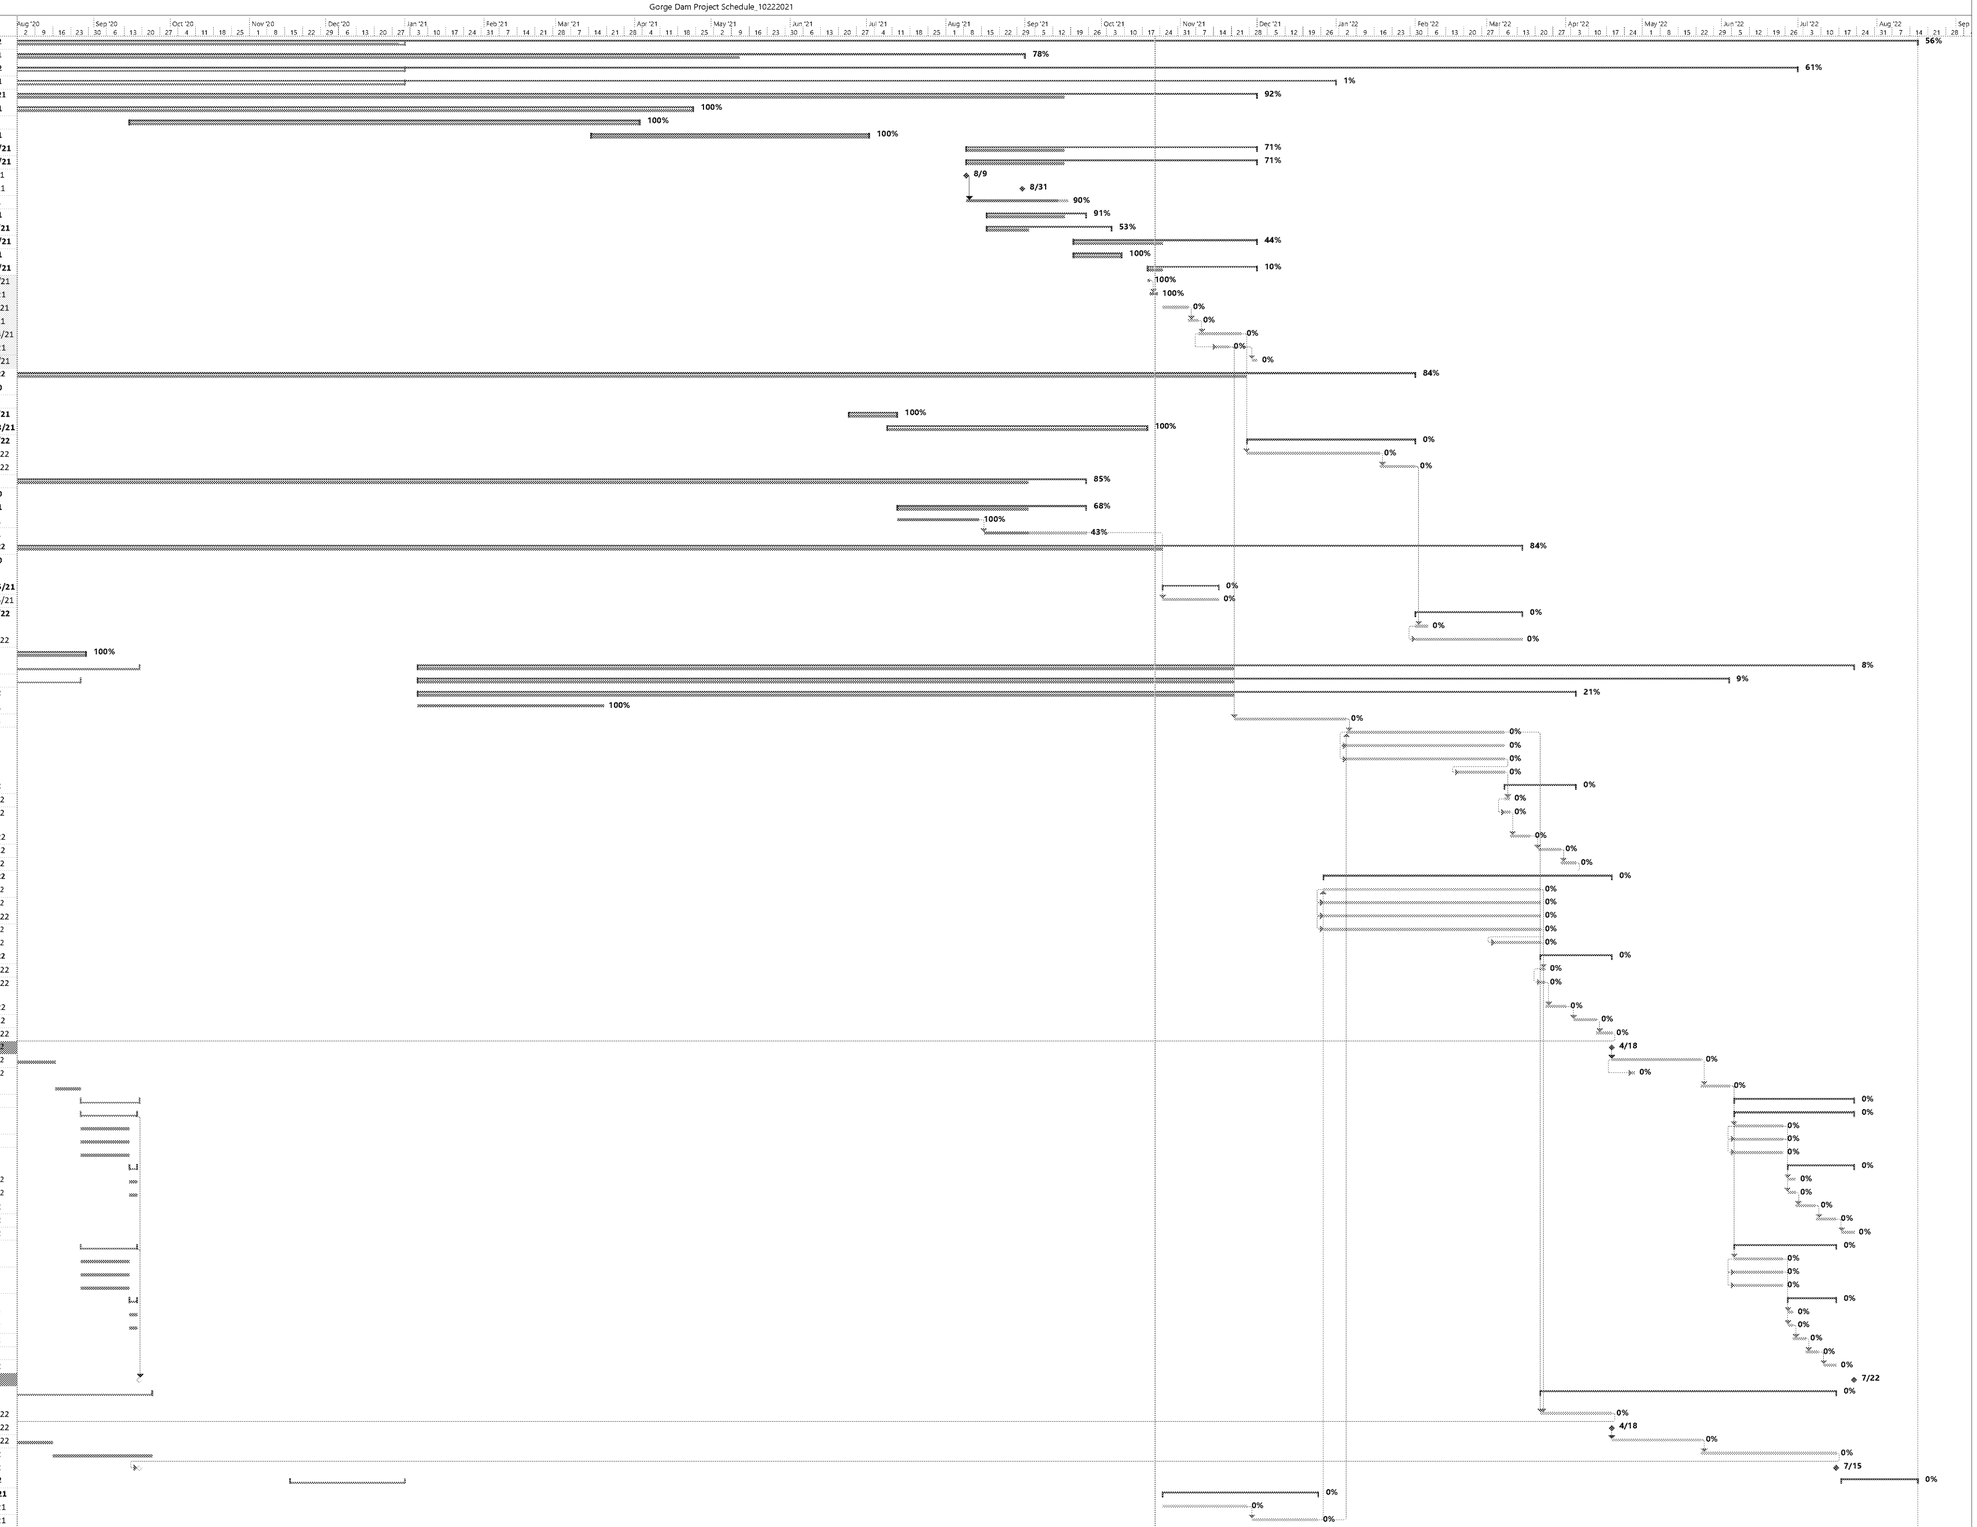


Gorge Dam Project Tracking Schedule
Fri 10/22/21

Baseline Milestone | Critical | Critical Progress | Split | Manual Task | Finish-only | Baseline Split | Summary Progress | Manual Summary | External Tasks | Inactive Task | Inactive Summary | Baseline
Baseline Summary | Critical Split | Task | Task Progress | Start-only | Duration-only | Milestone | Summary | Project Summary | External Milestone | Inactive Milestone | Deadline
