| ID | Task Name | Start | Finish | Predecessors | Duration |
|---|---|---|---|---|---|
| 0 | **Pebble EIS Milestone Schedule 02162018** | **Fri 2/16/18** | **Wed 4/15/20** | | **544 days** |
| 1 | **Project Start (NTP as Contract Negotiated)** | **Fri 2/16/18** | **Fri 2/16/18** | | **1 day** |
| 2 | **Task 1 - Project Management** | **Fri 2/16/18** | **Wed 4/15/20** | | **544 days** |
| 3 | Kick-off Meeting | Thu 2/22/18 | Thu 2/22/18 | 1SS+3 days | 1 day |
| 4 | **Project Work Plan** | **Fri 2/16/18** | **Tue 7/3/18** | | **96 days** |
| 5 | **Compile Draft Project Work Plan and Schedule** | **Fri 2/16/18** | **Fri 2/23/18** | **1SS** | **5 days** |
| 12 | USACE/PLP Approval | Mon 2/26/18 | Tue 2/27/18 | 5 | 2 days |
| 13 | Update/Amend Project Work Plan (post-scoping) | Wed 6/27/18 | Tue 7/3/18 | 268 | 5 days |
| 14 | **Project Management and Administration** | **Mon 2/19/18** | **Wed 4/15/20** | **3** | **543 days** |
| 15 | **Weekly Status Meeting/Teleconference** | **Tue 3/6/18** | **Tue 3/3/20** | | **502 days** |
| 121 | **Monthly Progress Report (and Invoice)** | **Mon 4/16/18** | **Wed 4/15/20** | | **504 days** |
| 147 | **Database Development & Maintenance (incl RFI tracking)** | **Mon 2/19/18** | **Wed 3/25/20** | **3** | **528 days** |
| 174 | **Task 2 - Scoping, Agency Coordination and Public Involvement** | **Tue 2/20/18** | **Tue 3/17/20** | | **522 days** |
| 175 | **Website Development & Maintenance** | **Tue 2/20/18** | **Tue 3/17/20** | | **522 days** |
| 176 | Develop Website and Mapping Interface | Tue 2/20/18 | Mon 3/19/18 | 1 | 20 days |
| 177 | **Update/Maintain Website and Mapping Interface** | **Tue 4/17/18** | **Tue 3/17/20** | | **482 days** |
| 202 | **Mailing List** | **Tue 2/20/18** | **Tue 1/21/20** | | **483 days** |
| 203 | Compile Initial List (statewide and Bristol Bay Tribes) | Tue 2/27/18 | Mon 3/12/18 | 148SS+5 days | 10 days |
| 204 | **Monthly Updates to Mailing List** | **Tue 2/20/18** | **Tue 1/21/20** | | **483 days** |
| 229 | **Public Scoping** | **Tue 2/20/18** | **Fri 4/27/18** | | **49 days** |
| 230 | **Notice of Intent (NOI)** | **Thu 2/22/18** | **Fri 4/27/18** | | **47 days** |
| 231 | Prepare NOI | Thu 2/22/18 | Wed 2/28/18 | 3SS | 5 days |
| 232 | USACE Review and Publish NOI | Thu 3/1/18 | Wed 3/28/18 | 231 | 20 days |
| 233 | NOI Published | Wed 3/28/18 | Wed 3/28/18 | 232 | 0 days |
| 234 | *Public Scoping Period* | *Wed 3/28/18* | *Fri 4/27/18* | *233* | *30 edays* |
| 235 | **Scoping Plan** | **Tue 2/20/18** | **Fri 3/16/18** | | **19 days** |
| 236 | Prepare Scoping Plan | Tue 2/20/18 | Wed 2/28/18 | 1,231FF | 7 days |
| 237 | USACE Review, Edit, Approve Scoping Plan | Thu 3/1/18 | Fri 3/2/18 | 236 | 2 days |
| 238 | Arrange/Secure Scoping Meeting Facilities | Mon 3/5/18 | Fri 3/16/18 | 237 | 10 days |
| 239 | **Scoping Information Package** | **Thu 2/22/18** | **Wed 3/28/18** | | **25 days** |
| 240 | Prepare Draft Scoping Information Package | Thu 2/22/18 | Wed 3/14/18 | 3SS | 15 days |
| 241 | USACE Review Scoping Information Package | Thu 3/15/18 | Wed 3/21/18 | 240 | 5 days |
| 242 | Finalize Scoping Information Package | Thu 3/22/18 | Wed 3/28/18 | 241,232FF | 5 days |
| 243 | **Newsletter #1** | **Thu 3/8/18** | **Wed 3/28/18** | | **15 days** |
| 244 | Prepare Draft Newsletter #1 | Thu 3/8/18 | Mon 3/12/18 | 240FS-5 days | 3 days |
| 245 | USACE Review Newsletter #1 | Tue 3/13/18 | Wed 3/14/18 | 244 | 2 days |
| 246 | Finalize and Publish Newsletter #1 | Thu 3/15/18 | Wed 3/28/18 | 232FF,245 | 10 days |
| 247 | **News Release #1** | **Thu 3/15/18** | **Wed 3/28/18** | | **10 days** |
| 248 | Prepare Draft News Release #1 | Thu 3/15/18 | Mon 3/19/18 | 240 | 3 days |
| 249 | USACE Review News Release #1 | Tue 3/20/18 | Wed 3/21/18 | 248 | 2 days |
| 250 | Finalize and Publish News Release #1 | Thu 3/22/18 | Wed 3/28/18 | 232FF,249 | 5 days |
| 251 | **Meeting Materials** | **Thu 3/22/18** | **Mon 4/16/18** | | **18 days** |
| 252 | Prepare Draft Meeting Materials (incl Fact Sheet, FAQs, comment form) | Thu 3/22/18 | Wed 4/4/18 | 241 | 10 days |
| 253 | USACE Review Meeting Materials | Thu 4/5/18 | Wed 4/11/18 | 252 | 5 days |
| 254 | Finalize and Produce Meeting Materials | Thu 4/12/18 | Mon 4/16/18 | 253 | 3 days |
| 255 | Public Scoping Meetings (10) | Wed 4/11/18 | Tue 4/24/18 | 232FS+9 days | 10 days |
| 256 | **Cooperating Agency Scoping Meeting** | **Wed 4/11/18** | **Tue 4/24/18** | | **10 days** |
| 257 | Cooperating Agency Scoping Meeting | Wed 4/11/18 | Tue 4/24/18 | 255SS | 10 days |
| 258 | Initiate Tribal Engagement (USACE leads) | Wed 4/11/18 | Tue 4/24/18 | 255SS | 10 days |
| 259 | **Scoping Summary Report** | **Thu 3/29/18** | **Tue 6/26/18** | | **63 days** |
| 260 | Compilation and Categorizing of Scoping Comments | Thu 3/29/18 | Wed 5/9/18 | 232 | 30 days |
| 261 | Determination of Comment Themes and Key Issues | Thu 5/10/18 | Wed 5/16/18 | 260 | 5 days |

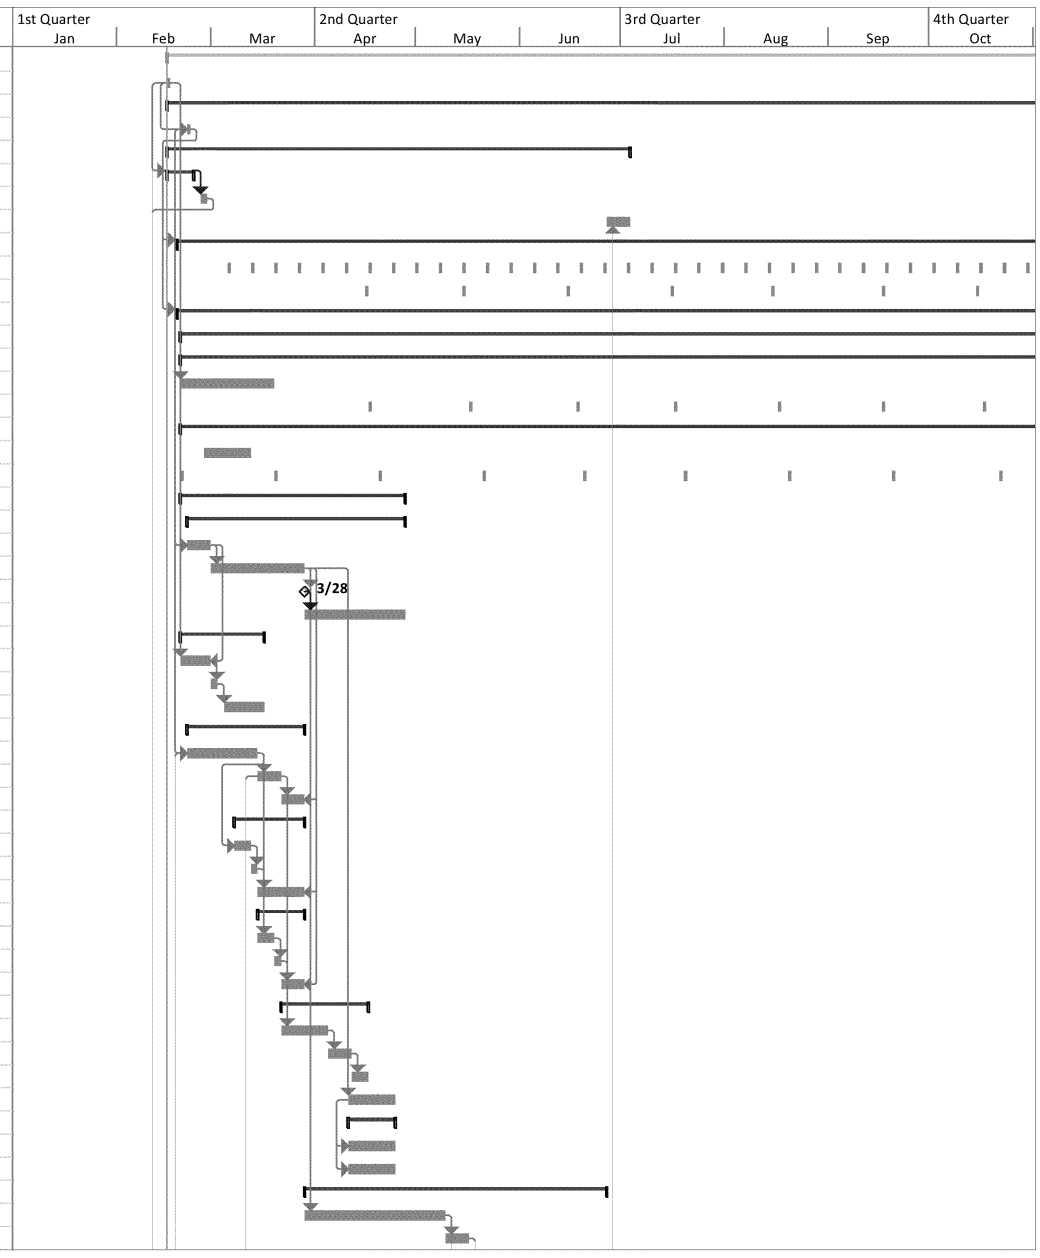

| ID | Task Name | Start | Finish | Predecessors | Duration |
|---|---|---|---|---|---|
| 262 | Meeting with USACE to Discuss Key Issues | Thu 5/17/18 | Thu 5/17/18 | 261 | 1 day |
| 263 | Finalize Key Issues | Fri 5/18/18 | Thu 5/24/18 | 262 | 5 days |
| 264 | Prepare Draft Public Scoping Summary Report | Thu 5/10/18 | Wed 5/23/18 | 260 | 10 days |
| 265 | USACE Review of Scoping Summary Report | Thu 5/24/18 | Thu 6/7/18 | 264 | 10 days |
| 266 | Revise Scoping Scoping Summary Report and Submit to USACE for Final Review | Fri 6/8/18 | Thu 6/14/18 | 265 | 5 days |
| 267 | USACE Review and Approval on Scoping Summary Report | Fri 6/15/18 | Thu 6/21/18 | 266 | 5 days |
| 268 | Print and Distribute Final Scoping Summary Report (post to website) | Fri 6/22/18 | Tue 6/26/18 | 267 | 3 days |
| 269 | **Cooperating Agency Coordination Meetings (Monthly)** | **Tue 5/15/18** | **Mon 3/16/20** | | **461 days** |
| 293 | **Tribal Engagement** | **Wed 5/16/18** | **Thu 1/16/20** | | **420 days** |
| 315 | **Draft EIS Public Meetings/Hearings** | **Tue 11/27/18** | **Sun 3/17/19** | | **75 days** |
| 316 | Prepare Notice of Availability (NOA) for Draft EIS | Tue 11/27/18 | Mon 12/3/18 | 398 | 5 days |
| 317 | USACE Review and Publish NOA for DEIS | Tue 12/4/18 | Wed 1/16/19 | 316 | 30 days |
| 318 | NOA for DEIS Published | Wed 1/16/19 | Wed 1/16/19 | 317 | 0 days |
| 319 | *Draft EIS Public Review Period* | *Wed 1/16/19* | *Sun 3/17/19* | *318* | *60 edays* |
| 320 | **Newsletter #2** | **Wed 12/26/18** | **Wed 1/16/19** | | **15 days** |
| 321 | Prepare Draft Newsletter #2 | Wed 12/26/18 | Fri 12/28/18 | 317SS+15 days | 3 days |
| 322 | USACE Review Newsletter #2 | Mon 12/31/18 | Wed 1/2/19 | 321 | 2 days |
| 323 | Finalize and Publish Newsletter #2 | Thu 1/3/19 | Wed 1/16/19 | 322,319SF | 10 days |
| 324 | **News Release #2** | **Thu 1/3/19** | **Wed 1/16/19** | | **10 days** |
| 325 | Prepare Draft News Release #2 | Thu 1/3/19 | Mon 1/7/19 | 322 | 3 days |
| 326 | USACE Review News Release #2 | Tue 1/8/19 | Wed 1/9/19 | 325 | 2 days |
| 327 | Finalize and Publish News Release #2 | Thu 1/10/19 | Wed 1/16/19 | 326,319SF | 5 days |
| 328 | **Hearing Preparations and Materials** | **Tue 12/4/18** | **Thu 2/7/19** | | **45 days** |
| 329 | Arrange/Secure Hearing Facilities & Court Reporters | Tue 12/4/18 | Mon 12/24/18 | 317SS | 15 days |
| 330 | Prepare Draft Hearing Materials | Tue 12/4/18 | Wed 1/9/19 | 329SS | 25 days |
| 331 | USACE Review Hearing Materials | Thu 1/10/19 | Thu 1/24/19 | 330 | 10 days |
| 332 | Finalize and Produce Hearing Materials | Fri 1/25/19 | Thu 2/7/19 | 331 | 10 days |
| 333 | **News Release #3** | **Fri 1/25/19** | **Thu 2/7/19** | | **10 days** |
| 334 | Prepare Draft News Release #3 | Fri 1/25/19 | Tue 1/29/19 | 331 | 3 days |
| 335 | USACE Review News Release #3 | Wed 1/30/19 | Thu 1/31/19 | 334 | 2 days |
| 336 | Finalize and Publish News Release #3 | Fri 2/1/19 | Thu 2/7/19 | 335 | 5 days |
| 337 | Public Hearings (10) | Fri 2/15/19 | Fri 3/1/19 | 317FS+20 days | 10 days |
| 338 | **Final EIS** | **Mon 10/28/19** | **Thu 1/9/20** | | **50 days** |
| 339 | Prepare Notice of Availability (NOA) for Final EIS | Mon 10/28/19 | Fri 11/8/19 | 416FF | 10 days |
| 340 | USACE Review and Publish NOA for FEIS | Tue 11/19/19 | Tue 12/10/19 | 417 | 15 days |
| 341 | NOA for FEIS Published | Tue 12/10/19 | Tue 12/10/19 | 340 | 0 days |
| 342 | *Final EIS Review Period* | *Tue 12/10/19* | *Thu 1/9/20* | *341* | *30 edays* |
| 343 | **Newsletter #3** | **Tue 11/12/19** | **Tue 12/10/19** | | **20 days** |
| 344 | Prepare Draft Newsletter #3 | Tue 11/12/19 | Mon 11/18/19 | 339 | 5 days |
| 345 | USACE Review Newsletter #3 | Tue 11/19/19 | Mon 11/25/19 | 344 | 5 days |
| 346 | Finalize and Publish Newsletter #3 | Tue 11/26/19 | Tue 12/10/19 | 340FF | 10 days |
| 347 | **News Release #4** | **Tue 11/12/19** | **Tue 12/10/19** | | **20 days** |
| 348 | Prepare Draft News Release #4 | Tue 11/12/19 | Mon 11/18/19 | 339 | 5 days |
| 349 | USACE Review News Release #4 | Tue 11/19/19 | Mon 11/25/19 | 348 | 5 days |
| 350 | Finalize and Publish News Release #4 | Wed 12/4/19 | Tue 12/10/19 | 340FF | 5 days |
| 351 | **Task 3 - Draft EIS** | **Fri 2/16/18** | **Wed 1/16/19** | | **231 days** |
| 352 | **EIS Outline, Templates, & Style Guide** | **Thu 2/22/18** | **Wed 5/2/18** | | **50 days** |
| 353 | Prepare EIS Outline | Thu 2/22/18 | Wed 3/14/18 | 240SS | 15 days |
| 354 | USACE Review, Modification, and Approval of EIS Outline | Thu 3/15/18 | Wed 3/21/18 | 353,241SS | 5 days |
| 355 | Prepare Document/Map Templates, Mapping Standards, and Style Guide | Thu 3/22/18 | Wed 4/25/18 | 354 | 25 days |
| 356 | USACE Review and Approval of Templates, Standards, Style Guide | Thu 4/26/18 | Wed 5/2/18 | 355 | 5 days |
| 357 | **Data Adequacy & Gaps Analysis** | **Fri 2/16/18** | **Mon 7/9/18** | **12** | **99 days** |

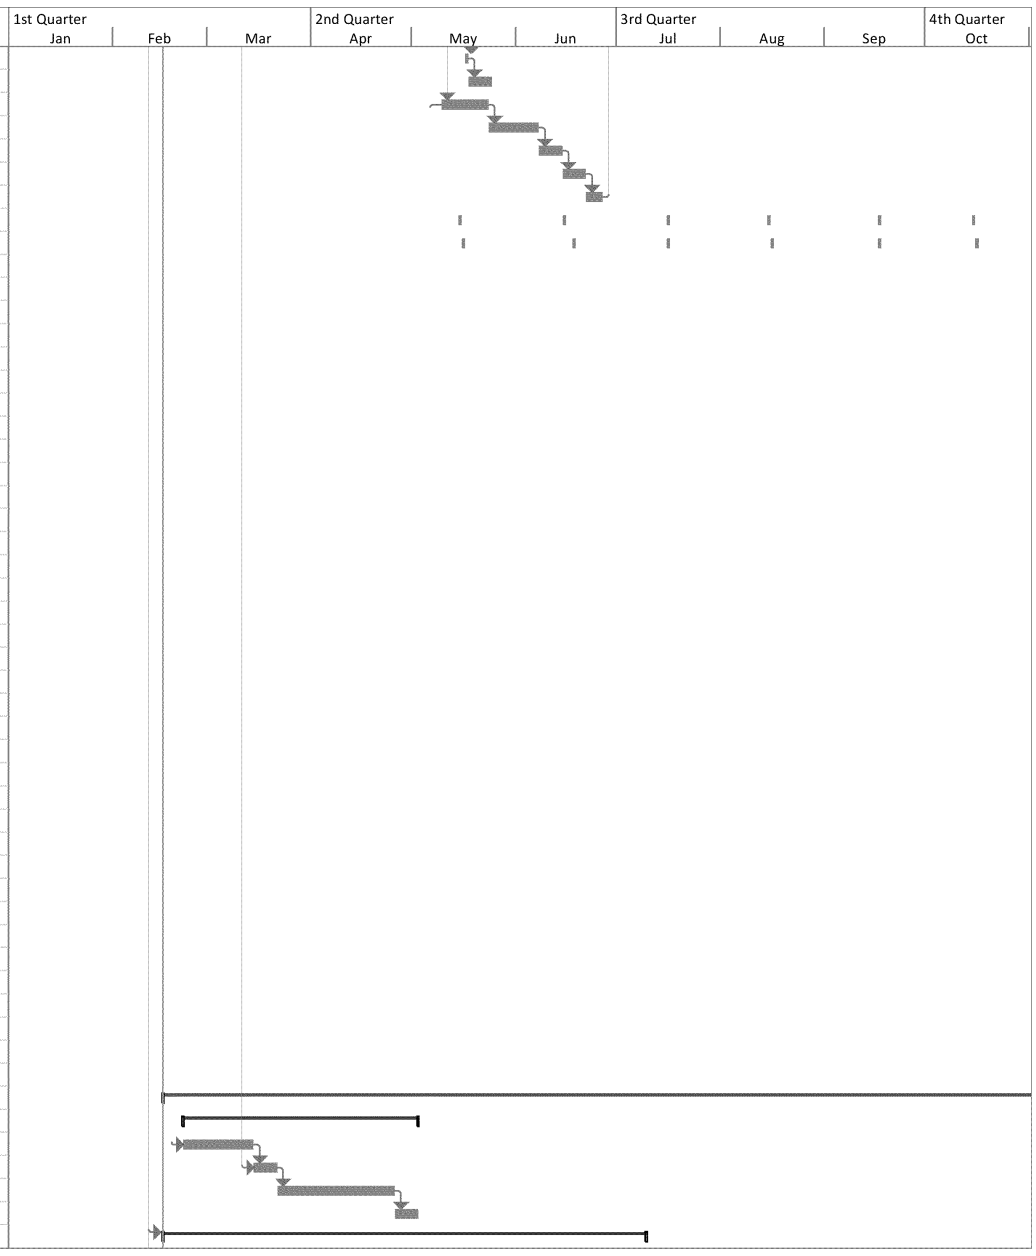

| ID | Task Name | Start | Finish | Predecessors | Duration |
|---|---|---|---|---|---|
| 358 | Obtain Reports, Models, GIS & AutoCAD files from PLP | Fri 2/16/18 | Wed 2/21/18 | 1SS | 3 days |
| 359 | Preliminary Data Gaps Analysis (initiate Chapters 3 and 4) | Wed 2/21/18 | Fri 3/23/18 | 358 | 30 edays |
| 360 | USACE Review Data Adequacy & Gaps Reports/Memos | Mon 3/26/18 | Fri 4/6/18 | 359 | 10 days |
| 361 | Data Gaps Filled (or Documented as Unavailable Info) | Mon 4/9/18 | Fri 5/18/18 | 360 | 30 days |
| 362 | Revise and Finalize Data Gaps Analysis (post alternatives) | Mon 6/25/18 | Mon 7/9/18 | 376 | 10 days |
| 363 | **Preliminary Draft EIS (PDEIS)** | **Thu 2/22/18** | **Fri 10/26/18** | | **173 days** |
| 364 | **Draft Chapter 1 - Purpose and Need** | **Wed 2/28/18** | **Tue 5/8/18** | | **50 days** |
| 365 | USACE Provides Draft Purpose and Need Statement | Wed 2/28/18 | Wed 2/28/18 | 12 | 1 day |
| 366 | Prepare Pre-Draft Chapter 1 | Wed 2/28/18 | Tue 4/10/18 | 12 | 30 days |
| 367 | USACE Review of Pre-Draft Chapter 1 | Wed 4/11/18 | Tue 5/1/18 | 366 | 15 days |
| 368 | Incorporate/Address Comments on Pre-Draft Chapter 1 | Wed 5/2/18 | Tue 5/8/18 | 367 | 5 days |
| 369 | **Draft Chapter 2 - Project Description/Alternatives** | **Thu 2/22/18** | **Tue 9/25/18** | | **151 days** |
| 370 | Prepare Description of Applicant's Proposed Project | Thu 2/22/18 | Wed 3/14/18 | 358 | 15 days |
| 371 | **Develop Alternatives** | **Thu 5/10/18** | **Mon 7/23/18** | | **51 days** |
| 372 | Identify Wide Range of Alternatives | Thu 5/10/18 | Wed 5/23/18 | 264SS | 10 days |
| 373 | Develop Criteria for Screening Alternatives | Thu 5/17/18 | Wed 5/23/18 | 372FF | 5 days |
| 374 | Screen Alternatives | Thu 5/24/18 | Thu 6/7/18 | 373 | 10 days |
| 375 | USACE Review of Potential Alternatives | Fri 6/8/18 | Thu 6/21/18 | 374 | 10 days |
| 376 | Meeting with USACE & CAs on Potential Alternatives | Fri 6/22/18 | Fri 6/22/18 | 375 | 1 day |
| 377 | Document Alternatives Dismissed from Detailed Consideration | Mon 6/25/18 | Mon 7/9/18 | 376 | 10 days |
| 378 | Prepare Potential Alternative Descriptions | Mon 6/25/18 | Mon 7/23/18 | 377SS | 20 days |
| 379 | Prepare Pre-Draft Chapter 2 | Tue 7/24/18 | Mon 8/20/18 | 378 | 20 days |
| 380 | USACE Review of Pre-Draft Chapter 2 | Tue 8/21/18 | Tue 9/11/18 | 379 | 15 days |
| 381 | Incorporate/Address Comments on Pre-Draft Chapter 2 | Wed 9/12/18 | Tue 9/25/18 | 380 | 10 days |
| 382 | **Draft Chapter 3 - Affected Environment** | **Thu 2/22/18** | **Thu 6/21/18** | | **85 days** |
| 383 | Prepare Affected Environment / Pre-Draft Chapter 3 | Thu 2/22/18 | Wed 5/16/18 | 358 | 60 days |
| 384 | USACE Review of Pre-Draft Chapter 3 | Thu 5/17/18 | Thu 6/7/18 | 383 | 15 days |
| 385 | Incorporate/Address Comments on Pre-Draft Chapter 3 | Fri 6/8/18 | Thu 6/21/18 | 384 | 10 days |
| 386 | **Draft Chapter 4 - Environmental Consequences** | **Mon 2/26/18** | **Tue 9/4/18** | | **134 days** |
| 387 | Develop Methodologies for Analyses of Direct, Indirect, and Cumulative Effects | Mon 2/26/18 | Fri 3/9/18 | 5 | 10 days |
| 388 | Evaluate Impacts of Applicant's Proposed Project - Pre-Draft Chapter 4 | Mon 3/12/18 | Mon 6/4/18 | 387 | 60 days |
| 389 | USACE Review of Pre-Draft Chapter 4 | Tue 6/5/18 | Mon 7/2/18 | 388 | 20 days |
| 390 | Incorporate/Address Comments on Pre-Draft Chapter 4 | Tue 7/3/18 | Tue 7/31/18 | 389 | 20 days |
| 391 | Evaluate Impacts of Alternatives, incorporate in Chapter 4 | Tue 7/24/18 | Tue 9/4/18 | 378 | 30 days |
| 392 | **Editing and Compilation** | **Tue 7/24/18** | **Fri 10/26/18** | **387FS-15 days** | **67 days** |
| 393 | Compile PDEIS (including final QA/QC) | Tue 7/24/18 | Tue 9/11/18 | 391SS | 35 days |
| 394 | USACE Review of PDEIS | Tue 9/11/18 | Thu 10/11/18 | 393 | 30 edays |
| 395 | Incorporate/Address Comments and Revise PDEIS | Fri 10/12/18 | Thu 10/25/18 | 394 | 10 days |
| 396 | Meet with USACE to Review Comments | Fri 10/26/18 | Fri 10/26/18 | 395 | 1 day |
| 397 | **Draft EIS (DEIS)** | **Mon 10/29/18** | **Wed 1/16/19** | | **55 days** |
| 398 | Revise and Submit DEIS to USACE for Review (by Chapter) | Mon 10/29/18 | Mon 11/26/18 | 396 | 20 days |
| 399 | USACE Review of DEIS Sections | Tue 11/27/18 | Mon 12/17/18 | 398 | 15 days |
| 400 | Revise DEIS and Submit Final DEIS to USACE | Tue 12/18/18 | Mon 12/24/18 | 399 | 5 days |
| 401 | USACE Approves Camera-Ready Version | Wed 12/26/18 | Wed 1/2/19 | 400 | 5 days |
| 402 | DEIS Production & Distribution (incl public viewing locations, website) | Thu 1/3/19 | Wed 1/16/19 | 401 | 10 days |
| 403 | **Task 4 - Final EIS (FEIS)** | **Thu 1/17/19** | **Tue 12/10/19** | | **226 days** |
| 404 | **Comment Analysis and Response** | **Thu 1/17/19** | **Tue 8/6/19** | | **140 days** |
| 405 | Receive and Catalogue Comments on DEIS | Thu 1/17/19 | Fri 3/29/19 | 319SS | 50 days |
| 406 | Draft Comment Responses | Mon 3/4/19 | Mon 6/10/19 | 405FS-20 days | 70 days |
| 407 | Meeting with USACE and Cooperating Agencies Re: Draft Responses | Tue 6/11/19 | Tue 6/11/19 | 406 | 1 day |
| 408 | USACE and Cooperating Agencies Review Draft Comment Responses | Tue 6/11/19 | Tue 7/9/19 | 407SS | 20 days |
| 409 | Finalize Comment Responses | Wed 7/10/19 | Tue 8/6/19 | 408 | 20 days |

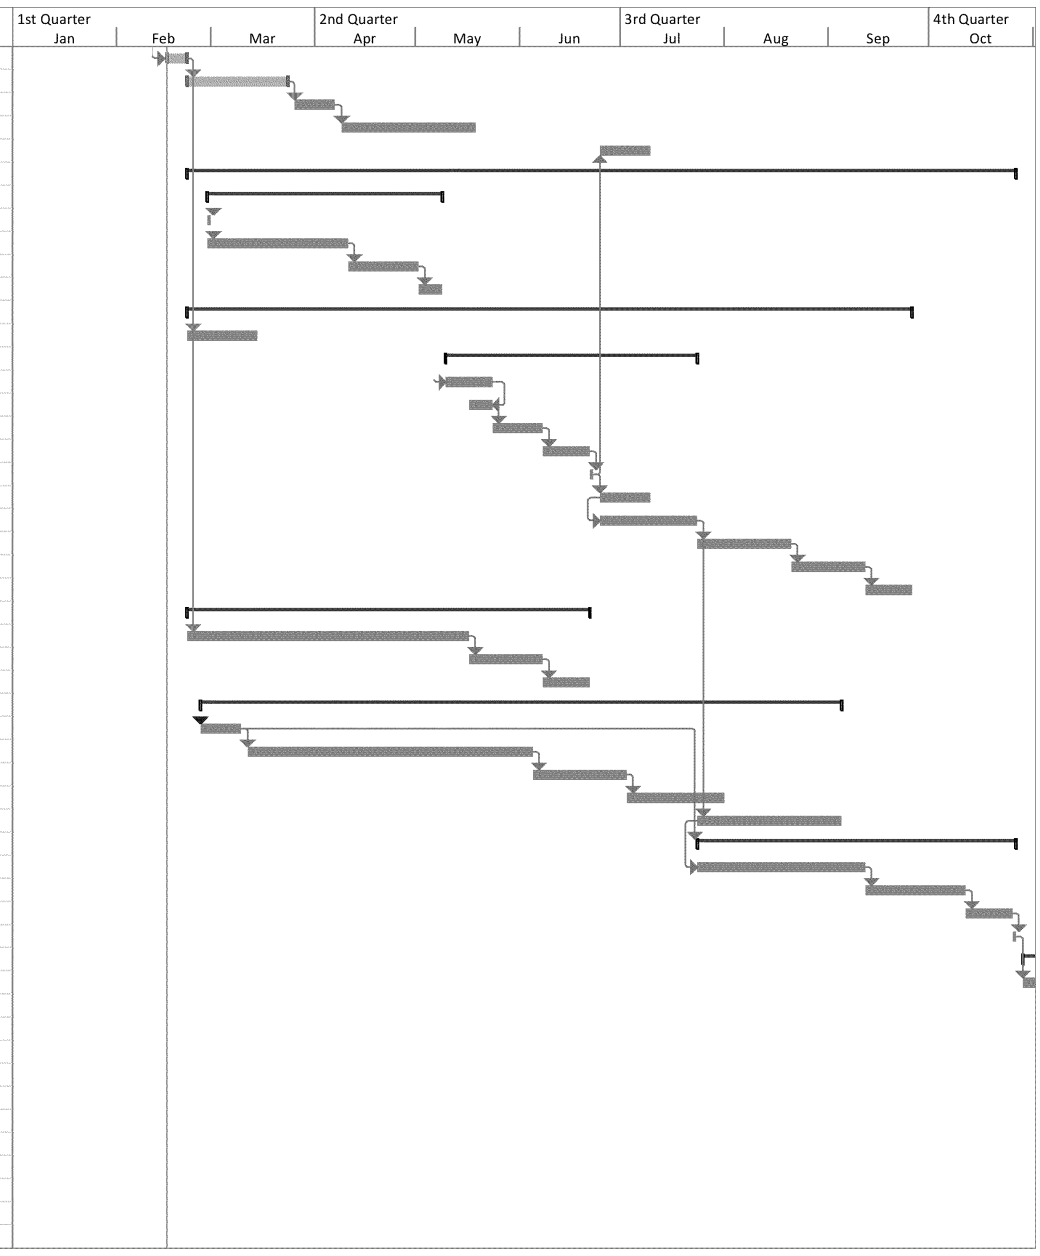

| ID | Task Name | Start | Finish | Predecessors | Duration |
|---|---|---|---|---|---|
| 410 | **Preliminary Final EIS (PFEIS)** | **Tue 6/11/19** | **Fri 10/18/19** | | **91 days** |
| 411 | Modify and Prepare PFEIS (incl QA/QC) | Tue 6/11/19 | Tue 8/20/19 | 406 | 50 days |
| 412 | USACE and Cooperating Agencies Review of PFEIS | Wed 8/21/19 | Wed 9/18/19 | 411 | 20 days |
| 413 | Review/Incorporate Comments and Revise PFEIS | Thu 9/19/19 | Thu 10/17/19 | 412 | 20 days |
| 414 | Meet with USACE and Cooperating Agencies to Review Comments | Fri 10/18/19 | Fri 10/18/19 | 413 | 1 day |
| 415 | **Final EIS (FEIS)** | **Mon 10/21/19** | **Tue 12/10/19** | | **35 days** |
| 416 | Revise FEIS (incl QA/QC) | Mon 10/21/19 | Fri 11/8/19 | 414 | 15 days |
| 417 | USACE Approves Camera-Ready Version (pg turn meetings) | Tue 11/12/19 | Mon 11/18/19 | 416 | 5 days |
| 418 | FEIS Production & Distribution (incl public viewing locations, website) | Tue 11/19/19 | Tue 12/10/19 | 417 | 15 days |
| 419 | Record of Decision | Mon 3/9/20 | Mon 3/9/20 | 418FS+90 eday | 0 edays |
| 420 | **Task 5 - Other Permits** | **Wed 2/28/18** | **Fri 10/25/19** | | **420 days** |
| 424 | **Task 6 - Administrative Record** | **Tue 2/20/18** | **Tue 3/31/20** | | **532 days** |
| 425 | Administrative Record Database Setup | Tue 2/20/18 | Mon 3/5/18 | 1 | 10 days |
| 426 | **Maintain Administrative Record (monthly, at a minimum)** | **Fri 3/16/18** | **Mon 3/16/20** | | **503 days** |
| 452 | Deliver Administrative Record | Tue 3/31/20 | Tue 3/31/20 | 451FS+10 days | 1 day |

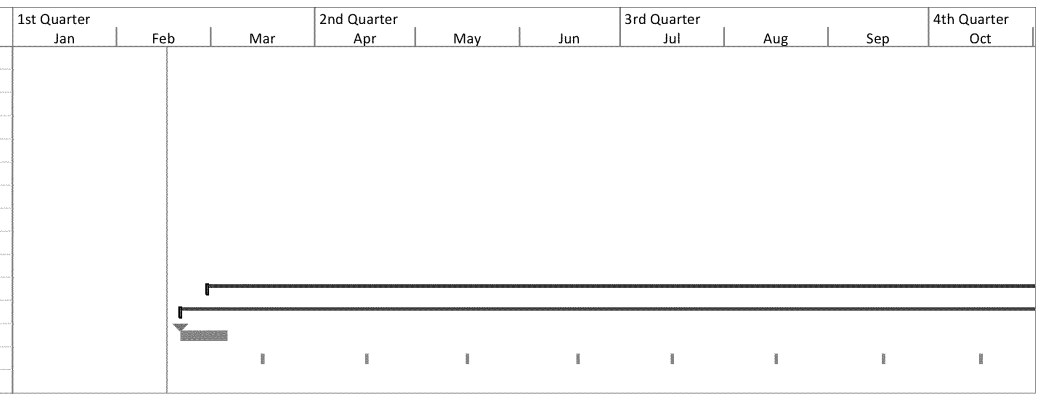

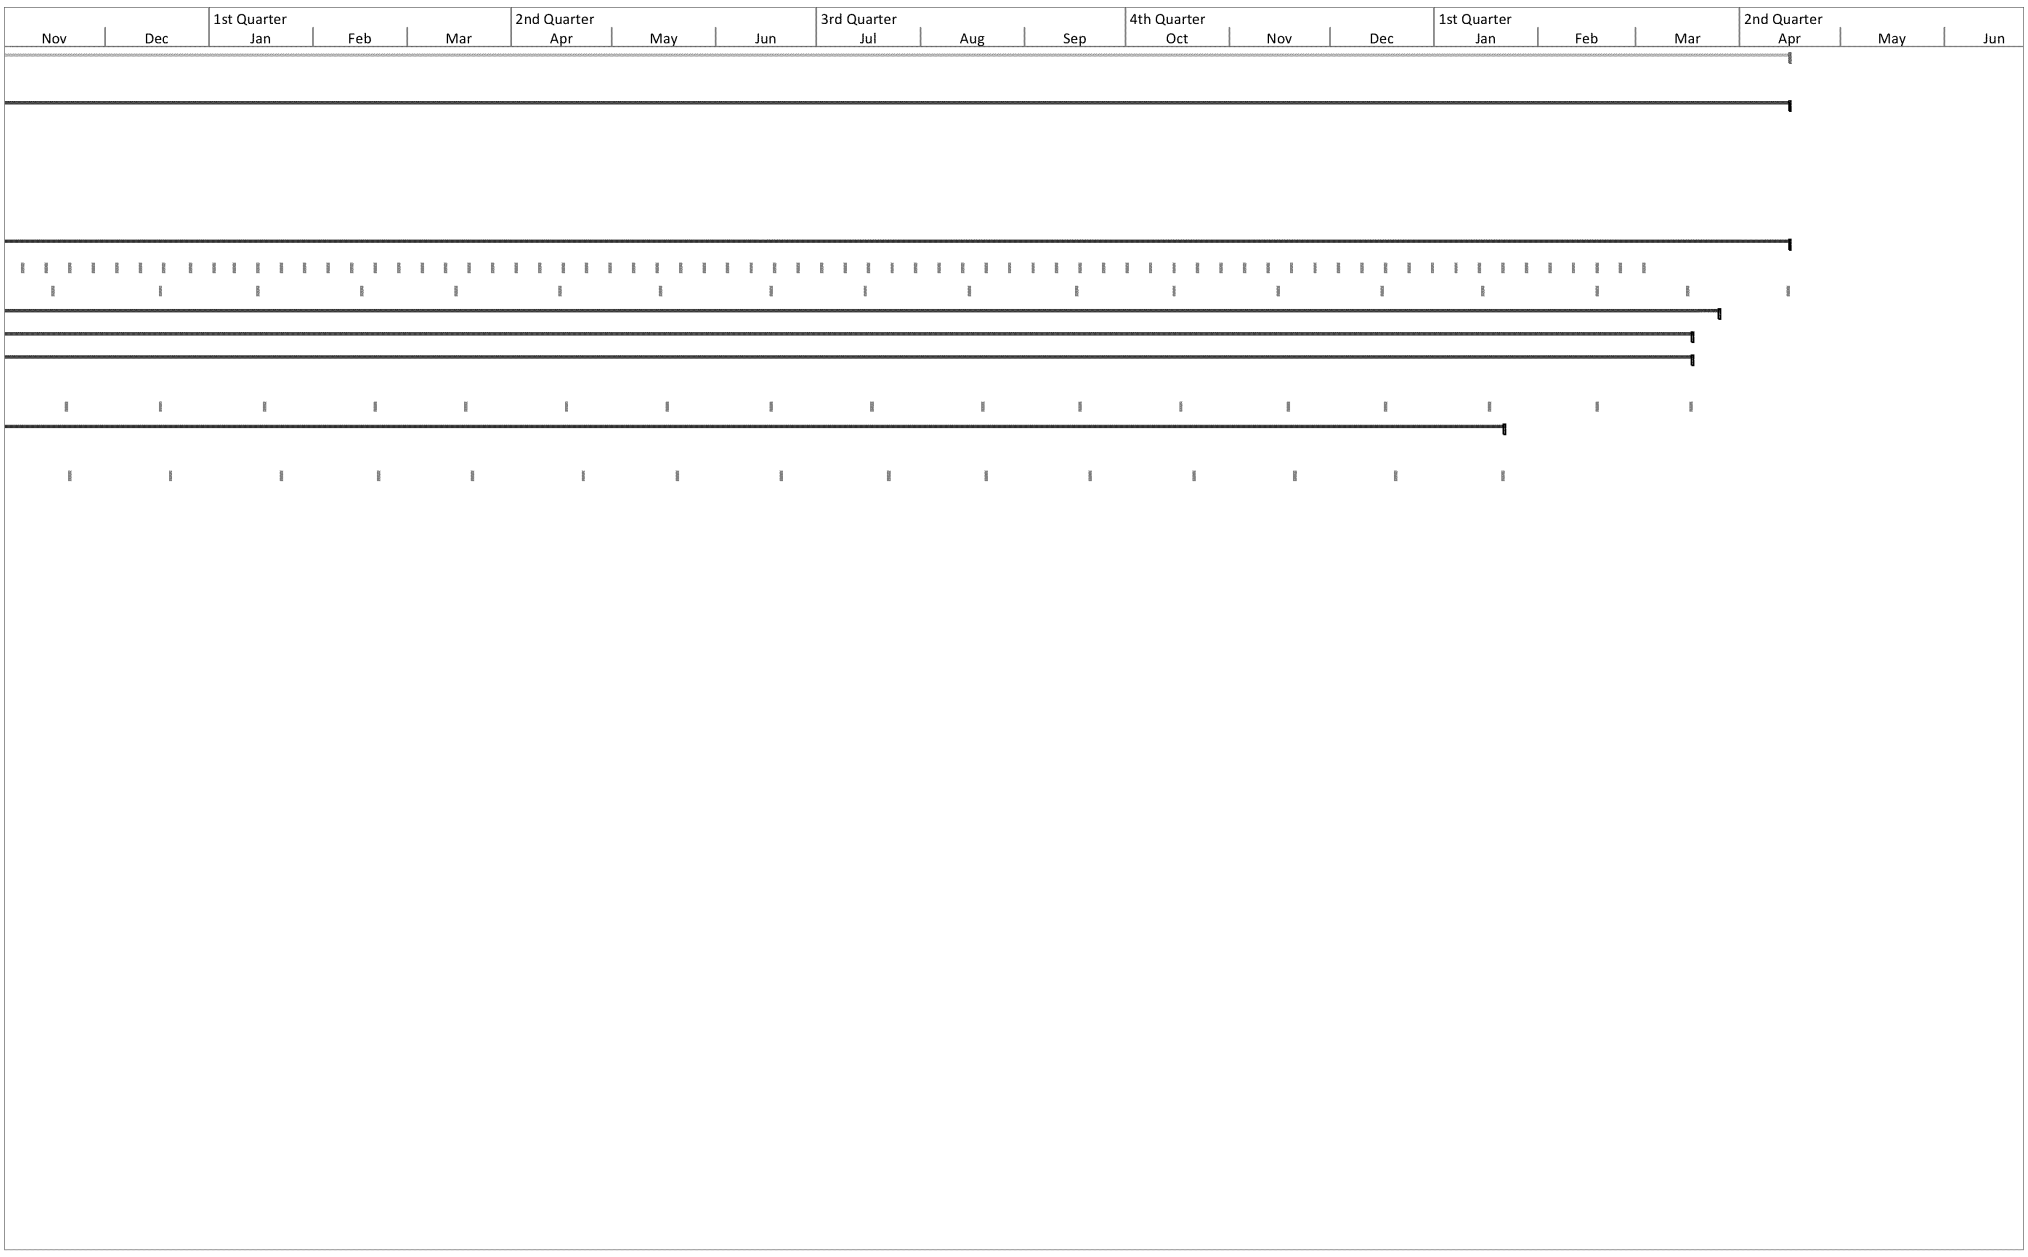
1st Quarter
2nd Quarter
3rd Quarter
4th Quarter
1st Quarter
2nd Quarter
Nov
Dec
Jan
Feb
Mar
Apr
May
Jun
Jul
Aug
Sep
Oct
Nov
Dec
Jan
Feb
Mar
Apr
May
Jun

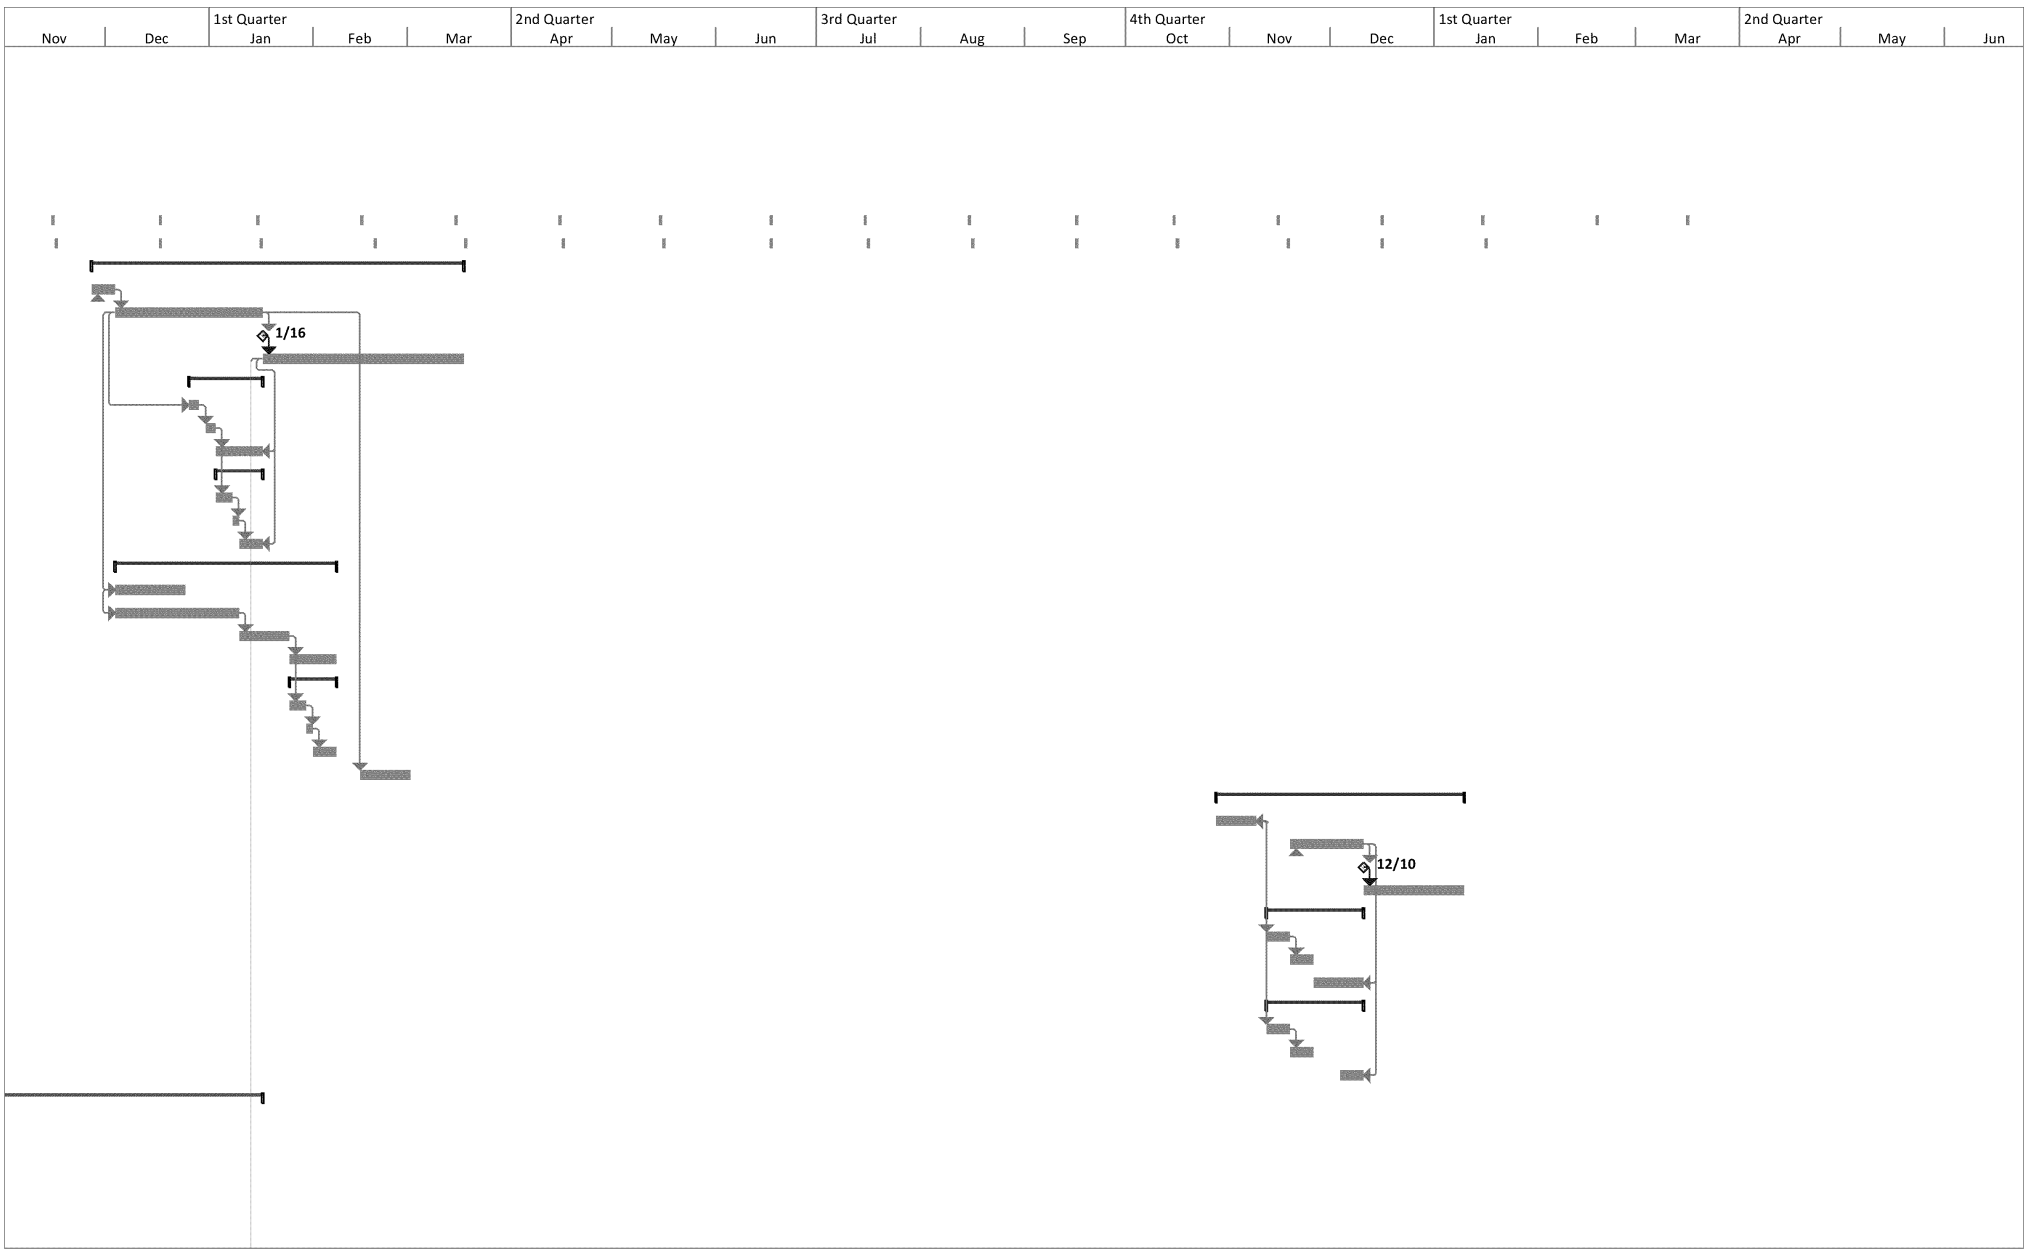
1st Quarter
2nd Quarter
3rd Quarter
4th Quarter
1st Quarter
2nd Quarter
Nov
Dec
Jan
Feb
Mar
Apr
May
Jun
Jul
Aug
Sep
Oct
Nov
Dec
Jan
Feb
Mar
Apr
May
Jun
1/16
12/10

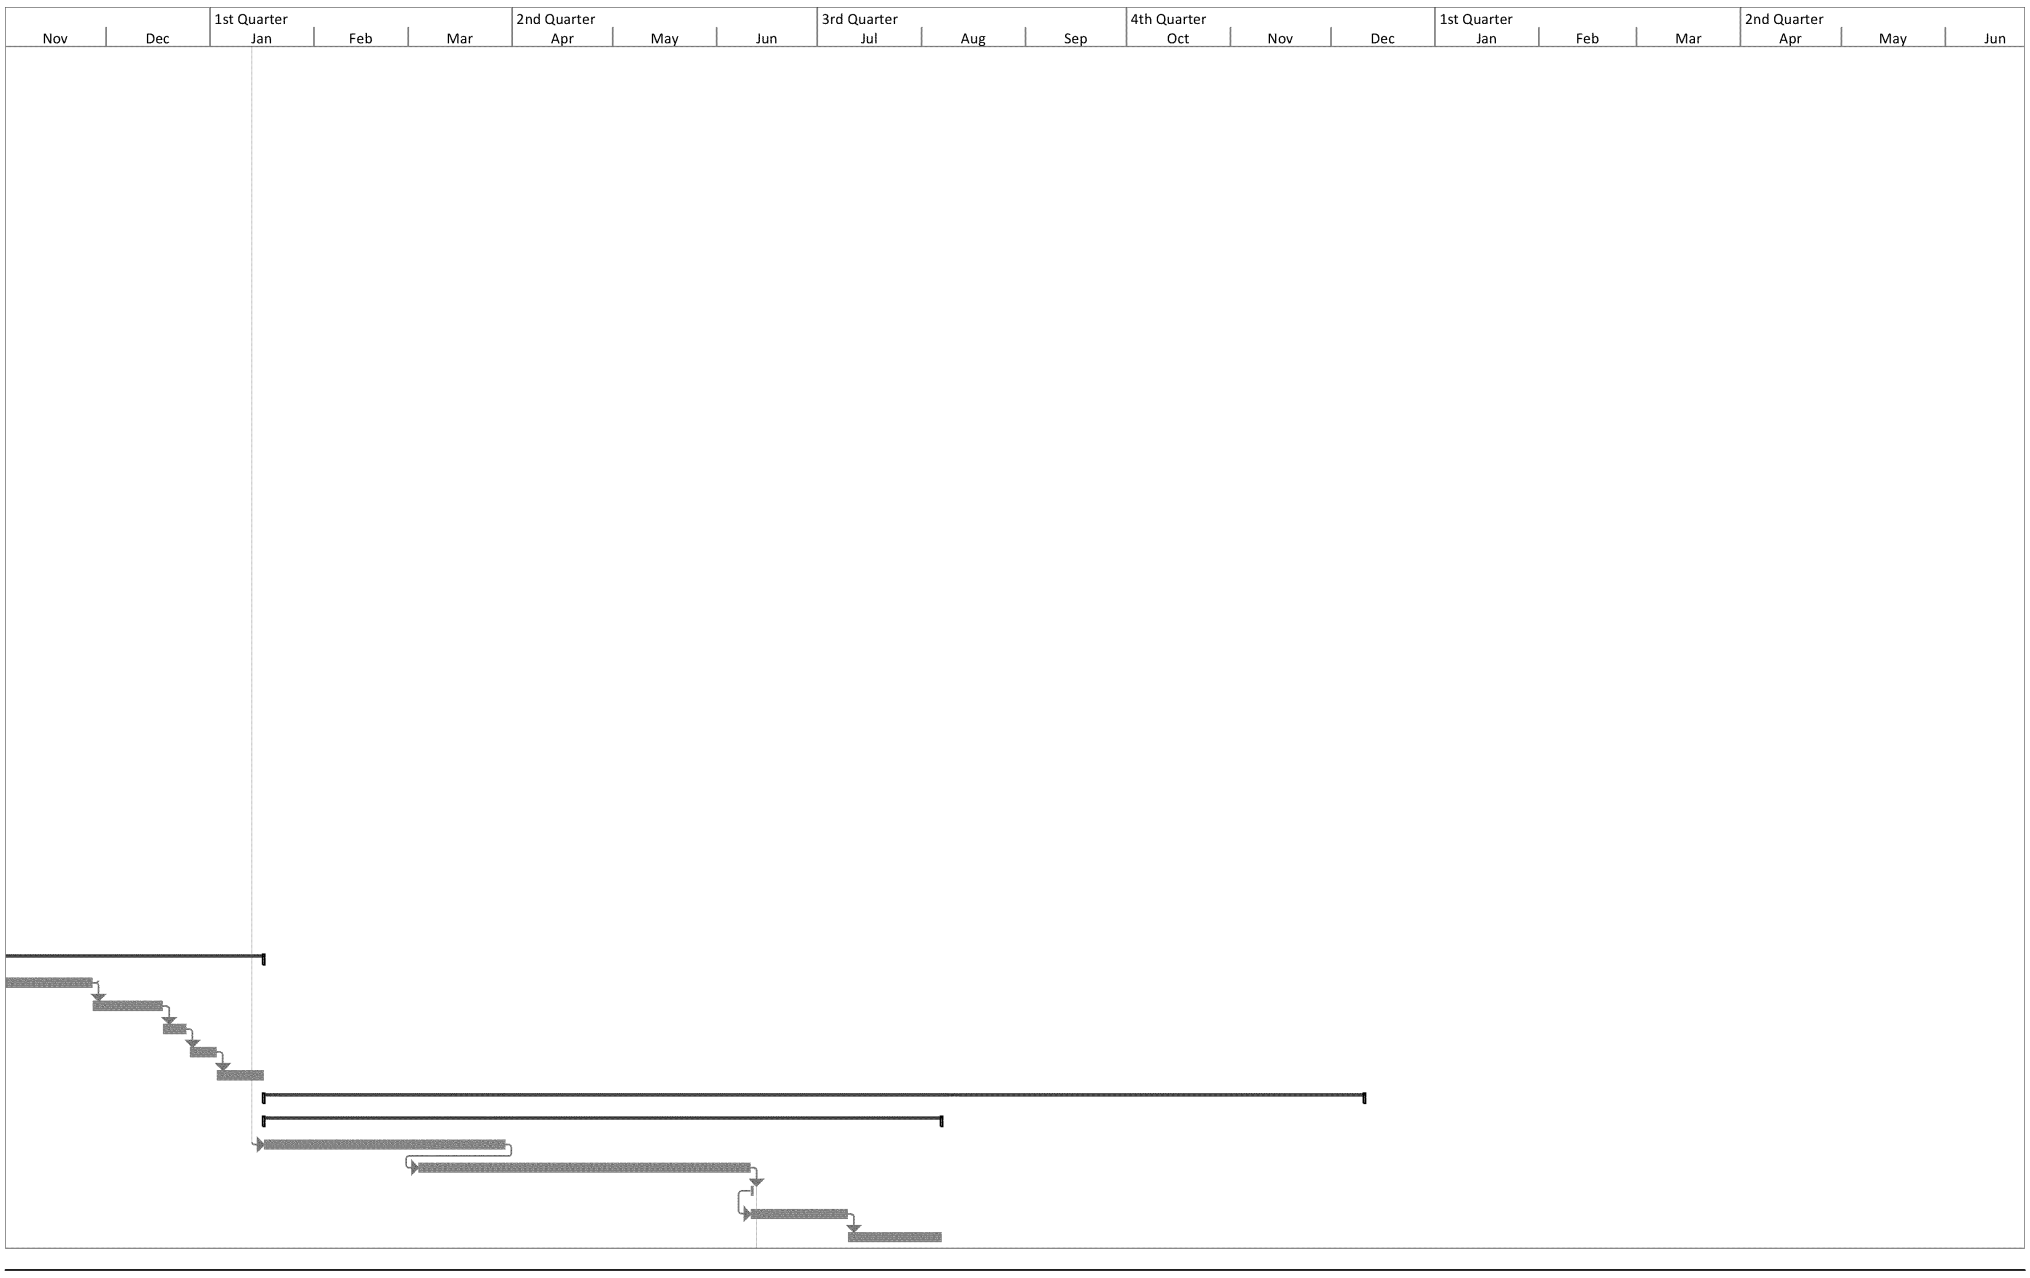
1st Quarter
2nd Quarter
3rd Quarter
4th Quarter
1st Quarter
2nd Quarter
Nov
Dec
Jan
Feb
Mar
Apr
May
Jun
Jul
Aug
Sep
Oct
Nov
Dec
Jan
Feb
Mar
Apr
May
Jun

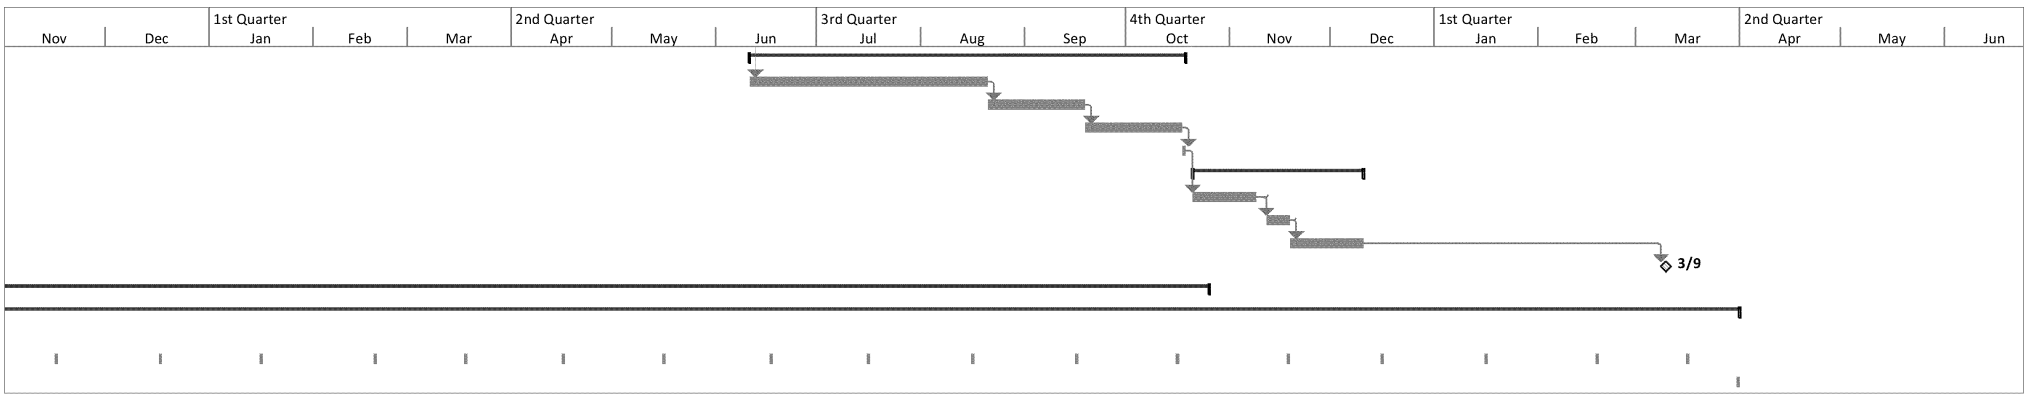
1st Quarter
2nd Quarter
3rd Quarter
4th Quarter
1st Quarter
2nd Quarter
Nov
Dec
Jan
Feb
Mar
Apr
May
Jun
Jul
Aug
Sep
Oct
Nov
Dec
Jan
Feb
Mar
Apr
May
Jun
3/9
