DGW-1I					
Sampling Month & Year	1,1-DCE	1,1,1-TCA	TCE	1,2-DCA	PCE
February-98	6	0	4	0.6	0
April-02	**21**	83	9 J	**150**	**47**
January-05	**26**	140	**31**	0	0
December-05	**13.6**	47.2	**21.6**	**18.4**	0
June-06	6.9	22	**12**	0	0
December-06	4.6	18	**9.7**	0	0
June-07	**26**	26	**13**	0	0
September-07	**46**	150	**8.9**	0	0
December-07	**93**	**340**	**46**	0	0
March-08	**33**	**250**	**39**	0	0
June-08	**88**	**370**	**45**	0	0
October-08	**63**	**470**	**68**	0	0
June-09	**70**	**390**	**51**	0	0
December-09	**91**	**630**	**110**	0	0
June-10	**110**	**640**	**71**	0	0
December-10	**75**	**460**	**72**	0	0
June-11	**63**	**340**	**50**	0	0
December-11	**60**	**360**	**52**	0	0
June-12	**120**	**710**	**90**	0	0
December-12	**53**	**240**	**42**	0	0
June-13	**54**	**260**	**39**	0	0
December-13	0	150	**26**	0	0
June-14	**33**	150	**24**	0	0
October-14	**88**	**420**	**54**	0	0
June-15	**85**	**310**	**41**	0	0
December-15	**42**	**250**	**32**	0	0
June-16	**82**	**350**	**61**	0	0
December-16	**38**	**290**	**38**	0	0
MCL	7	200	5	5	5

Concentrations reported in micrograms per liter.
Bold values exceed the MCL.
EPA Method 8260B was run. Only chemicals with detections above the MCLs were plotted.
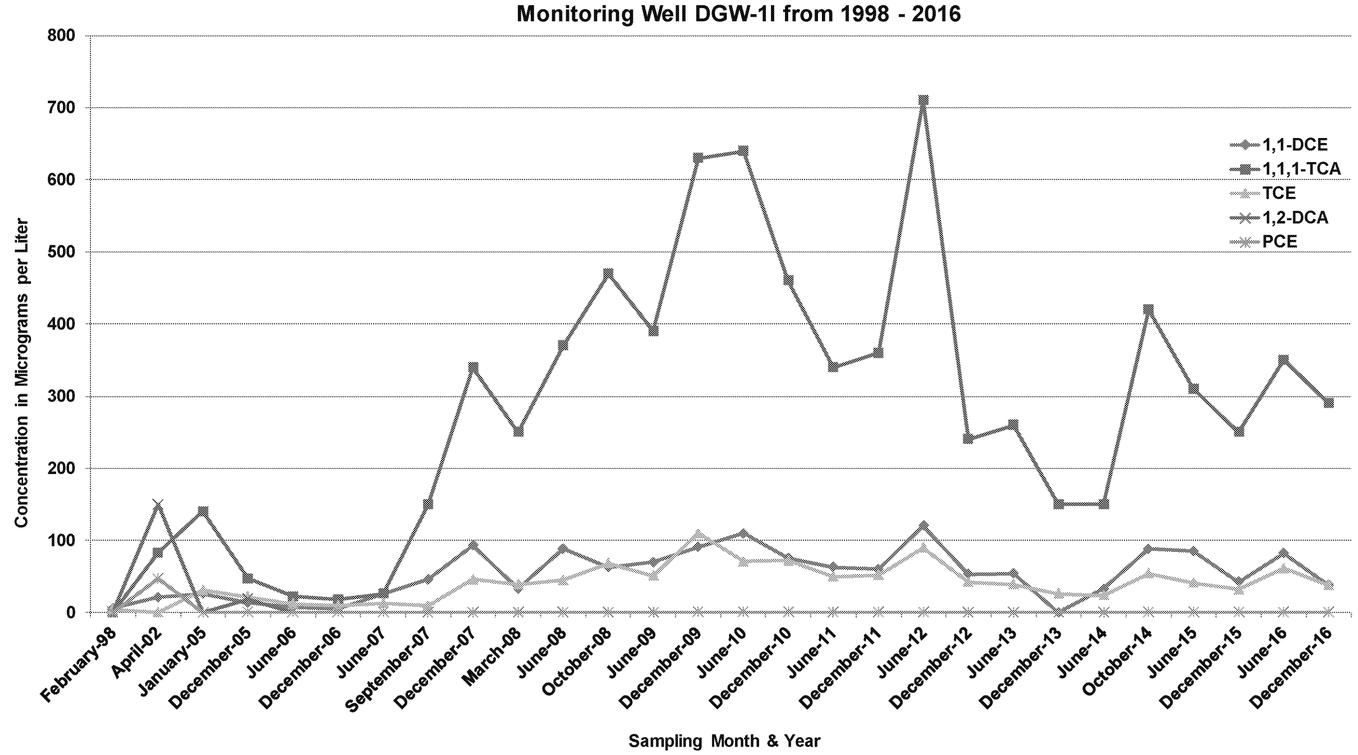
Figure 3-10
Trends in VOC Concentrations at the Central Wire Union, Illinois Plant for Parameters Exceeding the MCLs in Monitoring Well DGW-1I from 1998 - 2016
