Project # 13 - 5451

Jim Bridger Power Plant

Units #3 & #4 SCR Project PGL Schedule

Activity ID	Activity Name	Original Duration	Remaining Duration	Start	Finish	Total Float
	Bridger PGL Fall/Fall Outage	345	315	11-Feb-13 A	30-Nov-16	21
	Project Milestones	1	1	1-Jan-15	30-Nov-16	21
	Engineering	344	343	18-Mar-13 A	29-Nov-16	21
	Procurement	365	315	15-Sep-13 A	26-May-15	21
	Deliverables	90	90	12-May-14	25-Sep-15	21
	Construction	1,157	1,157	28-Aug-13 A	25-Aug-16	68
	Construction Common	1,141	1,105	28-Aug-13 A	25-Aug-16	68
	Civil Construction	364	361	20-Aug-13 A	28-Apr-15	436
	Ash Trench Pipe Relocation	278	278	04-Apr-14	28-Apr-15	147
	Lay-Down Area	24	24	17-Dec-13	24-Jan-14	135
	SCR Foundations Area	50	50	20-Jan-14	28-Mar-14	101
	SCR Unit #3	157	157	17-Dec-13	30-Jul-14	591
	SCR Unit #4	132	132	04-Feb-14	06-Aug-14	490
	Annhydrous Ammonia System	92	92	27-Jan-14	03-Jun-14	129
	Fan Foundations	29	29	12-May-14	19-Jun-14	657
	Fan Bay Alley	137	134	20-Aug-13 A	20-Jun-14	657
	Domestic Waterline Extension and Pavement Reinforcement System	35	35	27-Jan-14	14-Mar-14	129
	Misc Site Items	135	135	10-Dec-13	23-Jun-14	657
	Foundations, Slabs, and Grade Beams	394	394	23-Jan-14	28-Jul-15	371
	Foundations, Slabs, and Grade Beams (SCR Areas) Unit #3 by Activity	89	89	04-Feb-14	06-Jun-14	0
	Unit #3 Caissons	75	75	06-Feb-14	21-May-14	4
	Unit #3 Caps/Grade Beams	89	89	04-Feb-14	06-Jun-14	0
	Foundations, Slabs, and Grade Beams (SCR Areas) Unit #4 by Activity	62	62	29-Apr-14	23-Jul-14	82
	Unit #4 Caissons	50	50	01-May-14	09-Jul-14	84
	Unit #4 Caps/Grade Beams	62	62	29-Apr-14	23-Jul-14	82
	Unit #4 (SCR Area) ID Fans/Lube Oil Building	55	55	29-Apr-15	14-Jul-15	202
	(SCR Area) Unit #4 ID Fans North	40	40	29-Apr-15	23-Jun-15	217
	North Lube Oil Building Foundation	20	20	03-Jun-15	30-Jun-15	212
	(SCR Area) Unit #4 ID Fans South	45	45	06-May-15	07-Jul-15	152
	South Lube Oil Building Foundation	25	25	10-Jun-15	14-Jul-15	147
	Foundations, Slabs, and Grade Beams (VFD Building)	30	30	28-Aug-14	08-Oct-14	362
	VFD Building Drill Piers	16	16	28-Aug-14	18-Sep-14	362
	VFD Building Foundations	14	14	19-Sep-14	08-Oct-14	362
	Foundations, Slabs, and Grade Beams (Anhydrous Ammonia)	61	61	04-Jun-14	27-Aug-14	129
	Anhydrous Ammonia Drill Piers	15	15	04-Jun-14	24-Jun-14	129
	Anhydrous Ammonia Caps & Grade Beams	15	15	25-Jun-14	15-Jul-14	129
	Anhydrous Ammonia Slabs & Mats	31	31	16-Jul-14	27-Aug-14	129
	Foundations, Slabs, and Grade Beams (Anhydrous Ammonia System Pipe Rack) By Activity	77	77	04-Jun-14	18-Sep-14	129
	Anhydrous Ammonia System Pipe Rack Drill Piers/Foundations	77	77	04-Jun-14	18-Sep-14	129
	Foundation Misc	394	394	23-Jan-14	28-Jul-15	371
	Mechanical	270	270	30-May-14	11-Jun-15	404
	Electrical - Common	666	666	04-Feb-14	25-Aug-16	6

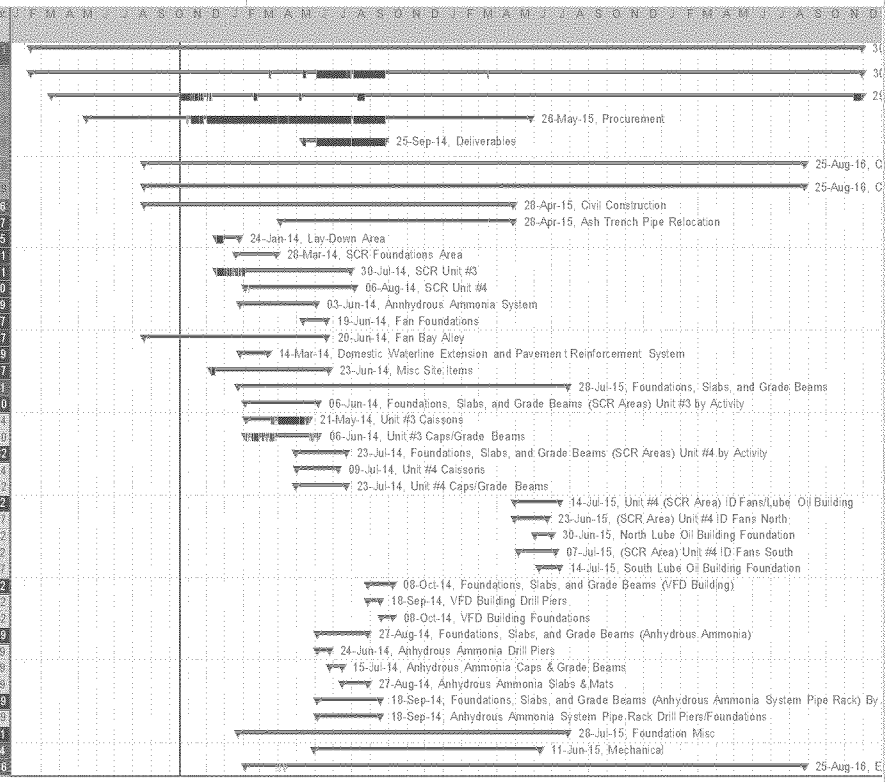

Actual Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

Data Date : 18-Oct-13 Run Date: 04-Nov-13

EPA-R8-2014-0028860002542
